



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL
IMPLEMENTASAUN
PROJETUS MUNISÍPIU MANUFAHI

MAIO 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO MANUFAHÍ

MAIO 2022

Prepara Husi :




(Eng. Fidelis Mardiano da Costa)

Eng. ba Edifício Público no Beé Saneamento, Município Manufahi



(Eng. Romulo J.M. Henrique)

Eng. ba Projeto Infraestrutura e Irigação, Município Manufahi ADN, I.P



(Silvino D R R Soares)

Eng. M & E, Município Manufahi ADN, I.P



(Arc. Francisco X D D Jeronimo)

Eng. Senior ba Edifício Público no Beé
Saneamento, ADN, I.P

Verifica Husi :



(Eng. Remigio da C.S. dos Santos)

Eng. Senior ba Projeto Infraestrutura e Irigação,
ADN, I.P



(Deolindo de F Marques)

Chefe Sek. Projeto M.E & ITC, ADN, I.P

Sertifica Husi :



(Eng. Emerenciana da Costa Maia Freitas)


Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :



(Mariano Renato Monteiro da Cruz, S. T. M. Eng)

Director Executivo, ADN, I.P



Contents

SUMÁRIO	0
Eng. ba Edifício Público no Beé Saneamento, Município Manufahi	0
ÍNDICE TABELA	0
I. INTRODUSAUN.	2
1.1 Enquadramento Legal.....	2
1.2 Perfil Município Manufahi.....	2
1.3. Lista Projecto.....	5
II. PROGRESSO FÍSICO	19
2.1 Progresso Físico Kada Fulan	19
III. OBSTÁCULO IHA TERENU.....	19
3.1 Obstáculo Serviço Iha Terenu	19
IV. REKOMENDASAUN IHA TERENU	20
4.1 Rekomendasaun Serviço Iha Terenu	20
 Tabela 1 : Postos Administrativos,Sucos no Aldeias.....	3
<i>Tabela 2.1: Força de Trabalho ADN, I.P Município Manufahi.</i>	<i>3</i>
<i>Tabela 3.2 : Lista Asset ADN,I.P Município Manufahi.</i>	<i>4</i>
<i>Tabela 4.3.1 :Projecto Município Manufahi Por Fundus Financiamento.....</i>	<i>5</i>
<i>Tabela 5.3.2 : Projecto Município Por Sector</i>	<i>9</i>
<i>Tabela 6.3.3 : Projecto Município Por Ministério</i>	<i>14</i>

I. INTRODUSAUN.

1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu aseguza katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefísiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projektu sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liuhusi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Manufahi



Mapa 2 hatudu pozisaun jeográfika Administrasaun Munisipal Manufahi iha luan 1,325 km² ho populasan nain 48,628 tuir Sensus 2010. Administrasaun Munisipal Manufahi iha Postos Administrativos ha'at, Sukus 29 no aldeias 137, mak hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos,Sucos no Aldeias.

Alas		Fatuberlio		Same		Turiscail	
Sukus	Aldeias	Sukus	Aldeias	Sukus	T.Aldeias	Sukus	Aldeias
Aituha	2	Bubussuso	5	Babulo	8	Aitemua	2
Dotic	3	FAtukahil	5	Betano	7	Beremana	3
Mahaquidan	5	Caicassa	4	Dai-sua	5	Fatucalo	2
Taitudac	5	Clauc	5	Grotu	3	Foholau	3
Uma berloic	4	Fahinehan	4	Holarua	13	Caimauc	5
-	-	-	-	Letefoho	7	Lessuata	4
Total	19	-	23	-	43	-	19

Data husi: Livro 3 B OJE 2021, pag 75

Tabela 2.1: Forca de Trabalho ADN, I.P Municipio Manufahi.

Forca de Trabalho ADN,I.P Municipio Manufahi/ Same								
No	Deskrisaun	Total Membros Kada Tinan						OBS
		2021	2022	2023	2024	2025	Total	
1	Engineiro	2					2	
2	Administrasaun no Financas	0					0	
3	Motorista	1					1	
4	Seguransa	0					0	
Total		3					3	

Tabela 3.2 : Lista Asset ADN,I.P Municipio Manufahi.

ASET ADN,IP MUNICIPIO MANUFAHI								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1						
2	Kareta	1						
3	Desktop HP / Monitor	1						
4	Laptop HP	1						
5	Printer Cannon	1						
6	UPS	1						
7	Armario File	2						At ona
8	Armario Tau hena	3						1 at ona
9	Meja escritorio	1						
10	Meja han	1						
11	Meja TV (kiik)	1						
12	Kadeira escritorio	6						
13	Kadeira han	4						
14	Sofa	1 Set						
15	Springbed +sumasu 4+sprei 3	3 Set						
16	Jeleira	1						
17	Water Dispenser	1						At ona
18	TV + Parabola	1 Set						Parabola La funciona
19	Kipas Angin	4						
20	Kompor	1						At ona
21	Kompor Gas	1						At ona
22	Rack sepatu	3						
23	Rack Piring	1						
24	Lampu	11						

25	Water Pump Sanyo	1						
----	------------------	---	--	--	--	--	--	--

1.3. Lista Projecto

Projetu hotu neébe akumula iha lista neé bazeia ba dados projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamto, tabela 1.3.2 Projetu por Sector no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabela 4.3.1 :Projecto Municipio Manufahi Por Fundus Finansiamto

NO	POSTO ADMINISTRATIVO	TOTAL FI		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	6	\$ 3,314,853.37	58.78%
2	Fatuberliu	4	\$ 5,712,801.12	65.00%
3	Same	8	\$ 3,375,484.71	78.05%
4	Turiscail	3	\$ 4,690,158.04	77.78%
	Grand Total	21	\$ 17,093,297.24	69.88%

NO	POSTO ADMINISTRATIVO	TOTAL LM Covid 19		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas			
2	Fatuberliu			
3	Same	3	\$ 383,412.81	66.73%
4	Turiscail			
Grand Total		3	\$ 383,412.81	66.73%

NO	POSTO ADMINISTRATIVO	TOTAL LM BS		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	2	\$ 587,548.52	66.20%
2	Fatuberliu			
3	Same	2	\$ 306,911.16	59.01%
4	Turiscail	1	\$ 570,200.00	70.00%
Grand Total		5	\$ 1,464,659.68	66.17%

NO	POSTO ADMINISTRATIVO	TOTAL LM CD		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	4	\$ 766,506.99	67.86%
2	Fatuberliu	5	\$ 1,318,810.35	43.01%
3	Same	9	\$ 605,811.31	49.14%
4	Turiscari			
	Grand Total	18	\$ 2,691,128.65	51.47%

c	POSTO ADMINISTRATIVO	TOTAL TRANSFERENCIA PUBLICO		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	3	\$ 329,649.24	0.00%
2	Fatuberliu	1	\$ 194,674.39	0.00%
3	Same	11	\$ 1,062,554.76	0.00%
4	Turiscari			
	Grand Total	15	\$ 1,586,878.39	0.00%

c	POSTO ADMINISTRATIVO	TOTAL PDID		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	1	\$ 269,482.11	14.96%
2	Fatuberliu			
3	Same	5	\$ 928,527.70	87.17%
4	Turiscail	1	\$ 7,530.00	69.97%
	Grand Total	7	\$ 1,205,539.81	70.92%

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM BS+CD+Covid19 + TP+PDID		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	16	\$ 5,268,040.23	55.01%
2	Fatuberliu	10	\$ 7,226,285.86	59.24%
3	Same	38	\$ 6,662,702.45	62.71%
4	Turiscail	5	\$ 5,267,888.04	76.93%
	Grand Total	69	\$ 24,424,916.58	63.09%

Dadus detallu kada projetu: #Anexu

Tabela 5.3.2 : Projecto Municipio Por Sector

NO	SECTOR PROJECTO	Alas		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO	2	\$ 299,631.00	50.63%
2	Basic Road Construction			
3	EDIFICIOS PUBLICOS			
4	EDUKASAUN	3	\$ 329,649.24	0.00%
5	ELETRIFIKASAUN NASIONAL	1	\$ 1,108,760.78	78.57%
6	ESTRADAS	6	\$ 2,354,740.57	49.95%
7	FLOOD CONTROL	1	\$ 269,482.11	14.96%
8	JUVENTUDE NO DESPORTU			
9	MANUTENSAUN NO REHABILITASAUN	3	\$ 905,776.53	72.70%
10	PONTES			
11	SAUDE			
12	SEGURANCA NO DEFESA			
13	SOLIDARIEDADE E SOCIAL			
14	TURISMO			
	Grand Total	16	\$ 5,268,040.23	55.01%

NO	SECTOR PROJECTO	Fatuberliu		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO			
2	Basic Road Construction			
3	EDIFICIOS PUBLICOS			
4	EDUKASAUN	1	\$ 194,674.39	0.00%
5	ELETRIFIKASAUN NASIONAL	1	\$ 806,642.49	81.00%
6	ESTRADAS	8	\$ 6,224,968.98	58.27%
7	FLOOD CONTROL			
8	JUVENTUDE NO DESPORTU			
9	MANUTENSAUN NO REHABILITASAUN			
10	PONTES			
11	SAUDE			
12	SEGURANCA NO DEFESA			
13	SOLIDARIEDADE E SOCIAL			
14	TURISMO			
	Grand Total	10	\$ 7,226,285.86	59.24%

N O	SECTOR PROYECTO	Same		
		TOTAL PROJECT O	MONTANTE KONTRATU (\$)	PERSENTAGE M EXECUSAUN (%)
1	AGUA E SANEAMENTO	2	\$ 137,426.79	20.08%
2	Basic Road Construction	1	\$ -	
3	EDIFICIOS PUBLICOS	3	\$ 610,160.22	65.14%
4	EDUKASAUN	11	\$ 1,062,554.76	0.00%
5	ELETRIFIKASAUN NASIONAL	3	\$ 1,738,584.93	85.12%
6	ESTRADAS	5	\$ 633,432.36	67.85%
7	FLOOD CONTROL			
8	JUVENTUDE NO DESPORTU	1	\$ 23,697.55	80.24%
9	MANUTENSAUN NO REHABILITASAUN	5	\$ 1,153,984.05	78.04%
10	PONTES	1	\$ 328,755.98	46.54%
11	SAUDE	2	\$ 312,000.61	82.01%
12	SEGURANCA NO DEFESA	1	\$ 76,149.37	0.00%
13	SOLIDARIEDADE E SOCIAL	2	\$ 536,957.37	95.96%
14	TURISMO	1	\$ 48,998.46	0.00%
	Grand Total	38	\$ 6,662,702.45	62.71%

N O	SECTOR PROJECTO	Turiscail		
		TOTAL PROJECT O	MONTANTE KONTRATU (\$)	PERSENTAGE M EXECUSAUN (%)
1	AGUA E SANEAMENTO	1	\$ 7,530.00	69.97%
2	Basic Road Construction			
3	EDIFICIOS PUBLICOS			
4	EDUKASAUN			
5	ELETRIFIKASAUN NASIONAL			
6	ESTRADAS	2	\$ 3,983,240.53	78.01%
7	FLOOD CONTROL			
8	JUVENTUDE NO DESPORTU			
9	MANUTENSAUN NO REHABILITASAUN	2	\$ 1,277,117.51	73.59%
10	PONTES			
11	SAUDE			
12	SEGURANCA NO DEFESA			
13	SOLIDARIEDADE E SOCIAL			
14	TURISMO			
	Grand Total	5	\$ 5,267,888.04	76.93%

N O	SECTOR PROYECTO	TOTAL MUNICIPIO MANUFAHI		
		TOTAL PROYECTO	MONTANTE KONTRATU (\$)	PERSENTAGE M EXECUSAUN (%)
1	AGUA E SANEAMENTO	5	\$ 444,587.79	41.52%
2	Basic Road Construction	1	\$ -	
3	EDIFICIOS PUBLICOS	3	\$ 610,160.22	65.14%
4	EDUKASAUN	15	\$ 1,586,878.39	0.00%
5	ELETRIFIKASAUN NASIONAL	5	\$ 3,653,988.20	82.22%
6	ESTRADAS	21	\$ 13,196,382.44	63.21%
7	FLOOD CONTROL	1	\$ 269,482.11	14.96%
8	JUVENTUDE NO DESPORTU	1	\$ 23,697.55	80.24%
9	MANUTENSAUN NO REHABILITASAUN	10	\$ 3,336,878.09	74.89%
10	PONTES	1	\$ 328,755.98	46.54%
11	SAUDE	2	\$ 312,000.61	82.01%
12	SEGURANCA NO DEFESA	1	\$ 76,149.37	0.00%
13	SOLIDARIEDADE E SOCIAL	2	\$ 536,957.37	95.96%
14	TURISMO	1	\$ 48,998.46	0.00%
	Grand Total	69	\$ 24,424,916.58	63.09%

Dadus detallu kada projetu: #Anexu A

Tabela 6.3.3 : Projecto Municipio Por Ministerio

NO	DONO DO PROJECTO	Alas		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ESTATAL			
2	MINISTERIO DA SAUDE			
3	MINISTERIO DAS OBRAS PUBLICAS	13	\$ 4,938,390.99	58.68%
4	MINISTERIO DO INTERIOR			
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	\$ 329,649.24	0.00%
6	MINISTERIO SAUDE			
7	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
8	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
	Grand Total	16	\$ 5,268,040.23	55.01%

NO	DONO DO PROJECTO	Fatuberliu		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSNTAGEM EXECUSAUN (%)
1	ESTATAL			
2	MINISTERIO DA SAUDE			
3	MINISTERIO DAS OBRAS PUBLICAS	9	\$ 7,031,611.47	60.88%
4	MINISTERIO DO INTERIOR			
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 194,674.39	0.00%
6	MINISTERIO SAUDE			
7	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
8	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
	Grand Total	10	\$ 7,226,285.86	59.24%

NO	DONO DO PROJECTO	Same		
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ESTATAL	4	\$ 568,413.14	95.05%
2	MINISTERIO DA SAUDE	2	\$ 312,000.61	82.01%
3	MINISTERIO DAS OBRAS PUBLICAS	16	\$ 3,984,425.89	74.91%
4	MINISTERIO DO INTERIOR	2	\$ 436,263.93	61.68%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	11	\$ 1,062,554.76	0.00%
6	MINISTERIO SAUDE	1	\$ 71,412.20	0.00%
7	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	\$ 178,633.46	71.88%
8	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 48,998.46	0.00%
	Grand Total	38	\$ 6,662,702.45	62.71%

NO	DONO DO PROJECTO	Turiscai		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ESTATAL	1	\$ 7,530.00	69.97%
2	MINISTERIO DA SAUDE			
3	MINISTERIO DAS OBRAS PUBLICAS	4	\$ 5,260,358.04	76.94%
4	MINISTERIO DO INTERIOR			
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
6	MINISTERIO SAUDE			
7	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
8	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
	Grand Total	5	\$ 5,267,888.04	76.93%

NO	DONO DO PROJECTO	TOTAL MUNICIPIO MANUFAHI		
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ESTATAL	5	\$ 575,943.14	94.73%
2	MINISTERIO DA SAUDE	2	\$ 312,000.61	82.01%
3	MINISTERIO DAS OBRAS PUBLICAS	42	\$ 21,214,786.39	66.99%
4	MINISTERIO DO INTERIOR	2	\$ 436,263.93	61.68%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	15	\$ 1,586,878.39	0.00%
6	MINISTERIO SAUDE	1	\$ 71,412.20	0.00%
7	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	\$ 178,633.46	71.88%
8	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 48,998.46	0.00%
	Grand Total	69	\$ 24,424,916.58	63.09%

Dadus detallu kada projetu: #Anexu A

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan ne'e hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu katak progresu actual fulan ida ne'e siknifika porsentagen servisu ne'ebe atinje deit iha fulan ne'e nia laran, montante actual fulan ida ne'e bazeia ba orsamentu ne'ebe hetan husi progresu fulan ida ne'e nia rasik no ikus porsentagen actual fulan ida ne'e hatudu progresu fisiku komulativu ne'ebe akumulula husi porsento anterior no fulan ida ne'e nian, kompletu ba detallu bele haree iha #Anexu B, detallu ba Back-Up #Anexu C no Fotografia bele hare #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

Obstaklu sira ne'ebé ma ami hasoru iha munisipiu Manufahi durante hala'o monitorizasaun no inspesaun projetu sira mak hanesan:

1. Transporte ida de'it difikulta ami atu hala'o inspesaun banhra iha pedidu pagamentu tamba seksaun Ponte Estrada mos presija halo monitorizasaun hodi atinji kuantidade de monitorizasaun
2. Linha internet fraku tamba ne'e maske ami atualiza progresu projetu kada loron mos unidade baze de dados nafatin la hetan dados hafoin semana rua ba leten. Ho difikulade ne'e unidade seksaun halo ami atraplla. Tamba ne'e maske ami iha munisipiu atualiza bebeik maibe laiha efisiensia no bele hamosu deskonfia katak engenheiru munisipiu la halo atualizasaun progresu projetu sira
3. Iha parte **instrusaun serbisu**, munisipiu halo "*tribe*" so pra aumenta volume serbsu de'it maibe fungsaun ida de'it.
4. Bainhira iha pedidu pagamentu, susar mai ami atu atinji kuantidade inspesaun
5. Susar ba seksaun Edifício Público, Agua e Saneamento (EPAS) atu atualiza progresu fiziku kada semana bainhira iha pedidu pagamentu tamba preukupa ho inspesaun pagamentu no prepara rekomendasaun pagamentu
6. Susar ba enjineru munisipiu atu atualiza progresu serbsu eletrisidade tamba responsabilidade enjineru munisipiu de'it mos susar atu finaliza

➤ **Obstaclo parte Eletricidade**

1. Durante halo monitorizasaun ba projeto neébe mak mensiona iha lista projektu Eng. M & E, ADN – I.P, la hasoru kontraktor sira tamba televomel fora da area hotu.
2. Eng. M & E, ADN – I.P, nunka hasoru tekniku husi kompania no parte kompania sempre delega tekniku neébe ba hein iha terenu, maibe tekniku neé rasik laiha konesimentu klean ho orbra refere.
3. Seksaun M & E, AND – I.P, labele kontrola projeto ho maximu tamba Eng. M & E ida hodi

kontrola Projeto Linha Electricidade ho Edifisio Publik Iha Municipio Ha'at (4).
4. Projeto eletricidade barak maka espasu ba lina laiha ona, hodi kompanha sira mos la halo servisu kontinuasaun.
5. Motorista menus difikulta ami nia servisu.

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Buka solusaun lalais ba projektu sira ne'ebé abandona ho projektu na'in se la'e engenheiru munisipiu ninia relatoriu laiha rejultadu no projektu sira sei continua abandona
2. Aumenta transporte nune'e bele facilita hala'o inspesaun
3. Diminui tiha parte instrusaun serbisu tamba enjinheru munisipiu halo "*tribe*" hodi aumenta volume serbsu maibe fungsaun ida de'it.

➤ **Recomendação parte Eletricidade**

1. Husu ba parte ITC, ADN – I.P bele kria Folder Sistem ba Seksaun M & E, ADN – I.P.
2. Husu atu aumenta tan rekursu iha Seksaun M & E, ADN – I.P

Note: Asinatura husi Eng Municipio Manufahi

Força de Trabalho ADN, I.P Municipio Manufahi

No	Deskrisaun	Identidade				
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	Asinatura
1	Engineiro	Fidelis Mardiano da Costa		Enjineiru EPAS		
		Romulo J.M Henrique		Enjineiru ITI		
		Johanes Hornay	011	Enjineiro VEBD		
		Silvino D. R. R. Soares		Enjineiru METIC		
2	Motorista	Silveiro da Costa		Motorista		

LISTA GERAL

ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAU N NASIONAL	Alas	Manufahi	Samboio Unip,Lda	DTL/MOP-SEE/CGI-PEN : 00001	\$ 1,108,760.78	Feb. 10, 2013	100.00%	78.57%	\$ 871,110.32	\$ 237,650.46	ON-GOING
2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consorcio Nacional Manufahi Lda	SSS/148/MOPTC-2017	\$ 553,599.46	Sept. 14, 2017	8.61%	7.75%	\$ 42,899.98	\$ 510,699.48	ON-GOING
3	Emergency new construction of gabion box protection random fill in area Lacro, Baria Laran, Uma Berloik, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consorcio 1912 MF Lda	SSS/279/MOPTC-2016	\$ 440,564.46	Oct. 27, 2016	100.00%	78.96%	\$ 347,876.05	\$ 92,688.41	ON-GOING
4	Rural Roads Routine Maintenance Dootic Weberek, Chainage 0+000 - 6+300, Dootic Wekakaoan, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAU N	Alas	Manufahi	Samboio Unip,Lda	MPW-RFQ-190017	\$ 71,803.67	Jan. 8, 2019	68.44%	61.60%	\$ 44,230.62	\$ 27,573.05	ON-GOING
5	Prefurasun Be'e mos iha Suku Uma Berloik, Aldeia Besusu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Alas	Manufahi	Buka Fini	MPWTC-NCB-170008	\$ 112,392.00	Aug. 16, 2017	100.00%	90.00%	\$ 101,152.80	\$ 11,239.20	ON-GOING
6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	\$ 269,482.11	Oct. 7, 2019	86.82%	14.96%	\$ 40,316.95	\$ 229,165.16	ON-GOING
7	Kontinuasaun Kanalizasaun Kanu Transmisau no Distribuisau Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Alas	Manufahi	Tane Unipessoal Lda	MOP - W - 190210	\$ 187,239.00	Nov. 21, 2019	30.00%	27.00%	\$ 50,554.31	\$ 136,684.69	ON-GOING
8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Alas	Manufahi	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	\$ 523,300.00	April 21, 2021	68.58%	68.58%	\$ 358,882.28	\$ 164,417.72	ON-GOING
9	Construction and Installation water Gravitation System in Mahaquidam Umerloic Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAU N	Alas	Manufahi	Verescar Unip. Lda	SSS/289/MOPTC-2016	\$ 499,455.17	Nov. 8, 2016	96.39%	78.70%	\$ 393,055.29	\$ 106,399.88	ON-GOING
10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Alas	Manufahi	My Friend Unip. Lda	MPW-W-190106	\$ 400,309.52	Nov. 5, 2020	99.66%	84.53%	\$ 338,396.26	\$ 61,913.26	ON-GOING
11	Rehabilitasaun Estrada Tekunu-Feriksare 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAU N	Alas	Manufahi	Aplayana unip. Lda	RT/062/MOPTC-2016	\$ 334,517.69	Aug. 3, 2016	80.00%	66.13%	\$ 221,221.39	\$ 113,296.30	ON-GOING
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consorcio Unimafa Lda	SSS/150/MOPTC-2017	\$ 377,955.81	Sept. 14, 2017	21.28%	19.15%	\$ 72,370.68	\$ 305,585.13	ON-GOING
13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaoan Chainage 0+000 - 8+600 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Alas	Manufahi	Werenek Unipessoal Lda	MPW-W-210093	\$ 59,011.32	July 23, 2021	58.58%	7.97%	\$ 15,884.54	\$ 415,568.18	ON-GOING
14	Konstrusaun ka rehabilitasaun ba EBC Mahaquidan	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBC MAHAQUIDAN	Kontratu ho Grupo Comunitariu	\$ 111,814.16	Oct. 15, 2021	4.92%	0.00%			
15	Konstrusaun ka rehabilitasaun ba EBF Bercoban	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF BERCOBAN	Kontratu ho Grupo Comunitariu	\$ 101,086.58	Oct. 15, 2022	4.80%	0.00%			
16	Konstrusaun ka rehabilitasaun ba EBF Manus	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF MANUS	Kontratu ho Grupo Comunitariu	\$ 116,748.50	Oct. 15, 2023	5.24%	0.00%			
17	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	\$ 451,569.10	Sept. 14, 2017	8.86%	7.97%	\$ 36,000.92	\$ 415,568.18	ON-GOING
18	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	concorcio Nacional ba Futuro	SSS/149/MOPTC-2017	\$ 468,687.16	Sept. 14, 2017	24.29%	21.86%	\$ 102,464.15	\$ 366,223.01	ON-GOING
19	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAU N NASIONAL	Fatuberliu	Manufahi	Funu Kolik Unip. Lda	MOPTC-VMOPTC/CGI-PEN : 00	\$ 806,642.49	Sept. 1, 2016	90.00%	81.00%	\$ 653,364.09	\$ 153,278.40	Abandon
20	New Construction of Sukaer Oan River cyclop Concrete Reteining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	Consorcio Nacional Samdil, Lda (CNS)	SSS/102/MOPTC-2017	\$ 3,985,902.37	Sept. 7, 2017	87.83%	73.30%	\$ 2,921,736.56	\$ 1,064,165.81	ON-GOING
21	R4D Rural Road Routine Maintenance, Tukunu Feriksare Chainage 0+000-6+350 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	MARDIROMIG VIQSAM, UNIPESSOAL LDA	MPW- W - 210096	\$ 27,105.00	July 23, 2021	24.97%	11.92%	\$ 3,230.33	\$ 23,874.67	ON-GOING
22	R4d Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Loskabubu	MPW-W-210099	\$ 337,115.79	July 23, 2021	78.81%	52.82%	\$ 178,069.50	\$ 159,046.29	ON-GOING
23	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Leo-Hilin Unipessoal Lda	MPW-W-210095	\$ 124,043.34	July 23, 2021	32.92%	29.63%	\$ 36,752.99	\$ 87,290.35	ON-GOING

LISTA GERAL

ANEXO A

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
24	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainag	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Alifa Pereira	MPW-W-210097	\$ 421,729.47	July 23, 2021	26.43%	23.79%	\$ 100,324.33	\$ 321,405.14	ON-GOING
25	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	\$ 408,816.75	July 23, 2021	64.99%	60.88%	\$ 248,885.92	\$ 159,930.83	ON-GOING
26	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Fatuberliu	Manufahi	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		194,674.39						
27	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAU N NASIONAL	Same	Manufahi	Dhalelan,Unip.Lda	/MOPTC-VOMPTC/CGI-PEN:00	\$ 88,665.83	March 25, 2015	100.00%	90.00%	\$ 79,799.25	\$ 8,866.58	PHO
28	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAU N NASIONAL	Same	Manufahi	Dediva Electrical Unip, Lda	MOPTC-VMOPTC/CGI-PEN : 00	\$ 921,673.84	July 6, 2016	96.00%	86.81%	\$ 800,071.34	\$ 121,602.50	ON-GOING
29	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAU N NASIONAL	Same	Manufahi	Fahlia Humalo Unip.Lda	MOPTC-VMOPTC/CGI-PEN : 00	\$ 728,245.26	Sept. 1, 2016	92.00%	82.38%	\$ 599,930.07	\$ 128,315.19	ON-GOING
30	Konstrusaun kanalizasaun bee mos iha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Same	Manufahi	Haksolok Java Motor Unip Lda	MOP - W - 190160	\$ 129,668.57	Dec. 1, 2019	18.50%	16.65%	\$ 21,593.56	\$ 108,075.01	ON-GOING
31	Nova fornecimento água do Bairro PNTL Manufahi	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	Same	Manufahi	Tom's Building Uipessoal Lda	SSS/053/MI-2017	\$ 76,149.37	Nov. 29, 2019	24.55%	0.00%	\$ -	\$ 76,149.37	ON-GOING
32	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Same	Manufahi	Consortorio Cablaki Oan Lda	SSS/270/MOPTC-2016	\$ 363,040.25	Oct. 19, 2016	100.00%	95.38%	\$ 346,267.25	\$ 16,773.00	ON-GOING
33	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Same	Manufahi	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	\$ 328,755.98	July 26, 2016	63.00%	46.54%	\$ 153,014.54	\$ 175,741.44	ON-GOING
34	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAU N	Same	Manufahi	El Const Unip. Lda	NCB/063/MOPTC-2016	\$ 700,656.46	Aug. 4, 2016	98.93%	89.16%	\$ 624,740.20	\$ 75,916.26	ON-GOING
35	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAU N	Same	Manufahi	Aplayana unip. Lda	RT/057/MOPTC-2016	\$ 168,297.72	Aug. 3, 2016	30.00%	18.17%	\$ 30,575.14	\$ 137,722.58	Abandon
36	Road Maintenance Section Same Urban Roads Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Renova Unip Lda	MPW - W - 190215	\$ 87,929.19	Dec. 2, 2019	71.88%	64.69%	\$ 56,880.06	\$ 31,049.13	ON-GOING
37	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAU N	Same	Manufahi	Quintas das Flores, Lda	MPW - W - 190123	\$ 177,242.59	June 10, 2019	100.00%	90.00%	\$ 159,518.18	\$ 17,724.41	PHO
38	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAU N	Same	Manufahi	Alifa Pereira	MPW -RFQ 190019	\$ 59,446.75	Aug. 1, 2019	90.13%	81.12%	\$ 48,222.09	\$ 11,224.66	ON-GOING
39	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAU N	Same	Manufahi	Leo - Dok	MPWTC-CD-170002	\$ 48,340.53	Jan. 8, 2019	86.31%	77.68%	\$ 37,549.81	\$ 10,790.72	ON-GOING
40	Fencing for Construction Monumento do Dom Boa Ventura	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-CD	EDIFICIOS PUBLICOS	Same	Manufahi	Loskabubu	RDTL/06/GM-MTAC/IV/2016	\$ 178,633.46	June 9, 2015	79.86%	71.88%	\$ 128,395.45	\$ 50,238.01	Abandon
41	Konstrusaun Tangki Beé no Menara Beé ba iha Edificio Administrasaun Municipiu Manufahi	ESTATAL	PDIM	AGUA E SANEAMENTO	Same	Manufahi	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	\$ 7,758.22	April 10, 2017	85.99%	77.39%	\$ 6,004.37	\$ 1,753.85	Abandon
42	Konstrusaun Kuartel Bombeiros iha Same-Manufahi	MINISTERIO DO INTERIOR	PDIM	EDIFICIOS PUBLICOS	Same	Manufahi	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	\$ 360,114.56	Aug. 19, 2016	83.02%	74.72%	\$ 269,076.60	\$ 91,037.96	Abandon
43	Renovasi gereja paroquia nossa senhora assuncao same	ESTATAL	PDIM	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	\$ 438,905.72	Aug. 7, 2017	98.81%	98.81%	\$ 433,699.77	\$ 5,205.95	FHO
44	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	ESTATAL	PDIM	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Consortorio Deatle Hare ba Oin Lda	07/PDIM/M-MF/IX/2019	\$ 98,051.65	Sept. 9, 2019	92.45%	83.20%	\$ 81,582.62	\$ 16,469.03	ON-GOING
45	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutur Bodik Tane Lisuk, Unip.Lda	ESTATAL	PDIM	JUVENTUDE NO DESPORTU	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	09/PDIM/M-MF/X/2019	\$ 23,697.55	Oct. 7, 2019	89.15%	80.24%	\$ 19,014.76	\$ 4,682.79	PHO
46	Konstrusaun Fatin isolamentu iha Municipio Manufahi, Timor Leste	MINISTERIO DA SAUDE	Fundo Covid-19	SAUDE	Same	Manufahi	Daloveya	RDTL-MS-DNA-DC-20-256	\$ 293,664.88	Sept. 12, 2020	98.65%	87.13%	\$ 255,869.88	\$ 37,795.00	ON-GOING
47	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Haut-Dairam Unipessoal Lda	MPW-W210092	\$ 46,754.63	July 23, 2021	44.37%	35.41%	\$ 16,554.11	\$ 30,200.52	ON-GOING

LISTA GERAL

ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
48	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Riabile Unipessoal Lda	MPW-W-210091	\$ 52,112.72	July 23, 2021	21.47%	19.39%	\$ 10,105.69	\$ 42,007.03	ON-GOING
49	New Construction of Laboratory ih CSI Luak, Manufahi relasiona ba covid19 at Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Same	Manufahi	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	\$ 71,412.20	Aug. 17, 2021	64.31%	11.67%	\$ 8,336.40	\$ 63,075.80	ON-GOING
50	Para A Construccao De Jardim De Herois De Manufahi (New Construction Of Campas, Gate And Leveling)	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTACAO NACIONAL	LM-CD	TURISMO	Same	Manufahi	My friend Constr. Unip. Lda	FQ No. 23/MACLN/DNAL/VI/202	\$ 48,998.46	Sept. 1, 2021	37.20%	0.00%		\$ 48,998.46	ON-GOING
51	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	MPW - W -210094	\$ 83,595.57	July 23, 2021	71.35%	0.00%		\$ 83,595.57	ON-GOING
52	Konstrusaun ka rehabilitasaun ba EBF Tefo	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF TEFO	Kontratu ho Grupo Comunitariu	\$ 99,986.68		5.06%				ON-GOING
53	Konstrusaun ka rehabilitasaun ba EBC Diligencia	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC DILIGENCIA	Kontratu ho Grupo Comunitariu	\$ 110,951.20		18.26%				ON-GOING
54	Konstrusaun ka rehabilitasaun ba EPE Turon	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE TURON	Kontratu ho Grupo Comunitariu	\$ 83,083.31		16.43%				ON-GOING
55	Konstrusaun ka rehabilitasaun ba EPE Domingos Savio Grotu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE DOMINGOS SAVIO	Kontratu ho Grupo Comunitariu	\$ 85,513.28		15.73%				ON-GOING
56	Konstrusaun ka rehabilitasaun ba EBF Silihasan	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF SILIHASAN	Kontratu ho Grupo Comunitariu	\$ 111,801.61		19.94%				ON-GOING
57	Konstrusaun ka rehabilitasaun ba EBF hatsana udo/Dai-sua Lama	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF HATSANA UDO / DAI-SUA LAMA	Kontratu ho Grupo Comunitariu	\$ 101,427.27		9.97%				ON-GOING
58	Konstrusaun ka rehabilitasaun ba EBF Blaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF BLARO	Kontratu ho Grupo Comunitariu	\$ 113,831.28		5.99%				ON-GOING
59	Konstrusaun ka rehabilitasaun ba EBF Rotuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF ROTUTO	Kontratu ho Grupo Comunitariu	\$ 71,892.87		18.58%				ON-GOING
60	Konstrusaun ka rehabilitasaun ba EBC Fatuco	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC FATUCO	Kontratu ho Grupo Comunitariu	\$ 10,986.63		22.48%				ON-GOING
61	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	\$ 140,614.24		18.78%				ON-GOING
62	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	\$ 132,466.39		15.51%				ON-GOING
63	New Construction Building for Central Electrical in Luak Manufahi, Ministry of Health Timor Leste	MINISTERIO DA SAUDE	Fundo Covid-19	SAUDE	Same	Manufahi	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-22-006	\$ 18,335.73		0.00%				ON-GOING
64	For Road Maintanance Section Jct Aituto-Same-Betano 23Km(A04)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Basic Road Constructi	Same	Manufahi	0.00%	MPW-W-220007	131,893.81						ON-GOING
65	Open New Road Turiscai - Mota Belihun Maubere, Turiscai - Liquidoe Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Turiscai	Manufahi	Aldepo Murak Unip.Lda	SSS/250/MOPTC-2016	\$ 3,413,040.53	Sept. 4, 2017	93.90%	79.35%	\$ 2,708,287.08	\$ 704,753.45	ON-GOING
66	Const. MCK (Saude) Orana	ESTATAL	PDIM	AGUA E SANEAMENTO	turiscai	Manufahi	Gersaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	\$ 7,530.00	May 23, 2019	75.00%	69.97%	\$ 5,268.79	\$ 2,261.21	ON-GOING
67	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railaco, Sanfuk, Tutu Luro - Same Fahi Nehan (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	turiscai	Manufahi	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	\$ 570,200.00	March 25, 2020	70.00%	70.00%	\$ 399,140.00	\$ 171,060.00	ON-GOING

LISTA GERAL

ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
68	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAU N	turiscas	Manufahi	Terra Livre Unip. Lda	SSS/299/MOPTC-2016	\$ 478,217.51	Nov. 23, 2016	90.44%	79.59%	\$ 380,612.95	\$ 97,604.56	PHO
69	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 4 : Turiscas to Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAU N	turiscas	Manufahi	Wan Husin Associates SDN. BHD. Jv Consultant & Engineering Intercontinental Unip. Lda	RT/031/MOP-2019	\$ 798,900.00	March 25, 2020	70.00%	70.00%	\$ 559,230.00	\$ 239,670.00	ON-GOING

Inspected by :



Eng. Romulo J.M Henrique
 Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio Manufahi A D N IP

Inspected by :



Eng. Fidelis Mardiano da Costa
 Engenheiro Edificio Public, Agua e Saneamento A D N IP

Inspected by :



Eng. Silvino D. R. R. Soares
 Engenheiro M&E, A D N IP

Certified by :



Eng. Emerenciana da Costa Maia Freitas
 Coordenadora da Unidade de controlu e validacao qualidade ADN.I.P

Verified by :



Eng. Remigio da C. S. dos Santos
 Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Verified by :



Arch. Francisco Xavier de D Jeronimo
 Engenheiro Senior da Edificio Public no Agua

Verified by :



Eng. Deolindo de Fatima Marques
 Chefe Sec.Proj. ME & ITC, A D N IP

LISTA GERAL ANEXO B
PROGRES MAIO 2022

NU.	NARAN PROJETO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 27 May 2022			OBSERVASAUN
						previous	this prog	% actual prog	
1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	Samboio Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	\$ 1,108,760.78	Feb. 10, 2013	100.00%	0.00%	100.00%	ON-GOING
2	Emergency proposed for the new constructioin of bridge box protection with retaining wall in Area Wee Kakau Oan 2	Consortio Nacional Manufahi Lda	SSS/148/MOPTC-2017	\$ 553,599.46	Sept. 14, 2017	8.61%	0.00%	8.61%	ON-GOING
3	Emergency new construction of gabion box protection random fill in area Lacro, Baria Laran, Uma Berloik, Alas	Consortio 1912 MF Lda	SSS/279/MOPTC-2016	\$ 440,564.46	Oct. 27, 2016	100.00%	0.00%	100.00%	ON-GOING
4	Rural Roads Routine Maintenance Dootic Weberek, Chainage 0+000 - 6+300, Dootic Wekakaoan, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi (162)	Samboio Unip,Lda	MPW-RFQ-190017	\$ 71,803.67	Jan. 8, 2019	68.44%	0.00%	68.44%	ON-GOING
5	Prefurasaun Be'e mos iha Suku Uma Berloik, Aldeia Besusu	Buka Fini	MPWTC-NCB-170008	\$ 112,392.00	Aug. 16, 2017	100.00%		100.00%	ON-GOING
6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	\$ 269,482.11	Oct. 7, 2019	86.82%		86.82%	ON-GOING
7	Kontinuasaun Kanalizasaun Kanu Transmisaun no Distribuisaun Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	Tane Unipessoal Lda	MOP - W - 190210	\$ 187,239.00	Nov. 21, 2019	30.00%		30.00%	ON-GOING
8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	\$ 523,300.00	April 21, 2021	68.58%		68.58%	ON-GOING
9	Construction and Installation water Gravitation System in Mahaquidam Umberloic Manufahi Municipality	Verescar Unip. Lda	SSS/289/MOPTC-2016	\$ 499,455.17	Nov. 8, 2016	89.96%		89.96%	ON-GOING
10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	My Friend Unip. Lda	MPW-W-190106	\$ 400,309.52	Nov. 5, 2020	99.66%	0.00%	99.66%	ON-GOING
11	Rehabilitasaun Estrada Tekunu-Feriksale 2 Sta. 2+500-4+250-Municipal of Same	Aplayana unip. Lda	RT/062/MOPTC-2016	\$ 334,517.69	Aug. 3, 2016	80.00%	0.00%	80.00%	ON-GOING
12	New construction of bridge with retaining wall in area we bikas	Consortio Unimafa Lda	SSS/150/MOPTC-2017	\$ 377,955.81	Sept. 14, 2017	21.28%	0.00%	21.28%	ON-GOING
13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaoan Chainage 0+000 - 8+600 Municipality Manufahi	Wereneq Unipessoal Lda	MPW-W-210093	\$ 59,011.32	July 23, 2021	58.58%	0.00%	58.58%	ON-GOING
14	Konstrusaun ka rehabilitasaun ba EBC Mahaquidan	MEJD PKRIE EBC MAHAQUIDAN	Kontratu ho Grupo Comunitariu	\$ 111,814.16	Oct. 15, 2021	0.00%	4.92%	4.92%	
15	Konstrusaun ka rehabilitasaun ba EBF Bercoban	MEJD PKRIE EBF BERCOBAN	Kontratu ho Grupo Comunitariu	\$ 101,086.58	Oct. 15, 2022	0.00%	4.80%	4.80%	
16	Konstrusaun ka rehabilitasaun ba EBF Manus	MEJD PKRIE EBF MANUS	Kontratu ho Grupo Comunitariu	\$ 116,748.50	Oct. 15, 2023	0.00%	5.24%	5.24%	
17	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	\$ 451,569.10	Sept. 14, 2017	8.86%	0.00%	8.86%	ON-GOING
18	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	concorcio Nasional ba Futuro	SSS/149/MOPTC-2017	\$ 468,687.16	Sept. 14, 2017	24.29%	0.00%	24.29%	ON-GOING

LISTA GERAL ANEXO B
PROGRES MAIO 2022

NU.	NARAN PROJETO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 27 May 2022			OBSERVASAUN
						previous	this prog	% actual prog	
19	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	Funu Kolik Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424	\$ 806,642.49	Sept. 1, 2016	90.00%		90.00%	Abandon
20	New Construction of Sukaer Oan River cyclop Concrete Reteining Wall and Gabion	Consortio National Samdil, Lda (CNS)	SSS/102/MOPTC-2017	\$ 3,985,902.37	Sept. 7, 2017	87.83%	0.00%	87.83%	ON-GOING
21	R4D Rural Road Routine Maintenance, Tukununu Feriksare Chainage 0+000-6+350 Manufahi Municipality	MARDIROMIG VIQSAM, UNIPESOAL LDA	MPW- W - 210096	\$ 27,105.00	July 23, 2021	24.97%	0.00%	24.97%	ON-GOING
22	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	Loskabubu	MPW-W-210099	\$ 337,115.79	July 23, 2021	78.81%	0.00%	78.81%	ON-GOING
23	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	Leo-Hilin Unipessoal Lda	MPW-W-210095	\$ 124,043.34	July 23, 2021	32.92%	0.00%	32.92%	ON-GOING
24	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	Alifa Pereira	MPW-W-210097	\$ 421,729.47	July 23, 2021	26.43%	47.46%	73.89%	ON-GOING
25	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	\$ 408,816.75	July 23, 2021	64.99%	31.75%	96.74%	ON-GOING
26	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		\$ 88,665.83		6.81%	3.44%	10.24%	
27	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	Dhalelan,Unip.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000300	\$ 88,665.83	March 25, 2015	100.00%		100.00%	PHO
28	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	Dediva Electrical Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385	\$ 921,673.84	July 6, 2016	96.00%		96.00%	ON-GOING
29	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430	\$ 728,245.26	Sept. 1, 2016	92.00%		92.00%	ON-GOING
30	Konstrusaun kanalizasaun bee mos iha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	Haksolok Java Motor Unip Lda	MOP - W - 190160	\$ 129,668.57	Dec. 1, 2019	18.50%		18.50%	ON-GOING
31	Nova fornecimento água do Bairro PNTL Manufahi	Tom's Building Uipessoal Lda	SSS/053/MI-2017	\$ 76,149.37	Nov. 29, 2019	24.55%		24.55%	ON-GOING
32	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	Consortio Cablaki Oan Lda	SSS/270/MOPTC-2016	\$ 363,040.25	Oct. 19, 2016	100.00%	0.00%	100.00%	ON-GOING
33	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	\$ 328,755.98	July 26, 2016	50.00%	13.00%	63.00%	ON-GOING
34	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	El Const Unip. Lda	NCB/063/MOPTC-2016	\$ 700,656.46	Aug. 4, 2016	98.93%	0.00%	98.93%	PHO
35	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipal of Same	Aplayana unip. Lda	RT/057/MOPTC-2016	\$ 168,297.72	Aug. 3, 2016	30.00%	0.00%	30.00%	Abandon



LISTA GERAL ANEXO B
PROGRES MAIO 2022

NU.	NARAN PROJETO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 27 May 2022			OBSERVASAUN
						previous	this prog	% actual prog	
36	Road Maintenance Section Same Urban Roads Municipality Manufahi	Renova Unip Lda	MPW - W - 190215	\$ 87,929.19	Dec. 2, 2019	71.88%	0.00%	71.88%	ON-GOING
37	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	Quintas das Flores, Lda	MPW - W - 190123	\$ 177,242.59	June 10, 2019	100.00%	0.00%	100.00%	ON-GOING
38	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi (162)	Alifa Pereira	MPW -RFQ 190019	\$ 59,446.75	Aug. 1, 2019	90.13%	0.00%	90.13%	ON-GOING
39	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi (162)	Leo - Dok	MPWTC-CD-170002	\$ 48,340.53	Jan. 8, 2019	86.31%	0.00%	86.31%	ON-GOING
40	Fencing for Construction Monument od Dom Boa Ventura	Loskabubu	RDTL/06/GM-MTAC/IV/2016	\$ 178,633.46	June 9, 2015	79.86%		79.86%	Abandon
41	Konstrusaun Tangki Beé no Menara Beé ba iha Edificio Administrasaun Municipiu Manufahi	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	\$ 7,758.22	April 10, 2017	85.99%		85.99%	Abandon
42	Konstrusaun Kuartel Bombeiros iha Same-Manufahi	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	\$ 360,114.56	Aug. 19, 2016	83.02%		83.02%	Abandon
43	Rehabilitasaun Igreja Paroquia Nossa Senhora Assuncao Same	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	\$ 438,905.72	Aug. 7, 2017	98.81%		98.81%	FHO
44	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	Consortio Deatle Hare ba Oin Lda	07/PDIM/M-MF/IX/2019	\$ 98,051.65	Sept. 9, 2019	92.45%		92.45%	PHO
45	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutor Bodik Tane Lisuk, Unip.Lda	Tutor Bodik Tane Lisuk, Unip.Lda	09/PDIM/M-MF/X/2019	\$ 23,697.55	Oct. 7, 2019	89.15%		89.15%	PHO
46	Konstrusaun Fatin isolamentu iha Municipio Manufahi, Timor Leste	Daloveya	RDTL-MS-DNA-DC-20-256	\$ 293,664.88	Sept. 12, 2020	98.65%		98.65%	ON-GOING
47	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	Haut-Dairam Unipessoal Lda	MPW-W210092	\$ 46,754.63	July 23, 2021	0.00%	44.37%	44.37%	ON-GOING
48	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	Riabile Unipessoal Lda	MPW-W-210091	\$ 52,112.72	July 23, 2021	21.47%	0.00%	21.47%	



LISTA GERAL ANEXO B
PROGRES MAIO 2022

NU.	NARAN PROJETO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 27 May 2022			OBSERVASAUN
						previous	this prog	% actual prog	
49	New Construction of Laboratory ih CSI Luak,Manufahi relasiona ba covid19 at Ministry of Health, Timor Leste	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	\$ 71,412.20	Aug. 17, 2021	58.76%	5.56%	64.31%	ON-GOING
50	PARA A CONSTRUCCAO DE JARDIM DE HEROIS DE MANUFAHI (New Construction of Campas, Gate and Leveling)	My friend Constr. Unip. Lda	RFQ No. 23/MACLN/DNAL/VI/2021	\$ 48,998.46	Sept. 1, 2021	37.20%	0.00%	37.20%	ON-GOING
51	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	Tutur Bodik Tane Lisuk, Unip.Lda	MPW - W -210094	\$ 83,595.57	July 23, 2021	71.35%	0.00%	71.35%	ON-GOING
52	Konstrusaun ka rehabilitasaun ba EBF Tefo	MEJD PKRIE EBF TEFO	Kontratu ho Grupo Comunitariu	\$ 99,986.68		0.00%	5.06%	5.06%	
53	Konstrusaun ka rehabilitasaun ba EBC Diligencia	MEJD PKRIE EBC DILIGENCIA	Kontratu ho Grupo Comunitariu	\$ 110,951.20		9.66%	8.59%	18.26%	
54	Konstrusaun ka rehabilitasaun ba EPE Turon	MEJD PKRIE EPE TURON	Kontratu ho Grupo Comunitariu	\$ 83,083.31		6.26%	10.17%	16.43%	
55	Konstrusaun ka rehabilitasaun ba EPE DOMingos Savio Grotu	MEJD PKRIE EPE DOMINGOS SAVIO	Kontratu ho Grupo Comunitariu	\$ 85,513.28		5.72%	10.01%	15.73%	
56	Konstrusaun ka rehabilitasaun ba EBF Silihasan	MEJD PKRIE EBF SILIHASAN	Kontratu ho Grupo Comunitariu	\$ 111,801.61		11.36%	8.58%	19.94%	
57	Konstrusaun ka rehabilitasaun ba EBF hatsana udo/Dai-sua Lama	MEJD PKRIE EBF HATSANA UDO / DAI-SUA LAMA	Kontratu ho Grupo Comunitariu	\$ 101,427.27		4.82%	5.15%	9.97%	
58	Konstrusaun ka rehabilitasaun ba EBF Blaro	MEJD PKRIE EBF BLARO	Kontratu ho Grupo Comunitariu	\$ 113,831.28		0.00%	5.99%	5.99%	
59	Konstrusaun ka rehabilitasaun ba EBF Rotuto	MEJD PKRIE EBF ROTUTO	Kontratu ho Grupo Comunitariu	\$ 71,892.87		10.04%	8.55%	18.58%	
60	Konstrusaun ka rehabilitasaun ba EBC Fatuco	MEJD PKRIE EBC FATUCO	Kontratu ho Grupo Comunitariu	\$ 10,986.63		15.79%	6.69%	22.48%	
61	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	\$ 140,614.24		11.74%	7.03%	18.78%	
62	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	\$ 132,466.39		9.93%	5.58%	15.51%	
63	New Construction Building for Central Electrical in Luak Manufahi, Ministry of Health Timor Leste	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-22-006	\$ 18,335.73		0.00%		0.00%	
64	For Road Maintanance Section Jct Aituto-Same-Betano 23Km(A04)	Bemos I Construction Unip. Lda	MPW-W-220007	\$ 131,893.81		0.00%		0.00%	

LISTA GERAL ANEXO B
PROGRES MAIO 2022

NU.	NARAN PROJETO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 27 May 2022			OBSERVAÇÃO
						previous	this prog	% actual prog	
65	Open New Road Turiscai - Mota Belihun Maubere, Turiscai - Liquido Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	Aldepo Murak Unip,Lda	SSS/250/MOPTC-2016	\$ 3,413,040.53	Sept. 4, 2017	93.90%	0.00%	93.90%	ON-GOING
66	Const. MCK (Saude) Orana	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	\$ 7,530.00	May 23, 2019	75.00%		75.00%	ON-GOING
67	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railaco, Sanfuk, Tutu Luro - Same Fahi Nehan (162)	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	\$ 570,200.00	March 25, 2020	70.00%	0.00%	70.00%	ON-GOING
68	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	Terra Livre Unip. Lda	SSS/299/MOPTC-2016	\$ 478,217.51	Nov. 23, 2016	90.44%		90.44%	PHO
69	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 4 : Turiscai to Alas	Wan Husin Associates SDN. BHD. Jv Consultant & Engineering Intercontinental Unip. Lda	0	\$ 798,900.00	43915	70.00%	0.00%	70.00%	ON-GOING

Inspected by :



Eng Romulo J.M Henrique
Engenheiro ba Projecto Infraestrutura
transportes e Irrigasaun Munisipio Manufahi
A D N IP

Inspected by :



Eng Fidelis Mardiano da Costa
Engenheiro Edificio Public, Agua e Saneamento A D N IP

Inspected by :



Eng Silvine D. R. R. Soares
Enjineiru M&E, A D N IP

Certified by :




Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao
qualidade ADN.I.P

Verified by :



Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura
transportes e Irrigasaun A D N IP

Verified by :



Arch. Francisco Xavier de D Jeronimo Engenheiro
Senior ba Edificio Public no Agua e Saneamento A D
N IP

Verified by :



Eng Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N IP



#ANEXU C1 (ALS 14)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC MAHAQUIDAN

No. kontratu :

Data Inspesaun : 11/05/2022

Fatin Inspesaun : Mahaquidan, Alas – Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :


Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Armasaun Feru Viga Baze

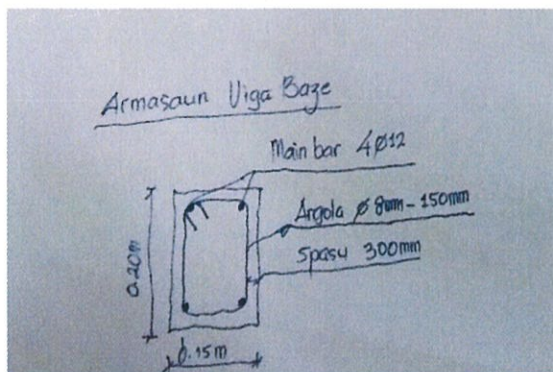

Ke'e Septitanck

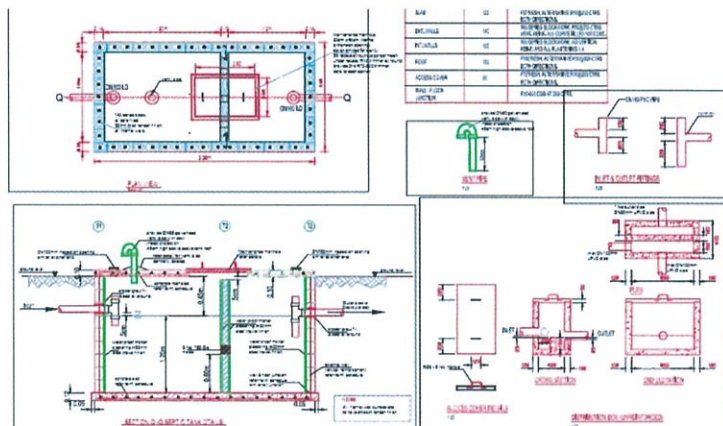

Observasaun iha tereno no Foto Aktual





#ANEXU C2 (ALS 14)

Projeto : Nova Construção Escola Básica Central Mahaquidan

Owner : MEJD

Localization : Mahaquidan, Alas Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION			
			MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,425.00	640.00	0.57%	640.00	0.57%
II	CLASSROOM BUILDING CA	\$ 62,569.45	4,858.35	4.35%	4,858.35	4.35%
III	TOILET BUILDING TB	\$ 25,164.97				
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,814.74				
A	CONSTRUCTION COST	\$ 102,974.16	\$ 5,498.35	4.92%	\$ 5,498.35	4.92%
B	CONTINGENCY	\$ 3,000.00				
C	OVERHEAD	\$ 5,840.00				
D	GRAND TOTAL	\$ 111,814.16	\$ 5,498.35	4.92%	\$ 5,498.35	4.92%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVO ADN, I.P.



ANEXU D

ADNLP Municipal Manual 2022

Site Instruction No.

I		IDENTITY OF PROJECT
		Name of Project: N.C. EBC Moheguindon
		Location Project: Mahaguidon 215 - Manigoto
		Coordinates Project:
		Owner Project: MEJO
		Contractor: Grupo Comunitario
		Consultant / Supervisor: MEJO
		Inspection Date: 25/05/2022

II		INFORMATION ON SITE			
A)	1)	MAJOR FINDINGS	INTERNATIONAL	NATIONAL	TOTAL
	2)	ENVIRONMENT		3	3
	3)	WELL LADDER		4	4
B)	4)	MAJOR FINDINGS		5	5
	5)	ENVIRONMENT			
C)	6)	ENVIRONMENT			
	7)	ENVIRONMENT			
D)	8)	ENVIRONMENT			
	9)	ENVIRONMENT			
E)	10)	ENVIRONMENT			
	11)	ENVIRONMENT			
F)	12)	ENVIRONMENT			
	13)	ENVIRONMENT			
G)	14)	ENVIRONMENT			
	15)	ENVIRONMENT			
H)	16)	ENVIRONMENT			
	17)	ENVIRONMENT			
I)	18)	ENVIRONMENT			
	19)	ENVIRONMENT			
J)	20)	ENVIRONMENT			
	21)	ENVIRONMENT			
K)	22)	ENVIRONMENT			
	23)	ENVIRONMENT			
L)	24)	ENVIRONMENT			
	25)	ENVIRONMENT			
M)	26)	ENVIRONMENT			
	27)	ENVIRONMENT			
N)	28)	ENVIRONMENT			
	29)	ENVIRONMENT			
O)	30)	ENVIRONMENT			
	31)	ENVIRONMENT			
P)	32)	ENVIRONMENT			
	33)	ENVIRONMENT			
Q)	34)	ENVIRONMENT			
	35)	ENVIRONMENT			
R)	36)	ENVIRONMENT			
	37)	ENVIRONMENT			
S)	38)	ENVIRONMENT			
	39)	ENVIRONMENT			
T)	40)	ENVIRONMENT			
	41)	ENVIRONMENT			
U)	42)	ENVIRONMENT			
	43)	ENVIRONMENT			
V)	44)	ENVIRONMENT			
	45)	ENVIRONMENT			
W)	46)	ENVIRONMENT			
	47)	ENVIRONMENT			
X)	48)	ENVIRONMENT			
	49)	ENVIRONMENT			
Y)	50)	ENVIRONMENT			
	51)	ENVIRONMENT			
Z)	52)	ENVIRONMENT			
	53)	ENVIRONMENT			
AA)	54)	ENVIRONMENT			
	55)	ENVIRONMENT			
AB)	56)	ENVIRONMENT			
	57)	ENVIRONMENT			
AC)	58)	ENVIRONMENT			
	59)	ENVIRONMENT			
AD)	60)	ENVIRONMENT			
	61)	ENVIRONMENT			
AE)	62)	ENVIRONMENT			
	63)	ENVIRONMENT			
AF)	64)	ENVIRONMENT			
	65)	ENVIRONMENT			
AG)	66)	ENVIRONMENT			
	67)	ENVIRONMENT			
AH)	68)	ENVIRONMENT			
	69)	ENVIRONMENT			
AI)	70)	ENVIRONMENT			
	71)	ENVIRONMENT			
AJ)	72)	ENVIRONMENT			
	73)	ENVIRONMENT			
AK)	74)	ENVIRONMENT			
	75)	ENVIRONMENT			
AL)	76)	ENVIRONMENT			
	77)	ENVIRONMENT			
AM)	78)	ENVIRONMENT			
	79)	ENVIRONMENT			
AN)	80)	ENVIRONMENT			
	81)	ENVIRONMENT			
AO)	82)	ENVIRONMENT			
	83)	ENVIRONMENT			
AP)	84)	ENVIRONMENT			
	85)	ENVIRONMENT			
AQ)	86)	ENVIRONMENT			
	87)	ENVIRONMENT			
AR)	88)	ENVIRONMENT			
	89)	ENVIRONMENT			
AS)	90)	ENVIRONMENT			
	91)	ENVIRONMENT			
AT)	92)	ENVIRONMENT			
	93)	ENVIRONMENT			
AU)	94)	ENVIRONMENT			
	95)	ENVIRONMENT			
AV)	96)	ENVIRONMENT			
	97)	ENVIRONMENT			
AW)	98)	ENVIRONMENT			
	99)	ENVIRONMENT			
AX)	100)	ENVIRONMENT			
	101)	ENVIRONMENT			
AY)	102)	ENVIRONMENT			
	103)	ENVIRONMENT			
AZ)	104)	ENVIRONMENT			
	105)	ENVIRONMENT			
BA)	106)	ENVIRONMENT			
	107)	ENVIRONMENT			
BB)	108)	ENVIRONMENT			
	109)	ENVIRONMENT			
BC)	110)	ENVIRONMENT			
	111)	ENVIRONMENT			
BD)	112)	ENVIRONMENT			
	113)	ENVIRONMENT			
BE)	114)	ENVIRONMENT			
	115)	ENVIRONMENT			
BF)	116)	ENVIRONMENT			
	117)	ENVIRONMENT			
BG)	118)	ENVIRONMENT			
	119)	ENVIRONMENT			
BH)	120)	ENVIRONMENT			
	121)	ENVIRONMENT			
BI)	122)	ENVIRONMENT			
	123)	ENVIRONMENT			
BJ)	124)	ENVIRONMENT			
	125)	ENVIRONMENT			
BK)	126)	ENVIRONMENT			
	127)	ENVIRONMENT			
BL)	128)	ENVIRONMENT			
	129)	ENVIRONMENT			
BM)	130)	ENVIRONMENT			
	131)	ENVIRONMENT			
BN)	132)	ENVIRONMENT			
	133)	ENVIRONMENT			
BO)	134)	ENVIRONMENT			
	135)	ENVIRONMENT			
BP)	136)	ENVIRONMENT			
	137)	ENVIRONMENT			
BQ)	138)	ENVIRONMENT			
	139)	ENVIRONMENT			
BR)	140)	ENVIRONMENT			
	141)	ENVIRONMENT			
BS)	142)	ENVIRONMENT			
	143)	ENVIRONMENT			
BT)	144)	ENVIRONMENT			
	145)	ENVIRONMENT			
BU)	146)	ENVIRONMENT			
	147)	ENVIRONMENT			
BV)	148)	ENVIRONMENT			
	149)	ENVIRONMENT			
BW)	150)	ENVIRONMENT			
	151)	ENVIRONMENT			
BX)	152)	ENVIRONMENT			
	153)	ENVIRONMENT			
BY)	154)	ENVIRONMENT			
	155)	ENVIRONMENT			
BZ)	156)	ENVIRONMENT			
	157)	ENVIRONMENT			
CA)	158)	ENVIRONMENT			
	159)	ENVIRONMENT			
CB)	160)	ENVIRONMENT			
	161)	ENVIRONMENT			
CC)	162)	ENVIRONMENT			
	163)	ENVIRONMENT			
CD)	164)	ENVIRONMENT			
	165)	ENVIRONMENT			
CE)	166)	ENVIRONMENT			
	167)	ENVIRONMENT			
CF)	168)	ENVIRONMENT			
	169)	ENVIRONMENT			
CG)	170)	ENVIRONMENT			
	171)	ENVIRONMENT			
CH)	172)	ENVIRONMENT			
	173)	ENVIRONMENT			
CI)	174)	ENVIRONMENT			
	175)	ENVIRONMENT			
CJ)	176)	ENVIRONMENT			
	177)	ENVIRONMENT			
CK)	178)	ENVIRONMENT			
	179)	ENVIRONMENT			
CL)	180)	ENVIRONMENT			
	181)	ENVIRONMENT			
CM)	182)	ENVIRONMENT			
	183)	ENVIRONMENT			
CN)	184)	ENVIRONMENT			
	185)	ENVIRONMENT			
CO)	186)	ENVIRONMENT			
	187)	ENVIRONMENT			
CP)	188)	ENVIRONMENT			
	189)	ENVIRONMENT			
CQ)	190)	ENVIRONMENT			
	191)	ENVIRONMENT			
CR)	192)	ENVIRONMENT			
	193)	ENVIRONMENT			
CS)	194)	ENVIRONMENT			
	195)	ENVIRONMENT			
CT)	196)	ENVIRONMENT			
	197)	ENVIRONMENT			
CU)	198)	ENVIRONMENT			
	199)	ENVIRONMENT			
CV)	200)	ENVIRONMENT			
	201)	ENVIRONMENT			
CW)	202)	ENVIRONMENT			
	203)	ENVIRONMENT			
CX)	204)	ENVIRONMENT			
	205)	ENVIRONMENT			
CY)	206)	ENVIRONMENT			
	207)	ENVIRONMENT			
CZ)	208)	ENVIRONMENT			
	209)	ENVIRONMENT			
DA)	210)	ENVIRONMENT			
	211)	ENVIRONMENT			
DB)	212)	ENVIRONMENT			
	213)	ENVIRONMENT			
DC)	214)	ENVIRONMENT			
	215)	ENVIRONMENT			
DD)	216)	ENVIRONMENT			
	217)	ENVIRONMENT			
DE)	218)	ENVIRONMENT			
	219)	ENVIRONMENT			
DF)	220)	ENVIRONMENT			
	221)	ENVIRONMENT			
DG)	222)	ENVIRONMENT			
	223)	ENVIRONMENT			
DH)	224)	ENVIRONMENT			
	225)	ENVIRONMENT			
DI)	226)	ENVIRONMENT			
	227)	ENVIRONMENT			
DJ)	228)	ENVIRONMENT			
	229)	ENVIRONMENT			
DK)	230)	ENVIRONMENT			
	231)	ENVIRONMENT			
DL)	232)	ENVIRONMENT			
	233)	ENVIRONMENT			
DM)	234)	ENVIRONMENT			
	235)	ENVIRONMENT			
DN)	236)	ENVIRONMENT			
	237)	ENVIRONMENT			
DO)	238)	ENVIRONMENT			
	239)	ENVIRONMENT			
DP)	240)	ENVIRONMENT			
	241)	ENVIRONMENT			
DQ)	242)	ENVIRONMENT			
	243)	ENVIRONMENT			
DR)	244)	ENVIRONMENT			
	245)	ENVIRONMENT			
DS)	246)	ENVIRONMENT			
	247)	ENVIRONMENT			
DT)	248)	ENVIRONMENT			
	249)	ENVIRONMENT			
DU)	250)	ENVIRONMENT			
	251)	ENVIRONMENT			
DV)	252)	ENVIRONMENT			
	253)	ENVIRONMENT			
DW)	254)	ENVIRONMENT			
	255)	ENVIRONMENT			
DX)	256)	ENVIRONMENT			
	257)	ENVIRONMENT			
DY)	258)	ENVIRONMENT			
	259)	ENVIRONMENT			
DZ)	260)	ENVIRONMENT			
	261)	ENVIRONMENT			
EA)	262)	ENVIRONMENT			
	263)	ENVIRONMENT			
EB)	264)	ENVIRONMENT			
	265)	ENVIRONMENT			
EC)	266)	ENVIRONMENT			
	267)	ENVIRONMENT			
ED)	268)	ENVIRONMENT			
	269)	ENVIRONMENT			
EE)	270)	ENVIRONMENT			
	271)	ENVIRONMENT			
EF)	272)	ENVIRONMENT			
	273)	ENVIRONMENT			
EG)	274)	ENVIRONMENT			
	275)	ENVIRONMENT			
EH)	276)	ENVIRONMENT			
	277)	ENVIRONMENT			
EI)	278)	ENVIRONMENT			
	279)	ENVIRONMENT			
EJ)	280)	ENVIRONMENT			
	281)	ENVIRONMENT			
EK)	282)	ENVIRONMENT			
	283)	ENVIRONMENT			
EL)	284)	ENVIRONMENT			
	285)	ENVIRONMENT			
EM)	286)	ENVIRONMENT			
	287)	ENVIRONMENT			
EN)	288)	ENVIRONMENT			
	289)	ENVIRONMENT			
EO)	290)	ENVIRONMENT			
	291)	ENVIRONMENT			
EP)	292)	ENVIRONMENT			
	293)	ENVIRONMENT			
EQ)	294)	ENVIRONMENT			
	295)	ENVIRONMENT			
ER)	296)	ENVIRONMENT			
	297)	ENVIRONMENT			
ES)	298)	ENVIRONMENT			
	299)	ENVIRONMENT			
ET)	300)	ENVIRONMENT			
	301)	ENVIRONMENT			
EU)	302)	ENVIRONMENT			
	303)	ENVIRONMENT			
EV)	304)	ENVIRONMENT			
	305)	ENVIRONMENT			
EW)	306)	ENVIRONMENT			
	307)	ENVIRONMENT			
EX)	308)	ENVIRONMENT			
	309)	ENVIRONMENT			
EY)	310)	ENVIRONMENT			
	311)	ENVIRONMENT			
EZ)	312)	ENVIRONMENT			
	313)	ENVIRONMENT			
FA)	314)	ENVIRONMENT			
	315)	ENVIRONMENT			
FB)	316)	ENVIRONMENT			
	317)	ENVIRONMENT			
FC)	318)	ENVIRONMENT			
	319)	ENVIRONMENT			
FD)	320)	ENVIRONMENT			
	321)	ENVIRONMENT			
FE)	322)	ENVIRONMENT			
	323)	ENVIRONMENT			
FF)	324)	ENVIRONMENT			
	325)	ENVIRONMENT			
FG)	326)	ENVIRONMENT			
	327)	ENVIRONMENT			
FH)	328)	ENVIRONMENT			
	329)	ENVIRONMENT			
FI)	330)	ENVIRONMENT			
	331)	ENVIRONMENT			
FJ)	332)	ENVIRONMENT		</	



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 15)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF BERCOBAN

No. kontratu :

Data Inspesaun : 11/05/2022

Fatin Inspesaun : Mahaquidan, Alas – Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun Feru Viga Baze

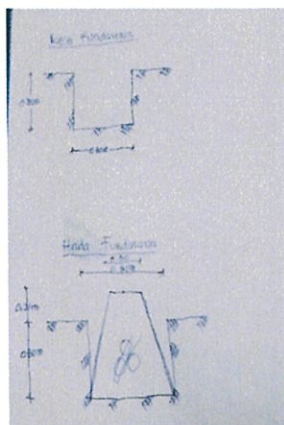



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (ALS 15)


Projeto : Nova Construção Escola Básica Filial Bercoban
Owner : MEJD
Localization : Bercoban Taitudak, Alas Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION			
			MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,775.00	\$ 675.00	0.67%	\$ 675.00	0.67%
II	CLASSROOM BUILDING C	\$ 52,034.01	\$ 4,172.12	4.13%	\$ 4,172.12	4.13%
III	TOILET BUILDING TB	\$ 25,446.29				
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 10,991.28				
A	CONSTRUCTION COST	\$ 92,246.58	\$ 4,847.12	4.80%	\$ 4,847.12	4.80%
B	CONTINGENCY	\$ 3,000.00				
C	OVERHEAD	\$ 5,840.00				
D	GRAND TOTAL	\$ 101,086.58	\$ 4,847.12	4.80%	\$ 4,847.12	4.80%


Verified by:
Date, / / 2022


Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



ANEXO D

ADN, I.P. Município Manufahi 2022

Site Instruction No. :

I		IDENTITY OF PROJECT			
		Name of Project	X.c. EBF Bercoban		
		Location Project	Bercoban Taikutete, Alas Manufahi		
		Coordinate Project			
		Owner Project	MEJO		
		Contractor	Grupo Comunitário		
		Consultant / Supervision	MEJO		
		Inspection Date	15-05-2022		
II		INFORMATION ON SITE			
A)		MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
1)		ENGINEERS		2	2
2)		SKILL LABOR		4	4
3)		UNSKILL LABOR		4	4
B)		EQUIPMENTS			
C)		MATERIALS			
		- Sand - Rebar 3mm, 10mm & 12mm			
		- Gravel - Plywood 9mm			
		- pc - Timber 1/6			
III		PROBLEM IDENTIFICATION ON SITE			
Obs - Alas		Udan			
IV		SOLUTION AND RECOMMENDATION			
Obs - Alas		Record data udan			
Obs - Alas		Kondens air di atas ho proyekti rain mune'e bole hare kastan			
Obs - Alas		betan			

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Fidelis Mariano de Costa
Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Date: 17/05/2022

Received by:

Jeferson Jesus Lopes
Site Supervision

Manuel Soares Sarmento
Contractor Site Engineering



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 16)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF MANUS

No. kontratu :

Data Inspesaun : 11/05/2022

Fatin Inspesaun : Manus Taitudak, Alas – Manufahi

Koordinadas :


Start Point : Long : , Latetude:

End Point : Long : , Latetude:

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Armasaun Feru Viga Baze

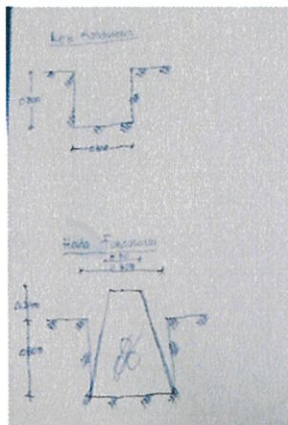

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (ALS 16)


Projeto : Nova Construção Escola Básica Filial Manus
Owner : MEJD
Localization : Manus Taitudak, Alas Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION			
			MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	ADN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 4,175.00	\$ 895.00	0.77%	\$ 895.00	0.77%
III	CLASSROOM BUILDING CA	\$ 65,117.90	\$ 5,516.80	3.20%	\$ 5,516.80	3.20%
IV	TOILET BUILDING TB	\$ 25,875.85	\$ 1,492.42	1.28%	\$ 1,492.42	1.28%
V	PROVISIONAL SUM FOR SITE-WORKS	\$ 12,739.75				
A	CONSTRUCTION COST	\$ 107,908.50	\$ 7,904.21	5.24%	\$ 7,904.21	5.24%
B	CONTINGENCY	\$ 3,000.00				
C	OVERHEAD	\$ 5,840.00				
D	GRAND TOTAL	\$ 116,748.50	\$ 7,904.21	5.24%	\$ 7,904.21	5.24%

Verified by:
Date, / / 2022


Fidelis Mariano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



ANEXU D

ADN, I.P. Município Manaus 2022

Site Instruction No. :

I					
IDENTITY OF PROJECT					
		Name of Project	: N.C. EBF Manaus		
		Location Project	: Manaus Tailudak, Alas Manufahi		
		Coordinate Project	:		
		Owner Project	: MEJO		
		Contractor	: Grupo Komunitariu		
		Consultant / Supervision	: MEJO		
		Inspection Date	: 11/5/2022		
II					
INFORMATION ON SITE					
A)		MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
1)		ENGINEERS		1	1
2)		SKILL LABOR		4	4
3)		UNSKILL LABOR		5	5
B)		EQUIPMENTS			
		- Gerador			
		-			
C)		MATERIALS			
		- PC - Rebar 12m, 10mm & 8mm - PHS 3/4 & 1/4			
		- Sarg - DVC 4", 3" & 2"			
		- Gravel - Paved 10mm & 12mm			
III					
PROBLEM IDENTIFICATION ON SITE					
IV					
SOLUTION AND RECOMMENDATION					
alter - Pau Hada direksi keet					
alter - Record dalam uban					
alter - Take structure grupu ho no tlg taka iha kuadra informasaun					
alter - atualiza time schedule					
alter - serba tur degenho, BOA & spek. tek.					
alter - karia atu halo mikans serbini Tenke heton aprovasaun					
alter - tur owner					
alter - prepare planu serbini no taka iha kuadra informasaun					

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

 Fideles M. de Costa
Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Date:/...../2022

Received by:

 Zeferino de Jesus Lopez
Site Supervision

 Jose da Costa Xavier
Contractor Site Engineering



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (FTB 10)

Back-up Data

Naran Projeto : Nova Construção ESTV Francisco Borja da Costa Fatuberliu
No. kontratu :

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Fatucahi, Fatuberliu - Manufahi

Koordinadas :


Start Point : Long , Latetude :

End Point : Long : - , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Fui Sinta Baze

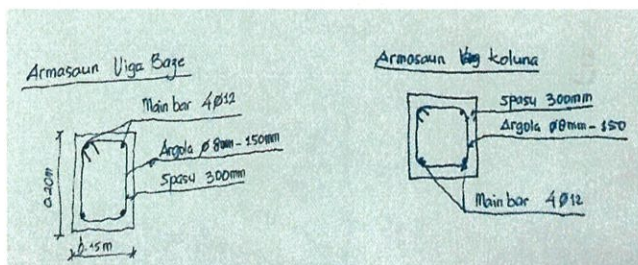

Observasaun iha tereno no Foto Aktual





ANEXU C2 (# FTB 10)

Projeto : Nova Construção Edifício Escritório + Laboratório Geral de Ciência ESTV Francisco
Borja da Costa Fatucahi
Owner : MEJD
Localization : Fatucahi, Fatuberliu Manufahi

MAIN SUMMARY			Up to 27042022 - progres		May Progress		Up to 27052022 - progres	
NO	ITEM SERVISU	A DN,I.P. VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,925.00	\$ 2,817.50	1.45%			\$ 2,817.50	1.45%
II	TEACHER OFFICE	\$ 79,969.81	\$ 6,357.83	3.27%	\$ 3,876.57	1.99%	\$ 10,234.40	5.26%
III	LABORATORY GERAL E CIENCIA	\$ 81,026.74	\$ 5,641.84	2.09%	\$ 2,816.83	1.45%	\$ 8,458.67	3.54%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 20,912.84						
A	CONSTRUCTION COST	\$ 185,834.39	\$ 14,817.17	6.81%	\$ 6,693.40	3.44%	\$ 21,510.57	10.24%
B	CONTIGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 194,674.39	\$ 14,817.17	6.81%	\$ 6,693.40	3.44%	\$ 21,510.57	10.24%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN,I.P.

Verified by:
Date, / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN,I.P.

Certified by:
Date, / / 2022



Eng. Emerenciana da Costa Maia
Coordenadora UCVC ADN,I.P.



ANEXU D

ADN, I.P. Munisipiu Manufahi 2022

Site Instruction No. :

I				
IDENTITY OF PROJECT				
Name of Project		N.C. Edifício Escritório + Lab. Geral de Cêncis		
Location Project		Fatucóhi, Fatubertu - Manufahi		
Coordinate Project				
Owner Project		MEJD		
Contractor		Grupo Comunitário		
Consultant / Supervision		MEJD		
Inspection Date		25/05/2022		
II				
INFORMATION ON SITE				
A)		MAN POWER	INTERNATIONAL	NATIONAL TOTAL
1)		ENGINEERS		2
2)		SKILL LABOR	6	4
3)		UNSKILL LABOR		4 6
B)		EQUIPMENTS		
C)		MATERIALS	- Brick concrete block 20/20/40	
		- Sand		
		- P.C		
		- Rebar 12mm, 10mm & 8mm		
III				
PROBLEM IDENTIFICATION ON SITE				
IV				
SOLUTION AND RECOMMENDATION				
Other - Acelera serviço para contrato				
Other - Documentação (fotografia / ou vídeo) de cada serviço / item				
Other - Serviço para degenho, BOD & spek tek.				
Other - Material para teste de aprovação para projeto na in				
fui spek tek.				
Please acknowledge receipt this instruction by signing and dating this copy.				
Please be guided accordingly				
 Fidelis M. da Costa Technic ADN, I.P.				
I here by acknowledge receipt the above site instruction.				
Date: ... / 2022				
Received by: 				
Irucensio J. Vicente				
Contractor Site Engineering				
Site Supervision				
Picture/video				
 Sebastiao Borges				



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 5)

Back-up Data

Naran Projeto : Nova fornecimento água do Bairro PNTL Manufahi
No. kontratu : SSS/053/MI-2017

Data Inspesaun : 12/5/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : -8.965856, Latetude : 125.661791

End Point : Long : -8.987874, Latetude : 125.665954

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Atividade laiha, hein mobilizsaun



Handwritten signature



#ANEXU C1 (SAME 16)

Back-up Data

Naran Projeto : **Konstrusaun Kuartel Bombeiros iha Same-Manufahi**
No. kontratu : **02/PDIM/M-MF/VIII/2016**

Data Inspesaun : **11/5/2022**

Fatin Inspesaun : Letefoho, Same - Manufahi

Koordinadas :

Start Point :

End Point :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Fura bee moss, Progressu seidauk iha tamba
seidauk hetan bee moos



Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 23)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK,
MANUFAHI, RELASIONA BA COVID 19 AT MINISTRY OF
HEALTH, TIMOR LESTE

No. kontratu : RDTL-MS-C19-DNA-RBK-21-088

Data Inspesaun : 12/05/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : 125.65449101, Latetude : -8.99989127

End Point : Long :, Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Supply Furniture

Dadauk ne'e identifika volume furniture
tamba seidauk loke hotu

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 23)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK,
MANUFAHI, RELASIONA BA COVID 19 AT MINISTRY OF
HEALTH, TIMOR LESTE

No. kontratu : RDTL-MS-C19-DNA-RBK-21-088

Data Inspesaun : 26/05/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : 125.65449101, Latetude : -8.99989127

End Point : Long :, Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Atividade terenu la iha, tamba ne'e laiha
instrusaun serbisu

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO
VII. GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU D (SAME 23)

PROJECT TITLE : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK, MANUFAHI, RELASIONA BA
COVID 19 AT MINISTRY OF HEALTH, TIMOR LESTE

LOCATION : LUAK - MANUFAHI MUNICIPALITY - TIMOR LESTE

PROJECT OWNER : MINISTRY OF HEALTH

BILL OF QUANTITY (BOQ)											
NO	DESCRIPTION	ORIGINAL CONTRACT				AND,I,P RECOMMENDATION					
		UNIT	QUANTITY	UNIT PRICE	AMOUNT	Up to 27042022 - progres		May Progress		Up to 27052022 - progres	
						AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PREPARATION WORKS				\$ 2,763.80	\$ 2,653.80	\$ 0.04	\$ -	0.00%	\$ 2,653.80	\$ 0.04
II	FUNDATION WORKS				\$ 2,858.25	\$ 2,331.57	\$ 0.03	\$ 526.68	0.74%	\$ 2,858.25	\$ 0.04
III	CONCRETE WORKS				\$ 4,976.55	\$ 1,694.43	\$ 0.02	\$ 362.05	0.51%	\$ 2,056.48	\$ 0.03
IV	WALL INSTALATION AND PLESTERING				\$ 4,969.75	\$ 4,728.08	\$ 0.07	\$ 241.67	0.34%	\$ 4,969.75	\$ 0.07
V	CARPENTER WORKS				\$ 5,290.00	\$ 5,290.00	\$ 0.07	\$ -	0.00%	\$ 5,290.00	\$ 0.07
VI	ROOFING WORKS				\$ 10,686.82	\$ 10,686.82	\$ 0.15	\$ -	0.00%	\$ 10,686.82	\$ 0.15
VII	CEILING WORKS				\$ 3,585.35	\$ 1,443.05	\$ 0.02	\$ 1,487.10	2.08%	\$ 2,930.15	\$ 0.04
VIII	FLOOR TILE WORKS				\$ 3,552.36	\$ 2,780.78	\$ 0.04	\$ 771.58	1.08%	\$ 3,552.36	\$ 0.05
IX	ELECTRICAL WORKS				\$ 3,708.00	\$ -	\$ -	\$ -	0.00%	\$ -	\$ -
X	SANITASI WORKS				\$ 4,710.78	\$ 2,742.15	\$ 0.04	\$ -	0.00%	\$ 2,742.15	\$ 0.04
XI	PAINTING WORKS				\$ 1,203.69	\$ 1,083.32	\$ 0.02	\$ 120.37	0.17%	\$ 1,203.69	\$ 0.02
XII	PROVISIONAL SUM FOR FURNITURE				\$ 8,000.00	\$ -	\$ -	\$ -	0.00%	\$ -	\$ -
XIII	FINAL CLEARING				\$ 300.00	\$ -	\$ -	\$ -	0.00%	\$ -	\$ -
A	CONTRUCTION COST (I +...+ XIII)				\$ 56,603.35	\$ 35,433.99	49.62%	\$ 3,509.45	4.91%	\$ 38,943.44	54.53%
B	Contractor fee 10% x (A * 10%)				\$ 5,660.53	\$ 3,543.40	4.96%	\$ 350.95	0.49%	\$ 3,894.34	5.45%
C	Overhead				\$ 2,550.00	\$ 2,160.00	3.02%	\$ 30.00	0.04%	\$ 2,190.00	3.07%
D	TAX 2% x (A + B + C)				\$ 1,296.32	\$ 822.75	1.15%	\$ 77.81	0.11%	\$ 900.56	1.26%
E	CONTINGENCY				\$ 5,300.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
F	TOTAL PROJECT COST (A + B + C + D + E)				\$ 71,412.20	\$ 41,960.14	58.76%	\$ 3,968.20	5.56%	\$ 45,928.34	64.31%

Prepared by:
Date, / / 2021




Eng. Fidelis Mardiano da Costa
Engenheiro Edifício Público, Água e Saneamento ADN, I.P.

Verified by:
Date, / / 2021


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Sênior Edifício Público, Água e Saneamento ADN-IP


Certified by:
Date, / / 2021


Eng. Emerenciana da Costa Maia
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN-IP

#ANEXU D (SAME 23)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	12/5/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil	

INTRUSAUN / REKOMENDASAUN	
Naran projeto : New Construction of Laboratory ih CSI Luak, Manufahi relasiona ba covid19 at Ministry of Health, Timor Leste	
Kompanha : Kartini Unip. Lda	

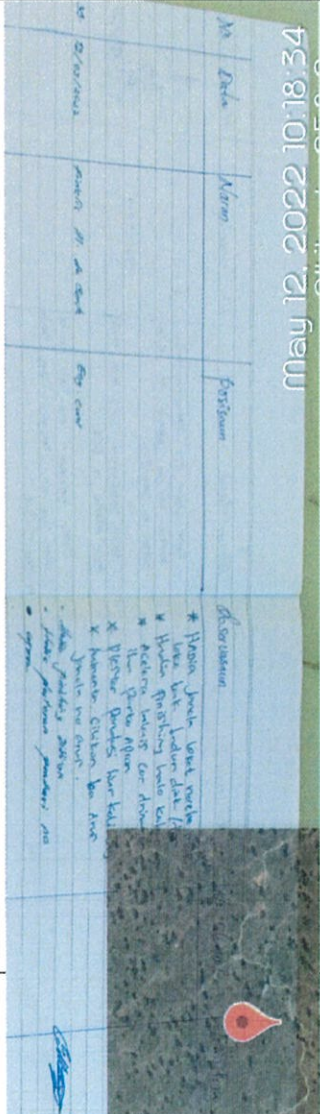INTRUSAUN / REKOMENDASAUN		
1	Hadi'ak finishing didi'ak	
2	Hadi'ak plesteran fondasi no apron	
3	Hadi'ak nut ceramic	



#ANEXU C1 (SAME 24)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF CAMPAS, GATE AND LEVELING
AREA AND GARDEN OF HEROES MANUFAHI

No. kontratu : 39/MACLN/IX/2021

Data Inspesaun : 17/05/2022

Fatin Inspesaun : Luak Manufahi

Koordinadas :

Start Point : Long :, Latetude :

End Point : Long :, Latetude :

Naran Inspetur : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Atividade la la'o





#ANEXU C1 (SAME 26)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF TEFO
No. kontratu :

Data Inspesaun : 13/05/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude:

End Point : Long : , Latetude:

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual



#ANEXU C1 (SAME 26)

Back-up Data




Naran Projeto : NOVA CONTRUÇÃO EBF TEFO

No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun armadura no molde Viga Baze

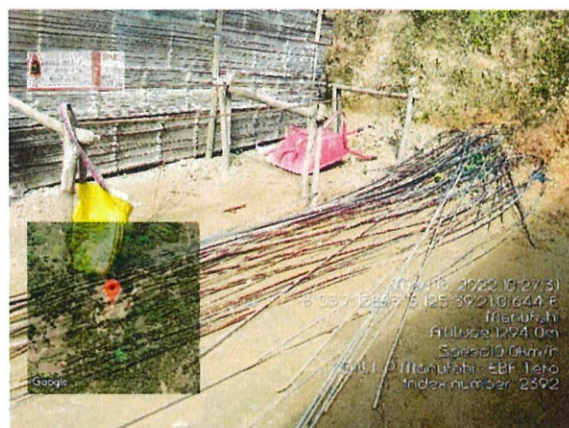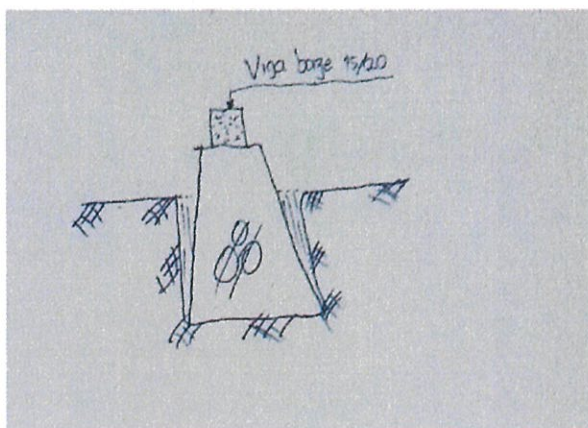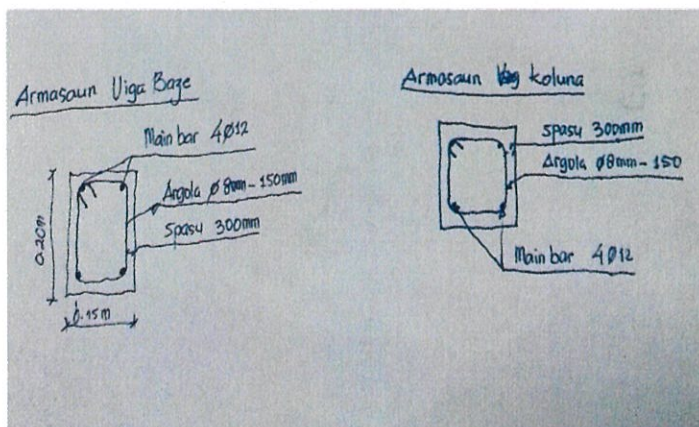



#ANEXU C2 (SAME 26)

Projeto : Nova Construção Edifício Escola Filial Tefo Holarua
Owner : MEJD
Localization : Holarua, Same- Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION			
NO	ITEM SERVIÇO	A DN VERIFIED	MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
			AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 4,175.00	\$ 740.00	0.74%	\$ 740.00	0.74%
II	CLASSROOM BUILDING C	\$ 51,047.62	\$ 4,321.92	4.32%	\$ 4,321.92	4.32%
III	TOILET BUILDING Tb	\$ 25,480.68				
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 10,443.39				
A	CONSTRUCTION COST	\$ 91,146.68	\$ 5,061.92	5.06%	\$ 5,061.92	5.06%
B	CONTINGENCY	\$ 3,000.00				
C	OVERHEAD	\$ 5,840.00				
D	GRAND TOTAL	\$ 99,986.68	\$ 5,061.92	5.06%	\$ 5,061.92	5.06%

Verified by:
Date, / / 2022



Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.

INSTRUSAUN / REKOMENDASAUN				
Naran projeto : New Construction of Laboratory ih CSI Luak,Manufahi relaciona ba covid19 at Ministry of Health, Timor Leste				
Kompanha : Kartini Unip. Lda				
#ANEXU D (SAME 23)		INSTRUSAUN / REKOMENDASAUN		
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun
I	12/5/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil
 Halo kordensaun diak ho entidade responsavel sira Serbisu tuir dezenho, BOQ & Spek tek. Karik atu halo mudansa serbisu balun tenke iha aprovasau husi projetu na'in molok halo serbisu				
		Asinatura		



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 27)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC DILIGENCIA
No. kontratu :

Data Inspesaun : 12/05/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :



End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun viga leten (Ringbalk)

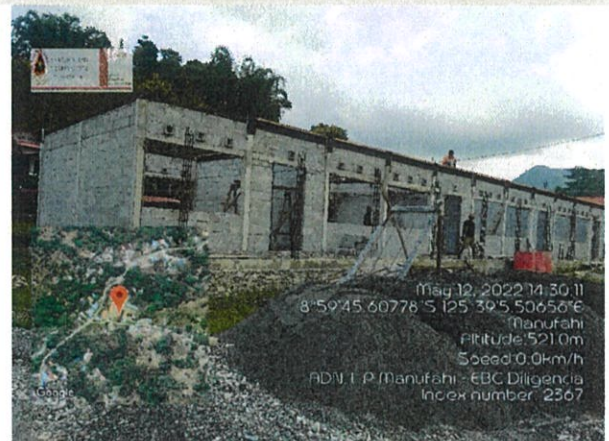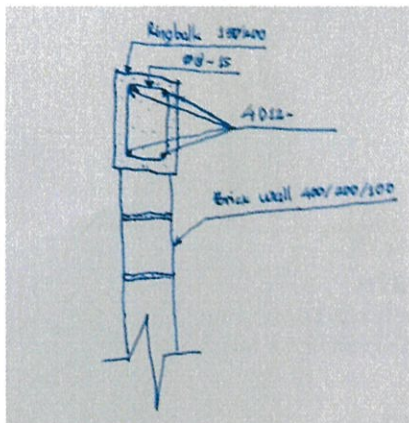

Pasang Loster 100mm





MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 27)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC DILIGENCIA
No. kontratu :

Data Inspeção : 07/04/2022

Fatin Inspeção : Same - Manufahi

Koordinadas :

Start Point : Long : , Latitude :


End Point : Long : , Latitude :

Naran Inspector : Eng. Fidelis Mardiano da Costa


Sketch & Foto Desenho

Observação iha terreno no Foto Aktual

Hada batako ba kemiringan madres

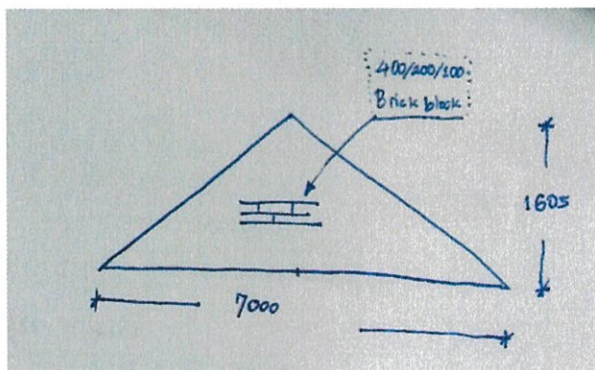

Supply 400/200/150 For Septotank

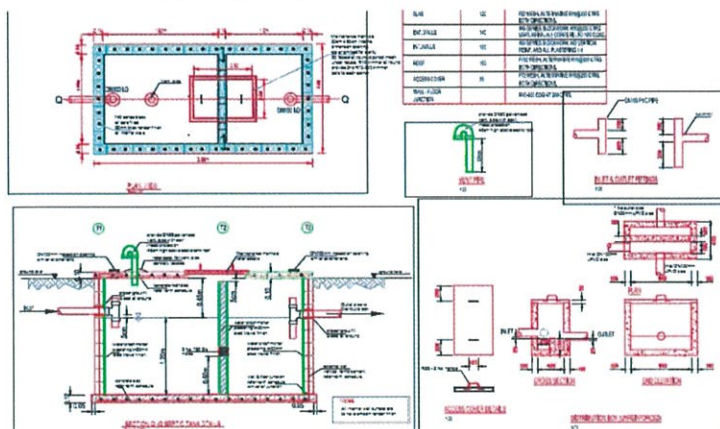



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 27)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC DILIGENCIA
No. kontratu :

Data Inspesaun : 22/05/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun Viga Leten (Ringbalk)

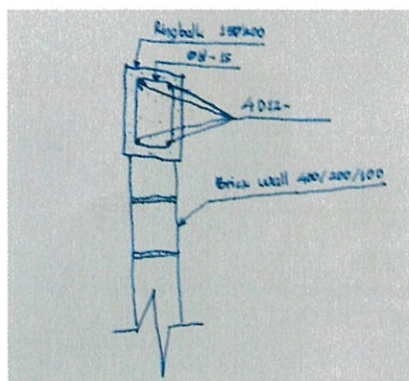

Septitank

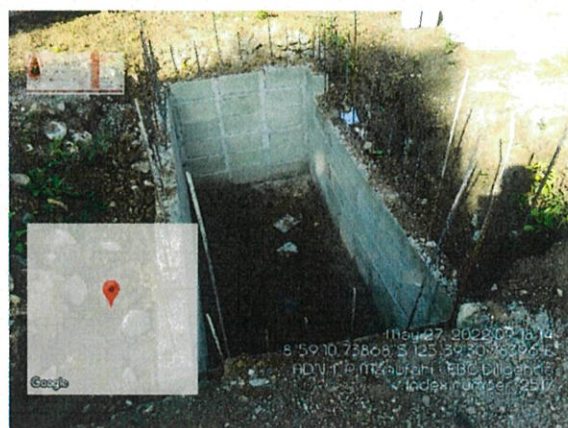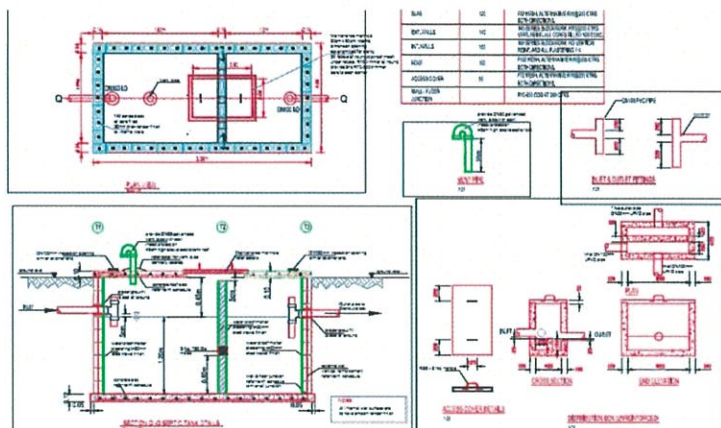



#ANEXU C2 (SAME 27)

Projeto : Nova Construção Escola Básica Central Diligência

Owner : MEJD

Localization : Letefoho, Same Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 27/04/2022 PROGRESS		MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 2,675.00	\$ 721.88	0.65%	\$ 33.75	0.03%	\$ 755.63	0.68%
II	CLASSROOM BUILDING CA	\$ 61,073.65	\$ 8,003.90	7.21%	\$ 5,733.11	5.17%	\$ 13,737.01	12.38%
III	TOILET BUILDING TB	\$ 24,613.61	\$ 1,994.68	1.80%	\$ 3,769.14	3.40%	\$ 5,763.82	5.19%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 12,284.68						
V	PROVISIONAL SUM FOR DEMOLITION	\$ 1,464.27						
A	CONSTRUCTION COST	\$ 102,111.20	\$ 10,720.46	9.66%	\$ 9,536.00	8.59%	\$ 20,256.45	18.26%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 110,951.20	\$ 10,720.46	9.66%	\$ 9,536.00	8.59%	\$ 20,256.45	18.26%

Verified by:
Date, / / 2022


Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora U/VQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, LP.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Nova Construcão Escola Bazica Central Diligencia

Kompanha : Gropu Komunitariu

#ANEXU D (SAME 27)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/5/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil		Fidelis M. de Costa Eng. Civil Manufahi Serbisu nafatin tuir segundu BOQ 20/05/2022 e gora Tex. - Banha Afu subante pabiku pag- mentu Tuiru itaun gemaun prazimal e serbisaun tuit behun	
1 Serbisu nafatin tuir dezenho, BOQ & spek. Tek.							
2 Banhira atu submete pedidu pagamentu tenke attach aprovasaun material & sertifikadu teste betaun							



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 28)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE TURON
No. kontratu :

Data Inspesaun : 12/05/2022

Fatin Inspesaun : Babulo, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa


Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun Feru ba lintle beam



“Pemasangan Batako”

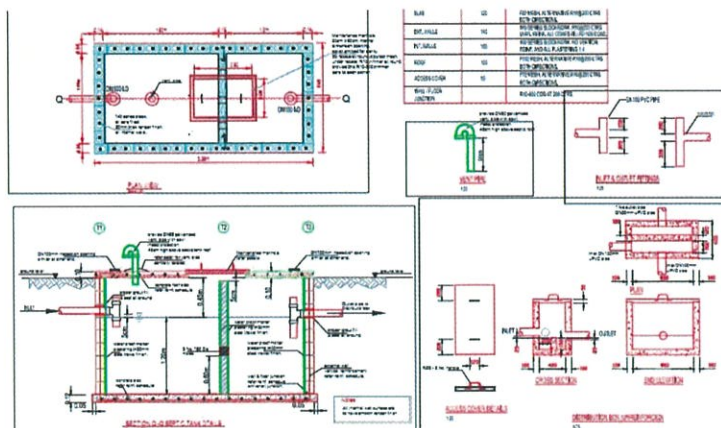



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 28)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE TURON
No. kontratu :

Data Inspesaun : 26/05/2022

Fatin Inspesaun : Babulo, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Hada Didin Bloku

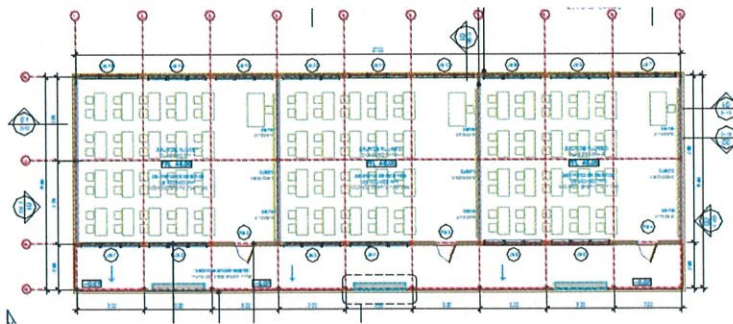



ANEXU C2 (SAME 28)

Projeto : Nova Construção Escola Pré Escolar Turon

Owner : MEJD

Localization : Babulo, Same Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 25/03/2022 PROGRESS		MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,175.00	\$ 1,770.00	2.13%	\$ 125.00	0.15%	1,895.00	2.28%
II	CLASSROOM BUILDING C2	\$ 57,907.13	\$ 3,434.36	4.13%	\$ 8,321.94	10.02%	11,756.30	14.15%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 13,161.18						
A	CONSTRUCTION COST	\$ 74,243.31	\$ 5,204.36	6.26%	\$ 8,446.94	10.17%	\$ 13,651.30	16.43%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 83,083.31	\$ 5,204.36	6.26%	\$ 8,446.94	10.17%	\$ 13,651.30	16.43%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022



Eng. Emerenciana da Costa Maia
Coordenadora UCVC ADN, I.P.



ANEXU D

ADN, I.P. Munisipiu Manufahi 2022

Site Instruction No. :

I	IDENTITY OF PROJECT					
	Name of Project	: N.C. Epa Turon				
	Location Project	: Babulo, Same - Manufahi				
	Coordinate Project	:				
	Owner Project	: MEJD				
	Contractor	: Grupo Comunitario				
	Consultant / Supervision	: MEJD				
	Inspection Date	: 26-05-2022				
II	INFORMATION ON SITE					
A)	MAN POWER	INTERNATIONAL		NATIONAL		TOTAL
1)	ENGINEERS			-		-
2)	SKILL LABOR			4		4
3)	UNSKILL LABOR			3		3
B)	EQUIPMENTS					
C)	MATERIALS					
	- D.C	- Rebar 12mm & 8mm				
	- Sand	- Brick Concrete block				
	- Gravel	-				
III	PROBLEM IDENTIFICATION ON SITE					
IV	SOLUTION AND RECOMMENDATION					
	<i>Obs - Serbisu fuir dejenho, BOO & spek. tek.</i>					
	<i>Obs - Tenke iha aprovasaun hui dono projetu ba mularasa serbinu sira ho justifikasoun ne'ebe ragoavel fuir tekniku.</i>					
Please acknowledge receipt this instuction by signing and dating this copy.						
Please be guided accordingly						
 Fidelis M. da Costa Technic ADN,I.P.						
I here by acknowledge receipt the above site instruction.						
Date:...../...../2022						
Received by:						
 Clementino de Andrade Contractor Site Engineering Foreman						
Site Supervision				Contractor Site Engineering		

Picture/video



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



INADN, LP.
Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU D (SAME 28)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	Asinatura
I	12/5/2022	Maunfahi / Same	Fidelis Mardiano da Costa	Eng. Civil	1	Serbisu nafatin fuir dezentu, BOQ & spek. Tek.
					2	Banhiru atu submete pedidu pagamentu tenke attach aprovasaun material & sertifikadu teste betaan

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Nova Construcacao Escola Pre Escolar Turon

Kompanha : Gropu Komunitariu

INSTRUSAUN / REKOMENDASAUN

12/05/2022	Eng. Civil	Fidelis Mardiano da Costa	Eng. Civil	12/05/2022	Eng. Civil	Fidelis Mardiano da Costa
------------	------------	---------------------------	------------	------------	------------	---------------------------



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 29)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE DOMINGOS SAVIO GROTU

No. kontratu :

Data Inspesaun : 10/05/2022

Fatin Inspesaun : Grotu, Same - Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Hada Parede Batako

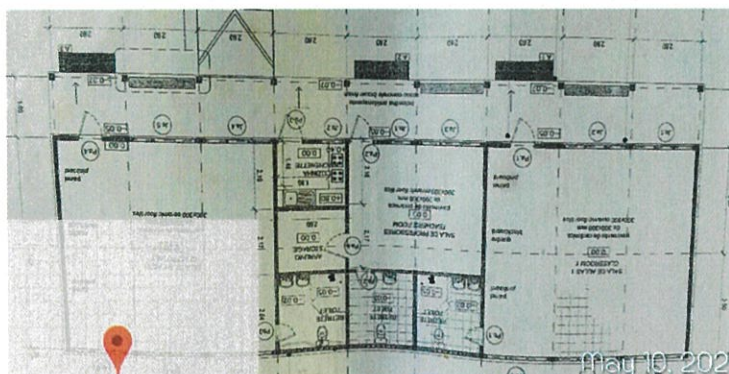

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 29)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE DOMINGOS SAVIO GROTU

No. kontratu :

Data Inspesaun : 26/05/2022

Fatin Inspesaun : Grotu, Same – Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Armasaun Feru Viga Baze

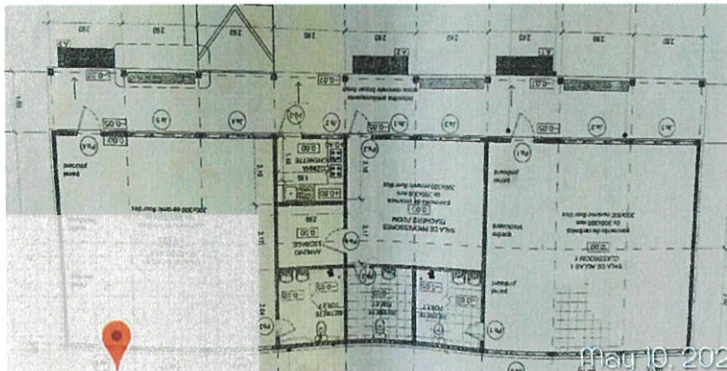

Observasaun iha tereno no Foto Aktual





ANEXU C2 (SAME 29)

Projeto : Nova Construção Escola Pré-Escolar Domingos Savio Grotu

Owner : MEJD

Localization : Grotu, Same Manufahi

MAIN SUMMARY			A D N, I.P. RECOMMENDATION					
			UP TO 25/03/2022 PROGRESS		MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	A D N VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,875.00	\$ 2,295.00	2.68%	\$ 185.00	0.22%	\$ 2,480.00	2.90%
II	CLASSROOM BUILDING C2	\$ 61,144.12	\$ 2,597.54	3.04%	\$ 8,376.39	9.80%	\$ 10,973.94	12.83%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,654.16						
A	CONSTRUCTION COST	\$ 76,673.28	\$ 4,892.54	5.72%	\$ 8,561.39	10.01%	\$ 13,453.94	15.73%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 85,513.28	\$ 4,892.54	5.72%	\$ 8,561.39	10.01%	\$ 13,453.94	15.73%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



ANEXU D

ADN, I.P. Munisipiu Manufahi 2022

Site Instruction No. :

I		IDENTITY OF PROJECT
	Name of Project	N.C. EPE Domingos Savio Grotu
	Location Project	Grotu
	Coordinate Project	
	Owner Project	MEJD
	Contractor	Grupo Komunitario
	Consultant / Supervision	MEJD
	Inspection Date	26-05-2022

II		INFORMATION ON SITE			
	A)	MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
	1)	ENGINEERS		1	1
	2)	SKILL LABOR		3	3
	3)	UNSKILL LABOR		4	4
	B)	EQUIPMENTS			
	C)	MATERIALS			
		- Seng	- Rebar 10mm, 12mm & 8mm		
		- PL	- Timber 4x6		
		- Gravel	- Plywood 9mm		

III		PROBLEM IDENTIFICATION ON SITE
	Obs -	Nivel lintel beam la apas fuir dezartu

IV		SOLUTION AND RECOMMENDATION
	Obs -	Husu la dono projektu a grupu komunitario tenke buka solusao la justifikao la nivel lintel beam motok kontinu
	Obs -	Servisu fuir dezartu, ROR & spek. tek.
	Obs -	Tenke ibi aprovasao huri dono projektu la mudansa servisu huri la justifikao la razeavel fuir tekniku.

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Date: ... / ... / 2022

Received by

Cipriano de Andrade Antunes dos S



ANEXO D

ADNLP, Municipio Manababo 2022

Site Instruction No.

I					
IDENTITY OF PROJECT					
		Name of Project	N.C. EDE S. Domingos Santo Cristo		
		Location Project	Coto. Santo. Manababo		
		Coordinate Project			
		Owner Project	MEJO		
		Contractor	Grupo Kometario		
		Consultant / Supervisor	MEJO		
		Inspection Date	10/5/2022		
II					
INFORMATION ON SITE					
A)		MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
1)		ENGINEERS			
2)		SKILL LABOR		3	3
3)		UNSKILL LABOR		3	3
B)		EQUIPMENTS			
		- Plumbing			
C)		MATERIALS			
		- Pipe Pvc			
		- Brick Concrete			
		- Sand			
		- PC			
		- Redon 12mm, 10mm y 8mm			
III					
PROBLEM IDENTIFICATION ON SITE					
IV					
SOLUTION AND RECOMMENDATION					
the - By Grupo Tere de Tere					
the - Serbisu Air de Tere. BOA a spec. Tere.					
the - Tere de Tere serbisu Tere de Tere de Tere					

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly


Technic ADNLP

I have by acknowledge receipt the above site instruction.

Date: 1/ /2022

Received by



Site Supervision

Contractor Site Engineering



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 30)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF SELEHASAN

No. kontratu :

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Betano, Same – Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :


Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho


Hada Batako



Dadauk ne'e Instalasaun bataku ba Parede haleu
hansan planta iha leten ho nia altura batako

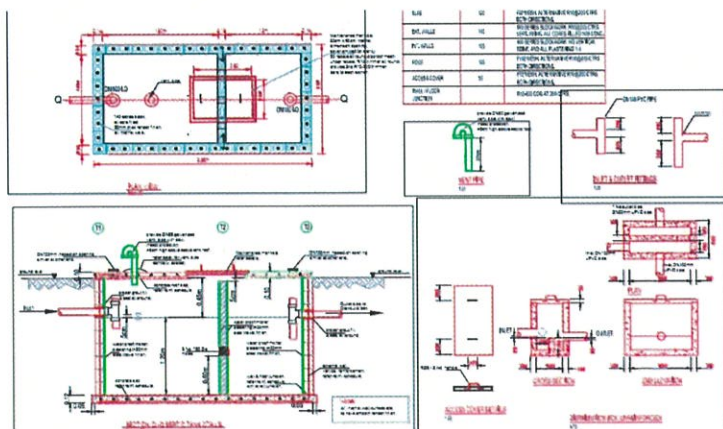

Observasaun iha tereno no Foto Aktual

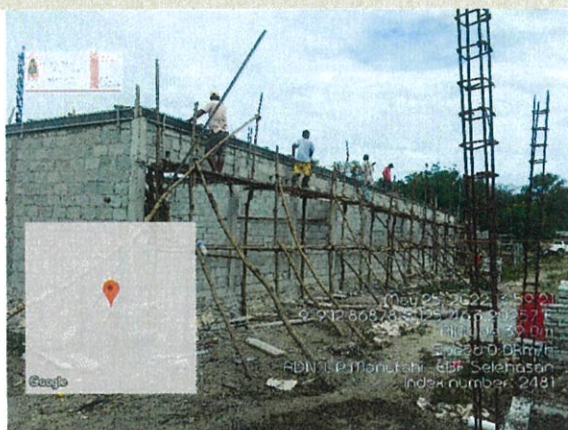



ANEXU C2 (SAME 30)


Projeto : Nova Construção Escola Básica Filial Selihasan
Owner : MEJD
Localization : Selihasan Betano , Same Manufahi

MAIN SUMMARY			A D N, I.P RECOMMENDATION					
			UP TO 26/04/2022 PROGRESS		MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
	ITEM SERVIÇO	A D N VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,275.00	\$ 1,743.75	1.56%	\$ 103.13	0.09%	\$ 1,846.88	1.65%
II	CLASSROOM BUILDING CA	\$ 61,808.99	\$ 4,300.98	3.85%	\$ 9,486.84	8.49%	\$ 13,787.83	12.33%
III	TOILET BUILDING TB	\$ 24,895.93	\$ 7,133.31	5.96%			\$ 7,133.31	5.96%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,921.67						
V	PROVISIONAL SUM FOR DEMOLITION	\$ 1,060.03						
A	CONSTRUCTION COST	\$ 102,961.61	\$ 13,178.05	11.37%	\$ 9,589.97	8.58%	\$ 22,768.02	19.94%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 111,801.61	\$ 13,178.05	11.37%	\$ 9,589.97	8.58%	\$ 22,768.02	19.94%

Verified by:
Date, / / 2022


Fidelis Machado da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022




Eng. Emerenciana da Costa Maia
Coordenadora UCVO ADN, I.P.



ANEXU D

ADN.I.P. Munisipiu Manufahl 2022

Site Instruction No. :

I	IDENTITY OF PROJECT			
	Name of Project	N.C. EBF. Selehasan		
	Location Project	Baturo, Santa - Marungahi		
	Coordinate Project			
	Owner Project	MEJD		
	Contractor	Grupo Komunitario		
	Consultant / Supervision	MEJD		
	Inspection Date	25/05/2022		
II	INFORMATION ON SITE			
A)	MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
1)	ENGINEERS		2	2
2)	SKILL LABOR		6	6
3)	UNSKILL LABOR		0	0
B)	EQUIPMENTS			
C)	MATERIALS			
	- P.C - Beton 12mm, 10mm x 8mm			
	- Sand - Plywood			
	- Gravel - R.H.S. 3/3			
III	PROBLEM IDENTIFICATION ON SITE			
IV	SOLUTION AND RECOMMENDATION			
	Chas - servisu fuir degenho, 300 x 500 x 100. Chas - Dokumentasun la kada servisu/item Chas - Aprobasun materialis hui senu projetu			
Please acknowledge receipt this instruction by signing and dating this copy.				
Please be guided accordingly				
 Fictalis M. de Costa Technic ADN.I.P.				
I here by acknowledge receipt the above site instruction.				
Site Supervision		Date: / / 2022 Received by:  Octaviana M.A. de Araujo Contractor Site Engineering		



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 31)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DAI-SUA LAMA
No. kontratu :

Data Inspesaun : 26/05/2022

Fatin Inspesaun :

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Fui Betaun Viga Baze

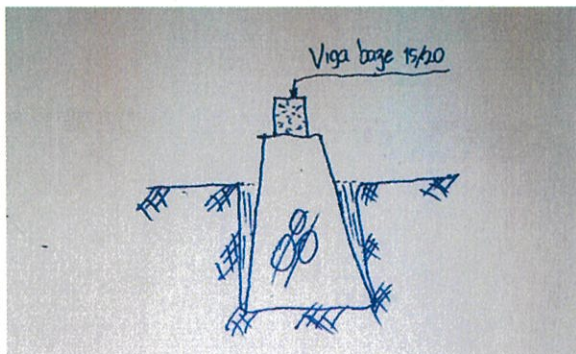

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 31)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DAI-SUA LAMA
No. kontratu :

Data Inspesaun : 10/05/2022

Fatin Inspesaun :

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Armasaun Viga Baze

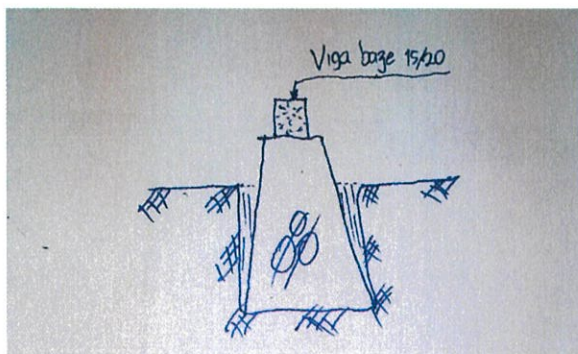

Observasaun iha tereno no Foto Aktual





#ANEXU C2 (SAME 31)

Projeto : Nova Construção Edifício Escola Filial Hatsanaudo Daisua

Owner : MEJD

Localization : Hatsanaudo Daisua , Same- Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 25/03/2022 PROGRESS		MAY PROGRESS		UP TO 27/05/2022 PROGRESS	
NO	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,475.00	\$ 825.00	0.81%	\$ 250.00	0.25%	\$ 1,075.00	1.06%
II	CLASSROOM BUILDING C	\$ 50,921.69	\$ 2,441.60	2.41%	\$ 4,973.36	4.90%	\$ 7,414.96	7.31%
III	TOILET BUILDING Tb	\$ 25,156.94	\$ 1,128.90	0.71%			\$ 1,128.90	0.71%
IV	PROVISIONAL-SUM FOR SITEWORKS (SW)	\$ 13,033.65						
A	CONSTRUCTION COST	\$ 92,587.27	\$ 4,395.50	3.93%	\$ 5,223.36	5.15%	\$ 9,618.86	9.08%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	\$ 908.00	0.90%			\$ 908.00	0.90%
D	GRAND TOTAL	\$ 101,427.27	\$ 5,303.50	4.82%	\$ 5,223.36	5.15%	\$ 10,526.86	9.97%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



ANEXU D

ADN, I.P. Munisípiu Manufahi 2022

Site Instruction No. :

IDENTITY OF PROJECT

Name of Project : N.º. 10F Haisara 480
Location Project : Daisua, Same - Manufahi
Coordinate Project :
Owner Project : MEJD
Contractor : Grupo Comunitaria
Consultant / Supervision : MEJD
Inspection Date : 10/03/2022

INFORMATION ON SITE

A)	MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
1)	ENGINEERS			
2)	SKILL LABOR		4	4
3)	UNSKILL LABOR		9	9
B)	EQUIPMENTS			
C)	MATERIALS			
- Rebar 12mm, 10mm & 8mm - 3cm				
- Plywood 9mm				
- p.c				

PROBLEM IDENTIFICATION ON SITE

Obs - 100 Serbis Tarde

SOLUTION AND RECOMMENDATION

Obs - 100 Serbis Tarde
Obs - 100 Serbis Tarde

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Edelis M. da Costa
Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Date:/2022

Received by:

Daniel Lopes
Contractor Site Engineering

Site Supervision

Picture/video

Poremkan



MINISTERI PERENCANAAN
KEKORPORATAN DAN
KEMERDEKAAN EKONOMI
REPUBLIC OF INDONESIA



DIREKTORAT JENDERAL
KEMERDEKAAN EKONOMI
KEMENTERIAN PERENCANAAN
KEKORPORATAN DAN
KEMERDEKAAN EKONOMI

ANEXU D

ADN.I.P. Munisiplu Manufahi 2022

Site Instruction No. :

I					
IDENTITY OF PROJECT					
Name of Project : <i>N.C. EBF Hotsana Udo</i>					
Location Project : <i>Desa Daisug Loma, Same - Manufahi</i>					
Coordinate Project :					
Owner Project : <i>MEJO</i>					
Contractor : <i>Gruppo Komunitario</i>					
Consultant / Supervision : <i>MEJO</i>					
Inspection Date : <i>26/05/2022</i>					
II					
INFORMATION ON SITE					
A)		MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
1)		ENGINEERS		<i>1</i>	<i>1</i>
2)		SKILL LABOR		<i>2</i>	<i>2</i>
3)		UNSKILL LABOR		<i>5</i>	<i>5</i>
B)		EQUIPMENTS			
C)		MATERIALS			
		<i>Rebar 12mm, 10mm & 8mm</i>	<i>- Gravel</i>		
		<i>P.C</i>	<i>- Plywood 9mm</i>		
		<i>sand</i>			
III					
PROBLEM IDENTIFICATION ON SITE					
IV					
SOLUTION AND RECOMMENDATION					
<i>cek - Eng. Gruppo periksa dan lakukan serbim (site) nunc' bala</i> <i>supervisiannya serbim site</i>					

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Technic ADN.I.P.

I here by acknowledge receipt the above site instruction.

Date: *26/05/2022*

Received by:

Daniel Lopez

Contractor Site Engineering

Site Supervision

Picture/video



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 31)

Back-up Data BLARO

Naran Projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DALSUA LAMA
No. kontratu :

Data Inspesaun : 13/05/2022

Fatin Inspesaun :

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun Kofrazen Viga Baze

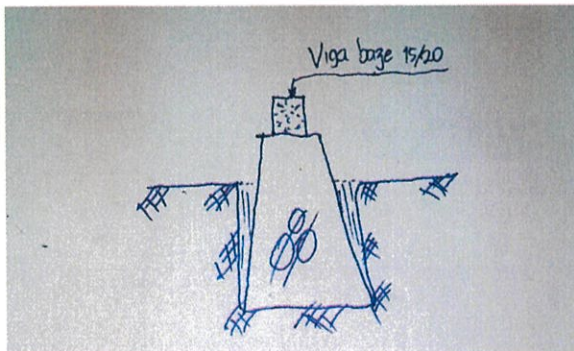



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público


Projeto : Nova Construção Escola Básica Filial Blaro
Owner : MEJD
Localization : Blaro - Holarua, Same Manufahi

MAIN SUMMARY			A D N, I.P. RECOMMENDATION			
			MAY PROGRESS		TO 27/05/2022 - PROGR	
	ITEM SERVIÇO	A D N VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,875.00	\$ 1,155.00	1.01%	\$ 1,155.00	1.01%
II	CLASSROOM BUILDING CA	\$ 64,486.89	\$ 5,657.97	4.97%	\$ 5,657.97	4.97%
III	TOILET BUILDING TB	\$ 25,966.99				
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 10,662.40				
A	CONSTRUCTION COST	\$ 104,991.28	\$ 6,812.97	5.99%	\$ 6,812.97	5.99%
B	CONTINGENCY	\$ 3,000.00				
C	OVERHEAD	\$ 5,840.00				
D	GRAND TOTAL	\$ 113,831.28	\$ 6,812.97	5.99%	\$ 6,812.97	5.99%


Verified by:
Date, / / 2022


Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Nova Konstrusaun EBF Hatsana Udo/Daisua Lama

Kompanha : Grupo Komunitaria

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	13/5/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil		Halo kordenasaun Pier ho entidade responsavel sira Respostas saun 13 mado Eng. civil Fidelis M. de Costa - Halo kordenasaun Pier ho entidade responsavel sira - Serbisu Pier dezenuha BOQ & spara ten - Kora udu halo mudansa serbisu Pierma haten aprovasaun husi projektu nain molok halo mudansa 	
					1	Halo kordenasaun di'ak ho entidade responsavel sira	
					2	Serbisu tuir dezenhu, BOQ & espek.Tek.	
					3	Karik atu halo mudansa serbisu tenke hetan aprovasaun husi projektu na'in molok halo mudansa	



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 33)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE ROTUTO
No. kontratu :

Data Inspesaun : 10/05/2022

Fatin Inspesaun : Rotuto, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :




End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

"Pengecoran" Sinta Baze

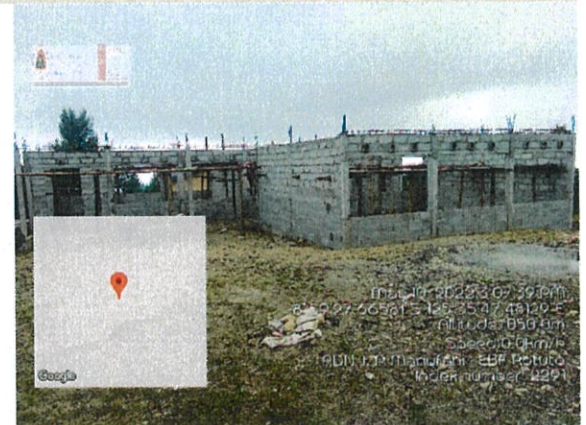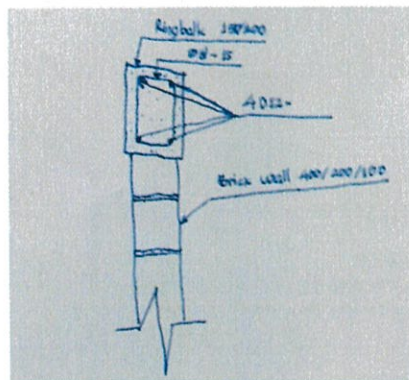



#ANEXU C2 (SAME 33)

Projeto : Nova Construção Edifício Escola EBF Rotuto

Owner : MEJD

Localization : Rotuto, Same Manufahi

MAIN SUMMARY

NO	ITEM SERVIÇO	A DN VERIFIED	Up to 27042022 - progress		April Progress		Up to 27042022 - progress	
			AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,675.00	\$ 961.00	1.34%	\$ 100.00	0.14%	\$ 1,061.00	1.48%
II	CLASSROOM BUILDING CL	\$ 52,911.97	\$ 5,772.76	8.03%	\$ 6,043.99	8.41%	\$ 11,816.75	16.44%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 5,899.87						
IV	PROVISIONAL SUM FOR DEMOLISH	\$ 566.03						
A	CONSTRUCTION COST	\$ 63,052.87	\$ 6,733.76	9.37%	\$ 6,143.99	8.55%	\$ 12,877.75	17.91%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	\$ 482.00	0.67%			\$ 482.00	0.67%
D	GRAND TOTAL	\$ 71,892.87	\$ 7,215.76	10.04%	\$ 6,143.99	8.55%	\$ 13,359.75	18.58%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



ANEXO D

ADN, LP, Município Manufahi 2022

Site Instruction No. 1

I	IDENTITY OF PROJECT				
	Name of Project	H.C. BRF Rotulo			
	Location Project	Rotulo, Soma - Manufahi			
	Coordinate Project				
	Owner Project	MEJO			
	Contractor	Grupo Komunitario			
	Consultant / Supervision	MEJO			
	Inspection Date	10/5/2022			
II	INFORMATION ON SITE				
	A)	MAN POWER	INTERNATIONAL	NATIONAL	TOTAL
	1)	ENGINEERS	0	0	0
	2)	SKILL LABOR	0	0	0
	3)	UNSKILL LABOR	0	0	0
	B)	EQUIPMENTS			
	C)	MATERIALS			
		- Rebar 12mm - Gravel			
		- Sand			
		- Pa			
III	PROBLEM IDENTIFICATION ON SITE				
	- Lintel Beams la nivel				
IV	SOLUTION AND RECOMMENDATION				
	- Tanke talia lintel beams ne'abe la nivel				
	- Serbisu mapatin juir degenho. Baa p spon teknik larik talia lintel beams teknik beton aprovasaun huti spon projektu				

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Technic ADN, LP

I here by acknowledge receipt the above site instruction.

Date: 10/5/2022

Received by:

Contractor Site Engineering

Site Supervision

Picture/Video

PROSIDENTE



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 34)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC 1,2,3 FATUCO
No. kontratu :

Data Inspesaun : 27/05/2022

Fatin Inspesaun : Hola-rua, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Reboka Didin



Pengecoran Sopi-Sopi

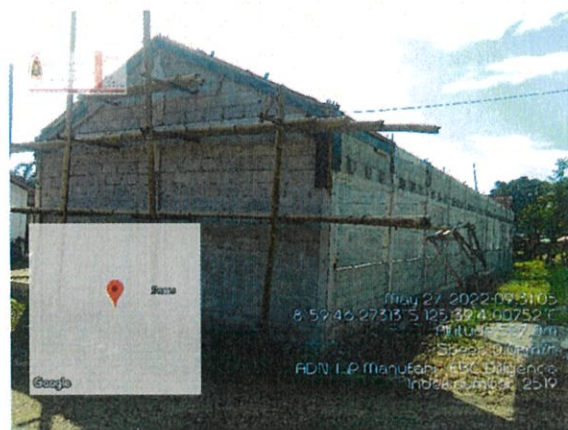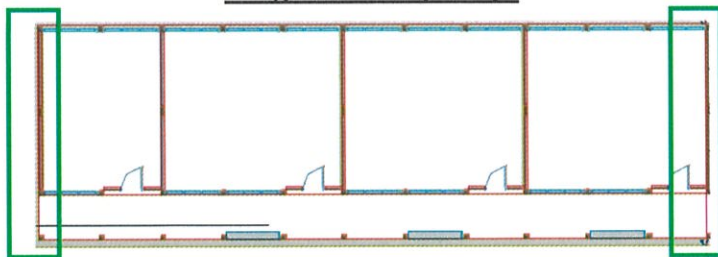



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 34)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC 1,2,3 FATUCO
No. kontratu :

Data Inspesaun : 17/05/2022

Fatin Inspesaun : Hola-rua, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa


Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

"Pengecoran" Sinta Baze ba "CA"

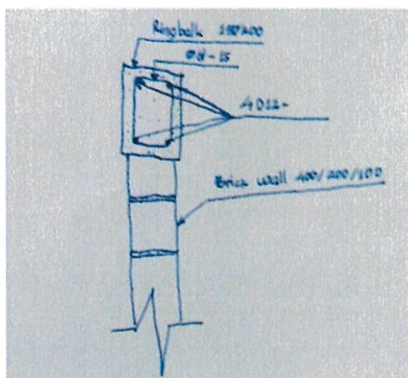

"Pengecoran" Sinta Baze ba "TB"

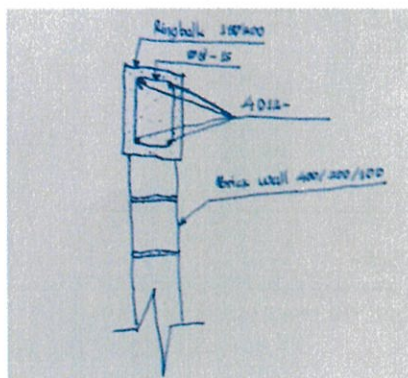



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 34)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC 1,2,3 FATUCO
No. kontratu :

Data Inspesaun : 12/05/2022

Fatin Inspesaun : Hola-rua, Same - Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho


"Pengecoran" Sinta Baze ba "CA"

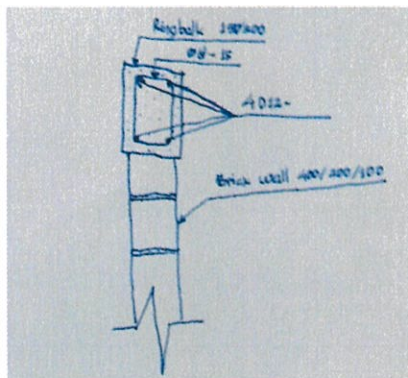

Observasaun iha tereno no Foto Aktual



Septic tank works

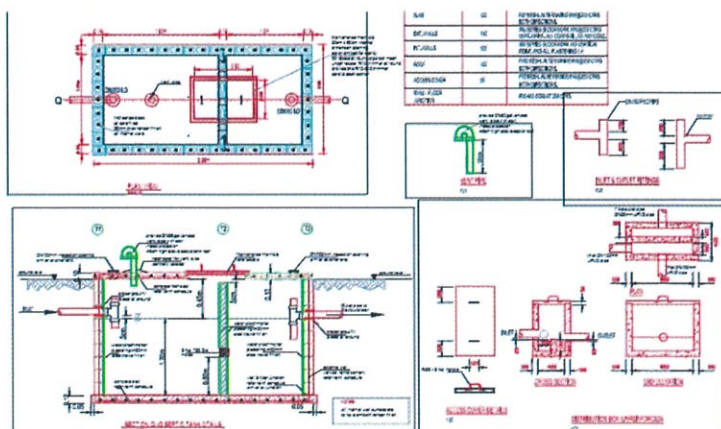



#ANEXU D (SAME 34)

Projeto : Nova Construção Escola Básica Central Fatuco
Owner : MEJD
Localization : Fatuco Holarua , Same Manufahi

MAIN SUMMARY			A D N, I.P. RECOMMENDATION					
			Up to 27042022 - progress		May Progress		Up to 27052022 - Progress	
	ITEM SERVIÇO	A D N VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 2,675.00	1,495.00	1.36%	\$ -	0.00%	1,495.00	1.36%
II	CLASSROOM BUILDING CA	\$ 61,554.47	10,755.44	9.79%	\$ 5,186.82	4.72%	15,942.26	14.51%
III	TOILET BUILDING TB	\$ 24,812.57	5,094.27	4.64%	\$ 2,160.94	1.97%	7,255.21	6.60%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,390.83						
V	PROVISIONAL SUM FOR DEMOLITION	\$ 587.75						
A	CONSTRUCTION COST	\$ 101,020.63	\$ 17,344.71	15.79%	\$ 7,347.76	6.69%	\$ 24,692.47	22.48%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 109,860.63	\$ 17,344.71	15.79%	\$ 7,347.76	6.69%	\$ 24,692.47	22.48%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVC ADN, I.P.



ANEXO D

ADN, I.P. Município Manufahi 2022

Site Instruction No. :

I				
IDENTITY OF PROJECT				
Name of Project		X. C. Fato EBC Fato		
Location Project		Holarua, Same - Manufahi		
Coordinate Project				
Owner Project		MEJO		
Contractor		Grupo Komunitariu		
Consultant / Supervision		MEJO		
Inspection Date		12-05-2022		

II				
INFORMATION ON SITE				
MAN POWER		INTERNATIONAL	NATIONAL	TOTAL
A)	1) ENGINEERS	-	-	-
	2) SKILL LABOR	-	7	7
	3) UNSKILL LABOR	-	0	0
B)	EQUIPMENTS			
C)	MATERIALS			
	- Sand - Rebor 12mm, 10mm & 8mm			
	- Gravel			
	- Po			

III				
PROBLEM IDENTIFICATION ON SITE				

IV				
SOLUTION AND RECOMMENDATION				
Obs - Eng. Grupo Fatoa destina ita tereno ho'i holo monitorizasaun				
Obs - Servisu Tur degeñu BDA e oper. tek.				
Obs - Karik atu holo mudansa servisu Fatoa ita aprovasaun huri dano projeto molor holo mudansa				

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Date:...../...../2022

Received by:

Carlos Soares

Site Supervision

Contractor Site Engineering



DEPARTMENT OF PUBLIC WORKS AND HIGHWAYS
CONSTRUCTION DIVISION



ANNEX D

ADN.I.P. Munisipal Marikina 2022

Site Instruction No.

I. IDENTITY OF PROJECT				
Name of Project		TBC - Fatuco		
Location Project		Holares, Same - Marikina		
Coordinate Project				
Owner Project		MEJO		
Contractor		Grupo Komunitario		
Consultant / Supervision		MEJO		
Inspection Date		27.05.2022		

II. INFORMATION ON SITE				
A) MAN POWER		INTERNATIONAL	NATIONAL	TOTAL
1) ENGINEERS			1	1
2) SKILL LABOR			8	8
3) UNSKILL LABOR			7	7
B) EQUIPMENTS				
- Mixer Concrete				
C) MATERIALS				
- Sand - Rebar 12mm, 10mm & 8mm				
- Gravel				
- PC				

III. PROBLEM IDENTIFICATION ON SITE				

IV. SOLUTION AND RECOMMENDATION				
- Terminate pagapaan tuig dekada 800 x 200 x 100.				
- Instalasyon program serbis.				
- Binigay sa subang pagmamahal tuig dekada 800 x 200 x 100.				
- Sa bawat 800 x 200 x 100 material site.				

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly.




Technic. ADN.I.P.

I have by acknowledging receipt the above site instruction.

Date: 1. 1. 2022

Received by:



Construction Division Engineering

Site Supervisor

Pictures/Video



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 35)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC SIMPANG TIGA

No. kontratu :

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa


Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Loster block installation



Lintel beam rebar installation





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 35)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC SIMPANG TIGA

No. kontratu :

Data Inspesaun : 11/05/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Iha inspesaun loron ida ne'e laiha atividade, tuir
informasaun husi grupu katak sei hein hela
material (rebar for lintel beam)





#ANEXU C2 (SAME 35)

Projeto : Nova Construção Edifício Escola Bazica Central Simpang Tiga

Owner : MEJD

Localization : Simpang Tiga Daisua, Same- Manufahi

MAIN SUMMARY			ADN,LP RECOMMENDATION							
			Up to 25032022 - progres		Up to 27042022 - progres		April Progress		Up to 27042022 - progres	
NO	ITEM SERVISU	A DN VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,675.00	\$ 1,105.00	0.79%	\$ 1,325.00	0.94%	\$ 150.00	0.11%	\$ 1,475.00	1.05%
II	CLASSROOM BUILDING C	\$ 49,223.37	\$ 2,888.03	2.05%	\$ 7,804.14	5.55%	\$ 9,741.84	6.93%	\$ 17,545.98	12.48%
III	CLASSROOM BUILDING Cdl	\$ 42,912.01	\$ 1,918.13	1.36%	\$ 5,951.64	4.23%			\$ 5,951.64	4.23%
IV	TOILET BUILDING Tb	\$ 24,347.83	\$ 1,334.47	0.95%	\$ 1,428.37	1.02%			\$ 1,428.37	1.02%
V	PROVISIONAL FOR SITEWORKS	\$ 10,945.68								
VI	PROVISIONAL FOR DEMOLISH	\$ 670.35								
A	CONSTRUCTION COST	\$ 131,774.24	\$ 7,245.64	5.15%	\$ 16,509.14	11.74%	\$ 9,891.84	7.03%	\$ 26,400.98	18.78%
B	CONTIGENCY	\$ 3,000.00								
C	OVERHEAD	\$ 5,840.00								
D	GRAND TOTAL	\$ 140,614.24	\$ 7,245.64	5.15%	\$ 16,509.14	11.74%	\$ 9,891.84	7.03%	\$ 26,400.98	18.78%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022



Eng. Emerenciana da Costa Maia
Coordenadora UCWO ADN, I.P.



ANEXU D

ADN, I.P. Munisiplu Manufahi 2022

Site Instruction No. :

I				
IDENTITY OF PROJECT				
Name of Project		EX. a. EBC. Simpang Tiga		
Location Project		Daisua, Same - Manufahi		
Coordinate Project				
Owner Project		MEJO		
Contractor		Grup Komunitario		
Consultant / Supervision		MEJO		
Inspection Date		25/05/2022		
II				
INFORMATION ON SITE				
A)		MAN POWER	INTERNATIONAL	NATIONAL TOTAL
1)		ENGINEERS		3 3
2)		SKILL LABOR		3 4
3)		UNSKILL LABOR		
B)		EQUIPMENTS		
C)		MATERIALS		
III				
PROBLEM IDENTIFICATION ON SITE				
IV				
SOLUTION AND RECOMMENDATION				
cths - Superejana didiak Instalhasan Bloku didin rune'e bale tur medida determinadu				
cths - Serbin hotu Tenke Tur degenho, BOD & spak. Tek.				
cths - Karik atu halo mudansa Serbin Tenke heten aprovasaun antes molok ser halo mudansa.				
Please acknowledge receipt this instruction by signing and dating this copy.				
Please be guided accordingly				
				
Technic ADN, I.P.				
I here by acknowledge receipt the above site instruction.				
Date: / / 2022				
Received by:				
				
Contractor Site Engineering				
Site Supervision				
Picture/video				



ANEXU D

ADN, I.P. Munisiplu Manufahi 2022

Site Instruction No. :

I				
IDENTITY OF PROJECT				
		Name of Project	: H.C. EBC Simpang Tiga	
		Location Project	: Daisua. Same - Manupahi	
		Coordinate Project	:	
		Owner Project	: MEJO	
		Contractor	: Grupo Komunitariu	
		Consultant / Supervision	: MEJO	
		Inspection Date	: 11-05-2022	
II				
INFORMATION ON SITE				
		MAN POWER	INTERNATIONAL	NATIONAL
A)		ENGINEERS		
1)		SKILL LABOR		
2)		UNSKILL LABOR		
3)				
B)		EQUIPMENTS		
C)		MATERIALS		
III				
PROBLEM IDENTIFICATION ON SITE				
IV				
SOLUTION AND RECOMMENDATION				
elms - Labeta instalata "kusen jendela" dala ida ho "lietel benu"				
e kolona tamba sei setaga "aluminium kusen jendela"				
elms - Servisa tuir degenha BOQ e spek. tek.				

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly

Fidelis M. da Costa

Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Site Supervision

Date:/...../2022

Received by:

Contractor Site Engineering




MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Estatística
Nacional, Instituto Público

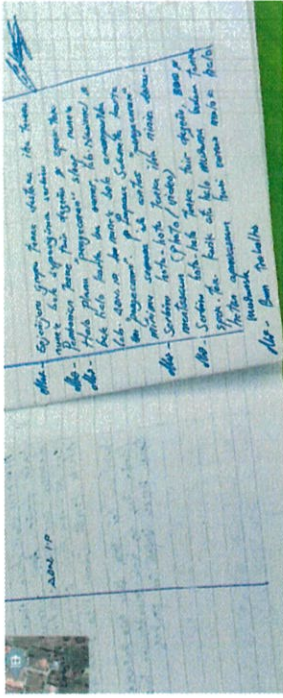INSTRUSAUN / REKOMENDASAUN					
Naran projeto : Nova Construcão Edifício EBC 1,2,3 Fatuco					
Kompanhia : Gropu Komunitariu					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	27/05/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil	
					Asinatura
					
1 Eng. Grupu tenke destaka iha terenu nune'e bele superviziona serbisu					
2 Pembesian tenke tuir dezenhu no spek. Tek.					
3 Halo planu pengecoran sloof nune'e bele halo karta ba owner, Lab Nasional no lab ADN,I.P nune'e bele akompanha pengecoran. Submete karta minimu semana ida antes loron pengecoran					
4 Serbisu hotu-hotu tenke iha ninia dokumentasaun (Photo/Video)					
5 Serbisu hotu-hotu tenke tuir dezenhu, BOQ no spek. Tek. Karik atu halo mudansa tenke hetan aprovasaun husi owner molok halo mudansa					
6 Bom traballu					



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 36)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO ESTV HALIBUR BETANO

No. kontratu :

Data Inspesaun : 17/05/2022

Fatin Inspesaun : Betano, Same - Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Pengecoran ring balk

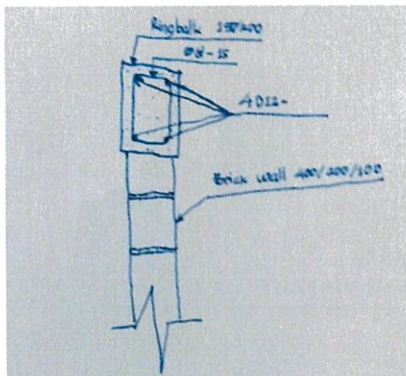

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 36)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO ESTV HALIBUR BETANO

No. kontratu :

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Betano, Same - Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho


Pengecoran ring balk

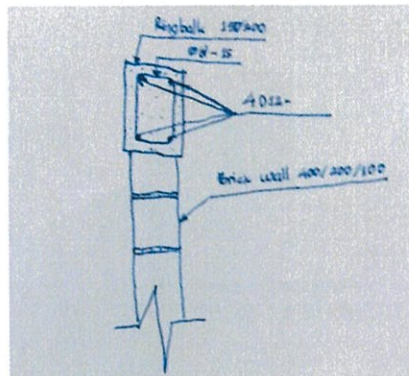

Observasaun iha tereno no Foto Aktual



Septitanck Works

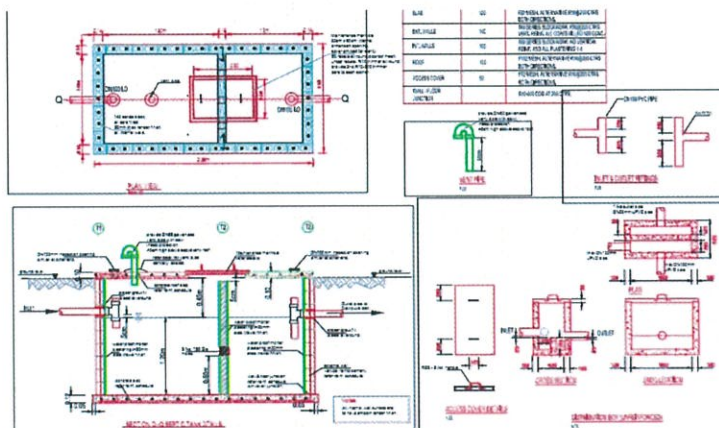



ANEXU C2 (# SAME 36)

Projeto : Nova Construção Edifício Escritório na ESTV Halibur Betano
Owner : MEJD
Localization : Betano, Same- Manufahi

MAIN SUMMARY			Up to 27042022 - progres		May Progress		Up to 27052022 - progres	
NO	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,175.00	1,905.00	1.44%	\$ 50.00	0.04%	1,955.00	1.48%
II	TEACHER OFFICE	\$ 79,003.71	11,117.97	8.39%	\$ 7,347.18	5.55%	18,465.14	13.94%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 41,447.68						
A	CONSTRUCTION COST	\$ 123,626.39	\$ 13,022.97	9.83%	\$ 7,397.18	5.58%	\$ 20,420.14	15.42%
B	CONTIGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	120.00	0.09%			120.00	0.09%
D	GRAND TOTAL	\$ 132,466.39	\$ 13,142.97	9.92%	\$ 7,397.18	5.58%	\$ 20,540.14	15.51%

Verified by:
Date, / / 2022


Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVC ADN, I.P.



ANEXU D

ADN, I.P. Municipi Manufahi 2022

Site Instruction No.:

I IDENTITY OF PROJECT

Name of Project

: N.C. ESTU Halibur Betano

Location Project

: Betano

Coordinate Project

:

Owner Project

: MEJD

Contractor

: Grupo Komunitariu

Consultant / Supervision

: MEJD

Inspection Date

: 17/05/2022

II INFORMATION ON SITE

MAN POWER

INTERNATIONAL

NATIONAL

TOTAL

A)

1)

ENGINEERS

1

1

2)

SKILL LABOR

4

4

3)

UNSKILL LABOR

6

6

B)

EQUIPMENTS

C)

MATERIALS

III PROBLEM IDENTIFICATION ON SITE

IV SOLUTION AND RECOMMENDATION

Nota - Prepare ~~ap~~ ~~aprovechamiento~~ ~~de~~ ~~material~~ ~~sira~~

Please acknowledge receipt this instruction by signing and dating this copy.

Please be guided accordingly


Technic ADN, I.P.

I here by acknowledge receipt the above site instruction.

Date: / / 2022

Received by


Contractor Site Engineering



ΣΤΑΔΝ, Ι.Ρ.

Agencia de
Desarrollo
Nacional, Instituto Público

#ANEXU D (SAMIE 23)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INTRUSAUN / REKOMENDASAUN	Asinatura
I	25/5/2022	Manufahi / Same	Ridelis Mardiano da Costa	Eng. Civil			
1	Serbiu tuir dezenhu, BOQ & spek.Tek						
2	Husu aprovasaun material husi dono projetu						
3	Halo dokumentasaun ba kada serbiu (Fotografia/Video)						

Page 1 of 3



Naran Eng. Munisipiu		FIDELIS MARDIANO DA COSTA							2022																															OBS				
		MANUFAHI					MAIU																																					
							Sa	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu							
POSTU	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU	ACTION	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31						
	8	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alifa Pereira	MPW-W-210097																																		ON-GOING				
	9	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Manu-Fahi Lui Unipessoal Lda	MPW-W210098																																		ON-GOING				
	10	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		Plan																																					
							Actual																																				17 la ba tamba fahé tempu la to'o	
S A M E	1	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	Dhalelan,Unip.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000300																																		PHO				
	2	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Dediva Electrical Unip, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385																																		ON-GOING				
	3	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430																																		ON-GOING				
	4	Konstrusaun kanalizasaun bee mos iha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Haksolok Java Motor Unip Lda	MOP - W - 190160	Plan																																	ON-GOING (BTL)				
							Actual																																					
	5	Nova fornecimento água do Bairro PNTL Manufahi	MINISTERIO DO INTERIOR	FI	Tom's Building Uipessoal Lda	SSS/053/MI-2017	Plan																																					
							Actual																																					
	6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortcio Cablaki Oan Lda	SSS/270/MOPTC-2016																																			La ba tha 18 & 25 tamba atividade terenu la la'o ho razaun hein materi ba tore			
	7	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	Monte Sul Unip.Lda	SSS/102/MOPTC-2016																																			ON-GOING			
	8	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOPTC-2016																																			ON-GOING			
	9	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/057/MOPTC-2016																																			Abandon			
	10	Road Maintenance Section Same Urban Roads Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Renova Unip Lda	MPW - W - 190215																																			ON-GOING			
	11	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Quintas das Flores, Lda	MPW - W - 190123																																			ON-GOING			
	12	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alifa Pereira	MPW -RFQ 190019																																			ON-GOING			
	13	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Leo - Dok	MPWTC-CD-170002																																			ON-GOING			
	14	Fencing for Construction Monumento do Dom Boa Ventura	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-CD	Loskabubu	RDTL/06/GM-MTAC/IV/2016	Plan																																					
							Actual																																				Abandon	
	15	Konstrusaun Tangki Beé no Menara Beé ba iha Edificio Administrasaun Municipiu Manufahi	ESTATAL	PDIM	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	Plan																																					
							Actual																																				Abandon	
	16	Konstrusaun Kuartel Bombeiros iha Same-Manufahi	MINISTERIO DO INTERIOR	PDIM	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	Plan																																					
							Actual																																				Abandon	
17	Renovasi gereja paroquia nossa senhora assuncao same	ESTATAL	PDIM	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	Plan																																						
						Actual																																						
18	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	ESTATAL	PDIM	Consortcio Deatle Hare ba Oin Lda	07/PDIM/M-MF/IX/2019	Plan																																						
						Actual																																						
19	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutur Bodik Tane Lisuk, Unip.Lda	ESTATAL	PDIM	Tutur Bodik Tane Lisuk, Unip.Lda	09/PDIM/M-MF/X/2019	Plan																																						
						Actual																																						
20	Konstrusaun Fatin isolamentu iha Municipio Manufahi, Timor Leste	MINISTERIO DA SAUDE	LM/CoVID	Daloveya	RDTL-MS-DNA-DC-20-256	Plan																																						
						Actual																																				ON-GOING	La halo monitorizasaun tamba konstrusaun fizikiu remata ona no dadauk ne hein de'it submisau pagamentu husi projetu na'in (Ministerio Saude)	
21	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Haut-Dairam Unipessoal Lda	MPW-W210092																																				ON-GOING			



Naran Eng. Munisipiu		FIDELIS MARDIANO DA COSTA					2022																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
		MANUFAHI					MAIU																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
POSTU	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU	ACTION	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
	22	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Riabale Unipessoal Lda	MPW-W-210091																																	ON-GOING																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
	23	New Construction of Laboratory ih CSI Luak,Manufahi Relasiona ba Covid19 at Ministry ofHealth, Timor Leste	MINISTERIO SAUDE	LM/CoVID	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	Plan																																ON-GOING	La ba iha 18 tamba atividade terenu la laiha																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
							Actual																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Prepara Husi :

(Eng. Fidelis Mardiano da Costa, L. Eng. Civ)
Eng. EPAS ADN,I.P. Munisipiu Manufahi

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januário Maia Guterres)
Adjunto Director Executivo ADN, I.P.

Name of Project
Location of Project
Work Item
Contractor Name

Construction Of New Bridge at Kaboska River.
 Aldeia Bemetan, Suco Betano Sub-Distrito Same, Distrito Manufahi
 Bill of Quantities
 Monte Sul Unip.Lda

Pay Item	Description	Original Contract	ADN Progress					
			Previous billing		This Billing		To Date	
			Cost (\$)	%	Cost (\$)	%	Cost (\$)	%
100	GENERAL REQUIREMENTS	\$ 10,900.00	\$ 4,325.00	1.32%	\$ 200.00	0.06%	\$ 4,525.00	1.38%
200	EARTHWORKS	\$ 20,373.64	\$ 4,163.59	1.27%	-	0.00%	\$ 4,163.59	1.27%
300	SUB BASE AND BASE COURSE	\$ 9,554.61	-	0.00%	-	0.00%	-	0.00%
400	SURFACE COURSE	\$ 12,591.00	-	0.00%	-	0.00%	-	0.00%
500	BRIDGE CONSTRUCTION	\$ 213,269.20	\$ 137,652.06	41.87%	\$ 37,514.33	11.41%	\$ 175,166.39	53.28%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	\$ 26,320.45	\$ 375.00	0.11%	\$ 375.00	0.11%	\$ 750.00	0.23%
A	TOTAL COST	\$ 293,008.90	\$ 146,515.65	44.57%	\$ 38,089.33	11.59%	\$ 184,604.98	56.15%
B	PROFIT & OVERHEAD 10% * A	\$ 29,300.89	\$ 14,651.57	4.46%	\$ 3,808.93	1.16%	\$ 18,460.50	5.62%
C	TAX 2% * (A + B)	\$ 6,446.20	\$ 3,223.34	0.98%	\$ 837.97	0.25%	\$ 4,061.31	1.24%
D	GRAND TOTAL COST (A + B + C)	\$ 328,755.98	\$ 164,390.56	50.00%	\$ 42,736.23	13.00%	\$ 207,126.79	63.00%

Prepared by : 

Eng. Romulo J.M. Henrique
 Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun
 Munispio Manufahi A D N IP

Verified by : 

Eng. Remigio da C.S.dos Santos
 Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Certified by : 

Eng. Emerenciana da Costa Maia Freitas
 Coordenadora da Unidade de controlo e validacao qualidade
 ADN IP

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (SAME 7)					
Naran projeto : Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub					
Kompanha : Monte Sul Unip.Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	5/5/2022	same villa	Romulo J.M.Henrique	Eng.M.Manufahi	1 Eng kompanhia e buku tamu iha tereno lailha
					2
					3
					4
					5
II					1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5

Asinatura

ANEXO C1 (SAME 21)

Back-up Data

Naran Projeto : R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu
Chainage 0+000 - 11+200, manufahi Municipality
No. kontratu : MPW - W - 210092

Data Inspesaun 05/5/2022

Fatin Inspesaun : Same Villa / Gtotu – Lianai - Grotu

Koordinadas :


Start Point : Latetude: 9.02101S, Long: 125.61878E

End Point : Latetude: 9.02913S, Long: 125.61682E

Naran Inspector : 1. Romulo J.M.Henrique

Sketch & Foto Desenho

Item Gabion Box

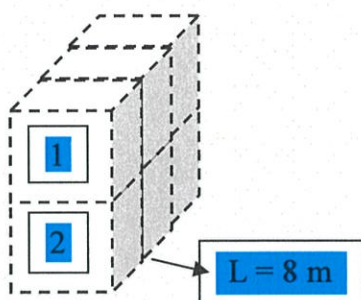

Observasaun iha tereno no Foto Aktu





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

Name of the Road : R4D Rural Road Routine Maintenance, Manico - Lianai-Grotu Chainage 0+000 - 11+200, Manufahi Municipality	
Contract No : MPW - W - 210092	
Contractor : Haut Dairam Unipessoal Lda	
Pay ITEM NO.	DESCRIPTION
R-01. General	
R-03 Earth work	
R-05 Granular sub-base and	
R-08 Structure	
R-10 Dayworks	
R-11 Routine maintenance	
R-15 Provisional Sum	
Total of R-Item	
G-01 Security	
G-02 Project Item	
G-03 Safety and Protection	
G-06 eremonal	
Total of G-Item	
A. Total - net cost	
B. Contractor's Profit (net cost x %); 10%	
C. General item	
D. Tax ((net cost + profit+ Over head) x 2 %)	
E. Total Evaluated price	

Prepared by :

Eng. Romulo J.M. Henrique

Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio Manufahi A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos

Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas

Coordenadora da Unidade de controlo e validacao qualidade ADN IP



REPUBLICA DE TIMOR-LESTE
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (SAME 21)					
Naran projeto : R4D Rural Road Routine Maintenance,Manico -Lianai-Grotu Chainage 0+000 - 11+200, manufahi Municipality					
Kompanha : Haud Dairam, Unip . Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	5/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1
					2
					3
					4
					5
II					1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5
					Asinatura
					Pagamento Ipc 01



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 9)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 6+000 - 9 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210098

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Fatuberliu / Caicasa


Koordinadas :

Start Point : Latetude: 9.01163S, Long: 125.92485E

End Point : Latetude: 8.83956S, Long: 125.63432E

Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

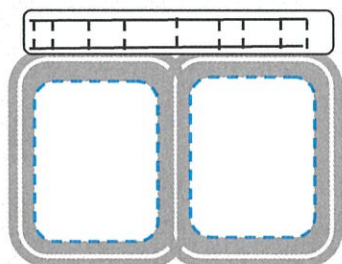

Observasaun iha tereno no Foto



Sketch & Foto Desenh Box Culvert 2

Observasaun iha tereno no Foto Aktu



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

Name of the Road: Caíasa - Fatu Cahí, Cha. 6+000 - 9+000
Contract No.: MPW-W-210098
Contractor: Manufahi Lui Unip. Lda.

Contractor: Manufahi Lui Unip. Lda.		ANEXO C2		ADN Progress							
Pay ITEM NO.	DESCRIPTION	ORIGINAL CONTRAC	Cost (\$)	BILLED QUANTITY		BILLED AMOUNT \$		Obs			
				Previous Billing		This Billing			To date		
				COST (\$)	%	COST (\$)	%	COST (\$)	%		
R-01. General		\$	4,260.00	\$ 2,870.00	0.70%	\$ 120.00		\$ 2,990.00	0.73%		
R-03 Earth work		\$	23,849.57	\$ 26,572.19	6.50%	\$ 5,082.72		\$ 31,654.91	7.74%		
R-05 Granular sub- base and		\$	7,871.18	\$ 8,045.79	1.97%	\$ 5,260.99		\$ 13,306.77	3.25%		
R-08 Structure		\$	296,194.69	\$ 176,882.40	43.27%	\$ 96,850.18		\$ 273,732.58	66.96%		
R-10 Dayworks		\$	350.00	\$ 350.00	0.09%	\$ -		\$ 350.00	0.09%		
R-11 Routine maintenance		\$	7,129.60	\$ -	0.00%	\$ -		\$ -	0.00%		
R-15 Provisional Sum		\$	1,500.00	\$ 3,000.00	0.73%	\$ 7,500.00		\$ 10,500.00	2.57%		
Total of R-Item		\$	341,155.03	\$ 216,220.38	0.53	\$ 107,313.89		\$ 323,534.26	79.14%		
G-01 Security		\$	1,518.00	\$ 1,138.50	0.28%	\$ 506.00		\$ 1,644.50	0.40%		
G-02 Project Item		\$	15,774.00	\$ 12,820.50	3.14%	\$ 6,902.50		\$ 19,723.00	4.82%		
G-03 Safety and Protection		\$	7,988.20	\$ 8,536.40	2.09%	\$ 1,802.40		\$ 10,338.80	2.53%		
G-06 eremonal		\$	250.00	\$ 125.00	0.03%	\$ -		\$ 125.00	0.03%		
Total of G-Item		\$	25,530.20	\$ 22,620.40	5.53%	\$ 9,210.90		\$ 31,831.30	7.79%		
A.Total - net cost		\$	341,155.03	\$ 216,220.38	52.89%	\$ 107,313.89		\$ 323,534.26	79.14%		
B Contractor's Profit (net cost x %) : 10%		\$	34,115.50	\$ 21,622.04	5.29%	\$ 10,731.39		\$ 32,353.43	7.91%		
C General item		\$	25,530.20	\$ 22,620.40	5.53%	\$ 9,210.90		\$ 31,831.30	7.79%		
D Tax ((net cost + profit+ Over head) x 2 %)		\$	8,016.01	\$ 5,209.26	1.27%	\$ 2,545.12		\$ 7,754.38	1.90%		
E. Total Evaluated price		\$	408,816.75	\$ 265,672.07	64.99%	\$ 129,801.30	31.75%	\$ 395,473.37	96.74%		

Prepared by :

[Signature]

Eng. Romulo J.M. Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Manufahi A D N IP

Verified by :

[Signature]

Eng. Remigio da C.s.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Certified by :

[Signature]

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao qualidade
ADN IP



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN				
ANEXO D (FTB 9)				
Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Cha. 6+000 - 9 + 000 , Manufahi Municipality				
Kompanha : Manufahi Lui Unip,Lda				
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Engenheiro A D N IP Município Manufahi
II				
III				
IV				
V				

INSTRUSAUN / REKOMENDASAUN		Asinatura
DATA NARAN HUSI KOMENTARIO / SUGESTÃO 05/15/22 Pousada (S.M.) 1km AM, 15/11/2022 - gerado um plano de melhoria para o futuro no local. - as melhorias serão feitas em fases e com o apoio da comunidade. - O plano será apresentado ao Conselho Municipal. - O plano será apresentado ao Conselho Municipal. 9.007/05S/125.919/47E 353° N Altitude: 84.2m Speed: 0.0 km/h Remark: Eng. Uzziaza 309 Index number: 227 Network: May 25, 2022 12:05:22 PM GMT+09:00 Local: May 25, 2022 12:05:21 PM GMT+09:00		



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 8)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 9+000 - 12 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210097

Data Inspesaun : 25/ 05 /2022

Fatin Inspesaun : Fatuberliu / Caicasa


Koordinadas : Start Point : Latetude 8,98929S, Long: 125.91554E

End Point : Latetude: 8.99180S , Long: 125.91715E

Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

Lean concrete & Plum concrete



Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

Catcaca Fatucahi Cha. 9+000 - 12 + 000
No. Contrato: MPW-W-210097
Contractor : Alifa , Unipessoal Lda

ANEXO CI			ADN Progress					
Pay ITEM NO.	DESCRIPTION	ORIGINAL CONTRAC	BILLED QUANTITY		BILLED AMOUNT \$		To date	Obs
		Cost (\$)	Previous Billing		This Billing			
			COST (\$)	%	COST (\$)	%	COST (\$)	%
R-01. General		\$ 6,750.00	\$ 2,700.00	0.64%	\$ -	0.00%	\$ 2,700.00	0.64%
R-03 Earth work		\$ 33,772.23	\$ 16,152.20	3.83%	\$ 3,206.71	0.76%	\$ 19,358.92	4.59%
R-05 Granular sub-base and		\$ 14,510.70	\$ -	0.00%	\$ 3,206.71	0.76%	\$ 3,206.71	0.76%
R-08 Structure		\$ 293,226.65	\$ 78,143.64	18.53%	\$ 151,872.98	36.01%	\$ 230,016.62	54.54%
R-10 Dayworks		\$ 350.00	\$ 70.00	0.02%	\$ -	0.00%	\$ 70.00	0.02%
R-11 Routine maintenance		\$ 5,699.75	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
R-15 Provisional Sum		\$ 1,500.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
Total of R-Item		\$ 355,809.33	\$ 97,065.84	23.02%	\$ 162,335.04	38.49%	\$ 259,400.89	61.51%
G-01 Security		\$ 1,440.00	\$ 360.00	0.09%	\$ -	0.00%	\$ 360.00	0.09%
G-02 Project Item		\$ 9,420.00	\$ 2,028.34	0.48%	\$ 10,320.00	2.45%	\$ 12,348.34	2.93%
G-03 Safety and Protection		\$ 10,960.00	\$ -	0.00%	\$ 7,326.00	1.74%	\$ 7,326.00	1.74%
G-06 removal		\$ 250.00	\$ 125.00	0.03%	\$ -	0.00%	\$ 125.00	0.03%
Total of G-Item		\$ 22,070.00	\$ 2,513.34	0.60%	\$ 17,646.00	4.18%	\$ 20,159.34	4.78%
A.Total - net cost		\$ 355,809.33	\$ 97,065.84	23.02%	\$ 162,335.04	38.49%	\$ 259,400.89	61.51%
B.Contrictor's Profit (net cost x %) : 10%		\$ 35,580.93	\$ 9,706.58	2.30%	\$ 16,233.50	3.85%	\$ 25,940.09	6.15%
C.General item		\$ 22,070.00	\$ 2,513.34	0.60%	\$ 17,646.00	4.18%	\$ 20,159.34	4.78%
D.Tax ((net cost + profit+ Over head) x 2 %)		\$ 8,269.21	\$ 2,185.72	0.52%	\$ 3,924.29	0.93%	\$ 6,110.01	1.45%
E. Total Evaluated price		\$ 421,729.47	\$ 111,471.48	26.43%	\$ 200,138.84	47.46%	\$ 311,610.32	73.89%

Prepared by :

Eng. Romulo J.M.Henrique
Munisipio Manufahi A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade
ADN IP



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXOD (FTB8)

Kompanha : Alifa Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1 2 3 4 5
II					1 2 3 4 5
III					1 2 3 4 5
IV					1 2 3 4 5
V					1 2 3 4 5



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 04)

Back-up Data

Naran Projeto : New Construction Of Sukar oan River Cyclop Concrete Retening Wall
And Gabion Work

No. kontratu :

Data Inspesaun : 25/5/2022

Fatin Inspesaun : Mota clere fatu berliu

Koordinadas :

Start Point : Long : 125.94733 E, Latetude : 9.030666666666668 S

End Point : Long : 125.94008334 E , Latetude ; 9.05274668 S S


Naran Inspector : 1.Romulo J.M.henrique

Sketch & Foto Desenho

Sketch Item servisu Bronjong

P = 624 m

T = 5 m

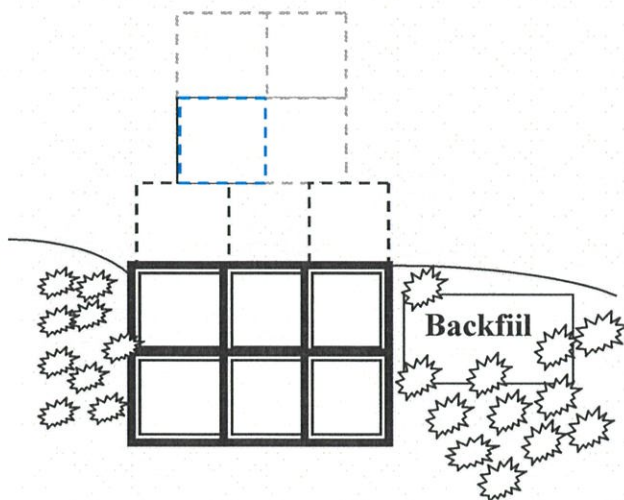

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desempenho
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (FTB 4)					
New Contruction of Sukaer oan river Cyclop Concrete Retaining Wall And Gabion					
Kompanha : Samdil Unipessoal Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1 2 3 4 5
II					1 2 3 4 5
III					1 2 3 4 5
IV					1 2 3 4 5
V					1 2 3 4 5

Asinatura

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (FTB 5)					
Naran projeto : R4D Rural Roads Rehabilitation Feriksale Chainage 0 + 000 - 6 + 350, Manufahi Municipality					
Kompanha : Mardiroring Viqsan Unip.Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1
					2
					3
					4
					5
II					1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5

Asinatura




ANEXO C1 (FTB 6)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 0+000 - 6 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210099

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :


Start Point : Latetude 9.01605S, Long: 125.92783E

EndPoint: Latetude: 8.83956S , Long: 125.63432E

Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

Plum Concrete



Observasaun iha tereno no Foto Aktu



Sketch & Foto Desenho

Observasaun iha tereno no Foto

REPUBLICA DE TIMOR-LESTE

MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, LP.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

ANEXO D (FTB 6)

Naran projeto :R4D Rural Road Spot Improvement Betano - Loro Chainage
0+000-6+000, Manufahi Municipality

Kompanha : Loskabubu Unip Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1
					2
					3
					4
					5
II					1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5

Asinatura

[Handwritten signature]



ANEXO C1 (SAME 25)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-
6+300 Municipality
No. kontratu : MPW - W - 210094

Data Inspesaun 25/5/2022

Fatin Inspesaun : Same Villa / Betano

Koordinadas :

Start Point : Latetude: 9.14481S, Long: 125.67136E

End Point : Latetude: 9.04344S, Long: 125.90355E

Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

Item Gravel



Observasaun iha tereno no Foto



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktu



INSTRUSAUN / REKOMENDASAUN				
ANEXO D (Same 25)				
Naran Projeto : R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300				
Kompanha : Tutur Bodik Tane Lisuk, Unip.Lda				
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi
II				
III				
IV				
V				

INSTRUSAUN / REKOMENDASAUN		Asinatura
1	Buku tamu no eng laih tereno Laiha	
2		
3		
4		
5		
1		
2		
3		
4		
5		
1		
2		
3		
4		
5		
1		
2		
3		
4		
5		
1		
2		
3		
4		
5		




MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

Naran Projeto		CONSTRUSAUN PONTE E RIO DE KASABOKA AT BE METAN ,BETANO SAME SUB DISTRIC MANUFAHI				
No. kontratu		SSS / 102/MOPTC-2016				
ANEXO C1 (SAME 7)						
Data Inspesaun		8/4/2022				
Fatin Inspesaun		SAME VILLA				
Koordinadas						
	Start Point	Long	9.16700S	Latetude		125.71613E
	End Point	Long	9.16684S	Latetude		125.71608E

Sketch & Foto Desenho

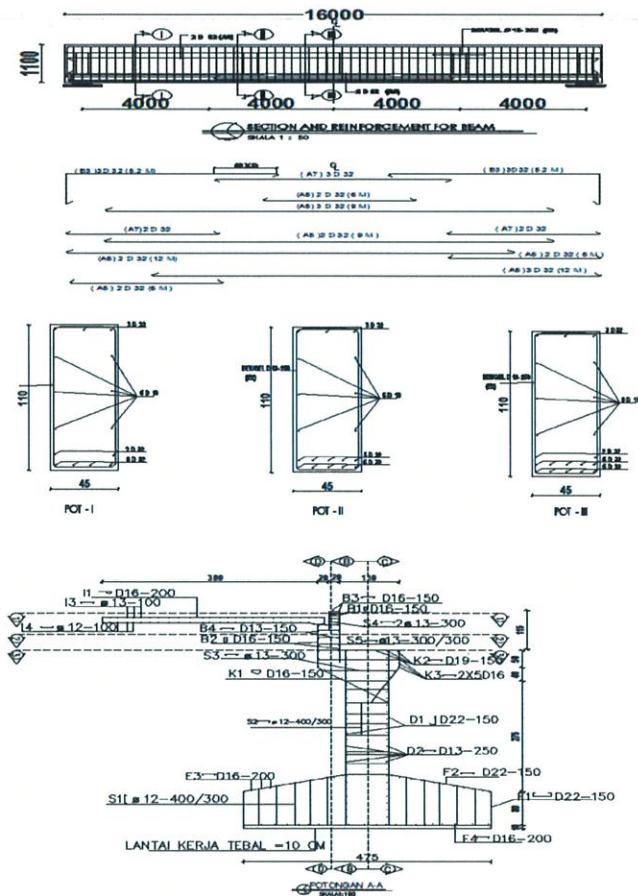



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, LP.

Agência de
Desenvolvimento
Territorial, Investimento Público

INSTRUSAUN / REKOMENDASAUN

ANEXO D (SAME 7)

Naran projeto : Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub

Kompanha : Monte Sul Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	25/5/2022	same villa	Romulo J.M.Henrique	Eng.M.Manufahi	1	Serbisu Parado Hela Eng no Buku tamu lha loaksi lalha	
					2		
					3		
					4		
					5		
II				Eng.M.Manufahi	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 7)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Sp Satu Cha. 0+000 - 7
+ 900 , Manufahi Municipality

No. kontratu : MPW - W - 210095

Data Inspesaun : 25/05/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :

Start Point : Latetude : 9.03677S, Long: 125.99846E

EndPoint: Latetude : 9.05708S, Long: 125.02474E


Naran Inspector : 1. Romulo J.M.Henrique

Sketch & Foto Desenho

Gravel



Observasaun iha tereno no Foto Aktu

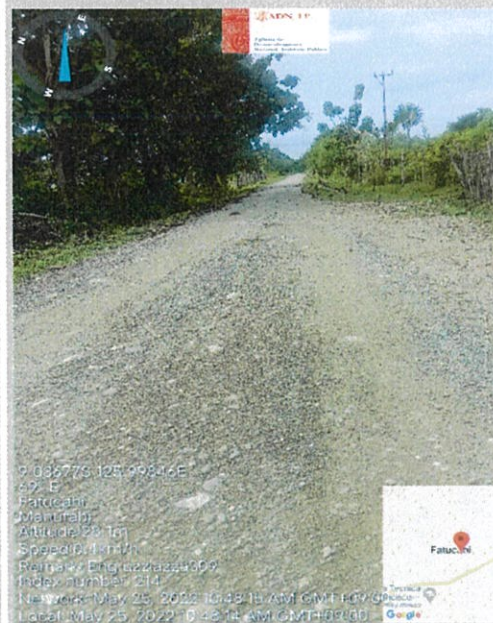

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (FTB 7)					
Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Sp Satu Cha. 0+000 - 7 + 900 , Manufahi Municipality					
Kompanha : Leo Hilin Unip,Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	25/052022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1
					2
					3
					4
					5
II					1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5

Asinatura





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (ALA 13)

Back-up Data

Naran Projeto : Rural Road Routine Maintanance , Dotic - Weberek Cha.

0+000 - 6 + 300 , & Dotic - Wekakaoan Cha , 0 + 000 - 8 + 600 Manufahi

Municipality

No. kontratu

: MPW - W - 210093

Data Inspesaun 25/5/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :


Start Point : Latetude: 9.06318S, Long: 125.89286E

End Point : Latetude: 9.04344S, Long: 125.90355E

Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

Observasaun iha tereno no Fo

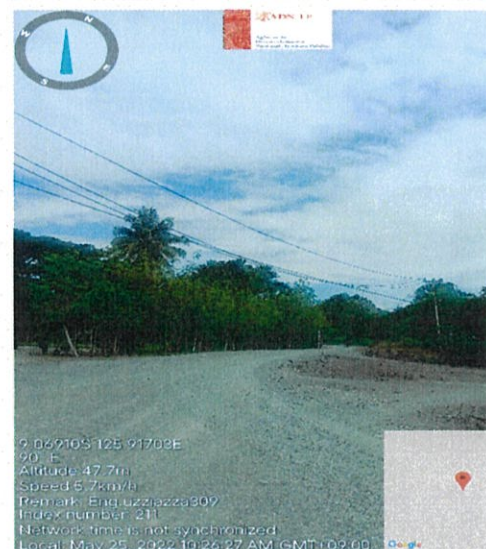



Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXOD (ALS 13)

Naran projeto :Rural Road Maintenance Dotik - Weberek Cha. 0+000 -6 + 300 & Dotik - Wekakaosan Cha, 0 + 000 - 8 + 600, Manufahi Municipality

Kompanha : Werenek Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	25/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1	Buku Tamo no Eng iha terreno lailha Serbisu Parado hela	
					2		
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		



ANEXO C1 (SAME 22)

Back-up Data

Naran Projeto : R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 -
1+200, Same - Rotuto Chainage 0+000 - 12+000 , Manufahi Municipality
No. kontratu : MPW - W - 210091

Data Inspesaun 26/5/2022

Fatin Inspesaun : Same Villa / Rotuto & Ladiki


Koordinadas :

Start Point : Latetude: 8.97481S, Long: 125.61921E

End Point : Latetude: 9.970755S, Long: 125.60544E

Naran Inspector : 1. Romulo J.M.Henrique

Sketch & Foto Desenho



Observasaun iha tereno no Foto Aktu



Sketch & Foto Desenho

Hamos Du'ut no hasai Rai husi Valeta laran

Observasaun iha tereno no Foto Aktu



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, IP.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

ANEXO D (SAME 22)

Naran projeto R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi

Kompanha : Riabile Unipessoal Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/5/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1	Eng iha tererno laih , Buku tamu mos laiha	
					2	Pagamento Ipc 01	
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		

 REPUBLICA DE TIMOR-LESTE MINISTÉRIO DO PLANO E ORDENAMENTO SECRETARIA DE PLANEJAMENTO E ORÇAMENTO ADN, LP Agência de Desenvolvimento Municipal, Saneamento Público																																				
Naran Eng.		Romulo J.M.Henrique																																		
Munisipiu		MANUFAHI																																		
Postu	No	NARAN PROJETU	DONO PROJETO	KATEGORIA PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	Action	MAIO																												OBSERVASAUN
								Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	
ALAS (ALS)	1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	Samboio Unip,Lda	RDITL/MOP-SEE/CGI-PEN : 0000119																														
	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakan Oan 2	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortorio Nacional Manufahi Lda	SSS/148/MOPTC-2017	Plan																									PARADO				
							Actual																													
	3	Emergency new construction of gabion box protection random fill in area Lacio, Baria Laran, Uma Berloik, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortorio 1912 MF Lda	SSS/279/MOPTC-2016	Plan																								PROJERU REMATA ONA					
							Actual																													
	4	Rural Roads Routine Maintenance Dotic Weberck, Chainage 0+000 - 6+300, Dotic Wekakaon, Chainage 0+000 - 8+600, Tukumu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Samboio Unip,Lda	MPW-RFQ-190017	Plan																								PARADO					
							Actual																													
	5	Prefurasan Be'e mos iha Suku Uma Berloik, Aldeia Besusu	MINISTERIO DAS OBRAS PUBLICAS	LM	Buka Fini	MPWTC-NCB-170008	Plan																													
							Actual																													
	6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	Plan																									PARADO				
							Actual																													
	7	Kontinuasaun Kanalizasaun Kanu Transmisau no Distribuissau Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM	Tane Unipessoal Lda	MOP - W - 190210	Plan																													
							Actual																													
8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	MINISTERIO DAS OBRAS PUBLICAS	LM	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033																															
9	Construction and Installation water Gravitation System in Mahaquidam Umberloik Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Vereskar Unip. Lda	SSS/289/MOPTC-2016	Plan																														
						Actual																														
10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	My Friend Unip. Lda	MPW-W-190106	Plan																									PHO / FALTA RETENSAUN					
						Actual																														
11	Rehabilitasaun Estrada Tekunu-Feriksate 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/062/MOPTC-2016	Plan																									PARADO					
						Actual																														
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortorio Unimafa Lda	SSS/150/MOPTC-2017	Plan																									PARADO					
						Actual																														
13	R4D Rural Road Routine Maintenance, Dotic - Weberck Chainage 0+000 - 6+300 and Dotic - Wekakaon Chainage 0+000 - 8+600 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Wereneck Unipessoal Lda	MPW-W-210093	Plan																									PA RADO HELA					
						Actual																														
FATUBERLIU (FTB)	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	Plan																									PARADO				
							Actual																													
	2	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	MINISTERIO DAS OBRAS PUBLICAS	FI	concorcio Nasional ba Futuro	SSS/149/MOPTC-2017	Plan																								PARADO					
							Actual																													
	3	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Funu Kolik Unip. Lda	RDITL/MOPTC-VMOPTC/CGI-PEN : 00000424																														
	4	New Construction of Sukaer Oan River cyclop Concrete Retaining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortorio Nacional Samdil, Lda (CNS)	SSS/102/MOPTC-2017	Plan																									PARADO HELA				
							Actual																													
	5	R4D Rural Road Routine Maintenance, Tukumu Feriksare Chainage 0+000-6+350 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MARDIROMIG VIQSAM, UNIPessoal LDA	MPW- W - 210096	Plan																									PARADO HELA				
							Actual																													
	6	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Loskabubu	MPW-W-210099	Plan																									ON-GOING				
							Actual																													
7	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Leo-Hilin Unipessoal Lda	MPW-W-210095	Plan																									ON-GOING					
						Actual																														
8	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alifa Pereira	MPW-W-210097	Plan																									ON-GOING					
						Actual																														
9	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Mamu-Fahi Lai Unipessoal Lda	MPW-W210098	Plan																									ON-GOING					
						Actual																														
	1	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	Dhalelan,Unip.Lda	RDITL/MOPTC-VOMPTC/CGI-PEN:0000300																														
	2	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Dediva Electrical Unip. Lda	RDITL/MOPTC-VMOPTC/CGI-PEN : 00000385	Plan																													
							Actual																													
	3	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbalau, Erluli, Luak, Ailok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	Fahia Humalo Unip.Lda	RDITL/MOPTC-VMOPTC/CGI-PEN : 00000430																														
	4	Konstrusaun kanalizasaun bee mos iha selhasan suco Betano, Posto Adm Same, Municipio Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM	Hakoolok Java Motor Unip Lda	MOP - W - 190160	Plan																													
							Actual																													
5	Nova fornecimento água do Bairro PNIL Manufahi	MINISTERIO DO INTERIOR	FI	Tom's Building Unipessoal Lda	SSS/053/MI-2017	Plan																														
						Actual																														
6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortorio Cablaki Oan Lda	SSS/270/MOPTC-2016	Plan																									PARADO					
						Actual																														
7	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	Plan																									PARADO					
						Actual																														

MINISTÉRIO DO PLANO E ORDENAMENTO VI CONSTITUINTE ADN, I.P. Agência de Desenvolvimento Nacional, Investimentos Públicos							PLANU INSPESAUN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
Naran Eng.							2022																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
Munisipiu							MANUFAHI																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
							MAIO																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
8	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOFTC-2016	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Note: Planu Periode inspesaun iha tercinu Implementa Planu Periode Inspensaun iha Terenu Inspeksaun Prosesu Pagamento

Prepara Husi :


(Eng. Romulo J.M. Henrique)
Engenheiro ADN IP Manufahi

Sertifika Husi :


(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN IP

Aprova Husi :


(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN IP



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 3)

Back-up Data

Naran Projeto : **New Installation MV, Line Transformer and LV Line from Dotik to Alas Manufahi District**

No. kontratu : RDTL/MOP-SEE/CGI-PEN : 0000119

Data Inspesaun : 26/5/2022

Fatin Inspesaun : Manufahi

Koordinadas :

Start Point : Long : -9,05.94.69, Latetude : 125,39.58.14

End Point : Long : -9,23.43.85, Latetude : 125,39.43.27


Naran Inspector : **1. Silvino D. R. Rebelo Soares**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu

Laiha Aktividade Iha Tereno

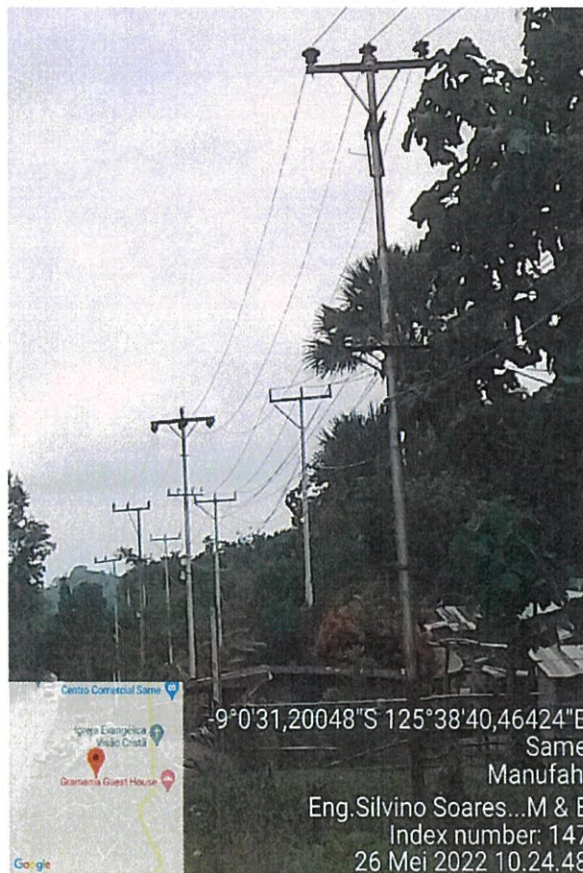



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 3)

Back-up Data


Naran Projeto : **New Installation MV, Line Transformer and LV Line from Dotik to Alas Manufahi District**

No. kontratu : **RDTL/MOP-SEE/CGI-PEN : 0000119**

Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual

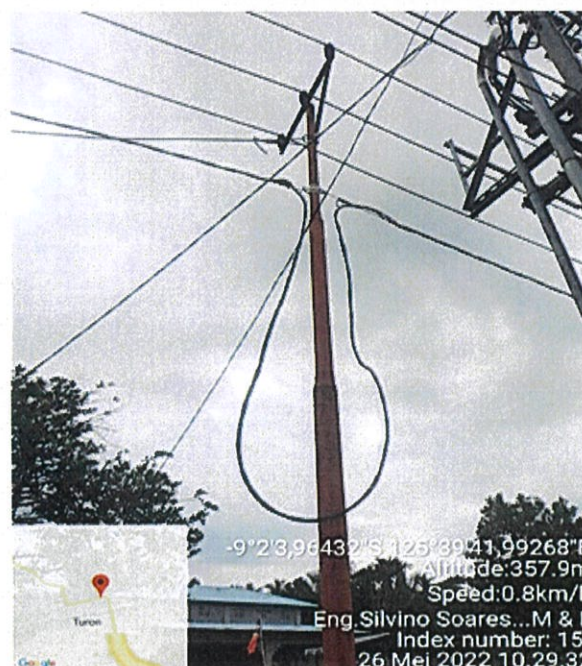



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 2)

Back-up Data

Naran Projeto : New Installation of MV, LV Line and House Connection from Tugu
Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi
Municipality

No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385

Data Inspesaun : 26/5/2022

Fatin Inspesaun : Manufahi – Tugu Betano

Koordinadas :

Start Point : Long : -9,95.43.78, Latetude : 125,43.46.02

End Point : Long :, Latetude :

Naran Inspector : 1. Silvino D. R. Rebelo Soares

Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual

Linha Refere Espaso Laiha Ona Atu
Kontinua





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 2)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality**

No. kontratu : **RD TL/MO PTC-VMO PTC/CGI-PEN : 00000385**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 2)

Back-up Data

Naran Projeto : New Installation of MV, LV Line and House Connection from Tugu
Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi
Municipality
No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385

Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN					
Naran projeto : New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi					
Kompanha : Dediva Electrical Unip, Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	26/5/2022	Manufahi / Same	Silvino D. R. R. Soares	Tekniku M & E - ADN, I.P	1
					2
					3
					4
					5
II					1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5
					Asinatura
					Trafo1 (100 KVA) Monta Lampu Manutensaun
					Hadia fiu nebe mak monu
					Muda Fiu TR, lokasi Betanu Simpan Tiga (Foti husi TR Existing)
					Arde Cdauk monta (Fiu TR Monu)



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FATUBERLIU – 4)

Back-up Data

Naran Projeto : New Installation MV, LV Line and House Connection from Tatekar to
Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality
No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424

Data Inspesaun : 26/5/2022

Fatin Inspesaun : Manufahi - Fatuberliu

Koordinadas :

Start Point : Long : -9,13.22.92, Latetude : 125,56.97.02

End Point : Long : -8,38.58.58, Latetude : 125,54.46.72

Naran Inspector : 1. Silvino D. R. Rebelo Soares


Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual

Basea Ba Data Nebe Mak Teknik ME – AND,I.P
Hatene Katak Linha Refere Laiha Ona Espaso Hodi
Kontinua.

Hadia Pin Post Nebe Mak Kleuk

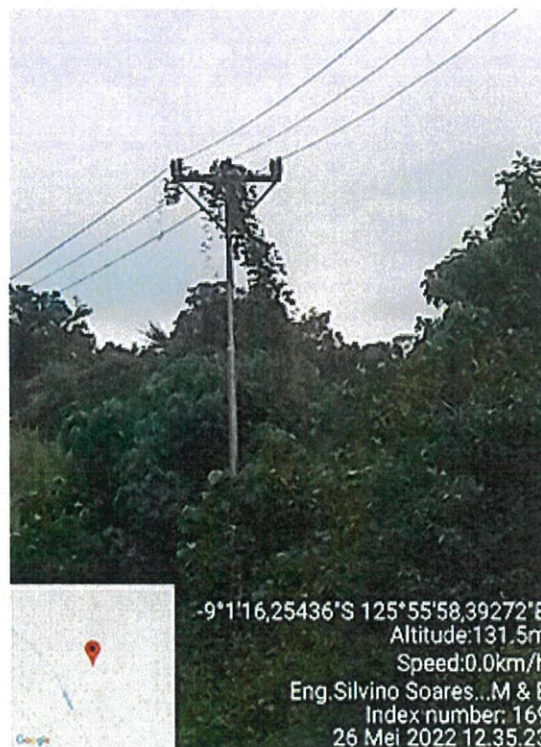

-9°1'16,25436"S 125°55'58,39272"E
Altitude:131.5m
Speed:0.0km/h
Eng.Silvino Soares...M & E
Index number: 169
26 Mei 2022 12.35.23



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FATUBERLIU – 4)

Back-up Data

Naran Projeto : New Installation MV, LV Line and House Connection from Tatekar to
Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality
No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FATUBERLIU – 4)

Back-up Data

Naran Projeto : New Installation MV, LV Line and House Connection from Tatekar to
Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality

No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (ALAS -1)

Back-up Data

Naran Projeto : New Installation MV, Line Transformer and LV Line from Dotik to Alas
Manufahi District

No. kontratu : RDTL/MOP-SEE/CGI-PEN : 0000119

Data Inspesaun : 26/5/2022

Fatin Inspesaun : Manufahi - Alas

Koordinadas :

Start Point : Long : -9,31.32.78, Latetude : 125,52.57.15

End Point : Long : -9,05.43.78, Latetude : 125,46.53.59


Naran Inspector : 1. Silvino D. R. Rebelo Soares

Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual

Hadai Treckschoor Nebe Mak Mamar

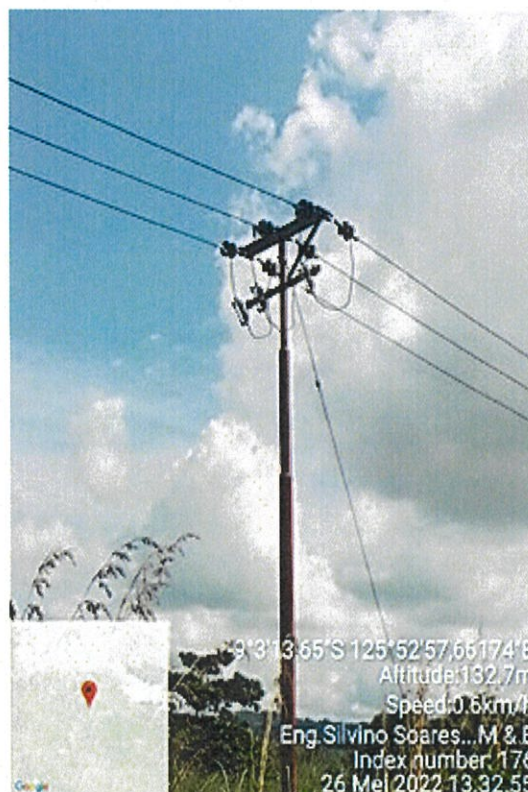



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (ALAS -1)

Back-up Data

Naran Projeto : New Installation MV, Line Transformer and LV Line from Dotik to Alas
Manufahi District
No. kontratu : RDTL/MOP-SEE/CGI-PEN : 0000119

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (ALAS -1)

Back-up Data

Naran Projeto : **New Installation MV, Line Transformer and LV Line from Dotik to Alas
Manufahi District**

No. kontratu : **RDTL/MOP-SEE/CGI-PEN : 0000119**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual





MINISTERIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District

Kompanha : Samboio Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/5/2022	MANUFAHI / ALAS	SILVNO D. R. R SOARES	TEKNIKO M & E, ADN - I.P	1	Tenki Hadia Schoor Nebe Mak Mamar no Kotu Tena	
					2	Tenki Pintia Fali Airing Nebe Mak Tinta Sai Hotu Ona	
					3	Tesi AI Nebe Mak Besik Ba Linha MV ho LV	
					4	Halos Airing Nebe Mak Halis	
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL ORA  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público							PLANU INSPESAUN																															
Naran Eng.	Silvino Domingos Rita Rebelo Soares						2022																															
Município	MUNICIPIO MANUFAHI NO POSTOS																																					
Município / Posto	No. Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	Action	Maio																															OBS
							1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
	35	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	36	Konstrusaun ka rehabilitasaun ba ESTV Halbur Betano	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
TURISCAI (TRS)	2	Const. MCK (Saude) Orana	Gerasaun Malkau Unip. Lda	01/PDIMM-MF/V/2019	PDIM	ESTATAL	Plan																															
							Actual																															
TOTAL PROJETO ON-GOING																																						

Note:

Planu Periode inspesaun iha tereinu

Implementa Planu Periode Inspensaun

Relatoriu avaliasuan mensal iha Dili

Inspesaun Proceu Pagamentu

Prepara Husi :



(Silvino D.R. Rebelo Soares)
Eng. Electricidade, ADN - I.P

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ,ADN -

Aprova Husi :



(Eng. Januario Maia Guterres)
Adjunto Director Executivo,ADN - I.P



2022

Municipio	MUNICIPIO MANUFAHI NO POSTOS
-----------	------------------------------

Maio

OBS

[illegible]

 MINISTÉRIO DO PLANO E ORDENAMENTO VII CONTRATO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público							PLANU INSPESAUN																																	
Naran Eng.	Silvino Domingos Rita Rebelo Soares						2022																																	
Município	MUNICIPIO MANUFAHI NO POSTOS																																							
Município / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	Action	Maio																															OBS	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		
TURISCAI (TRS)	35	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	36	Konstrusaun ka rehabilitasaun ba ESTV Halbur Betano	MEJD PKRIE ESTV HALBUR BETANO	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	2	Const. MCK (Saude) Orana	Gerasaun Malika Unip. Lda	01/PDIM-MFV/2019	PDIM	ESTATAL	Plan																																	
							Actual																																	
		TOTAL PROJETO ON-GOING																																						

Note:

Planu Periode inspesaun iha tercinu


Implementa Planu Periode Inspesaun


Relatoriu avaliasuan mensal iha Dili

Inspesaun Proceso Pagamentu

Prepara Husi:

(Silvino D. R. Rebelo Soares)
Eng. Electricidade, ADN - I.P.

Sertifica Husi:

(Eng. Emerenciana da Costa Mala Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN -

Aprova Husi:

(Eng. Januario Mala Guterres)
Adjunto Director Executivo, ADN - I.P.
