



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL
IMPLEMENTASAUN
PROJETUS MUNISÍPIU MANUFAHI

SETEMBRO 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO MANUFAHÍ


SETEMBRO 2022

Prepara Husi :




(Eng. Fidelis Mardiano da Costa)

Eng. ba Edifício Público no Beé Saneamento, Município Manufahi



(Eng. Romulo J.M. Henrique) & (Eng. Majorico Cele Tali)

Eng. ba Projeto Infraestrutura e Irigasaun, Município Manufahi ADN, I.P



(Silvino D R R Soares)

Eng. M & E, Município Manufahi ADN, I.P

Verifika Husi :



(Arc. Francisco X D D Jeronimo)
Eng. Senior ba Edifício Público no Beé
Saneamento, ADN, I.P



(Eng. Remigio da C.S.dos Santos)
Eng. Senior ba Projeto Infraestrutura e Irigasaun,
ADN, I.P



(Deolindo de F Marques)

Chefe Sek. Projeto M.E & ITC, ADN, I.P

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)

Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :



(Mariano Renato Monteiro da Cruz, S. T, M. Eng)

Director Executivo, ADN, I.P



Contents

SUMÁRIO	0
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Manufahi	0
INDICE TABELA	0
I. INTRODUSAUN.	2
1.1 Enkuadramentu Legal.....	2
1.2 Perfil Municipio Manufahi.....	2
1.3. Lista Projecto.....	5
II. PROGRESU FISIKU	19
2.1 Progreso Fisiku Kada Fulan	19
III. OBSTÁCLO IHA TERENU	19
3.1 Obstáculo Servisu Iha Terenu	19
IV. REKOMENDASAUN IHA TERENU	20
4.1 Rekomendasaun Servisu Iha Terenu	20
Tabela 1 : Postos Administrativos,Sucos no Aldeias.	3
Tabela 2.1: Forca de Trabalho ADN, I.P Municipio Manufahi.	3
Tabela 3.2 : Lista Asset ADN,I.P Municipio Manufahi.	4
Tabela 4.3.1 :Projecto Municipio Manufahi Por Fundus Finansiamento.....	5
Tabela 5.3.2 : Projecto Municipio Por Sector	9
Tabela 6.3.3 : Projecto Municipio Por Ministerio	14

I. INTRODUSAUN.


1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefísiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimento nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projetu sira iha programa Kapital Desenvolvimento nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liuhusi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Manufahi

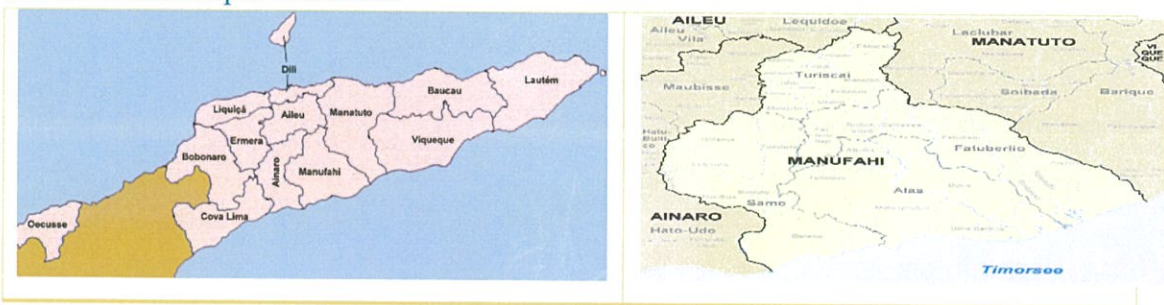

Mapa 2 hatudu pozisaun jeográfika Administrasaun Munisipal Manufahi iha luan 1,325 km² ho populasan nain 48,628 tuir Sensus 2010. Administrasaun Munisipal Manufahi iha Postos Administrativos ha'at, Sukus 29 no aldeias 137, mak hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos,Sucos no Aldeias.

Alas		Fatuberlio		Same		Turiscail	
Sukus	Aldeias	Sukus	Aldeias	Sukus	T.Aldeias	Sukus	Aldeias
Aituha	2	Bubussuso	5	Babulo	8	Aitemua	2
Dotic	3	FAtukahi	5	Betano	7	Beremana	3
Mahaquidan	5	Caicassa	4	Dai-sua	5	Fatucalo	2
Taitudac	5	Clauc	5	Grotu	3	Foholau	3
Uma berloic	4	Fahinehan	4	Holarua	13	Caimauc	5
-	-	-	-	Letefoho	7	Lessuata	4
Total	19	-	23	-	43	-	19

Data husi: Livro 3 B OJE 2021, pag 75

Tabela 2.1: Forca de Trabalho ADN, I.P Municipio Manufahi.

Forca de Trabalho ADN,I.P Municipio Manufahi/ Same								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	2					2	
2	Administrasaun no Financas	0					0	
3	Motorista	1					1	
4	Seguransa	0					0	
Total		3					3	

Tabela 3.2 : Lista Asset ADN,I.P Municipio Manufahi.

ASET ADN,IP MUNICIPIO MANUFAHI								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1						
2	Kareta	1						
3	Desktop HP / Monitor	1						
4	Laptop HP	1						
5	Printer Cannon	1						
6	UPS	1						
7	Armario File	2						At ona
8	Armario Tau hena	3						1 at ona
9	Meja escritorio	1						
10	Meja han	1						
11	Meja TV (kiik)	1						
12	Kadeira escritorio	6						
13	Kadeira han	4						
14	Sofa	1 Set						
15	Springbed +sumasu 4+sprei 3	3 Set						
16	Jeleira	1						
17	Water Dispenser	1						At ona
18	TV + Parabola	1 Set						Parabola La funciona
19	Kipas Angin	4						
20	Kompor	1						At ona
21	Kompor Gas	1						At ona
22	Rack Piring	1						
23	Lampu	11						
24	Water Pump Sanyo	1						

1.3. Lista Projecto

Projetu hotu neébe akumulá iha lista neé bazeia ba dados projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamento, tabela 1.3.2 Projetu por Sector no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabela 4.3.1 :Projecto Municipio Manufahi Por Fundus Finansiamento

NO	POSTO ADMINISTRATIVO	TOTAL FI		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	6	\$ 3,314,853.37	58.78%
2	Fatuberliu	5	\$ 6,315,903.07	68.24%
3	Same	10	\$ 7,629,797.23	35.44%
4	Turiscái	3	\$ 4,690,158.04	77.78%
Grand Total		24	\$ 21,950,711.71	57.45%

NO	POSTO ADMINISTRATIVO	TOTAL LM Covid 19		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas			
2	Fatuberliu			
3	Same	3	\$ 383,412.81	88.62%
4	Turiscái			
Grand Total		3	\$ 383,412.81	88.62%

NO	POSTO ADMINISTRATIVO	TOTAL LM BS		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	2	\$ 587,548.52	72.60%
2	Fatuberliu			
3	Same	2	\$ 306,911.16	64.79%
4	Turiscail	1	\$ 570,200.00	70.00%
	Grand Total	5	\$ 1,464,659.68	69.95%

NO	POSTO ADMINISTRATIVO	TOTAL LM CD		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	4	\$ 766,506.99	67.86%
2	Fatuberliu	5	\$ 1,318,810.35	57.79%
3	Same	9	\$ 737,705.12	59.46%
4	Turiscail	1	\$ 278,252.69	0.00%
	Grand Total	19	\$ 3,101,275.15	55.49%

c	POSTO ADMINISTRATIVO	TOTAL TRANFERENCIA PUBLICO		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	3	\$ 329,649.24	24.87%
2	Fatuberliu	1	\$ 194,674.39	0.00%
3	Same	11	\$ 1,062,554.76	24.22%
4	Turiscái			
Grand Total		15	\$ 1,586,878.39	21.38%

c	POSTO ADMINISTRATIVO	TOTAL PDID		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	4	\$ 514,865.29	53.58%
2	Fatuberliu			
3	Same	5	\$ 928,527.70	90.41%
4	Turiscái	1	\$ 7,530.00	69.97%
Grand Total		10	\$ 1,450,922.99	77.23%

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM BS+CD+Covid19 + TP+PDID		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	19	\$ 5,513,423.41	59.00%
2	Fatuberliu	11	\$ 7,829,387.81	64.78%
3	Same	40	\$ 11,048,908.78	43.24%
4	Turiscail	6	\$ 5,546,140.73	73.07%
	Grand Total	76	\$ 29,937,860.73	57.30%

Dadus detallu kada projetu: #Anexu

Tabela 5.3.2 : Projecto Municipio Por Sector

NO	SECTOR PROJECTO	Alas		
		TOTAL PROJECT O	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	FLOOD CONTROL	1	\$ 39,533.06	75.13%
2	AGUA E SANEAMENTO	2	\$ 299,631.00	50.63%
3	Basic Road Construction			
4	EDIFICIOS PUBLICOS			
5	EDUKASAUN	3	\$ 329,649.24	24.87%
6	ELETRIFIKASAUN NASIONAL	1	\$ 1,108,760.78	78.57%
7	ESTRADAS	6	\$ 2,354,740.57	51.55%
8	ESTRADAS E PONTES			
9	FLOOD CONTROL	3	\$ 475,332.23	51.79%
10	JUVENTUDE NO DESPORTU			
11	MANUTENSAUN NO REHABILITASAUN	3	\$ 905,776.53	72.70%
12	PONTES			
13	SAUDE			
14	SEGURANCA NO DEFESA			
15	SOLIDARIEDADE E SOCIAL			
16	TURISMO			
	Grand Total	19	\$ 5,513,423.41	59.00%

NO	SECTOR PROJECTO	Fatuberliu		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	FLOOD CONTROL			
2	AGUA E SANEAMENTO			
3	Basic Road Construction			
4	EDIFICIOS PUBLICOS			
5	EDUKASAUN	1	\$ 194,674.39	0.00%
6	ELETRIFIKASAUN NASIONAL	1	\$ 806,642.49	81.00%
7	ESTRADAS	8	\$ 6,224,968.98	61.40%
8	ESTRADAS E PONTES	1	\$ 603,101.95	98.91%
9	FLOOD CONTROL			
10	JUVENTUDE NO DESPORTU			
11	MANUTENSAUN NO REHABILITASAUN			
12	PONTES			
13	SAUDE			
14	SEGURANCA NO DEFESA			
15	SOLIDARIEDADE E SOCIAL			
16	TURISMO			
	Grand Total	11	\$ 7,829,387.81	64.78%

NO	SECTOR PROJECTO	Same		
		TOTAL PROJEC TO	MONTANTE KONTRATU (\$)	PERSNTAGEM EXECUSAUN (%)
1	FLOOD CONTROL			
2	AGUA E SANEAMENTO	2	\$ 137,426.79	20.08%
3	Basic Road Construction	1	\$ 131,893.81	59.74%
4	EDIFICIOS PUBLICOS	3	\$ 610,160.22	78.55%
5	EDUKASAUN	12	\$ 5,024,213.54	5.12%
6	ELETRIFIKASAUN NASIONAL	4	\$ 2,031,238.67	72.85%
7	ESTRADAS	5	\$ 633,432.36	74.49%
8	ESTRADAS E PONTES			
9	FLOOD CONTROL			
10	JUVENTUDE NO DESPORTU	1	\$ 23,697.55	89.15%
11	MANUTENSAUN NO REHABILITASAUN	5	\$ 1,153,984.05	85.96%
12	PONTES	1	\$ 328,755.98	46.54%
13	SAUDE	2	\$ 312,000.61	88.75%
14	SEGURANCA NO DEFESA	1	\$ 76,149.37	0.00%
15	SOLIDARIEDADE E SOCIAL	2	\$ 536,957.37	97.65%
16	TURISMO	1	\$ 48,998.46	32.43%
	Grand Total	40	\$ 11,048,908.78	43.24%

NO	SECTOR PROJECTO	Turiscai		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	FLOOD CONTROL			
2	AGUA E SANEAMENTO	1	\$ 7,530.00	69.97%
3	Basic Road Construction			
4	EDIFICIOS PUBLICOS			
5	EDUKASAUN			
6	ELETRIFIKASAUN NASIONAL			
7	ESTRADAS	2	\$ 3,983,240.53	78.01%
8	ESTRADAS E PONTES			
9	FLOOD CONTROL			
10	JUVENTUDE NO DESPORTU			
11	MANUTENSAUN NO REHABILITASAUN	3	\$ 1,555,370.20	60.43%
12	PONTES			
13	SAUDE			
14	SEGURANCA NO DEFESA			
15	SOLIDARIEDADE E SOCIAL			
16	TURISMO			
	Grand Total	6	\$ 5,546,140.73	73.07%

NO	SECTOR PROJECTO	TOTAL MUNICIPIO MANUFAHI		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	FLOOD CONTROL	1	\$ 39,533.06	75.13%
2	AGUA E SANEAMENTO	5	\$ 444,587.79	41.52%
3	Basic Road Construction	1	\$ 131,893.81	59.74%
4	EDIFICIOS PUBLICOS	3	\$ 610,160.22	78.55%
5	EDUKASAUN	16	\$ 5,548,537.17	6.12%
6	ELETRIFIKASAUN NASIONAL	6	\$ 3,946,641.94	76.12%
7	ESTRADAS	21	\$ 13,196,382.44	65.29%
8	ESTRADAS E PONTES	1	\$ 603,101.95	98.91%
9	FLOOD CONTROL	3	\$ 475,332.23	51.79%
10	JUVENTUDE NO DESPORTU	1	\$ 23,697.55	89.15%
11	MANUTENSAUN NO REHABILITASAUN	11	\$ 3,615,130.78	71.65%
12	PONTES	1	\$ 328,755.98	46.54%
13	SAUDE	2	\$ 312,000.61	88.75%
14	SEGURANCA NO DEFESA	1	\$ 76,149.37	0.00%
15	SOLIDARIEDADE E SOCIAL	2	\$ 536,957.37	97.65%
16	TURISMO	1	\$ 48,998.46	32.43%
	Grand Total	76	\$ 29,937,860.73	57.30%

Dadus detallu kada projetu: #Anexu A

Tabela 6.3.3 : Projecto Municipio Por Ministerio

NO	DONO DO PROJECTO	Alas		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P			
2	ESTATAL			
3	MINISTERIO DA SAUDE			
4	MINISTERIO DAS OBRAS PUBLICAS	16	\$ 5,183,774.17	61.17%
5	MINISTERIO DO ENSINO SUPERIOR, CIENCIA E CULTURA			
6	MINISTERIO DO INTERIOR			
7	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	\$ 329,649.24	24.87%
8	MINISTERIO SAUDE			
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
Grand Total		19	\$ 5,513,423.41	59.00%

NO	DONO DO PROJECTO	Fatuberliu		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSNTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P			
2	ESTATAL			
3	MINISTERIO DA SAUDE			
4	MINISTERIO DAS OBRAS PUBLICAS	10	\$ 7,634,713.42	66.44%
5	MINISTERIO DO ENSINO SUPERIOR, CIENCIA E CULTURA			
6	MINISTERIO DO INTERIOR			
7	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 194,674.39	0.00%
8	MINISTERIO SAUDE			
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
Grand Total		11	\$ 7,829,387.81	64.78%

NO	DONO DO PROJECTO	Same		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P	1	\$ 292,653.74	0.00%
2	ESTATAL	4	\$ 568,413.14	97.02%
3	MINISTERIO DA SAUDE	2	\$ 312,000.61	88.75%
4	MINISTERIO DAS OBRAS PUBLICAS	16	\$ 4,116,319.70	77.67%
5	MINISTERIO DO ENSINO SUPERIOR, CIENCIA E CULTURA	1	\$ 3,961,658.78	0.00%
6	MINISTERIO DO INTERIOR	2	\$ 436,263.93	66.01%
7	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	11	\$ 1,062,554.76	24.22%
8	MINISTERIO SAUDE	1	\$ 71,412.20	88.06%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	\$ 178,633.46	71.88%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 48,998.46	32.43%
Grand Total		40	\$ 11,048,908.78	43.24%

NO	DONO DO PROJECTO	Turiscai		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P			
2	ESTATAL	1	\$ 7,530.00	69.97%
3	MINISTERIO DA SAUDE			
4	MINISTERIO DAS OBRAS PUBLICAS	5	\$ 5,538,610.73	73.07%
5	MINISTERIO DO ENSINO SUPERIOR, CIENCIA E CULTURA			
6	MINISTERIO DO INTERIOR			
7	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
8	MINISTERIO SAUDE			
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
	Grand Total	6	\$ 5,546,140.73	73.07%

NO	DONO DO PROJECTO	TOTAL MUNICIPIO MANUFAHI		
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P	1	\$ 292,653.74	0.00%
2	ESTATAL	5	\$ 575,943.14	96.67%
3	MINISTERIO DA SAUDE	2	\$ 312,000.61	88.75%
4	MINISTERIO DAS OBRAS PUBLICAS	47	\$ 22,473,418.02	68.91%
5	MINISTERIO DO ENSINO SUPERIOR, CIENCIA E CULTURA	1	\$ 3,961,658.78	0.00%
6	MINISTERIO DO INTERIOR	2	\$ 436,263.93	66.01%
7	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	15	\$ 1,586,878.39	21.38%
8	MINISTERIO SAUDE	1	\$ 71,412.20	88.06%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	\$ 178,633.46	71.88%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 48,998.46	32.43%
Grand Total		76	\$ 29,937,860.73	57.30%

Dadus detallu kada projetu: #Anexu A

II. PROGRESU FISIKU

2.1 Progreso Fisiku Kada Fulan

Progresu Fisiku kada fulan ne'e hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu katak progresu actual fulan ida ne'e sikonfika porsentagen servisu ne'ebe atinje deit iha fulan ne'e nia laran, montante actual fulan ida ne'e bazeia ba orsamentu ne'ebe hetan husi progresu fulan ida ne'e nia rasik no ikus porsentagen actual fulan ida ne'e hatudu progresu fisiku komulativu ne'ebe akumula husi porsento anterior no fulan ida ne'e nian, kompletu ba detallu bele haree iha #Anexu B, detallu ba Back-Up #Anexu C no Fotografia bele hare #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

Obstaklu sira ne'ebé ma ami hasoru iha munisipiu Manufahi durante hala'o monitorizasaun no inspesaun projetu sira mak hanesan:

1. Transporte ida de'it difikulta ami atu hala'o inspesaun banhira iha pedidu pagamentu tamba seksaun Ponte Estrada mos presija halo monitorizasaun hodi atinji kuantidade de monitorizasaun
2. Linha internet fraku tamba ne'e maske ami atualiza progresu projetu kada loron mos unidade baze de dados nafatin la hetan dados hafoin semana rua ba leten. Ho difikulade ne'e unidade seksaun halo ami atraplla. Tamba ne'e maske ami iha munisipiu atualiza bebeik maibe laiha efisiensia no bele hamosu deskonfia katak engenheiru munisipiu la halo atualizasaun progresu projetu sira
3. Iha parte **instrusaun serbisu**, munisipiu halo "*tribe*" so pra aumenta volume serbsu de'it maibe fungsaun ida de'it.
4. Bainhira iha pedidu pagamentu, susar mai ami atu atinji kuantidade inspesaun
5. Susar ba seksaun Edificio Público, Agua e Saneamento (EPAS) atu atualiza progresu fiziku kada semana bainhira iha pedidu pagamentu tamba preukupa ho inspesaun pagamentu no prepara rekomendasaun pagamentu
6. Susar ba enjineru munisipiu atu atualiza progresu serbsu eletrisidade tamba responsabilidade enjineru munisipiu de'it mos susar atu finaliza

➤ **Obstaclo parte Eletricidade**

1. Durante halo monitorizasaun ba projeto neébe mak mensiona iha lista projektu Eng. M & E, ADN – I.P, la hasoru kontraktor sira tamba televomel fora da area hotu.
2. Eng. M & E, ADN – I.P, nunka hasoru tekniku husi kompania no parte kompania sempre delega tekniku neébe ba hein iha terenu, maibe tekniku neé rasik laiha konesimentu klean ho orbra refere.
3. Seksaun M & E, AND – I.P, labele kontrola projeto ho maximu tamba Eng. M & E ida hodi
kontrola Projeto Linha Electricidade ho Edifisio Publik Iha Municipio Ha'at (4).
4. Projeto eletricidade barak maka espasu ba lina laiha ona, hodi kompanha sira mos la halo servisu kontinuasaun.
5. Motorista menus difikulta ami nia servisu.

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Buka solusaun lalais ba projektu sira ne'ebé abandona ho projektu na'in se la'e engenheiru munisipiu ninia relatoriu laiha rejultadu no projeto sira sei kontinua abandona
2. Aumenta transporte nune'e bele fasilita hala'o inspesaun
3. Diminui tiha parte instrusaun serbisu tamba enjinheru munisipiu halo "*tribe*" hodi aumenta volume serbsu maibe fungsaun ida de'it.

➤ **Recomendação parte Eletricidade**

1. Husu ba parte ITC, ADN – I.P bele kria Folder Sistem ba Seksaun M & E, ADN – I.P.
2. Husu atu aumenta tan rekursu iha Seksaun M & E, ADN – I.P

Note: Asinatura husi Eng Municipio Manufahi

Força de Trabalho ADN, I.P Municipio Manufahi						
No	Deskrisaun	Identidade				
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	Asinatura
1	Engineiro	Fidelis Mardiano da Costa		Enjineiru EPAS		
		Romulo J.M Henrique		Enjineiru ITI		
		Majorico Cele Tali		Enjineiru ITI		
		Johanes Hornay	011	Enjineiro VEBD		

		Silvino D. R. R. Soares		Enjineiru METIC		
2	Motorista	Silveiro da Costa		Motorista		



LISTA GERAL
ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Alas	Manufahi	Samboio Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	\$ 1,108,760.78	Feb. 10, 2013	100.00%	78.57%	\$ 871,110.32	\$ 237,650.46	PHO
2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consortorio Nacional Manufahi Lda	SSS/148/MOPTC-2017	\$ 553,599.46	Sept. 14, 2017	8.61%	7.75%	\$ 42,899.98	\$ 510,699.48	ON-GOING
3	Emergency new construction of gabion box protection random fill in area Lacro, Baria Laran, Uma Berloik, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consortorio 1912 MF Lda	SSS/279/MOPTC-2016	\$ 440,564.46	Oct. 27, 2016	100.00%	78.96%	\$ 347,876.05	\$ 92,688.41	ON-GOING
4	Rural Roads Routine Maintenance Dootic Weberek, Chainage 0+000 - 6+300, Dootic Wekakaoan, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Samboio Unip,Lda	MPW-RFQ-190017	\$ 71,803.67	Jan. 8, 2019	68.44%	61.60%	\$ 44,230.62	\$ 27,573.05	ON-GOING
5	Prefurasau Be'e mos iha Suku Uma Berloik, Aldeia Besusu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Alas	Manufahi	Buka Fini	MPWTC-NCB-170008	\$ 112,392.00	Aug. 16, 2017	100.00%	90.00%	\$ 101,152.80	\$ 11,239.20	PHO
6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	\$ 269,482.11	Oct. 7, 2019	86.82%	14.96%	\$ 40,316.95	\$ 229,165.16	ON-GOING
7	Kontinuasaun Kanalizasaun Kanu Transmisau no Distribuisau Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Alas	Manufahi	Tane Unipessoal Lda	MOP - W - 190210	\$ 187,239.00	Nov. 21, 2019	30.00%	27.00%	\$ 50,554.31	\$ 136,684.69	ON-GOING
8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Alas	Manufahi	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	\$ 523,300.00	April 21, 2021	68.58%	68.58%	\$ 358,882.28	\$ 164,417.72	ON-GOING
9	Construction and Installation water Gravitation System in Mahaquidam Umaberloik Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Verescar Unip. Lda	SSS/289/MOPTC-2016	\$ 499,455.17	Nov. 8, 2016	89.96%	78.70%	\$ 393,055.29	\$ 106,399.88	ON-GOING
10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Alas	Manufahi	My Friend Unip. Lda	MPW-W-190106	\$ 400,309.52	Nov. 5, 2020	99.66%	93.93%	\$ 375,995.84	\$ 24,313.68	FHO
11	Rehabilitasaun Estrada Tekunu-Feriksare 2 Sta. 2+500-4+250- Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Aplayana unip. Lda	RT/062/MOPTC-2016	\$ 334,517.69	Aug. 3, 2016	80.00%	66.13%	\$ 221,221.39	\$ 113,296.30	ON-GOING
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consortorio Unimafa Lda	SSS/150/MOPTC-2017	\$ 377,955.81	Sept. 14, 2017	25.42%	19.15%	\$ 72,370.68	\$ 305,585.13	ON-GOING
13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaoan Chainage 0+000 - 8+600 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Alas	Manufahi	Werenek Unipessoal Lda	MPW-W-210093	\$ 59,011.32	July 23, 2021	58.58%	26.92%	\$ 15,884.54	\$ 415,568.18	ON-GOING
14	Konstrusaun ka rehabilitasaun ba EBC Mahaquidan	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBC MAHAQUIDAN	Kontratu ho Grupo Comunitariu	\$ 111,814.16	Oct. 15, 2021	29.57%	29.57%	\$ 33,063.11	\$ 415,568.18	ON-GOING
15	Konstrusaun ka rehabilitasaun ba EBF Bercoban	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF BERCOBAN	Kontratu ho Grupo Comunitariu	\$ 101,086.58	Oct. 15, 2022	23.64%	23.64%	\$ 23,899.33	\$ 415,568.18	ON-GOING
16	Konstrusaun ka rehabilitasaun ba EBF Manus	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF MANUS	Kontratu ho Grupo Comunitariu	\$ 116,748.50	Oct. 15, 2023	19.91%	19.91%	\$ 25,028.19	\$ 415,568.18	ON-GOING
17	Konstrusaun Bronjong & Normalizasaun Mota Clere Weberek, Dotik - Alas Manufahi	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	Sarifasalma Hahinarianledo Unip. Lda	17/PDIM/M-MF/IX/2019	\$ 39,533.06		100.00%	75.13%	\$ 29,700.41	\$ 415,568.18	ON-GOING
18	Projecto Konstrusaun Bronjong & Normalizasaun Mota Clere (Alas manufahi) Suco Dotik	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	01/PDIM/M-MF/II/2020	\$ 142,218.12		100.00%	100.00%	\$ 142,218.11	\$ 415,568.18	FHO
19	Projecto Konstrusaun Bronjong & Normalizasaun Mota Clere (Alas - Manufahi) Suco Dotik L	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	LELACUCLAIC UNIP, LDA.	03/PDIM/M-MF/II/2020	\$ 63,632.00		100.00%	100.00%	\$ 63,632.00	\$ 415,568.18	FHO
20	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	\$ 451,569.10	Sept. 14, 2017	9.25%	7.97%	\$ 36,000.92	\$ 415,568.18	ON-GOING
21	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	concorcio Nacional ba Futuro	SSS/149/MOPTC-2017	\$ 468,687.16	Sept. 14, 2017	24.29%	21.86%	\$ 102,464.15	\$ 366,223.01	ABANDON
22	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Fatuberliu	Manufahi	Funu Kolik Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424	\$ 806,642.49	Sept. 1, 2016	90.00%	81.00%	\$ 653,364.09	\$ 153,278.40	Abandon
23	New Construction of Sukaer Oan River cyclop Concrete Reteining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	Consortorio Nacional Samdil, Lda (CNS)	SSS/102/MOPTC-2017	\$ 3,985,902.37	Sept. 7, 2017	87.83%	73.30%	\$ 2,921,736.56	\$ 1,064,165.81	ON-GOING



LISTA GERAL
ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
24	R4D Rural Road Routine Maintenance, Tukununu Feriksare Chainage 0+000-6+350 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	MARDIROMIG VIQSAM, UNIPESOAL LDA	MPW- W - 210096	\$ 27,105.00	July 23, 2021	24.97%	11.92%	\$ 3,230.33	\$ 23,874.67	ON-GOING
25	R4d Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Loskabubu	MPW-W-210099	\$ 337,115.79	July 23, 2021	100.00%	52.82%	\$ 178,069.50	\$ 159,046.29	ON-GOING
26	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Leo-Hilin Unipessoal Lda	MPW-W-210095	\$ 124,043.34	July 23, 2021	73.50%	58.84%	\$ 72,989.44	\$ 51,053.90	ON-GOING
27	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Alifa Pereira	MPW-W-210097	\$ 421,729.47	July 23, 2021	93.38%	48.19%	\$ 203,237.23	\$ 218,492.24	ON-GOING
28	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	\$ 408,816.75	July 23, 2021	100.00%	74.50%	\$ 304,556.74	\$ 104,260.01	ON-GOING
29	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Fatuberliu	Manufahi	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		194,674.39		17.47%	0.00%	\$ -	\$ 194,674.39	ON-GOING
30	Emergency proposed for the new construction of bridge with retaining wall in Area Wee Kakau Oan 1	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	Fatuberliu	Manufahi	Consortio Alkafer .Lda	SSS/211/MOPTC-2016	\$ 603,101.95		0.00%	98.91%	\$ 596,530.15	\$ 6,571.80	ON-GOING
31	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dhalelan,Unip.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000300	\$ 88,665.83	March 25, 2015	100.00%	90.00%	\$ 79,799.25	\$ 8,866.58	PHO
32	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dediva Electrical Unip, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385	\$ 921,673.84	July 6, 2016	96.00%	86.81%	\$ 800,071.34	\$ 121,602.50	ON-GOING
33	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430	\$ 728,245.26	Sept. 1, 2016	92.00%	82.38%	\$ 599,930.07	\$ 128,315.19	ON-GOING
34	Konstrusaun kanalizasaun bee mos iha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Same	Manufahi	Haksolok Java Motor Unip Lda	MOP - W - 190160	\$ 129,668.57	Dec. 1, 2019	18.50%	16.65%	\$ 21,593.56	\$ 108,075.01	ON-GOING
35	Nova fornecimento água do Bairro PNTL Manufahi	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	Same	Manufahi	Tom's Building Uipessoal Lda	SSS/053/MI-2017	\$ 76,149.37	Nov. 29, 2019	24.55%	0.00%	\$ -	\$ 76,149.37	ON-GOING
36	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Same	Manufahi	Consortio Cablaki Oan Lda	SSS/270/MOPTC-2016	\$ 363,040.25	Oct. 19, 2016	100.00%	95.38%	\$ 346,267.25	\$ 16,773.00	ON-GOING
37	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Same	Manufahi	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	\$ 328,755.98	July 26, 2016	66.10%	46.54%	\$ 153,014.54	\$ 175,741.44	ON-GOING
38	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	El Const Unip. Lda	NCB/063/MOPTC-2016	\$ 700,656.46	Aug. 4, 2016	99.36%	99.07%	\$ 694,155.78	\$ 6,500.68	PHO
39	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Aplayana unip. Lda	RT/057/MOPTC-2016	\$ 168,297.72	Aug. 3, 2016	30.00%	18.17%	\$ 30,575.14	\$ 137,722.58	Abandon
40	Road Maintenance Section Same Urban Roads Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Renova Unip Lda	MPW - W - 190215	\$ 87,929.19	Dec. 2, 2019	71.88%	64.69%	\$ 56,880.06	\$ 31,049.13	ON-GOING
41	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Quintas das Flores, Lda	MPW - W - 190123	\$ 177,242.59	June 10, 2019	100.00%	100.00%	\$ 177,242.44	\$ 0.15	FHO
42	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Alifa Pereira	MPW -RFQ 190019	\$ 59,446.75	Aug. 1, 2019	90.13%	81.12%	\$ 48,222.09	\$ 11,224.66	ON-GOING
43	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Leo - Dok	MPWTC-CD-170002	\$ 48,340.53	Jan. 8, 2019	86.31%	86.31%	\$ 41,722.01	\$ 6,618.52	ON-GOING
44	Fencing for Construction Monumento do Dom Boa Ventura	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-CD	EDIFICIOS PUBLICOS	Same	Manufahi	Loskabubu	RDTL/06/GM-MTAC/IV/2016	\$ 178,633.46	June 9, 2015	79.86%	71.88%	\$ 128,395.45	\$ 50,238.01	Abandon
45	Konstrusaun Tangki Beé no Menara Beé ba iha Edificio Administrasaun Municipiu Manufahi	ESTATAL	PDIM	AGUA E SANEAMENTO	Same	Manufahi	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	\$ 7,758.22	April 10, 2017	85.99%	77.39%	\$ 6,004.37	\$ 1,753.85	Abandon
46	Projecto New Construction Bombeiros same -Manufahi	MINISTERIO DO INTERIOR	PDIM	EDIFICIOS PUBLICOS	Same	Manufahi	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	\$ 360,114.56	Aug. 19, 2016	88.85%	79.97%	\$ 287,969.25	\$ 72,145.31	PHO



LISTA GERAL
ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
47	Renovasi gereja paroquia nossa senhora assuncao same	ESTATAL	PDIM	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	\$ 438,905.72	Aug. 7, 2017	98.81%	98.81%	\$ 433,699.77	\$ 5,205.95	FHO
48	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	ESTATAL	PDIM	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Consortio Deatle Hare ba Oin Lda	07/PDIM/M-MF/IX/2019	\$ 98,051.65	Sept. 9, 2019	92.45%	92.45%	\$ 90,647.36	\$ 7,404.29	FHO
49	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutur Bodik Tane Lisuk, Unip.Lda	ESTATAL	PDIM	JUVENTUDE NO DESPORTU	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	09/PDIM/M-MF/X/2019	\$ 23,697.55	Oct. 7, 2019	89.15%	89.15%	\$ 21,127.51	\$ 2,570.04	FHO
50	Konstrusaun Fatin isolamentu iha Municipio Manufahi, Timor Leste	MINISTERIO DA SAUDE	Fundo Covid-19	SAUDE	Same	Manufahi	Daloveya	RDTL-MS-DNA-DC-20-256	\$ 293,664.88	Sept. 12, 2020	99.65%	94.29%	\$ 276,911.01	\$ 16,753.87	PHO
51	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Haut-Dairam Unipessoal Lda	MPW-W210092	\$ 46,754.63	July 23, 2021	44.37%	35.41%	\$ 16,554.11	\$ 30,200.52	Projeto Parado
52	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Riabile Unipessoal Lda	MPW-W-210091	\$ 52,112.72	July 23, 2021	21.47%	19.39%	\$ 10,105.69	\$ 42,007.03	ON-GOING
53	New Construction of Laboratory iha CSI Luak, Manufahi , relasiona ba covid 19 at ministry of health,Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Same	Manufahi	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	\$ 71,412.20	Aug. 17, 2021	97.85%	88.06%	\$ 62,888.53	\$ 8,523.67	ON-GOING
54	Para A Construccao De Jardim De Herois De Manufahi (New Construction Of Campas, Gate And Leveling)	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	TURISMO	Same	Manufahi	My friend Constr. Unip. Lda	RFQ No. 23/MACLN/DNAL/VI/20 21	\$ 48,998.46	Sept. 1, 2021	76.25%	32.43%	\$ 15,892.08	\$ 33,106.38	ON-GOING
55	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	MPW - W -210094	\$ 83,595.57	July 23, 2021	55.88%	50.29%	\$ 42,039.13	\$ 41,556.44	ON-GOING
56	Konstrusaun ka rehabilitasaun ba EBF Tefo	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF TEFO	Kontratu ho Grupo Comunitariu	\$ 99,986.68		15.55%	0.00%		\$ 99,986.68	ON-GOING
57	Konstrusaun ka rehabilitasaun ba EBC Diligencia	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC DILIGENCIA	Kontratu ho Grupo Comunitariu	\$ 110,951.20		25.37%	25.37%	\$ 28,152.99	\$ 82,798.21	ON-GOING
58	Konstrusaun ka rehabilitasaun ba EPE Turon	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE TURON	Kontratu ho Grupo Comunitariu	\$ 83,083.31		30.33%	30.33%	\$ 25,196.06	\$ 57,887.25	ON-GOING
59	Konstrusaun ka rehabilitasaun ba EPE DOMingos Savio Grotu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE DOMINGOS SAVIO	Kontratu ho Grupo Comunitariu	\$ 85,513.28		26.29%	26.29%	\$ 22,484.47	\$ 63,028.81	ON-GOING
60	Konstrusaun ka rehabilitasaun ba EBF Silihasan	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF SILIHASAN	Kontratu ho Grupo Comunitariu	\$ 111,801.61		30.01%	30.01%	\$ 33,551.05	\$ 78,250.56	ON-GOING
61	Konstrusaun ka rehabilitasaun ba EBF hatsana udo/Dai-sua Lama	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF HATSANA UDO / DAI-SUA LAMA	Kontratu ho Grupo Comunitariu	\$ 101,427.27		25.06%	25.06%	\$ 25,418.17	\$ 76,009.10	ON-GOING
62	Konstrusaun ka rehabilitasaun ba EBF Blaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF BLARO	Kontratu ho Grupo Comunitariu	\$ 113,831.28		16.82%	0.00%		\$ 113,831.28	ON-GOING
63	Konstrusaun ka rehabilitasaun ba EBF Rotuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF ROTUTO	Kontratu ho Grupo Comunitariu	\$ 71,892.87		25.71%	25.71%	\$ 18,484.46	\$ 53,408.41	ON-GOING
64	Konstrusaun ka rehabilitasaun ba EBC Fatuco	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC FATUCO	Kontratu ho Grupo Comunitariu	\$ 109,860.63		32.05%	32.05%	\$ 35,209.83	\$ 74,650.80	ON-GOING
65	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	\$ 140,614.24		27.93%	27.93%	\$ 39,279.94	\$ 101,334.30	ON-GOING
66	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	\$ 132,466.39		22.30%	22.30%	\$ 29,543.78	\$ 102,922.61	ON-GOING
67	New Construction Building for Central Electrical in Luak Manufahi, Ministry of Health Timor Leste	MINISTERIO DA SAUDE	Fundo Covid-19	SAUDE	Same	Manufahi	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-22-006	\$ 18,335.73		92.03%	0.00%		\$ 18,335.73	ON-GOING
68	For Road Maintanance Section Jct Aituto-Same-Betano 23Km(A04)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Basic Road Construction	Same	Manufahi	Bemos I Construction Unip. Lda	MPW-W-220007	\$ 131,893.81		80.48%	59.74%	\$ 78,798.94	\$ 53,094.87	ON-GOING
69	New Construction of Tower protection Wall No 92 Section Betano -Viqueque Manufahi Municipality	ELECTRICIDADE DE TIMOR LESTE, E.P	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	My friend Constr. Unip. Lda	NCB/028/MOP-2020	\$ 292,653.74		0.00%	0.00%		\$ 292,653.74	ON-GOING
70	New Construction of Infrastructure and landscape work at polytechnic Institute of Betano in Same, Manufahi municipality	MINISTERIO DO ENSINO SUPERIOR, CIENCIA E CULTURA	FI	EDUKASAUN	Same	Manufahi	Chongqing International Construct	ICB/026/MESCC-2021	\$ 3,961,658.78		0.00%				
71	Open New Road Turiscai - Mota Belihun Maubere, Turiscai - Liquidoe Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Turiscas	Manufahi	Aldepo Murak Unip,Lda	SSS/250/MOPTC-2016	\$ 3,413,040.53	Sept. 4, 2017	93.90%	79.35%	\$ 2,708,287.08	\$ 704,753.45	ON-GOING
72	Const. MCK (Saude) Orana	ESTATAL	PDIM	AGUA E SANEAMENTO	turiscas	Manufahi	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	\$ 7,530.00	May 23, 2019	75.00%	69.97%	\$ 5,268.79	\$ 2,261.21	ON-GOING
73	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railaco, Sanfuk, Tutu Luro - Same Fahi Nehan (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	turiscas	Manufahi	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	\$ 570,200.00	March 25, 2020	70.00%	70.00%	\$ 399,140.00	\$ 171,060.00	ON-GOING



LISTA GERAL
ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
74	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Terra Livre Unip. Lda	SSS/299/MOPTC-2016	\$ 478,217.51	Nov. 23, 2016	90.44%	79.59%	\$ 380,612.95	\$ 97,604.56	PHO
75	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 4 : Turiscas to Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Wan Husin Associates SDN. BHD. Jv Consultant & Engineering Intercontinental Unip. Lda	RT/031/MOP-2019	\$ 798,900.00	March 25, 2020	70.00%	70.00%	\$ 559,230.00	\$ 239,670.00	ON-GOING
76	Spot Improvement Baltade - Orluli, Chainage 0+000 - 2+500 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Daloveya Unipessoal Lda	MPW-W-220001	\$ 278,252.69		0	0.00%	\$ -	\$ 278,252.69	ON-GOING

Inspected by :

Eng. Romulo J.M. Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio
Manufahi A D N IP

Eng. Majorico Cele Tali
Verified by :

Eng. Remigio da C. S. dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e
Irrigasaun A D N IP

Inspected by :

Eng. Fidelis Mardiano da Costa
Engenheiro Edificio Public, Agua e Saneamento A D N
IP

Verified by :

Arch. Francisco Xavier de D. Jeronimo Engenheiro
Senior ba Edificio Public no Agua e Saneamento

Inspected by :

Eng. Silvino D. R. R. Soares
Engenheiro M & E, A D N IP

Verified by :

Eng. Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e
validacao qualidade ADN.I.P



LISTA GERAL ANEXO B
PROGRES SETEMBRO 2022

NU.	No Distri ct	NARAN PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Wednesday, 28 September 2022			OBSERVASAUN	
										previous	Sept. prog.	% Up to Sept prog		
1	1	New Installation MV, Line Transformer and LV Line from Dotik to Alas Manufahi District	ELETRIFIKASAUN NASIONAL	Alas	Manufahi	Samboio Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	\$ 1,108,760.78	Feb. 10, 2013	100.00%		100.00%	ON-GOING	
2	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2	ESTRADAS	Alas	Manufahi	Consortio Nacional Manufahi Lda	SSS/148/MOPTC-2017	\$ 553,599.46	Sept. 14, 2017	8.61%		8.61%	ON-GOING	
3	3	Emergency new construction of gabion box protection random fill in area Lacio, Baria Laran, Uma Berloik, Alas	ESTRADAS	Alas	Manufahi	Consortio 1912 MF Lda	SSS/279/MOPTC-2016	\$ 440,564.46	Oct. 27, 2016	100.00%		100.00%	ON-GOING	
4	4	Rural Roads Routine Maintenance Dootic Weberek, Chainage 0+000 - 6+300, Dootic Wekakaoan, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Samboio Unip,Lda	MPW-RFQ-190017	\$ 71,803.67	Jan. 8, 2019	68.44%		68.44%	ON-GOING	
5	5	Prefurasaun Be'e mos iha Suku Uma Berloik, Aldeia Besusu	AGUA E SANEAMENTO	Alas	Manufahi	Buka Fini	MPWTC-NCB-170008	\$ 112,392.00	Aug. 16, 2017	100.00%	0.00%	100.00%	ON-GOING	Projetu refere LM BTL,E.P tamba AND,I.P la halo ona monitorizasaun
6	6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	\$ 269,482.11	Oct. 7, 2019	86.82%		86.82%	ON-GOING	
7	7	Kontinuasaun Kanalizasaun Kanu Transmisaun no Distribuisaun Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	AGUA E SANEAMENTO	Alas	Manufahi	Tane Unipessoal Lda	MOP - W - 190210	\$ 187,239.00	Nov. 21, 2019	30.00%	0.00%	30.00%	ON-GOING	Projetu refere LM BTL,E.P tamba AND,I.P la halo ona monitorizasaun
8	8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	ESTRADAS	Alas	Manufahi	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	\$ 523,300.00	April 21, 2021	68.58%		68.58%	ON-GOING	
9	9	Construction and Installation water Gravitation System in Mahaquidam Umberloic Manufahi Municipality	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Verescar Unip. Lda	SSS/289/MOPTC-2016	\$ 499,455.17	Nov. 8, 2016	89.96%	0.00%	89.96%	ON-GOING	Projetu refere la halo atividade iha terenu, dadauk ne'e hein de'it submisaun pagamentu final
10	10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	ESTRADAS	Alas	Manufahi	My Friend Unip. Lda	MPW-W-190106	\$ 400,309.52	Nov. 5, 2020	99.66%		99.66%	ON-GOING	
11	11	Rehabilitasaun Estrada Tekunu-Feriksare 2 Sta. 2+500-4+250-Municipal of Same	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Aplayana unip. Lda	RT/062/MOPTC-2016	\$ 334,517.69	Aug. 3, 2016	80.00%		80.00%	ON-GOING	
12	12	New construction of bridge with retaining wall in area we bikas	ESTRADAS	Alas	Manufahi	Consortio Unimafa Lda	SSS/150/MOPTC-2017	\$ 377,955.81	Sept. 14, 2017	21.28%	4.14%	25.42%	ON-GOING	
13	13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaoan Chainage 0+000 - 8+600 Municipality Manufahi	ESTRADAS	Alas	Manufahi	Werenek Unipessoal Lda	MPW-W-210093	\$ 59,011.32	July 23, 2021	58.58%		58.58%	ON-GOING	
14	14	Konstrusaun ka rehabilitasaun ba EBC Mahaquidan	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBC MAHAQUIDAN	Kontratu ho Grupo Comunitariu	\$ 111,814.16	Oct. 15, 2021	22.38%	7.19%	29.57%	ON-GOING	Progresu atual seidauk inklui serbisu provisional sum tamba owner seidauk hatama ninia brick down
15	15	Konstrusaun ka rehabilitasaun ba EBF Bercoban	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF BERCOBAN	Kontratu ho Grupo Comunitariu	\$ 101,086.58	Oct. 15, 2022	20.44%	3.20%	23.64%	ON-GOING	Progresu atual seidauk inklui serbisu provisional sum tamba owner seidauk hatama ninia brick down
16	16	Konstrusaun ka rehabilitasaun ba EBF Manus	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF MANUS	Kontratu ho Grupo Comunitariu	\$ 116,748.50	Oct. 15, 2023	19.30%	0.61%	19.91%	ON-GOING	Progresu atual seidauk inklui serbisu provisional sum tamba owner seidauk hatama ninia brick down
17	17	Konstrusaun Bronjong & Normalizasaun Mota Clere Weberek, Dotik - Alas Manufahi	FLOOD CONTROL	Alas	Manufahi	Sarifasalma Hahiniarianledo Unip. Lda	17/PDIM/M-MF/IX/2019	\$ 39,533.06		100.00%		100.00%		
18	18	Projecto Konstrusaun Bronjong & Normalizasaun Mota Clere (Alas manufahi) Suco Dotik	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	01/PDIM/M-MF/II/2020	\$ 142,218.12		100.00%		100.00%		
19	19	Projecto Konstrusaun Bronjong & Normalizasaun Mota Clere (Alas - Manufahi) Suco Dotik L	FLOOD CONTROL	Alas	Manufahi	LELACUCLAIC UNIP, LDA.	03/PDIM/M-MF/II/2020	\$ 63,632.00		100.00%		100.00%		
20	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	ESTRADAS	Fatuberliu	Manufahi	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	\$ 451,569.10	Sept. 14, 2017	8.86%	0.39%	9.25%	ON-GOING	
21	2	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	ESTRADAS	Fatuberliu	Manufahi	concorcio Nacional ba Futuro	SSS/149/MOPTC-2017	\$ 468,687.16	Sept. 14, 2017	24.29%		24.29%	ON-GOING	
22	3	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	ELETRIFIKASAUN NASIONAL	Fatuberliu	Manufahi	Funu Kolik Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424	\$ 806,642.49	Sept. 1, 2016	90.00%		90.00%	Abandon	



LISTA GERAL ANEXO B
PROGRES SETEMBRO 2022

NU.	No Distri ct	NARAN PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Wednesday, 28 September 2022			OBSERVASAUN	
										previous	Sept. prog.	% Up to Septt prog		
23	4	New Construction of Sukaer Oan River cyclop Concrete Retaining Wall and Gabion	ESTRADAS	Fatuberliu	Manufahi	Consorcio National Samdil, Lda (CNS)	SSS/102/MOPTC-2017	\$ 3,985,902.37	Sept. 7, 2017	87.83%		87.83%	ON-GOING	
24	5	R4D Rural Road Routine Maintenance, Tukununu Feriksare Chainage 0+000-6+350 Manufahi Municipality	ESTRADAS	Fatuberliu	Manufahi	MARDIROMIG VIQSAM, UNIPESOAL LDA	MPW- W - 210096	\$ 27,105.00	July 23, 2021	24.97%		24.97%	ON-GOING	
25	6	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	ESTRADAS	Fatuberliu	Manufahi	Loskabubu	MPW-W-210099	\$ 337,115.79	July 23, 2021	99.65%	0.35%	100.00%	ON-GOING	
26	7	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	ESTRADAS	Fatuberliu	Manufahi	Leo-Hilin Unipessoal Lda	MPW-W-210095	\$ 124,043.34	July 23, 2021	71.82%	1.68%	73.50%	ON-GOING	
27	8	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	ESTRADAS	Fatuberliu	Manufahi	Alifa Pereira	MPW-W-210097	\$ 421,729.47	July 23, 2021	93.38%		93.38%	ON-GOING	
28	9	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	ESTRADAS	Fatuberliu	Manufahi	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	\$ 408,816.75	July 23, 2021	98.19%	1.81%	100.00%	ON-GOING	
29	10	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	EDUKASAUN	Fatuberliu	Manufahi	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		\$ 194,674.39		17.47%	0.00%	17.47%	ON-GOING	
30	11	Emergency proposed for the new construction of bridge with retaining wall in Area Wee Kakau Oan I	ESTRADAS E PONTES	Fatuberliu	Manufahi	Consorcio Alkafer .Lda	SSS/211/MOPTC-2016	\$ 603,101.95		0.00%		0.00%		
31	1	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dhalelan,Unip.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000300	\$ 88,665.83	March 25, 2015	100.00%		100.00%	PHO	
32	2	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dediva Electrical Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385	\$ 921,673.84	July 6, 2016	96.00%		96.00%	ON-GOING	
33	3	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430	\$ 728,245.26	Sept. 1, 2016	92.00%		92.00%	ON-GOING	
34	4	Konstrusaun kanalizasaun bee mos iha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	AGUA E SANEAMENTO	Same	Manufahi	Haksolok Java Motor Unip Lda	MOP - W - 190160	\$ 129,668.57	Dec. 1, 2019	18.50%	0.00%	18.50%	ON-GOING	Projetu refere LM BTL,E.P tamba ADN,I.P la halo ona monitorizasaun
35	5	Nova fornecimento água do Bairro PNTL Manufahi	SEGURANCA NO DEFESA	Same	Manufahi	Tom's Building Uipessoal Lda	SSS/053/MI-2017	\$ 76,149.37	Nov. 29, 2019	24.55%	0.00%	24.55%	ON-GOING	
36	6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	ESTRADAS	Same	Manufahi	Consorcio Cablaki Oan Lda	SSS/270/MOPTC-2016	\$ 363,040.25	Oct. 19, 2016	100.00%		100.00%	ON-GOING	
37	7	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	PONTES	Same	Manufahi	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	\$ 328,755.98	July 26, 2016	64.52%	1.58%	66.10%	ON-GOING	
38	8	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	El Const Unip. Lda	NCB/063/MOPTC-2016	\$ 700,656.46	Aug. 4, 2016	99.36%		99.36%	PHO	
39	9	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipal of Same	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Aplayana unip. Lda	RT/057/MOPTC-2016	\$ 168,297.72	Aug. 3, 2016	30.00%		30.00%	Abandon	
40	10	Road Maintenance Section Same Urban Roads Municipality Manufahi	ESTRADAS	Same	Manufahi	Renova Unip Lda	MPW - W - 190215	\$ 87,929.19	Dec. 2, 2019	71.88%		71.88%	ON-GOING	
41	11	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Quintas das Flores, Lda	MPW - W - 190123	\$ 177,242.59	June 10, 2019	100.00%		100.00%	FHO	
42	12	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Alifa Pereira	MPW -RFQ 190019	\$ 59,446.75	Aug. 1, 2019	90.13%		90.13%	ON-GOING	
43	13	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Leo - Dok	MPWTC-CD-170002	\$ 48,340.53	Jan. 8, 2019	86.31%		86.31%	ON-GOING	



LISTA GERAL ANEXO B
PROGRES SETEMBRO 2022

NU.	No Distri ct	NARAN PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Wednesday, 28 September 2022			OBSERVASAUN	
										previous	Sept. prog.	% Up to Septt prog		
44	14	Fencing for Construction Monument od Dom Boa Ventura	EDIFICIOS PUBLICOS	Same	Manufahi	Loskabubu	RDTL/06/GM-MTAC/IV/2016	\$ 178,633.46	June 9, 2015	79.86%	0.00%	79.86%	Abandon	
45	15	Konstrusaun Tangki Beé no Menara Beé ba iha Edificio Administrasaun Municipiu Manufahi	AGUA E SANEAMENTO	Same	Manufahi	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	\$ 7,758.22	April 10, 2017	85.99%	0.00%	85.99%	Abandon	Haktuir husi Administrador M. Manufahi katak hakrak atu taka projetu refre tamba kompanhia lakohi kopera hodi hadia defetu sira nee'be iha
46	16	Konstrusaun Kuartel Bombeiros iha Same-Manufahi	EDIFICIOS PUBLICOS	Same	Manufahi	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	\$ 360,114.56	Aug. 19, 2016	88.85%	0.00%	88.85%	PHO	
47	17	Rehabilitasaun Igreja Paroquia Nossa Senhora Assuncao Same	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	\$ 438,905.72	Aug. 7, 2017	98.81%	0.00%	98.81%	FHO	
48	18	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Consortio Deatle Hare ba Oin Lda	07/PDIM/M-MF/IX/2019	\$ 98,051.65	Sept. 9, 2019	92.45%	0.00%	92.45%	FHO	
49	19	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutur Bodik Tane Lisuk, Unip.Lda	JUVENTUDE NO DESPORTU	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	09/PDIM/M-MF/X/2019	\$ 23,697.55	Oct. 7, 2019	89.15%	0.00%	89.15%	FHO	
50	20	Konstrusaun Fatin isolamentu iha Municipio Manufahi, Timor Leste	SAUDE	Same	Manufahi	Daloveya	RDTL-MS-DNA-DC-20-256	\$ 293,664.88	Sept. 12, 2020	99.65%	0.00%	99.65%	FHO	
51	21	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	ESTRADAS	Same	Manufahi	Haut-Dairam Unipessoal Lda	MPW-W210092	\$ 46,754.63	July 23, 2021	44.37%		44.37%	ON-GOING	
52	22	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	ESTRADAS	Same	Manufahi	Riabile Unipessoal Lda	MPW-W-210091	\$ 52,112.72	July 23, 2021	21.47%		21.47%		
53	23	New Construction of Laboratory ih CSI Luak,Manufahi relasiona ba covid19 at Ministry of Health, Timor Leste	EDIFICIOS PUBLICOS	Same	Manufahi	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	\$ 71,412.20	Aug. 17, 2021	97.85%		97.85%	ON-GOING	
54	24	PARA A CONSTRUCCAO DE JARDIM DE HEROIS DE MANUFAHI (New Construction of Campas, Gate and Leveling)	TURISMO	Same	Manufahi	My friend Constr. Unip. Lda	RFQ No. 23/MACLN/DNAL/VI/2021	\$ 48,998.46	Sept. 1, 2021	76.12%	0.13%	76.25%	ON-GOING	
55	25	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	ESTRADAS	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	MPW - W -210094	\$ 83,595.57	July 23, 2021	55.88%		55.88%	ON-GOING	
56	26	Konstrusaun ka rehabilitasaun ba EBF Tefo	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF TEFO	Kontratu ho Grupo Comunitariu	\$ 99,986.68		15.55%	0.00%	15.55%		
57	27	Konstrusaun ka rehabilitasaun ba EBC Diligencia	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC DILIGENCIA	Kontratu ho Grupo Comunitariu	\$ 110,951.20		25.12%	0.25%	25.37%		Progresu atual seidauk inklui serbisu provisional sum tamba owner seidauk hatama ninia brick down
58	28	Konstrusaun ka rehabilitasaun ba EPE Turon	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE TURON	Kontratu ho Grupo Comunitariu	\$ 83,083.31		27.89%	2.43%	30.33%		Progresu atual seidauk inklui serbisu provisional sum tamba owner seidauk hatama ninia brick down
59	29	Konstrusaun ka rehabilitasaun ba EPE DÓmingos Savio Grotu	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE DOMINGOS SAVIO	Kontratu ho Grupo Comunitariu	\$ 85,513.28		22.35%	3.94%	26.29%		
60	30	Konstrusaun ka rehabilitasaun ba EBF Silihasan	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF SILIHASAN	Kontratu ho Grupo Comunitariu	\$ 111,801.61		28.30%	1.71%	30.01%		Progresu atual seidauk inklui serbisu provisional sum tamba owner seidauk hatama ninia brick down
61	31	Konstrusaun ka rehabilitasaun ba EBF hatsana udo/Dai-sua Lama	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF HATSANA UDO / DAI-SUA LAMA	Kontratu ho Grupo Comunitariu	\$ 101,427.27		19.61%	5.45%	25.06%		
62	32	Konstrusaun ka rehabilitasaun ba EBF Blaro	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF BLARO	Kontratu ho Grupo Comunitariu	\$ 113,831.28		16.82%	0.00%	16.82%		
63	33	Konstrusaun ka rehabilitasaun ba EBF Rotuto	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF ROTUTO	Kontratu ho Grupo Comunitariu	\$ 71,892.87		25.01%	0.70%	25.71%		



LISTA GERAL ANEXO B
PROGRES SETEMBRO 2022

NU.	No Distri ct	NARAN PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Wednesday, 28 September 2022			OBSERVASAUN	
										previous	Sept. prog.	% Up to Septt prog		
64	34	Konstrusaun ka rehabilitasaun ba EBC Fatuco	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC FATUCO	Kontratu ho Grupo Comunitariu	\$ 10,986.63		25.99%	6.06%	32.05%		Progresu atual seidak inklui serbisu provisional sum tamba owner seidak hatama ninia brick down
65	35	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	\$ 140,614.24		25.93%	2.01%	27.93%		
66	36	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	EDUKASAUN	Same	Manufahi	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	\$ 132,466.39		19.31%	2.99%	22.30%		Progresu atual seidak inklui serbisu provisional sum tamba owner seidak hatama ninia brick down
67	37	New Construction Building for Central Electrical in Luak Manufahi, Ministry of Health Timor Leste	SAUDE	Same	Manufahi	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-22-006	\$ 18,335.73		82.00%	10.04%	92.03%		Progresu atual seidak inklui serbisu eletridade tamba eng. Eletridade ADN.I.P ladauk update
68	38	For Road Maintanance Section Jet Aituto-Same-Betano 23Km(A04)	Basic Road Construction	Same	Manufahi	Bemos I Construction Unip. Lda	MPW-W-220007	\$ 131,893.81		77.71%	2.77%	80.48%		
69	39	New Construction of Tower protection Wall No 92 Section Betano -Viqueque Manufahi Municipality	ELETRIFIKASAUN NASIONAL	Same	Manufahi	My friend Constr. Unip. Lda	NCB/028/MOP-2020	\$ 292,653.74		0.00%		0.00%	foun	
70	40	New Construction of Infrastructure and landscape work at polytechnic Institute of Betano in Same, Manufahi municipality	EDUKASAUN	Same	Manufahi	Chongqing International Construction Corporation	ICB/026/MESCC-2021	\$ 3,961,658.78		0.00%		0.00%		Seidak Hahu
71	1	Open New Road Turiscas - Mota Belihun Maubere, Turiscas - Liquidoe Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	ESTRADAS	Turiscas	Manufahi	Aldepo Murak Unip.Lda	SSS/250/MOPTC-2016	\$ 3,413,040.53	Sept. 4, 2017	93.90%		93.90%	ON-GOING	
72	2	Const. MCK (Saude) Orana	AGUA E SANEAMENTO	turiscas	Manufahi	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	\$ 7,530.00	May 23, 2019	75.00%	0.00%	75.00%	Haktuir husi Administrador M. Manufahi katak hakrak atu taka projetu refre tamba kompanhia lakohi kopera hodi hadia defetu sira nee'be'ia	
73	3	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railaco, Sanfuk, Tutu Luro - Same Fahi Nehan (162)	ESTRADAS	turiscas	Manufahi	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	\$ 570,200.00	March 25, 2020	70.00%		70.00%	ON-GOING	
74	4	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Terra Livre Unip. Lda	SSS/299/MOPTC-2016	\$ 478,217.51	Nov. 23, 2016	90.44%	0.00%	90.44%	PHO	
75	5	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 4 : Turiscas to Alas	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Wan Husin Associates SDN. BHD. Jv Consultant & Engineering Intercontinental Unip. Lda	0	\$ 798,900.00	43915	70.00%		70.00%	ON-GOING	
76	6	Spot Improvement Baltade - Orluli, Chainage 0+000 - 2+500 Manufahi Municipality	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Daloveya Unipessoal Lda	MPW-W-220001	\$ 278,252.69		0.00%		0.00%	ON-GOING	

Inspected by :

Eng Romulo J.M Henrique
Engenheiro ba Projecto Infraestrutur e Irrigasaun Munisipio Manufahi A D N IP

Eng Majorico Cele Tali
Engenheiro ba Projecto Infraestrutur e Irrigasaun Munisipio Manufahi A D N IP

Verified by :

Eng Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutur e Irrigasaun A D N IP

Inspected by :

Eng Fidelis Mardiano da Costa
Engenheiro Edificio Public, Agua e
Saneamento A D N IP

Verified by :

Arlindo Francisco Xavier de D Jeronimo
Engenheiro Senior ba Edificio Public no Agua e
Saneamento A D N IP

Inspected by :

Eng Silvino D. R. R. Soares
Engenheiro M&E, A D N IP

Verified by :

Eng Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N IP

Certified by :

Eng Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e
validacao qualidade ADN.I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 14)

Back-up Data

Naran Projeto : **Konstrusaun ka rehabilitasaun ba EBC Mahaquidan**

No. kontratu :

Data Inspesaun : 09/09/2022

Fatin Inspesaun : Mahaquidan, Alas – Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%

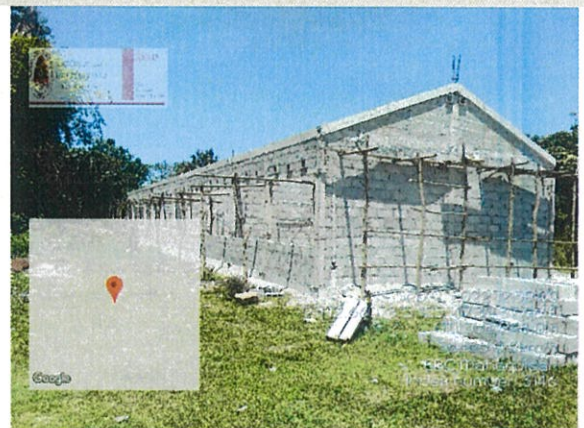



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (ALS 14)

Projeto : Konstrusaun ka Rehalibitasaun ba EBC Mahaquidan
Owner : MEJD
Localization : Cnua Alas, Mahaquidan, Alas Manufahi

MAIN SUMMARY

A D N, I.P RECOMMENDATION									
UP TO 29/07/2022 PROGRESS				SEPTEMBER PROGRESS			UP TO DATE_1ST PAYMENT		
	ITEM SERVISU	ORIGINAL CONTRACT	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT	
I	PRELIMINARIES	\$ 3,425.00	1,262.50	0.01			\$ 1,262.50	1.13%	
II	CLASSROOM BUILDING CA	\$ 62,569.45	17,669.80	0.16	4,859.37	4.35%	\$ 22,529.18	20.15%	
III	TOILET BUILDING TB	\$ 25,164.97	6,090.40	0.05	1,603.53	1.43%	\$ 7,693.93	6.88%	
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,814.74					\$ -	0.00%	
A	CONSTRUCTION COST	\$ 102,974.16	\$ 25,022.71	22.38%	\$ 6,462.90	5.78%	\$ 31,485.61	28.16%	
B	CONTINGENCY	\$ 3,000.00							
C	OVERHEAD	\$ 5,840.00					\$ 1,577.50	1.41%	1.41%
D	GRAND TOTAL	\$ 111,814.16	\$ 25,022.71	22.38%	\$ 8,040.40	7.19%	\$ 33,063.11	29.57%	

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN,I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Enginheiro Senior EPAS ADN,I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN,I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 15)

Back-up Data

Naran Projeto : Konstrusaun ka rehabilitasaun ba EBF Bercoban

No. kontratu :

Data Inspesaun : 09/09/2022

Fatin Inspesaun : Lurin, Taitudac, Alas, Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%

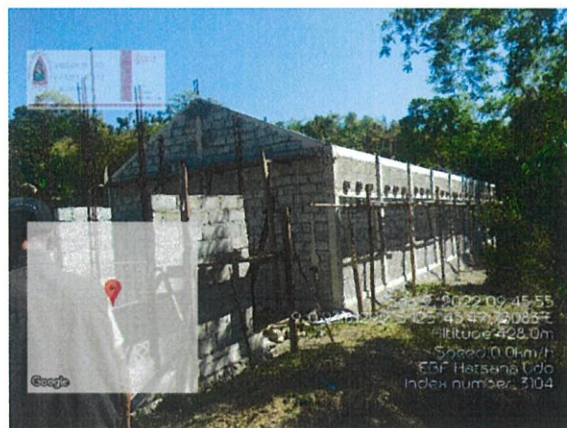



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (ALS 15)

Projeto : Konstrusaun ka Rehalibitasaun ba EBF Bercoban
Owner : MEJD
Localization : Lurin, Taitudac

MAIN SUMMARY

A D N, I.P. RECOMMENDATION									
UP TO 29/07/2022				SEPTEMBER			UP TO DATE FIRST		
PROGRESS				PROGRESS			PAYMENT		
				AMOUNT	WIEGHT		AMOUNT	WIEGHT	
I	PRELIMINARIES		\$	3,775.00			\$	832.50	0.82%
II	CLASSROOM BUILDING C		\$	52,034.01			\$	14,199.10	14.05%
III	TOILET BUILDING TB		\$	25,446.29			\$	7,290.23	7.21%
IV	PROVISIONAL SUM FOR SITE-WORKS		\$	10,991.28					
A	CONSTRUCTION COST		\$	92,246.58			\$	22,321.83	22.08%
B	CONTINGENCY		\$	3,000.00					
C	OVERHEAD		\$	5,840.00			\$	1,577.50	1.56%
D	GRAND TOTAL		\$	101,086.58			\$	23,899.33	23.64%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, 1 / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, 1 / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



#ANEXU C2 (ALS 16)

Projeto : Konstrusaun ka Rehalibitasaun ba EBF Manus
Owner : MEJD
Localization : Manus, Taitudak, Alas Manufahi

MAIN SUMMARY		A D N, I.P RECOMMENDATION					
		UP TO 29/07/2022		SEPTEMBER		UP TO DATE 1 ST	
		PROGRESS		PROGRESS		PAYMENT	
	ITEM SERVICE	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 4,175.00	1.18%	\$ 625.00	0.54%	\$ 2,000.00	1.71%
III	CLASSROOM BUILDING CA	\$ 65,117.90	15.44%	\$ 190.78	0.16%	\$ 18,211.82	15.60%
IV	TOILET BUILDING TB	\$ 25,875.85	3.51%	\$ (766.86)	-1%	\$ 3,326.37	2.85%
V	PROVISIONAL SUM FOR SITE-WORKS	\$ 12,739.75				\$ -	0.00%
A	CONSTRUCTION COST	\$ 107,908.50	20.12%	\$ 48.92	0.04%	\$ 23,538.19	20.16%
B	CONTINGENCY	\$ 3,000.00					
C	OVERHEAD	\$ 5,840.00				\$ 1,490.00	1.28%
D	GRAND TOTAL	\$ 116,748.50	20.12%	\$ 23,489.27	1.32%	\$ 25,028.19	21.44%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVCQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 24)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF CAMPAS, GATE AND LEVELING
AREA AND GARDEN OF HEROES MANUFAHI

No. kontratu : 39/MACLN/IX/2021

Data Inspesaun : 27/09/2022

Fatin Inspesaun : Luak Manufahi

Koordinadas :

Start Point : Long :, Latetude :

End Point : Long :, Latetude :

Naran Inspetur : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Betonajen ba plaka camp





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (SAME 24)

PROJECT OWNER :MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL
TITLE PROJECT :NEW CONSTRUCTION OF CAMPAS, GATE AND LEVELING AREA AND GARDEN OF HEROES MANUFAHI
PROJECT LOCATION :LUAK - MANUFAHI

SUMMARY

NO	DESCRIPTION WORKS	AMOUNT (\$ USD)	AND,I.P RECOMMENDATION					
			UP - TO - JULY		SEPTEMBER PROGRESS		UP - TO - SEPTEMBER	
			AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
A	PERSIAPAN	\$ 860.00	\$ 656.250	1.339%	\$ 50.000	0.102%	\$ 706.250	1.441%
B	KONSTRUKSI KUBURAN	\$ 16,937.70	\$ 7,372.556	15.047%	\$ 8.347	0.017%	\$ 7,380.903	15.064%
C	PERLENGKAPAN GAPURA & LANDSCAPE	\$ 3,772.15	\$ 3,498.788	7.141%	\$ -	0.000%	\$ 3,498.788	7.141%
D	PEMBERSIHAN & LEVELING AREA	\$ 21,191.70	\$ 21,191.697	43.250%	\$ -	0.000%	\$ 21,191.697	43.250%
F	CONSTRUCTION COAST	\$ 42,761.55	\$ 32,719.29	66.78%	\$ 58.35	0.12%	\$ 32,777.64	66.90%
G	CONTRACTOR FEE AND OVER HEAD 10% X (F)	\$ 4,276.16	\$ 3,271.93	6.68%	\$ 5.83	0.01%	\$ 3,277.76	6.69%
H	OVERHEAD	\$ 1,000.00	\$ 575.00	1.17%	\$ -	0.00%	\$ 575.00	1.17%
I	TAX PAYMENT 2% X (F+ G + H)	\$ 960.75	\$ 731.32	1.49%	\$ 1.28	0.00%	\$ 732.61	1.50%
J	GRAND TOTAL A + B + C + D	\$ 48,998.46	\$ 37,297.54	76.12%	\$ 65.46	0.13%	\$ 37,363.01	76.25%

Prepared by:
Date, 11 / 9 / 2022

Eng. Fidelis Mardiano da Costa
Engenheiro Edifício Público, Água e Saneamento ADN,I.P.
Município Manufahi

Verified by:
Date, 11 / 9 / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Sênior Edifício Público, Água e Saneamento ADN,I.P

Certified by:
Date, 11 / 9 / 2022

Eng. Emerenciana da Costa Maia
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN,I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 27)

Back-up Data

Naran Projeto : **Konstrusaun ka Rehalibitasaun ba EBC Diligencia**

No. kontratu :

Data Inspesaun : **12/09/2022**

Fatin Inspesaun : Letefoho, Same Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (SAME 27)

Projeto : Konstrusaun ka Rehalibitasaun ba EBC Dilligencia

Owner : MEJD

Localization : Letefoho, Same Manufahi

MAIN SUMMARY		ADN, I.P. RECOMMENDATION					
NO	ITEM SERVISU	ORIGINAL CONTRACT	P		SEPTEMBER		UP TO DATE_1ST
			AMOUNT	WIEGHT	AMOUNT	WIEGHT	PAYMENT
I	PRELIMINARIES	\$ 2,675.00	\$ 980.63	0.88%			\$ 980.63 0.88%
II	CLASSROOM BUILDING CA	\$ 61,073.65	\$ 18,866.56	17.00%	\$ (214.02)	-0.19%	\$ 18,652.54 16.81%
III	TOILET BUILDING TB	\$ 24,613.61	\$ 6,992.33	6.30%			\$ 6,992.33 6.30%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 12,284.68					
V	PROVISIONAL SUM FOR DEMOLITION	\$ 1,464.27	\$ 754.36	0.68%	\$ (754.36)	-0.68%	\$ - 0.00%
A	CONSTRUCTION COST	\$ 102,111.20	\$ 27,593.88	24.87%	\$ (968.38)	-0.87%	\$ 26,625.49 24.00%
B	CONTINGENCY	\$ 3,000.00					
C	OVERHEAD	\$ 5,840.00			\$ 1,527.50	1.38%	\$ 1,527.50 1.38%
D	GRAND TOTAL	\$ 110,951.20	\$ 27,593.88	24.87%	\$ 559.12	0.50%	\$ 28,152.99 25.37%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Enginheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 28)

Back-up Data

Naran Projeto : **Konstrusaun no Rehabilitasaun EPE Turon**
No. kontratu :

Data Inspesaun : **12/09/2022**

Fatin Inspesaun : Turon, Babulo, Same, Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%

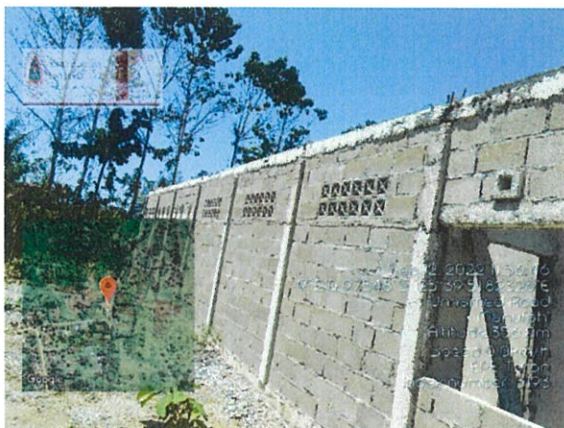



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXU C2 (SAME 28)

Projeto : Konstrusaun no Rehabilitasaun EPE Turon
Owner : MEJD
Localization : Babulo , Same Manufahi

MAIN SUMMARY		ADN, I.P. RECOMMENDATION					
		UP TO 30/07/2022 PROGRESS		SEPTEMBER PROGRESS		UP TO 30/0/2022 PROGRESS	
ORIGINAL							
	ITEM SERVISU	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	WIEGHT
I	PRELIMINARIES	\$ 3,175.00	1,691.00	2.04%	\$ (315.00)	-0.38%	1.66%
II	CLASSROOM BUILDING C2	\$ 57,907.13	21,484.35	25.86%	\$ 1,200.71	1.45%	27.30%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 13,161.18					0.00%
A	CONSTRUCTION COST	\$ 74,243.31	\$ 23,175.35	27.89%	\$ 885.71	1.07%	28.96%
B	CONTINGENCY	\$ 3,000.00					
C	OVERHEAD	\$ 5,840.00			\$ 1,135.00	1.37%	1.37%
D	GRAND TOTAL	\$ 83,083.31	\$ 23,175.35	27.89%	\$ 2,020.71	2.43%	30.33%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.

Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 29)

Back-up Data

Naran Projeto : Konstrusaun ka rehabilitasaun ba EPE DOmingos Savio Grotu

No. kontratu :

Data Inspesaun : 08/09/2022

Fatin Inspesaun : Grotu, Same- Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Dadauk ne'e atividade la la'o





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXU C2 (SAME 29)

Projeto : Konstrusaun ka rehabilitasaun ba EPE Domingos Savio Grotu

Owner : MEJD

Localization : Grotu, Same Manufahi

MAIN SUMMARY

NO	ITEM SERVISU	ORIGINAL CONTRACT	A D N, I.P RECOMMENDATION					
			UP TO 26/08/2022 PROGRESS		SEPTEMBER PROGRESS		UP TO DATE_1RST PAYMENT	
			AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,875.00	\$ 2,480.00	2.90%	\$ (1,105.00)	-1.29%	\$ 1,375.00	1.61%
II	CLASSROOM BUILDING C2	\$ 61,144.12	\$ 16,727.31	19.56%	\$ 3,174.66	3.71%	\$ 19,901.97	23.27%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,654.16						
A	CONSTRUCTION COST	\$ 76,673.28	\$ 19,207.31	22.46%	\$ 2,069.66	2.42%	\$ 21,276.97	24.88%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	\$ -	0.00%	\$ 1,207.50	1.41%	\$ 1,207.50	1.41%
D	GRAND TOTAL	\$ 85,513.28	\$ 19,207.31	22.46%	\$ 3,277.16	3.83%	\$ 22,484.47	26.29%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Enginheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVC ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 30)

Back-up Data

Naran Projeto : **Konstrusaun ka Rehalibitasaun ba EBF Silihasan**
No. kontratu :

Data Inspesaun : 09/09/2022

Fatin Inspesaun : Silihasan, Betano, Same, Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Iinspesaun ida ne'e ba inspesaun pagamentu
25%





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXU C2 (SAME 30)

Projeto : Konstrusaun ka Rehalibitasaun ba EBF Silihasan
Owner : MEJD
Localization : Silihasan Betano , Same Manufahi

MAIN SUMMARY		A D N, I.P RECOMMENDATION					
NO	ITEM SERVISU	ORIGINAL CONTRAT	UP TO 27/08/2022 PROGRESS		SEPTEMBER PROGRESS		UP TO DATE_1RST PAYMENT
			AMOUNT	WIEGHT	AMOUNT	WIEGHT	
I	PRELIMINARIES	\$ 3,275.00	\$ 1,171.88	1.05%	\$ 350.00	0.31%	\$ 1,521.88 1.36%
II	CLASSROOM BUILDING CA	\$ 61,808.99	\$ 15,887.78	14.21%	\$ 423.95	0.38%	\$ 16,311.73 14.59%
III	TOILET BUILDING TB	\$ 24,895.93	\$ 13,719.24	12.27%	\$ 813.20	0.73%	\$ 14,532.45 13.00%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,921.67					\$ - 0.00%
V	PROVISIONAL SUM FOR DEMOLITION	\$ 1,060.03					\$ - 0.00%
A	CONSTRUCTION COST	\$ 102,961.61	\$ 30,778.90	27.53%	\$ 1,587.15	1.42%	\$ 32,366.05 28.95%
B	CONTIGENCY	\$ 3,000.00					\$ - 0.00%
C	OVERHEAD	\$ 5,840.00			\$ 1,185.00	1.06%	\$ 1,185.00 1.06%
D	GRAND TOTAL	\$ 111,801.61	\$ 30,778.90	27.53%	\$ 2,772.15	2.48%	\$ 33,551.05 30.01%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN,I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN,I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN,I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 31)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DAI-SUA LAMA
No. kontratu :

Data Inspesaun : 08/09/2022

Fatin Inspesaun : Daisua, Same Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%

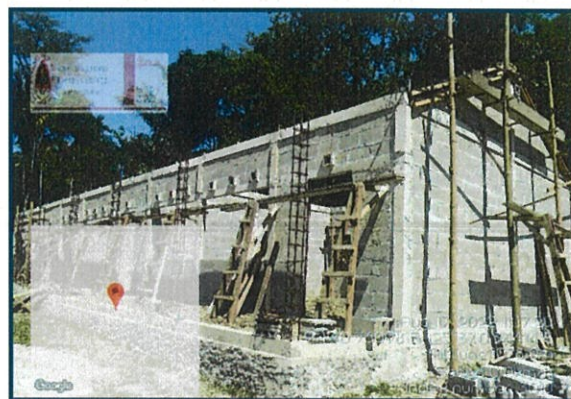



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (SAME 31)

Projeto : Konstrusaun ka Rehabilitasaun EBF Hatsanaudo Daisua / Daisua Lama

Owner : MEJD

Localization : Hatsanaudo Daisua , Same- Manufahi

		ADN, I.P. RECOMMENDATION					
		UP TO 27/08/2022			SEPTEMBER		
MAIN SUMMARY		PROGRESS			PROGRESS		
		ORIGINAL CONTRACT		AMOUNT		WIEGHT	
NO	ITEM SERVISU						
I	PRELIMINARIES	\$	3,475.00	\$	1,075.00	1.06%	
II	CLASSROOM BUILDING C	\$	50,921.69	\$	14,917.77	14.71%	
III	TOILET BUILDING Tb	\$	25,156.94	\$	2,992.94	2.95%	
IV	PROVISIONAL-SUM FOR SITEWORKS (SW)	\$	13,033.65				
A	CONSTRUCTION COST	\$	92,587.27	\$	18,985.71	18.72%	23.21%
B	CONTINGENCY	\$	3,000.00				
C	OVERHEAD	\$	5,840.00	\$	908.00	0.90%	1.85%
D	GRAND TOTAL	\$	101,427.27	\$	19,893.71	19.61%	25.06%

Verified by:
Date, // 19 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVCQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 33)

Back-up Data

Naran Projeto : **Konstrusaun ka rehabilitasaun ba EBF Rotuto**
No. kontratu :

Data Inspesaun : 08/09/2022

Fatin Inspesaun : Rotuto, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



EPAS ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (SAME 33)

Projeto : Konstrusaun ka rehabilitasaun ba EBF Rotuto
Owner : MEJD
Localization : Rotuto, Same Manufahi

MAIN SUMMARY

NO	ITEM SERVISU	ORIGINAL CONTRACT	A D N,I,P RECOMMENDATION					
			Up to 27082022 - progres		September Progress		UT TO DATE_1RST PAYMENT	
			AMOUNT	WEIGHTH	AMOUNT	WEIGHTH	AMOUNT	WEIGHTH
I	PRELIMINARIES	\$ 3,675.00	\$ 1,241.00	1.73%	\$ (225.00)	-0.31%	\$ 1,016.00	1.41%
II	CLASSROOM BUILDING CL	\$ 52,911.97	\$ 15,848.77	22.04%	\$ 409.69	0.57%	\$ 16,258.46	22.61%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 5,899.87						
IV	PROVISIONAL SUM FOR DEMOLISH	\$ 566.03	\$ 481.13	0.67%	\$ (481.13)	-0.67%	\$ -	0.00%
A	CONSTRUCTION COST	\$ 63,052.87	\$ 17,570.90	24.44%	\$ (296.44)	-0.41%	\$ 17,274.46	24.03%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	\$ 482.00	0.67%	\$ 728.00	1.01%	\$ 1,210.00	1.68%
D	GRAND TOTAL	\$ 71,892.87	\$ 18,052.90	25.11%	\$ 431.56	0.60%	\$ 18,484.46	25.71%

Verified by:

Date, 11 / 9 / 2022

Eng. Fidelis Mardiano da Costa, L. eng. Civ.

Eng. EPAS ADN, I.P.

Verified by:

Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo

Enginheiro Senior EPAS ADN, I.P.

Certified by:

Date, / / 2022

Eng. Emerenciana da Costa Maia

Coordenadora UCVQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 34)

Back-up Data

Naran Projeto : **Konstrusaun ka Rehalibitasaun ba EBC Fatuco**
No. kontratu :

Data Inspesaun : 12/09/2022

Fatin Inspesaun : Hola-rua, Same, Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%

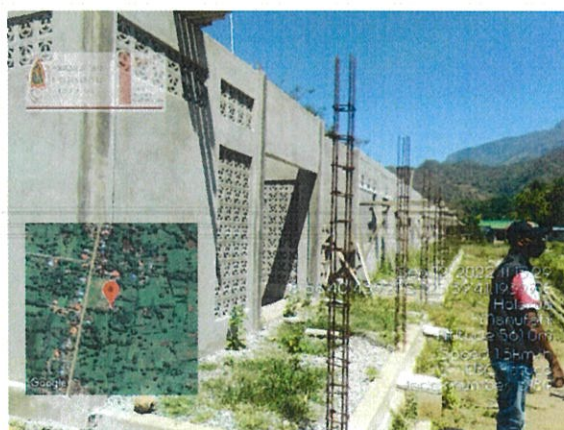



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU D (SAME 34)

Projeto : Konstrusaun ka Rehalibitasaun ba EBC Fatuco
Owner : MEJD
Localization : Fatuco Holarua , Same Manufahi

MAIN SUMMARY		A D N, I.P. RECOMMENDATION					
		Up to 27062022 - Progres			SPTEMBER_PROGRES S		
	ITEM SERVISU	A D N VERIFIED	AMOUNT	WEIGHTH	AMOUNT	WEIGHTH	UP TO DATE_IRST PAYMENT
I	PRELIMINARIES	\$ 2,675.00	1,495.00	1.36%	\$ (250.00)	-0.23%	1,245.00 1.13%
II	CLASSROOM BUILDING CA	\$ 61,554.47	18,563.03	16.90%	\$ 1,250.68	1.14%	19,813.71 18.04%
III	TOILET BUILDING TB	\$ 24,812.57	8,454.22	7.70%	\$ 1,056.90	0.96%	9,511.12 8.66%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,390.83					- 0.00%
V	PROVISIONAL SUM FOR DEMOLITION	\$ 587.75					- 0.00%
A	CONSTRUCTION COST	\$ 101,020.63	\$ 28,512.25	25.95%	\$ 2,057.59	1.87%	\$ 30,569.83 27.83%
B	CONTIGENCY	\$ 3,000.00					\$ - 0.00%
C	OVERHEAD	\$ 5,840.00			\$ 4,640.00	4.22%	\$ 4,640.00 4.22%
D	GRAND TOTAL	\$ 109,860.63	\$ 28,512.25	25.95%	\$ 6,697.59	6.10%	\$ 35,209.83 32.05%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.

Eng. EPAS ADN,I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo

Engenheiro Senior EPAS ADN,I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia

Coordenadora UCVQ ADN,I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 35)

Back-up Data

Naran Projeto : Konstrusaun ka Rehalibitasaun ba EBC Simpang Tiga

No. kontratu :

Data Inspesaun : 08/09/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (SAME 35)

Projeto : Konstrusaun ka Rehalibitasaun ba EBC Simpang Tiga

Owner : MEJD

Localization : Loti, Daisua, Same- Manufahi

MAIN SUMMARY

ADN,I.P RECOMMENDATION									
				Up to 30072022 - progres			SEPTEMBER_PROGRES		
							\$		
NO	ITEM SERVISU	A DN VERIFIED	AMOUNT	WEIGHTH	AMOUNT	WEIGHTH	AMOUNT	WEIGHTH	UP TO DATE_IRST PAYMENT
I	PRELIMINARIES	\$ 3,675.00	\$ 1,325.00	0.94%	\$ 1,325.00	0.94%	\$ 1,325.00	0.94%	
II	CLASSROOM BUILDING C	\$ 49,223.37	\$ 19,357.78	13.77%	\$ 19,357.78	-3.18%	\$ (4,477.31)	10.58%	
III	CLASSROOM BUILDING Cdl	\$ 42,912.01	\$ 8,998.23	6.40%	\$ 8,998.23	2.62%	\$ 3,680.01	9.02%	
IV	TOILET BULDING Tb	\$ 24,347.83	\$ 6,779.61	4.82%	\$ 6,779.61	1.45%	\$ 2,039.12	6.27%	
V	PROVISIONAL FOR SITEWORKS	\$ 10,945.68					\$ -	0.00%	
VI	PROVISIONAL FOR DEMOLISH	\$ 670.35					\$ -	0.00%	
A	CONSTRUCTION COST	\$ 131,774.24	\$ 36,460.62	25.93%	\$ 36,460.62	0.88%	\$ 1,241.82	26.81%	
B	CONTINGENCY	\$ 3,000.00							
C	OVERHEAD	\$ 5,840.00					\$ 1,577.50	1.12%	
D	GRAND TOTAL	\$ 140,614.24	\$ 36,460.62	25.93%	\$ 36,460.62	2.01%	\$ 2,819.32	27.93%	

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN,I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Enginheiro Senior EPAS ADN,I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN,I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 36)

Back-up Data

Naran Projeto : **Konstrusaun no Rehabilitasaun ESTV Halibur Betano**
No. kontratu :

Data Inspesaun : **08/09/2022**

Fatin Inspesaun : Betano, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu 25%

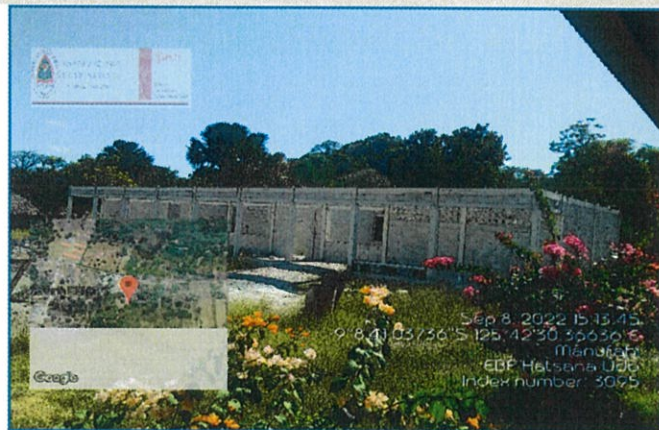



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXU C2 (# SAME 36)

Projeto : Konstrusaun no Rehabilitasaun ESTV Halibur Betano
Owner : MEJD
Localization : Betano ,Same- Manufahi

MAIN SUMMARY			A D N,I,P RECOMMENDATION					
			Up to 27082022 - PROGRESS		SEPTEMBER_ PROGRESS		UP TO DATE_IRST PAYMENT	
NO	ITEM SERVISU	ORIGINAL CONTRACT	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,175.00	1,200.00	0.91%	\$ 625.00	0.47%	\$ 1,825.00	1.38%
II	TEACHER OFFICE	\$ 79,003.71	24,280.37	18.33%	\$ 1,705.91	1.29%	\$ 25,986.28	19.62%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 41,447.68					\$ -	0.00%
A	CONSTRUCTION COST	\$ 123,626.39	\$ 25,480.37	19.24%	\$ 2,330.91	1.76%	\$ 27,811.28	20.99%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	120.00	0.09%	\$ 1,612.50	1.22%	\$ 1,732.50	1.31%
D	GRAND TOTAL	\$ 132,466.39	\$ 25,600.37	19.33%	\$ 3,943.41	2.98%	\$ 29,543.78	22.30%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN,I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Enginheiro Senior EPAS ADN,I.P.

Verified by:
Date, / / 2022

Eng. Emerenciana Da Costa Maia
Coordenadora UCVQ ADN,I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 37)

Back-up Data

Naran Projeto : New Construction Building for Central Electrical in Luak Manufahi,
Ministry of Health Timor Leste
No. kontratu : RDTL-MS-C19-DNA-DC-22-006

Data Inspesaun : 27/09/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa L, Eng. Civ.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu PHO





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



EPAS ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

Anexo c2 # (SAME 37)

SUMMARY

PROJECT TITLE : NEW CONSTRUCTION BUILDING for CENTRAL ELECTRICAL

LOCATION : LUAK - MANUFAHI

ORIGINAL CONTRACT			July Progress		September Progress		Up to September 30 th , 2022- Progress	
NO	DESCRIPTION	Total Amount (USD)	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PREPARATION WORKS	\$ 600.00	\$ 250.00	1.36%	\$ 350.00	1.91%	\$ 600.00	3.27%
II	CONSTRUCTION HOUSE FOR GENSET	\$ 295.20	\$ 295.20	1.61%	\$ -	0.00%	\$ 295.20	1.61%
III	FONDATION WORK	\$ 1,254.92	\$ 1,254.92	6.84%	\$ -	0.00%	\$ 1,254.92	6.84%
IV	CONCRETE WORK	\$ 880.51	\$ 716.17	3.91%	\$ 164.34	0.90%	\$ 880.51	4.80%
V	COLOM	\$ 743.83	\$ 629.29	3.43%	\$ 114.54	0.62%	\$ 743.83	4.06%
VI	TOP BEAM	\$ 1,459.29	\$ 854.22	4.66%	\$ 942.84	5.14%	\$ 1,797.06	9.80%
VII	WALL INSTALATION WORK	\$ 1,475.70	\$ 1,475.70	8.05%	\$ -	0.00%	\$ 1,475.70	8.05%
VIII	DOOR WORK	\$ 1,102.00	\$ 1,102.00	6.01%	\$ -	0.00%	\$ 1,102.00	6.01%
IX	ROOFING WORK	\$ 3,626.82	\$ 3,626.82	19.78%	\$ -	0.00%	\$ 3,626.82	19.78%
X	CEILING WORK	\$ 2,175.18	\$ 1,666.39	9.09%	\$ 508.79	2.77%	\$ 2,175.18	11.86%
XI	ELECTRICAL WORK	\$ 863.14	\$ -	0.00%	\$ 563.14	3.07%	\$ 563.14	3.07%
XII	PAINTING WORK	\$ 452.69	\$ 452.69	2.47%	\$ -	0.00%	\$ 452.69	2.47%
XIII	FINAL CLEARING	\$ 100.00	\$ -	0.00%	\$ 100.00	0.55%	\$ 100.00	0.55%
A	CONTRUCTION COST (I + XIII)	\$ 15,029.29	\$ 12,323.41	67.21%	\$ 2,743.65	14.96%	\$ 15,067.06	82.17%
B	Fee Contractor (10% x A)	\$ 1,502.93	\$ 1,232.34	6.72%	\$ 274.36	1.50%	\$ 1,506.71	8.22%
D	TAX 2% x (A + B)	\$ 300.59	\$ 246.47	1.34%	\$ 54.87	0.30%	\$ 301.34	1.64%
E	CONTINGENCY	\$ 1,502.93	\$ 1,232.34	6.72%	\$ -1,232.34	-6.72%	\$ -	0.00%
F	TOTAL PROJECT COST (A + B + C + D)	\$ 18,335.73	\$ 15,034.56	82.00%	\$ 1,840.54	10.04%	\$ 16,875.10	92.03%

Verified by:
Date, 11 / 9 / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Verified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Cordenadora UC VQ ADN, I.P.

Page 1 of 3

[illegible]

[illegible]

Prepara Husi :


(Eng. Fidelis Mardiano da Costa)
Eng. EPAS ADN,I.P. Munisipiu Manufahi

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)

Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

Aprova Husi : 

(Eng. Januario Maia Guterres)

Adjunto Director Ejecutivo ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



EADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 3)

Back-up Data

Naran Projeto : New Installation MV, Line Transformer and LV Line from Dotik to Alas
Manufahi District

No. kontratu : RDTL/MOP-SEE/CGI-PEN : 0000119

Data Inspesaun : 27/9/2022

Fatin Inspesaun : Manufahi

Koordinadas :

Start Point : Long : -9,05.94.69, Latetude : 125,39.58.14

End Point : Long : -9,23.43.85, Latetude : 125,39.43.27

Naran Inspector : 1. Silvino D. R. Rebelo Soares

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



EADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME - 3)

Back-up Data

Naran Projeto : **New Installation MV, Line Transformer and LV Line from Dotik to Alas
Manufahi District**
No. kontratu : RDTL/MOP-SEE/CGI-PEN : 0000119

Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E
ORDENAMENTO
VII GOVERNO CONSTITUCIONAL



ADN, LP.
Agência de
Desenvolvimento
Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District

Kompanha : Fahilia Humalo Unip. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	27/9/2022	MANUFAHI / ALAS	SILVNO D. R. R SOARES	TEKNIKO M & E, ADN - I.P	1	Tenki Hadia Schoor Nebe Mak Mamar no Kotu Tena	
					2	Tenki Pinta Fali Airing Nebe Mak Tinta Sai Hotu Ona	
					3	Tesi Ai Nebe Mak Besik Ba Linha MV ho LV	
					4	Halos Airing Nebe Mak Halis	
					5	Cor Airing Nebe Mak Sedaunk Cor	
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		

Naran Eng.	Silvino Domingos Rita Rebelo Soares							2022																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Municipio	MUNICIPIO MANUFAHI NO POSTOS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	Action	Setp																														OBS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
ALAS (ALS)	1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	Sambolo Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

 MINISTÉRIO DO PLANO E ORDENAMENTO  ADN, I.P. Agência de Desenvolvimento Nacional, Investimento Público							PLANU INSPESAUN																															
Naran Eng. Silvino Domingos Rita Rebelo Soares							2022																															
Município MUNICIPIO MANUFAHI NO POSTOS																																						
Município / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	Action	Setp																														OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
TURISCAI (TRS)	35	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	36	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
2	Const. MCK (Saude) Orana	Gerasaun Mallkau Unip. Lda	01/PDIM/M-MF/V/2019	PDIM	ESTATAL	Plan																																
						Actual																																
TOTAL PROJETO ON-GOING																																						

Note:

 Planu Periode inspesaun iha tereinu
  Implementa Planu Periode Inspesaun
  Relatoriu avaliasuan mensal iha Dili
  Inspesaun Proceso Pagamentu

Prepara Husi :

(Silvino D. R. Rebelo Soares)
Eng. Electricidade, ADN - I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ,ADN -

Aprova Husi :

(Eng. Jamborio Maia Guterres)
Adjunto Director Executivo,ADN - I.P.



ANEXO C1 (Same 26)

Back-up Data

Naran Projeto : JCT AITUTO - SAM E- BETANO 23KM (A04)

No. kontratu : MPW-W-220007

Data Inspesaun : 14/ 09 /2022

Fatin Inspesaun : Aituto / Same

Koordinadas : Start Point : Latetude -8,9998699S, Long: 125.654606E

End Point : Latetude: 8.99180S , Long: 125.91715E


Naran Inspector : 1. Romulo J.M.Henrique

2. Majorico Cele Tali

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Item Structure Excavation

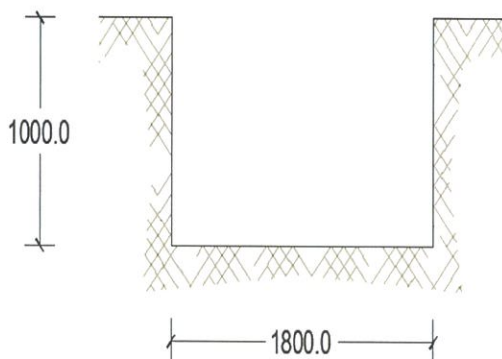



ANEXO C1 (Same 26)


Back-up Data

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktua

Item Stone Massonry in unit Milimeter

Area = 1.98 m²

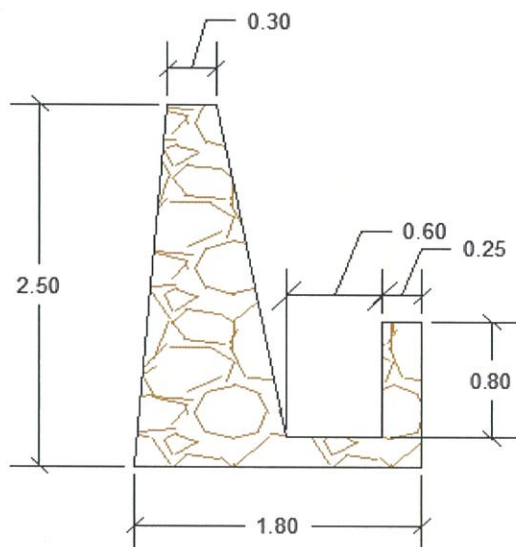

19 September 2022
137° SE
ADN IP. M. Manufahi
kak@Majo



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

CONTRACT NO. : MPW-W-220007
CONTRACT NAME : ROAD MAINTENANCE SECTIONS : JCT AITUTO - SAM E- BETANO 23KM (A04) MANUFAHI MUNICIPALITY
CONTRACTOR NAME : BEMOS,1 UNIPessoal LDA.
CERTIFICATE NO. : PAYMENT NO 01 (FIRST PAYMENT)
PERIOD COVERED : UP TO JUNE 2022

ANEXO C2										
NO. PAY ITEM	ITEM DESCRIPTION	Original Contrac	AND, IP, PROGRES							
			BILLED QUANTITY		BILLED AMOUNT \$		To Date		Observasaun	
			Previos Billing		This Billing					
		Cost (\$)	Amount (\$)	%	Amount (\$)	%	Amount (\$)	%	Amount (\$)	%
100	GENERAL	\$ 5,000.00	\$ 2,500.00	1.90%	\$ -	0.00%	\$ 2,500.00	1.90%		
200	EARTWORK	\$ 24,018.00	\$ 15,131.16	11.47%	\$ 180.00	0.14%	\$ 15,311.16	11.61%		
500	BRIDGE CONTRUCTION	\$ 5,100.00	\$ 5,100.00	3.87%	\$ -	0.00%	\$ 5,100.00	3.87%		
600	DRAINAGE & SLOPE PROTECTION STR.	\$ 39,888.96	\$ 26,596.70	20.17%	\$ 3,071.25	2.33%	\$ 29,667.95	22.49%		
700	MISCELLANEOUS STRUCTURES	\$ 40,500.00	\$ 40,500.00	30.71%	\$ -	0.00%	\$ 40,500.00	30.71%		
	Total	\$ 114,506.96	\$ 89,827.86	68.11%	\$ 3,251.25	2.47%	\$ 93,079.11	70.57%		
	Provit (10%)	\$ 11,450.70	\$ 8,982.79	6.81%	\$ 325.13	0.25%	\$ 9,307.91	7.06%		
	Overhead	\$ 3,350.00	\$ 1,675.00	1.27%	\$ -	0.00%	\$ 1,675.00	1.27%		
	Tax (2%)	\$ 2,586.15	\$ 2,009.71	1.52%	\$ 71.53	0.05%	\$ 2,081.24	1.58%		
	Grand Total	\$ 131,893.81	\$ 102,495.36	77.71%	\$ 3,647.90	2.77%	\$ 106,143.26	80.48%		

Prepared by :

Verified by :

Certified by :

1. Eng. Romulo J.M. Henrique
Engenheiro da Projecto Infraestrutura transportes e Irrigasaun
Manufahi A D N IP

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade
ADN IP



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

REPÚBLICA DEMOCRÁTICA DE TIMOR-LESTE

MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, LP.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

ANEXO D (Same 26)

Naran projeto :ROAD MAINTENANCE SECTIONS : JCT AITUTO - SAM E-
BETANO 23KM (A04) MANUFAHI MUNICIPALITY

Kompanha : Bee mos Unip Ida

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	14/9/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi		Monitorio ba Projeito Husu Atu Acelera Serbisu tamba iha Erozaun (rai halai) hodi eveita ba kumunidade nia rai no uma iha leten tamba nee preisija protese lalais.	
II	14/9/2022	Manufahi / Same	Majorico Cele Tali	Enginheiro A D N IP Municipio Manufahi		Serbisu tuir Orientaun BOQ no Dezenho karik iha mudansa item serbisu presija kordena ho Dona do projeto	
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		



ANEXO C1 (FTB 8)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 9+000 - 12 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210097

Data Inspesaun : 20/ 09 /2022


Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas : Start Point : Latetude -8,9998699S, Long: 125.654606E
End Point : Latetude: 8.99180S , Long: 125.91715E


Naran Inspector : 1. Romulo J. M. Henrique
: 2. Majorico Cele Tali

Sketch & Foto Desenho

Item Cement Concrete pavement



Item Structure Excavation



Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público


ADN, I.P.

INSTRUSAUN / REKOMENDASAUN

ANEXO D (FTB 8)

Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Cha. 9+000 - 12 + 000 , Manufahi Municipality

Kompanha : Alifa Unip,Lda

INSTRUSAUN / REKOMENDASAUN					Asinatura				
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN			
I	20/0/2022	Manufahi / Same	Romulo J.M Henrique	Engenheiro A D N IP Município Manufahi	1				
					2				
					3				
					4				
					5				
II	20/0/2022	Manufahi / Same	Majorico Cele Tali	Engenheiro A D N IP Município Manufahi	1				
					2				
					3				
					4				
					5				
III					1				
					2				
					3				
					4				
					5				
IV					1				
					2				
					3				
					4				
					5				
V					1				
					2				
					3				
					4				
					5				



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME 7)

Back-up Data

Naran Projeto : CONSTRUSAUN PONTE E RIO DE KASABOKA AT BE METAN ,
BETANO SAME SUB DISTRIC MANUFAHI
No. kontratu : SSS / 102/MOPTC-2016

Data Inspesaun 20/9/2022

Fatin Inspesaun : Same Villa

Koordinadas :


Start Point : Latetude: -9.1672S, Long: 125.7161E

End Point : Latetude: -9.1672S, Long: 125.7161E

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Item Stone Masonry Wall, L = 25 m





VIII GOVERNO CONSTITUCIONAL
MINISTÉRIO DO PLANEAMENTO E
INVESTIMENTO ESTRATÉGICO



ADN
Agência de
Desenvolvimento
Nacional

Name of Project
Location of Project
Work Item
Contractor Name

Construction Of New Bridge at Kaboska River.
Aldeia Bemetan, Suco Betano Sub-Distrito Same, Distrito Manufahi
Bill of Quantities
Monte Sul Unip.Lda

Pay Item	Description	Original Contract Cost (\$)	ADN Progress			
			Anexo C2			
			Previous billing		This Billing	
		Cost (\$)	Cost (\$)	%	Cost (\$)	To Date Cost (\$)
100	GENERAL REQUIREMENTS	\$ 10,900.00	\$ 5,125.00	1.56%	\$ -	\$ 5,125.00
200	EARTHWORKS	\$ 20,373.64	\$ 4,163.59	1.27%	\$ -	\$ 4,163.59
300	SUB BASE AND BASE COURSE	\$ 9,554.61	\$ -	0.00%	\$ -	\$ -
400	SURFACE COURSE	\$ 12,591.00	\$ -	0.00%	\$ -	\$ -
500	BRIDGE CONSTRUCTION	\$ 213,269.20	\$ 175,166.39	53.28%	\$ -	\$ 175,166.39
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	\$ 26,320.45	\$ 4,608.20	1.40%	\$ 4,629.84	\$ 9,238.04
A	TOTAL COST	\$ 293,008.90	\$ 189,063.18	57.51%	\$ 4,629.84	\$ 193,693.02
B	PROFIT & OVERHEAD 10% * A	\$ 29,300.89	\$ 18,906.32	5.75%	\$ 462.98	\$ 19,369.30
C	TAX 2% * (A + B)	\$ 6,446.20	\$ 4,159.39	1.27%	\$ 101.86	\$ 4,261.25
D	GRAND TOTAL COST (A + B + C)	\$ 328,755.98	\$ 212,128.89	64.52%	\$ 5,194.68	\$ 217,323.57

Prepared by :

Verified by :

Certified by :

1. Eng. Romulo J.M. Henriques 2. Eng. Maiorico Cele Tali
Engenheiro da Projecto Infraestrutura transportes e Irrigasaun Municipio Manufahi A
D N IP

Eng. Remigio da C.S. dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D
N IP

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade
ADN IP



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (SAME 21)

Back-up Data

Naran Projeto : R4D Rural Road Routine Maintenance, Manico -Lianai-Grotu
Chainage 0+000 - 11+200, Manufahi Municipality
No. kontratu : MPW - W - 210092

Data Inspesaun 21/9/2022

Fatin Inspesaun : Same Villa / Gtotu – Lianai - Grotu

Koordinadas :

Start Point : Latetude: -9.0353S, Long: 125.6069E

End Point : Latetude: -9.02913S, Long: 125.61682E

Naran Inspector : 1. Romulo J.M.Henrique

: 2. Majorico Cele Tali

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PIANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

ADN, I.P.

INSTRUSAUN / REKOMENDASAUN

ANEXO D (SAME 21)

Naran projeto : R4D Rural Road Routine Maintenance, Manico - Lianai-Grotu
Chainage 0+000 - 11+200, manufahi Municipality

Kompanha : Haud Dairam, Unip . Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	21/9/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1	Projeto Parado Hela	
					2		
					3		
					4		
					5		
II	21/9/2022	Manufahi / Same	Majorico Cele Tali	Enginheiro A D N IP Municipio Manufahi	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 2)

Back-up Data

Naran Projeto : Emergency proposed for the new cons. of bridge, Gabions & retaining wall in Area Fatuk Mutin

No. kontratu : SSS/151/MOPTC-2017

Data Inspesaun : 20/09/2022

Fatin Inspesaun : Fatuberliu

Koordinadas :

Start Point : Long : 9.0327183S, Latetude : 125.9946616 E



Naran Inspector : 1. Romulo J. M. Henrique

2. Majorico Cele Tali

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item Servisu Gabions Wall





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



INAP, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

Project / Location : Emergency Proposed For new Construction of bridge, with retaining wall in area fatu mutin, fatukahi adminstrive manufahi municipality
Contractor : Concorcio fatuledu timor Lda.
Location : Baria Laran, Uma Berloik, Alas Sub District. Manufahi District
Posto : Fatuberliu
Municipality : Manufahi

ANEXO C2

Pay Item	Description	Cost (\$)	A.D.N progres						%
			BILLET WORKS AMOUNT						
			Previous Billing		This Billing		To Date		
			Cost (\$)	%	Cost (\$)	%	Cost (\$)	%	
			Cost (\$)	%	Cost (\$)	%	Cost (\$)	%	
100	General Requirements	\$ 39,017.55	\$ 2,631.09	0.58%	-	0.00%	\$ 2,631.09	0.58%	
200	Earth Work	\$ 11,730.32	\$ 2,060.20	0.46%	287.31	0.06%	\$ 2,347.51	0.52%	
300	Concerete structural Protection	\$ 40,756.95	-	0.00%	-	0.00%	\$ -	0.00%	
500	Bridge Contruction	\$ 253,921.80	\$ 33,845.19	7.50%	-	0.00%	\$ 33,845.19	7.50%	
600	Concerete slope protection Structureure	\$ 102,920.05	\$ 1,464.55	0.32%	1,481.04	0.33%	\$ 2,945.59	0.65%	
700	Miscelleneaeous Structureure	\$ 3,222.43	\$ -	0.00%	-	0.00%	\$ -	0.00%	
A	TOTAL CONSTRUCTION COST	\$ 451,569.10	\$ 40,001.03	8.86%	1,768.35	0.39%	\$ 41,769.38	9.25%	

Prepared by :

1. Eng. Romulo J.M. Henrique
Engenheiro ba Projecto Infraestrutura e Irrigasaun - Municipio Manufahi A
D N IP

Verified by :

Eng. Remigio da C.S. dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D
N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade
ADN IP



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIA GOVERNO CONSTITUCIONAL



ADN, LP.

Agência de
Informação e
Monitoramento
Nacional, Estatístico e Público

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (FTB2)					
Naran projeto : Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin					
Kompanha : Concorcio Fatuledu.Lda					
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	22/9/2022	Alas	Romulo J.M.Henrique	Eng.M.Manufahi	1
II	22/9/2022	Alas	Majorico Cele Tali	Eng.M.Manufahi	2
III					3
IV					4
V					

INSTRUSAUN / REKOMENDASAUN		Asinatura
Monitorio Ba Projeto		
Husu ba kompania atu aloka Enginheiro tekniku iha rerenno atu nunee ami bele komfirma konaba item serbisu sira		
Sujere ba kompania atu aumenta tan trabalhador hodi nunee bele acelera serbisu tuir tempo determinasaun iha Kontrato		
Sujere ba kompania atu halo renovasaun ba Papan nama Proyek		
Husu ba kompania atu koordena ho Dono do Projeto ka Obras Publika molok atu ezejuta no halo serbisu ba item refere .		



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (ALS 2)

Back-up Data

Naran Projeto : Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2

No. kontratu : SSS/148/MOPTC-2017

Data Inspesun : 22/09/2022

Fatin Inspesun : Wekakao Oan

Koordinadas :

Start Point : Long : -9.036777078 Latetude : 125.8481587



Naran Inspector : 1. Romulo J. M. Henrique

: 2. Majorico Cele Tali

Aktual Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch tem concrete structural protection

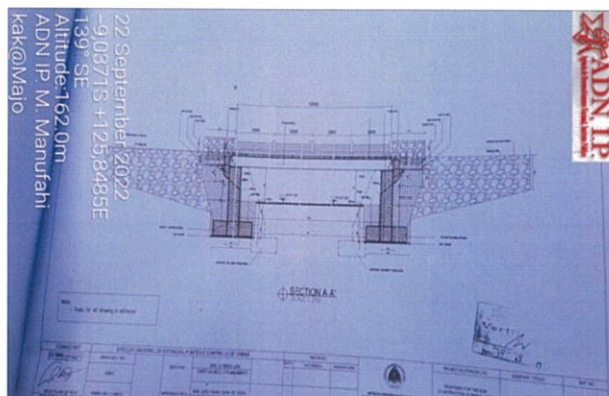



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL




ADN, I.P.

Agência de
Normalização Pública

INSTRUSAUN / REKOMENDASAUN ANEXO C1 (ALS 2)

Naran projeto : Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2

Kompanha : Consorcio Nacional Manufahi Lda

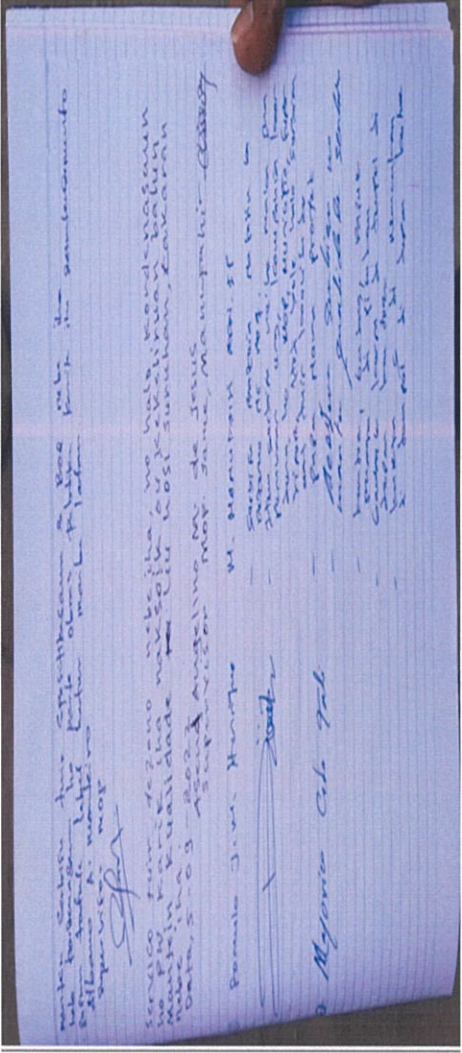No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/9/2022	Manufahi / Alas	Romulo J. M. Henrique	Eng.A D N IP Manufahi	1	Equipa halo Monitorizasaun ba Projeto Serbisu bazeia nafatin ba Dezenu no BOQ, iha item servisu neebe maka iha dokumentus laran, husu ba Eng. Kompania atu koordena ho dono do projeto MOP, Eng. Supervisor Municipio hodi bele halo servisu tuir kualidade	
II	22/9/2022	Manufahi / Alas	Majorico Cele Tali	Eng.A D N IP Manufahi	2	Bazeia ba Equipa ADN, IP. Halo Monitorizasaun ba projeto iha tereno kompania hahu kontinua servisu konstrusaun refere maibe ita seidauk bele konsidera nia progresu fisiku tamba kompania servisu ba item CONCRETE STRUCTURAL PROTECTION latuir espesifikasaun ka BOQ hatete, Concrete Retaining Wall (30 mpa) mas kompania ezejuta fali stone masonry wall karik iha ona virifikasaun no aprovasaun husi dono do projeto maka equipa ADN IP bele konsidera nia progresu fisiku nec.	
III					3		
IV					4		



ANEXO C1 (FTB 9)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 6+000 - 9 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210098

Data Inspesaun : 20/09/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :

Start Point : Latetude: 9.01163S, Long: 125.92485E

End Point : Latetude: 8.83956S, Long: 125.63432E



Naran Inspector : 1. Romulo J.M.henrique

: 2. Majorico Cele Tali

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Projeto Finaliza ona 100 %

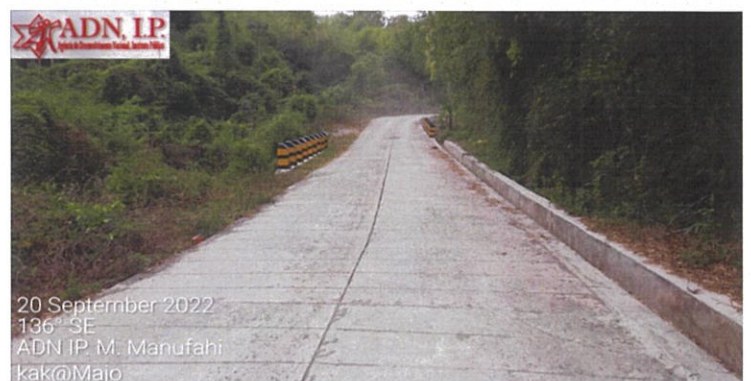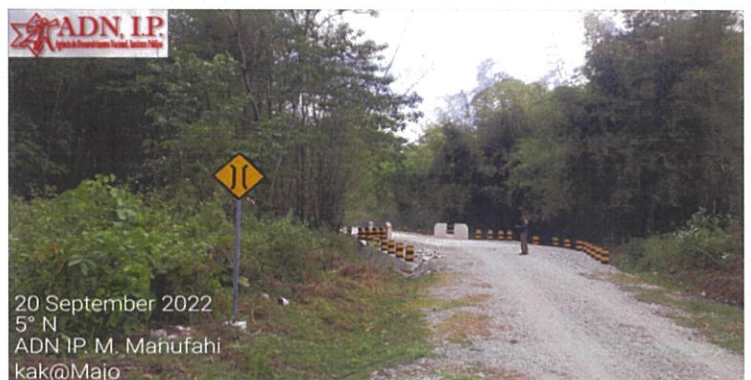



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Name of the Road: Caicasa - Fatu Cahi, Cha. 6+000 - 9+000
Contract No. : MPW-W-210098

Contractor: Manufahi Lui Unip. Lda.

ANEXO C2									
Pay ITEM NO.	DESCRIPTION	ADN Progress							
		ORIGINAL CONTRAC		BILLED QUANTITY		BILLED AMOUNT \$		Obs	
		Cost (\$)		Previous Billing	This Billing	To date			
		COST (\$)	%	COST (\$)	%	COST (\$)	%		
R-01. General		\$ 4,260.00	0.73%	\$ 2,990.00	0.31%	\$ 4,260.00	1.04%		
R-03 Earth work		\$ 23,849.57	5.61%	\$ 22,929.53	0.23%	\$ 23,849.57	5.83%		
R-05 Granular sub- base and base		\$ 7,871.18	1.93%	\$ 7,871.18	0.00%	\$ 7,871.18	1.93%		
R-08 Structure		\$ 296,194.69	71.76%	\$ 293,347.12	0.70%	\$ 296,194.69	72.45%		
R-10 Dayworks		\$ 350.00	0.09%	\$ 350.00	0.00%	\$ 350.00	0.09%		
R-11 Routine maintenance		\$ 7,129.60	1.74%	\$ 7,129.60	0.00%	\$ 7,129.60	1.74%		
R-15 Provisional Sum		\$ 1,500.00	0.37%	\$ 1,500.00	0.00%	\$ 1,500.00	0.37%		
G-01 Security	Total of R-Item	\$ 341,155.03	82.22%	\$ 336,117.43	1.23%	\$ 341,155.03	83.45%		
G-02 Project Item		\$ 1,518.00	0.34%	\$ 1,391.50	0.03%	\$ 1,518.00	0.37%		
G-03 Safety and Protection		\$ 15,774.00	3.51%	\$ 14,349.50	0.35%	\$ 15,774.00	3.86%		
G-06 erenonal Coosts		\$ 7,988.20	1.94%	\$ 7,937.60	0.01%	\$ 7,988.20	1.95%		
		\$ 250.00	0.03%	\$ 125.00	0.03%	\$ 250.00	0.06%		
	Total of G-Item	\$ 25,530.20	5.82%	\$ 23,803.60	0.42%	\$ 25,530.20	6.24%		
A	Total - net cost	\$ 341,155.03	82.22%	\$ 336,117.43	1.23%	\$ 341,155.03	83.45%		
B	Contractor's Profit (net cost x %) ; 10%	\$ 34,115.50	8.22%	\$ 33,611.74	0.12%	\$ 34,115.50	8.34%		
C	General item	\$ 25,530.20	5.82%	\$ 23,803.60	0.42%	\$ 25,530.20	6.24%		
D	Tax ((net cost + profit+ Over head) x 2 %)	\$ 8,016.01	1.93%	\$ 7,870.66	0.04%	\$ 8,016.01	1.96%		
E	Total Evaluated price	\$ 408,816.75	98.19%	\$ 401,403.43	1.81%	\$ 408,816.75	100%		

Prepared by :

1. Romulo J.M. Henrique 2. Majorico Cele Tali
Engenheiro ba Projecto Infraestrutura transporte e Irrigasaun Munisipio
Manufahi A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A
D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlu e validacao qualidade
ADN IP



ANEXO D (FTB 9)

Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Cha. 6+000 - 9 + 000 , Manufahi Municipality

Kompanha : Manufahi Lui Unip,Lda

Asinatura

Equipa halo Monitorizaun ba projeto

Projeto Finaliza 100 %. Sujere nafatin ba kompania atu halo kontrola nafatin ba proyekto refere tamba sei iha tempu rensaun.

Cliff



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 7)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Sp Satu Cha. 0+000 - 7
+ 900 , Manufahi Municipality

No. kontratu : MPW - W - 210095

Data Inspesaun : 20/09/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :

Start Point : Latetude : 9.03677S, Long: 125.99846E

EndPoint: Latetude : 9.05708S, Long: 125.02474E


Naran Inspector : 1. Romulo J. M. Henrique

: 2. Majorico Cele Tali



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Item Granular sub- base and base



Item Stone Masonry

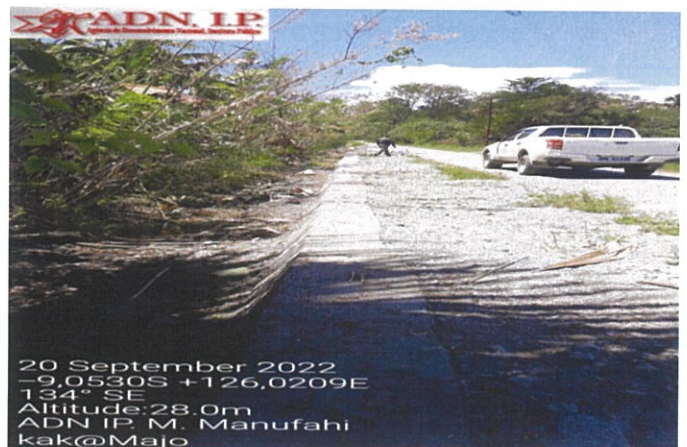



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

Name of the Road : Caicasa - Fatucabi Sp Satu , 0 + 000 - 7 + 900
Contract No : MPW - W - 210095

Contractor : Leo - Hilin Unipessoal Lda		ANEXO C1						
Pay ITEM NO.		ADN Progress						
DESCRIPTION		ORIGINAL CONTRAC	BILLED QUANTITY		BILLED AMOUNT \$		Obs	
			Previous Billing		This Billing			
			COST (\$)	%	COST (\$)	%		
R-01.	General	\$ 2,200.00	\$ 1,150.00	0.93%	\$ 50.00	0.04%	\$ 1,200.00	0.97%
R-03	Earth work	\$ 13,593.30	\$ 8,993.90	7.25%	\$ 408.10	0.33%	\$ 9,402.00	7.58%
R-05	Granular sub- base and base	\$ 25,544.92	\$ 21,320.16	17.19%	\$ 326.55	0.26%	\$ 21,646.71	17.45%
R-08	Structure	\$ 42,809.20	\$ 30,351.73	24.47%	\$ 1,076.88	0.87%	\$ 31,428.61	25.34%
R-10	Dayworks	\$ 700.00	\$ 175.00	0.14%	\$ -	0.00%	\$ 175.00	0.14%
R-11	Routine maintenance	\$ 15,873.60	\$ 9,817.40	7.91%	\$ -	0.00%	\$ 9,817.40	7.91%
R-15	Provisional Sum	\$ 1,000.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
Total of R-Item		\$ 101,721.02	\$ 71,808.19	57.89%	\$ 1,861.53	1.50%	\$ 73,669.72	59.39%
G-01	Security	\$ 1,800.00	\$ 1,500.00	1.21%	\$ -	0.00%	\$ 1,500.00	1.21%
G-02	Project Item	\$ 5,304.00	\$ 4,578.00	3.69%	\$ -	0.00%	\$ 4,578.00	3.69%
G-03	Safety and Protection	\$ 2,014.00	\$ 1,974.00	1.59%	\$ -	0.00%	\$ 1,974.00	1.59%
G-06	eremonal Coosts	\$ 600.00	\$ 300.00	0.24%	\$ -	0.00%	\$ 300.00	0.24%
Total of G-Item		\$ 9,718.00	\$ 8,352.00	6.73%	\$ -	0.00%	\$ 8,352.00	6.73%
A	Total - net cost	\$ 101,721.02	\$ 71,808.19	57.89%	\$ 1,861.53	1.50%	\$ 73,669.72	59.39%
B	Contractor's Profit (net cost x %) : 10%	\$ 10,172.10	\$ 7,180.82	5.79%	\$ 186.15	0.15%	\$ 7,366.97	5.94%
C	General item	\$ 9,718.00	\$ 8,352.00	6.73%	\$ -	0.00%	\$ 8,352.00	6.73%
D	Tax ((net cost + profit+ Over head) x 2 %)	\$ 2,432.22	\$ 1,746.82	1.41%	\$ 40.95	0.03%	\$ 1,787.77	1.44%
E	Total Evaluated price	\$ 124,043.34	\$ 89,087.83	71.82%	\$ 2,088.64	1.68%	\$ 91,176.47	73.50%

Certified by :

Verified by :

Prepared by :

[Signature]

[Signature]

[Signature]

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

1. Romulo J.M.Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Manufahi A D N IP



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, LP.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN					
ANEXO D (FTB 7)					
Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Sp Satu Cha. 0+000 - 7 + 900 , Manufahi Municipality					
Kompanha : Leo Hilin Unip,Lda					
INSTRUSAUN / REKOMENDASAUN					Asinatura
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	20/09/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1
					2
					3
					4
					5
II	20/09/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1
					2
					3
					4
					5
III					1
					2
					3
					4
					5
IV					1
					2
					3
					4
					5
V					1
					2
					3
					4
					5

Monitorio ba projeto

Husu ba kompania atu hadian serbisu Item **Granular sub- base and base** neebe sedauk diak, iha ketebalan, surfase sae tun (gelombang) no mos kompaktus sedauk metin presija rega mos ho bee.

Husu ba kompania atu aloka Eginheiro tekniko iha tereno tamba Equipa AND, IP halo monitorizasaun ba konstrusaun projeto Eginheiro tekniku kompania laiha tereno hodi komfirma item serbisu refere.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 6)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 0+000 - 6 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210099

Data Inspesaun : 19/07/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :

Start Point : Latetude 9.01605S, Long: 125.92783E

End Point: Latetude: 8.83956S , Long: 125.63432E

Naran Inspector : 1. Romulo J. M. Henrique

: 2. Majorico Cele Tali

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Item Traffic Signboard



Item Garanular Pavement- Gravel Surface





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIA GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Planejamento e
Ordenamento
Nacional, Instituto Público

Name of the Road : Caicasa - Fatucahi , 0 + 000 - 6 + 000

Contract No : MPW - W - 210099

Contractor : Loskabubu Unipessoal Lda

ANEXO C2

Pay ITEM NO.	DESCRIPTION	ORIGINAL CONTRAC	ADN Progress						Obs
			BILLED QUANTITY		BILLED AMOUNT \$		To date		
			This Billing		COST (\$)	%			
			Previous Billing	%					
		Cost (\$)	COST (\$)	%	COST (\$)	%	COST (\$)	%	
R-01.	General	\$ 4,520.00	\$ 3,467.50	1.03%	\$ 1,052.50	0.31%	\$ 4,520.00	1.34%	
R-03	Earth work	\$ 54,159.21	\$ 54,159.21	16.07%	\$ -	0.00%	\$ 54,159.21	16.07%	
R-05	Granular sub- base and base	\$ 55,087.20	\$ 55,087.20	16.34%	\$ -	0.00%	\$ 55,087.20	16.34%	
R-08	Structure	\$ 157,702.29	\$ 157,702.29	46.78%	\$ -	0.00%	\$ 157,702.29	46.78%	
R-10	Dayworks	\$ 350.00	\$ 350.00	0.10%	\$ -	0.00%	\$ 350.00	0.10%	
R-11	Routine maintenance	\$ 8,361.00	\$ 8,361.00	2.48%	\$ -	0.00%	\$ 8,361.00	2.48%	
R-15	Provisional Sum	\$ 1,500.00	\$ 1,500.00	0.44%	\$ -	0.00%	\$ 1,500.00	0.44%	
	Total of R-Item	\$ 281,679.71	\$ 280,627.21	83.24%	\$ 1,052.50	0.31%	\$ 281,679.71	83.56%	
G-01	Security	\$ 1,380.00	\$ 1,380.00	0.41%	\$ -	0.00%	\$ 1,380.00	0.41%	
G-02	Project Item	\$ 12,540.00	\$ 12,540.00	3.72%	\$ -	0.00%	\$ 12,540.00	3.72%	
G-03	Safety and Protection	\$ 6,488.00	\$ 6,488.00	1.92%	\$ -	0.00%	\$ 6,488.00	1.92%	
G-06	eremonal Costs	\$ 250.00	\$ 250.00	0.07%	\$ -	0.00%	\$ 250.00	0.07%	
	Total of G-Item	\$ 20,658.00	\$ 20,658.00	6.13%	\$ -	0.00%	\$ 20,658.00	6.13%	
A	Total - net cost	\$ 281,679.71	\$ 280,627.21	83.24%	\$ 1,052.50	0.31%	\$ 281,679.71	83.56%	
B	Contractor's Profit (net cost x %) ; 10%	\$ 28,167.97	\$ 28,062.72	8.32%	\$ 105.25	0.03%	\$ 28,167.97	8.36%	
C	General item	\$ 20,658.00	\$ 20,658.00	6.13%	\$ -	0.00%	\$ 20,658.00	6.13%	
D	Tax (net cost + profit+ Over head) x 2 %	\$ 6,610.11	\$ 6,586.96	1.95%	\$ 23.16	0.01%	\$ 6,610.11	1.96%	
E	Total Evaluated price	\$ 337,115.79	\$ 335,934.88	99.65%	\$ 1,180.91	0.35%	\$ 337,115.79	100%	

Prepared by :

Verified by :

Certified by :

1. Eng. Romulo J.M. Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Municipal Manufahi A D N IP

Eng. Remigio da C.S. dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade ADN IP



Agência de
Desenvolvimento
Nacional, Instituto Público

VIII GOVERNO CONSTITUCIONAL

Kompanha : Loskabubu Unip Lda

Handwritten signature

REPUBLICA DE TIMOR-LESTE MINISTERIO DO PLANO E ORDENAMENTO ADN, LP Agencia de Desenvolvimento e Planeamento PLANU INSPESAUN																																						
Naran Eng.		Eng. Majorico Cele Tali		2022																																		
Munisipiu		MANUFAHI																																				
Postu	No	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	Action	SETEMBRO																														OBSERVASAUN
								1	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
ALAS (ALS)	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2	MINISTERIO DAS OBRAS PUBLICAS	FI	Conorcio Nacional Manufahu Lda	SSS/148/MOPTC-2017	Plan																													ON GOING (Konstrusaun hahu fila fali iha fulan klaran Setembro nian)		
							Actual																															
	3	Emergency new construction of gabion box protection random fill in area Lacio, Bara Laran, Uma Berloio, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	Conorcio 1912 MF Lda	SSS/279/MOPTC-2016	Plan																												FHO (Projeto refere finaliza ona)			
							Actual																															
	4	Rural Roads Routine Maintenance Dotic, Weberck, Chainage 0+000 - 6+300, Dotic, Wekakaon, Chainage 0+000 - 8+600, Tukumu Ferikare, Chainage 0+000 - 4+300 Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Samboio Unip Lda	MPW-RFQ-190017	Plan																												Parado			
							Actual																															
	6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota C'ere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	Plan																												FHO (Projeto refere finaliza ona)			
							Actual																															
	8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipo Roads" Package 6 : Alas - Wedauberek	MINISTERIO DAS OBRAS PUBLICAS	LM	PT. Bikarna Jr Aureum Solis Consultant Unip Lda	MPW-CS-2000033	Plan																															
							Actual																															
10	Rural Roads Rehabilitation Ferikare Chainage 4+300 - 6+350 Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	My Friend Unip. Lda	MPW-W-190106	Plan																													FHO (Projeto refere finaliza ona)			
						Actual																																
11	Rehabilitasaun Estrada Tekumu-Ferikare 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/062/MOPTC-2016	Plan																													Parado			
						Actual																																
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	Conorcio Unumafa Lda	SSS/150/MOPTC-2017	Plan																													ON GOING			
						Actual																																
13	R4D Rural Road Routine Maintenance, Dotic - Weberck Chainage 0+000 - 6+300 and Dotic - Wekakaon Chainage 0+000 - 8+600 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Werenek Unpessoal Lda	MPW-W-210093	Plan																													ON-GOING			
						Actual																																
FATUBERLU (FTB)	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	Conorcio Fatuledu Lda	SSS/151/MOPTC-2017	Plan																												ON-GOING			
							Actual																															
	2	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besa	MINISTERIO DAS OBRAS PUBLICAS	FI	conorcio Nacional ba Futuro	SSS/149/MOPTC-2017	Plan																												Parado			
							Actual																															
	4	New Construction of Sukar Oan River cyclop Concrete Retaining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	Conorcio Nacional Samdi. Lda (CNS)	SSS/102/MOPTC-2017	Plan																												Parado			
							Actual																															
	5	R4D Rural Road Routine Maintenance, Tukumu Ferikare Chainage 0+000-6+350 Manufahu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MARDIROMIG VQSAM, UNIPESOAAL LDA	MPW-W-210096	Plan																											Parado				
							Actual																															
	6	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Loskabubu	MPW-W-210099	Plan																												PHO			
							Actual																															
7	R4D Rural Road Spot Improvement Caicasa - Fatucasu SP SATU Chainage 0+000 - 7+900 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Leo-Hilin Unpessoal Lda	MPW-W-210095	Plan																												ON-GOING				
						Actual																																
8	R4D Rural Road Spot Improvement Caicasa - Fatucasu Chainage 0+000 - 6+000 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alida Pereira	MPW-W-210097	Plan																												ON-GOING (Maibe serbisu iha fulan Setembro progresu laiha mudansa)				
						Actual																																
9	R4D Rural Road Spot Improvement Caicasa - Fatucasu Chainage 6+000 - 9+000 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Mamu-Fahu Lus Unpessoal Lda	MPW-W210098	Plan																												PHO				
						Actual																																
10	New construction of tower Protection Wall no 92 Section Betano - Viqueque manufahu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM	My friend Constr. Unip. Lda	NCB/ 028/MOP- 2020	Plan																												Parado				
						Actual																																
SAME (SAME)	6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Conorcio Cablaku Oan Lda	SSS/270/MOPTC-2016	Plan																												Parado			
							Actual																															
	7	Construção Ponte e rio de Kaboska at Betetan, Betano, Same Sub District, Manufahu	MINISTERIO DAS OBRAS PUBLICAS	FI	Monte Sul Unip Lda	SSS/102/MOPTC-2016	Plan																												ON GOING			
							Actual																															
	8	Periodic Maintenance Same - Kamilaran - Aihili - Rotutu Sta. 0+000-12+000 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOPTC-2016	Plan																												FHO (Projeto refere finaliza ona)			
							Actual																															
	9	Mantenisaun Estrada Manico-Lunai-Groto Sta. 0+000-10+550- no Manutenisaun Estrada Ladaki Sta. 0+000-1+200 Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/057/MOPTC-2016	Plan																											Parado				
							Actual																															
	10	Road Maintenance Section Same Urban Roads Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM	Renova Unip Lda	MPW-W-190215	Plan																												Parado			
							Actual																															
	11	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76.4 km Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Quintas das Flores. Lda	MPW-W-190123	Plan																															

Note:	Planu Periode inspesaun iha tercinu	Implementa Planu Periode Inspeksaun iha Tercinu	Relatorio Mensal Iha Dili	Inspeksaun Proccesu Pagamento
--------------	-------------------------------------	---	---------------------------	-------------------------------

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)

Coordenador da Unidade de Controlo e Validação de Qualidade ADN IP



Aprova Husi 3

(Eng. Januario Maia Guterres)
Adjunto Director Ejecutivo ADN IP

 MINISTÉRIO DO PLANO E ORDENAMENTO SECRETARIA DE PLANEJAMENTO E ORÇAMENTO ADN, L.P. Agência de Apoio à Administração Municipal Assessoria Técnica e Consultoria		PLANU INSPESAUN																																				
Naran Eng.		Eng. Romulo J. M. Henrique					2022																															
Munisipiu		MANUFAHI																																				
Posta	No	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	Action	SETEMBRO																														OBSERVA SAUN
								\	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
ALAS (ALS)	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kalau Oan 2	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcao Nacional Manufahu Lda	SSS/148/MOPTC-2017	Plan Actual																											ON GOING (Konstrusaun hahu fila fali iha fulan klan Setembro nian)				
	3	Emergency new construction of gabion box protection random fill in area Lacio, Bara Laran, Uma Berlok, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcao 1912 MF Lda	SSS/279/MOPTC-2016	Plan Actual																											FHO (Projeto refere finaliza ona)				
	4	Rural Roads Routine Maintenance Dotic Weberck, Chainage 0+000 - 6+100, Dotic Wekakaon, Chainage 0+000 - 8+600, Tukumu Feriksaare, Chainage 0+000 - 4+300 Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Samboio Unip.Lda	MPW-RFQ-190017	Plan Actual																											Parado				
	6	Konstrusaun Barrera 300m no Normalizasaun 400 m Mota Clere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	Aplayana unip. Lda	16/PDIM-MF/IX/2019	Plan Actual																												FHO (Projeto refere finaliza ona)			
	8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wodauberek	MINISTERIO DAS OBRAS PUBLICAS	LM	PT. Bikarma Jr Aureum Solu Consultant Unip Lda	MPW-CS-2000033	Plan Actual																															
	10	Rural Roads Rehabilitation Feriksaare Chainage 4+300 - 6+350 Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	My Friend Unip. Lda	MPW-W-190106	Plan Actual																												FHO (Projeto refere finaliza ona)			
	11	Rehabilitasaun Estrada Tukumu-Feriksaale 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/062/MOPTC-2016	Plan Actual																											Parado				
	12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcao Unimafa Lda	SSS/150/MOPTC-2017	Plan Actual																												ON GOING			
	13	R4D Rural Road Routine Maintenance, Dotic - Weberck Chainage 0+000 - 6+300 and Dotic - Wekakaon Chainage 0+000 - 8+600 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Werenek Unipessoal Lda	MPW-W-210093	Plan Actual																												ON-GOING			
	FATUBERLIU (FTB)	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcao Fatuletu Lda	SSS/151/MOPTC-2017	Plan Actual																												ON-GOING		
2		Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	MINISTERIO DAS OBRAS PUBLICAS	FI	concorcao Nacional ba Futuro	SSS/149/MOPTC-2017	Plan Actual																												Parado			
4		New Construction of Sukaei Oan River cyclop Concrete Retaining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcao Nacional Samdi, Lda (CNS)	SSS/102/MOPTC-2017	Plan Actual																												Parado			
5		R4D Rural Road Routine Maintenance, Tukumu Feriksaare Chainage 0+000-6+350 Manufahu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MARDIKOMIG VTOSSAM, UNIPESOA Lda	MPW-W-210096	Plan Actual																												Parado			
6		R4D RURAL ROAD SPOT IMPROVEMENT CAKASA - FATUCAHI CHAINAGE 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Loskabubu	MPW-W-210099	Plan Actual																												PHO			
7		R4D Rural Road Spot Improvement Cakasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Leo-Hian Unipessoal Lda	MPW-W-210093	Plan Actual																												ON-GOING			
8		R4D Rural Road Spot Improvement Cakasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alida Pereira	MPW-W-210097	Plan Actual																												ON-GOING (Maibe serbisu iha fulan Setembro progresu laiha mudansa)			
9		R4D Rural Road Spot Improvement Cakasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Mamo Fahi Lsu Unipessoal Lda	MPW-W210098	Plan Actual																												PHO			
10		New construction of tower Protection Wall no 92 Section Betano - Vaqueque manufahu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM	My friend Constr. Unip. Lda	NCB/ 028/MOP- 2020	Plan Actual																												Parado			
SAME (SAME)		6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Concorcao Cablaki Oan Lda	SSS/270/MOPTC-2016	Plan Actual																												Parado		
	7	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahu	MINISTERIO DAS OBRAS PUBLICAS	FI	Monte Sol Unip Lda	SSS/102/MOPTC-2016	Plan Actual																												ON GOING			
	8	Periodic Maintenance Same - Kamilaran - Ashili - Rotutu Sta. 0+000-12+ 000 Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOPTC-2016	Plan Actual																												FHO (Projeto refere finaliza ona)			
	9	Manutensaun Estrada Manico-Luanai-Groto Sta. 0+000-10+ 550- no Manutensaun Estrada Ladaki Sta. 0+000-1+ 200 Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/057/MOPTC-2016	Plan Actual																												Parado			
	10	Road Maintenance Section Same Urban Roads Municipality Manufahu	MINISTERIO DAS OBRAS PUBLICAS	LM	Renova Unip Lda	MPW-W-190215	Plan Actual																												Parado			
	11	Routine Road Maintenance Same - Betano - Dior - (A05, A14) / 76,4 km Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Quintas das Flores, Lda	MPW-W-190123	Plan Actual																												FHO (Projeto refere finaliza ona)			
	12	Rural Roads Maintenance Manico - Groto, Chainage 0+000 - 11+200 km Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Alida Pereira	MPW-RFQ 190019	Plan Actual																												Parado			
	13	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahu (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Leo - Dok	MPWTC-CD-170002	Plan Actual																												FHO (Projeto refere finaliza ona)			
	14	Fencing for Construction Monument od Dom Boa Ventura	MINISTERIO TURISMO KOMERCO E INDUSTRIA	LM	Loskabubu	RD/TL/06/GM-MT/AC/IV/2016	Plan Actual																															
	15	Konstrusaun Tangki Beé no Menara Beé ba iha Edifício Administração Municipiu Manufahu	ESTATAL	PDIM	Cold Lsu Unip. Lda	05/PDIM-MF/IV/2017	Plan Actual																															

Note: Planu Periode Inspesau iha Tercinu	Implementa Planu Periode Inspesau iha Terenu	Relatorio Mensal Iha Dili	Inspesau Proceu Pagamento
--	---	--------------------------------------	--------------------------------------

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)

Coordenador da Unidade de Controlo e Validação de Qualidade ADN IP



Aprova Husi

(Eng. Jaguarino Maia Guterres)
Adjunto Director Ejecutivo ADN IP



SAME (SAME)	MINISTERIO DO PLANO E ORDENAMENTO		ADN, I.P.		Agência de Desenvolvimento Nacional, Turismo e Património		PLANU INSPESAUN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
	Naran Eng.		Romulo J.M.Henrique					2022																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
	Munisipiu		MANUFAHI																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
			SETEMBRO																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
	8	Periodic Maintenance Same - Kamilaran - Aihuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOPTC-2016	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Note:

Planu Periode inspesaun iha tercinu

Implementa Planu Periode Inspesaun iha Tereau

Relatorio Mensal iha Dili

Inspeksaun Proceu Pagamento

Prepara Husi :



Eng. Romulo J.M.Henrique
Engenheiro ADN IP Manufahi

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validaaun de Qualidade ADN IP

Aprova Husi :



(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN IP

 MINISTERIO DO PLANO REPÚBLICA DE MOZAMBIQUE  ADN, L.P. Agência de Desenvolvimento Nacional, Investimentos Públicos							PLANU INSPESAUN																													
Naran Eng. Majorico Cele Tali							2022																													
Munisipiu MANUFAHI																																				
Postu	No	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	Action	SETEMBRO																												OBSERVASAUN
								Ma	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr			
ALAS (ALS)	1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	Samboio Unip,Lda	RDITL/MOP-SEE/CGI-PEN : 0000119																														
	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau On 2	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Nacional Manufahi Lda	SSS/148/MOPTC-2017	Plan																													
							Actual																													
	3	Emergency new construction of gabion box protection random fill in area Lacho, Baria Laran, Uma Berlok, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio 1912 MF Lda	SSS/279/MOPTC-2016	Plan																													
							Actual																													
	4	Rural Roads Routine Maintenance Dotic Weberek, Chainage 0+000 - 6+300, Dotic Wekakaon, Chainage 0+000 - 8+600, Tukusu Ferikase, Chainage 0+000 - 4+300 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Samboio Unip,Lda	MPW-RFQ-190017	Plan																													
							Actual																													
	5	Prefurasaun Be'e mos iha Saku Uma Berlok, Aldeia Bessau	MINISTERIO DAS OBRAS PUBLICAS	LM	Buka Fini	MPWTC-NCB-170008	Plan																													
							Actual																													
	6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Cleo	MINISTERIO DAS OBRAS PUBLICAS	PDIM	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	Plan																													
							Actual																													
	7	Konstrusaun Kanalizasaun Kanu Transmisiaun no Distribuissau Hosi Bomba Uma Berlok ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM	Tane Unipessoal Lda	MOP - W - 190210	Plan																													
							Actual																													
8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	MINISTERIO DAS OBRAS PUBLICAS	LM	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033																															
9	Construction and Installation water Gravitation System in Mahaquidam Umberloic Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Verescar Unip. Lda	SSS/289/MOPTC-2016	Plan																														
						Actual																														
10	Rural Roads Rehabilitation Ferikase Chainage 4+300 - 6+350 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	My Friend Unip. Lda	MPW-W-190106	Plan																														
						Actual																														
11	Rehabilitasaun Estrada Tekunu-Ferikase 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/062/MOPTC-2016	Plan																														
						Actual																														
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Unimafa Lda	SSS/150/MOPTC-2017	Plan																														
						Actual																														
13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaon Chainage 0+000 - 8+600 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Werenek Unipessoal Lda	MPW-W-210093	Plan																														
						Actual																														
FATUBERLU (FTB)	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Fatulehu Lda	SSS/151/MOPTC-2017	Plan																													
							Actual																													
	2	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Beai	MINISTERIO DAS OBRAS PUBLICAS	FI	concorcio Nacional ba Futuro	SSS/149/MOPTC-2017	Plan																													
							Actual																													
	3	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberlu-Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Funu Kolik Unip. Lda	RDITL/MOPTC-VMOPTC/CGI-PEN : 00000424																														
	4	New Construction of Sukaer On River cyclop Concrete Retaining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Nacional Samdi, Lda (CNS)	SSS/102/MOPTC-2017	Plan																													
							Actual																													
	5	R4D Rural Road Routine Maintenance, Tukumu Ferikase Chainage 0+000-6+350 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MARDIROMIG VQSAM, UNIPESOA Lda	MPW - W - 210096	Plan																													
							Actual																													
	6	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Loskabubu	MPW-W-210099	Plan																													
							Actual																													
	7	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Leo-Hilin Unipessoal Lda	MPW-W-210095	Plan																													
							Actual																													
8	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alia Pereira	MPW-W-210097	Plan																														
						Actual																														
9	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	Plan																														
						Actual																														
10	New construction of tower Protection Wall no 92 Section Betano - Viqueque manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM	My friend Constr. Unip. Lda	NCB/ 028/MOP- 2020	Plan																														
						Actual																														
	1	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District		FI	Dhalelan,Unip.Lda	RDITL/MOPTC-VOMPTC/CGI-PEN:0000300																														
	2	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Dediva Electrical Unip. Lda	RDITL/MOPTC-VMOPTC/CGI-PEN : 00000385	Plan																													
							Actual																													
	3	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erlili, Luak, Ailok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	Fahia Humalo Unip.Lda	RDITL/MOPTC-VMOPTC/CGI-PEN : 00000430																														
	4	Konstrusaun kanalizasaun bee mos iha selhasan suco Betano, Posto Adm Same, Municipio Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM	Haksolok Java Motor Unip Lda	MOP - W - 190160	Plan																													
							Actual																													
	5	Nova fornecimento água do Bairro PNTL Manufahi	MINISTERIO DO INTERIOR	FI	Tom's Building Unipessoal Lda	SSS/053/MI-2017	Plan																													
						Actual																														
6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Cablaki On Lda	SSS/270/MOPTC-2016	Plan																														
						Actual																														
7	Construção Ponte e rio de Kabonka at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	Monte Sul Unip.Lda	SSS/102/MOPTC-2016																															

 MINISTERIO DO PLANO E ORDENAMENTO REPUBLICA DE TIMOR-LESTE  ADN, IP Agência de Regulação e Normalização Manufahi, Suco de Luro, 162							PLANU INSPESAUN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
Naran Eng.		Romulo J.M.Henrique																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
Munisipiu		MANUFAHI					2022																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
							SETEMBRO																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
8	Periodic Maintenance Same - Kamilaran - Ahuli - Rotutu Sta. 0+000-12+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOPTC-2016	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Note:

Planu Periode inspesaun iha tercinu

Implementa Planu Periode Inspesaun iha Terenu

Relatorio Mensal iha Dili

Inspeksaun Procecu Pagamento

Prepara Husi :

(Eng. Majorico C. Tale)
Engenheiro ADN IP Manufahi

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN IP

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN IP
