



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL
IMPLEMENTASAUN
PROJETUS MUNISÍPIU MANUFAHI

JULHO 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO MANUFAHÍ


JULHO 2022

Prepara Husi :


(Eng. Fidelis Mardiano da Costa)

Eng. ba Edifício Público no Bê Saneamento, Município Manufahi


 
(Eng. Romulo J.M. Henrique) & (Eng. Majorice Cele Tali)
Eng. ba Projeto Infraestrutura e Irigasaun, Município Manufahi ADN, I.P


(Silvino D R R Soares)

Eng. M & E, Município Manufahi ADN, I.P

Verifika Husi :


(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edifício Público no Bê Saneamento, ADN, I.P


(Eng. Remigio da C.S.dos Santos)
Eng. Senior ba Projeto Infraestrutura e Irigasaun, ADN, I.P


(Deolindo de F Marques)
Chefe Sek. Projeto M.E & ITC, ADN, I.P

Sertifika Husi :


(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :


(Mariano Renato Monteiro da Cruz, S. T, M. Eng)
Director Executivo, ADN, I.P

Contents

SUMÁRIO	0
Eng. ba Edifício Público no Beé Saneamento, Município Manufahi	0
ÍNDICE TABELA	0
I. INTRODUSAUN.	2
1.1 Enquadramento Legal.....	2
1.2 Perfil Município Manufahi.....	2
1.3. Lista Projecto.....	5
II. PROGRESSO FÍSICO	19
2.1 Progresso Físico Kada Fulan	19
III. OBSTÁCULO IHA TERENU	19
3.1 Obstáculo Serviço Iha Terenu	19
IV. REKOMENDASAUN IHA TERENU	20
4.1 Rekomendasaun Serviço Iha Terenu	20
 Tabela 1 : Postos Administrativos,Sucos no Aldeias.....	3
<i>Tabela 2.1: Força de Trabalho ADN, I.P Município Manufahi.</i>	3
<i>Tabela 3.2 : Lista Asset ADN,I.P Município Manufahi.</i>	4
<i>Tabela 4.3.1 :Projecto Município Manufahi Por Fundus Financiamento.....</i>	5
<i>Tabela 5.3.2 : Projecto Município Por Sector</i>	9
<i>Tabela 6.3.3 : Projecto Município Por Ministério</i>	14

I. INTRODUSAUN.

1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefisiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projetu sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liuhusi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Manufahi



Mapa 2 hatudu pozisaun jeográfika Administrasaun Munisipal Manufahi iha luan 1,325 km² ho populasau nain 48,628 tuir Sensus 2010. Administrasaun Munisipal Manufahi iha Postos Administrativos ha'at, Sukus 29 no aldeias 137, mak hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos,Sucos no Aldeias.

Alas		Fatuberlio		Same		Turiscail	
Sukus	Aldeias	Sukus	Aldeias	Sukus	T.Aldeias	Sukus	Aldeias
Aituha	2	Bubussuso	5	Babulo	8	Aitemua	2
Dotic	3	FAtukahi	5	Betano	7	Beremana	3
Mahaquidan	5	Caicassa	4	Dai-sua	5	Fatucalo	2
Taitudac	5	Clauc	5	Grotu	3	Foholau	3
Uma berloic	4	Fahinehan	4	Holarua	13	Caimauc	5
-	-	-	-	Letefoho	7	Lessuata	4
Total	19	-	23	-	43	-	19

Data husi: Livro 3 B OJE 2021, pag 75

Tabela 2.1: Forca de Trabalho ADN, I.P Municipio Manufahi.

Forca de Trabalho ADN,I.P Municipio Manufahi/ Same								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engenheiro	2					2	
2	Administrasaun no Financas	0					0	
3	Motorista	1					1	
4	Seguransa	0					0	
Total		3					3	

Tabela 3.2 : Lista Asset ADN,I.P Municipio Manufahi.

ASET ADN,IP MUNICIPIO MANUFAHI								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1						
2	Kareta	1						
3	Desktop HP / Monitor	1						
4	Laptop HP	1						
5	Printer Cannon	1						
6	UPS	1						
7	Armario File	2						At ona
8	Armario Tau hena	3						1 at ona
9	Meja escritorio	1						
10	Meja han	1						
11	Meja TV (kiik)	1						
12	Kadeira escritorio	6						
13	Kadeira han	4						
14	Sofa	1 Set						
15	Springbed +sumasu 4+sprei 3	3 Set						
16	Jeleira	1						
17	Water Dispenser	1						At ona
18	TV + Parabola	1 Set						Parabola La funciona
19	Kipas Angin	4						
20	Kompor	1						At ona
21	Kompor Gas	1						At ona
22	Rack sepatu	3						
23	Rack Piring	1						
24	Lampu	11						

25	Water Pump Sanyo	1						
----	------------------	---	--	--	--	--	--	--

1.3. Lista Projecto

Projetu hotu neébe akumula iha lista neé bazeia ba dadus projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamiento, tabela 1.3.2 Projetu por Sector no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabela 4.3.1 :Projecto Municipio Manufahi Por Fundus Finansiamiento

NO	POSTO ADMINISTRATIVO	TOTAL FI		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	6	\$ 3,314,853.37	58.78%
2	Fatuberliu	5	\$ 6,315,903.07	68.24%
3	Same	9	\$ 3,668,138.45	71.82%
4	Turiscail	3	\$ 4,690,158.04	77.78%
	Grand Total	23	\$ 17,989,052.93	69.72%

NO	POSTO ADMINISTRATIVO	TOTAL LM Covid 19		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas			
2	Fatuberliu			
3	Same	3	\$ 383,412.81	74.40%
4	Turiscail			
	Grand Total	3	\$ 383,412.81	74.40%

NO	POSTO ADMINISTRATIVO	TOTAL LM BS		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	2	\$ 587,548.52	72.60%
2	Fatuberliu			
3	Same	2	\$ 306,911.16	64.79%
4	Turiscail	1	\$ 570,200.00	70.00%
	Grand Total	5	\$ 1,464,659.68	69.95%

NO	POSTO ADMINISTRATIVO	TOTAL LM CD		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	4	\$ 766,506.99	67.86%
2	Fatuberliu	5	\$ 1,318,810.35	47.23%
3	Same	9	\$ 737,705.12	40.36%
4	Turiscail	1	\$ 278,252.69	0.00%
Grand Total		19	\$ 3,101,275.15	46.46%

c	POSTO ADMINISTRATIVO	TOTAL TRANSFERENCIA PUBLICO		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	3	\$ 329,649.24	0.00%
2	Fatuberliu	1	\$ 194,674.39	0.00%
3	Same	11	\$ 1,062,554.76	0.00%
4	Turiscail			
Grand Total		15	\$ 1,586,878.39	0.00%

c	POSTO ADMINISTRATIVO	TOTAL PDID		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	2	\$ 309,015.17	22.66%
2	Fatuberliu			
3	Same	5	\$ 928,527.70	88.37%
4	Turiscail	1	\$ 7,530.00	69.97%
	Grand Total	8	\$ 1,245,072.87	71.95%

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM BS+CD+Covid19 + TP+PDID		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Alas	17	\$ 5,307,573.29	55.87%
2	Fatuberliu	11	\$ 7,829,387.81	63.01%
3	Same	39	\$ 7,087,250.00	59.78%
4	Turiscail	6	\$ 5,546,140.73	73.07%
	Grand Total	73	\$ 25,770,351.83	62.81%

Dadus detallu kada projetu: #Anexu

Tabela 5.3.2 : Projecto Municipio Por Sector

NO	SECTOR PROJECTO	Alas		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO	2	\$ 299,631.00	50.63%
2	Basic Road Construction			
3	EDIFICIOS PUBLICOS			
4	EDUKASAUN	3	\$ 329,649.24	0.00%
5	ELETRIFIKASAUN NASIONAL	1	\$ 1,108,760.78	78.57%
6	ESTRADAS	6	\$ 2,354,740.57	51.55%
7	ESTRADAS E PONTES			
8	FLOOD CONTROL	2	\$ 309,015.17	22.66%
9	JUVENTUDE NO DESPORTU			
10	MANUTENSAUN NO REHABILITASAUN	3	\$ 905,776.53	72.70%
11	PONTES			
12	SAUDE			
13	SEGURANCA NO DEFESA			
14	SOLIDARIEDADE E SOCIAL			
15	TURISMO			
	Grand Total	17	\$ 5,307,573.29	55.87%

NO	SECTOR PROJECTO	Fatuberliu		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO			
2	Basic Road Construction			
3	EDIFICIOS PUBLICOS			
4	EDUKASAUN	1	\$ 194,674.39	0.00%
5	ELETRIFIKASAUN NASIONAL	1	\$ 806,642.49	81.00%
6	ESTRADAS	8	\$ 6,224,968.98	59.17%
7	ESTRADAS E PONTES	1	\$ 603,101.95	98.91%
8	FLOOD CONTROL			
9	JUVENTUDE NO DESPORTU			
10	MANUTENSAUN NO REHABILITASAUN			
11	PONTES			
12	SAUDE			
13	SEGURANCA NO DEFESA			
14	SOLIDARIEDADE E SOCIAL			
15	TURISMO			
	Grand Total	11	\$ 7,829,387.81	63.01%

NO	SECTOR PROJECTO	Same		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO	2	\$ 137,426.79	20.08%
2	Basic Road Construction	1	\$ 131,893.81	0.00%
3	EDIFICIOS PUBLICOS	3	\$ 610,160.22	66.51%
4	EDUKASAUN	11	\$ 1,062,554.76	0.00%
5	ELETRIFIKASAUN NASIONAL	4	\$ 2,031,238.67	72.85%
6	ESTRADAS	5	\$ 633,432.36	67.85%
7	ESTRADAS E PONTES			
8	FLOOD CONTROL			
9	JUVENTUDE NO DESPORTU	1	\$ 23,697.55	89.15%
10	MANUTENSAUN NO REHABILITASAUN	5	\$ 1,153,984.05	79.58%
11	PONTES	1	\$ 328,755.98	46.54%
12	SAUDE	2	\$ 312,000.61	88.75%
13	SEGURANCA NO DEFESA	1	\$ 76,149.37	0.00%
14	SOLIDARIEDADE E SOCIAL	2	\$ 536,957.37	97.65%
15	TURISMO	1	\$ 48,998.46	0.00%
	Grand Total	39	\$ 7,087,250.00	59.78%

NO	SECTOR PROJECTO	Turiscail		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGE M EXECUSAUN (%)
1	AGUA E SANEAMENTO	1	\$ 7,530.00	69.97%
2	Basic Road Construction			
3	EDIFICIOS PUBLICOS			
4	EDUKASAUN			
5	ELETRIFIKASAUN NASIONAL			
6	ESTRADAS	2	\$ 3,983,240.53	78.01%
7	ESTRADAS E PONTES			
8	FLOOD CONTROL			
9	JUVENTUDE NO DESPORTU			
10	MANUTENSAUN NO REHABILITASAUN	3	\$ 1,555,370.20	60.43%
11	PONTES			
12	SAUDE			
13	SEGURANCA NO DEFESA			
14	SOLIDARIEDADE E SOCIAL			
15	TURISMO			
	Grand Total	6	\$ 5,546,140.73	73.07%

NO	SECTOR PROJECTO	TOTAL MUNICIPIO MANUFAHI		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO	5	\$ 444,587.79	41.52%
2	Basic Road Construction	1	\$ 131,893.81	0.00%
3	EDIFICIOS PUBLICOS	3	\$ 610,160.22	66.51%
4	EDUKASAUN	15	\$ 1,586,878.39	0.00%
5	ELETRIFIKASAUN NASIONAL	6	\$ 3,946,641.94	76.12%
6	ESTRADAS	21	\$ 13,196,382.44	63.91%
7	ESTRADAS E PONTES	1	\$ 603,101.95	98.91%
8	FLOOD CONTROL	2	\$ 309,015.17	22.66%
9	JUVENTUDE NO DESPORTU	1	\$ 23,697.55	89.15%
10	MANUTENSAUN NO REHABILITASAUN	11	\$ 3,615,130.78	69.62%
11	PONTES	1	\$ 328,755.98	46.54%
12	SAUDE	2	\$ 312,000.61	88.75%
13	SEGURANCA NO DEFESA	1	\$ 76,149.37	0.00%
14	SOLIDARIEDADE E SOCIAL	2	\$ 536,957.37	97.65%
15	TURISMO	1	\$ 48,998.46	0.00%
	Grand Total	73	\$ 25,770,351.83	62.81%

Dadus detallu kada projetu: #Anexu A

Tabela 6.3.3 : Projecto Municipio Por Ministerio

NO	DONO DO PROJECTO	Alas		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P			
2	ESTATAL			
3	MINISTERIO DA SAUDE			
4	MINISTERIO DAS OBRAS PUBLICAS	14	\$ 4,977,924.05	59.57%
5	MINISTERIO DO INTERIOR			
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	\$ 329,649.24	0.00%
7	MINISTERIO SAUDE			
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
Grand Total		17	\$ 5,307,573.29	55.87%

NO	DONO DO PROJECTO	Fatuberliu		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P			
2	ESTATAL			
3	MINISTERIO DA SAUDE			
4	MINISTERIO DAS OBRAS PUBLICAS	10	\$ 7,634,713.42	64.61%
5	MINISTERIO DO INTERIOR			
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 194,674.39	0.00%
7	MINISTERIO SAUDE			
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
Grand Total		11	\$ 7,829,387.81	63.01%

NO	DONO DO PROJECTO	Same		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P	1	\$ 292,653.74	0.00%
2	ESTATAL	4	\$ 568,413.14	97.02%
3	MINISTERIO DA SAUDE	2	\$ 312,000.61	88.75%
4	MINISTERIO DAS OBRAS PUBLICAS	16	\$ 4,116,319.70	72.94%
5	MINISTERIO DO INTERIOR	2	\$ 436,263.93	61.68%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	11	\$ 1,062,554.76	0.00%
7	MINISTERIO SAUDE	1	\$ 71,412.20	11.67%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	\$ 178,633.46	71.88%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 48,998.46	0.00%
Grand Total		39	\$ 7,087,250.00	59.78%

NO	DONO DO PROJECTO	Turiscas		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P			
2	ESTATAL	1	\$ 7,530.00	69.97%
3	MINISTERIO DA SAUDE			
4	MINISTERIO DAS OBRAS PUBLICAS	5	\$ 5,538,610.73	73.07%
5	MINISTERIO DO INTERIOR			
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
7	MINISTERIO SAUDE			
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
	Grand Total	6	\$ 5,546,140.73	73.07%

NO	DONO DO PROJECTO	TOTAL MUNICIPIO MANUFAHI		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	ELECTRICIDADE DE TIMOR LESTE, E.P	1	\$ 292,653.74	0.00%
2	ESTATAL	5	\$ 575,943.14	96.67%
3	MINISTERIO DA SAUDE	2	\$ 312,000.61	88.75%
4	MINISTERIO DAS OBRAS PUBLICAS	45	\$ 22,267,567.90	67.13%
5	MINISTERIO DO INTERIOR	2	\$ 436,263.93	61.68%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	15	\$ 1,586,878.39	0.00%
7	MINISTERIO SAUDE	1	\$ 71,412.20	11.67%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	\$ 178,633.46	71.88%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 48,998.46	0.00%
	Grand Total	73	\$ 25,770,351.83	62.81%

Dadus detallu kada projetu: #Anexu A

II. PROGRESU FISIKU

2.1 Progreso Fisiku Kada Fulan

Progresu Fisiku kada fulan ne'e hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu katak progresu actual fulan ida ne'e siknifika porsentagen servisu ne'ebe atinje deit iha fulan ne'e nia laran, montante actual fulan ida ne'e bazeia ba orsamentu ne'ebe hetan husi progresu fulan ida ne'e nia rasik no ikus porsentagen actual fulan ida ne'e hatudu progresu fisiku komulativu ne'ebe akumula husi porsento anterior no fulan ida ne'e nian, kompletu ba detallu bele haree iha #Anexu B, detallu ba Back-Up #Anexu C no Fotografia bele hare #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

Obstaklu sira ne'ebé ma ami hasoru iha munisipiu Manufahi durante hala'o monitorizasaun no inspesaun projetu sira mak hanesan:

1. Transporte ida de'it difikulta ami atu hala'o inspesaun banhira iha pedidu pagamentu tamba seksaun Ponte Estrada mos presija halo monitorizasaun hodi atinji kuantidade de monitorizasaun
2. Linha internet fraku tamba ne'e maske ami atualiza progresu projetu kada loron mos unidade baze de dados nafatin la hetan dados hafoin semana rua ba leten. Ho difikulade ne'e unidade seksaun halo ami atraplla. Tamba ne'e maske ami iha munisipiu atualiza bebeik maibe laiha efisiensia no bele hamosu deskonfia katak engenheiru munisipiu la halo atualizasaun progresu projetu sira
3. Iha parte **instrusaun serbisu**, munisipiu halo "*tribe*" so pra aumenta volume serbsu de'it maibe fungsaun ida de'it.
4. Bainhira iha pedidu pagamentu, susar mai ami atu atinji kuantidade inspesaun
5. Susar ba seksaun Edifício Público, Agua e Saneamento (EPAS) atu atualiza progresu fiziku kada semana bainhira iha pedidu pagamentu tamba preukupa ho inspesaun pagamentu no prepara rekomendasaun pagamentu
6. Susar ba enjineru munisipiu atu atualiza progresu serbsu eletrisidade tamba responsabilidade enjineru munisipiu de'it mos susar atu finaliza

➤ Obstacle parte Eletricidade

1. Durante halo monitorizasaun ba projeto neébe mak mensiona iha lista projektu Eng. M & E, ADN – I.P, la hasoru kontraktor sira tamba televomel fora da area hotu.
2. Eng. M & E, ADN – I.P, nunka hasoru tekniku husi kompania no parte kompania sempre delega tekniku neébe ba hein iha terenu, maibe tekniku neé rasik laiha konesimentu klean ho orbra refere.
3. Seksaun M & E, AND – I.P, la bele kontrola projeto ho maximu tamba Eng. M & E ida hodi
kontrola Projeto Linha Electricidade ho Edifisio Publik Iha Municipio Ha'at (4).
4. Projeto eletricidade barak maka espasu ba lina laiha ona, hodi kompanha sira mos la halo servisu kontinuasaun.
5. Motorista menus difikulta ami nia servisu.

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Buka solusaun lalais ba projeto sira ne'ebé abandona ho projeto na'in se la'e engenheiru munisipiu ninia relatoriu laiha rejultadu no projeto sira sei continua abandona
2. Aumenta transporte nune'e bele facilita hala'o inspesaun
3. Diminui tiha parte instrusaun serbisu tamba enjinheru munisipiu halo "*tribe*" hodi aumenta volume serbsu maibe fungsaun ida de'it.

➤ Recomendação parte Eletricidade

1. Husu ba parte ITC, ADN – I.P bele kria Folder Sistem ba Seksaun M & E, ADN – I.P.
2. Husu atu aumenta tan rekursu iha Seksaun M & E, ADN – I.P

Note: Asinatura husi Eng Municipio Manufahi

Força de Trabalho ADN, I.P Municipio Manufahi						
No	Deskrisaun	Identidade				
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	Asinatura
1	Engineiro	Fidelis Mardiano da Costa		Enjineiru EPAS		
		Romulo J.M Henrique		Enjineiru ITI		
		Majorico Cele Tali		Enjineiru ITI		
		Johanes Hornay	011	Enjineiro VEBD		

		Silvino D. R. R. Soares		Enjineiru METIC		
2	Motorista	Silveiro da Costa		Motorista		

LISTA GERAL
ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Alas	Manufahi	Samboio Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	\$ 1,108,760.78	Feb. 10, 2013	100.00%	78.57%	\$ 871,110.32	\$ 237,650.46	PHO
2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consortorio Nacional Manufahi Lda	SSS/148/MOPTC-2017	\$ 553,599.46	Sept. 14, 2017	8.61%	7.75%	\$ 42,899.98	\$ 510,699.48	ON-GOING
3	Emergency new construction of gabion box protection random fill in area Lacro, Baria Laran, Uma Berloik, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consortorio 1912 MF Lda	SSS/279/MOPTC-2016	\$ 440,564.46	Oct. 27, 2016	100.00%	78.96%	\$ 347,876.05	\$ 92,688.41	ON-GOING
4	Rural Roads Routine Maintenance Dootic Weberek, Chainage 0+000 - 6+300, Dootic Wekakaoan, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Samboio Unip,Lda	MPW-RFQ-190017	\$ 71,803.67	Jan. 8, 2019	68.44%	61.60%	\$ 44,230.62	\$ 27,573.05	ON-GOING
6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	\$ 269,482.11	Oct. 7, 2019	86.82%	14.96%	\$ 40,316.95	\$ 229,165.16	ON-GOING
7	Kontinuasaun Kanalizasaun Kanu Transmisaun no Distribuisaun Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Alas	Manufahi	Tane Unipessoal Lda	MOP - W - 190210	\$ 187,239.00	Nov. 21, 2019	30.00%	27.00%	\$ 50,554.31	\$ 136,684.69	ON-GOING
8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Alas	Manufahi	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	\$ 523,300.00	April 21, 2021	68.58%	68.58%	\$ 358,882.28	\$ 164,417.72	ON-GOING
9	Construction and Installation water Gravitation System in Mahaquidam Umaberloik Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Verescar Unip. Lda	SSS/289/MOPTC-2016	\$ 499,455.17	Nov. 8, 2016	89.96%	78.70%	\$ 393,055.29	\$ 106,399.88	ON-GOING
11	Rehabilitasaun Estrada Tekunu-Feriksare 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Aplayana unip. Lda	RT/062/MOPTC-2016	\$ 334,517.69	Aug. 3, 2016	80.00%	66.13%	\$ 221,221.39	\$ 113,296.30	ON-GOING
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Alas	Manufahi	Consortorio Unimafa Lda	SSS/150/MOPTC-2017	\$ 377,955.81	Sept. 14, 2017	21.28%	19.15%	\$ 72,370.68	\$ 305,585.13	ON-GOING
13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaoan Chainage 0+000 - 8+600 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Alas	Manufahi	Werenek Unipessoal Lda	MPW-W-210093	\$ 59,011.32	July 23, 2021	58.58%	26.92%	\$ 15,884.54	\$ 415,568.18	ON-GOING
14	Konstrusaun ka rehabilitasaun ba EBC Mahaquidan	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBC MAHAQUIDAN	Kontratu ho Grupo Comunitariu	\$ 111,814.16	Oct. 15, 2021	22.38%	0.00%		\$ 415,568.18	ON-GOING
15	Konstrusaun ka rehabilitasaun ba EBF Bercoban	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF BERCOBAN	Kontratu ho Grupo Comunitariu	\$ 101,086.58	Oct. 15, 2022	20.44%	0.00%		\$ 415,568.18	ON-GOING
16	Konstrusaun ka rehabilitasaun ba EBF Manus	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF MANUS	Kontratu ho Grupo Comunitariu	\$ 116,748.50	Oct. 15, 2023	19.30%	0.00%		\$ 415,568.18	ON-GOING
17	Konstrusaun Bronjong & Normalizasaun Mota Clere Weberek, Dotik - Alas Manufahi	MINISTERIO DAS OBRAS PUBLICAS	PDIM	FLOOD CONTROL	Alas	Manufahi	Sarifasalma Hahinarianledo Unip. Lda	17/PDIM/M-MF/IX/2019	\$ 39,533.06		75.13%	75.13%	29,700.41	\$ 415,568.18	ON-GOING
18	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	\$ 451,569.10	Sept. 14, 2017	8.86%	7.97%	\$ 36,000.92	\$ 415,568.18	ON-GOING
21	New Construction of Sukaer Oan River cyclop Concrete Reteining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatuberliu	Manufahi	Consortorio National Samdil, Lda (CNS)	SSS/102/MOPTC-2017	\$ 3,985,902.37	Sept. 7, 2017	87.83%	73.30%	\$ 2,921,736.56	\$ 1,064,165.81	ON-GOING
22	R4D Rural Road Routine Maintenance, Tukununu Feriksare Chainage 0+000-6+350 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	MARDIROMIG VIQSAM, UNIPESOAL LDA	MPW- W - 210096	\$ 27,105.00	July 23, 2021	24.97%	11.92%	\$ 3,230.33	\$ 23,874.67	ON-GOING
23	R4d Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Loskabubu	MPW-W-210099	\$ 337,115.79	July 23, 2021	99.65%	52.82%	\$ 178,069.50	\$ 159,046.29	ON-GOING
24	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Leo-Hilin Unipessoal Lda	MPW-W-210095	\$ 124,043.34	July 23, 2021	71.82%	29.63%	\$ 36,752.99	\$ 87,290.35	ON-GOING
25	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainag	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Alifa Pereira	MPW-W-210097	\$ 421,729.47	July 23, 2021	93.38%	23.79%	\$ 100,324.33	\$ 321,405.14	ON-GOING
26	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Fatuberliu	Manufahi	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	\$ 408,816.75	July 23, 2021	98.19%	74.50%	304,556.74	\$ 104,260.01	ON-GOING


LISTA GERAL
ANEXO A

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
27	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Fatuberliu	Manufahi	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		\$ 194,674.39		15.06%	0.00%	\$ -	\$ 194,674.39	ON-GOING
28	Emergency proposed for the new construction of bridge with retaining wall in Area Wee Kakau Oan I	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	Fatuberliu	Manufahi	Consortorio Alkafer .Lda	SSS/211/MOPTC-2016	\$ 603,101.95		98.91%	98.91%	\$ 596,530.15	\$ 6,571.80	ON-GOING
30	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dediva Electrical Unip, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385	\$ 921,673.84	July 6, 2016	96.00%	86.81%	\$ 800,071.34	\$ 121,602.50	ON-GOING
31	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430	\$ 728,245.26	Sept. 1, 2016	92.00%	82.38%	\$ 599,930.07	\$ 128,315.19	ON-GOING
32	Konstrusaun kanalizasaun bee mo sha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Same	Manufahi	Haksolok Java Motor Unip Lda	MOP - W - 190160	\$ 129,668.57	Dec. 1, 2019	18.50%	16.65%	\$ 21,593.56	\$ 108,075.01	ON-GOING
33	Nova fornecimento água do Bairo PNTL Manufahi	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	Same	Manufahi	Tom's Building Uipessoal Lda	SSS/053/MI-2017	\$ 76,149.37	Nov. 29, 2019	24.55%	0.00%	\$ -	\$ 76,149.37	ON-GOING
34	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Same	Manufahi	Consortorio Cablaki Oan Lda	SSS/270/MOPTC-2016	\$ 363,040.25	Oct. 19, 2016	100.00%	95.38%	\$ 346,267.25	\$ 16,773.00	ON-GOING
35	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Same	Manufahi	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	\$ 328,755.98	July 26, 2016	76.00%	46.54%	\$ 153,014.54	\$ 175,741.44	ON-GOING
36	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	El Const Unip. Lda	NCB/063/MOPTC-2016	\$ 700,656.46	Aug. 4, 2016	98.93%	89.16%	\$ 624,740.20	\$ 75,916.26	ON-GOING
38	Road Maintenance Section Same Urban Roads Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Renova Unip Lda	MPW - W - 190215	\$ 87,929.19	Dec. 2, 2019	71.88%	64.69%	\$ 56,880.06	\$ 31,049.13	ON-GOING
40	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Alifa Pereira	MPW -RFQ 190019	\$ 59,446.75	Aug. 1, 2019	90.13%	81.12%	\$ 48,222.09	\$ 11,224.66	ON-GOING
41	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Leo - Dok	MPWTC-CD-170002	\$ 48,340.53	Jan. 8, 2019	86.31%	77.68%	\$ 37,549.81	\$ 10,790.72	ON-GOING
49	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Haut-Dairam Unipessoal Lda	MPW-W210092	\$ 46,754.63	July 23, 2021	44.37%	35.41%	\$ 16,554.11	\$ 30,200.52	ON-GOING
50	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Riabile Unipessoal Lda	MPW-W-210091	\$ 52,112.72	July 23, 2021	21.47%	19.39%	\$ 10,105.69	\$ 42,007.03	ON-GOING
51	New Construction of Laboratory Building" Luak, Municipio Manufahi	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Same	Manufahi	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	\$ 71,412.20	Aug. 17, 2021	97.85%	11.67%	\$ 8,336.40	\$ 63,075.80	ON-GOING
52	Para A Construccao De Jardim De Herois De Manufahi (New Construction Of Campas, Gate And Leveling)	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	TURISMO	Same	Manufahi	My friend Constr. Unip. Lda	RFQ No. 23/MACLN/DNAL/VI/2021	\$ 48,998.46	Sept. 1, 2021	76.12%	0.00%		\$ 48,998.46	ON-GOING
53	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Same	Manufahi	Tutur Bodik Tane Lisuk, Unip.Lda	MPW - W -210094	\$ 83,595.57	July 23, 2021	71.35%	0.00%		\$ 83,595.57	ON-GOING
54	Konstrusaun ka rehabilitasaun ba EBF Tefo	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF TEFO	Kontratu ho Grupo Comunitariu	\$ 99,986.68		15.55%	0.00%			ON-GOING
55	Konstrusaun ka rehabilitasaun ba EBC Diligencia	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC DILIGENCIA	Kontratu ho Grupo Comunitariu	\$ 110,951.20		24.55%	0.00%			ON-GOING
56	Konstrusaun ka rehabilitasaun ba EPE Turon	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE TURON	Kontratu ho Grupo Comunitariu	\$ 83,083.31		27.89%	0.00%			ON-GOING
57	Konstrusaun ka rehabilitasaun ba EPE Domingos Savio Grotu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE DOMINGOS SAVIO	Kontratu ho Grupo Comunitariu	\$ 85,513.28		21.79%	0.00%			ON-GOING
58	Konstrusaun ka rehabilitasaun ba EBF Silihasan	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF SILIHASAN	Kontratu ho Grupo Comunitariu	\$ 111,801.61		28.18%	0.00%			ON-GOING

**LISTA GERAL
ANEXO A**

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	OBS
59	Konstrusaun ka rehabilitasaun ba EBF hatsana udo/Dai-sua Lama	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF HATSANA UDO / DAI-SUA LAMA	Kontratu ho Grupo Comunitariu	\$ 101,427.27		17.32%	0.00%			ON-GOING
60	Konstrusaun ka rehabilitasaun ba EBF Blaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF BLARO	Kontratu ho Grupo Comunitariu	\$ 113,831.28		16.82%	0.00%			ON-GOING
61	Konstrusaun ka rehabilitasaun ba EBF Rotuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF ROTUTO	Kontratu ho Grupo Comunitariu	\$ 71,892.87		22.28%	0.00%			ON-GOING
62	Konstrusaun ka rehabilitasaun ba EBC Fatuco	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC FATUCO	Kontratu ho Grupo Comunitariu	\$ 10,986.63		25.99%	0.00%			ON-GOING
63	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	\$ 140,614.24		25.93%	0.00%			ON-GOING
64	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Same	Manufahi	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	\$ 132,466.39		19.25%	0.00%			ON-GOING
65	New Construction Building for Central Electrical in Luak Manufahi, Ministry of Health Timor Leste	MINISTERIO DA SAUDE	Fundo Covid-19	SAUDE	Same	Manufahi	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-22-006	\$ 18,335.73		82.00%	0.00%			ON-GOING
66	For Road Maintanance Section Jct Aituto-Same-Betano 23Km(A04)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Basic Road Construction	Same	Manufahi	Bemos I Construction Unip. Lda	MPW-W-220007	\$ 131,893.81		77.71%	0.00%			ON-GOING
67	New Construction of Tower protection Wall No 92 Section Betano -Viqueque Manufahi Municipality	ELETRICIDADE DE TIMOR LESTE, E.P	FI	ELETRIFIKASAUN NASIONAL	Same	Manufahi	My friend Constr. Unip. Lda	NCB/028/MOP-2020	\$ 292,653.74		0.00%	0.00%			ON-GOING
68	Open New Road Turiscai - Mota Belihun Maubere, Turiscai - Liquideoe Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Turiscas	Manufahi	Aldepo Murak Unip,Lda	SSS/250/MOPTC-2016	\$ 3,413,040.53	Sept. 4, 2017	93.90%	79.35%	\$ 2,708,287.08	\$ 704,753.45	ON-GOING
69	Const. MCK (Saude) Orana	ESTATAL	PDIM	AGUA E SANEAMENTO	turiscas	Manufahi	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	\$ 7,530.00	May 23, 2019	75.00%	69.97%	\$ 5,268.79	\$ 2,261.21	ON-GOING
70	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railaco, Sanfuk, Tutu Luro - Same Fahi Nehan (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	turiscas	Manufahi	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	\$ 570,200.00	March 25, 2020	70.00%	70.00%	\$ 399,140.00	\$ 171,060.00	ON-GOING
71	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Terra Livre Unip. Lda	SSS/299/MOPTC-2016	\$ 478,217.51	Nov. 23, 2016	90.44%	79.59%	\$ 380,612.95	\$ 97,604.56	PHO
72	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 4 : Turiscas to Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Wan Husin Associates SDN. BHD. Jv Consultant & Engineering Intercontinental Unip. Lda	RT/031/MOP-2019	\$ 798,900.00	March 25, 2020	70.00%	70.00%	\$ 559,230.00	\$ 239,670.00	ON-GOING
73	Spot Improvement Baltade - Orluli, Chainage 0+000 - 2+500 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Daloveya Unipessoal Lda	MPW-W-220001	278,252.69		0.00%	0.00%	\$ -	\$ 278,252.69	ON-GOING

Inspected by :



Eng Romulo J.M Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio Manufahi A D N I P


Eng Majorico Cele Tali

Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio

Verified by :



Eng. Remigio da C. S. dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N I P

Inspected by :



Eng. Fidelis Meridiano da Costa
Engenheiro Edificio Public, Agua e Saneamento A D N I P

Verified by :



Arch. Francisco Xavier de D Jeronimo
Engenheiro Senior ba Edificio Public no Agua e

Inspected by :



Eng Silvano D. R. R. Soares
Enjineiru M & E , A D N I P

Verified by :



Eng Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N I P

Certified by :



Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao qualidade ADN.I.P



**LISTA GERAL ANEXO B
PROGRES JULHO 2022**

NU.	No District	NARAN PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 29 July 2022			OBSERVASAUN
										% Up to June prog	July Progress	% Up to July prog	
1	1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	ELETRIFIKASAUN NASIONAL	Alas	Manufahi	Samboio Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	\$ 1,108,760.78	Feb. 10, 2013	100.00%		100.00%	ON-GOING
2	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oan 2	ESTRADAS	Alas	Manufahi	Consortio Nacional Manufahi Lda	SSS/148/MOPTC-2017	\$ 553,599.46	Sept. 14, 2017	8.61%		8.61%	ON-GOING
3	3	Emergency new construction of gabion box protection random fill in area Lacro, Baria Laran, Uma Berloik, Alas	ESTRADAS	Alas	Manufahi	Consortio 1912 MF Lda	SSS/279/MOPTC-2016	\$ 440,564.46	Oct. 27, 2016	100.00%		100.00%	ON-GOING
4	4	Rural Roads Routine Maintenance Dootic Weberek, Chainage 0+000 - 6+300, Dootic Wekakaoan, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Samboio Unip,Lda	MPW-RFQ-190017	\$ 71,803.67	Jan. 8, 2019	68.44%		68.44%	ON-GOING
5	5	Prefurasaun Be'e mos iha Suku Uma Berloik, Aldeia Besusu	AGUA E SANEAMENTO	Alas	Manufahi	Buka Fini	MPWTC-NCB-170008	\$ 112,392.00	Aug. 16, 2017	100.00%		100.00%	ON-GOING
6	6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	FLOOD CONTROL	Alas	Manufahi	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	\$ 269,482.11	Oct. 7, 2019	86.82%		86.82%	ON-GOING
7	7	Kontinuasaun Kanalizasaun Kanu Transmisaun no Distribuisaun Hosi Bomba Uma Berloik ba to Dotic, Posto Administrativo Alas, Municipio Manufahi/ 162	AGUA E SANEAMENTO	Alas	Manufahi	Tane Unipessoal Lda	MOP - W - 190210	\$ 187,239.00	Nov. 21, 2019	30.00%		30.00%	ON-GOING
8	8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedauberek	ESTRADAS	Alas	Manufahi	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	\$ 523,300.00	April 21, 2021	68.58%		68.58%	ON-GOING
9	9	Construction and Installation water Gravitation System in Mahaquidan Umberloic Manufahi Municipality	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Verescar Unip. Lda	SSS/289/MOPTC-2016	\$ 499,455.17	Nov. 8, 2016	89.96%		89.96%	ON-GOING
10	10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	ESTRADAS	Alas	Manufahi	My Friend Unip. Lda	MPW-W-190106	\$ 400,309.52	Nov. 5, 2020	99.66%		99.66%	ON-GOING
11	11	Rehabilitasaun Estrada Tekunu-Feriksare 2 Sta. 2+500-4+250-Municipal of Same	MANUTENSAUN NO REHABILITASAUN	Alas	Manufahi	Aplayana unip. Lda	RT/062/MOPTC-2016	\$ 334,517.69	Aug. 3, 2016	80.00%		80.00%	ON-GOING
12	12	New construction of bridge with retaining wall in area we bikas	ESTRADAS	Alas	Manufahi	Consortio Unimafa Lda	SSS/150/MOPTC-2017	\$ 377,955.81	Sept. 14, 2017	21.28%		21.28%	ON-GOING
13	13	R4D Rural Road Routine Maintenance, Dotic - Weberek Chainage 0+000 - 6+300 and Dotic - Wekakaoan Chainage 0+000 - 8+600 Municipality Manufahi	ESTRADAS	Alas	Manufahi	Wereneq Unipessoal Lda	MPW-W-210093	\$ 59,011.32	July 23, 2021	58.58%		58.58%	ON-GOING
14	14	Konstrusaun ka rehabilitasaun ba EBC Mahaquidan	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBC MAHAQUIDAN	Kontratu ho Grupo Comunitariu	\$ 111,814.16	Oct. 15, 2021	4.92%	17.46%	22.38%	
15	15	Konstrusaun ka rehabilitasaun ba EBF Bercoban	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF BERCOBAN	Kontratu ho Grupo Comunitariu	\$ 101,086.58	Oct. 15, 2022	4.80%	15.65%	20.44%	
16	16	Konstrusaun ka rehabilitasaun ba EBF Manus	EDUKASAUN	Alas	Manufahi	MEJD PKRIE EBF MANUS	Kontratu ho Grupo Comunitariu	\$ 116,748.50	Oct. 15, 2023	5.24%	14.06%	19.30%	
17	17	Konstrusaun Bronjong & Normalizasaun Mota Clere Weberek, Dotic - Alas Manufahi	FLOOD CONTROL	Alas	Manufahi	Sarifasalma Hahinarianledo Unip. Lda	17/PDIM/M-MF/IX/2019	\$ 39,533.06		75.13%		75.13%	

LISTA GERAL ANEXO B PROGRES JULHO 2022

NU.	No District	NARAN PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 29 July 2022			OBSERVASAUN
										% Up to June prog	July Progress	% Up to July prog	
18	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	ESTRADAS	Fatuberliu	Manufahi	Concorcio Fatuledu.Lda	SSS/151/MOPTC-2017	\$ 451,569.10	Sept. 14, 2017	8.86%		8.86%	ON-GOING
19	2	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Besi	ESTRADAS	Fatuberliu	Manufahi	concorcio Nacional ba Futuro	SSS/149/MOPTC-2017	\$ 468,687.16	Sept. 14, 2017	24.29%		24.29%	ON-GOING
20	3	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	ELETRIFIKASAUN NASIONAL	Fatuberliu	Manufahi	Funu Kolik Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424	\$ 806,642.49	Sept. 1, 2016	90.00%		90.00%	Abandon
21	4	New Construction of Sukaer Oan River cyclop Concrete Reteining Wall and Gabion	ESTRADAS	Fatuberliu	Manufahi	Consortio National Samdil, Lda (CNS)	SSS/102/MOPTC-2017	\$ 3,985,902.37	Sept. 7, 2017	87.83%		87.83%	ON-GOING
22	5	R4D Rural Road Routine Maintenance, Tukununu Feriksare Chainage 0+000-6+350 Manufahi Municipality	ESTRADAS	Fatuberliu	Manufahi	MARDIROMIG VIQSAM, UNIPESSOAL LDA	MPW- W - 210096	\$ 27,105.00	July 23, 2021	24.97%		24.97%	ON-GOING
23	6	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	ESTRADAS	Fatuberliu	Manufahi	Loskabubu	MPW-W-210099	\$ 337,115.79	July 23, 2021	78.81%	20.84%	99.65%	ON-GOING
24	7	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	ESTRADAS	Fatuberliu	Manufahi	Leo-Hilin Unipessoal Lda	MPW-W-210095	\$ 124,043.34	July 23, 2021	32.92%	38.90%	71.82%	ON-GOING
25	8	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	ESTRADAS	Fatuberliu	Manufahi	Alifa Pereira	MPW-W-210097	\$ 421,729.47	July 23, 2021	73.89%	19.50%	93.38%	ON-GOING
26	9	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	ESTRADAS	Fatuberliu	Manufahi	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	\$ 408,816.75	July 23, 2021	96.74%	1.45%	98.19%	ON-GOING
27	10	Konstrusaun ka rehabilitasaun ba ESTV Francisco Borja da Costa	EDUKASAUN	Fatuberliu	Manufahi	MEJD PKRIE ESTV FRACISCO BORJA DA COSTA		\$ 194,674.39		12.14%	2.93%	15.06%	ON-GOING
28	11	Emergency proposed for the new construction of bridge with retaining wall in Area Wee Kakau Oan 1	ESTRADAS E PONTES	Fatuberliu	Manufahi	Consortio Alkafer .Lda	SSS/211/MOPTC-2016	\$ 603,101.95		98.91%		98.91%	
29	1	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dhalelan,Unip.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000300	\$ 88,665.83	March 25, 2015	100.00%		100.00%	PHO
30	2	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Dediva Electrical Unip, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385	\$ 921,673.84	July 6, 2016	96.00%		96.00%	ON-GOING
31	3	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erluli, Luak, Ailok Laran Turon - Manufahi district	ELETRIFIKASAUN NASIONAL	Same	Manufahi	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430	\$ 728,245.26	Sept. 1, 2016	92.00%		92.00%	ON-GOING
32	4	Konstrusaun kanalizasaun bee mos iha selihasan suco Betano, Posto Adm Same, Municipio Manufahi /162	AGUA E SANEAMENTO	Same	Manufahi	Haksolok Java Motor Unip Lda	MOP - W - 190160	\$ 129,668.57	Dec. 1, 2019	18.50%		18.50%	ON-GOING
33	5	Nova fornecimento água do Bairro PNTL Manufahi	SEGURANCA NO DEFESA	Same	Manufahi	Tom's Building Uipessoal Lda	SSS/053/MI-2017	\$ 76,149.37	Nov. 29, 2019	24.55%		24.55%	ON-GOING
34	6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	ESTRADAS	Same	Manufahi	Consortio Cablaki Oan Lda	SSS/270/MOPTC-2016	\$ 363,040.25	Oct. 19, 2016	100.00%		100.00%	ON-GOING
35	7	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	PONTES	Same	Manufahi	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	\$ 328,755.98	July 26, 2016	76.00%		76.00%	ON-GOING
36	8	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	El Const Unip. Lda	NCB/063/MOPTC-2016	\$ 700,656.46	Aug. 4, 2016	98.93%		98.93%	PHO



**LISTA GERAL ANEXO B
PROGRES JULHO 2022**

NU.	No District	NARAN PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 29 July 2022			OBSERVASAUN
										% Up to June prog	July Progress	% Up to July prog	
37	9	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipality of Same	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Aplayana unip. Lda	RT/057/MOPTC-2016	\$ 168,297.72	Aug. 3, 2016	30.00%		30.00%	Abandon
38	10	Road Maintenance Section Same Urban Roads Municipality Manufahi	ESTRADAS	Same	Manufahi	Renova Unip Lda	MPW - W - 190215	\$ 87,929.19	Dec. 2, 2019	71.88%		71.88%	ON-GOING
39	11	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Quintas das Flores, Lda	MPW - W - 190123	\$ 177,242.59	June 10, 2019	100.00%		100.00%	FHO
40	12	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Alifa Pereira	MPW -RFQ 190019	\$ 59,446.75	Aug. 1, 2019	90.13%		90.13%	ON-GOING
41	13	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi (162)	MANUTENSAUN NO REHABILITASAUN	Same	Manufahi	Leo - Dok	MPWTC-CD-170002	\$ 48,340.53	Jan. 8, 2019	86.31%		86.31%	ON-GOING
42	14	Fencing for Construction Monument od Dom Boa Ventura	EDIFICIOS PUBLICOS	Same	Manufahi	Loskabubu	RDTL/06/GM-MTAC/IV/2016	\$ 178,633.46	June 9, 2015	79.86%		79.86%	Abandon
43	15	Konstrusaun Tangki Beé no Menara Beé ba iha Edificio Administrasaun Municipiu Manufahi	AGUA E SANEAMENTO	Same	Manufahi	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	\$ 7,758.22	April 10, 2017	85.99%		85.99%	Abandon
44	16	Konstrusaun Kuartel Bombeiros iha Same-Manufahi	EDIFICIOS PUBLICOS	Same	Manufahi	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	\$ 360,114.56	Aug. 19, 2016	83.02%	5.83%	88.85%	Abandon
45	17	Rehabilitasaun Igreja Paroquia Nossa Senhora Assuncao Same	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	\$ 438,905.72	Aug. 7, 2017	98.81%		98.81%	FHO
46	18	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	SOLIDARIEDADE E SOCIAL	Same	Manufahi	Consortio Deatle Hare ba Oin Lda	07/PDIM/M-MF/IX/2019	\$ 98,051.65	Sept. 9, 2019	92.45%		92.45%	FHO
47	19	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutor Bodik Tane Lisuk, Unip.Lda	JUVENTUDE NO DESPORTU	Same	Manufahi	Tutor Bodik Tane Lisuk, Unip.Lda	09/PDIM/M-MF/X/2019	\$ 23,697.55	Oct. 7, 2019	89.15%		89.15%	FHO
48	20	Konstrusaun Fatin isolamentu iha Municipio Manufahi, Timor Leste	SAUDE	Same	Manufahi	Daloveya	RDTL-MS-DNA-DC-20-256	\$ 293,664.88	Sept. 12, 2020	99.65%		99.65%	FHO
49	21	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	ESTRADAS	Same	Manufahi	Haut-Dairam Unipessoal Lda	MPW-W210092	\$ 46,754.63	July 23, 2021	44.37%		44.37%	ON-GOING
50	22	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	ESTRADAS	Same	Manufahi	Riabile Unipessoal Lda	MPW-W-210091	\$ 52,112.72	July 23, 2021	21.47%		21.47%	
51	23	New Construction of Laboratory ih CSI Luak,Manufahi relaciona ba covid19 at Ministry of Health, Timor Leste	EDIFICIOS PUBLICOS	Same	Manufahi	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-072	\$ 71,412.20	Aug. 17, 2021	64.31%	33.53%	97.85%	ON-GOING
52	24	PARA A CONSTRUCCAO DE JARDIM DE HEROIS DE MANUFAHI (New Construction of Campas, Gate and Leveling)	TURISMO	Same	Manufahi	My friend Constr. Unip. Lda	RFQ No. 23/MACLN/DNAL/VI/2021	\$ 48,998.46	Sept. 1, 2021	37.20%	38.92%	76.12%	ON-GOING
53	25	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	ESTRADAS	Same	Manufahi	Tutor Bodik Tane Lisuk, Unip.Lda	MPW - W -210094	\$ 83,595.57	July 23, 2021	71.35%		71.35%	ON-GOING
54	26	Konstrusaun ka rehabilitasaun ba EBF Tefo	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF TEFO	Kontratu ho Grupo Comunitariu	\$ 99,986.68		5.06%	10.49%	15.55%	



**LISTA GERAL ANEXO B
PROGRES JULHO 2022**

NU.	No District	NARAN PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 29 July 2022			OBSERVASAUN
										% Up to June prog	July Progress	% Up to July prog	
55	27	Konstrusaun ka rehabilitasaun ba EBC Diligencia	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC DILIGENCIA	Kontratu ho Grupo Comunitariu	\$ 110,951.20		22.60%	1.96%	24.55%	
56	28	Konstrusaun ka rehabilitasaun ba EPE Turon	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE TURON	Kontratu ho Grupo Comunitariu	\$ 83,083.31		27.41%	0.48%	27.89%	
57	29	Konstrusaun ka rehabilitasaun ba EPE Domingos Savio Grotu	EDUKASAUN	Same	Manufahi	MEJD PKRIE EPE DOMINGOS SAVIO	Kontratu ho Grupo Comunitariu	\$ 85,513.28		15.73%	6.06%	21.79%	
58	30	Konstrusaun ka rehabilitasaun ba EBF Silihasan	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF SILIHASAN	Kontratu ho Grupo Comunitariu	\$ 111,801.61		28.18%		28.18%	
59	31	Konstrusaun ka rehabilitasaun ba EBF hatsana udo/Dai-sua Lama	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF HATSANA UDO / DAI-SUA LAMA	Kontratu ho Grupo Comunitariu	\$ 101,427.27		10.38%	6.95%	17.32%	
60	32	Konstrusaun ka rehabilitasaun ba EBF Blaro	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF BLARO	Kontratu ho Grupo Comunitariu	\$ 113,831.28		5.99%	10.83%	16.82%	
61	33	Konstrusaun ka rehabilitasaun ba EBF Rotuto	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBF ROTUTO	Kontratu ho Grupo Comunitariu	\$ 71,892.87		18.58%	3.69%	22.28%	
62	34	Konstrusaun ka rehabilitasaun ba EBC Fatuco	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC FATUCO	Kontratu ho Grupo Comunitariu	\$ 10,986.63		25.99%		25.99%	
63	35	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	EDUKASAUN	Same	Manufahi	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	\$ 140,614.24		22.35%	3.58%	25.93%	
64	36	Konstrusaun ka rehabilitasaun ba ESTV Halibur Betano	EDUKASAUN	Same	Manufahi	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	\$ 132,466.39		18.02%	1.22%	19.25%	
65	37	New Construction Building for Central Electrical in Luak Manufahi, Ministry of Health Timor Leste	SAUDE	Same	Manufahi	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-22-006	\$ 18,335.73		0.00%	82.00%	82.00%	
66	38	For Road Maintanance Section Jct Aituto-Same-Betano 23Km(A04)	Basic Road Construction	Same	Manufahi	Bemos I Construction Unip. Lda	MPW-W-220007	\$ 131,893.81		0.00%	77.71%	77.71%	
67	39	New Construction of Tower protection Wall No 92 Section Betano -Viqueque Manufahi Municipality		Same	Manufahi	My friend Constr. Unip. Lda	NCB/028/MOP-2020	\$ 292,653.74		0.00%		0.00%	foun
68	1	Open New Road Turiscail - Mota Belihun Maubere, Turiscail - Liquidoe Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	ESTRADAS	Turiscail	Manufahi	Aldepo Murak Unip,Lda	SSS/250/MOPTC-2016	\$ 3,413,040.53	Sept. 4, 2017	93.90%		93.90%	ON-GOING



LISTA GERAL ANEXO B
PROGRES JULHO 2022

NU.	No District	NARAN PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Friday, 29 July 2022			OBSERVASAUN
										% Up to June prog	July Progress	% Up to July prog	
69	2	Const. MCK (Saude) Orana	AGUA E SANEAMENTO	turiscas	Manufahi	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	\$ 7,530.00	May 23, 2019	75.00%		75.00%	Haktuir husi Administrator M. Manufahi katak hakrak atu taka projetu refre tamba kompanhia lakohi kopera hodi hadia defetu sira nee'be iha
70	3	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railaco, Sanfuk, Tutu Luro - Same Fahi Nehan (162)	ESTRADAS	turiscas	Manufahi	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	\$ 570,200.00	March 25, 2020	70.00%		70.00%	ON-GOING
71	4	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Terra Livre Unip. Lda	SSS/299/MOPTC-2016	\$ 478,217.51	Nov. 23, 2016	90.44%		90.44%	PHO
72	5	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 4 : Turiscas to Alas	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Wan Husin Associates SDN. BHD. Jv Consultant & Engineering Intercontinental Unip. Lda	0	\$ 798,900.00	43915	70.00%		70.00%	ON-GOING
73	6	Spot Improvement Baltade - Orluli, Chainage 0+000 - 2+500 Manufahi Municipality	MANUTENSAUN NO REHABILITASAUN	turiscas	Manufahi	Daloveya Unipessoal Lda	MPW-W-220001	\$ 278,252.69					

Responsabilidade EPAS

Inspected by :

Eng Romulo J.M Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio Manufahi A D N IP

Eng Majorico Cele Tali
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun Munisipio Manufahi A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Inspected by :

Eng Fidelis Mardiano da Costa
Engenheiro Edificio Public, Agua e Saneamento A D N IP

Verified by :

Arch. Francisco Xavier de D. Jeronimo Engenheiro Senior ba Edificio Public no Agua e Saneamento A D N IP

Inspected by :

Eng Silvino D. R. R. Soares
Enjineiru M & E , A D N IP

Verified by :

Eng Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade ADN.I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (FTB 10)

Back-up Data

Naran Projeto : Nova Construção ESTV Francisco Borja da Costa Fatuberlliu
No. kontratu :

Data Inspesaun : 19/08/2022

Fatin Inspesaun : Fatucahi, Fatuberliu - Manufahi

Koordinadas :

Start Point : Long , Latetude :

End Point : Long : - , Latetude :


Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Armasaun armadura viga kakuluk (ringbalk)

ba Eskritoriu



Betonazen viga kakuluk (ringbalk) ba

laboratory





ANEXU C2 (# FTB 10)

Projeto : Nova Construção Edifício Escritório + Laboratório Geral de Ciência ESTV Francisco
Borja da Costa Fatucahi
Owner : MEJD
Localization : Fatucahi, Fatuberliu Manufahi

MAIN SUMMARY			Up to 27062022 - progres		July Progress		Up to 27072022 - Progres	
NO	ITEM SERVIÇO	A DN, I.P. VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,925.00	\$ 2,817.50	1.45%	\$ (1,205.00)	-0.62%	\$ 1,612.50	0.83%
II	TEACHER OFFICE	\$ 79,969.81	\$ 12,379.45	6.36%	\$ 4,492.40	2.31%	\$ 16,871.85	8.67%
III	LABORATORY GERAL E CIENCIA	\$ 81,026.74	\$ 10,000.83	4.33%	\$ 2,408.37	1.24%	\$ 12,409.20	5.57%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 20,912.84						
A	CONSTRUCTION COST	\$ 185,834.39	\$ 25,197.79	12.14%	\$ 5,695.77	2.93%	\$ 30,893.55	15.06%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 194,674.39	\$ 25,197.79	12.14%	\$ 5,695.77	2.93%	\$ 30,893.55	15.06%

Verified by:
Date, / / 2022


Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisca Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVO ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 14)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC MAHAQUIDAN

No. kontratu :

Data Inspesaun : 26/07/2022

Fatin Inspesaun : Mahaquidan, Alas – Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Armasaun armadura ba viga (ringballk)

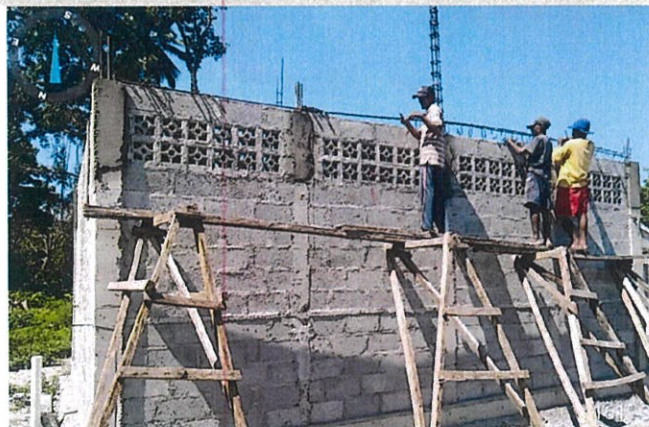



#ANEXU C2 (ALS 14)

Projeto : Nova Construção Escola Básica Central Mahaquidan
Owner : MEJD
Localization : Mahaquidan, Alas Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 27/05/2022 PROGRESS		JULY PROGRESS		UP TO 29/07/2022 PROGRESS	
	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,425.00	640.00	0.57%	622.50	0.56%	1,262.50	0.01
II	CLASSROOM BUILDING CA	\$ 62,569.45	4,858.35	4.35%	12,811.45	11.46%	17,669.80	0.16
III	TOILET BUILDING TB	\$ 25,164.97			6,090.40	5.45%	6,090.40	0.05
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,814.74						
A	CONSTRUCTION COST	\$ 102,974.16	\$ 5,498.35	4.92%	\$ 19,524.35	17.46%	\$ 25,022.71	22.38%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 111,814.16	\$ 5,498.35	4.92%	\$ 19,524.35	17.46%	\$ 25,022.71	22.38%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisca Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 15)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF NERCOBAN

No. kontratu :

Data Inspesaun : 26/07/2022

Fatin Inspesaun : Bercoban Taitudak, Alas – Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Instalasaun batako





#ANEXU C2 (ALS 15)

Projeto : Nova Construção Escola Básica Filial Bercoban
Owner : MEJD
Localization : Bercoban Taitudak, Alas Manufahi

MAIN SUMMARY				ADN, I.P. RECOMMENDATION					
				UP TO 27/05/2022 PROGRESS		JULY PROGRESS		UP TO 29/07/2022 PROGRESS	
	ITEM/SERVISU	A DN VERIFIED		AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,775.00		\$ 675.00	0.67%	\$ 157.50	0.16%	\$ 832.50	0.82%
II	CLASSROOM BUILDING C	\$ 52,034.01		\$ 4,172.12	4.13%	\$ 10,336.88	10.23%	\$ 14,509.00	14.35%
III	TOILET BUILDING TB	\$ 25,446.29				\$ 5,321.97	5.26%	\$ 5,321.97	5.26%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 10,991.28							
A	CONSTRUCTION COST	\$ 92,246.58		\$ 4,847.12	4.80%	\$ 15,816.35	15.65%	\$ 20,663.47	20.44%
B	CONTINGENCY	\$ 3,000.00							
C	OVERHEAD	\$ 5,840.00							
D	GRAND TOTAL	\$ 101,086.58		\$ 4,847.12	4.80%	\$ 15,816.35	15.65%	\$ 20,663.47	20.44%

Verified by:
Date, / / 2022


Fidelis Mardiana da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVC ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (ALS 16)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF MANUS

No. kontratu :

Data Inspesaun : 26/07/2022

Fatin Inspesaun : Manus Taitudak, Alas – Manufahi

Koordinadas :

Start Point : Long : , Latetude:

End Point : Long : , Latetude:

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Asesu dalan ba lokalizasaun projetu kotu



Remark: Eng Lopes, Nova Contrução EBF Manus
26 Jul 2022 11:15:46





#ANEXU C2 (ALS 16)


Projeto : Nova Construção Escola Bazica Filial Manus
Owner : MEJD
Localization : Manos Taitudak, Alas Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
	ITEM SERVIÇO	A DN VERIFIED	UP TO 27/05/2022 PROGRESS		JULY PROGRESS		UP TO 29/07/2022 PROGRESS	
			AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 4,175.00	\$ 895.00	0.77%	\$ 480.00	0.41%	\$ 1,375.00	1.18%
III	CLASSROOM BUILDING CA	\$ 65,117.90	\$ 5,516.80	3.20%	\$ 12,504.25	10.71%	\$ 18,021.05	13.91%
IV	TOILET BUILDING TB	\$ 25,875.85	\$ 1,492.42	1.28%	\$ 3,428.52	3%	\$ 4,920.94	4.21%
V	PROVISIONAL SUM FOR SITE-WORKS	\$ 12,739.75						
A	CONSTRUCTION COST	\$ 107,908.50	\$ 7,904.21	5.24%	\$ 16,412.77	14.06%	\$ 24,316.99	19.30%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 116,748.50	\$ 7,904.21	5.24%	\$ 16,412.77	14.06%	\$ 24,316.99	19.30%

Verified by:
Date, / / 2022


Fidelis Marcelino da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UC VQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 16)

Back-up Data

Naran Projeto : Konstrusaun Kuartel Bombeiros iha Same-Manufahi

No. kontratu : 02/PDIM/M-MF/VIII/2016

Data Inspesaun : 27/07/2022

Fatin Inspesaun : Grotu, Same – Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Dadauk ne'e atividade la la'o

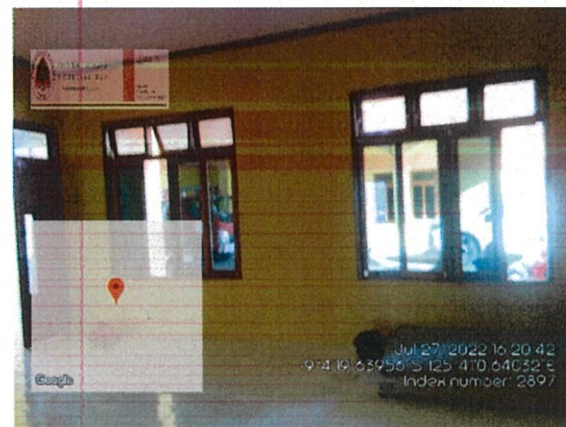



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 16)

Back-up Data

Naran Projeto : **Konstrusaun Kuartel Bombeiros iha Same-Manufahi**

No. kontratu : 02/PDIM/M-MF/VIII/2016

Data Inspesaun : 28/07/2022

Fatin Inspesaun : Grotu, Same – Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : **Eng. Fidelis Mardiano da Costa**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Fizikamente 100% nune'e dadauk ne'e prosesu
pagamentu 100% lao'o hela





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



OWNER
PROJECT TITLE
LOCATION
CONTRACTOR

: SECRETARY OF STATE FOR SECURITY
: KONSTRUSAUN KUARTEL BOMBEIROS IHA SAME-MANUFAHI
: MANUFAHI DISTRICT - TIMOR LESTE
: MEMBERS UNIP. LDA

SUMMARY

NO	ORIGINAL CONTRACT DESCRIPTION	CCO - ADN.I.P. VERIFICATION				ADN.I.P. RECOMMENDATION						
		DEDUCTION (-)		ADDITION (+)		REVISED	TO DATE - 4 TH PAYMENT		THIS BILL 5 TH PAYMENT		TO DATE - 5 TH PAYMENT	
		AMOUNT (USD)	AMOUNT (USD)	AMOUNT (USD)	AMOUNT (USD)	AMOUNT (USD)	AMOUNT (USD)	Weight (%)	AMOUNT (USD)	Weight (%)	AMOUNT (USD)	Weight (%)
I	PRELIMINARY & GENERAL	\$ 8,585.15	\$ -	\$ -	\$ 8,585.15	\$ 7,348.63		2.04%	\$ 1,236.52	0.34%	\$ 8,585.15	2.38%
II	MAIN BUILDING	\$ 193,575.41	\$ 31,131.02	\$ 13,793.76	\$ 176,794.30	\$ 175,274.24		48.67%	\$ 1,520.06	0.42%	\$ 176,794.30	49.09%
III	EXTERNAL BUILDING (TOILET AND WARE HOUSE)	\$ 32,329.66	\$ 6,340.83	\$ 1,819.27	\$ 27,893.86	\$ 27,633.42		7.67%	\$ 260.44	0.07%	\$ 27,893.86	7.75%
IV	FENCE AND GATE	\$ 36,775.63	\$ 218.29	\$ 95.00	\$ 36,652.34	\$ 33,699.78		9.36%	\$ 2,952.56	0.82%	\$ 36,652.34	10.18%
V	LANDSCAPING	\$ 10,566.93	\$ 3,380.91	\$ -	\$ 7,186.02	\$ -		0.00%	\$ 7,186.02	2.00%	\$ 7,186.02	2.00%
VI	CAR SERVICE	\$ 5,651.55	\$ -	\$ -	\$ 5,651.55	\$ 3,439.68		0.96%	\$ 2,211.86	0.61%	\$ 5,651.55	1.57%
VII	VOLLEY COURT	\$ 10,563.91	\$ 3,295.82	\$ -	\$ 7,268.09	\$ 9,775.96		2.71%	\$ (2,507.86)	-0.70%	\$ 7,268.09	2.02%
VIII	WATER TOWER	\$ 22,909.48	\$ 7,766.25	\$ -	\$ 15,143.23	\$ 9,293.53		2.58%	\$ 5,849.70	1.62%	\$ 15,143.23	4.21%
A	TOTAL AMOUNT	\$ 320,957.72	\$ 52,133.12	\$ 15,708.03	\$ 285,174.54	\$ 266,465.24		73.99%	\$ 18,709.30	5.20%	\$ 285,174.54	79.19%
B	CONTRACTOR FEE AND OVERHEAD (10% x A)	\$ 32,095.77	\$ 5,213.31	\$ 1,570.80	\$ 28,517.45	\$ 26,646.52		7.40%	\$ 1,870.93	0.52%	\$ 28,517.45	7.92%
C	TAX (2% x (A+B))	\$ 7,061.07	\$ 1,146.93	\$ 345.58	\$ 6,273.84	\$ 5,862.24		1.63%	\$ 411.60	0.11%	\$ 6,273.84	1.74%
D	TOTAL	\$ 360,114.56	\$ 58,493.36	\$ 17,624.41	\$ 319,965.84	\$ 298,974.00		83.02%	\$ 20,991.83	5.83%	\$ 319,965.84	88.85%

Prepared by:
Date, / / 2022

Eng. Fidelis Mardiano da Costa
Engenheiro Edifício Público, Água e Saneamento ADN.I.P.
Município Manufahi

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior Edifício Público, Água e Saneamento ADN.I.P.

Certified by:
Date, / / 2022

Eng. Emerenciano da Costa Maia
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN.I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 19)

Back-up Data

Naran Projeto : Konstruksi Pagar Keliling Stadion Ailuli (Same-Manufahi)
No. kontratu : 09/PDIM/M-MF/X/2019

Data Inspesaun : 11/07/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ida ne'e ba inspesaun pagamentu





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII QUATRO ANO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

Nama Proyek : Konstruksi Pagar Keliling Stadion Alilui (Same-Manufahi)
Suco : Lefefoho
Posto Administrativo : Same
Município : Manufahi
Contraktor : Tutar Bofdik Tane Lisuk Unip Lda

BACKUP DATA

NO	DESCRIPTION	AMOUNT	Amendment				CCO Submission				ADN RECOMMENDED					
			Amount \$		Amount \$		Amount \$		Amount \$		Up to Date-3rd payment		This Bill-4th payment		Up to Date-4th payment	
			Add.	Del.	Tot.	Add.	Del.	Tot.	AMOUNT	%	AMOUNT	%	AMOUNT	%	AMOUNT	%
I	PEKERJAAN PERSIAPAN	\$ 375.00	-	-	\$ 375.00	-	-	\$ 375.00	\$ 181.67	0.77%	\$ 193.33	0.82%	\$ 375.00	1.58%		
II	PEKERJAAN TANAH, FONDASI & SLOOF	\$ -	\$ 566.31	-	\$ 566.31	\$ 1,576.81	-	\$ 2,143.12	\$ 566.31	2.39%	\$ 1,576.81	6.65%	\$ 2,143.12	9.04%		
III	PEKERJAAN PAGAR & TANAMAN POHON	\$ -	\$ 2,482.85	-	\$ 2,482.85	-	-	\$ 337.55	\$ 2,485.30	10.49%	\$ -	0.00%	\$ 2,485.30	10.49%		
IV	PEKERJAAN PEMASANGAN PAVING	\$ 16,754.06	\$ 235.16	-	\$ 16,989.22	-	-	\$ 3,529.85	\$ 13,459.38	56.80%	\$ -	0.00%	\$ 13,459.38	56.80%		
V	Overhead	\$ 404.17	-	-	\$ 404.17	-	-	\$ 404.17	\$ 210.00	0.89%	\$ 194.17	0.82%	\$ 404.17	1.71%		
A	Total Konstruksi	\$ 17,129.06	\$ 3,624.32	-	\$ 20,753.39	\$ 1,576.81	\$ 3,867.40	\$ 18,462.80	\$ 16,692.65	70.44%	\$ 1,770.15	7.47%	\$ 18,462.80	77.91%		
B	Contractor fee and Over head 10% x (A)	\$ 1,712.91	\$ 362.43	-	\$ 2,075.34	\$ 157.68	\$ 386.74	\$ 1,846.28	\$ 1,669.27	7.04%	\$ 177.01	0.75%	\$ 1,846.28	7.79%		
C	Overhead	\$ 404.17	-	-	\$ 404.17	-	-	\$ 404.17	\$ 210.00	0.89%	\$ 194.17	0.82%	\$ 404.17	1.71%		
D	Tax payment 2% x (A + B + C)	\$ 384.92	\$ 79.74	-	\$ 464.66	\$ 34.69	\$ 85.08	\$ 414.26	\$ 371.44	1.57%	\$ 42.83	0.18%	\$ 414.26	1.75%		
E	GRAND TOTAL (A + B + C + D)	\$ 19,631.06	\$ 4,066.49	-	\$ 23,697.55	\$ 1,769.19	\$ 4,339.22	\$ 21,127.51	\$ 18,943.36	79.94%	\$ 2,184.16	9.22%	\$ 21,127.51	89.15%		

Prepared by:
Date, / / 2021

Eng. Fideis Machado da Costa
Município Manufahi

Verified by:
Date, / / 2021

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior Edifício Público, Água e Saneamento ADN, I.P.

Certified by:
Date, / / 2021

Eng. Emergentina da Costa Maia
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.



#ANEXU C1 (SAME 23)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK,
MANUFAHI, RELASIONA BA COVID 19 AT MINISTRY OF
HEALTH, TIMOR LESTE

No. kontratu : RDTL-MS-C19-DNA-RBK-21-088

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : 125.65449101, Latetude : -8.99989127


End Point : Long :, Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Fízikiamente projetu ne'e remata ona no
dadaaunk ne'e hein de'it submisaun
pagamentu final

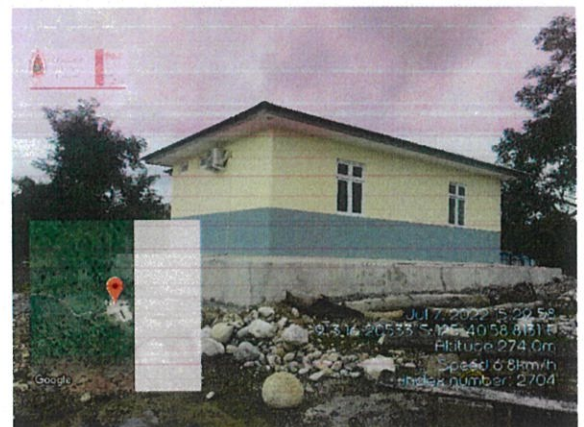



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 23)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK,
MANUFAHI, RELASIONA BA COVID 19 AT MINISTRY OF
HEALTH, TIMOR LESTE

No. kontratu : RDTL-MS-C19-DNA-RBK-21-088

Data Inspesaun : 11/07/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : 125.65449101, Latetude : -8.99989127


End Point : Long :, Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Inspesaun ne'e ba inspesaun pagamentu
final

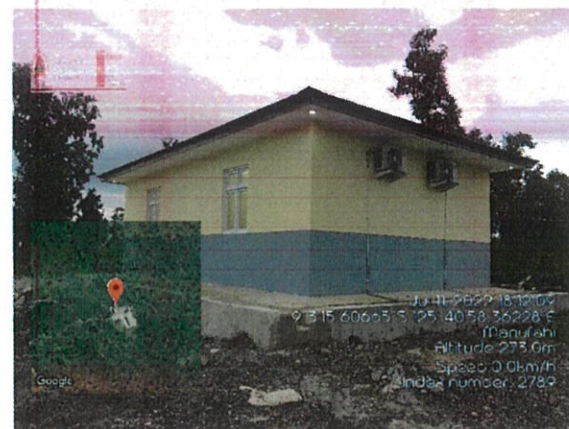



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 23)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK,
MANUFAHI, RELASIONA BA COVID 19 AT MINISTRY OF
HEALTH, TIMOR LESTE

No. kontratu : RDTL-MS-C19-DNA-RBK-21-088

Data Inspesaun : 19/07/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : 125.65449101, Latetude : -8.99989127

End Point : Long :, Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Akomponha ekipa laboratoriu AND,I.P
hodi halo *hummer test* ba *flooring* hodi
fasilita pagamentu final



Observasaun iha tereno no Foto Aktual





PROJECT TITLE : NEW CONSTRUCTION OF LABORATORY IHA CSI LUAK, MANUFAHI, RELASIONA BA
COVID 19 AT MINISTRY OF HEALTH, TIMOR LESTE

LOCATION : LUAK - MANUFAHI MUNICIPALITY - TIMOR LESTE

PROJECT OWNER : MINISTRY OF HEALTH

BILL OF QUANTITY (BOQ)

NO	DESCRIPTION	ORIGINAL CONTRACT				OWNER PROPOSAL - CCO						ADN,IP RECOMMENDATION PROPOSAL - CCO											
		UNIT	QUANTITY	UNIT PRICE	AMOUNT	Deduction (-)		Addition (+)		Revised		Deduction (-)		Addition (+)		Revised		Up to 27052022		July Progress		Up to date (11/07/2021) - PHO Payment	
						QTT	Amount	QTT	Amount	QTT	Amount	QTT	Amount	QTT	Amount	QTT	Amount	AMOUNT	WEIGHTH	AMOUNT	WEIGHTH	AMOUNT	WEIGHTH
I	PREPARATION WORKS				\$ 2,764.34	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,764.34	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,764.34	\$ 2,653.80	3.72%	\$ 110.54	0.15%	\$ 2,764.34	3.87%
II	FUNDATION WORKS				\$ 2,858.25	\$ -	\$ -	\$ -	\$ 1,516.83	\$ -	\$ 4,375.07	\$ -	\$ -	\$ -	\$ 1,516.83	\$ -	\$ 4,375.07	\$ 2,858.25	4.00%	\$ 1,516.83	2.12%	\$ 4,375.07	6.13%
III	CONCRETE WORKS				\$ 4,976.55	\$ -	\$ -	\$ -	\$ 2,372.64	\$ -	\$ 7,349.20	\$ -	\$ 442.58	\$ -	\$ 1,891.49	\$ -	\$ 6,425.47	\$ 2,056.48	2.88%	\$ 4,368.99	6.12%	\$ 6,425.47	9.00%
IV	WALL INSTALATION AND PLESTERING				\$ 4,969.75	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 4,969.75	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 4,969.75	\$ 4,969.75	6.96%	\$ -	0.00%	\$ 4,969.75	6.96%
V	CARPENTER WORKS				\$ 5,290.00	\$ -	\$ -	\$ -	\$ 550.00	\$ -	\$ 5,840.00	\$ -	\$ -	\$ -	\$ 550.00	\$ -	\$ 5,840.00	\$ 5,290.00	7.41%	\$ 550.00	0.77%	\$ 5,840.00	8.18%
VI	ROOFING WORKS				\$ 10,686.82	\$ -	\$ -	\$ -	\$ 928.69	\$ -	\$ 11,855.70	\$ -	\$ -	\$ -	\$ 1,310.44	\$ -	\$ 11,997.26	\$ 10,686.82	14.96%	\$ 1,310.44	1.83%	\$ 11,997.26	16.80%
VII	CEILING WORKS				\$ 3,585.35	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,585.35	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,585.35	\$ 2,930.15	4.10%	\$ 655.20	0.92%	\$ 3,585.35	5.02%
VIII	FLOOR TILE WORKS				\$ 3,552.36	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,552.36	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,552.36	\$ 3,552.36	4.97%	\$ -	0.00%	\$ 3,552.36	4.97%
IX	ELECTRICAL WORKS				\$ 3,708.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,708.00	\$ -	\$ 2,389.00	\$ -	\$ 2,714.29	\$ -	\$ 3,533.29	\$ -	0.00%	\$ 3,533.29	4.95%	\$ 3,533.29	4.95%
X	SANITASI WORKS				\$ 4,710.78	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 4,710.78	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 4,710.78	\$ 2,742.15	3.84%	\$ 1,968.63	2.76%	\$ 4,710.78	6.60%
XI	PAINTING WORKS				\$ 1,203.69	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,203.69	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,203.69	\$ 1,203.69	1.69%	\$ -	0.00%	\$ 1,203.69	1.69%
XII	PROVISIONAL SUM FOR FURNITURE				\$ 8,000.00	\$ -	\$ -	\$ -	\$ 8,000.00	\$ -	\$ 8,000.00	\$ -	\$ -	\$ -	\$ 6,703.21	\$ -	\$ 6,703.21	\$ -	0.00%	\$ 6,703.21	9.39%	\$ 6,703.21	9.39%
XIII	FINAL CLEARING				\$ 300.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 300.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 300.00	\$ -	0.00%	\$ 300.00	0.42%	\$ 300.00	0.42%
A	CONSTRUCTION COST (I +...+ XIII)				\$ 56,605.89	\$ -	\$ -	\$ -	\$ 13,368.16	\$ -	\$ 62,214.23	\$ -	\$ 2,831.58	\$ -	\$ 14,686.26	\$ -	\$ 59,960.57	\$ 38,943.44	54.53%	\$ 21,017.13	29.43%	\$ 59,960.57	83.96%
B	Contractor fee 10% x (A * 10%)				\$ 5,660.59	\$ -	\$ -	\$ -	\$ 1,336.82	\$ -	\$ 6,221.42	\$ -	\$ 283.16	\$ -	\$ 1,468.63	\$ -	\$ 5,996.06	\$ 3,894.34	5.45%	\$ 2,101.71	2.94%	\$ 5,996.06	8.40%
C	Overhead				\$ 2,550.00	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,550.00	\$ 2,550.00	\$ -	\$ -	\$ -	\$ -	\$ 2,550.00	\$ 2,190.00	3.07%	\$ 360.00	0.50%	\$ 2,550.00	\$ 0.04
D	TAX 2% x (A + B + C)				\$ 1,296.33	\$ -	\$ -	\$ -	\$ 294.10	\$ -	\$ 1,419.71	\$ 51.00	\$ 62.29	\$ -	\$ 323.10	\$ -	\$ 1,370.13	\$ 900.56	1.26%	\$ 469.58	0.66%	\$ 1,370.13	1.92%
E	CONTIGENCY				\$ 5,300.00		\$ -		\$ -		\$ -		\$ -		\$ -		\$ -	\$ -	0.00%	\$ -	0.00%	\$ -	\$ -
F	TOTAL PROJECT COST (A + B + C + D + E)				\$ 71,412.80	\$ -	\$ -	\$ -	\$ 14,999.08	\$ -	\$ 72,405.37	\$ 2,601.00	\$ 3,177.03	\$ -	\$ 16,477.98	\$ -	\$ 69,876.76	\$ 45,928.34	64.31%	\$ 23,948.42	33.53%	\$ 69,876.76	97.85%

Prepared by:
Date, / / 2021

Eng. Fidelis Mardiano da Costa

Engenheiro Edifício Público, Água e Saneamento ADN, I.P. Município Manufahi

Verified by:
Date, / / 2021

Arch. Francisco Xavier de Deus Jeronimo

Engenheiro Senior Edifício Público, Água e Saneamento ADN-IP

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia

Coordenadora da Unidade de Controlo e Validação de Qualidade ADN-IP



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 24)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF CAMPAS, GATE AND LEVELING
AREA AND GARDEN OF HEROES MANUFAHI

No. kontratu : 39/MACLN/IX/2021

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Luak Manufahi

Koordinadas :

Start Point : Long :, Latetude :

End Point : Long :, Latetude :


Naran Inspetur : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Clearing leveling Works

A = 23,546.33 Sqm

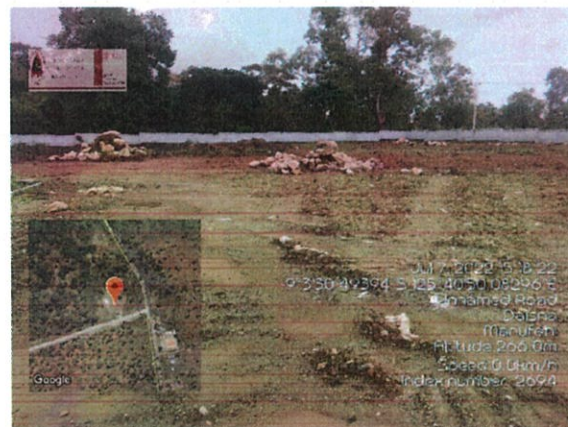



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 24)

Back-up Data

Naran Projeto : NEW CONSTRUCTION OF CAMPAS, GATE AND LEVELING
AREA AND GARDEN OF HEROES MANUFAHI

No. kontratu : 39/MACLN/IX/2021

Data Inspesaun : 21/07/2021

Fatin Inspesaun : Luak Manufahi

Koordinadas :

Start Point : Long :, Latetude :

End Point : Long :, Latetude :

Naran Inspetur : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Clearance & Leveling

A = 23,546.33 Sqm

Observasaun iha tereno no Foto Aktual





ADN, LP.

Agência de
Normas e Padrões
Nacionais Instituto Público



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ANEXU C2 (SAME 24)

PROJECT OWNER : MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO
NACIONAL
TITLE PROJECT : NEW CONSTRUCTION OF CAMPAS, GATE AND LEVELING AREA AND
GARDEN OF HEROES MANUFAHI

BILL OF QUANTITY (BOQ) PROGRESS

BILL OF QUANTITY (BOQ) PROGRESS											
No	DESCRIPTION WORKS	Unit	Qty	Unit Price	Amount	AND I.P RECOMMENDATION					
						Up-To-January			July Progress		
						QTY	AMOUNT	WEIGHT	QTY	AMOUNT	WEIGHT
A PERSIAPAN											
1	Mobilisasi	Ls	1.00	\$ 250.00	\$ 250.00	0.85	\$ 212.50	0.43%	0.15	\$ 37.50	0.08%
2	Demobilisasi	Ls	1.00	\$ 150.00	\$ 150.00	-	\$ -	0.00%	1.00	\$ 150.00	0.31%
3	Papan Nama Proyek	Bh	1.00	\$ 110.00	\$ 110.00	-	\$ -	0.00%	-	\$ -	0.00%
4	Penyediaan Air dan Listrik kerja	Ls	1.00	\$ 150.00	\$ 150.00	0.75	\$ 93.75	0.19%	0.25	\$ 37.50	0.08%
5	Direksi Kit dan gudang proyek	Ls	1.00	\$ 200.00	\$ 200.00	0.75	\$ 125.00	0.26%	0.75	\$ 125.00	0.26%
6	Dokument dan Laporan										
	Sub Total				\$ 860.00		\$ 431.25	0.88%		\$ 225.00	0.46%
	TOTAL A				\$ 860.00		\$ 431.25	0.88%		\$ 225.00	0.46%
B KONSTRUKSI KUBURAN											
I PEKERJAAN TANAH											
1	Pemasangan Bowlplank untuk kuburan	Ls	1.00	\$ 100.00	\$ 100.00	1.00	\$ 100.00	0.20%	0.00	\$ -	0.00%
2	Galian Tanah dengan Alat Berat (Excavator)	m3	64.20	\$ 4.20	\$ 269.64	64.20	\$ 269.64	0.55%	0.00	\$ -	0.00%
3	Menimbun Kembali Galian Tanah	m3	16.05	\$ 1.24	\$ 19.90	8.03	\$ -	0.00%	8.03	\$ 9.95	0.02%
4	Urugan Pasir Lantai Kuburan	m3	7.30	\$ 13.66	\$ 99.72	9.13	\$ 438.76	0.90%	-1.83	\$ (24.93)	-0.05%
5	Perataan dan Pemadatan Tanah	m3	23.35	\$ 3.10	\$ 72.39	11.68	\$ 36.19	0.07%	11.68	\$ 36.19	0.07%
	Sub Total				\$ 561.65		\$ 844.59	1.72%		\$ 21.21	0.04%
II PEKERJAAN BETON											
1	Plat Beton dengan Tebal 100 mm $f_c = 19.3$ Mpa atau K225	m3	4.09	\$ 113.31	\$ 463.44	-	\$ -	0.00%	4.09	\$ 463.44	0.95%
2	Besi Beton untuk Plat dengan Ø 12 mm	kg	404.49	\$ 1.10	\$ 444.94	-	\$ -	0.00%	404.49	\$ 444.94	0.91%
3	Bekisting Plat Beton & Papan Nama dengan Tebal 100 mm	m2	25.58	\$ 22.00	\$ 562.76	-	\$ -	0.00%	-	\$ -	0.00%
4	Papan Nama Beton $f_c = 19.3$ Mpa atau K225	m3	3.69	\$ 113.31	\$ 418.11	-	\$ -	0.00%	-	\$ -	0.00%
5	Besi Beton untuk Papan nama dengan Ø 8 mm	kg	247.65	\$ 1.10	\$ 272.42	-	\$ -	0.00%	-	\$ -	0.00%
6	Bekisting Papan Nama	m2	18.91	\$ 22.00	\$ 416.02	-	\$ -	0.00%	-	\$ -	0.00%
7	Beton untuk Dinding $f_c = 19.3$ Mpa atau K225	m3	16.79	\$ 113.31	\$ 1,902.47	-	\$ -	0.00%	16.79	\$ 1,902.47	3.88%
8	Besi beton untuk Dinding dengan Ø 12 mm	kg	1,708.26	\$ 1.10	\$ 1,879.09	-	\$ -	0.00%	1,708.26	\$ 1,879.09	3.83%
9	Bekisting Beton untuk Dinding	m2	77.41	\$ 23.47	\$ 1,816.81	-	\$ -	0.00%	77.41	\$ 1,816.81	3.71%
	Sub Total				\$ 8,176.06		\$ -	0.00%		\$ 6,506.75	13.28%
III PEKERJAAN PAPAN NAMA											
1	Pasang Papan Nama dengan Material Granit + Komplit	Unit	41.00	\$ 200.00	\$ 8,200.00	-	\$ -	0.00%	-	\$ -	0.00%
	Assesories + Pemasang				\$ 8,200.00	-	\$ -	0.00%	-	\$ -	0.00%
	Sub Total				\$ 16,937.70		\$ 844.59	1.72%		\$ 6,527.96	13.32%
TOTAL B											
C PERLENGKAPAN GAPURA & LANDSCAPE											
I PEKERJAAN PINTU GAPURA											
1	Pintu Utama Gapura dengan Besi Hollow 70 x 50 x 2 mm	kg	134.01	\$ 2.00	\$ 268.02	100.51	\$ 201.02	0.41%	33.50	\$ 67.01	0.14%
2	Pintu Utama Gapura dengan Besi Beton dengan diameter 25 mm	kg	193.96	\$ 1.10	\$ 213.36	145.47	\$ 160.02	0.33%	48.49	\$ 53.34	0.11%
3	Pintu Utama gapura dengan Besi Beton dengan diameter 16 mm	kg	39.22	\$ 1.10	\$ 43.14	29.42	\$ 32.36	0.07%	9.81	\$ 10.79	0.02%

Handwritten signature/initials.

No	DESCRIPTION WORKS	Unit	Qty	Unit Price	Amount	AND,I.P RECOMMENDATION						Up-To-30072022		
						July Progress			QTY	WEIGHT	QTY	AMOUNT	WEIGHT	QTY
						QTY	AMOUNT	WEIGHT						
4	Engsel Pintu Besi untuk Gapura Besar	Unit	4.00	\$ 25.00	\$ 100.00									
5	Grendel Pintu Gapura Besar	Unit	2.00	\$ 25.00	\$ 50.00									
6	Pengecatan Pintu Gapura Besar	m2	18.69	\$ 2.50	\$ 46.73									
7	Cup Flower Decoratif Keseluruhan Gapura Besar	Ls	1.00	\$ 150.00	\$ 150.00									
8	Pintu Utama Gapura Kecil dengan Besi Hollow 70 x 50 x 2 mm	Kg	69.51	\$ 2.00	\$ 139.02									
9	Pintu Gapura Kecil dengan Besi Beton dengan diameter 25 mm	kg	74.46	\$ 1.10	\$ 81.91									
10	Pintu Gapura Kecil dengan Besi Beton dengan diameter 16 mm	Kg	23.51	\$ 1.10	\$ 25.86									
11	Engsel Pintu Gapura Kecil	Unit	4.00	\$ 25.00	\$ 100.00									
12	Grendel Pintu Gapura Kecil	Unit	2.00	\$ 25.00	\$ 50.00									
13	Pengecatan Pintu Gapura Kecil	m2	4.37	\$ 2.00	\$ 8.74									
14	Cup Flower Decoratif Keseluruhan Gapura Kecil	Ls	1.00	\$ 100.00	\$ 100.00									
15	Pasang Kerb Stone Untuk Tanaman Bunga dan Rumpuk	m'	184.26	\$ 13.00	\$ 2,395.38									
	Sub Total				\$ 3,772.15									
	TOTAL C				\$ 3,772.15									
D	PEMBERSIHAN & LEVELING AREA													
1	Pembersihan Lokasi & Leveling Area Keseluruhan (Konfirmasi Teknik MCLN)	m2	23,546.33	\$ 0.90	\$ 21,191.70									
	Sub Total				\$ 21,191.70									
	TOTAL D				\$ 21,191.70									
E	OVERHEAD													
1	Site safety and Protective Clothing	Ls	1.00	\$ 100.00	\$ 100.00									
2	Site Engineer fee	Ls	1.00	\$ 200.00	\$ 200.00									
3	Security fee for (2 Person)	Bh	1.00	\$ 200.00	\$ 200.00									
4	As-Built drawing	Ls	1.00	\$ 150.00	\$ 150.00									
5	Material sampling and testing	Ls	1.00	\$ 200.00	\$ 200.00									
6	Laporan dan dokumentasi proyek	Ls	1.00	\$ 150.00	\$ 150.00									
	Overhead Works Cost				\$ 1,000.00									
F	CONSTRUCTION COAST				\$ 42,761.55									
G	CONTRACTOR FEE AND OVER HEAD 10% X (F)				\$ 4,276.16									
H	OVERHEAD				\$ 1,000.00									
I	TAX PAYMENT 2% X (F+G+H)				\$ 960.75									
J	GRAND TOTAL F + G + H + I				\$ 48,998.46									

Prepared by:
Date, / / 2021

Eng.Fidelis Mardiano da Costa
Enginheiro Edificio Publico, Agua e Saneamento ADN,I.P. Municipio Manufahi

Verified by:
Date, / / 2021

Arch. Francisco Xavier de Deus Jeronimo
Enginheiro Senior Edificio Publico, Agua e Saneamento ADN,I.P.

Certified by:
Date, / / 2021

Eng. Emerenciana da Costa Maia
Coordenadora da Unidade de Controlo e Validacao de Qualidade ADN,I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 27)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC DILIGENCIA
No. kontratu :

Data Inspesaun : 08/072022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Provizoriamente atividade la la'o





#ANEXU C2 (SAME 27)


Projeto : Nova Construção Escola Básica Central Diligência
Owner : MEJD
Localization : Letefoho, Same Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 27/06/2022 PROGRESS		JULY PROGRESS		UP TO 27/07/2022 PROGRESS	
	ITEM SERVIÇO	ADN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 2,675.00	\$ 980.63	0.88%			\$ 980.63	0.88%
II	CLASSROOM BUILDING CA	\$ 61,073.65	\$ 17,337.29	15.63%	\$ 1,419.95	1.28%	\$ 18,757.25	16.91%
III	TOILET BUILDING TB	\$ 24,613.61	\$ 6,749.52	6.08%			\$ 6,749.52	6.08%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 12,284.68						
V	PROVISIONAL SUM FOR DEMOLITION	\$ 1,464.27			\$ 754.36	0.68%	\$ 754.36	0.68%
A	CONSTRUCTION COST	\$ 102,111.20	\$ 25,067.44	22.59%	\$ 2,174.31	1.96%	\$ 27,241.75	24.55%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 110,951.20	\$ 25,067.44	22.59%	\$ 2,174.31	1.96%	\$ 27,241.75	24.55%

Verified by:
Date, / / 2022


Fidelis Mardiano da Costa L., eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UQVQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 28)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE TURON
No. kontratu :

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Babulo, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Provizoriamente atividade la la'o

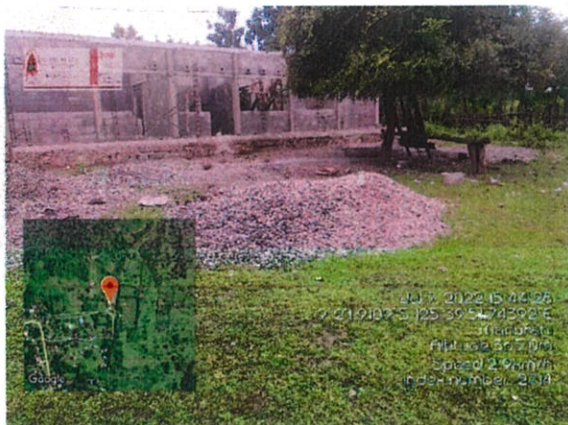



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 28)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE TURON
No. kontratu :

Data Inspesaun : 21/07/2022

Fatin Inspesaun : Babulo, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Serbisu Reboka





ANEXU C2 (SAME 28)


Projeto : Nova Construção Escola Pré Escolar Turon

Owner : MEJD


Localization : Babulo , Same Manufahi

MAIN SUMMARY				ADN, I.P. RECOMMENDATION					
ORIGINAL				UP TO 27/06/2022 PROGRESS		JULY PROGRESS		UP TO 30/07/2022 PROGRESS	
	ITEM SERVIÇO	A DN VERIFIED		AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,175.00		1,895.00	2.28%	\$ (204.00)	-0.25%	1,691.00	2.04%
II	CLASSROOM BUILDING C2	\$ 57,907.13		20,877.40	25.13%	\$ 606.95	0.73%	21,484.35	25.86%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 13,161.18							
A	CONSTRUCTION COST	\$ 74,243.31		\$ 22,772.40	27.41%	\$ 402.95	0.48%	\$ 23,175.35	27.89%
B	CONTIGENCY	\$ 3,000.00							
C	OVERHEAD	\$ 5,840.00							
D	GRAND TOTAL	\$ 83,083.31		\$ 22,772.40	27.41%	\$ 402.95	0.48%	\$ 23,175.35	27.89%


Verified by:
Date, / / 2022


Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCV ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 30)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF SELEHASAN

No. kontratu :

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Betano, Same – Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Provizoriamente atividade la la'o

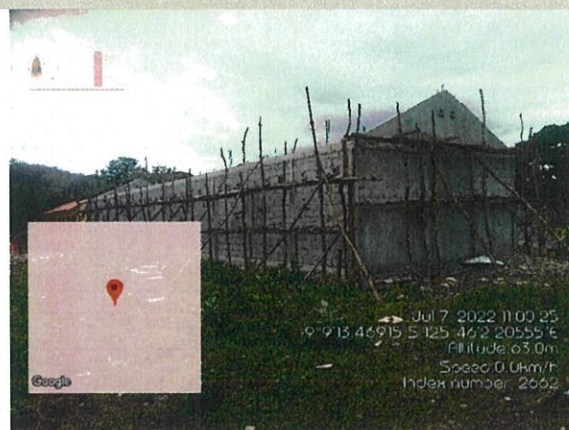



ANEXU C2 (SAME 30)


Projeto : Nova Construção Escola Básica Filial Selihasan
Owner : MEJD
Localization : Selihasan Betano , Same Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 27/05/2022 PROGRESS		JUNE PROGRESS		UP TO 27/06/2022 PROGRESS	
	ITEM SERVIÇO	ADN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,275.00	\$ 1,846.88	1.65%			\$ 1,846.88	1.65%
II	CLASSROOM BUILDING CA	\$ 61,808.99	\$ 13,787.83	12.33%	\$ 2,923.16	2.61%	\$ 16,710.99	14.95%
III	TOILET BUILDING TB	\$ 24,895.93	\$ 7,133.31	5.96%	\$ 6,291.41	5.63%	\$ 13,424.73	11.59%
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 11,921.67						
V	PROVISIONAL SUM FOR DEMOLITION	\$ 1,060.03						
A	CONSTRUCTION COST	\$ 102,961.61	\$ 22,768.02	19.94%	\$ 9,214.58	8.24%	\$ 31,982.59	28.19%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 111,801.61	\$ 22,768.02	19.94%	\$ 9,214.58	8.24%	\$ 31,982.59	28.19%


Verified by:
Date, / / 2022


Fideis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 31)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DAI-SUA LAMA
No. kontratu :

Data Inspeção : 26/07/2022

Fatin Inspeção :

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observação iha terreno no Foto Aktual

Instalasaun Armadura Viga (ringbalk)



Instalasaun diding batako





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 31)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DAI-SUA LAMA
No. kontratu :

Data Inspesaun : 08/07/2022

Fatin Inspesaun :

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :


Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Instalasaun didin Bloku



Observasaun iha tereno no Foto Aktual

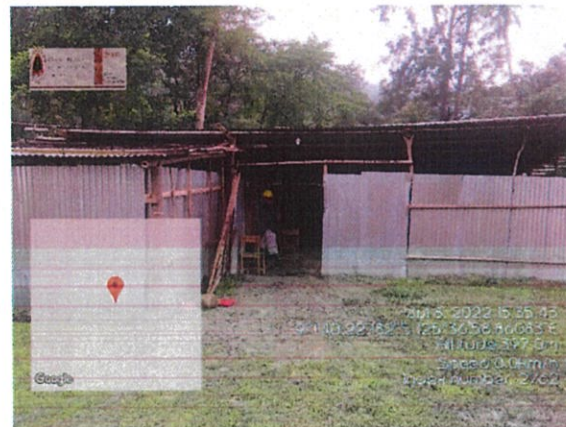



#ANEXU C2 (SAME 31)

Projeto : Nova Construção Edifício Escola Filial Hatsanaudo Daisua

Owner : MEJD


Localization : Hatsanaudo Daisua, Same- Manufahi

MAIN SUMMARY			ADN, I.P. RECOMMENDATION					
			UP TO 27/05/2022 PROGRESS		JULY PROGRESS		UP TO 29/07/2022 PROGRESS	
NO	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WIEGHT	AMOUNT	WIEGHT	AMOUNT	WIEGHT
I	PRELIMINARIES	\$ 3,475.00	\$ 1,075.00	1.06%			\$ 1,075.00	1.06%
II	CLASSROOM BUILDING C	\$ 50,921.69	\$ 7,414.96	7.31%	\$ 5,181.06	5.11%	\$ 12,596.02	12.42%
III	TOILET BUILDING Tb	\$ 25,156.94	\$ 1,128.90	1.11%	\$ 1,864.04	1.84%	\$ 2,992.94	2.95%
IV	PROVISIONAL-SUM FOR SITEWORKS (SW)	\$ 13,033.65						
A	CONSTRUCTION COST	\$ 92,587.27	\$ 9,618.86	9.48%	\$ 7,045.10	6.95%	\$ 16,663.96	16.43%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	\$ 908.00	0.90%			\$ 908.00	0.90%
D	GRAND TOTAL	\$ 101,427.27	\$ 10,526.86	10.38%	\$ 7,045.10	6.95%	\$ 17,571.96	17.32%


Verified by:
Date, / / 2022


Fidelis Mardiane da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Sênior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UC VQ ADN, I.P.



Naran projeto : NOVA CONTRUÇÃO EBF HATSANA UDO/DAI-SUA LAMA

#ANEXU D (SAME 31)

2022-10-30 10:38:18
 S 125.360 31295.0
 Unnamed Road
 Altitude: 5910
 Speed: 0.0km/h



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 32)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBF BLARO
No. kontratu :

Data Inspesaun : /07/2022

Fatin Inspesaun :

Koordinadas :

Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Provizoriamente serbisu la la'o

Observasaun iha tereno no Foto Aktual





Projeto : Nova Construção Escola Básica Filial Blaro
Owner : MEJD
Localization : Blaro - Holarua, Same Manufahi

MAIN SUMMARY			A D N, I.P. RECOMMENDATION							
			UP TO 27/05/2022 - PROGRESS		JULY PROGRESS		UP TO 29/07/2022 - PROGRESS			
	ITEM SERVIÇO	A D N VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,875.00	\$ 1,155.00	1.01%	\$ 145.00	0.13%	\$ 1,300.00	1.14%		
II	CLASSROOM BUILDING CA	\$ 64,486.89	\$ 5,657.97	4.97%	\$ 12,186.23	10.71%	\$ 17,844.20	15.68%		
III	TOILET BUILDING TB	\$ 25,966.99								
IV	PROVISIONAL SUM FOR SITE-WORKS	\$ 10,662.40								
A	CONSTRUCTION COST	\$ 104,991.28	\$ 6,812.97	5.99%	\$ 12,331.23	10.83%	\$ 19,144.20	16.82%		
B	CONTINGENCY	\$ 3,000.00								
C	OVERHEAD	\$ 5,840.00								
D	GRAND TOTAL	\$ 113,831.28	\$ 6,812.97	5.99%	\$ 12,331.23	10.83%	\$ 19,144.20	16.82%		

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 33)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EPE ROTUTO
No. kontratu :

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Rotuto, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :



End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Provizoriamente atividade la la'o

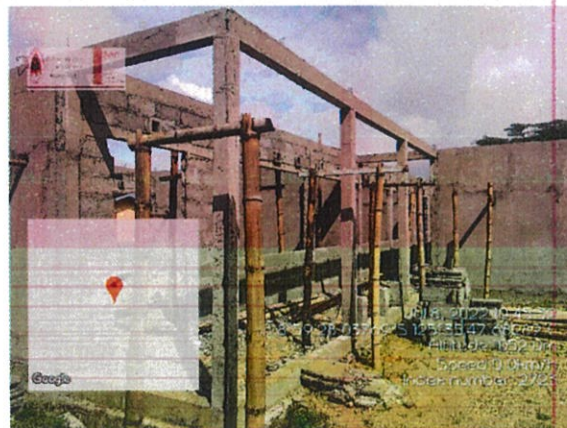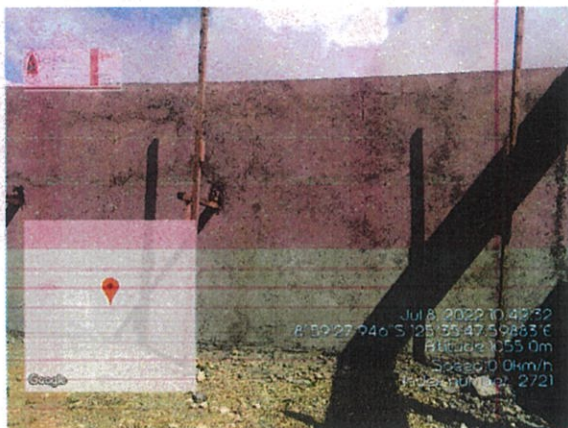



#ANEXU C2 (SAME 33)

Projeto : Nova Construção Edifício Escola EBF Rotuto

Owner : MEJD

Localization : Rotuto, Same Manufahi

MAIN SUMMARY

NO	ITEM SERVISU	A DN VERIFIED	Up to 27052022 - progres		July Progress		Up to 30072022 - progres	
			AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,675.00	\$ 1,061.00	1.48%	\$ 105.00	0.15%	\$ 1,166.00	1.62%
II	CLASSROOM BUILDING CL	\$ 52,911.97	\$ 11,816.75	16.44%	\$ 2,549.51	3.55%	\$ 14,366.26	19.98%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 5,899.87						
IV	PROVISIONAL SUM FOR DEMOLISH	\$ 566.03						
A	CONSTRUCTION COST	\$ 63,052.87	\$ 12,877.75	17.91%	\$ 2,654.51	3.69%	\$ 15,532.26	21.60%
B	CONTIGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	\$ 482.00	0.67%			\$ 482.00	0.67%
D	GRAND TOTAL	\$ 71,892.87	\$ 13,359.75	18.58%	\$ 2,654.51	3.69%	\$ 16,014.26	22.28%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, LP. Agência de Desenvolvimento Nacional, Instituto Público				INSTRUSAUN / REKOMENDASAUN			
Naran projeto : Nova Construcáo EPE Rotuto							
Kompanha : Gropu Komunitariu							
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/7/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil		Projetu de m. Constr. 1. 08/10/2022 2. 08/10/2022 3. 08/10/2022 4. 08/10/2022 5. 08/10/2022 6. 08/10/2022 7. 08/10/2022 8. 08/10/2022 9. 08/10/2022 10. 08/10/2022 11. 08/10/2022 12. 08/10/2022 13. 08/10/2022 14. 08/10/2022 15. 08/10/2022 16. 08/10/2022 17. 08/10/2022 18. 08/10/2022 19. 08/10/2022 20. 08/10/2022	
1 Aselera prosesu submisaun pagamentu nune'e bele kontinua serbisu							
2 Hadi'ak roste balun (Kintu kotuk) ne'ebe la nivel							



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 35)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC SIMPANG TIGA

No. kontratu :

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :


Start Point : Long : , Latetude :

End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Columns Above Ground Level of the Toilet


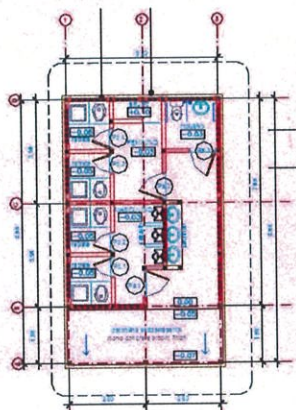


H = 3.2m
A = 0.15 x 0.15
Qtt = 25no
V = 1.69cu.m

Observasaun iha tereno no Foto Aktual



Ringbalk concrete

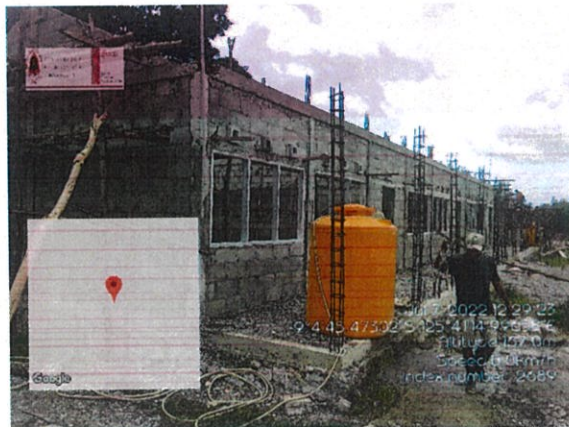



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 35)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO EBC SIMPANG TIGA

No. kontratu :

Data Inspesaun : 21/07/2022

Fatin Inspesaun : Daisua, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Wall Block works for roofing sloping



$$A = 0.5 * 1.61m * 7.25m$$

$$A = 5.836sqm$$





#ANEXU C2 (SAME 35)

Projeto : Nova Construção Edifício Escola Básica Central Simpang Tiga

Owner : MEJD

Localization : Simpang Tiga Daisua, Same- Manufahi

MAIN SUMMARY			ADN,LP RECOMMENDATION					
			Up to 27062022 - progres		July Progress		Up to 30072022 - progres	
NO	ITEM SERVIÇO	A DN VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,675.00	\$ 1,475.00	1.05%	\$ (150.00)	-0.11%	\$ 1,325.00	0.94%
II	CLASSROOM BUILDING C	\$ 49,223.37	\$ 19,357.78	13.77%			\$ 19,357.78	13.77%
III	CLASSROOM BUILDING Cdl	\$ 42,912.01	\$ 8,998.23	6.40%			\$ 8,998.23	6.40%
IV	TOILET BUILDING Tb	\$ 24,347.83	\$ 1,601.37	1.14%	\$ 5,178.24	3.68%	\$ 6,779.61	4.82%
V	PROVISIONAL FOR SITEWORKS	\$ 10,945.68						
VI	PROVISIONAL FOR DEMOLISH	\$ 670.35						
A	CONSTRUCTION COST	\$ 131,774.24	\$ 31,432.38	22.35%	\$ 5,028.24	3.58%	\$ 36,460.62	25.93%
B	CONTINGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00						
D	GRAND TOTAL	\$ 140,614.24	\$ 31,432.38	22.35%	\$ 5,028.24	3.58%	\$ 36,460.62	25.93%

Verified by:
Date, / / 2022



Fidelis Mardiano da Costa L. eng. Civ.
Eng. EPAS ADN, I.P.


Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UC/VQ ADN, I.P.

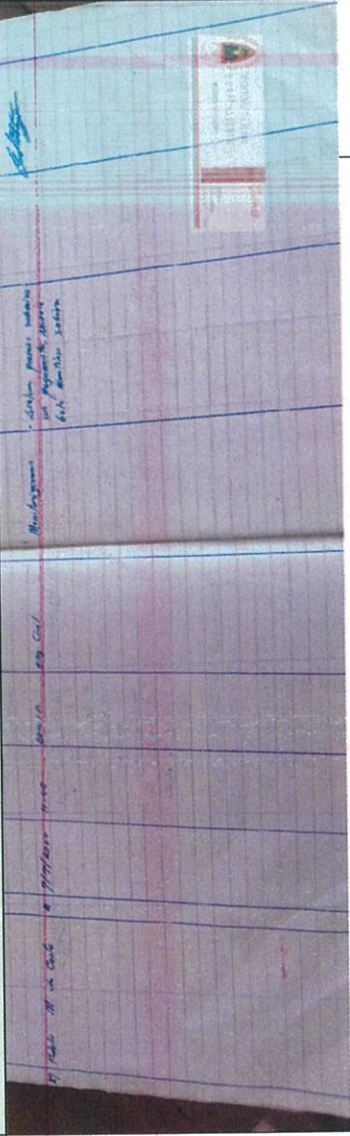 					INSTRUSAUN / REKOMENDASAUN				
MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL					Naran projeto : Nova Construção EBC Sempang Tiga				
#ANEXU D (SAME 35)					Kompanha : Gropu Komunitariu				
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN			Asinatura
I	7/7/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil					
					1	Aselera prosesu submissaun pagamentu nune'e bele kontinua serbisu			

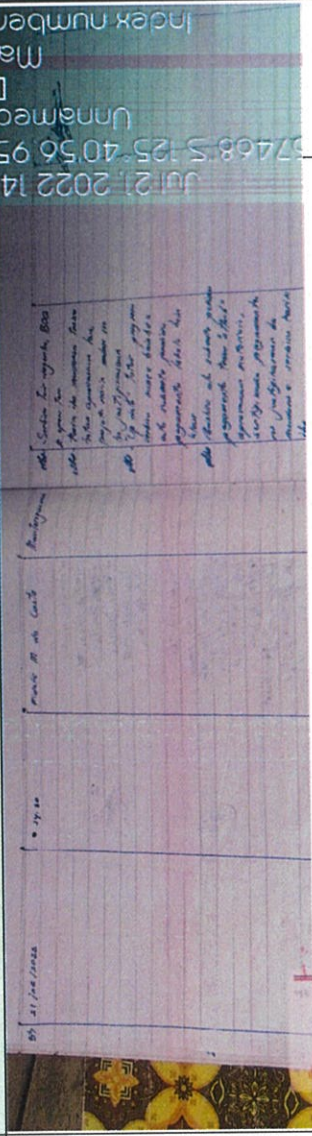 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, LP. Agência de Desenvolvimento Nacional, Instituto Público					INSTRUSAUN / REKOMENDASAUN				
					Naran projeto : Nova Construcão EBC Simpang Tiga				
					Kompanha : Gropu Komunitariu				
#ANEXU D (SAME 35)					INSTRUSAUN / REKOMENDASAUN				
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No				
I	21/7/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil					
					1				
					2				
					3				
					4	1 Serbisu tuir dezenhu, BOQ & spek. Tek 2 Karik iha mudansa tenke hetan aprovasaun husi projektu na'in no justifikasaun 3 Up date tutuir progresu serbisu nune'e bainhira atu submete pedidu pagamentu la bele hein kleur 4 Bainhira atu submete pedidu pagamentu tenke attach aprovasaun materiais, sertifikadu pagamentu no justifikasaun karik iha mudansa serbisu			



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 36)

Back-up Data

Naran Projeto : NOVA CONTRUÇÃO ESTV HALIBUR BETANO

No. kontratu :

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Betano, Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Dadauk ne'e atividade terenu laiha tamba ne'e
hein submisaun pagamentu ba segundu faze

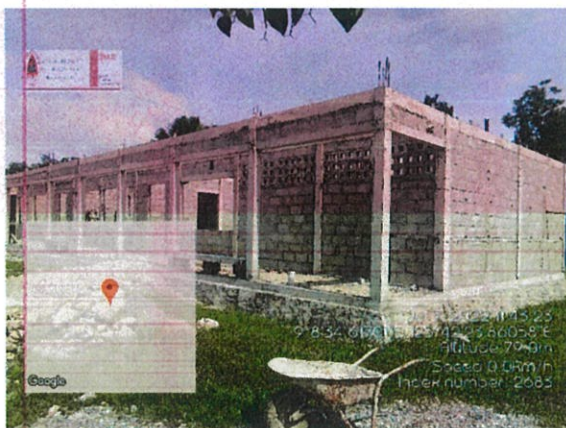



ANEXU C2 (# SAME 36)


Projeto : Nova Construção Edifício Escritório na ESTV Halibur Betano
Owner : MEJD
Localization : Betano, Same- Manufahi

MAIN SUMMARY			A D N, I.P. RECOMMENDATION					
			Up to 27062022 - progres		July Progress		Up to 30072022 - progres	
NO	ITEM SERVISU	A DN VERIFIED	AMOUNT	WEIGHT	AMOUNT	WEIGHT	AMOUNT	WEIGHT
I	PRELIMINARIES	\$ 3,175.00	1,155.00	0.87%	\$ 45.00	0.03%	1,200.00	0.91%
II	TEACHER OFFICE	\$ 79,003.71	22,596.24	17.06%	\$ 1,575.80	1.19%	24,172.04	18.25%
III	PROVISIONAL SUM FOR SITE-WORKS	\$ 41,447.68						
A	CONSTRUCTION COST	\$ 123,626.39	\$ 23,751.24	17.93%	\$ 1,620.80	1.22%	\$ 25,372.04	19.15%
B	CONTIGENCY	\$ 3,000.00						
C	OVERHEAD	\$ 5,840.00	120.00	0.09%			120.00	0.09%
D	GRAND TOTAL	\$ 132,466.39	\$ 23,871.24	18.02%	\$ 1,620.80	1.22%	\$ 25,492.04	19.24%


Verified by:
Date, / / 2022



Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022


Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Certified by:
Date, / / 2022


Eng. Emerenciana da Costa Maia
Coordenadora UCVQ ADN, I.P.

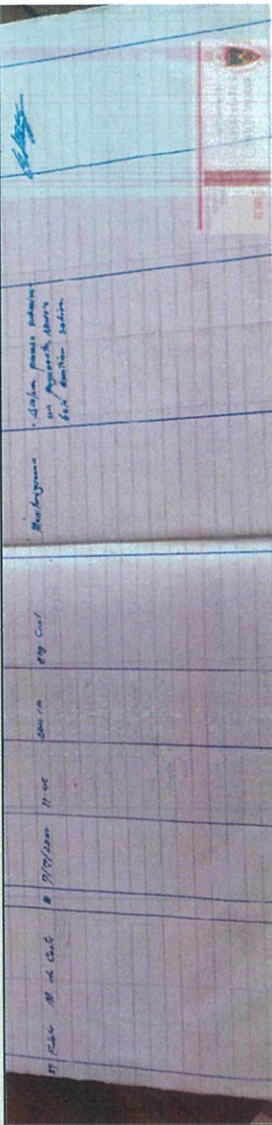 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL				 ADN, LP. Agência de Desenvolvimento Nacional, Instituto Público				INSTRUSAUN / REKOMENDASAUN			
Naran projeto : Nova Construcão ESTV Halibur Betano											
Kompanha : Gropu Komunitariu											
		#ANEXU D (SAME 36)									
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura			
I	7/7/2022	Manufahi / Same	Fidelis Mardiano da Costa	Eng. Civil							
					1	Aselera prosesu submisaun pagamentu nune'e bele kontinua serbisu					



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SAME 37)

Back-up Data

Naran Projeto : New Construction Building for Central Electrical in Luak Manufahi,
Ministry of Health Timor Leste
No. kontratu : RDTL-MS-C19-DNA-DC-22-006

Data Inspesaun : 07/07/2022

Fatin Inspesaun : Same - Manufahi

Koordinadas :

Start Point : Long : , Latetude :


End Point : Long : , Latetude :

Naran Inspector : Eng. Fidelis Mardiano da Costa L, Eng. Civ.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Atividade laiha, Hein konesaun gengset

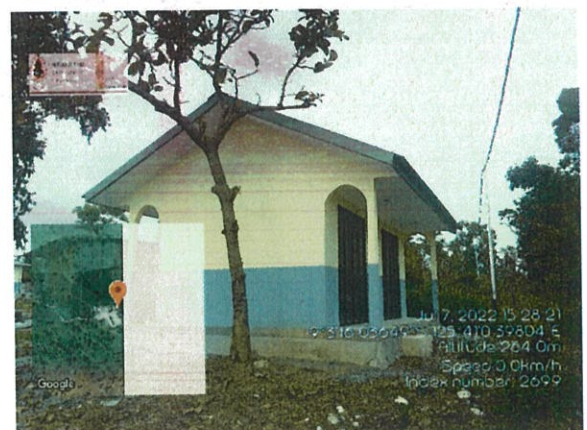



Anexu c2 (SAME 37)

SUMMARY

PROJECT TITLE : NEW CONSTRUCTION BUILDING for CENTRAL ELECTRICAL

LOCATION : LUAK - MANUFAHI

ORIGINAL CONTRACT			July Progress	
NO	DESCRIPTION	Total Amount (USD)	AMOUNT	WEIGHT
I	PREPARATION WORKS	\$ 600.00	\$ 250.00	1.36%
II	CONSTRUCTION HOUSE FOR GENSET	\$ 295.20	\$ 295.20	1.61%
III	FONDATION WORK	\$ 1,254.92	\$ 1,254.92	6.84%
IV	CONCRETE WORK	\$ 880.51	\$ 716.17	3.91%
V	COLOM	\$ 743.83	\$ 629.29	3.43%
VI	TOP BEAM	\$ 1,459.29	\$ 854.22	4.66%
VII	WALL INSTALATION WORK	\$ 1,475.70	\$ 1,475.70	8.05%
VIII	DOOR WORK	\$ 1,102.00	\$ 1,102.00	6.01%
IX	ROOFING WORK	\$ 3,626.82	\$ 3,626.82	19.78%
X	CEILING WORK	\$ 2,175.18	\$ 1,666.39	9.09%
XI	ELECTRICAL WORK	\$ 863.14	\$ -	0.00%
XII	PAINTING WORK	\$ 452.69	\$ 452.69	2.47%
XIII	FINAL CLEARING	\$ 100.00	\$ -	0.00%
A	CONTRUCTION COST (I + XIII)	\$ 15,029.29	\$ 12,323.41	67.21%
B	Fee Contractor (10% x A)	\$ 1,502.93	\$ 1,232.34	6.72%
D	TAX 2% x (A + B)	\$ 300.59	\$ 246.47	1.34%
E	CONTIGENCY	\$ 1,502.93	\$ 1,232.34	6.72%
F	TOTAL PROJECT COST (A + B + C + D)	\$ 18,335.73	\$ 15,034.56	82.00%

Verified by:
Date, / / 2022

Fidelis Mardiano da Costa, L. eng. Civ.
Eng. EPAS ADN, I.P.

Verified by:
Date, / / 2022

Arch. Francisco Xavier de Deus Jeronimo
Engenheiro Senior EPAS ADN, I.P.

Verified by:
Date, / / 2022

Eng. Emerenciana da Costa Maia
Cordenadora UCM Q ADN, I.P.

Page 1 of 3

Page 2 of 3

Page 3 of 3

ANEXO C1 (Same 26)

Back-up Data

Naran Projeto : JCT AITUTO - SAM E- BETANO 23KM (A04)

No. kontratu : MPW-W-220007

Data Inspesaun : 18/ 07 /2022


Fatin Inspesaun : Aituto / Same

Koordinadas : Start Point : Latetude -8,9998699S, Long: 125.654606E


End Point : Latetude: 8.99180S , Long: 125.91715E

Naran Inspector : 1. Romulo J.M.Henrique

Sketch & Foto Desenho

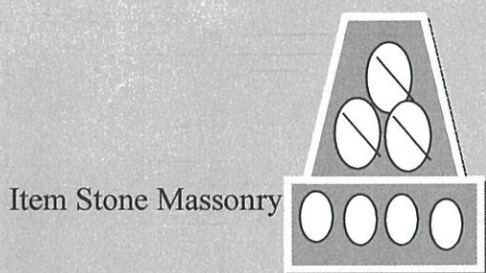

Observasaun iha tereno no Foto Aktual

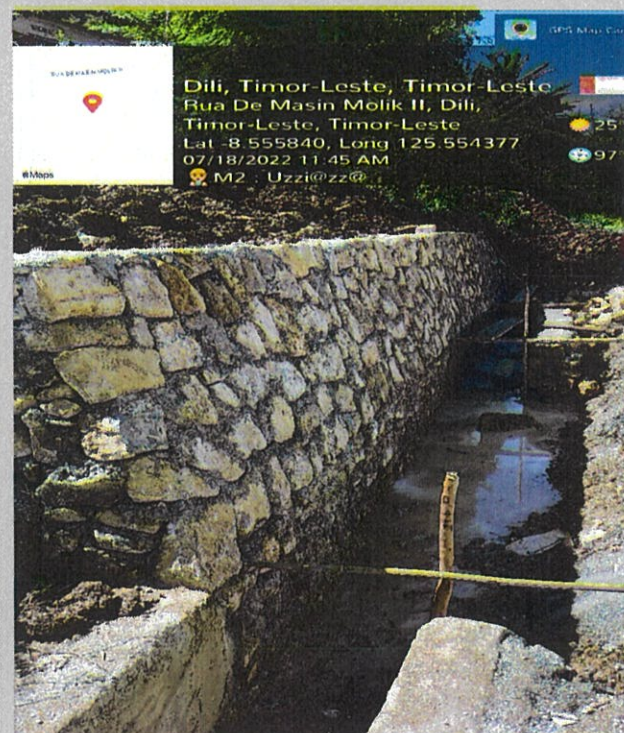



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL




ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público


ANEXO C1 (Same 26) Back-up Data

Sketch & Foto Desenho

Item Guard Drill



Observasaun iha tereno no Foto Aktual

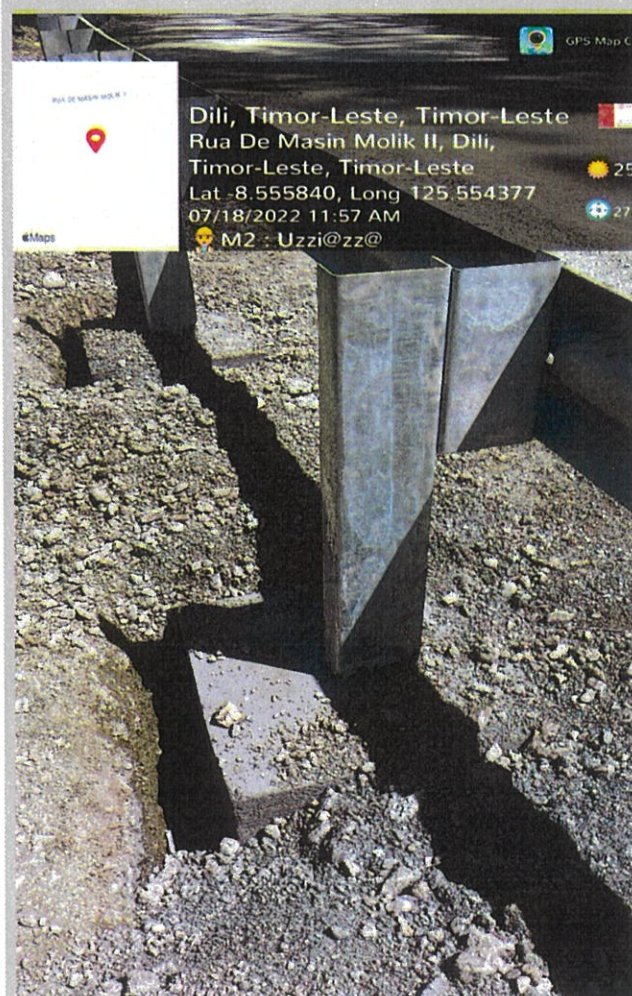



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

CONTRACT NO. : MPW-W-220007
CONTRACT NAME : ROAD MAINTENANCE SECTIONS : JCT AITUTO - SAM E- BETANO 23KM (A04) MANUFAHI MUNICIPALITY
CONTRACTOR NAME : BEMOS,1 UNIPessoal LDA.
CERTIFICATE NO. : PAYMENT NO 01 (1ST PAYMENT)
PERIOD COVERED : UP TO JUNE 2022

ANEXO C2		ADN Progress							
		BILLED QUANTITY		BILLED AMOUNT \$		Observasaun			
NO. PAY ITEM	ITEM DESCRIPTION	Original Contract cost (\$)	Previous Billing Amount (\$)	%	This Billing Amount (\$)	%	To Date Amount (\$)	%	
100	GENERAL	\$ 5,000.00			\$ 2,500.00	1.90%	\$ 2,500.00	1.90%	
200	EARTWORK	\$ 24,018.00			\$ 14,291.16	10.84%	\$ 14,291.16	10.84%	
500	BRIDGE CONTRUCTION	\$ 5,100.00			\$ 5,100.00	3.87%	\$ 5,100.00	3.87%	
600	DRAINAGE & SLOPE PROTECTION STR.	\$ 39,888.96			\$ 26,596.70	20.17%	\$ 26,596.70	20.17%	
700	MISCELLANEOUS STRUCTURES	\$ 40,500.00			\$ 40,500.00	30.71%	\$ 40,500.00	30.71%	
Total		\$ 114,506.96			\$ 88,987.86	67.47%	\$ 88,987.86	67.47%	
Provit (10%)		\$ 11,450.70			\$ 8,898.79	6.75%	\$ 8,898.79	6.75%	
Overhead		\$ 3,350.00			\$ 2,603.42	1.97%	\$ 2,603.42	1.97%	
Tax (2%)		\$ 2,586.15			\$ 2,009.80	1.52%	\$ 2,009.80	1.52%	
Grand Total		\$ 131,893.81			\$ 102,499.86	77.71%	\$ 102,499.86	77.71%	

Prepared by :

Eng. Romulo J.M. Henrique
Enginheiro ba Projecto Infraestrutura transportes e
Irrigasaun Munisipio Manufahi A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos
Enginheiro Senior Projecto Infraestrutura transportes e
Irrigasaun A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao qualidade
ADN IP



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 9)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 6+000 - 9 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210098

Data Inspesaun : 19/07/2022

Fatin Inspesaun : Fatuberliu / Caicasa


Koordinadas :

Start Point : Latetude: 9.01163S, Long: 125.92485E


End Point : Latetude: 8.83956S, Long: 125.63432E

Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

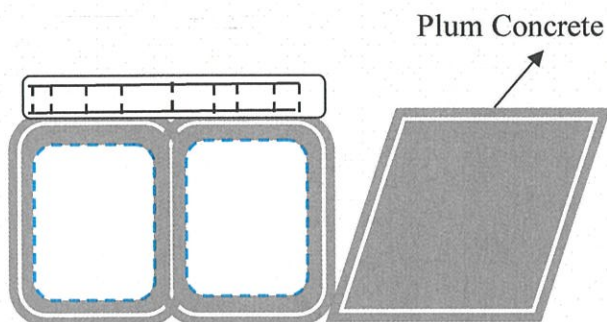

Observasaun iha tereno no Foto Aktual

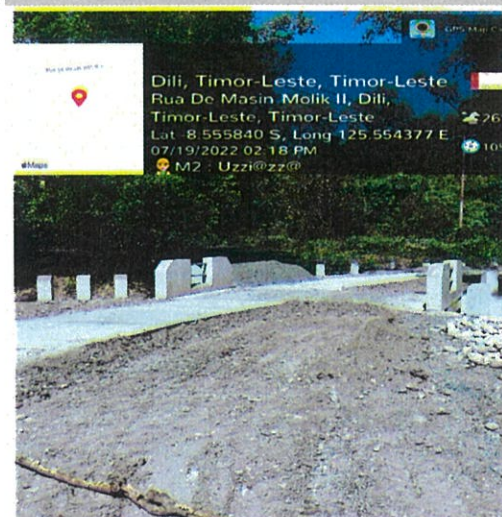

Sketch & Foto Desenh Box Culvert 2

Observasaun iha tereno no Foto Aktual



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

Name of the Road: Calcaia - Fatu Cahli, Cha. 6+000 - 9+000
Contract No. : MPW-W-210098
Contractor: Manufahi Lui Unip. Lda.

ANEXO C2

Pay ITEM NO.		DESCRIPTION	ORIGINAL CONTRAC		ADN Progress						Obs
			Cost (\$)	BILLED QUANTITY		BILLED AMOUNT \$					
				Previous Billing		This Billing		To date			
				COST (\$)	%	COST (\$)	%	COST (\$)	%		
	R-01. General		\$ 4,260.00	\$ 2,990.00	0.73%	\$ -	0.00%	\$ 2,990.00	0.73%		
	R-03 Earth work		\$ 23,849.57	\$ 31,654.91	7.74%	\$ 81.12	0.02%	\$ 31,736.03	7.76%		
	R-05 Granular sub- base and		\$ 7,871.18	\$ 13,306.77	3.25%	\$ 1,216.80	0.30%	\$ 14,523.57	3.55%		
	R-08 Structure		\$ 296,194.69	\$ 273,732.58	66.96%	\$ 3,996.60	0.98%	\$ 277,729.18	67.93%		
	R-10 Dayworks		\$ 350.00	\$ 350.00	0.09%	\$ -	0.00%	\$ 350.00	0.09%		
	R-11 Routine maintenance		\$ 7,129.60	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%		
	R-15 Provisional Sum		\$ 1,500.00	\$ 10,500.00	2.57%	\$ -	0.00%	\$ 10,500.00	2.57%		
	Total of R-Item		\$ 341,155.03	\$ 323,534.26	0.79	\$ 5,294.52	1.30%	\$ 328,828.78	80.43%		
	G-01 Security		\$ 1,518.00	\$ 1,644.50	0.40%	\$ -	0.00%	\$ 1,644.50	0.40%		
	G-02 Project Item		\$ 15,774.00	\$ 19,723.00	4.82%	\$ -	0.00%	\$ 19,723.00	4.82%		
	G-03 Safety and Protection		\$ 7,988.20	\$ 10,338.80	2.53%	\$ -	0.00%	\$ 10,338.80	2.53%		
	G-06 eremonal		\$ 250.00	\$ 125.00	0.03%	\$ -	0.00%	\$ 125.00	0.03%		
	Total of G-Item		\$ 25,530.20	\$ 31,831.30	7.79%	\$ -	0.00%	\$ 31,831.30	7.79%		
	A.Total - net cost		\$ 341,155.03	\$ 323,534.26	79.14%	\$ 5,294.52	1.30%	\$ 328,828.78	80.43%		
	B Contractor's Profit (net cost x %) ; 10%		\$ 34,115.50	\$ 32,353.43	7.91%	\$ 529.45	0.13%	\$ 32,882.88	8.04%		
	C General item		\$ 25,530.20	\$ 31,831.30	7.79%	\$ -	0.00%	\$ 31,831.30	7.79%		
	D Tax ((net cost + profit+ Over head) x 2 %)		\$ 8,016.01	\$ 7,754.38	1.90%	\$ 116.48	0.03%	\$ 7,870.86	1.93%		
	E. Total Evaluated price		\$ 408,816.75	\$ 395,473.37	96.74%	\$ 5,940.45	1.45%	\$ 401,413.82	98.19%		

Prepared by :

Eng. Romulo J.M.Henrique

Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Manufahi A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos

Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D
N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas

Coordenadora da Unidade de controlo e validacao qualidade
ADN IP



ΣΑΔΝ, Ι.Ρ.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXOD (FTB9)

Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Cha. 6+000 - 9 + 000 , Manufahi Municipality

Kompanha : Manufahi Lui Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No
I	19/7/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Municipio Manufahi	1 2 3 4 5
II					1 2 3 4 5
III					1 2 3 4 5
IV					1 2 3 4 5
V					1 2 3 4 5



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 6)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 0+000 - 6 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210099

Data Inspesaun : 19/07/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :


Start Point : Latetude 9.01605S, Long: 125.92783E

EndPoint: Latetude: 8.83956S , Long: 125.63432E


Naran Inspector : 1. Romulo J.M.henrique

Sketch & Foto Desenho

Plum Concrete



Observasaun iha tereno no Foto Aktual

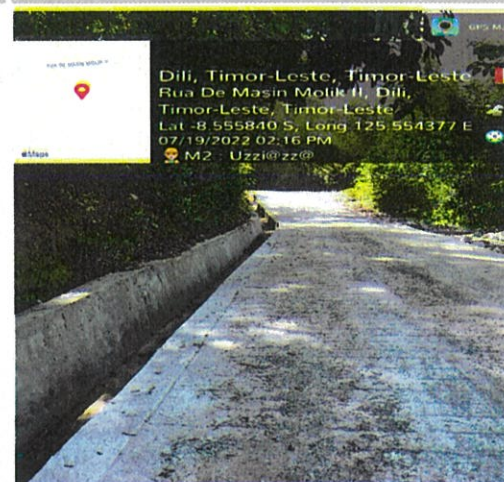

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

Name of the Road : Caicasa - Fatucali, 0 + 000 - 6 + 000											
Contract No : MPW - W - 210099											
Contractor : Loskabubu Unipessoal Lda											
Pay ITEM NO.	DESCRIPTION	ORIGINAL CONTRAC		BILLED QUANTITY		This Billing		BILLED AMOUNT \$		ADN Progress	
		Cost (\$)		Previous Billing							
				COST (\$)	%	COST (\$)	%	COST (\$)	%		Obs
R-01. General		\$ 4,520.00		1905.00	0.57%	\$ -	0.00%	\$ 1,905.00	0.57%		
R-03 Earth work		\$ 54,159.21		11,129.82	3.30%	\$ -	0.00%	\$ 11,129.82	3.30%		
R-05 Granular sub- base and		\$ 55,087.20		50,543.82	14.99%	\$ 50,543.82	14.99%	\$ 101,087.64	29.99%		
R-08 Structure		\$ 157,702.29		173,145.85	51.36%	\$ 12,070.15	3.58%	\$ 185,216.00	54.94%		
R-10 Dayworks		\$ 350.00		84.00	0.02%	\$ -	0.00%	\$ 84.00	0.02%		
R-11 Routine maintenance		\$ 8,361.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
R-15 Provisional Sum		\$ 1,500.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
Total of R-Item		\$ 281,679.71		236,808.49	70.25%	\$ 62,613.97	18.57%	\$ 299,422.46	88.82%		
G-01 Security		\$ 1,380.00		\$ -	0.00%	\$ -	0.00%	\$ -	0.00%		
G-02 Project Item		\$ 12,540.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
G-03 Safety and Protection		\$ 6,488.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
G-06 eremonal		\$ 250.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
Total of G-Item		\$ 20,658.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
A.Total - net cost		\$ 281,679.71		236,808.49	70.25%	\$ 62,613.97	18.57%	\$ 299,422.46	88.82%		
B Contractor's Profit (net cost x %); 10%		\$ 28,167.97		23,680.85	7.02%	\$ 6,261.40	1.86%	\$ 29,942.25	8.88%		
C General item		\$ 20,658.00		-	0.00%	\$ -	0.00%	\$ -	0.00%		
D Tax ((net cost + profit+ Over head) x 2 %)		\$ 6,610.11		5,209.79	1.55%	\$ 1,377.51	0.41%	\$ 6,587.29	1.95%		
E. Total Evaluated price		\$ 337,115.79		265,699.12	78.82%	\$ 70,252.87	20.84%	\$ 335,951.99	99.65%		

Prepared by :

Verified by :

Certified by :

[Signature]

Eng. Romulo J.M.Henrique
Engenheiro ba Projecto Infraestrutura Transportes e Irrigasaun
Munisipio Manufahi A D N IP

[Signature]

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D
N IP

[Signature]

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlo e validacao qualidade
ADN IP



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

ANEXO D (FTB 6)

Naran projeto :R4D Rural Road Spot Improvement Betano - Loro Chainage
0+000-6+000, Manufahi Municipality

Kompanha : Loskabubu Unip Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	19/7/2022	Manufahi / Same	Romulo J.M Henrique	Enginheiro A D N IP Município Manufahi	1	buku tamu e eng iha terreno laiha	
					2		
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		



ANEXO C1 (FTB 8)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Cha. 9+000 - 12 + 000 ,
Manufahi Municipality

No. kontratu : MPW - W - 210097

Data Inspesaun : 27/ 07 /2022

Fatin Inspesaun : Fatuberliu / Caicasa


Koordinadas : Start Point : Latetude -8,9998699S, Long: 125.654606E

End Point : Latetude: 8.99180S , Long: 125.91715E


Naran Inspector : 1. Romulo J.M.Henrique

Sketch & Foto Desenho

Lean concrete & Plum concrete



Observasaun iha tereno no Foto Aktual

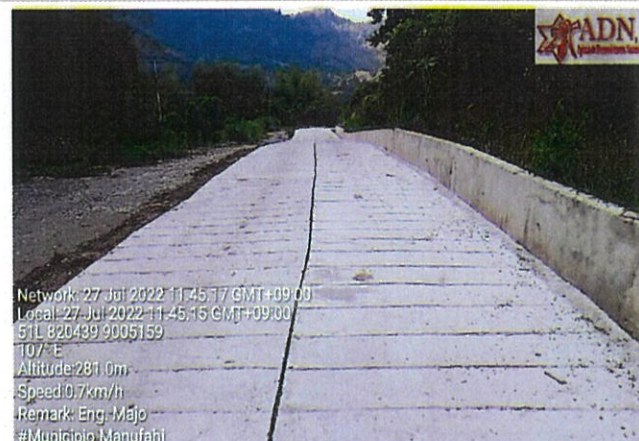

Network: 27 Jul 2022 11:45:17 GMT+09:00
Local: 27 Jul 2022 11:45:15 GMT+09:00
GIL 820439 9005159
107° E
Altitude: 281.0m
Speed: 0.7km/h
Remark: Eng. Mejo
#Município Manufahi



ΣΑΔΝ, Ι.Ρ.

Agência de
Desenvolvimento
Nacional, Instituto Público

Certified by:

Verified by :

Certified by :

Eng. Romulo J.M.Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Manufahi A D N IP

Eng. Remigio da C.S.dos Santos

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controle e validacao qualidade
ADN IP



ΣΤΑΔΙΟΝ, Ι.Π.

Agência de
Desenvolvimento
Nacional, Instituto Público

Kompanha : Alifa Unip,Lda



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C1 (FTB 7)

Back-up Data

Naran Projeto : Rural Road Spot Improvement Caicasa Fatucahi Sp Satu Cha. 0+000 - 7
+ 900 , Manufahi Municipality

No. kontratu : MPW - W - 210095

Data Inspesaun : 27/07/2022

Fatin Inspesaun : Fatuberliu / Caicasa

Koordinadas :

Start Point : Latetude : 9.03677S, Long: 125.99846E

EndPoint: Latetude : 9.05708S, Long: 125.02474E

Naran Inspector : 1. Romulo J.M.Henrique

Sketch & Foto Desenho

Gravel



Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



Agência de
Desenvolvimento
Nacional, Instituto Público

Name of the Road : Catcaca - Faucahi Sp Satu , 0 + 000 - 7 + 900
Contract No : MPW - W - 210095
Contractor : Leo - Hilin Unipessoal Lda

ANEXO C1

Contractor : Leo - Hini Unipessoal Lda			ADN Progress						
Pay ITEM NO.	DESCRIPTION	ORIGINAL CONTRAC	BILLED QUANTITY		BILLED AMOUNT \$		To date		Obs
			Previous Billing		This Billing				
		Cost (\$)	COST (\$)	%	COST (\$)	%	COST (\$)	%	
R-01. General		\$ 2,200.00	950.00	0.77%	\$ 200.00	0.16%	\$ 1,150.00	0.93%	
R-03 Earth work		\$ 13,593.30	3,322.27	2.68%	\$ 330.33	0.27%	\$ 3,652.60	2.94%	
R-05 Granular sub- base and		\$ 25,544.92	-	0.00%	\$ 22,594.27	18.21%	\$ 22,594.27	18.21%	
R-08 Structure		\$ 42,809.20	25,757.77	20.77%	\$ 9,167.90	7.39%	\$ 34,925.67	28.16%	
R-10 Dayworks		\$ 700.00	175.00	0.14%	\$ -	0.00%	\$ 175.00	0.14%	
R-11 Routine maintenance		\$ 15,873.60	2,084.00	1.68%	\$ 7,224.50	5.82%	\$ 9,308.50	7.50%	
R-15 Provisional Sum		\$ 1,000.00	-	0.00%	\$ -	0.00%	\$ -	0.00%	
	Total of R-Item	\$ 101,721.02	32,289.04	26.03%	\$ 39,517.00	31.86%	\$ 71,806.04	57.89%	
G-01 Security		\$ 1,800.00	600	0.48%	\$ 900.00	0.73%	\$ 1,500.00	1.21%	
G-02 Project Item		\$ 5,304.00	1,764.00	1.42%	\$ 2,814.00	2.27%	\$ 4,578.00	3.69%	
G-03 Safety and Protection		\$ 2,014.00	1,854.00	1.49%	\$ 120.00	0.10%	\$ 1,974.00	1.59%	
G-06 eremonal		\$ 600.00	300.00	0.24%	\$ -	0.00%	\$ 300.00	0.24%	
	Total of G-Item	\$ 9,718.00	4,518.00	3.64%	\$ 3,834.00	3.09%	\$ 8,352.00	6.73%	
	A.Total - net cost	\$ 101,721.02	32,289.04	26.03%	\$ 39,517.00	31.86%	\$ 71,806.04	57.89%	
B	Contractor's Profit (net cost x %) ; 10%	\$ 10,172.10	3,228.90	2.60%	\$ 3,951.70	3.19%	\$ 7,180.60	5.79%	
C	General item	\$ 9,718.00	4,518.00	3.64%	\$ 3,834.00	3.09%	\$ 8,352.00	6.73%	
D	Tax ((net cost + profit+ Over head) x 2 %)	\$ 2,432.22	800.72	0.65%	\$ 946.05	0.76%	\$ 1,746.77	1.41%	
	E. Total Evaluated price	\$ 124,043.34	40,836.66	32.92%	\$ 48,248.76	38.90%	\$ 89,085.42	71.82%	

Prepared by :

Verified by :

Certified by :

Eng. Romulo J.M.Henrique
Engenheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Manufahi A D N IP

Eng. Remigio da C.S.dos Santos
Engenheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D
N IP

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao qualidade
ADN IP



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXOD (FTB 7)

**Naran projeto :Rural Road Spot Improvement Caicasa Fatucahi Sp Satu Cha.
0+000 - 7 + 900 , Manufahi Municipality**

Kompanha : Leo Hilin Unip,Lda



MINISTÉRIO DO PLANO E ORDENAMENTO VI - GOVERNO CONSTITUCIONAL ADN, LP Agência de Apoio Desenvolvimento Nacional - Serviços Públicos							PLANU INSPESAUN																															
Naran Eng. Munisipiu		Romulo J.M.Henrique					2022																															
		MANUFAHI					JULHO																															
Postu	No	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	Action	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	OBSERVASAUN		
								4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31			
ALAS (ALS)	1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	MINISTERIO DAS OBRAS PUBLICAS	FI	Samboio Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119																																
	2	Emergency proposed for the new construction of bridge box protection with retaining wall in Area Wee Kakau Oun 2	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Nacional Manufahi Lda	SSS/148/MOPTC-2017	Plan																													PARADO		
	3	Emergency new construction of gabion box protection random fill in area Lacio, Baria Laran, Uma Berlok, Alas	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio 1912 MF Lda	SSS/279/MOPTC-2016	Plan																													PROJERU REMATA ONA		
							Actual																															
	4	Rural Roads Routine Maintenance Dootie Weberet, Chainage 0+000 - 6+300, Dootie Wekakaon, Chainage 0+000 - 8+600, Tukunu Feriksare, Chainage 0+000 - 4+300 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Samboio Unip,Lda	MPW-RFQ-190017	Plan																												PARADO			
	5	Prefurasau Be'e mos iha Suku Uma Berlok, Aldeia Besusu	MINISTERIO DAS OBRAS PUBLICAS	LM	Buka Fini	MPWTC-NCB-170008	Plan																															
							Plan																															
							Actual																															
	6	Konstrusaun Barreira 300m no Normalizasaun 400 m Mota Clere	MINISTERIO DAS OBRAS PUBLICAS	PDIM	Aplayana unip. Lda	16/PDIM/M-MF/IX/2019	Plan																													PARADO		
	7	Kontinuasaun Kanalizasaun Kanu Transmisuun no Distribuisuun Hosi Bomba Uma Berlok ba to Dotie, Posto Administrativo Alas, Munisipiu Manufahi/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM	Tane Unipessoal Lda	MOP - W - 190210	Plan																															
	8	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 6 : Alas - Wedaurek	MINISTERIO DAS OBRAS PUBLICAS	LM	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	MPW-CS-2000033	Actual																															
							Plan																															
	9	Construction and Installation water Gravitation System in Mahaquidam Umberko Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Verescar Unip. Lda	SSS/289/MOPTC-2016	Plan																															
10	Rural Roads Rehabilitation Feriksare Chainage 4+300 - 6+350 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	My Friend Unip. Lda	MPW-W-190106	Plan																														FHO		
						Actual																																
11	Rehabilitasaun Estrada Tekunu-Feriksare 2 Sta. 2+500-4+250-Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/062/MOPTC-2016	Plan																														PARADO		
						Actual																																
12	New construction of bridge with retaining wall in area we bikas	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Unimafa Lda	SSS/150/MOPTC-2017	Plan																														PARADO		
						Actual																																
13	R4D Rural Road Routine Maintenance, Dotie - Weberet Chainage 0+000 - 6+300 and Dotie - Wekakaon Chainage 0+000 - 8+600 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Wererek Unipessoal Lda	MPW-W-210093	Plan																													parado hela laih aktividade			
						Actual																																
FATUBERLIU (FTB)	1	Emergency proposed for the new cons of bridge, Gabions & retaining wall in Area Fatuk Mutin	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Fatuleda Lda	SSS/151/MOPTC-2017	Plan																													PARADO		
							Actual																															
	2	Emergency proposed for new construction of bridge, gabions box protection with retaining wall in area Beao, Fatu Beai	MINISTERIO DAS OBRAS PUBLICAS	FI	concorcio Nasional ba Futuro	SSS/149/MOPTC-2017	Plan																												PARADO			
							Actual																															
	3	New Installation MV, LV Line and House Connection from Tatekar to Kledik, Kirantetuk, Fukiran and Fatuberliu-Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Funa Kolik Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000424																																
	4	New Construction of Sukaei Oan River cyclop Concrete Retaining Wall and Gabion	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Nacional Samdil, Lda (CNS)	SSS/102/MOPTC-2017	Plan																												parado hela aktividade laih			
							Actual																															
	5	R4D Rural Road Routine Maintenance, Tukununu Feriksare Chainage 0+000-6+350 Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MARDIROMIG VIQSAM, UNIPESOA Lda	MPW- W - 210096	Plan																												parado hela aktividade laih			
							Actual																															
	6	R4D RURAL ROAD SPOT IMPROVEMENT CAICASA - FATUCAHI CHAINAGE 0+000-6+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Loskabubu	MPW-W-210099	Plan																													ON-GOING		
							Actual																															
	7	R4D Rural Road Spot Improvement Caicasa - Fatucahi SP SATU Chainage 0+000 - 7+900 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Leo-Hilan Unipessoal Lda	MPW-W-210095	Plan																													ON-GOING		
							Actual																															
8	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 0+000 - 6+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alifa Pereira	MPW-W-210097	Plan																													ON-GOING			
						Actual																																
9	R4D Rural Road Spot Improvement Caicasa - Fatucahi Chainage 6+000 - 9+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Manu-Fahi Lui Unipessoal Lda	MPW-W210098	Plan																													ON-GOING			
						Actual																																
10	New construction of tower Protection Wall no 92 Section Betano - Viqueque manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM	My friend Constr. Unip. Lda	NCB/ 028/MOP- 2020	Plan																													parado to agora tanha amandamen contratu husi owner sidauk lha			
						Actual																																
1	New installatio of feeder 2 MV and LV line in Casa, Betano - Manufahi District		FI	Dhalelan,Unip.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000300																																	
2	New Installation of MV, LV Line and House Connection from Tugu Betano to Otorita, Trans Pemuda, Tani and Sesurai - Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Dediva Electrical Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000385	Plan																																
3	New Installation Mv, Lv Line & House Connection From Holarua to Datina, Carbulau, Erlak, Lusak, Adok Laran Turon - Manufahi district	MINISTERIO DAS OBRAS PUBLICAS	FI	Fahlia Humalo Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000430																																	
4	Konstrusaun kanalizasaun bee mos iha selhasan suco Betano, Posto Adm Same, Munisipiu Manufahi /162	MINISTERIO DAS OBRAS PUBLICAS	LM	Haksotok Java Motor Unip Lda	MOP - W - 190160	Plan																																
5	Nova fornecimento água do Bairro PNTE, Manufahi	MINISTERIO DO INTERIOR	FI	Tom's Building Unipessoal Lda	SSS/053/MI-2017	Actual																																
6	Emergency proposed for the New construction of drain channel with pipe culvert in area Lalika, Betano, Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Consortio Cablaki Oan Lda	SSS/270/MOPTC-2016	Plan																													PARADO			
						Actual																																
7	Construção Ponte e rio de Kaboska at Bemetan, Betano, Same Sub District, Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	Monte Sul Unip.Lda	SSS/102/MOPTC-2016	Plan																													PARADO			
						Actual																																

MINISTERIO DO PLANO E ORDENAMENTO ADN, IP Agência de Regulação e Supervisão Reguladora Nacional da Energia Elétrica							PLANU INSPESAUN																											
Naran Eng.							Romulo J.M.Henrique																											
Munisipiu							MANUFAHI																											
							2022																											
SAME (SAME)							JULHO																											
	8	Periodic Maintenance Same - Kamilaran - Ailuli - Rotutu Sta. 0+000-12+ 000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	El Const Unip. Lda	NCB/063/MOFTC-2016	Plan																							FHO				
							Actual																											
	9	Manutensaun Estrada Manico-Lianai-Grotu Sta. 0+000-10+ 550- no Manutensaun Estrada Ladiki Sta. 0+000-1+ 200 Municipal of Same	MINISTERIO DAS OBRAS PUBLICAS	FI	Aplayana unip. Lda	RT/057/MOFTC-2016	Plan																								PARADO			
							Actual																											
	10	Road Maintenance Section Same Urban Roads Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM	Renova Unip Lda	MPW - W - 190215	Plan																								PARADO			
							Actual																											
	11	Routine Road Maintenance Same - Betano - Dilor - (A05, A14) / 76,4 km Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Quintas das Flores, Lda	MPW - W - 190123	Plan																								FHO			
							Actual																											
	12	Rural Roads Maintenance Manico - Gruto, Chainage 0+000 - 11+200 km Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Alifa Pereira	MPW -RFQ 190019	Plan																								PARADO			
							Actual																											
	13	Rural Roads Maintenance Same - Rotuto Chainage 1+700 - 12+000 and Ladaki Chainage 0+000 - 1+200 Municipality Manufahi (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Leo - Dok	MPWTC-CD-170002	Plan																								PARADO			
							Actual																											
	14	Fencing for Construction Monument of Dom Boa Ventura	MINISTERIO TURISMO COMERCIO E INDUSTRIA	LM	Lonkabubu	RDTL/06/GM-MTAC/IV/2016	Plan																											
							Actual																											
	15	Konstrusaun Tangki Beé no Menara Beé ba iha Edifício Administrasaun Municipiu Manufahi	ESTATAL	PDIM	Cold Lixi Unip. Lda	05/PDIM/M-MF/IV/2017	Plan																											
							Actual																											
	16	Konstrusaun Kuartel Bombeiros iha Same-Manufahi	MINISTERIO DO INTERIOR	PDIM	Mamber Unip. Lda	02/PDIM/M-MF/VIII/2016	Plan																											
							Actual																											
	17	Rehabilitasaun Igreja Paroquia Nossa Senhora Assuncao Same	ESTATAL	PDIM	Dani Star Unip. Lda	011/PDIM/M-MF/VIII/2017	Plan																											
							Actual																											
	18	Konstrusaun Landscape Igreja Nossa Senhor Assunção Same	ESTATAL	PDIM	Consortio Deatle Hare ba On Lda	07/PDIM/M-MF/IX/2019	Plan																											
							Actual																											
	19	Konstrusaun Pagar Keliling Stadion Ailuli (Same-Manufahi)-Tutor Bodik Tane Liank, Unip.Lda	ESTATAL	PDIM	Tutor Bodik Tane Liank, Unip.Lda	09/PDIM/M-MF/X/2019	Plan																											
							Actual																											
	20	Konstrusaun Fatm isolamentu iha Municipio Manufahi, Timor Leste	MINISTERIO DA SAUDE	LM/CoVID	Daloveya	RDTL-MS-DNA-DC-20-256	Plan																											
							Actual																											
	21	R4D Rural Road Routine Maintenance, Manico - Lianai - Grotu Chainage 0+000 - 11+200 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Haut-Dairam Unipessoal Lda	MPW-W210092	Plan																									PARADO HELA		
							Actual																											
	22	R4D Rural Road Routine Maintenance, Ladaki Chainage 0+000 - 1+200, Same - Rotuto Chainage 0+000 - 12+000 Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Riabile Unipessoal Lda	MPW-W-210091	Plan																									PARADO HELA		
							Actual																											
	23	New Construction of Laboratory ih CSI Liank,Manufahi relatona ba covid19 at Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	Kartini Unipessoal Lda	RDTL-MS-DNA-3CB-21-072	Plan																											
							Actual																											
	24	PARA A CONSTRUCCAO DE JARDIM DE HERÓIS DE MANUFAHI (New Construction of Campes, Gate and Leveling)	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	My friend Constr. Unip. Lda	RFQ No. 23/MACLN/DNAL/VI/2021	Plan																											
							Actual																											
	25	R4D Rural Road Spot Improvement Betano - Loro Chainage 0+000-6+300	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Tutor Bodik Tane Liank, Unip.Lda	MPW - W -210094	Plan																									PARADO HELA		
							Actual																											
	26	For Road Maintenance Section Jet Aituto - Same - Betano 23 km (A04) Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM	Bemos I Construction , Unip Lda	MOP/CD/NCB/21054	Plan																									ON-GOING		
						Actual																												
TURISCAI (TRS)	1	Open New Road Turiscail - Mota Belihun Maubere, Turiscail - Liquidoe Stage 1 (Sta. 0+000 - 7+050) Municipality Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	Aldepo Murak Unip.Lda	SSS/250/MOFTC-2016	Plan																								PROGRES FISIKO REMATA ONA HEIN PAGAMENTO			
							Actual																											
	2	Const. MCK (Saude) Orana	ESTATAL	PDIM	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	Plan																											
							Actual																											
	3	For Preparation of Detail Engineering Design and Building Document Preparation for New Bridges in 2019 Suco Liurai, Maubara - 1 Bera Railsoo, Sanfak, Tutu Luro - Same Fahi Nehan (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	Lelo Engineering Unip. Lda JV PT. Multi Karadiga Jasa & PT. Cipta Design Indonesia	MPW-CS-2000032	Plan																											
4	Construction and Installation of Water Gravitation System for Multy Village (Manumera, Caimauk and Orana) Manufahi Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Terra Livre Unip. Lda	SSS/299/MOFTC-2016	Plan																												
						Actual																												
5	Balate to Uriuli Cha, Sta. 0 + 000 - 2 + 500	MINISTERIO DAS OBRAS PUBLICAS	LM	Daloveya Construction Unip. Lda		Plan																									ON-GOING			
						Actual																												

Note:

Planu Periode Inspesaun iha Terenu

Implementa Planu Periode Inspesaun iha Terenu

Relatorio Mensal iha Dili

Inspesaun Proceso Pagamento

Prepara Husi :



(Eng. Romulo J.M. Henrique)

Engenheiro ADN IP Manufahi

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)

Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN IP

Aprova Husi :



(Eng. Januario Maia Dutres)

Adjunto Director Executivo ADN IP

2022

Naran Eng.	Silvino Domingos Rita Rebelo Soares						2022																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
Municipio	MUNICIPIO MANUFAHI NO POSTOS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	Action	JULHO																															OBS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
ALAS (ALS)	1	New Installation MV,Line Transformer and LV Line from Dotik to Alas Manufahi District	Sambolo Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000119	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público							PLANU INSPESAUN																																
Naran Eng.	Silvino Domingos Rita Rebelo Soares						2022																																
Município	MUNICIPIO MANUFAHI NO POSTOS																																						
Município / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	Action	JULHO																															OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
TURISCAI (TRS)	35	Konstrusaun ka rehabilitasaun ba EBC simpang Tiga	MEJD PKRIE EBC SIMPANG TIGA	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	36	Konstrusaun ka rehabilitasaun ba ESTV Halibur Befano	MEJD PKRIE ESTV HALIBUR BETANO	Kontratu ho Grupo Comunitariu	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
TURISCAI (TRS)	2	Const. MCK (Saude) Orana	Gerasaun Malikau Unip. Lda	01/PDIM/M-MF/V/2019	PDIM	ESTATAL	Plan																																
							Actual																																
TOTAL PROJETO ON-GOING																																							

Note:

Planu Periode inspesaun iha tereinu

Implementa Planu Periode Inspensaun

Relatoriu avaliasuan mensal iha Dili

Inspesaun Prosesu Pagamentu

Prepara Husi :

(Silvino D. R. Rebelo Soares)
Eng. Electricidade, ADN - I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ,ADN -

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo,ADN - I.P
