



REPÚBLICA DEMOCRÁTICA DE TIMOR-LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL **IMPLEMENTASAUN PROJETUS** **MUNISÍPIU MANATUTO**

FEBEREIRU 2023




SUMÁRIO
RELATÓRIO
IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICIPIO
MANATUTO
FEBREIRO 2023

Prepara Hui :



(Eng. Quico Adelino Junior)
Eng. do Projecto Edifício Público Beé no
Saneamento Município Manatuto, ADN, I.P



(Eng. Jose R. Carlos Gusmão)
Eng. do Projecto Infraestrutura e
Irrigação Município Manatuto, ADN, I.P



(Eng. Adonis Julio Fernandes)
Eng. do Projecto ME, ADN, I.P




(Eng. Domingos da Costa e Silva)
Eng. do Projecto Infraestrutura e
Irrigação Município Manatuto, ADN, I.P

Verifika Husi :



(Arc. Fransisco X D D Jeronimo)

**Eng. Senior ba Edificio Publiku no Beé
Saneamentu, ADN, I.P**



(Eng. Remigio da C. S. dos Santos)

**Eng. Senior ba Projetu Infraestrutura e
Irigasaun, ADN, I.P**



(Eng. Deolindo de F. Marques)

Chefe Seksaun ba Projetu M.E & ITC, ADN, I.P

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)

**Coordenadora Unidade de Controlo e Validação de Qualidade,
ADN, I.P**

Aprova Husi :



(Mariano Renato Monteiro da Cruz, S. T. M. Eng)

Director Executivo, ADN, I.P



INDICE

SUMÁRIO	1
INDICE	3
I. INTRODUSAUN	3
1.1 Enkuadramentu Legal.....	3
1.2 Perfil Municipio Manatuto.....	3
1.3. Lista Projectos.....	7
II. PROGRESU FISIKU	25
2.1 Progreso Fisiku Kada Fulan.....	25
III. OBSTÁCLO IHA TERENU	26
3.1 Obstáculo Servisu Iha Terenu	26
IV. REKOMENDASAUN IHA TERENU	27
4.1 Rekomendasaun Servisu Iha Terenu	27

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias	4
Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Manatuto.....	4
Tabela 1.2 : Lista Asset ADN,I.P Municipio Manatuto	6
Tabela 1.3.1 : Projecto Municipio Manatuto Por Fundus Finansiamentos	7
Tabela 1.3.2 : Projecto Municipio Manatuto Por Sectores.....	11
Tabela 1.3.3 : Projecto Municipio Manatuto Por Ministerio.....	18
Tabela 1.4 : Dadus Populasaun Munisipiu Manatuto	25

I . INTRODUSAUN.

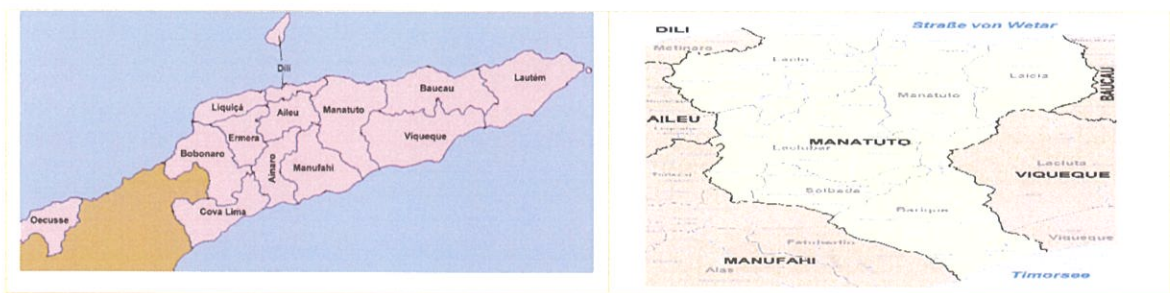
1.1.Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho qualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefisiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizasaun no sertifikasaun qualidade ba projetu sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liuhusi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria

1.2. Perfil Municipio Manatuto



Mapa 2 hatudu pozisaun jeográfika Administrasaun Munisipal Manatuto iha luan 1,706 km² ho populasaun nain 42,742 tuir Sensus 2010. Administrasaun Munisipal Manatutoiha Postos Administrativos nen (6), Sukus 29 no aldeias 99 , mak hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos, Sucos no Aldeias.

Natarbora		Laclo		Laklubar		Laleia	
Sukus	Aldeia	Sukus	Aldei	Suku	Aldeia	Sukus	Aldeias
Aubeon	2	Hohorai	4	Batara	4	Cairui	7
Barique	2	Locomesak	5	Hatu ma quere k	3	Hatulara n	3
Fatuwaque	2	Uma kaduak	3	Funar	4	Lifau	3
Manehat	3	Uma naruk	4	Mane lima	6		
Uma Boco	2			-	8		
				Sanan a Na'i	4		
Total	11		18		30		13

Data husi: Livro 3 B OJE 2021, pag 69

Manatuto		Soibada	
sukus	Aldeia	sukus	aldeias
Ailili	2	Fatuma querek	2
Aitekas	4	Leo-hat	2
Cribas	5	Manlala	2
Iliheu	5	Maun Fahe	2
Ma'abat	2	Somoro	2
Sau	2		
	22		10

Tabela 1.1: Forca de Trabalho ADN, I.P Municipio Manatuto

Forca de Trabalho ADN,I.P Municipio Manututu								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	3	3	3			3	
2	Administrasau n no Financas	0	0	0			0	
3	Motorista	1	1	1			1	
4	Seguransa	0	0	0			0	
Total		4					4	

Tabela 1.2 : Lista Asset ADN,I.P Municipio Manatuto.

ASET ADN,IP MUNICIPIO MANATUTO								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1	1	1				
2	Kareta	1	1	1				
3	Desktop HP / Monitor	1	1	1				
4	Laptop HP	1	1	1				
5	Printer Cannon	1	1	1				
6	UPS	1	1	1				Aát ona
7	Armario File	2	2	2				
8	Armario Tau hena	3	3	3				
9	Meja escritorio	1	1	1				
10	Meja han	1	1	1				
11	Meja TV (kiik)	1	1	1				
12	Kadeira escritorio	6	6	6				
13	Kadeira han	4	4	4				
14	Sofa	1 Set	1 Set	1 Set				
15	Springbed +sumasu 4+sprei 3	3 Set	3 Set	3 Set				
16	Jeleira	1	1	1				Aát ona
17	Water Dispenser	1	1	1				
18	TV + Parabola	1 Set	1 Set	1 Set				
19	AC	4	4	4				1 aát ona
20	Kipas Angin	4	4	4				
21	Kompor	1	1	1				Aát ona
22	Kompor Gas	1	1	1				

23	Rack sepatu	3	3	1				Aát ona
24	Rack Piring	1	1	3				
25	Lampu	11	11	1				
26	Water Pump Sanyo	1	1	11				
				1				

1.3 : Lista Projectos

Projetu hotu ne'ebe akumulula iha lista ne'e bazeia ba dadus projetu ne'ebe sei lao hela no mos projeto ne'ebe abandona ona tinan barak, projeto hirak ne'e fahe tuir lista 1.3.1 Projeto Por Fundus Finansiamientos, 1.3.2 Projeto Por Sectors no 1.3.3 Projeto Por Ministerios.

1.3.1 : Lista Projectos Municipio Manatuto Por Fundus Finansiamientos

NO	POSTO ADMINISTRATIVU	TOTAL FI+Fundu Covid-19+LM-BS+LM-CD+LM-TP+PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique	10	\$ 2.398.501,20	42,62%
2	Laclo	9	\$ 49.837.529,51	87,47%
3	Laclubar	10	\$ 36.823.796,83	86,10%
4	Laleia	2	\$ 392.472,03	12,03%
5	Manatuto Villa	18	\$ 42.264.184,24	79,49%
6	Soibada	5	\$ 4.286.667,82	85,46%
	Grand Total	54	\$ 136.003.151,63	83,55%

NO	POSTO ADMINISTRATIVU	FI		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique		\$ -	0,00%
2	Laclo	3	\$ 48.698.873,04	87,85%
3	Laclubar	2	\$ 35.075.150,37	88,18%
4	Laleia		\$ -	0,00%
5	Manatuto Villa	6	\$ 40.765.491,57	80,74%
6	Soibada	1	\$ 3.553.954,20	93,93%
	Grand Total	12	\$ 128.093.469,18	85,85%

NO	POSTO ADMINISTRATIVU	Fundo Covid-19		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique		\$ -	0,00%
2	Laclo		\$ -	0,00%
3	Laclubar		\$ -	0,00%
4	Laleia		\$ -	0,00%
5	Manatuto Villa	2	\$ 598.668,36	86,09%
6	Soibada		\$ -	0,00%
	Grand Total	2	\$ 598.668,36	86,09%

NO	POSTO ADMINISTRATIVU	LM-BS		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique	2	\$ 404.938,08	54,93%
2	Laclo	2	\$ 240.323,02	44,35%
3	Laclubar	2	\$ 675.432,39	40,19%
4	Laleia		\$ -	0,00%
5	Manatuto Villa	1	\$ 29.275,84	15,92%
6	Soibada		\$ -	0,00%
	Grand Total	7	\$ 1.349.969,33	44,82%

NO	POSTO ADMINISTRATIVU	LM-CD		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique	7	\$ 1.876.648,24	38,63%
2	Laclo	2	\$ 646.243,79	84,96%
3	Laclubar	2	\$ 661.982,34	55,55%
4	Laleia	2	\$ 305.588,74	8,32%
5	Manatuto Villa	1	\$ 182.701,57	6,14%
6	Soibada	3	\$ 630.201,31	47,08%
	Grand Total	17	\$ 4.303.365,99	45,90%

NO	POSTO ADMINISTRATIVU	LM-TP		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique		\$ -	0,00%
2	Laclo	1	\$ 98.147,27	23,56%
3	Laclubar	2	\$ 202.223,29	25,59%
4	Laleia	1	\$ 86.883,29	25,06%
5	Manatuto Villa	5	\$ 382.490,63	15,84%
6	Soibada	1	\$ 102.512,31	27,56%
	Grand Total	10	\$ 872.256,79	21,27%

NO	POSTO ADMINISTRATIVU	PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	Barique	1	\$ 116.914,88	63,99%
2	Laclo	1	\$ 153.942,39	84,29%
3	Laclubar	2	\$ 209.008,44	41,51%
4	Laleia		\$ -	0,00%
5	Manatuto Villa	2	\$ 305.556,27	28,66%
6	Soibada		\$ -	0,00%
	Grand Total	6	\$ 785.421,98	48,24%

1.3.2 : Lista Projectos Municipio Manatuto Por Sectors

NO	POR SECTOR	TOTAL MUNICIPIO MANATUTO		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA	1	\$ 370.511,25	15,83%
2	AGUA E SANEAMIENTO	1	\$ 162.377,94	41,85%
3	COMERCIO	1	\$ 153.942,39	84,29%
4	EDIFICIOS PUBLICOS	7	\$ 1.168.395,22	54,65%
5	EDUKASAUN	10	\$ 1.054.958,36	18,65%
6	ELETRIFIKASAUN NASIONAL	2	\$ 1.076.003,44	78,57%
7	ESTRADAS	15	\$ 9.109.569,39	61,96%
8	ESTRADAS E PONTES	1	\$ 394.194,73	0,00%
9	FLOOD CONTROL	2	\$ 432.138,16	56,30%
10	IMPRESTIMO	4	\$ 115.112.106,35	86,96%
11	JUVENTUDE NO DESPORTU	1	\$ 2.362.976,44	76,00%
12	MANUTENSAUN NO REHABILITASAUN	2	\$ 157.560,52	41,96%
13	PONTES	1	\$ 3.553.954,20	93,93%
14	SAUDE	4	\$ 588.906,97	70,84%
15	TURISMO	2	\$ 305.556,27	28,66%
	Grand Total	54	\$ 136.003.151,63	83,55%

NO	POR SECTOR	Barique		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA	1	\$ 370.511,25	15,83%
2	AGUA E SANEAMENTO	1	\$ 162.377,94	41,85%
3	COMERCIO		\$ -	0,00%
4	EDIFICIOS PUBLICOS	1	\$ 408.460,73	78,09%
5	EDUKASAUN		\$ -	0,00%
6	ELETRIFIKASAUN NASIONAL		\$ -	0,00%
7	ESTRADAS	3	\$ 940.115,74	29,92%
8	ESTRADAS E PONTES		\$ -	0,00%
9	FLOOD CONTROL	1	\$ 242.560,14	63,68%
10	IMPRESTIMO		\$ -	0,00%
11	JUVENTUDE NO DESPORTU		\$ -	0,00%
12	MANUTENSAUN NO REHABILITASAUN	2	\$ 157.560,52	41,96%
13	PONTES		\$ -	0,00%
14	SAUDE	1	\$ 116.914,88	63,99%
15	TURISMO		\$ -	0,00%
	Grand Total	10	\$ 2.398.501,20	42,62%

NO	POR SECTOR	Laclo		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA		\$ -	0,00%
2	AGUA E SANEAMIENTO		\$ -	0,00%
3	COMERCIO	1	\$ 153.942,39	84,29%
4	EDIFICIOS PUBLICOS	1	\$ 50.745,00	34,95%
5	EDUKASAUN	1	\$ 98.147,27	23,56%
6	ELETRIFIKASAUN NASIONAL	1	\$ 380.582,61	72,08%
7	ESTRADAS	3	\$ 649.558,35	84,99%
8	ESTRADAS E PONTES		\$ -	0,00%
9	FLOOD CONTROL	1	\$ 189.578,02	46,86%
10	IMPRESTIMO	1	\$ 48.314.975,87	87,98%
11	JUVENTUDE NO DESPORTU		\$ -	0,00%
12	MANUTENSAUN NO REHABILITASAUN		\$ -	0,00%
13	PONTES		\$ -	0,00%
14	SAUDE		\$ -	0,00%
15	TURISMO		\$ -	0,00%
	Grand Total	9	\$ 49.837.529,51	87,47%

NO	POR SECTOR	Laclubar		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA		\$ -	0,00%
2	AGUA E SANEAMIENTO		\$ -	0,00%
3	COMERCIO		\$ -	0,00%
4	EDIFICIOS PUBLICOS		\$ -	0,00%
5	EDUKASAUN	2	\$ 202.223,29	25,59%
6	ELETRIFIKASAUN NASIONAL	1	\$ 695.420,83	82,11%
7	ESTRADAS	3	\$ 1.337.414,73	47,79%
8	ESTRADAS E PONTES		\$ -	0,00%
9	FLOOD CONTROL		\$ -	0,00%
10	IMPRESTIMO	1	\$ 34.379.729,54	88,30%
11	JUVENTUDE NO DESPORTU		\$ -	0,00%
12	MANUTENSAUN NO REHABILITASAUN		\$ -	0,00%
13	PONTES		\$ -	0,00%
14	SAUDE	2	\$ 209.008,44	41,51%
15	TURISMO		\$ -	0,00%
	Grand Total	9	\$ 36.823.796,83	86,10%

NO	POR SECTOR	Laleia		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA		\$ -	0,00%
2	AGUA E SANEAMENTO		\$ -	0,00%
3	COMERCIO		\$ -	0,00%
4	EDIFICIOS PUBLICOS	1	\$ 277.330,43	0,00%
5	EDUKASAUN	1	\$ 86.883,29	25,06%
6	ELETRIFIKASAUN NASIONAL		\$ -	0,00%
7	ESTRADAS	1	\$ 28.258,31	90,00%
8	ESTRADAS E PONTES		\$ -	0,00%
9	FLOOD CONTROL		\$ -	0,00%
10	IMPRESTIMO		\$ -	0,00%
11	JUVENTUDE NO DESPORTU		\$ -	0,00%
12	MANUTENSAUN NO REHABILITASAUN		\$ -	0,00%
13	PONTES		\$ -	0,00%
14	SAUDE		\$ -	0,00%
15	TURISMO		\$ -	0,00%
	Grand Total	3	\$ 392.472,03	12,03%

NO	POR SECTOR	Manatuto Villa		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA		\$ -	0,00%
2	AGUA E SANEAMIENTO		\$ -	0,00%
3	COMERCIO		\$ -	0,00%
4	EDIFICIOS PUBLICOS	3	\$ 364.960,55	72,47%
5	EDUKASAUN	5	\$ 565.192,20	12,70%
6	ELETRIFIKASAUN NASIONAL		\$ -	0,00%
7	ESTRADAS	2	\$ 5.590.919,46	69,52%
8	ESTRADAS E PONTES	1	\$ 394.194,73	0,00%
9	FLOOD CONTROL		\$ -	0,00%
10	IMPRESTIMO	2	\$ 32.417.400,94	84,01%
11	JUVENTUDE NO DESPORTU	1	\$ 2.362.976,44	76,00%
12	MANUTENSAUN NO REHABILITASAUN		\$ -	0,00%
13	PONTES		\$ -	0,00%
14	SAUDE	1	\$ 262.983,65	97,19%
15	TURISMO	2	\$ 305.556,27	28,66%
	Grand Total	17	\$ 42.264.184,24	79,49%

NO	POR SECTOR	Soibada		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN(%)
1	AGRICULTURA		\$ -	0,00%
2	AGUA E SANEAMIENTO		\$ -	0,00%
3	COMERCIO		\$ -	0,00%
4	EDIFICIOS PUBLICOS	1	\$ 66.898,51	55,80%
5	EDUKASAUN	1	\$ 102.512,31	27,56%
6	ELETRIFIKASAUN NASIONAL		\$ -	0,00%
7	ESTRADAS	3	\$ 563.302,80	46,05%
8	ESTRADAS E PONTES		\$ -	0,00%
9	FLOOD CONTROL		\$ -	0,00%
10	IMPRESTIMO		\$ -	0,00%
11	JUVENTUDE NO DESPORTU		\$ -	0,00%
12	MANUTENSAUN NO REHABILITASAUN		\$ -	0,00%
13	PONTES	1	\$ 3.553.954,20	93,93%
14	SAUDE		\$ -	0,00%
15	TURISMO		\$ -	0,00%
	Grand Total	6	\$ 4.286.667,82	85,46%

1.3.3 : Lista Projectos Municipio Manatuto Por Ministerios

NO	POR MINISTERIO	GRAND TOTAL		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL	2	\$ 305.556,27	28,66%
2	MINISTERIO AGRICULTURA E PESCAS	1	\$ 370.511,25	15,83%
3	MINISTERIO DA DEFESA	1	\$ 189.578,02	46,86%
4	MINISTERIO DA JUSTICA	1	\$ 29.275,84	15,92%
5	MINISTERIO DAS OBRAS PUBLICAS	27	\$ 129.808.326,71	84,90%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	12	\$ 1.121.856,87	20,86%
7	MINISTERIO PLANU E ORDENAMENTU	1	\$ 277.330,43	0,00%
8	MINISTERIO SAUDE	5	\$ 924.591,68	73,22%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$ 204.687,39	72,06%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 408.460,73	78,09%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	1	\$ 2.362.976,44	76,00%
	Grand Total	54	\$ 136.003.151,63	83,55%

NO	POR MINISTERIO	Barique		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL		\$ -	0,00%
2	MINISTERIO AGRIKULTURA E PESCAS	1	\$ 370.511,25	15,83%
3	MINISTERIO DA DEFESA		\$ -	0,00%
4	MINISTERIO DA JUSTICA		\$ -	0,00%
5	MINISTERIO DAS OBRAS PUBLICAS	7	\$ 1.502.614,34	37,92%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		\$ -	0,00%
7	MINISTERIO PLANU E ORDENAMENTU		\$ -	0,00%
8	MINISTERIO SAUDE	1	\$ 116.914,88	63,99%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0,00%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 408.460,73	78,09%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0,00%
Grand Total		10	\$ 2.398.501,20	42,62%

NO	POR MINISTERIO	Laclo		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL		\$ -	0,00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0,00%
3	MINISTERIO DA DEFESA	1	\$ 189.578,02	46,86%
4	MINISTERIO DA JUSTICA		\$ -	0,00%
5	MINISTERIO DAS OBRAS PUBLICAS	5	\$ 49.345.116,83	87,81%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 98.147,27	23,56%
7	MINISTERIO PLANU E ORDENAMENTU		\$ -	0,00%
8	MINISTERIO SAUDE		\$ -	0,00%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$ 204.687,39	72,06%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0,00%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0,00%
	Grand Total	9	\$ 49.837.529,51	87,47%

NO	POR MINISTERIO	Laclubar		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL		\$ -	0,00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0,00%
3	MINISTERIO DA DEFESA		\$ -	0,00%
4	MINISTERIO DA JUSTICA		\$ -	0,00%
5	MINISTERIO DAS OBRAS PUBLICAS	5	\$ 36.412.565,10	86,69%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	2	\$ 202.223,29	25,59%
7	MINISTERIO PLANU E ORDENAMENTU		\$ -	0,00%
8	MINISTERIO SAUDE	2	\$ 209.008,44	41,51%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0,00%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0,00%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0,00%
Grand Total		9	\$ 36.823.796,83	86,10%

NO	POR MINISTERIO	Laleia		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL		\$ -	0,00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0,00%
3	MINISTERIO DA DEFESA		\$ -	0,00%
4	MINISTERIO DA JUSTICA		\$ -	0,00%
5	MINISTERIO DAS OBRAS PUBLICAS	1	\$ 28.258,31	90,00%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 86.883,29	25,06%
7	MINISTERIO PLANU E ORDENAMENTU	1	\$ 277.330,43	0,00%
8	MINISTERIO SAUDE		\$ -	0,00%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0,00%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0,00%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0,00%
	Grand Total	3	\$ 392.472,03	12,03%

NO	POR MINISTERIO	Manatuto Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL	2	\$ 305.556,27	28,66%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0,00%
3	MINISTERIO DA DEFESA		\$ -	0,00%
4	MINISTERIO DA JUSTICA	1	\$ 29.275,84	15,92%
5	MINISTERIO DAS OBRAS PUBLICAS	4	\$ 38.402.515,13	81,04%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	6	\$ 565.192,20	12,70%
7	MINISTERIO PLANU E ORDENAMENTU		\$ -	0,00%
8	MINISTERIO SAUDE	3	\$ 598.668,36	86,09%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0,00%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0,00%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	1	\$ 2.362.976,44	76,00%
	Grand Total	17	\$ 42.264.184,24	79,49%

NO	POR MINISTERIO	Soibada		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EZECUSAUN (%)
1	ESTATAL		\$ -	0,00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0,00%
3	MINISTERIO DA DEFESA		\$ -	0,00%
4	MINISTERIO DA JUSTICA		\$ -	0,00%
5	MINISTERIO DAS OBRAS PUBLICAS	4	\$ 4.117.257,00	87,38%
6	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	2	\$ 169.410,82	38,71%
7	MINISTERIO PLANU E ORDENAMENTU		\$ -	0,00%
8	MINISTERIO SAUDE		\$ -	0,00%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0,00%
10	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0,00%
11	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0,00%
Grand Total		6	\$ 4.286.667,82	85,46%

1.4. Dadus Populasaun Munisipiu Manatuto

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Barique	5,833	1,924	1,617	1,183	1,109
Laclo	8,193	2,250	2,185	1,919	1,838
Laclubar	12,777	3,445	3,571	2,924	2,836
Laleia	3,930	1,181	1,189	817	743
Manatuto	15,446	4,741	4,609	3,109	2,987
Soibada	3,511	237	213	239	259

Fontes : Projeksaun Populasaun bazea ba Census Populasaun no Umakain 2015,

Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1. Progressu Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan nia laran, husi lista #anexu B hatudu progresu aktual fulan ida ne'e ho nia prensentagen servisu, montante aktual bazeia ba orsamento ne'ebe hetan husi progresu fulan ida ne'e, ikus liu prentangen aktual fulan ida ne'e hatudu progresu fisiku komulativu husi prosentun antrior no fulan ida ne'e nian, lista kompletu ba detallu bele hare iha #anexu B, detallu ba back-up #anexu C, no Instrusaun Servisu #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1. Obtáclo Servisu iha Terenu

Observasaun geral ba projeto hirak nebe mak implementa iha Munisipio Manatuto

1. Projeto Lao la tuir tempo nebee asina entre parte rua
2. Laiha tekniko supervisaun husi projeto nain atu halo kontrolo diaramente
3. Tekniko kompanha la iha tereno
4. Skill badaen neebe mak la dun professional

Obstalku teknik A.D.N hasoru

1. Distansia ne'ebe dook difikulta teknik atu servisu lalais
2. Kondisaun estrada neébe a'at
3. Kontraktor sira ne'ebe mak servisu iha terreno barak mak la tuir Spesifikasaun ne'ebe iha kontartu laran.
4. Planu Mapamentu Enginheiro Munisipiu la konsege realiza tuir planu tamba hare hosi nia distansia ne'ebe dook.
5. Sistema dropbox iha Munisipiu dala ruma iha problema lina internet

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Presija tebes atu aumenta ema iha Munisipiu atu nune bele halo servisu ba administrasaun ne'ebe efektivu.
2. Sebele sistema dropbox tau mos iha dekstop Munisipiu para labele atraja ami nia servisu.

Note: Asinatura Husi Eng. Municipio Manatuto

Força de Trabalho ADN,I.P Municipio Manatuto						
No	Deskrisaun	Identidade				Asinatura
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	
1	Enjineiru	Quico Adelino Junior	240	Enjineiru EPAS		
		José R. Carlos Gusmão	168	Enjineiru ITI		
		Domingos da Costa e Silva	250	Enjineiru ITI		

		Adonis Julio Fernandes	152	Enjineiru ME		
2	Enjineira	Olivia Soares	112	Enjineira VEBD		
3	Motorista	Timoteo da Silva Morais	120	Motorista		

#ANEXU A

MUNICIPIO MANATUTO (LISTA GERAL)

Localizasaun Projeto

NU.	PMIS CODE	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	MONT. KONT. (\$)	DATA KONT.	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	Status Projecto	OBS
1	P0281	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	\$ 2,561,405.06	Aug. 25, 2018	63.80%	57.33%	\$ 1,468,479.04	\$ 1,092,926.02	ON-GOING	
2	P0282	Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Nananiu, Unip. Lda JV Ina Forek, Lda	\$ 3,029,514.40	Aug. 25, 2017	89.20%	79.82%	\$ 2,418,275.38	\$ 611,239.02	ON-GOING	
3	P0326	Construção de novo Estadio de Futebol em Manatuto	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Manatuto Villa	Manatuto	Obrai Unipesoal, Lda	\$ 2,362,976.44	June 30, 2015	82.08%	76.00%	\$ 1,795,843.89	\$ 567,132.55	ON-GOING	
4	P0377	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	R.D Interior Junior Construction / Hebei Road and Bridge Group	\$ 28,011,854.94	Feb. 10, 2014	94.91%	85.62%	\$ 23,983,565.18	\$ 4,028,289.76	ON-GOING	
5	P0379	Consultant Supervision (M-L & L-N)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	Sinotech Engineering Consultant	\$ 4,405,546.00	Sept. 3, 2014	73.76%	73.76%	\$ 3,249,684.75	\$ 1,155,861.25	ON-GOING	
6	P0788	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Unip. Lda	\$ 79,155.54	Dec. 18, 2019	88.07%	79.26%	\$ 62,737.67	\$ 16,417.87	ON-GOING	
7	P0789	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Lda	\$ 226,400.73	Dec. 18, 2019	43.70%	10.97%	\$ 24,834.32	\$ 201,566.41	ON-GOING	
8	P0872	Servisu Manutensaun Edifisiu CRC Munisiup Manatuto	MINISTERIO DA JUSTICA	LM-BS	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Baboe Unip Lda	\$ 29,275.84	March 1, 2020	15.92%	15.92%	\$ 4,660.85	\$ 24,614.99	ON-GOING	
9	P0954	Konstrusaun Fatin Isolamentu iha Municipiu Manatuto, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Manatuto Villa	Manatuto	Talamori Unip.Lda	\$ 262,983.65	09-Dec-20	100.00%	97.19%	\$ 255,587.87	\$ 7,395.78	ON-GOING	
10	P2538	New Construction of Fence at Izolation Covid-19 in Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	K-6, UNIPESOAL LDA	\$ 257,748.51	Jan. 12, 2022	88.89%	74.56%	\$ 192,164.43	\$ 65,584.08	ON-GOING	
11	P2539	Supply and Installtion Main Power For Isolation and Laboratorium Building Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Fraternity Unipessoal Lda	\$ 77,936.20	Jan. 12, 2022	92.28%	86.81%	\$ 67,657.50	\$ 10,278.70	ON-GOING	
12	P1806	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE ESG KAY RALA	\$ 62,996.83	Oct. 15, 2021	48.32%	24.62%	\$ 15,507.66	\$ 47,489.17	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 16.42%
13	P1808	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF RENTAU	\$ 64,383.50	Oct. 15, 2021	53.92%	50.49%	\$ 32,504.67	\$ 31,878.83	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 1.53%
14	P1809	Konstrusaun ka Rehabilitasaun ba PE Rembor	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE PE REMBOR	\$ 88,918.34	Oct. 15, 2021	45.26%	0.00%	\$ -	\$ 88,918.34	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 15.81%
15	P1811	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF OBRATO	\$ 66,144.65	Oct. 15, 2021	54.19%	22.03%	\$ 14,570.40	\$ 51,574.25	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 16.02%
16	P2041	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF BAHADIK	\$ 100,047.31	Oct. 15, 2021	14.58%	14.58%	\$ 14,590.20	\$ 85,457.11	ON-GOING	
17	P1953	Konstrusaun foun ba EBC Vasco da Gama-Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	Manatuto Villa	Manatuto	Parapa Bemiziuu Star Unipessoal Lda	\$ 182,701.57	Dec. 7, 2022	6.82%	6.14%	\$ 11,214.18	\$ 171,487.39	ON-GOING	
18	P1581	Rehabilitasaun Estrada Rural, Rembor Chainage, Manatuto 0+000-3+000 (3.0 Km	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	Manatuto Villa	Manatuto	Kartini Unipessoal Lda	\$ 394,194.73	April 28, 2022	0.00%	0.00%	\$ -	\$ 394,194.73	ON-GOING	
19	P0627	Rehabilitasaun Kampu Fotebolli iha Postu Administrativu Laleia	MINISTERIO PLANU E ORDENAMENTU	LM-CD	EDIFICIOS PUBLICOS	Laleia	Manatuto	DCO Unip.Lda	\$ 277,330.43	July 18, 2019	0.00%	0.00%	\$ -	\$ 277,330.43	ON-GOING	

#ANEXU A

MUNICIPIO MANATUTO (LISTA GERAL)

Localizasaun Projeto

NU.	PMIS CODE	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	MONT. KONT. (\$)	DATA KONT.	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	Status Projecto	OBS
20	P0986	R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laleia	Manatuto	As Jazesia Unipessoal Lda	\$ 28,258.31	June 10, 2021	100.00%	90.00%	\$ 25,432.48	\$ 2,825.83	ON-GOING	
21	P1810	Konstrusaun ka Rehabilitasaun ba EP Cairui	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laleia	Manatuto	MEJD PKRIE EP CAIRUI	\$ 86,883.29	Oct. 15, 2021	28.43%	25.06%	\$ 21,771.04	\$ 65,112.25	ON-GOING	
22	P0114	New Installation Mv, Lv Line & House Connection From Laclubar Vila to Funar And Fatuk Manu - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laclubar	Manatuto	Tasibala III Unip. Lda	\$ 695,420.83	June 7, 2016	91.52%	82.11%	\$ 571,034.27	\$ 124,386.56	ON-GOING	
23	P0378	Road Network Upgrading Sector Project (RNUSP)Upgrading and Maintenance of Laclubar Junction - Natarbora Road (Sta. 100+360 - Sta. 144+995)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Laclubar	Manatuto	China Nuclear Industry 22ND Construction Co; LTD	\$ 34,379,729.54	Nov. 20, 2014	92.04%	88.30%	\$ 30,356,507.52	\$ 4,023,222.02	ON-GOING	
24	P0899	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Hatuwari Unip. Lda	\$ 481,029.67	Aug. 25, 2020	54.37%	11.80%	\$ 126,501.30	\$ 354,528.37	ON-GOING	
25	P0917	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Ryzena Unipessoal Lda	\$ 194,402.72	Dec. 20, 2019	82.83%	74.55%	\$ 144,924.09	\$ 49,478.63	ON-GOING	
26	P0977	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Sun Rise Golden Construction 02 Lda	\$ 448,209.39	June 10, 2021	95.04%	82.05%	\$ 367,756.59	\$ 80,452.80	ON-GOING	
27	P0983	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Adahiak Orlao Unipessoal Lda	\$ 213,772.95	June 10, 2021	7.12%	0.00%	\$ -	\$ 213,772.95	ON-GOING	
28	P0775	Kontinuasaun Konst. Postu Saude Iha Suku Fatumakerek	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Hatuwari Unip. Lda	\$ 120,962.71	July 28, 2019	71.23%	64.11%	\$ 77,547.51	\$ 43,415.20	ON-GOING	
29	P1803	Konstrusaun ka Rehabilitasaun ba EBF Batara	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF BATARA	\$ 102,060.99	Oct. 15, 2021	51.55%	25.60%	\$ 26,125.75	\$ 75,935.24	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 7.08%
30	P1804	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF AISIU-UM	\$ 100,162.30	Oct. 15, 2021	25.60%	25.59%	\$ 25,626.77	\$ 74,535.53	ON-GOING	
31	P0316	Construction of New Steel Bridge 100m in Milotu Sahe river, jct. Fatucamanau, Soibada, Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Soibada	Manatuto	FIRDO UNIPESOAL LDA	\$ 3,553,954.20	Feb. 27, 2017	100.00%	93.93%	\$ 3,338,377.84	\$ 215,576.36	ON-GOING	
32	P0932	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 10 Soibada to Soibada Town	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	\$ 164,154.00	March 25, 2020	70.00%	70.00%	\$ 114,907.80	\$ 49,246.20	ON-GOING	
33	P0981	R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 203,036.57	June 10, 2021	50.73%	41.78%	\$ 84,819.65	\$ 118,216.92	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 3.10%
34	P0984	R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Ryzena Unipessoal Lda	\$ 196,112.23	June 10, 2021	55.40%	30.42%	\$ 59,662.31	\$ 136,449.92	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 5.20%
35	P1814	Projetu Rehabilitasaun Ensinu Sekundariu Tekniku Vokasional Soibada, Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDIFICIOS PUBLICOS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 66,898.51	Nov. 26, 2021	82.90%	55.80%	\$ 37,330.95	\$ 29,567.56	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 3.93%
36	P1807	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Soibada	Manatuto	MEJD PKRIE EBC WEAIHUDIK	\$ 102,512.31	Oct. 15, 2021	35.85%	27.56%	\$ 28,253.89	\$ 74,258.42	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 4.09%
37	P0940	Construction of Sahen Bridge Approach Protection (A14) Manatuto (MPW-W-190157) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	FLOOD CONTROL	Barique	Manatuto	Yoku Unipessoal Lda	\$ 242,560.14	Oct. 24, 2019	70.75%	63.68%	\$ 154,455.92	\$ 88,104.22	Abandona	
38	P0404	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	MINISTERIO AGRICULTURA E PESCAS	LM-CD	AGRICULTURA	Barique	Manatuto	Tasibala II Const	\$ 370,511.25	Sept. 13, 2016	17.59%	15.83%	\$ 58,645.87	\$ 311,865.38	Abandona	Abandona
39	P0540	Rural Roads Routine Maintenance Uma Boco - Aubeon, Sta. 0+000 - 6+000, Manututo Municipality (Manutensaun)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Zenobia Diak Unip.Lda	\$ 15,875.56	Jan. 7, 2017	100.00%	87.26%	\$ 13,853.09	\$ 2,022.47	PHO	Abandona
40	P0784	Konstrusaun Postu Saude Aimeta Laran-Barique	MINISTERIO SAUDE	PDIM	SAUDE	Barique	Manatuto	Malack II Unip. Lda	\$ 116,914.88	Sept. 23, 2019	71.10%	63.99%	\$ 74,817.23	\$ 42,097.65	ON-GOING	

#ANEXU A

MUNICIPIO MANATUTO (LISTA GERAL)

Localizasaun Projeto

NU.	PMIS CODE	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	MONT. KONT. (\$)	DATA KONT.	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	Status Projecto	OBS
41	P0873	Konstrusaun Sistema Bee Mos Iha Suco Aubeon no Aimetalaran /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Barique	Manatuto	Malaca Unip Lda	\$ 162,377.94	Oct. 8, 2019	46.50%	41.85%	\$ 67,961.57	\$ 94,416.37	ON-GOING	
42	P0921	R4D Rural Periodic Maintenance Kaen Laran - Barique Chainage 0+000 - 9+000 & Routine, Hatularan-Cairui Chainage 0+000-9+800 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Manufahi Kiik Unip. Lda	\$ 141,684.96	Aug. 25, 2019	41.78%	36.88%	\$ 52,260.01	\$ 89,424.95	ON-GOING	
43	P0978	R4D Rural Road Spot Improvement Agriculture Center - Aubeon Chainage 3+000-6+200	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	We"coi Unipessoal Lda	\$ 343,111.47	June 10, 2021	63.25%	21.97%	\$ 75,370.79	\$ 267,740.68	ON-GOING	
44	P0982	R4D Rural Road Spot Improvement Uma Boco - Agriculture Center Chainage 0+000 - 3+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Linoel	\$ 296,211.81	June 10, 2021	18.83%	15.96%	\$ 47,266.94	\$ 248,944.87	ON-GOING	
45	P0985	R4D Rural Road Spot Improvement Kaen-Laran - Barique Chainage 0+000-9+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Gimso Brothers Unip. Lda	\$ 300,792.46	July 10, 2021	98.30%	52.76%	\$ 158,690.94	\$ 142,101.52	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 9.70%
46	P1056	New construction of Gapura and gabion wall protection no jardim de heroes de Natarbora	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Barique	Manatuto	Senizu	\$ 408,460.73	Oct. 18, 2021	95.79%	78.09%	\$ 318,953.66	\$ 89,507.07	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 1.34%
47	P0061	New Installation MV, LV Line and House Connection from Lacio to Mantane - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Lacio	Manatuto	Anopa Electrical Unip. Lda	\$ 380,582.61	Sept. 1, 2016	95.99%	72.08%	\$ 274,330.03	\$ 106,252.58	ON-GOING	
48	P0221	Emergency Rehabilitation Project in Subao Boo, Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lacio	Manatuto	Sahan I Unip.Lda	\$ 3,314.56	Sept. 27, 2016	100.00%	90.00%	\$ 2,983.11	\$ 331.45	PHO	Falta Retensaun
49	P0926	For Roads & Bridges Maintenance Section : Mantanen Lacio, Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lacio	Manatuto	Egana, Unip. Lda	\$ 223,843.79	Dec. 13, 2019	68.89%	56.58%	\$ 126,647.74	\$ 97,196.05	ON-GOING	
50	P0692	Rehabilitation of Behau Mini Tradisional Food	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Lacio	Manatuto	Esa-Un	\$ 50,745.00	May 2, 2016	38.83%	34.95%	\$ 17,736.12	\$ 33,008.88	PENDENTE	
51	P0776	Konstrusaun Mercado Komunitaria Kikan Ilmano	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	COMERCIO	Lacio	Manatuto	Surprise Unip. Lda	\$ 153,942.39	Sept. 12, 2016	97.16%	84.29%	\$ 129,753.97	\$ 24,188.42	ON-GOING	
52	P0396	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Lacio	Manatuto	Sinohydro Corporation Limited	\$ 48,314,975.87	May.3, 2016	88.12%	87.98%	\$ 42,506,027.78	\$ 5,808,948.09	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 0.14%
53	P1805	Konstrusaun ka Rehabilitasaun ba EBC Remanarun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Lacio	Manatuto	MEJD PKRIE EBC REMANARUN	\$ 98,147.27	Oct. 15, 2021	30.64%	23.56%	\$ 23,122.26	\$ 75,025.01	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 7.06%
54	P2603	Rehabilitation of Reinforced Concrete Ramp at Behau	MINISTERIO DA DEFESA	LM-BS	FLOOD CONTROL	Lacio	Manatuto	Baboe Unip Lda	\$ 189,578.02	May 23, 2022	93.39%	46.86%	\$ 88,843.95	\$ 100,734.07	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Fevereiro Aumenta 41.32%
		TOTAL							\$ 135,492,705.90				\$ 113,210,178.73	\$ 22,181,793.10		

1. Eng. José Roberto C. Gusmão
Eng. ba Projeto Infrastrutura e
Irigasaun Municipiu Manatuto, ADN, I.P

Prepara Husi:
2. Eng. Domingus D.X. Silva
Eng. ba Projeto Infrastrutura e
Irigasaun Municipiu Manatuto, ADN, I.P

3. Eng. Quico Adelino Junior
Eng. ba Projeto Infrastrutura e Edificiu Público, Be'e
no Saneamento Municipiu Manatuto, ADN, I.P

4. Eng. Adonis Julio Fernandes
Eng. ba Projeto ME, ADN, I.P

Certifika Husi:
Eng. Emerenciana da Costa Maia Freitas
Coordenadora Da Unidade de Controlo e Validação De
Qualidade ADN,I.P

LISTA #ANEXU B

PROGRESSU FISIKU KADA FULAN																
					LOKALIZASAUN PROJETU						Jan-23			Feb-23		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress	This Month Progress	Kumulati vo Progress	Previous Progress	This Month Progress	Kumulativo Progress
1	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	SSS/062/MOPTC-2017	\$ 2,561,405.06	Aug. 25, 2018	63.80%		63.80%	63.80%		63.80%
2	Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Nananiu, Unip. Lda JV Ina Forek, Lda	SSS/061/MOPTC-2017	\$ 3,029,514.40	Aug. 25, 2017	89.20%		89.20%	89.20%		89.20%
3	Construção de novo Estadio de Futebol em Manatuto	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Manatuto Villa	Manatuto	Obrai Unipessoal, Lda	ICB/0128/SEJD-2014	\$ 2,362,976.44	June 30, 2015	82.08%		82.08%	82.08%		82.08%
4	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	R.D Interior Junior Construction / Hebei Road and Bridge Group	ICB/023/MPW-2013	\$ 28,011,854.94	Feb. 10, 2014	94.91%		94.91%	94.91%		94.91%
5	Consultant Supervision (M-L & L-N)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	Sinotech Engineering Consultant	QCBS/019/MPW-2013	\$ 4,405,546.00	Sept. 3, 2014	73.76%		73.76%	73.76%		73.76%
6	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Unip. Lda	08/PDIM-VMNTT/XII/2019	\$ 79,155.54	Dec. 18, 2019	88.07%		88.07%	88.07%		88.07%
7	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Lda	01/PDIM-VMNTT/XII/2019	\$ 226,400.73	Dec. 18, 2019	43.70%		43.70%	43.70%		43.70%
8	Servisu Manutensaun Edifislu CRC Munisiplu Manatuto	MINISTERIO DA JUSTICA	LM-BS	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Baboe Unip Lda	019/Janeiro/2020	\$ 29,275.84	March 1, 2020	15.92%		15.92%	15.92%		15.92%
9	Konstrusaun Fatin Isolamentu Iha Municipi Manatuto, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Manatuto Villa	Manatuto	Talamori Unip.Lda	RDTL-MS-DNA-DC-20-254	\$ 262,983.65	9-Dec-20	100.00%		100.00%	100.00%		100.00%
10	New Construction of Fence at Isolation Covid-19 in Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	K-6, UNIPESSOAL LDA	RDTL-MS-C19-DNA-DC-21-227	\$ 257,748.51	Jan. 12, 2022	88.89%		88.89%	88.89%		88.89%
11	Supply and Installation Main Power For Isolation and Laboratorium Building Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Fraternity Unipessoal Lda	RDTL-MS-C19-DNA-DC-21-227	\$ 77,936.20	Jan. 12, 2022	92.28%		92.28%	92.28%		92.28%
12	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE ESG KAY RALA	-	\$ 62,996.83	Oct. 15, 2021	31.90%		31.90%	31.90%	16.42%	48.32%
13	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF RENTAU	-	\$ 64,383.50	Oct. 15, 2021	26.64%	29.33%	55.97%	55.97%	1.53%	57.49%
14	Konstrusaun ka Rehabilitasaun ba PE Rembor	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE PE REMBOR	-	\$ 88,918.34	Oct. 15, 2021	24.37%	5.15%	29.52%	29.52%	15.81%	45.33%
15	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF OBRATO	-	\$ 66,144.65	Oct. 15, 2021	38.17%		38.17%	38.17%	16.02%	54.19%
16	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF BAHADIK	-	\$ 100,047.31	Oct. 15, 2021	14.58%		14.58%	14.58%		14.58%
17	Konstrusaun foun ba EBC Vasco da Gama-Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	Manatuto Villa	Manatuto	Parapa Bemizuu Star Unipessoal Lda		\$ 182,701.57	Dec. 7, 2022	6.82%		6.82%	6.82%	2.85%	9.67%
18	Rehabilitasaun Estrada Rural ,Rembor Chainage, Manatuto 0+000-3+000 (3.0 Km	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	Manatuto Villa	Manatuto	Kartini Unipessoal Lda		\$ 394,194.73	April 28, 2022	0.00%		0.00%	0.00%		0.00%
19	Rehabilitasaun Kampu Foteboll Iha Postu Administrativu Laleia	MINISTERIO PLANU E ORDENAMENTU	LM-CD	EDIFICIOS PUBLICOS	Laleia	Manatuto	DCO Unip.Lda	011LM/AND/MPIE/VI/DILI/2019/EDIFICIO DEPARTMENT	\$ 277,330.43	July 18, 2019	0.00%		0.00%	0.00%		0.00%
20	R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laleia	Manatuto	As Jazesia Unipessoal Lda	MPW-W-210055	\$ 28,258.31	June 10, 2021	100.00%		100.00%	100.00%		100.00%
21	Konstrusaun ka Rehabilitasaun ba EP Cairui	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laleia	Manatuto	MEJD PKRIE EP CAIRUI	-	\$ 86,883.29	Oct. 15, 2021	25.20%		25.20%	25.20%	20.97%	46.17%
22	New Installation Mv, Lv Line & House Connection From Laclubar Vila to Funar And Fatuk Manu - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laclubar	Manatuto	Tasibala III Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000412	\$ 695,420.83	June 7, 2016	91.52%		91.52%	91.52%		91.52%
23	Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Laclubar	Manatuto	China Nuclear Industry 22ND Construction Co; LTD	ICB/04/MPW-2014	\$ 34,379,729.54	Nov. 20, 2014	92.04%		92.04%	92.04%		92.04%
24	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Hatuwari Unip. Lda	MPW-W-NCB-R-190035	\$ 481,029.67	Aug. 25, 2020	54.37%		54.37%	54.37%		54.37%
25	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Ryzena Unipessoal Lda	MOP/DGOP/DNEPCC/0871-VIII/2020	\$ 194,402.72	Dec. 20, 2019	82.83%		82.83%	82.83%		82.83%
26	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Sun Rise Golden Construction 02 Lda	MPW-W-210057	\$ 448,209.39	June 10, 2021	95.04%		95.04%	95.04%		95.04%
27	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Adahiak Orlao Unipessoal Lda	MPW-W-210056	\$ 213,772.95	June 10, 2021	7.12%		7.12%	7.12%		7.12%
28	Konstrasaun Postu Saude Laclubar Funar- Postu Administrativo Laclubar	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	MERCY, Unipessoal Lda	04/PDIM-VMNTT/VI/2022	\$ 120,962.71	July 28, 2019	11.63%		11.63%	11.63%		11.63%
29	Konstrusaun ka Rehabilitasaun ba EBF Batara	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF BATARA	-	\$ 102,060.99	Oct. 15, 2021	25.60%	19.96%	45.57%	45.57%	7.08%	52.65%
30	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF AISIU-UM	-	\$ 100,162.30	Oct. 15, 2021	25.59%		25.59%	25.59%		25.59%
31	Construction of New Steel Bridge 100m in Milotu Sahe river, jct.Fatucamanau, Soibada, Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Soibada	Manatuto	FIRDO UNIPESSOAL LDA	SSS/013/MOPTC-2017	\$ 3,384,214.14	Feb. 27, 2017	100.00%		100.00%	100.00%		100.00%
32	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 10 Soibada to Soibada Town	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000024	\$ 164,154.00	March 25, 2020	70.00%		70.00%	70.00%		70.00%
33	R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	MPW-W-210059	\$ 203,036.57	June 10, 2021	47.63%		47.63%	47.63%	3.10%	50.73%
34	R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Ryzena Unipessoal Lda	MPW-W-210060	\$ 196,112.23	June 10, 2021	50.20%		50.20%	50.20%	5.20%	55.40%
35	Projeto Rehabilitasaun Ensinu Sekundariu Tekniku Vokasional Soibada, Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDIFICIOS PUBLICOS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	RFQ-R : 21/036 - Q	\$ 66,898.51	Nov. 26, 2021	55.08%		55.08%	55.08%	3.93%	59.01%
36	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Soibada	Manatuto	MEJD PKRIE EBC WEAIHUDIK	-	\$ 102,512.31	Oct. 15, 2021	28.06%		28.06%	28.06%	4.09%	32.15%
37	Construction of Sahen Bridge Approach Protection (A14) Manatuto (MPW-W-190157) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	FLOOD CONTROL	Barique	Manatuto	Yoku Unipessoal Lda	MPW-W-190157	\$ 242,560.14	Oct. 24, 2019	70.75%		70.75%	70.75%		70.75%
38	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	MINISTERIO AGRICULTURA E PESCAS	LM-CD	AGRICULTURA	Barique	Manatuto	Tasibala II Const	RDTL/PO:2016-11272	\$ 370,511.25	Sept. 13, 2016	17.59%		17.59%	17.59%		17.59%
39	Rural Roads Routine Maintenance Uma Boco - Aubeon, Sta. 0+000 - 6+000, Manututo Municipality (Manutensaun)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Zenobia Diak Unip.Lda	MPWTC - CD - 170003	\$ 15,875.56	Jan. 7, 2017	100.00%		100.00%	100.00%		100.00%
40	Konstrusaun Postu Saude Aimeta Laran-Barique	MINISTERIO SAUDE	PDIM	SAUDE	Barique	Manatuto	Malack II Unip. Lda	03/PDIM-VMNTT/IX/2019	\$ 116,914.88	Sept. 23, 2019	71.10%		71.10%	71.10%		71.10%
41	Konstrusaun Sistema Bee Mos Iha Suco Aubeon no Aimetalaran /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Barique	Manatuto	Malaca Unip Lda	No. Kontratu : MOP-W-190233	\$ 162,377.94	Oct. 8, 2019	46.50%		46.50%	46.50%		46.50%
42	R4D Rural Periodic Maintenance Kaen Laran - Barique Chainage 0+000 - 9+000 & Routine, Hatularan-Cairui Chainage 0+000-9+800 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Manufahi Kiik Unip. Lda	MPW-W-W-190080	\$ 141,684.96	Aug. 25, 2019	41.78%		41.78%	41.78%		41.78%
43	R4D Rural Road Spot Improvement Agriculture Center - Aubeon Chainage 3+000-6+200	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	We"coi Unipessoal Lda	MPW-W-210062	\$ 343,111.47	June 10, 2021	44.80%	18.45%	63.25%	63.25%		63.25%

LISTA #ANEXU B

PROGRESSU FISIKU KADA FULAN																
					LOKALIZASAUN PROJETU						Jan-23			Feb-23		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress	This Month Progress	Kumulativo Progress	Previous Progress	This Month Progress	Kumulativo Progress
44	R4D Rural Road Spot Improvement Uma Boco - Agriculture Center Chainage 0+000 - 3+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Linoel	MPW-W-210061	\$ 296,211.82	June 10, 2021	18.83%		18.83%	18.83%		18.83%
45	R4D Rural Road Spot Improvement Kaen-Laran - Barique Chainage 0+000-9+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Gimso Brothers Unip. Lda	MPW-W-210058	\$ 300,792.46	July 10, 2021	88.60%		88.60%	88.60%	9.70%	98.30%
46	New construction of Gapura and gabion wall protection no jardim de herois de Natarbora	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTACAO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Barique	Manatuto	Senizu		\$ 408,460.73		84.79%	7.70%	92.49%	92.49%	1.34%	93.83%
47	New Installation MV, LV Line and House Connection from Lacto to Mantane - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Lacto	Manatuto	Anopa Electrical Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000421	\$ 380,582.61	Sept. 1, 2016	95.99%		95.99%	95.99%		95.99%
48	Emergency Rehabilitation Project in Subao Boo, Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lacto	Manatuto	Sahan I Unip.Lda	SSS/304/MOPTC-2016	\$ 3,314.56	Sept. 27, 2016	100.00%		100.00%	100.00%		100.00%
49	Routine Roads Maintenance - Lacto, Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lacto	Manatuto	Egana, Unip. Lda	MPW-W-190251	\$ 223,836.50	Dec. 13, 2019	68.89%		68.89%	68.89%		68.89%
50	Rehabilitation of Behau Mini Tradisional Food	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Lacto	Manatuto	Esa-Un	RDTL:74/GMTAC/XII/2015	\$ 50,745.00	May 2, 2016	38.83%		38.83%	38.83%		38.83%
51	Konstrusaun Mercado Komunitaria Kikan Ilmano	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	COMERCIO	Lacto	Manatuto	Surprise Unip. Lda	07/PDIM-II/MNTT/VIII/2016	\$ 153,942.39	Sept. 12, 2016	97.16%		97.16%	97.16%		97.16%
52	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Lacto	Manatuto	Sinohydro Corporation Limited	ICB/07/MPW-2014	\$ 48,314,975.87	May.3, 2016	87.98%		87.98%	87.98%	0.14%	88.12%
53	Konstrusaun ka Rehabilitasaun ba EBC Remanarun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Lacto	Manatuto	MEJD PKRIE EBC REMANARUN	-	\$ 98,147.27	Oct. 15, 2021	23.59%		23.59%	23.59%	7.06%	30.64%
54	Rehabilitation of Reinforced Concrete Ramp at Behau	MINISTERIO DA DEFESA	LM-BS	FLOOD CONTROL	Lacto	Manatuto	Baboe Unip Lda		\$ 189,578.02	May 23, 2022	52.07%		52.07%	52.07%	41.32%	93.39%

Prepara Husi:

1. Eng. Jose N. Carlos, Gusmão
Eng. ba Projeto Infrastrutura e Irigasaun
Municipiu Manatuto, ADN, I.P

3. Eng. Adonis Julio Fernandes
Eng. ba Projeto ME, ADN, I.P

2. Eng. Domingos D.X.Silva
Eng. ba Projeto Infrastrutura e Irigasaun
Municipiu Manatuto, ADN, I.P

4. Eng. Quico Agelino Junior
Eng. ba Projeto Infrastrutura e Irigasaun
Municipiu Manatuto, ADN, I.P

Verifika Husi:

Eng. Remigio da c.s dos Santos
Eng. Senior ba Projeto Infrastrutura e Irigasaun, ADN, I.P

Eng/Arq.Francisco Xavier de D. Jeronimo
Eng. Senior ba Porjecto Edificio Publico Bee no Saneamento,ADN,I.P

Eng. Decilindo de Fatima Marques
ChefeSeksau ME& ITC, ADN, I.P

Certifika Husi :

Eng. Emerenciana da Costa M.Freitas
Coordenadora Da Unidade de Controlo e Validacao De Qualidade ADN,I.P



ANEXO C2 (LA-8)

#ANEXU C2 (LA-8)

Projeitu : REHABILITATION OF REINFORCED CONCRETE RAMP AT BEHAU
Fatin Projeitu : Posto Administrativo Lacio, Municipio Manatuto
Contraktor : Baboe Unipessoal, Lda
No. kontratu :

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	PROGRESS PAYMENT BY A D N					
			PERCENT PREVIOUS	PERCENT PREVIOUS	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
		(US\$)	BILLING					
100	Mobilization and Demobilization	\$ 2,000.00	\$ 1,000.00	0.53%	\$ 2,450.00	1.29%	\$ 3,450.00	1.82%
200	Clearing and Grubbing	\$ 250.00	\$ 250.00	0.13%	\$ -	0.00%	\$ 250.00	0.13%
300	Remove of Existing Ramp	\$ 5,000.00	\$ 5,000.00	2.64%	\$ -	0.00%	\$ 5,000.00	2.64%
400	Geobags for Protection	\$ 73,006.50	\$ 73,006.50	38.51%	\$ -	0.00%	\$ 73,006.50	38.51%
500	Dewatering inside the Geobags protection	\$ 4,000.00	\$ -	0.00%	\$ 4,320.00	2.28%	\$ 4,320.00	2.28%
600	Lean Concrete	\$ 5,092.50	\$ -	0.00%	\$ 7,356.26	3.88%	\$ 7,356.26	3.88%
700	Reinforcing Steel	\$ 25,995.42	\$ -	0.00%	\$ 6,929.09	3.66%	\$ 6,929.09	3.66%
800	Structure Concrete Class A, 25 Mpa Concrete	\$ 38,918.00	\$ -	0.00%	\$ 31,207.47	16.46%	\$ 31,207.47	16.46%
900	Rouble Mount	\$ 7,047.20	\$ -	0.00%	\$ 3,032.71	1.60%	\$ 3,032.71	1.60%
1000	Precast Concrete A, 25 Mpa	\$ 8,800.00	\$ 19,459.00	10.26%	\$ 8,837.94	4.66%	\$ 28,296.94	14.93%
1100	Removal of Temporary Geobags for Protection	\$ 19,468.40	\$ -	0.00%	\$ 4,227.68	2.23%	\$ 4,227.68	2.23%
A	Construction Cost	\$ 189,578.02	\$ 98,715.50	52.07%	\$ 68,361.16	36.06%	\$ 167,076.66	88.13%
B	Profit (10% x A)		\$ -	0.00%	\$ 6,836.12	3.61%	\$ 16,707.67	8.81%
C	OverHead			0.00%	\$ 1,600.00	0.84%	\$ 1,600.00	0.84%
D	Tax 2 % x (A+B+C)		\$ -	0.00%	\$ 1,535.95	0.81%	\$ 3,707.69	1.96%
E	Contingency		\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
E	GRAND/GROSS TOTAL	\$ 189,578.02	\$ 98,715.50	52.07%	\$ 78,333.22	41.32%	\$ 189,092.01	93.39%

Inspeção Hui:

(Eng. José R. Carlos Gusmão)

Eng. ba Projecto Infraestrutura Transporte e Irigação Munisipiu Manatuto, ADN.I.P.

(Eng. Domingos D.X. Silva)

Eng. ba Projecto Infraestrutura Transporte e Irigação Munisipiu Manatuto, ADN.I.P.

Verifica Hui:

(Eng. Remigio da C.S. dos Santos)

Eng. Senior ba projeto Infraestrutura, Transporte e Irigasaun, ADN.I.P.

Sertifika hui:

Eng. Emerenciana da Costa Maia Freitas

Coordenadora da Unidade de Controlo e Validação de Qualidade, ADN.I.P.



#ANEXU C2 (LA-7)

Naran Projeitu: Konstrusaun ka Rehabilitasaun ba EBC Remanarun

Lokalidade : Suco Hatuermera, Posto Administrativo Laclo

Projeitu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY					PROGRESS BY A D N					
No	MAIN SUMMARY	Page No		Amount	PROGRESS PREVIOUS		PROGRESS FEBRUARY		TOTAL TO DATE	
					Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	PP/3		\$ 3.075,00	\$ 1.860,00	1,90%	\$ -	0,00%	\$ 1.860,00	1,90%
II	CLASSROOM BUILDING C	C/39	(i)	\$ 49.095,82	\$ 12.898,97	13,16%	\$ 6.916,10	7,06%	\$ 19.815,07	20,21%
III	TOILET BULDING Tb	TB/39	(i)	\$ 24.265,03	\$ 6.650,80	6,78%	\$ -	0,00%	\$ 6.650,80	6,78%
IV	PROVISIONAL SUM FOR SITE WORKS	SW/24	(i)	\$ 12.248,77	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
A	CONSTRUCTION COST			\$ 88.684,62	\$ 21.409,76	21,84%	\$ 6.916,10	7,06%	\$ 28.325,86	28,90%
B	CONTIGENCIA			\$ 3.000,00	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
C	OVERHEAD			\$ 6.340,00	\$ 1.712,50	1,75%	\$ -	0,00%	\$ 1.712,50	1,75%
D	GRAND TOTAL			\$ 98.024,62	\$ 44.532,03	23,59%	\$ 13.832,20	7,06%	\$ 58.364,23	30,64%

Prepara husi :

(Eng. Quico Adelino Junior)

Eng. ba Projeto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P.

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P.



#ANEXU C2 (BA - 9)

Naran Projeto : R4D RUAL ROAD SPOT IMROVEMENT, KEAN LARAN - BARIQUE CHAINAGE 0+000 - 9 + 000
No. kontratu : MPW - W - 210058
Postu : Barique
Suku : Barique
Naran Kompanhia : Gimso ,Unip. Lda

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	PROGRESS PAYMENT BY A D N					
			PREVIOUS BILLING (USD)	PERECENT PREVIOUS BILLING	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
		(US\$)						
R-01	General	\$ 2,980.11	\$ 2,980.11	0.99%	\$ -	0.00%	\$ 2,980.11	0.99%
R-03	Earth work	\$ 11,414.65	\$ 11,414.65	3.79%	\$ -	0.00%	\$ 11,414.65	3.79%
R - 05	Sub-base, Base and Pavement	\$ 32,040.00	\$ 32,040.00	10.65%	\$ -	0.00%	\$ 32,040.00	10.65%
R-08	Structures	\$ 181,126.91	\$ 168,939.02	56.16%	\$ 26,009.09	8.65%	\$ 194,948.11	64.81%
R-10	Dayworks	\$ 175.00	\$ 112.00	0.04%	\$ -	0.00%	\$ 112.00	0.04%
R-11	Routine Maintenance	\$ 14,384.50	\$ 10,580.50	3.52%	\$ -	0.00%	\$ 10,580.50	3.52%
R-15	Provisional Sum	\$ 200.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
A	Construction Cost	\$ 242,321.16	\$ 226,066.28	75.16%	\$ 26,009.09	8.65%	\$ 252,075.36	83.80%
B	Profit (10% x A)	\$ 24,232.12	\$ 22,606.63	7.52%	\$ 2,600.91	0.86%	\$ 25,207.54	8.38%
C	General Item	\$ 28,341.30	\$ 12,600.00	4.19%	\$ -	0.00%	\$ 12,600.00	4.19%
D	Tax 2 % x (A+B)	\$ 5,897.89	\$ 5,225.46	1.74%	\$ 572.20	0.19%	\$ 5,797.66	1.93%
E	GRAND/GROSS TOTAL	\$ 300,792.46	\$ 808.64	88.60%	\$ 29,182.20	9.70%	\$ 295,680.56	98.30%

Inspeksaun Husi:

Verifika Husi :

Sertifika husi :

1. (Eng.Domingos DX. Silva)

Eng. ba Projecto Infraestrutura Transporte e
Irigação Munisipiu Manatuto, ADN.I.P

(Eng. Remigio da c.s dos Santos)

Eng. Senior ba projeto Infraestrutura, Transporte e
Irigasaun, ADN.I.P

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade, ADN.I.P

2. (Eng. Jose R Carlos Gusmão)

Eng. ba Projecto Infraestrutura Transporte e
Irigação Munisipiu Manatuto, ADN.I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (BA-10) SUMMARY BOQ

PEMILIK PROYEK : MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA
LIBERTAÇÃO NACIONAL
NAMA PROYEK : NEW CONSTRUCTION OF GAPURA AND GABION WALL
PROTECTION IN GARDEN OF HEROES
LOKASI : NATARBORA - MANATUTO

SUMMARY

NO	URAIAN PEKERJAAN	ORIGINAL CONTRACT	PROGRESS BY A D N					
			PREVIOUS PROGRESS		PROGRESS FEBRUARY		PROGRESS TO DATE	
		TOTAL BIAYA (US\$)	AMOUNT	(%)	AMOUNT	(%)	AMOUNT	(%)
I	PERSIAPAN	\$ 6.550,00	\$ 4.600,00	1,13%	\$ -	0,00%	\$ 4.600,00	1,13%
II	KONSTRUKSI GAPURA	\$ 34.469,21	\$ 14.548,62	3,56%	\$ 4.879,37	1,19%	\$ 19.427,99	4,76%
III	PEMASANGAN BRONJONG	\$ 318.618,69	\$ 315.479,06	77,24%	\$ -	0,00%	\$ 315.479,06	77,24%
A	TOTAL	\$ 359.637,90	\$ 334.627,68	81,92%	\$ 4.879,37	1,19%	\$ 339.507,05	83,12%
B	CONTRACTOR FEE (10% x A)	\$ 35.963,79	\$ 33.462,77	8,19%	\$ 487,94	0,12%	\$ 33.950,71	8,31%
C	OVERHEAD	\$ 4.850,00	\$ 2.272,50	0,56%	\$ -	0,00%	\$ 2.272,50	0,56%
D	TAX (2% x (A+B+C))	\$ 8.009,03	\$ 7.407,26	1,81%	\$ 107,35	0,03%	\$ 7.514,61	1,84%
E	GRAND TOTAL (A+B+C+D)	\$ 408.460,73	\$ 377.770,21	92,49%	\$ 5.474,65	1,34%	\$ 383.244,86	93,83%

Prepara husi :

(Eng. Quico Adelino Junior)

Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)

Eng. Senior ba Edificio Publico no Agua Saneamento
ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P



REPÚBLICA DE TIMOR-LESTE
GOVERNO DA RAIA
MUNICÍPIO DE MANATUTO

#ANEXU C2 (SO - 3)

Road Name : Manlala(Manufahi Kiik) - Soibada Chainage start 0 + 000
Municipality : Manatuto Chainage end 2+000
Postu : Soibada Length 2.0 Km
Sukos : Manufahi Kiik

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST (US\$)	PROGRESS PAYMENT BY A D N					
			PREVIOUS BILLING (USD)	PERCENT PREVIOUS BILLING	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
R-01	General	\$ 2,990.00	\$ 2,970.00	1.46%	\$ -	0.00%	\$ 2,970.00	1.46%
R-03	Earth work	\$ 11,037.21	\$ 12,532.73	6.17%	\$ -	0.00%	\$ 12,532.73	6.17%
R-05	Sub-base, Base and Pavament	\$ 13,353.74	\$ 12,473.94	6.14%	\$ -	0.00%	\$ 12,473.94	6.14%
R-08	Structures	\$ 121,257.00	\$ 34,991.55	17.23%	\$ 5,604.02	2.76%	\$ 40,595.57	19.99%
R-10	Dayworks	\$ 1,750.00	\$ 175.00	0.09%	\$ -	0.00%	\$ 175.00	0.09%
R-11	Routine maintenance	\$ 4,205.00	\$ 4,205.00	2.07%	\$ -	0.00%	\$ 4,205.00	2.07%
R-15	Provisional sum	\$ 200.00	\$ 200.00	0.10%	\$ -	0.00%	\$ 200.00	0.10%
A	Construction Cost	\$ 154,792.95	\$ 67,548.22	33.27%	\$ 5,604.02	2.8%	\$ 73,152.24	36.0%
B	Profit & Over Head (10% x A)	\$ 15,479.29	\$ 6,754.82	3.33%	\$ 560.40	0.28%	\$ 7,315.22	3.60%
C	General Item	\$ 28,783.23	\$ 20,611.00	10.15%	\$ -	0.00%	\$ 20,611.00	10.15%
D	Tax 2 % x (A+B)	\$ 3,981.11	\$ 1,898.28	0.93%	\$ 123.29	0.06%	\$ 2,021.57	1.00%
E	GRAND/GROSS TOTAL	\$ 203,036.57	\$ 96,812.32	47.63%	\$ 6,287.71	3.10%	\$ 103,100.03	50.73%

Inspeksaun Husi:

1. (Eng. Domingos D.X. Silva)
Eng. ba Projecto Infraestrutura Transporte e
Irigação Munisipiu Manatuto, ADN.I.P

2. (Eng. José B. Carlos Gusmão)
Eng. ba Projecto Infraestrutura Transporte e
Irigação Munisipiu Manatuto, ADN.I.P

Verifika Husi :

(Eng. Remigio da C.S. dos Santos)
Eng. Senior ba projeto Infraestrutura,
Transporte e Irigasaun, ADN.I.P

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade, ADN.I.P



#ANEXU C2 (SO - 4)

PROJECT NAME

: R4D RURAL ROAD SPOT IMPROVEMENT, SOIBADA - FATUMAKEREK CHAINAGE 8+000 - 10+700

CONT.NUMBER

: MPW - W - 210060

SUCO

SASAH - FATUMAQUEREC

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST (US\$)	PROGRESS PAYMENT BY ADN					
			PREVIOUS BILLING (USD)	PERCENT PREVIOUS BILLING	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
R-01	General	\$ 3,040.00	\$ 1,550.00	0.79%	\$ 1,490.00	0.76%	\$ 3,040.00	1.55%
R-03	Earth Work	\$ 9,242.27	\$ 23,085.64	11.77%	\$ 6,947.06	3.54%	\$ 30,032.70	15.31%
R - 05	Sub-base, Base and Pavement	\$ 12,677.94	\$ 5,890.59	3.00%	\$ -	0.00%	\$ 5,890.59	3.00%
R - 08	Structure	\$ 119,043.38	\$ 28,815.41	14.69%	\$ 6,102.69	3.11%	\$ 34,918.09	17.81%
R-10	Dayworks	\$ 1,750.00	\$ 490.00	0.25%	\$ 105.00	0.05%	\$ 595.00	0.30%
R-11	Routine Maintenance	\$ 5,800.25	\$ 11,319.00	5.77%	\$ -5,549.80	-2.83%	\$ 5,769.20	2.94%
R-15	Provisional Sum	\$ 200.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
A	Construction Cost	\$ 151,753.84	\$ 71,150.63	36.28%	\$ 9,094.95	4.64%	\$ 80,245.58	40.9%
B	Profit (10% x A)	\$ 15,175.38	\$ 7,115.06	3.63%	\$ 909.50	0.46%	\$ 8,024.56	4.09%
C	General Item	\$ 25,337.67	\$ 18,252.70	9.31%	\$ -	0.00%	\$ 18,252.70	9.31%
D	Tax 2 % x (A+B)	\$ 3,845.34	\$ 1,565.31	0.98%	\$ 200.09	0.10%	\$ 2,130.46	1.09%
E	GRAND/GROSS TOTAL	\$ 196,112.23	\$ 98,083.71	50.20%	\$ 10,204.54	5.20%	\$ 108,653.30	55.40%

Inspeksaun Husi:

1. (Eng. José R. C. Gusmão)

Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Manatuto, ADN.I.P

2. (Eng. Domingo D.X.Silva)

Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Manatuto, ADN.I.P

Verifika Husi :

Eng. Aniceto da Costa

Eng. Senior ba projeto Infraestrutura,
Transporte e Irrigação, ADN.I.P

Sertifika husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e
Validação de Qualidade, ADN.I.P



#ANEXU C2 (SO-5)
SUMMARY BOQ

NARAN PROJEITO : REHABILITAÇÃO ESCRITÓRIO ESCOLA SECUNDÁRIA TÉCNICA VOCACIONAL SOIBADA

FATIN PROJEITO : MANLALA, SOIBADA, MANATUTO

NO	DESCRIPTION	AMOUNT \$	PROGRESS PAYMENT BY A D N					
			PREVIOUS PROGRESS		PROGRESS FEBRUARY		PROGRESS TO DATE	
			AMOUNT (US\$)	WEIGHT (%)	AMOUNT (US\$)	WEIGHT (%)	AMOUNT (US\$)	WEIGHT (%)
I	PRELIMINARIES (PEKERJAAN PERSIAPAN)	\$ 1.778,89	\$ 978,89	1,46%	\$ -	0,00%	\$ 978,89	1,46%
II	DEMOLITION, CONCRETE & FINISHES (Pek. bongkaran ,beton & Pek.finishes)	\$ 9.586,05	\$ 7.725,91	11,55%	\$ -357,08	-0,53%	\$ 7.368,83	11,01%
III	STEEL ROOF STRUCTURE & CEILING (Structur Atap Baja dan Plafond)	\$ 18.320,41	\$ 3.537,63	5,29%	\$ 4.917,09	7,35%	\$ 8.454,72	12,64%
IV	ROOFING (Pek. Atap)	\$ 6.442,56	\$ 6.442,56	9,63%	\$ -	0,00%	\$ 6.442,56	9,63%
V	WINDOWS AND DOORS (Pekerjaan Jendela dan Pintu)	\$ 8.047,00	\$ 6.245,00	9,34%	\$ -1.947,50	-2,91%	\$ 4.297,50	6,42%
VI	PAINTING (Pek. Pengecatan)	\$ 3.144,00	\$ 2.279,75	3,41%	\$ -328,42	-0,49%	\$ 1.951,33	2,92%
VII	PLUMBING AND DRAINAGE (Pek. perpipaan)	\$ 2.558,76	\$ 1.123,94	1,68%	\$ -	0,00%	\$ 1.123,94	1,68%
VIII	ELECTRICAL INSTALLATION (full installation)	\$ 2.545,75	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
IX	EXTERNAL ELECTRICAL SERVICES (full installation) (Instalasi listrik bagian luar)	\$ 1.238,64	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
X	EXTERNAL WATER SERVICE PLUMBING (Perpipaan air bersih)	\$ 249,47	\$ 249,47	0,37%	\$ -	0,00%	\$ 249,47	0,37%
XI	EXTERNAL SEWER DRAINAGE (Perpipaan air kotor bagian luar)	\$ 2.803,73	\$ 2.803,73	4,19%	\$ 59,21	0,09%	\$ 2.862,94	4,28%
XII	OVERHEAD							
A	CONSTRUCTION COST	\$ 56.715,25	\$ 31.386,88	46,92%	\$ 2.343,31	3,50%	\$ 33.730,18	50,42%
B	CONTRACTOR FEE (10% x A)	\$ 5.671,52	\$ 3.138,69	4,69%	\$ 234,33	0,35%	\$ 3.373,02	5,04%
C	OVERHEAD	\$ 3.200,00	\$ 1.600,00	2,39%	\$ -	0,00%	\$ 1.600,00	2,39%
D	TAX (2% x (A+B+C)	\$ 1.311,74	\$ 722,51	1,08%	\$ 51,55	0,08%	\$ 774,06	1,16%
E	CONTINGENCY (10% X A)	\$ -	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
F	GRAND TOTAL (A+B+C+D+E)	\$ 66.898,51	\$ 36.848,07	55,08%	\$ 2.629,19	3,93%	\$ 39.477,26	59,01%

Prepara husi :

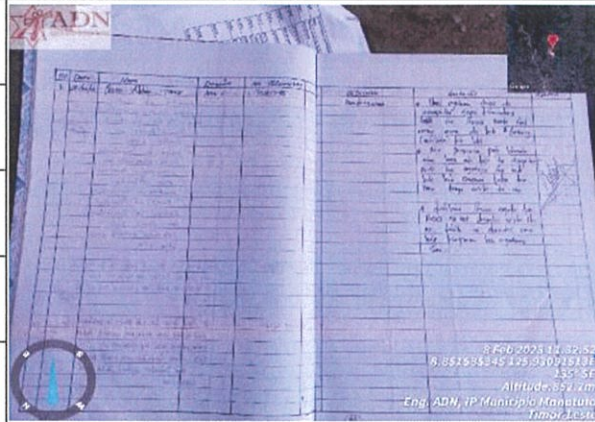

(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto,ADN,I.P

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no
Agua Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação
de Qualidade ADN,I.P

REPÚBLICA DEMOCRÁTICA DE TIMOR-LESTE MINISTÉRIO DO PLANO E ORDENAMENTO VII GOVERNO CONSTITUCIONAL ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					#ANEXU D (SO-6) INSTRUSAUN / REKOMENDASAUN			
Konstrusaun ka Rehabilitasaun ba EBC Weaihudik								
Kompanha : GRUPO KOMUNITARIO WEAIHUDIK								
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura
I	08/02/2023	Manatuto/Soibada	Quico Adelino Junior	Tek A D N, IP	1	Husu enjinheiru grupu atu akompanha grupu komunitariu iha servisu monta steel roofing ninian atu bele centering (niveladu) tuir lolos.		
					2	Ba pengecoran parte varanda nian husu atu bele iha akompanhamentu husi enjinheiru sira hodi bele halo campuran beton tuir mix design ne'ebe iha ona.		
					3	Kontinua servisu nafatin tuir BOQ no mos dezenhu ne'ebe iha ona, karik iha duvidas ruma bele komfirma ho enjinheiru sira.		
					4			
					5			



#ANEXU C2 (SO-6) SUMMARY BOQ

Naran Projeitu: Konstrusaun ka Rehabilitasaun ba EBC Weaihudik
Lokalidade : Manufahi Ki'ik, Posto Administrativo Soibada
Projeitu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY				ORIGINAL CONTRACT	PROGRESS BY A D N					
No	MAIN SUMMARY		Page No	Amount	PROGRESS PREVIOUS		PROGRESS FEBRUARY		TOTAL TO DATE	
					Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES		PP/3	\$ 3.075,00	\$ 1.975,00	1,93%	\$ -	0,00%	\$ 1.975,00	1,93%
II	CLASSROOM BUILDING C		C/39 (i)	\$ 51.164,59	\$ 16.719,65	16,31%	\$ 4.196,86	4,09%	\$ 20.916,52	20,40%
III	TOILET BULDING Tb		TB/39 (i)	\$ 25.091,96	\$ 8.855,65	8,64%	\$ -	0,00%	\$ 8.855,65	8,64%
IV	PROVISIONAL SUM FOR SITE WORKS		SW/24 (i)	\$ 13.840,76						
A	CONSTRUCTION COST			\$ 93.172,31	\$ 27.550,31	26,88%	\$ 4.196,86	4,09%	\$ 31.747,17	30,97%
B	CONTIGENCIA			\$ 3.000,00						
C	OVERHEAD			\$ 6.340,00	\$ 1.210,00	1,18%	\$ -	0,00%	\$ 1.210,00	1,18%
D	GRAND TOTAL			\$ 102.512,31	\$ 28.760,31	28,06%	\$ 4.196,86	4,09%	\$ 32.957,17	32,15%

Prepara husi :

(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P.

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

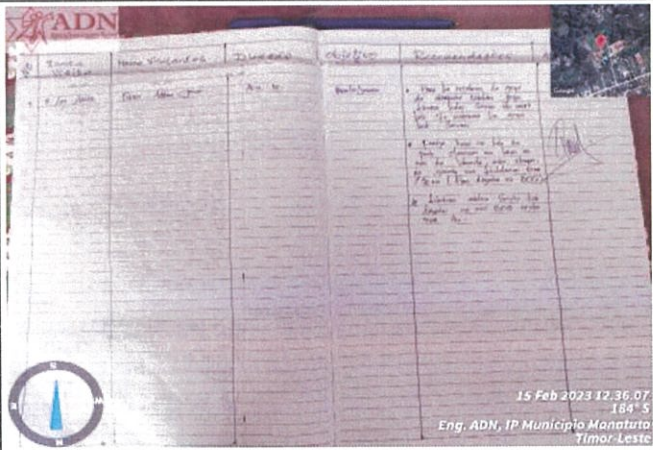
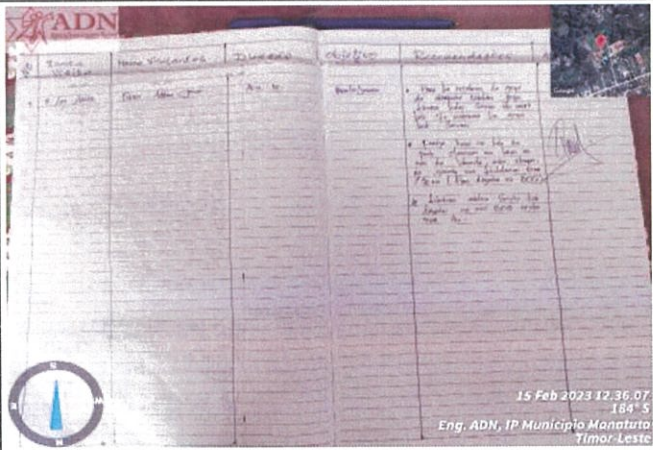
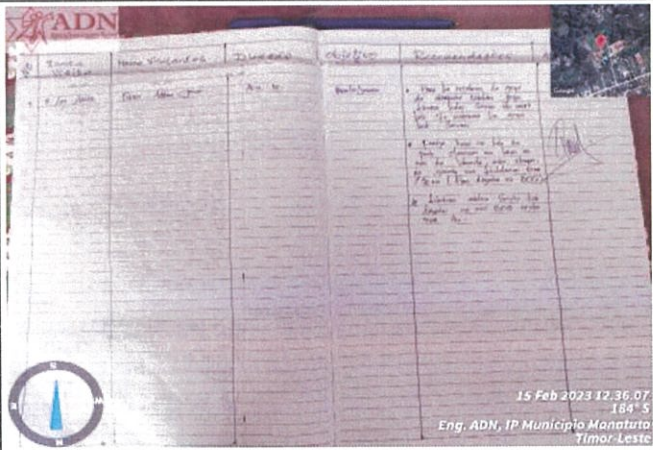
Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P



2023

Naran Eng.	Quico Adelino Junior							2023																												
Município	MUNICIPIO MANATUTO NO POSTOS																																			
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Fevereiro																												OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
MANATUTO VILA (MV)	3	Construção de novo Estadio de Futebol em Manatuto	Obrai Unipesoal, Lda	ICB/0128/SEJD-2014	FI	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	Plan	1			4	5								10										24	25	26	27	28	On Going	
							Actual																													
	6	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	Carya Timor Leste Unip. Lda	08/PDIM-I/MNTT/XII/2019	PDIM	ESTATAL	Plan	1												10										24					On Going	
							Actual																													
	7	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	Carya Timor Leste Lda	01/PDIM-I/MNTT/XII/2019	PDIM	ESTATAL	Plan	1												10										24					On Going	
							Actual																													
	8	Servisu Manutensaun Edifisiu CRC Munisipiu Manatuto	Baboe Unip Lda	019/Janeiro/2020	LM	MINISTERIO DA JUSTICA	Plan	1												10										24					On Going	
							Actual																													
	9	Konstrusaun Fatin Isolamentu iha Munisipiu Manatuto	Talamori Unip,Lda	RDTL-MS-DNA-DC-20-254	Fundo Covid-19	MINISTERIO SAUDE	Plan	1													10										24					On Going
							Actual																													
	10	New Construction of Fence at Izolation Covid-19 in Ma'abat Manatuto Municipality	MINISTERIO SAUDE	RDTL-MS-C19-DNA-DC-21-227	Fundo Covid-19	MINESTERIO SAUDE	Plan	1													10										24					On Going
							Actual																													
	11	Supplay and Installation Main Power For Isolation an Laboratorium Building Maabat Manatuto	MINISTERIO SAUDE	RDTL-MS-C19-DNA-DC-21-229	Fundo Covid-19	MINESTERIO SAUDE	Plan		2													10									24					On Going
							Actual																													
	12	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MEJD PKRIE ESG KAY RALA	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		2													10									24					On Going
							Actual																													
	13	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MEJD PKRIE EBF RENTAU	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		2													10									24					On Going
							Actual																													
	14	Konstrusaun ka Rehabilitasaun ba PE Rembor	MEJD PKRIE PE REMBOR	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		2												10										24					On Going
							Actual																													
15	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MEJD PKRIE EBF OBRATO	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		2												10										24					On Going	
						Actual																														

 MINISTERIO DO PLANO E ORDINAMENTO VEL GOVERNO CONSTITUCIONAL  ADN, IP Agência de Desenvolvimento Nacional, Instituto Público <tr><td colspan="5"></td><td colspan="3">#ANEXU D (LAC-8) INSTRUSAUN / REKOMENDASAUN</td></tr> <tr><td colspan="5"></td><td colspan="3">Konstrusaun ka Rehabilitasaun ba EBF Batara</td></tr> <tr><td colspan="5"></td><td colspan="3">Kompanha : GRUPO KOMUNITARIO BATARA</td></tr> <tr><th>No</th><th>Data inspesaun</th><th>Municipiu / Posto</th><th>Naran Eng.</th><th>Pozisaun</th><th>No</th><th>INSTRUSAUN / REKOMENDASAUN</th><th>Fotografia</th><th>Asinatura</th></tr> <tr><td rowspan="4">I</td><td rowspan="4">15/02/2023</td><td rowspan="4">Laclubar</td><td rowspan="4">Quico Adelino Junior</td><td rowspan="4">Tek A D N, IP</td><td>1</td><td>Husu na anjinheiru do grupo atu akompanga wainhira grupo komesa halao servisu atu nune'e bele fo instrusaun ba grupo hodi servisu.</td><td rowspan="4"></td><td rowspan="4"></td></tr> <tr><td>2</td><td>Presija hasai rai balu iha parte classroom nia laran no mos iha varanda , antes stamper , no garante nia kedalaman 50mm / 70mm (hare tuir dezenhu no mos BOQ).</td></tr> <tr><td>3</td><td>Kontinua aselera servisu tuir dezenhu no mos BOQ ne'ebe mak iha.</td></tr> <tr><td></td><td></td></tr>										#ANEXU D (LAC-8) INSTRUSAUN / REKOMENDASAUN								Konstrusaun ka Rehabilitasaun ba EBF Batara								Kompanha : GRUPO KOMUNITARIO BATARA			No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura	I	15/02/2023	Laclubar	Quico Adelino Junior	Tek A D N, IP	1	Husu na anjinheiru do grupo atu akompanga wainhira grupo komesa halao servisu atu nune'e bele fo instrusaun ba grupo hodi servisu.			2	Presija hasai rai balu iha parte classroom nia laran no mos iha varanda , antes stamper , no garante nia kedalaman 50mm / 70mm (hare tuir dezenhu no mos BOQ).	3	Kontinua aselera servisu tuir dezenhu no mos BOQ ne'ebe mak iha.		
					#ANEXU D (LAC-8) INSTRUSAUN / REKOMENDASAUN																																															
					Konstrusaun ka Rehabilitasaun ba EBF Batara																																															
					Kompanha : GRUPO KOMUNITARIO BATARA																																															
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura																																												
I	15/02/2023	Laclubar	Quico Adelino Junior	Tek A D N, IP	1	Husu na anjinheiru do grupo atu akompanga wainhira grupo komesa halao servisu atu nune'e bele fo instrusaun ba grupo hodi servisu.																																														
					2	Presija hasai rai balu iha parte classroom nia laran no mos iha varanda , antes stamper , no garante nia kedalaman 50mm / 70mm (hare tuir dezenhu no mos BOQ).																																														
					3	Kontinua aselera servisu tuir dezenhu no mos BOQ ne'ebe mak iha.																																														



#ANEXU C2 (LAC-8)

TÍTULO DO PROJECTO : KONSTRUSAUN KA REHABILITASAUN BA EBF BATARA
FATIN PROJEITO : BATARA, MANATUTO
DONO DO PROJEITO : MINISTÉRIO DA EDUCAÇÃO JUVENTUDE E DESPORTO

NO.	MAIN SUMMARY WORK DESCRIPTION	ORIGINAL CONTRACT AMOUNT US\$	WEIGHT (%)	REPORT PROGRESS BY ADN IP					
				Previous Progress		Progress February		Up to Date	
				Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	\$ 3.575,00	3,50%	\$ 2.195,00	2,15%	\$ -	0,00%	\$ 2.195,00	2,15%
II	DEMOLITION	\$ 300,00	0,29%	\$ 300,00	0,29%	\$ -	0,00%	\$ 300,00	0,29%
III	CLASSROOM BUILDING	\$ 50.717,94	49,69%	\$ 30.690,27	30,07%	\$ 2.078,40	2,04%	\$ 32.768,68	32,11%
IV	TOILET BUILDING	\$ 25.427,93	24,91%	\$ 9.992,28	9,79%	\$ 5.149,29	5,05%	\$ 15.141,57	14,84%
V	PROVISIONAL SUM FOR SITEWORK	\$ 12.700,12	12,44%	\$ -	0,00%		0,00%	\$ -	0,00%
A	CONSTRUCTION COST	\$ 92.720,99	90,85%	\$ 43.177,55	42,31%	\$ 7.227,69	7,08%	\$ 50.405,24	49,39%
B	CONTIGENCY	\$ 3.000,00	2,94%	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
C	OVERHEAD	\$ 6.340,00	6,21%	\$ 2.204,50	2,16%	\$ -	0,00%	\$ 2.204,50	2,16%
D	GRAND TOTAL	\$ 102.060,99	100,00%	\$ 45.382,05	44,47%	\$ 7.227,69	7,08%	\$ 52.609,74	51,55%

Prepara Husi :

(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico no Agua
Saneamento Municipio Manatuto, ADN, I.P.

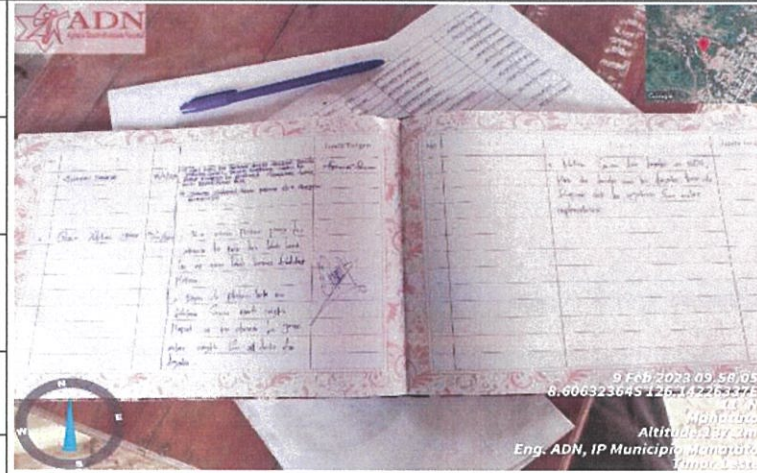
Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN,I.P

 MINISTERIO DO PLANO E ORDENAMENTO VII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					#ANEXU D1 (LAC-10) INSTRUSAUN / REKOMENDASAUN			
					Projetu : Konstrusaun Postu Saude Funar, Laclubar			
					Kompanhia : MERCY UNIP. LDA			
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura
I	15/02/2023	Funar, Laclubar	Quico Adelino Junior	Enginheiru ADN IP Municipiu Manatuto	1	Husu engenheiru atu tau atensaun ba pambesian top beam ninian, mantem jarak tuir dezenhu ba nia tulangan pokok no mos tulangan sengkang sira		
					2	Presija monta beton tahu hodi garante selimut beton tuir dezenhu.		
					3	Husu kompanhia antes pengecoran presija envia karta ba lab. Obras no cc ba lab. ADN IP atu halo akompanhamentu ba pengecoran top beam no mos dak beton teras ninian		
					4	Enjinheiru kontinua fo assistensia tekniku ba trabalhador sira hodi servisu tuir dezenhu no mos BOQ.		
					5			

 MINISTÉRIO DO PLANO E ORDENAMENTO VIA GOVERNO CONSTITUCIONAL ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					#ANEXU D (LAL-3) INSTRUSAUN / REKOMENDASAUN			
Naran projeto : Konstrusaun ka Rehabilitasaun ba EP Cairui								
Kompanha : GRUPO KOMUNITARIO CAIRUI								
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura
I	09/02/2023	Manatuto Vila	Quico Adelino Junior	Tek A D N, IP	1	Ba servisu Plesteran presija tau atensaun ba kadar be'e labele barak liu atu nune'e labele hamenus kualidade plesteran.		
					2	Depois de plesteran bele ona kontinua servisu monta rangka plafond, no tau atensaun ba jarak antara rangka sira tenki tuir dezenhu.		
					3	Kontinua servisu tuir dezenhu no mos BOQ, karik iha duvida ruma ho dezenhu , husu atu komfirma uluk ho enjinheiru sira molok implementasaun.		
					4			
					5			



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (LAL-3) SUMMARY BOQ

Naran Projeitu: Konstrusaun ka Rehabilitasaun ba EP Cairui

Lokalidade : Suco Cairui, Posto Administrativo Laleia

Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

NO	MAIN SUMMARY	ORIGINAL CONTRACT		PROGRESS BY A D N					
		Page No	AMOUNT	PREVIOUS PROGRESS		PROGRESS FEBRUARY		TOTAL TO DATE	
				Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	PP/3	\$ 3.075,00	\$ 1.725,00	1,99%	\$ -	0,00%	\$ 1.725,00	1,99%
II	CLASSROOM BUILDING C2	C2/47 (i)	\$ 58.021,79	\$ 18.949,08	21,81%	\$ 16.660,38	19,18%	\$ 35.609,45	40,99%
III	PROVISIONAL SUM FOR SITE WORKS	SW/20 (i)	\$ 7.901,93	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
A	CONSTRUCTION COST		\$ 68.998,72	\$ 20.674,08	23,80%	\$ 16.660,38	19,18%	\$ 37.334,45	42,97%
B	CONTIGENCIA		\$ 3.000,00	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
C	OVERHEAD		\$ 6.340,00	\$ 1.220,00	1,40%	\$ 1.560,00	1,80%	\$ 2.780,00	3,20%
D	GRAND TOTAL		\$ 86.883,29	\$ 21.894,08	25,20%	\$ 18.220,38	20,97%	\$ 40.114,45	46,17%

Prepara husi :



(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P.

Verifika Husi :


(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :


(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P.

 MINISTÉRIO DO PLANO E ORDENAMENTO VII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					#ANEXU D (MV-10) INSTRUSAUN / REKOMENDASAUN			
					Naran projeto : New Construction Fence			
					Kompanha : K6 Unipesoal, Lda			
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura
I	16/02/2023	Manatuto Vila	Quico Adelino Junior	Tek A D N, IP	1	Husu enjinheiru kompanhia atu komfirma didiak design beton ba security pos ninian molok halo pengecoran. Karik nia design ba mutu beton la hanesan ho mutu beton kolom ba fence nian , presija envia fila fali carta ba lab. Obras publica hodi halo akompanhamento no foti sampel beton hodi ba test iha lab. obras hodi bele pasa sertifikadu beton ba security post ninian.		
					2	Enjinheiru tenki halo akompanhamentu ba badaen sira atu garante servisu tuir dezenhu no mos BOQ.		
					3			



#ANEXU C2 (MV-12) SUMMARY BOQ

Naran Projeto: Reabilitação do Escritório, ID Emis - 1096
Lokalidade : Suco Aiteas, Posto Administrativo Manatuto
Projeto nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

NO.	MAIN SUMMARY	Page No	ORIGINAL CONTRACT		PROGRESS BY A D N					
				Amount	PREVIOUS PROGRESS		PROGRESS FEBRUARY		TOTAL TO DATE	
					Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	PP/3		\$ 3.075,00	\$ 2.125,00	3,37%	\$ -	0,00%	\$ 2.125,00	3,37%
II	REFURBISHED TEACHER OFFICE BUILDING Rf	RF/51	(i)	\$ 50.581,84	\$ 17.971,62	28,53%	\$ 7.523,62	11,94%	\$ 25.495,24	40,47%
A	CONSTRUCTION COST			\$ 53.656,84	\$ 20.096,62	31,90%	\$ 7.523,62	11,94%	\$ 27.620,24	43,84%
B	CONTIGENCIA			\$ 3.000,00	\$ -	0%	\$ -	0%	\$ -	0,00%
C	OVERHEAD			\$ 6.340,00	\$ -	0%	\$ 2.820,00	4,48%	\$ 2.820,00	4,48%
D	GRAND TOTAL			\$ 62.996,84	\$ 20.096,62	31,90%	\$ 10.343,62	16,42%	\$ 30.440,24	48,32%

Prepara husi :

(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P

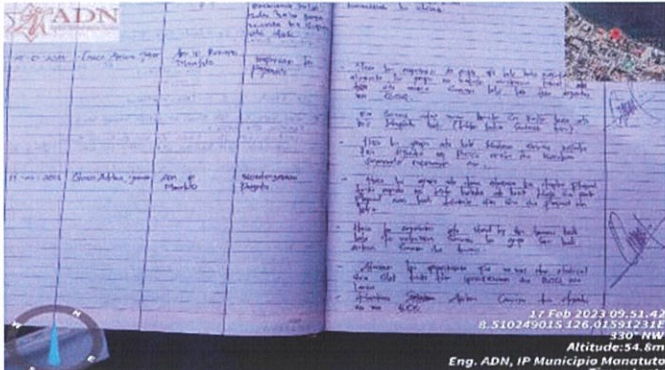
Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P

**Kompanha : GRUPO KOMUNITARIO RENTAU**

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura
I	17/02/2023	Manatuto Vila	Quico Adelino Junior	Engenheiru ADN IP Municipiu Manatuto	1	Husu ba grupo atu toma atensaun ba triplex plafond tenki rapidu no keta haluha atu husik kuak iha parte plafond nian hodi kontrola fiu sira iha plafond nia leten.		
					2	Husu enjinheiru atu stand by iha terrenu hodi bele fo instrusaun servisu ba grupo sira hodi aselera servisu iha terrenu.		
					3	Atensaun ba spesifikasaun fiu no mos item electrical sira seluk tenke tuir spesifikasaun ne'ebe iha BOQ nia laran		
					4	Kontinua aselera servisu tuir dezenhu no mos BOQ.		



#ANEXU C2 (MV-13)

SUMMARY BOQ

Naran Projeitu: Konstrusaun ka Rehabilitasaun ba EBF Rentau
Lokalidade : Suco Aiteas, Posto Administrativo Manatuto
Projeitu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY		ORIGINAL CONTRACT		PROGRESS REPORT BY A D N					
No	MAIN SUMMARY	Page No	Amount	Progress Previous		Progress February		Total To Date	
				Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	PP/3	\$ 3,075.00	\$ 1,950.00	3.03%	\$ -	0.00%	\$ 1,950.00	3.03%
II	CLASSROOM BUILDING C	C/39	\$ 48,345.34	\$ 32,287.18	50.15%	\$ 983.62	1.53%	\$ 33,270.80	51.68%
III	PROVISIONAL SUM FOR SITE WORKS	SW/10	\$ 3,623.16	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
A	CONSTRUCTION COST		\$ 55,043.50	\$ 34,237.18	53.18%	\$ 983.62	1.53%	\$ 35,220.80	54.70%
B	CONTINGENCY		\$ 3,000.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
C	OVERHEAD		\$ 6,340.00	\$ 1,795.00	2.79%	\$ -	0.00%	\$ 1,795.00	2.79%
D	GRAND TOTAL		\$ 64,383.50	\$ 36,032.18	55.96%	\$ 983.62	1.53%	\$ 37,015.80	57.49%

Prepara husi :

(Eng. Quico Adelino Junior)
Eng. ba Projeitu Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P.

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua Saneamento
ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (MV-14) SUMMARY BOQ

Naran Projetu: Konstrusaun ka Rehabilitasaun ba PE Rembor
Lokalidade : Suco Aiteas, Posto Administrativo Manatuto
Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

NO	MAIN SUMMARY	ORIGINAL CONTRACT		PROGRESS BY A D N					
		Page No	AMOUNT	PREVIOUS PROGRESS		PROGRESS FEBRUARY		PROGRESS TO DATE	
				Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	PP/3 (i)	\$ 3.075,00	\$ 1.787,50	2,01%	\$ 62,50	0,07%	\$ 1.850,00	2,08%
II	CLASSROOM BUILDING C2	C2/47 (i)	\$ 57.778,14	\$ 22.837,03	25,68%	\$ 12.306,56	13,84%	\$ 35.143,59	39,52%
III	PROVISIONAL SUM FOR SITE WORKS	SW/23 (i)	\$ 9.959,28	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
A	CONSTRUCTION COST		\$ 70.812,42	\$ 24.624,53	27,69%	\$ 12.369,06	13,91%	\$ 36.993,59	41,60%
B	CONTIGENCIA		\$ 3.000,00	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
C	OVERHEAD		\$ 6.340,00	\$ 1.620,00	1,82%	\$ 1.690,00	1,90%	\$ 3.310,00	3,72%
D	GRAND TOTAL		\$ 88.918,34	\$ 26.244,53	29,52%	\$ 14.059,06	15,81%	\$ 40.303,59	45,33%

Prepara husi :

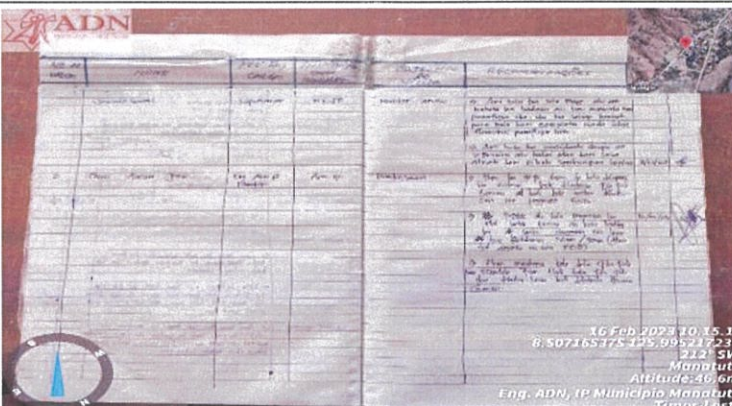
(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P.

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P

 MINISTERIO DO PLANO F. ORDENAMENTO VI GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					#ANEXU D (MV-15) INSTRUSAUN / REKOMENDASAUN			
					Naran projeto : Konstrusaun ka Rehabilitasaun ba EBF Obrato			
					Kompanha : GRUPO KOMUNITARIO OBRATO			
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Fotografia	Asinatura
I	16/02/2023	Manatuto Vila	Quico Adelino Junior	Tek A D N, IP	1	Husu ba grupo depois de halo kompras ba material, bele kontinua fila fali servisu hodi bele aselera kontrusaun nia progressu fiziku.		
					2	Molok atu halo pengecoran ba plat lantai presija atu halo leveling ba lantai classroom nia laran to kedalaman 50mm/70mm (hare'e dezenhu no mos BOQ).		
					3	Husu enjinheiru bele kria fila fali time schedule foun hodi taka fila fali iha kantor laran hodi kontrola horariu servisu.		
					4			
					5			



#ANEXU C2 (MV-15) SUMMARY BOQ

Naran Projetu: Konstrusaun ka Rehabilitasaun ba EBF Obrato

Lokalidade : Suco Sau, Posto Administrativo Manatuto

Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY		ORIGINAL CONTRACT		PROGRESS BY A D N					
No	MAIN SUMMARY	Page No	Amount	Previous Progress		Progress February		Total To Date	
				Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)	Amount (US\$)	Weigth (%)
I	PRELIMINARIES	PP/3	\$ 3.075,00	\$ 1.975,00	2,99%	\$ -	0,00%	\$ 1.975,00	2,99%
II	CLASSROOM BUILDING C	C/39 (i)	\$ 48.332,46	\$ 21.902,69	33,11%	\$ 10.595,80	16,02%	\$ 32.498,49	49,13%
III	PROVISIONAL SUM FOR SITE WORKS	SW/11 (i)	\$ 5.397,19	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
A	CONSTRUCTION COST		\$ 56.804,65	\$ 23.877,69	36,10%	\$ 10.595,80	16,02%	\$ 34.473,49	52,12%
B	CONTINGENCY		\$ 3.000,00	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
C	OVERHEAD		\$ 6.340,00	\$ 1.372,50	2,07%	\$ -	0,00%	\$ 1.372,50	2,07%
D	GRAND TOTAL		\$ 66.144,65	\$ 25.250,19	38,17%	\$ 10.595,80	16,02%	\$ 35.845,99	54,19%

Prepara husi :

(Eng. Quico Adelino Junior)
Eng. ba Projeto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P.

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Eng. Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P.



#ANEXU C2 (MV-17)

SUMMARY

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA BASICA CENTRAL VASCO DA GAMA
FATIN PROJEITO : AITEAS, MANATUTO
DONO DO PROJEITO : MINISTERIO DA EDUCAÇÃO JUVENTUDE E DESPORTO

NO	ITEM SERVISU	AMOUNT US\$	PROGRESS BY A D N IP					
			Previous Progress		Progress February		Total to Date	
			Amount (US\$)	%	Amount (US\$)	%	Amount (US\$)	%
i	PRELIMINARIES WORKS	\$ 6.300,00	\$ 2.137,50	1,17%	\$ -	0,00%	\$ 2.137,50	1,17%
ii	CLASSROOM BUILDING C	\$ 49.620,84	\$ 3.924,82	2,15%	\$ -	0,00%	\$ 3.924,82	2,15%
iii	TEACHER OFFICE	\$ 67.466,67	\$ 3.428,09	1,88%	\$ 4.634,93	2,54%	\$ 8.063,02	4,41%
iv	TOILET BUILDING Tb	\$ 17.325,64	\$ 910,39	0,50%	\$ -	0,00%	\$ 910,39	0,50%
v	SITEWORKS	\$ 15.136,11	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
A	CONSTRUCTION COST	\$ 155.849,26	\$ 10.400,81	5,69%	\$ 4.634,93	2,54%	\$ 15.035,74	8,23%
B	CONTRACTOR FEE (10% x A)	\$ 15.584,93	\$ 1.040,08	0,57%	\$ 463,49	0,25%	\$ 1.503,57	0,82%
C	OVERHEAD	\$ 3.100,00	\$ 775,00	0,42%	\$ -	0,00%	\$ 775,00	0,42%
D	TAX (2% x (A+B+C))	\$ 3.490,68	\$ 244,32	0,13%	\$ 101,97	0,06%	\$ 346,29	0,19%
E	CONTIGENCY	\$ 4.679,68	\$ -	0,00%	\$ -	0,00%	\$ -	0,00%
F	TOTAL COST (A + B + C + D + E)	\$ 182.701,57	\$ 12.460,20	6,82%	\$ 5.200,39	2,85%	\$ 17.660,60	9,67%

Prepara Husi :

(Eng. Quico Adelino Junior)
Eng. ba Projecto Edificio Publico no Agua Saneamento
Municipio Manatuto, ADN, I.P.

Verifika Husi :

(Arch. Francisco Xavier De D. Jeronimo)
Engenheiro Senior ba Edificio Publico no Agua
Saneamento ADN, I.P.

Sertifika husi :

(Eng. Emerenciana Da Costa Maia)
Kordenadora da Unidade de Controlo e Validasaun
de Kualidade ADN, I.P.



#ANEXU C2 (LA- 6)

Project Name : National Road No. 1 Upgrading Project Dili-Manatuto (Package A01-01)
Contractor : SINOHYDRO Corporation Limited
Cover Period: : May, 25, 2022-Jun, 24 2022
IPC no. : 22 (Performance Based and Maintenance 01)

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
I	GENERAL REQUIREMENTS	\$ 2,117,704.79	\$ 2,477,289.04	5.13%	\$ -	0.00%	\$ 2,477,289.04	5.13%	\$ (359,584.25)
II	OTHER GENERAL REQUIREMENTS	\$ 60,741.33	\$ 100,090.78	0.21%	\$ -	0.00%	\$ 100,090.78	0.21%	\$ (39,349.45)
III	MAIN HIGHWAY AND ROADWORKS	\$ 21,727,995.40	\$ 22,260,906.29	46.07%	\$ -	0.00%	\$ 22,260,906.29	46.07%	\$ (532,910.89)
IV	BRIDGE CONSTRUCTION	\$ 3,335,858.97	\$ 3,046,622.76	6.31%	\$ -	0.00%	\$ 3,046,622.76	6.31%	\$ 289,236.21
V	DRAINAGE IMPROVEMENT WORKS	\$ 5,657,802.38	\$ 4,912,939.99	10.17%	\$ -	0.00%	\$ 4,912,939.99	10.17%	\$ 744,862.39
VI	SLOPE PROTECTION WORKS	\$ 8,976,499.18	\$ 6,684,281.94	13.83%	\$ -	0.00%	\$ 6,684,281.94	13.83%	\$ 2,292,217.24
VII	MISCELLANEOUS STRUCTURES	\$ 1,940,034.97	\$ 1,744,400.25	3.61%	\$ -	0.00%	\$ 1,744,400.25	3.61%	\$ 195,634.72
VIII	BIO-ENGINEERING WORKS	\$ 223,524.79	\$ 129,155.84	0.27%	\$ -	0.00%	\$ 129,155.84	0.27%	\$ 94,368.95
DW	DAYWORKS	\$ 955,457.75	\$ 749,699.96	1.55%	\$ -	0.00%	\$ 749,699.96	1.55%	\$ 205,757.79
IX	PROVISIONAL SUM	\$ 294,000.00	\$ 400,631.29	0.83%	\$ -	0.00%	\$ 400,631.29	0.83%	\$ (106,631.29)
X	CONTINGENCIES	\$ 1,200,000.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%	\$ 1,200,000.00
	TOTAL =	\$ 46,489,619.56	\$ 42,506,020.32	87.98%	\$ -	0.00%	\$ 42,506,020.32	87.98%	\$ 3,983,599.24
	PERFORMANCE BASED MAINTENANCE	\$ 1,825,356.19	\$ -	0.00%	\$ 69,921.06	0.14%	\$ 69,921.06	0.14%	\$ 1,755,435.13
	CONTRACT AMOUNT	\$ 48,314,975.87	\$ 42,506,020.32	87.98%	\$ 69,921.06	0.14%	\$ 42,575,941.38	88.12%	\$ 5,739,034.48
	GRAND TOTAL	\$ 48,314,975.87	\$ 42,506,020.32	87.98%	\$ 69,921.06	0.14%	\$ 42,575,943.56	88.12%	\$ 5,739,032.31

Inspeksaun Husi:

1. (Eng. José R Carlos Gusmão)
Eng. ba Projecto Infraestrutura
Transporte e Irrigação Munisipiu
Manatuto, ADN, I.P.

2. (Eng. Domingos da C.X Silva)
Eng. ba Projecto Infraestrutura
Transporte e Irrigação Munisipiu
Manatuto, ADN, I.P.

3. (Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projecto (Imprestimo)
ADN, I.P.

3. (Eng. Vidal Guterres)
Eng. PMU ba Projecto (Imprestimo)
ADN, I.P.

Verifika Husi :

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba projeto Infraestrutura,
Transporte e Irigasaun, ADN, I.P.

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN, I.P.

Naran Eng.		Quico Adelino Junior						2023																												
Município		MUNICIPIO MANATUTO NO POSTOS																																		
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Fevereiro																												OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
	16	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MEJD PKRIE EBF BAHADIK	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																												On Going	
							Actual																													
	17	Konstrusaun EBC Vasco da Gama - Manatuto	Parapa Bemizu Stae Unipessoal Lda	-	LM-CD	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																												On Going	
							Actual																													
L A L E A (L A L)	1	Rehabilitasaun Kampu Foteboll iha Postu Administrativu Laleia	DCO Unip.Lda	011LM/AND/MPIE/VII/DILI/2019/E DIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																											On Going		
							Actual																													
	3	Konstrusaun ka Rehabilitasaun ba EP Cairui	MEJD PKRIE EP CAIRUI	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																											On Going		
							Actual																													
L A C L U B A R (L A C)	7	Kontinusaun Konst. Postu Saude Iha Suku Fatumakerek	Hatuwari Unip. Lda	02/PDD-II/MNTT/VII/2015	PDIM	MINISTERIO SAUDE	Plan																											On Going		
							Actual																													
	8	Konstrusaun ka Rehabilitasaun ba EBF Batara	MEJD PKRIE EBF BATARA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																											On Going		
							Actual																													
	9	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MEJD PKRIE EBF AISIU-UM		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																											On Going		
							Actual																													
	10	Konstrusaun Posto Saude Iha iha Suku Funar - Lklubar	Mercy Unipessoal Lda.		PDIM	MINISTERIO SAUDE	Plan																											On Going		
							Actual																													



Naran Eng.	Quico Adelino Junior							2023																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
Município	MUNICIPIO MANATUTO NO POSTOS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Fevereiro																												OBS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
SOIBADA (SO)	5	Projetu Rehabilitasaun Ensinu Sekundariu Tekniku Vokasional Soibada, Manatuto	Manufahi Kiik Unip. Lda	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																												On Going																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
							Actual																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Note:


Plano Periode inspesaun iha tereinu

Implementasaun Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :




Eng. Quico Adelino Junior
(Eng. Projeto Edificio Publico, Agua e Saneamento Municipiu Manatuto, ADN.I.P.)

Sertifika Husi :



Eng. Emerenciana da Costa Maia Freitas
(Coordenador da Unidade de Controlo e Validasaun de Qualidade. ADN.I.P.)

Aprova Husi :



Eng. Januario Maia Guterres
(Adjunto Director Executivo, ADN.I.P.)

Naran Eng.		José R.Carlos Gusmão					2023																																
Município		Manatuto																																					
Município / Posto		No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Fevereiro																												OBS .		
									1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28			
MANATUTO VILA (MV)	1	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	SSS/062/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, atu informa dest projeto refere finaliza 100% iha tereno, no kompania hein rekomendadasaun itas hus DNEPCC (MOP).
	2	Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Municipio Manatuto	Nananiu, Unip. Lda JV Ina Forek, Lda	SSS/061/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, atu informa dest projeto refere finaliza 100% iha tereno, no kompania hein rekomendadasaun itas hus DNEPCC (MOP).
	4	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group	ICB/023/MPW-2013	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, atu informa dest projeto refere monitoriza hus Eng neebe mak responsabiza hus Impesitimu.
	5	Consultant Supervision (M-L & L-N)	Sinotech Engineering Consultant		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going	
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, atu informa dest projeto refere monitoriza hus Eng neebe mak responsabiza hus Impesitimu.
	16	Rehabilitasaun Estrada Rural Rembor, Chainage 0+000-3+000 Km	Kartini Unipessoal Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On Going
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, tamba kondisaun mota tun makas teluk sira lebele ultrapasa no atu informa dest projeto refere hahu ona servisu Excavation iha terenu ita tiran 2022 maibe kompania sedsuk mobiliza equipamento no servisu iha terenu.
LALEIA (LAL)	3	R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	As Jazesia Unipessoal Lda	MPW-W-210055	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																PBO
LACLUBAR (LAC)	2	Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan)	China Nuclear Industry 22ND Construction Co. LTD	ICB/04/MPW-2014	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going	
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, atu informa dest projeto refere monitoriza hus Eng neebe mak toma reponsabiza Impesitimu.
	5	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	Hatuwari Unip. Lda	MPW-W-NCB-R-190035	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo, atu informa dest projeto refere komesa servisu fila fali ona iha terenu, no kompania servisu tur volume neebe sedsuk kompleta.
	6	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	Ryzena Unipessoal Lda	MOP/DGOP/DNEPCC/0871-VIII/2020	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going			
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo tamba hus kontratu soun hus Nasional, atu informa dest projeto refere sei abandona kontinua iha tiran 2022 ate agora 2023 kompania sedsuk kontinua servisu.
	7	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	Sun Rise Golden Construction 02 Lda	MPW-W-210057	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																Relatoriu Fulan Fevereiro Eng. Munisipu Manatuto la halo Impesaun Maximo tamba kondisaun udan no atu informa dest projeto refere remata ona rai servisu iha terenu maibe teluk sedsuk ba fatin refere ho rajuun tamba estrada liga ba fatin makerek. Villa sei kondisaun s'it no kareta sedsuk bele asenu.
	8	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	Adahiak Oriao Unipessoal Lda	MPW-W-210056	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																



							PLANU INSPESAUN																													
Naran Eng.	Domingos D. X. Silva						2023																													
Município	Manatuto																																			
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono dô Projeto	Action	Fevereiro																												OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
MANATUTO VILA (MV)	1	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	SSS/062/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													
	2	Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Municipio Manatuto	Nananiu, Unip. Lda JV Ina Forek, Lda	SSS/061/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													
	4	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group	ICB/023/MPW-2013	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													
	5	Consultant Supervision (M-L & L-N)	Sinotech Engineering Consultant		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	16	Rehabilitasaun Estrada Rural Rembor, Chainage 0+000-3+000 Km	Kartini Unipessoal Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
LALÉIA (LAL.)	3	R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	As Jazesia Unipessoal Lda	MPW-W-210055	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													
LACLUBAR (LAC)	2	Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan)	China Nuclear Industry 22ND Construction Co, LTD	ICB/04/MPW-2014	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													
	5	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	Hatuwan Unip. Lda	MPW-W-NCB-R-190035	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																										On Going			
							Actual																													
	6	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	Ryzena Unipessoal Lda	MOP/DGOP/DNEPCC/0871-VIII/2020	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																										On Going			
							Actual																													
	7	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	Sun Rise Golden Construction 02 Lda	MPW-W-210057	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													
	8	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	Adahiak Oriao Unipessoal Lda	MPW-W-210056	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going		
							Actual																													



REPUBLICA DE TIMOR-LESTE MINISTÉRIO DO PLANO E ORDENAMENTO GOVERNO CONSTITUCIONAL ADN, LP Agência de Normas e Qualidade Sociedade por Accões							PLANU INSPESAUN																													
Naran Eng.	Domingos D. X. Silva						2023																													
Município	Manatuto																																			
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	. Fevereiro																												
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	OBS
SOIBADA (SO)	1	Construction of New Steel Bridge 100m in Milotu Sahe river, jct Fatucamanau, Soibada, Timor Leste	FIRDO UNIPESSOAL LDA	SSS/013/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	4	R4D Rural Road Spot Improvement Maniata (Manufahi Kiik) - Soibada Chainage 0+000-2+000	Manufahi Kiik Unip. Lda	MPW-W-210059	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	5	R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700	Ryzena Unipessoal Lda	MPW-W-210060	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going
							Actual																													
BARIQUE (BA)	1	Construction of Sahen Bridge Approach Protection (A14) Manatuto (MPW-W-190157) (162)	Yoku Unipessoal Lda	MPW-W-190157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	3	Rural Roads Routine Maintenance Uma Boco - Aubeon, Sta 0+000 - 6+000, Manututo Municipality (Manutensaun)	Zenobia Diak Unip Lda	MPWTC - CD - 170003	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	7	R4D Rural Periodic Maintenance Kaen Laran - Barique Chainage 0+000 - 9+000 & Routine, Hatularan-Cairui Chainage 0+000-9+800 (162)	Manufahi Kiik Unip. Lda	MPW-W-W-190080	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	8	R4D Rural Road Spot Improvement Agriculture Center - Aubeon Chainage 3+000-6+200	We'coi Unipessoal Lda	MPW-W-210062	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	9	R4D Rural Road Spot Improvement Uma Boco - Agriculture Center Chainage 0+000 - 3+000	Linoel	MPW-W-210061	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	10	R4D Rural Road Spot Improvement Kaen-Laran - Barique Chainage 0+000-9+000	Gimso Brothers Unip. Lda	MPW-W-210058	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
LACLO (LA)	2	Emergency Rehabilitation Project in Subao Boo, Municipio Manatuto	Sahan I Unip Lda	SSS/304/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	4	Routine Roads Maintenance - Laclo, Manatuto Municipality	Egana, Unip. Lda	MPW-W-190251	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	8	National Road No 1 Upgrading Project Dili - Manatuto (Package A01-01)	Sinohydro Corporation Limited	ICB/07/MPW-2014	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going	
							Actual																													
	10	Rehabilitation of Reinforced Concrete Ramp at Behau	Baboe Unip Lda		LM-BS	MINISTERIO DA DEFESA	Plan																												On Going	
							Actual																													
TOTAL PROJETO ON-GOING																																				

Note: Plano Periode inspesaun iha tereinu Implementasaun Plano Periode inspesaun iha tereinu Relatoriu avaliasun mensal iha Dili Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Domingos D. X. Silva)
Eng. ba Projeto Infraestrutura Transporte e Ingasaun Municipi
Manatuto, ADN LP

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de
Qualidade, ADN LP

Aprova Masi

(Eng. Januario Maki Guterres)
Adjunto Directo Administrativo, ADN LP

PLANU INSPESAUN

[illegible]

Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		Fevereiro																											
								We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																												
							Actual																												
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																												
							Actual																												
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																												
							Actual																												
	21	For Preparation of detailed engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																												
							Actual																												
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																												
							Actual																												
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																												
							Actual																												
	24	Preparation of detailed Design for Rahabilitation municipio Roads Package 4 : turiscari to Alas	Wan Husin & Associates SDN BHD Jv Consultant & eng. Intercontinental Unip Lda	MPW- CS 2000028	LM		Plan																												
							Actual																												
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																													
						Actual																													
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																													
						Actual																													
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																													
						Actual																													
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																													
						Actual																													
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																													
						Actual																													
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aurcum Solis Consultant, Unip Lda Jv PT Bikarna	MPW- CS 2000033	LM	MOP	Plan																													
						Actual																													
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarna JV Aurcum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																													
						Actual																													
32	Intersection in the Existing dili liquisa road to conect akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																												FHO	
						Actual																													
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																													
						Actual																													
34	Konsultan Suprevisi for Konstruction Suprevison of daradau ingation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																												Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu	
						Actual																													
35	Suprevison Consultant for Construction of Intersection in the Existing Dili-Liquisa Road to Connect Access Road from Tibar Bay port (National Road)	Lelo Unipessoal Lda			LM	MOP	Plan																												
						Actual																													
36	Preparation of Detailed Engineering Design (DED) For New Cable Stayed Bridge Over the Becusse River, in Dili Total Length +	TPT Timor Unip Lda			LM	MOP	Plan																												
						Actual																													
TOTAL PROJETO ON-GOING																																			
Note:		Planu Periode inspesaun iha tereinu Implementa Periode inspesaun iha tereinu Relatoriu avaliasuan mensal iha Dili Inspesaun Pagamentu Anual iha tereinu																																	
Prepara Husi :		Sertifika Husi :		Aprova Husi :																															
 (Eng. Vidal Guterres) Eng. PMU ba Projetu (Impréstimo), ADN, I.P.		 (Eng. Emerenciana da Costa Maia Freitas) Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.		 (Eng. Januario Maia Guterres) Adjunto Director Executivo, ADN, I.P.																															

SERVISU BA
KONSULTAN DESIGN
SEI AJUSTA TUIR
PLANO HUSI
PROJECTO NAIN .OU
BAZEIA BA
DOKUMENTOS
KONSULTAN NIAN
NEBE SUBMETE MAI
HUSI PROJECTO
NAIN.

FHO

Konsultan la serviso ona
iha tereno,maibe
pagamento seidauk hotu

2023

Fevereiro

IMPRESTIMO



Município / Posto	No.	Nódo Projeto	Nódo Companhia	No Contrato	Kategoria	Dono do Projeto		Fevereiro																											
								We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Selo - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																								SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUBMETE MAI HUSI PROJECTO NAIN.				
							Actual																												
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																												
							Actual																												
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bratojul Unip Lda	MPW-CS-2000025	LM	MOP	Plan																												
							Actual																												
	21	For Preparation of detailed engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																												
							Actual																												
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																												
							Actual																												
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																												
							Actual																												
	24	Preparation of detailed Design for Rahabilitation municipio Roads Package 4 : turiscat to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Intercontinental Unip Lda	MPW- CS 2000028	LM		Plan																												
							Actual																												
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																												
						Actual																													
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																													
						Actual																													
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niccles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																													
						Actual																													
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																													
						Actual																													
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																													
						Actual																													
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarna	MPW- CS 2000033	LM	MOP	Plan																													
						Actual																													
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarna JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																													
						Actual																													
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																													
						Actual																													
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																													
						Actual																													
34	Konsultan Suprevisi for Konstruktion Suprevison of daradau irigation Schema	PT. Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																													
						Actual																													
35	Suprevison Consultant for Construction of Intersection in the Existing Dili-Liquisa Road to Connect Access Road from Tibar Bay port (National Road)	Lelo Unipessoal Lda.		LM	MOP	Plan																													
						Actual																													
36	Preparation of Detailed Engineering Design (DED) For New Cable Stayed Bridge Over the Becusse River, in Dili Total Length +	TPT Timor Unip Lda		LM	MOP	Plan																													
						Actual																													
TOTAL PROJETO ON-GOING																																			

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Aniceto da Costa)

Eng. PMU ba Projeto (Impréstimo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)

Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)

Adjunto Director Executivo, ADN, I.P.

PLANU INSPESAUN

Naran Engª. Teresa Gomes								2023																												Observasaun
Município	MUNICIPIO DILI NO POSTOS																																			
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		Fevereiro																												
								We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)/Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																												PHO	
							Actual																													
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																												FHO	
							Actual																													
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction - Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																												PHO	
							Actual																													
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan																												Halo relatorio pagamento	
							Actual																													
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan																												Monotorizasaun Projecto	
							Actual																													
	6	Road Network Upgrading Project (RNUP) Upgrading and Maintanance of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Relatorio Pagamento	
							Actual																													
	7	Road Climate Resilience project (RCRP) upgrading project and maintainance of Dili- Ainaro Road Lot 3(Solerema - Bandudaru Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																												FHO	
							Actual																													
	8	Road Climate Resilience project (RCRP) upgrading and maintainance of Dili- Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																												FHO	
							Actual																													
	9	Road Climate Resilience project (RCRP) upgrading and maintainance of Dili- Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																												FHO	
						Actual																														
10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no. 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co.,Ltd JV with Kunhwa Engineering and Consulting Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																												PHO		
						Actual																														
11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.,Ltd JV with Kunhwa Engineering and Consulting Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																												Encontro ho PMU		
						Actual																														
12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Relatorio		
						Actual																														
13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Lautem - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd. and in Association with Deting Science, INC., and Kai Watu Kmanek Consultants, Unip.Lda		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Relatorio		
						Actual																														
14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Lautem - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																												Monotorizasaun Projecto		
						Actual																														
15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultant and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Philis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolvêr Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Relatorio		
						Actual																														
16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																												Monotorizasaun Projecto		
						Actual																														
17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																												Monotorizasaun Projecto		
						Actual																														

Município / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Fevereiro																											
								We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																												
							Actual																												
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt Multi Karadi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																												
							Actual																												
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragejui Unip Lda	MPW-CS -2000025	LM	MOP	Plan																												
							Actual																												
	21	For Preparation of detailed engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																												
							Actual																												
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																												
							Actual																												
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																												
							Actual																												
	24	Preparation of detailed Design for Rahabilitation municipio Roads Package 4 : turiscari to Alas	Wan Husin & Associates SDN BHD Jv Consultant & eng. Intercontinental Unip Lda	MPW- CS 2000028	LM		Plan																												
							Actual																												
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																													
						Actual																													
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																													
						Actual																													
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																													
						Actual																													
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																													
						Actual																													
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																													
						Actual																													
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarna	MPW- CS 2000033	LM	MOP	Plan																													
						Actual																													
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarna JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																													
						Actual																													
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																										FHO			
						Actual																													
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																													
						Actual																													
34	Konsultan Suprevisi for Konstruktion Suprevison of daradau irrigation Schema	PT. Suanda karya Jv KWK	REP/042/MAF/2017	FI	MOP	Plan																										Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu			
						Actual																													
35	Suprevison Consultant for Construction of Intersection in the Existing Dili-Liquisa Road to Connect Access Road from Tibar Bay port (National Road)	Lelo Unipessoal Lda.		LM	MOP	Plan																													
						Actual																													
36	Preparation of Detailed Engineering Design (DED) For New Cable Stayed Bridge Over the Becusse River, in Dili Total Length +	TPT Timor Unip Lda		LM	MOP	Plan																													
						Actual																													
TOTAL PROJETO ON-GOING																																			
Note:							Planu Periode inspesaun iha tereinu Implementa Periode inspesaun iha tereinu Relatoriu avaliasuan mensal iha Dili Inspesaun Pagamentu Anual iha tereinu																												
Prepara Husi :							Sertifika Husi :							Aprova Husi :																					
(Eng. Teresa Gomes) Eng. PMU ba Projetu (Impréstimo), ADN, I.P.							(Eng. Emerenciana da Costa Maia Freitas) Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.							(Eng. Januario Maia Guterres) Adjunto Director Executivo, ADN, I.P.																					

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUBMETE MAI HUSI PROJECTO NAIN.

FHO

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu






Naran Eng ³ , Augusta da Costa Ferreira							2023																												Observasaun																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
Município	MUNICIPIO DILI NO POSTOS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		Fevereiro																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
								We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						

Município / Posto	No.	Nóran Projeto	Nóran Companhia	No Contrato	Kategoria	Dono do Projeto		Fevereiro																											
								We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Selo - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																												
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv. Pt Multi Karidi - Guna Jasa & PT Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Actual																												
							Plan																												
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisoralai	Bratojoul Unip Lda	MPW-CS -2000025	LM	MOP	Actual																												
							Plan																												
	21	For Preparation of detailed engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Starplan Utama	MPW - CS- 2000022	LM	MOP	Actual																												
							Plan																												
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : I JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Starplan Utama	MPW - CS- 2000030	LM	MOP	Actual																												
							Plan																												
	23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Starplan Utama	MPW- CS 2000024	LM	MOP	Actual																												
							Plan																												
	24	Preparation of detailed Design for Rahabilitation municipio Roads Package 4 : turiscari to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Intercontinental Unip Lda	MPW- CS 2000028	LM		Actual																												
							Plan																												
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Actual																												
							Plan																												
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Actual																													
						Plan																													
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niccles Unip Lda	MPW- CS 2000026	LM	MOP	Actual																													
						Plan																													
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Actual																													
						Plan																													
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Actual																													
						Plan																													
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aurcum Solis Consultant, Unip Lda Jv PT Bikarna	MPW- CS 2000033	LM	MOP	Actual																													
						Plan																													
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarna JV Aurcum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Actual																													
						Plan																													
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP-009/MOP/2019	FI	MOP	Actual																													
						Plan																													
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Actual																													
						Plan																													
34	Konsultan Suprevisi for Konstruction Suprevison of daradau ingation Schema	PT Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Actual																													
						Plan																													
35	Suprevison Consultant for Construction of Intersection in the Existing Dili-Liquisa Road to Connect Access Road from Tibar Bay port (National Road)	Lelo Unipessoal Lda.		LM	MOP	Actual																													
						Plan																													
36	Preparation of Detailed Engineering Design (DED) For New Cable Stayed Bridge Over the Becusse River, in Dili Total Length +	TPT Timor Unip Lda		LM	MOP	Actual																													
						Plan																													
TOTAL PROJETO ON-GOING																																			
Note: Planu Periode inspesaun iha tereinu Implementa Periode inspesaun iha tereinu Relatoriu avaliasuan mensal iha Dili Inspesaun Pagamentu Anual iha tereinu Prepara Husi : (Eng^a. Augusta da Costa Ferreira) Eng. PMU ba Projetu (Impréstimo), ADN, I.P. Sertifika Husi : (Eng. Emerenciana da Costa Maia Freitas) Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P. Aprova Husi : (Eng. Januario Maia Guterres) Adjunto Director Executivo, ADN, I.P.																																			

Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	FEBREIRO																												OBS		
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28			
LACLUBAR (L)	2	Konstrusaun Posto Saude Iha iha Suku Funar - Lakiubar	MERCY, Unipessoal Lda	04/PDIM I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																															
							Actual																															
	3	Kontinuasaun Konst. Postu Saude Iha Suku Fatumakerek	Hatuwari Unip. Lda	02/PDD- II/MNTT/VII/2015	PDIM	MINISTERIO SAUDE	Plan																															
							Actual																															
SOIBADA	1	Projetu Rehabilitasaun Ensinu Sekundariu Tekniku Vokasional Soibada, Manatuto	Manufahi Kiik Unip. Lda	RFQ-R : 21/036 - Q	LM-CD	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	2	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MEJD PKRIE EBC WEAIHUDIK	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
BARIQUE (BA)	1	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	Tasibala II Const	RDTL/PO:2016-11272	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																															
							Actual																															
	2	Konstrusaun Posto Saude Aimeta Laran-Barique	Malack II Unip. Lda	03/PDIM- I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																															
							Actual																															
	3	Konstrusaun Sistema Bee Mos Iha Suco Aubeon no Aimetalaran /162	Malaca Unip Lda	No. Kontratu : MOP- W-190233	LM-BS	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	4	New construction of Gapura and gabion wall protection no jardim de herois de Natarbora	Senizu	-	LM-CD	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	Plan																															
							Actual																															
LACLO (LA)	1	New Installation MV, LV Line and House Connection from Lacio to Mantane - Manatuto Municipality	Anopa Electrical Unip. Lda	RDTL/MOPTC- VMOPTC/CGI-PEN : 00000421	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	Konstrusaun Edificio Posto Administrativo Lacio	Ailili Const. Unip. Lda	02/PDIM- I/MNTT/IX/2019	PDIM	ESTATAL	Plan																															
							Actual																															
	3	Rehabilitation of Behau Mini Tradisional Food	Esa-Un	RDTL:74/GMTAC/X II/2015	LM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																															
							Actual																															
	4	Konstrusaun Mercado Komunitaria Kikan Ilimano	Surprise Unip. Lda	07/PDIM- II/MNTT/VIII/2016	PDIM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																															
							Actual																															
	5	Konstrusaun ka Rehabilitasaun ba PE Rembor	MEJD PKRIE PE REMBOR	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	6	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MEJD PKRIE EBF BAHADIK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
TOTAL PROJETO ON-GOING																																						

Note:

Plano Periode inspesaun iha tereinu
Implementasaun Plano Periode inspesaun iha tereinu
Relatoriu avaliasuan mensal iha Dili
Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

 (Adonis Julio Fernandes)
 Eng. Electricidade, ADN, I.P

Certifika Husi :

 (Emerenciana da Costa Maia Freitas)
 Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P

Aprova Husi :

 (Eng. Januario Maia Guterres)
 Adjunto Director Executivo, ADN, I.P
