



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL
IMPLEMENTASAUN
PROJETUS MUNISÍPIU LIQUICA
OUTUBRO 2022



SUMÁRIO


RELATÓRIO

IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO LIQUICA OUTUBRO 2022


Prepara Husi :


(Eng. Juninho Antonio A. Da Cruz)
Eng. ba Edifício Público no Beé Saneamentu,
Município Liquica ADN, I.P


(Eng. Marcos Ximenes de Araujo)
Eng. ba Projeto Infraestrutura, Transporte e
Irigasaun, Município Liquica ADN, I.P



(Eng. Antonia de Fatima Moraes)
Eng. ba Edifício Público no Beé Saneamentu,
Município Liquica ADN, I.P


(Eng. Luduvina Maria H. Guterres)
Eng. ba Projeto Infraestrutura, Transporte e
Irigasaun, Município Liquica ADN, I.P


(Eng. Camilio de Jesus)
Eng. ba Projeto ME Município Liquica
ADN, I.P

Verifika Husi :


(Arc. Francisco X D D Jeronimo)
Eng. Senior ba Edifício Público no Beé
Saneamentu, ADN, I.P


(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba Projeto Infraestrutura e
Irigasaun, ADN, I.P


(Deolindo de Fatima Marques)
Chefe Seksaun ba Projeto M. E & ITC, ADN, I.P

Sertifika Husi :


(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade,
ADN, I.P

Aprova Husi :


(Mariano Renato Monteiro da Cruz, S. T. M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO	1
I. INTRODUSAUN.....	3
1.1 Enkuadramentu Legal.....	3
1.2 Perfil Municipio Liquica	3
1.3 Lista Projecto	7
II. PROGRESU FISIKU	18
2.1 Progreso Fisiku Kada Fulan.....	18
III OBSTÁKLU IHA TERENU	18
3.1 Obstáclo Servisu Iha Terenu.....	18
VI. REKOMENDASAUN IHA TERENU	19
4.1 Rekomendasaun Servisu iha Terenu	19

INDICE TABELA

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica	5
Tabela 1. 2: Lista Asset ADN,I.P Municipio Liquica	5
Tabela 1.3. 1 Projecto Municipio Liquica Por Fundus Financiamento.....	7
Tabela 1.3. 2 Projecto Municipio Liquica Por Sectores.....	9
Tabela 1.3. 3 Projecto Municipio Liquica Por Ministerios.....	14
Tabela 4. 1 Dadus Populasaun Munisipiu Liquica	18

I. INTRODUSAUN.


1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho qualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefísiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizasaun no sertifikasaun qualidade ba Projeto sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Liquica

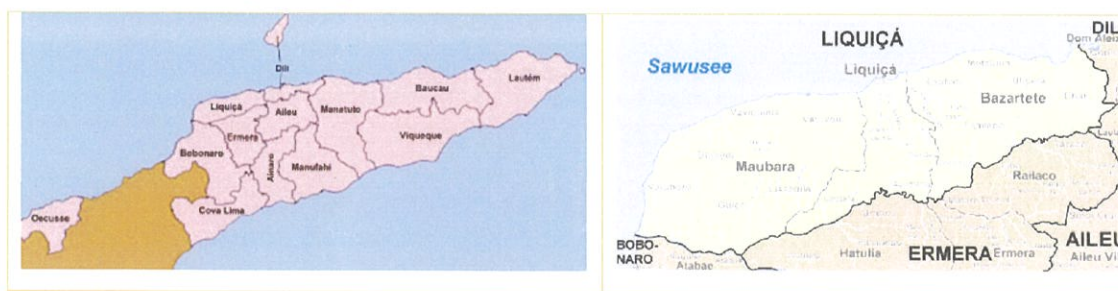

Mapa hatudu pozisaun Administrasaun Munisipal Liquica iha luan area 543 km² ho populasaun nain – 63,403 tuir Sensus 2010. Administrasaun Munisipal Liquica iha Postu Administrativu tolu (3), Sukus 23 no aldeias 134, mak hanesan hatudu iha Tabela 1

Tabela 1: Postos Administrativos, Sucos no Aldeias.

Bazartete		Liquica		Maubara	
sukus	Aldeias	Sukus	Aldeias	Sukus	Aldeias
Fahilelo	3	Açumano	4	Gugleur	11
Fatumasi	4	Darulete	4	Guiço	5
Lauhata	5	Dato	10	Lissadila	7
Leorema	10	Hatuquesi	8	Maubaralissa	5
Maumeta	4	Leotala	5	Vatuboro	5
Metagou	3	Loidahar	4	Vatuvou	10
Motaulun	3	Luculai	4	Vaviquinia	7
Tibar	4	-	-	-	-
Ulmera	9	-	-	-	-
Total	45	-	39	-	50

Data husi: Livro 3B OJE 2021, pag 58

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica

Força de Trabalho ADN, I.P Municipio Liquica								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro		2				2	
2	Administrasaun no Financas		0				0	
3	Motorista		1				1	
4	Seguransa		0				0	
Total			3				3	

Tabela 1. 2 : Lista Asset ADN,I.P Municipio Liquica

ASSET ADN,IP MUNICIPIO LIQUICA								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio		1					
2	Kareta		1					
3	Desktop HP / Monitor		1					
4	Laptop HP		1					
5	Printer Cannon		1					
6	UPS		1					
7	Armario File		1					
8	Armario Tau hena		3					
9	Meja escritorio		1					
10	Meja han		1					
11	Meja TV (kiik)		1					
12	Kadeira escritorio		6					
13	Kadeira han		4					

14	Sofa		1 Set					
15	Springbed +sumasu 4+sprei 3		3 Set					
16	Jeleira		1					
17	Water Dispenser		1					Aát
18	TV + Parabola		1 Set					
19	AC		4					
20	Kipas Angin		1					
21	Kompor		1					
22	Kompor Gas		1					
23	Rack sepatu		3					
24	Rack Piring		1					
25	Lampu		11					
26	Water Pump Sanyo		0					

1.3 Lista Projecto

Projeto hotu ne'ebe akumula iha lista neé bazeia ba dados Projeto nebe sei lao hela no mos Projeto nebe abandona ona iha tinan barak nia laran, Projeto hirak ne'e fahe tuir lista tabela 1.3.1 Projeto Por Fundus Financiamento, Tabela 1.3.2 Projeto Por Sector no tabela 1.3.3 Projeto Por Ministerio, no lista detallu kada Projeto bele hare iha #Aneksu A.

Tabela 1.3. 1 Projeto Municipio Liquica Por Fundus Financiamento



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM (CD + BS + TP + FUNDO COVID etc..) + EMERGENCY + PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	29	\$10,522,091.43	\$2,434,275.74	23.13%
2	LIQUICA VILA	26	\$5,849,524.82	\$2,655,643.39	45.40%
3	MAUBARA	21	\$12,770,126.24	\$9,132,805.92	71.52%
	Grand Total	76	\$29,141,742.49	\$14,222,725.05	48.81%

NO	POSTO ADMINISTRATIVO	FI			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	5	\$7,247,828.32	\$546,664.59	7.54%
2	LIQUICA VILA	5	\$3,337,190.73	\$1,857,615.54	55.66%
3	MAUBARA	7	\$10,886,608.70	\$8,562,990.98	78.66%
	Grand Total	17	\$21,471,627.75	\$10,967,271.11	51.08%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	LM -CD			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	7	\$834,783.75	\$259,426.98	31.08%
2	LIQUICA VILA	11	\$1,528,099.12	\$512,692.60	33.55%
3	MAUBARA	7	\$951,175.37	\$256,895.33	27.01%
	Grand Total	25	\$3,314,058.24	\$1,029,014.91	31.05%

NO	POSTO ADMINISTRATIVO	LM -BS			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	6	\$897,734.42	\$717,903.81	79.97%
2	LIQUICA VILA	3	\$332,370.82	\$241,807.82	72.75%
3	MAUBARA	2	\$344,450.27	\$175,003.84	50.81%
	Grand Total	11	\$1,574,555.51	\$1,134,715.47	72.07%

NO	POSTO ADMINISTRATIVO	LM -TP			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	\$289,002.61		
2	LIQUICA VILA	6	\$474,930.65	\$43,527.43	9.17%
3	MAUBARA	3	\$359,595.59		
	Grand Total	13	\$1,123,528.85	\$43,527.43	3.87%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	FUNDO - COVID			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	\$433,364.88	\$313,531.42	72.35%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	4	\$433,364.88	\$313,531.42	72.35%

NO	POSTO ADMINISTRATIVO	EMERGENCY			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	1	\$ 502,473.28	\$ 441,060.32	87.78%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	1	\$ 502,473.28	\$ 441,060.32	87.78%

NO	POSTO ADMINISTRATIVO	PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	2	\$ 316,904.17	\$155,688.62	49.13%
2	LIQUICA VILA	1	\$ 176,933.50		
3	MAUBARA	2	\$ 228,296.31	\$137,915.77	60.41%
	Grand Total	5	\$ 722,133.98	\$293,604.39	40.66%

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 2 Projeto Municipio Liquica Por Sectores



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA	2	\$91,877.21	\$80,662.08	87.79%
2	AGUA E SANEAMENTO	3	\$293,629.77	\$167,315.56	56.98%
3	EDIFICIOS PUBLICOS	2	\$210,635.04		
4	EDUKASAUN	18	\$1,956,926.91	\$433,161.38	22.13%
5	ELÉCTRICIDADE	8	\$7,578,728.67	\$1,893,321.03	24.98%
6	ESTRADAS E PONTES	29	\$15,553,331.56	\$9,654,899.60	62.08%
7	MANUTENSAUN NO REHABILITASAUN	6	\$1,070,017.57	\$867,928.26	81.11%
8	PORTOS	1	\$1,394,750.00	\$657,275.92	47.12%
9	SAUDE	4	\$433,364.88	\$313,531.42	72.35%
10	SEGURANCA NASIONAL	1	\$58,107.88	\$50,129.80	86.27%
11	TURISMO	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		76	\$29,141,742.49	\$14,222,725.05	48.81%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA	2	\$91,877.21	\$80,662.08	87.79%
2	AGUA E SANEAMENTO	2	\$122,664.12	\$94,609.06	77.13%
3	EDIFICIOS PUBLICOS	1	\$154,189.34		
4	EDUKASAUN	7	\$783,470.96	\$180,599.14	23.05%
5	ELÉCTRICIDADE	2	\$5,296,850.84	\$449,325.76	8.48%
6	ESTRADAS E PONTES	9	\$3,016,113.87	\$708,700.68	23.50%
7	MANUTENSAUN NO REHABILITASAUN	1	\$565,452.33	\$556,717.80	98.46%
8	PORTOS				
9	SAUDE	4	\$433,364.88	\$313,531.42	72.35%
10	SEGURANCA NASIONAL	1	\$58,107.88	\$50,129.80	86.27%
11	TURISMO				
Grand Total		29	\$10,522,091.43	\$2,434,275.74	23.13%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA				
2	AGUA E SANEAMENTO				
3	EDIFICIOS PUBLICOS				
4	EDUKASAUN	7	\$642,009.75	\$114,646.47	17.86%
5	ELETRIFIKASAUN NASIONAL	3	\$1,490,077.80	\$807,719.98	54.21%
6	ESTRADA- IMPRESTIMO	10	\$1,818,122.03	\$764,790.56	42.06%
7	ESTRADAS	5	\$504,565.24	\$311,210.46	61.68%
8	FLOOD CONTROL	1	\$1,394,750.00	\$657,275.92	47.12%
9	MANUTENSAUN NO REHABILITASAUN				
10	PORTOS				
11	SAUDE				
Grand Total		26	\$5,849,524.82	\$2,655,643.39	45.40%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA				
2	AGUA E SANEAMENTO	1	\$170,965.65	\$72,706.50	42.53%
3	EDIFICIOS PUBLICOS	1	\$56,445.70		
4	EDUKASAUN	4	\$531,446.20	\$137,915.77	25.95%
5	ELETRIFIKASAUN NASIONAL	3	\$791,800.03	\$636,275.29	80.36%
6	ESTRADA- IMPRESTIMO	10	\$10,719,095.66	\$8,181,408.36	76.33%
7	ESTRADAS				
8	FLOOD CONTROL				
9	MANUTENSAUN NO REHABILITASAUN				
10	PORTOS				
11	SAUDE	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		21	\$12,770,126.24	\$9,132,805.92	71.52%

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 3 Projeto Municipio Liquica Por Ministerios



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	3	\$387,568.54		
2	MINISTERIO AGRICULTURA E PISCAS	3	\$139,176.53	\$118,527.60	85.16%
3	MINISTERIO DAS OBRAS PUBLICAS	43	\$24,171,989.95	\$12,463,096.24	51.56%
4	MINISTERIO DO INTERIOR	1	\$58,107.88	\$50,129.80	86.27%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	18	\$1,956,926.91	\$433,161.38	22.13%
6	MINISTERIO PLANU E ORDENAMENTU	1	\$99,484.80	\$82,502.69	82.93%
7	MINISTERIO SAUDE	4	\$433,364.88	\$313,531.42	72.35%
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN	1	\$1,394,750.00	\$657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		76	\$29,141,742.49	\$14,222,725.05	48.81%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	1	\$154,189.34	\$-	0.00%
2	MINISTERIO AGRICULTURA E PESCAS	2	\$91,877.21	\$80,662.08	87.79%
3	MINISTERIO DAS OBRAS PUBLICAS	13	\$8,901,596.36	\$1,726,850.61	19.40%
4	MINISTERIO DO INTERIOR	1	\$58,107.88	\$50,129.80	86.27%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	\$783,470.96	\$180,599.14	23.05%
6	MINISTERIO PLANU E ORDENAMENTU	1	\$99,484.80	\$82,502.69	82.93%
7	MINISTERIO SAUDE	4	\$433,364.88	\$313,531.42	72.35%
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
Grand Total		29	\$10,522,091.43	\$2,434,275.74	23.13%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	1	\$176,933.50		
2	MINISTERIO AGRICULTURA E PISCAS	1	\$47,299.32	\$37,865.52	80.06%
3	MINISTERIO DAS OBRAS PUBLICAS	16	\$3,588,532.25	\$1,845,855.48	51.44%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	\$642,009.75	\$114,646.47	17.86%
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN	1	\$1,394,750.00	\$657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
Grand Total		26	\$5,849,524.82	\$2,655,643.39	45.40%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	1	\$56,445.70	\$-	0.00%
2	MINISTERIO AGRICULTURA E PISCAS				
3	MINISTERIO DAS OBRAS PUBLICAS	14	\$11,681,861.34	\$8,890,390.15	76.10%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	4	\$531,446.20	\$137,915.77	25.95%
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		21	\$12,770,126.24	\$9,132,805.92	71.52%

Dados Detallu Kada Projeto #Anexu A

Tabela 4. 1 : Dadus Populasaun Munisipiu Liquica

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Bazartete	31,983	9,158	9,039	7,089	6,697
Liquiça	25,334	6,978	7,348	5,672	5,337
Maubara	25,234	7,088	6,802	5,766	5,578

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi Progressu servisu nebe kompanha sira atinji iha fulan neé nia laran, husi lista nebe iha #Anexu B hatudu progressu aktual fulan ida neé ho nia persentagen servisu, montante aktual bazeia ba orsamento nebe hetan husi progressu fulan ida neé, ikus liu persentagen aktual fulan ida neé hatudu progressu fisiku komulativa husi porsento anterior no fulan ida neé nian, lista kompletu ba detailho bele hare iha #Anexu B, detallu ba Backup Fotografia #Anexu C1, Detallu ba Backup BoQ #Anexu C2 no Instrusaun servisu bele hare #Anexu D

III. OBSTÁKLU IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

Durante iha Fulan ida nia laran, problema nebe ami enjineiru municipio hasoru mak hanesan :

1. Projeto lao tarde
2. Companhia balun servisu la tuir spesifikasaun
3. Companhia balun servisu la iha Site Engineer
4. Difikulidade ba Ekipa ADN M.Liquica hasoru susar ba Be'e mos

VI. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu iha Terenu

1. Rekomenda ba Kompanhia sira servisu tuir spesifikasaun nebe iha ona
2. Rekomenda ba Kompanhia sira tenke iha Site Engineer iha terenu

Rekomenda ba ADN.I.P. Nacional liu-liu ba Superior sira hodi hare ba Edificio ADN.I.P.

Note : Assinatura Husi Enjineiru Municipio Liquica

Força de Trabalho ADN,I.P Municipio Liquica					
No	Deskrisaun	Identidade			
		Naran Kompletu e Asinatura	Nu. ID Card	Pozisaun	Fotografia
1	Enjineiru	 Juninho António A. Da Cruz	216	Enjineiru EPAS	
		 Marcus Ximenes de Araujo	172	Enjineiru ITI	
		 Luduvina Maria H. Guterres	251	Enjineira ITI	

		 Antonia de Fatima Morais	241	Enjineira EPAS	
		 Camilio de Jesus	061	Enjineiru METIC	
2	Enjineira	 Nencia F.O. do Rêgo	173	Enjineira VEBD	
3	Motorista	 Rui Antonio Gaio	029	Motorista	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Outubro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVASAUN
1	New Installation MV/LV Line and House Connection for Bazartete Vila to Leorema -Bazartete Sub District-Liquica District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	BAZARTETE	LIQUICA	Mina Petro Leste Unip, Lda	RDTL-11004589	\$ 499,250.84		100.00%	90.00%	\$ 449,325.76	\$ 49,925.08	ABANDONA	
2	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Banir Lema	MPW-W-190097	\$ 565,452.33	Aug. 14, 2019	100.00%	98.46%	\$ 556,717.80	\$ 8,734.53	FHO	Progresio Fisiko 100% e hela pagamento retensaun 10%
3	Novo Konstrusaun Edifício Escola Técnico Vocacional (ES-TECVOC) Maumeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	BAZARTETE	LIQUICA	Vida Olak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	\$ 162,714.83	Aug. 16, 2019	95.68%	95.68%	\$ 155,688.62	\$ 7,026.21	FHO	FHO Iha Agosto 2022
4	R4D Rural Road Periodic Maintenance Libalao - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Lep Laco Dato	MPW-W-190111	\$ 73,270.51	Sept. 5, 2019	100.00%	97.90%	\$ 71,729.53	\$ 8,712.25	FHO	Progresu fizkamente 100 % e sel falta pagamento ba retensaun
5	Konstrusaun Moralia Foun Matadouro Tibar	MINISTERIO AGRICULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Manoko Unip. Lda	RDTL-MAP-PO2019-19726	\$ 23,950.17	Dec. 5, 2019	77.60%	69.84%	\$ 16,726.74	\$ 7,223.43	ON-GOING	Provezoriamente servisu paradu hela
6	Konstrusaun Foun EBF Hotugara Bazartete, Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	EDUKASAUN	BAZARTETE	LIQUICA	Milcha Unip Lda	(RFO/19/029-Q-R)	\$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	\$ 24,910.52	\$ 42,582.17	ON-GOING	
7	Hamos Tangki Estasaun Tratamento Agua Residuals Etar Tibar / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Culoco Unipessoal Lda	Contract No.MOP-W-190184	\$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	\$ 12,106.37	\$ 11,072.90	ON-GOING	Provezoriamente servisu paradu hela
8	New Water Supply of Bairos PNTL Liquica	MINISTERIO DO INTERIOR	FI	SEGURANCA NASIONAL	BAZARTETE	LIQUICA	Holul Unipessoal, Lda	SSS/054/MI-2019	\$ 58,107.88	Nov. 29, 2019	86.27%	86.27%	\$ 50,129.80	\$ 10,484.57	FHO	
9	Konstrusaun Armagen Foun Matadouro	MINISTERIO AGRICULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Nasesaiobu	MAP-PO2019-19532	\$ 67,927.04	Dec. 5, 2019	94.12%	94.12%	\$ 63,935.34	\$ 17,617.77	FHO	Progresu fizkamente remata ona
10	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	\$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	\$ 44,268.56	\$ 22,289.34	ON-GOING	ongoing
11	New construction of Isolation for covid 19 in liquica, Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	SENIZU UNIPESSOAL LDA	MS-DNA-NCB-20-163	\$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	\$ 212,156.22	\$ 31,211.86	PHO	Projeto refere hela retensaun (10%) e Fisiku Iha Tereno atinji delt 96.86%
12	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Alpeio-Liquica	MINISTERIO PLANU E ORDENAMENTU	LM-CD	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Tinocya	022LM/RDTL/MPIE/AND/DA-RFO/IX/2019/EDIFICIO DEPARTMENT	\$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	\$ 82,502.69	\$ 16,982.11	ON-GOING	Falta retensaun
13	Emergency Project For Tibar River	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Sail Magu Unipessoal Lda	RT/067/MOP-2021	\$ 502,473.28	Sept. 20, 2021	99.75%	87.78%	\$ 441,060.32	\$ 61,412.96	ON-GOING	ON-GOING
14	Konstrusaun Edifício Posto Administrativo Bazartete & Moru Haleu	ESTATAL	PDIM	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	Aquarius Construction Unip,Lda	02/SMA-AML/PDIM VIII/2021	\$ 154,189.34	Aug. 31, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	
15	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	\$ 149,732.87	Oct. 01, 2021	41.45%	29.06%	\$ 43,507.04	\$ 106,225.83	ON-GOING	
16	R4D Rural Road Spot Improvement Fahilebo - Fatumasi Chainage 0+000-2+300 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-RFO - 21017	\$ 88,852.44	Oct. 01, 2021	19.17%	13.35%	\$ 11,862.47	\$ 76,989.97	ON-GOING	
17	R4D Rural Road Spot Improvement Libalao - Fahilebo Chainage 0+000-7+000, liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Hatuleo Unip Lda	MPW-W-210144	\$ 88,425.80	Oct. 01, 2021	60.35%	35.54%	\$ 31,422.82	\$ -	ON-GOING	
18	Rural Road Spot Improvement Maumeta-Metagou-Bazartete Chainage 0+000 -10+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	CRAELEKI BERCOLI UNIPESSOAL LDA	MPW-W-210145	\$ 62,024.04	Oct. 01, 2021	30.43%	24.93%	\$ 15,463.72	\$ 46,560.32	ON-GOING	SEIDAUK REGISTO IHA SISTEMA
19	R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	TM Calleba Unip,Lda	MPW-W-210158	\$ 158,465.33	Oct. 01, 2021	44.80%	29.31%	\$ 46,445.75	\$ 112,019.58	ON-GOING	SEIDAUK REGISTO IHA SISTEMA
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Blamali Unipessoal Lda	RDTL-MS	\$ 65,271.52		97.21%	87.49%	\$ 57,106.64	\$ 8,164.68	ON-GOING	
21	Supply and installation Connection for Isolation and Laboratorium Buliding Maumeta Liquica	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	ZYC UNIPESSOAL LDA	RDTL-MS-C19-DNA-DC-21-228	\$ 58,167.58	11/01/2022	24.74%	0.00%	\$ -		ON-GOING	
22	Konstrusaun Foun ESTV Leorema - Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	BAZARTETE	LIQUICA	U-Rema Unip. Lda.	NCB-15/MEJ/D/DNA/2021	\$ 264,260.83	1/11/2021	35.45%	0.00%	\$ -		ON-GOING	
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJO PKRIE EPE BAURA	-	\$ 9,072.12	15/10/2021	22.03%	0.00%	\$ -		ON-GOING	
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJD PKRIE EPE ERMETA	-	\$ 86,365.84	15/10/2021	17.22%	0.00%	\$ -		ON-GOING	
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJD PKRIE EPE CASSAIT	-	\$ 78,250.89	15/10/2021	17.13%	0.00%	\$ -		ON-GOING	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Outubro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVASAUN
26	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJO PKRIE ESG-PARALELO	-	\$ 115,313.76	15/10/2021	16.00%	0.00%	\$ -		ON-GOING	
27	Meinhoramento no Supliu Energia Eléctricidade husi Sub Stasaun Liquica ba Portu Tibar (Engineering Procurement Construction - Design, Supply, Installation, Testing and Commissioning Extension Transformer Bay Of the Existing 150/20kV Liquica Substation to Supply Power to Tibar Bay Port)	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRIDADE	BAZARTETE	LIQUICA	China Shandong International Economic And Technical Cooperation Group. LTD	RFP/054/MOP-2021	\$ 4,797,600.00	Dec. 16, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	
28	Supervision Consultant for Construction of Intersection in the Existing Dili - Liquica Road to Connect Access Road from Tibar Bay Port (National Road - A03) Sta. 0+000 - Sta. 0+620	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Leio Engineering Unipessoal Lda	RFP/072/MOP-2021	\$ 154,000.00	Dec. 14, 2021	95.77%	30.66%	\$ 47,209.03	\$ 106,790.97	ON-GOING	
29	Construction of Intersection in the Existing Dili- Liquica Road to Connect Access Road from Tibar Bay Port (National Road-A03)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Altuia Construction, Lda	RT/070/MOP-2021	\$ 1,738,869.60	Dec. 1, 2021					ON-GOING	
30	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbalá - Loes (A03) Municipality Liquica /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	\$ 153,851.88	Dec. 5, 2019	100.00%	95.49%	\$ 146,911.62	\$ 6,940.26	FHO	Servisu lha Tereno remata tina ona, sei hein kompanha Amenda kontratu nebe mate tina ona
31	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	MINISTERIO TRANSPORTES E KOMUNIKASAUN	FI	PORTOS	LIQUICA VILA	LIQUICA	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	\$ 1,394,750.00	May 17, 2017	100%	47.12%	\$ 657,275.92	\$ 737,474.08	ON-GOING	
32	R4D Rural Road Periodic Maintenance Albeno - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Nheu	MPW-W-RFQ-190093	\$ 55,012.05	Aug. 22, 2019	100%	99.91%	\$ 54,964.83	\$ 5,543.70	FHO	Projeto refere hela retensaun (10%) e Fisiku lha Tereno atinji delt 99.91%
33	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Albeno Chainage 0+000 - 7+600 Rutine Maintenance Taitabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Goubara Unip Lda	MPW-W-190096	\$ 71,468.49	Aug. 19, 2019	92.32%	100.00%	\$ 71,468.49	\$ 7,146.85	FHO	
34	New Installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRIDADE	LIQUICA VILA	LIQUICA	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	\$ 593,093.80	Jan. 6, 2017	92.77%	67.45%	\$ 400,036.22	\$ 193,057.58	ON-GOING	
35	New Installation of MV, LV Line and House Connection from Liquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuemo, Konli Leopa, Alpeio, Maumeta, and Leopa - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRIDADE	LIQUICA VILA	LIQUICA	Busa Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	\$ 276,484.00	July 6, 2016	80.84%	83.49%	\$ 230,841.25	\$ 45,642.75	ON-GOING	
36	R4D Rural Road Rehabilitation Bebadiri - Lebokakao Chainage 0+000 - 5+000 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	15 Raelti Unip. Lda	RT/034/MOP-2019	\$ 452,362.93	Dec. 20, 2019	97.15%	86.79%	\$ 392,619.64	\$ 59,743.29	ON-GOING	
37	Manutensaun Kanais Irrigasaun Faulara - Liquica	MINISTERIO AGRICULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Banir Lema Unip.Lda	RDTL 0000	\$ 47,299.32	Aug. 18, 2021	88.95%	80.06%	\$ 37,865.52	\$ 9,433.80	PHO	
38	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	\$ 176,933.50	Aug. 31, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	
39	R4D Rural Road Spot Improvement Beriakuudu - Laberiaka Chainage 0+000-2+500	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	\$ 131,219.62	Oct. 01, 2021	48.18%	43.46%	\$ 57,030.68	\$ 74,188.94	ON-GOING	
40	R4D Rural Road Spot Improvement Taitabi - Kutulau Chainage 0+000-1+700, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	\$ 123,631.72	Oct. 01, 2021	61.00%	34.51%	\$ 42,662.88	\$ 80,968.84	ON-GOING	
41	R4D Rural Road Spot Improvement Metagou - Albeno Chainage 0+000-7+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	MOP - CD - NCB - R - 21038	\$ 238,739.71	Oct. 01, 2021	40.21%	0.00%	\$ -	\$ -	ON-GOING	
42	R4D Rural Road Spot Improvement Dato - Loidahar Chainage 0+000-12+300, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Luquell Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	\$ 188,589.13	Oct. 01, 2021	51.00%	34.78%	\$ 65,594.85	\$ 122,994.28	ON-GOING	
43	R4D Rural Road Spot Improvement Albeno - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Calulu, Unip Lda	MOP - CD - NCB - R - 21035	\$ 162,215.27	Oct. 01, 2021	54.94%	26.60%	\$ 43,152.43	\$ 119,062.84	ON-GOING	
44	R4D Rural Road Spot Improvement Albeno - Asumanu - Leurema Chainage 0+000-5+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	\$ 165,363.43	Oct. 01, 2021	45.83%	39.81%	\$ 65,827.42	\$ 99,536.01	ON-GOING	
45	R4D Rural Road Spot Improvement Beriakuudu - Laberiaka Chainage 2+500-5+400	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Claridade Unip,Lda	MPW-W-210163	\$ 167,071.89	Oct. 01, 2021	30.65%	23.41%	\$ 39,104.89	\$ 127,967.00	ON-GOING	
46	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Craeleki Bercoill, Unip Lda	MPW-W-210143	\$ 76,423.05	Oct. 01, 2021	40.74%	34.33%	\$ 26,250.43	\$ 50,172.62	ON-GOING	
47	Projeto Konstrusaun foun ESG publico 01 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	LIQUICA VILA	LIQUICA	Roman Furak Unip,Lda	NCB 16/MEJD/DNA/2021	\$ 167,079.099	Nov. 1, 2021	47.70%	42.57%	\$ 71,119.04	\$ 95,960.05	ON-GOING	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Outubro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVA SAUN
48	For Roads Maintenance Section : Tibar - Liquica - Maubara, Carimbala - Loes (A03)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Chanel Chander Unipessoal Lda	MPW-W-210202	\$ 112,505.280	13/12/2021	32.14%	28.93%	\$ 32,547.34	\$ 79,957.94	ON-GOING	
49	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRIE EBC MAUBOQUE	-	\$ 112,530.010	15/10/2021	17.42%	0.00%	\$ -	\$ -	ON-GOING	
50	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRIE EBC 1,2,3 LIQUICA	-	\$ 99,456.040	15/10/2021	23.22%	23.22%	\$ 23,094.93	\$ 76,361.11	ON-GOING	
51	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRIE EPE LOIDAHAR	-	\$ 79,735.630	15/10/2021	25.63%	25.63%	\$ 20,432.50	\$ 59,303.13	ON-GOING	
52	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laciolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRIE Ebf 1,2 LACIOLEMA	-	\$ 89,650.660	15/10/2021	14.62%	0.00%	\$ -	\$ -	ON-GOING	
53	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRIE EBF 1,2 TOLEMA	-	\$ 88,407.020	15/10/2021	22.24%	0.00%	\$ -	\$ -	ON-GOING	
54	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRIE EBF 1,2 LUCULAI	-	\$ 5,151.290	15/10/2021	45.13%	0.00%	\$ -	\$ -	ON-GOING	
55	Consultant Services to Supervise EPC Contractor for the Up-gradation of Liquica 150/20KV Substation to Supply Power to Tibar Bay Port	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	LIQUICA VILA	LIQUICA	PT. Artefak Arkindo (Indonesian) JV with Jazicasnu Unipessoal Lda	RFP/054/MOP-2021	\$ 620,500.000	Dec. 16, 2021	23.33%	28.50%	\$ 176,842.51	\$ 443,657.49	ON-GOING	
56	Addt. Poste Ilga Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	MAUBARA	LIQUICA	Fu Unip,Lda	RDTL - 0000	\$ 13,000.00	Jan. 1, 2016	0.00%	0.00%	\$ -	\$ 13,000.00	ON-GOING	Kontratu ladaukiha no fiziku la eziste
57	New installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	MAUBARA	LIQUICA	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CIGI-PEN : 00000364	\$ 288,760.22	July 6, 2016	83.73%	75.36%	\$ 217,606.07	\$ 71,154.15	ON-GOING	
58	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	MAUBARA	LIQUICA	Montana Diak, Unipessoal, Lda	SSS/126/MOPTC-2017	\$ 1,901,334.67	Sept. 7, 2017	99.98%	99.98%	\$ 1,900,879.16	\$ 455.51	FHO	
59	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	\$ 275,000.00	Dec. 27, 2016	0.00%	0.00%	\$ 104,500.00	\$ 170,500.00	ON-GOING	ADN, I.P la hare
60	Novo Konstrusaun Edifício ESTV Lisadila	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	MAUBARA	LIQUICA	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	\$ 171,850.61	Aug. 16, 2019	89.17%	80.25%	\$ 137,915.77	\$ 33,934.84	ON-GOING	
61	Reabilitasaun Sistema be'e mos lha aidela Pandevou ho Mau-Uno,Sucu Culco /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	MAUBARA	LIQUICA	Oceania Const Unip.Lda	NCB-MOP-190051	\$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	\$ 72,706.50	\$ 98,259.15	ON-GOING	Provizoriamente paradu hela
62	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	MAUBARA	LIQUICA	Dongsung Engineering Co.,Ltd JV with Kuntiwa Engineering and Consulting Co.Ltd.	RFP/038/MOPTC/2016	\$ 7,695,101.00	May 3, 2017	76.97%	76.97%	\$ 5,921,336.53	\$ 1,771,764.47	ON-GOING	
63	R4D Rural Road Maintenance Beriaukulidu - Laberlaka Chainage 0 + 000 - 5 + 400 Nunuleta - Darulema Chainage 0 + 000 - 1 + 600 Vaviquinia - Maubaraissa Chainage 0 + 000 - 12 + 500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Luliana Unip.,Lda	MPW-W-190098	\$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	\$ 43,761.73	\$ 6,940.86	PHO	
64	Konstrusaun Moru Haeu no Posto Siguransa ba Edificio Posto Administrativo Maubara	ESTATAL	PDIM	EDIFICIOS PUBLICOS	MAUBARA	LIQUICA	Rafio Unip. Lda	01/AMLSMA-PDIM/VIII/2021	\$ 56,445.70	July 21, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ADN, I.P la Hare
65	R4D Rural Road Spot Improvement Nunulete - Darulema Chainage 0 + 000-2 + 000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Rito - Pu, Unipessoal,Lda	MOP - CD-RFQ - 21013	\$ 67,382.23	Oct. 01, 2021	2.07%	0.00%	\$ -	\$ -	ON-GOING	
66	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 4 + 800-9 + 600	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Malibo, Unipessoal LDA	MOP - CD - NCB-R- 21033	\$ 152,622.90	Oct. 01, 2021	35.83%	25.75%	\$ 39,294.58	\$ 113,328.32	ON-GOING	
67	R4D Rural Road Spot Improvement Barkau (Vaviquenia)-Maubaraissa Chainage 0 + 000-4 + 200	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS E PONTES	MAUBARA	LIQUICA	Nheu, Unipessoal LDA	MOP - CD - NCB-R- 21027	\$ 173,484.62	Oct. 01, 2021	45.61%	58.97%	\$ 102,297.34	\$ 71,187.28	ON-GOING	
68	R4D Rural Road Spot Improvement Malaisera- Lissadila Chainage 0 + 000-4 + 800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Murak, Unipessoal Lda	MPW-W-210157	\$ 153,049.65	Oct. 01, 2021	43.43%	27.12%	\$ 41,501.12	\$ 111,548.53	ON-GOING	
69	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaraissa, Chainage 8 + 400-12 + 500)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Meta Loe Crae Bau Unip,Lda	MPW-W-210160	\$ 198,698.25	Oct. 01, 2021	44.41%	39.89%	\$ 79,267.01	\$ 119,431.24	ON-GOING	
70	R4D Rural Road Spot Improvement Samarapo - Cisu Chainage 0 + 000-2 + 000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Naziko Unip Lda	-	\$ 114,789.50	Oct. 01, 2021	11.39%	0.00%	\$ -	\$ -	ON-GOING	
71	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaraissa Chainage 4 + 200-8 + 400)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-210161	\$ 213,930.25	Oct. 01, 2021	34.86%	24.81%	\$ 53,070.89	\$ 160,859.36	ON-GOING	
72	Konstrusaun ka Reabilitasaun ba EBF Gariana	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	MEJD PKRIE EBF GARIANA	-	\$ 117,902.04	Oct. 15, 2021	1.98%	0.00%	\$ -	\$ -	ON-GOING	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Outubro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVAUN
73	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	MEJO PKRIE EBF TAPO MANUHULU	-	\$ 100,033.33	Oct. 15, 2021	10.61%	0.00%	\$ -	\$ -	ON-GOING	
74	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	MEJO PKRIE ESG-PARALELO MAUBARA/BATUVOU	-	\$ 141,660.22	Oct. 15, 2021	14.14%	0.00%	\$ -	\$ -	ON-GOING	
75	Feasibility study for New Construction of Industrial Park in Liquica, Timor Leste	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	HABERAN UNIPESOAAL LDA (TIMOR LESTE) in Joint Venture with PT ITS TEKNO SAINS (INDONESIA)	RFP/077/MTCI-2021	\$ 225,373.00	March 24, 2022					ON-GOING	
76	Installation foun ba Linha de Media Tensaun, Baixa Tensaun e Baixadas em Liquica - Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	MAUBARA	LIQUICA	Nla construction, Lda	0000	\$ 490,039.81	Dec. 4, 2012	94.93%	85.44%	\$ 418,669.22	\$ 71,370.59	ON-GOING	
	TOTAL								\$ 29,141,742.49				\$ 14,222,725.05	48.81%		

PREPARA HUSI,

(Eng. Marcus Ximenes de Araujo)
Eng. ba Projeto Infrastrutura Transporte
e Irigasaun, ADN,I.P

VERIFIKA HUSI,

(Eng. Remigio da C.S.dos Santos)
Engineru Senior ba Projeto Infrastrutura Transporte e Irigasaun
ADN,I.P.

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora da Unidade de Controlo e
Validasaun de Qualidade, ADN,I.P

(Eng. Juninho Antonio A. da Cruz)
Eng. ba Edificio Publiku Agua e

(Arg. Francisco Xavier D.D. Jeronimo)
Engineru Senior ba Projeto Edificio Publiko
no Be'e Saneamento ADN,I.P.

(Eng. Deolindo de Fatima Marques)
Chefe Seksaun Mekanikal
e Elektrikal & ITC ADN,I.P

(Eng. Antónia de Fatima Morais Soares)
Engineru ba Edificio Publiku Agua e Saneamento ADN,I.P

(Eng. Ludovina Maria Helena Guterres)
Engineru ba Projeto Infrastrutura Transporte
e Irigasaun ADN,I.P

(Eng. Camilio de Jesus)
Eng. Mekanikal e Elektrikal ADN,I.P



#ANEXO B

PROGRESSU FISIKU FULAN OUTUBRO MUNICIPIO LIQUICA

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVASAUN	Oct-22		
												Previous Progress (%)	This Month Progress (%)	Komulative Progress (%)
1	New installation MV, LV line and House Connection for Bazartete Vila to Leorema - Bazarate Sub District, Liquica District	Mina Petro Leste Unip, Lda	RDTL-11004589	\$ 499,250.84	Oct. 1, 2020	100.00%	90.00%	\$ 449,325.76	\$ 49,925.08	ABANDONA				
2	Rural Road Rehabilitation Metagou Bazarate 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica	Banir Lema	MPW-W-190097	\$ 565,452.33	Aug. 14, 2019	100.00%	88.81%	\$ 501,046.02	\$ 64,406.31	PHO	FHO			
3	Novo Konstrusaun Edifício Escola Tecnico Vocacional (ES-TECVOC) Maumeta)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	\$ 162,714.83	Aug. 16, 2019	95.68%	86.11%	\$ 140,119.76	\$ 22,595.07	ON-GOING	FHO	95.68%	0.00%	95.68%
4	R4D Rural Road Periodic Maintenance Libaloa - Fahlebo Chainage 0+000 - 7+000 & Fahlebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahlebo Municipality Chainage 0+000 - 6+500	Lep Iaco Dato	MPW-W-190111	\$ 73,270.51	Sept. 5, 2019	100.00%	88.11%	\$ 64,558.26	\$ 8,712.25	PHO	FHO			
5	Konstrusaun Moraiha Foun Matadouro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	\$ 23,950.17	Dec. 5, 2019	77.60%	69.84%	\$ 16,726.74	\$ 7,223.43	ON-GOING	Provezoriamente servisu paradu hela	77.60%	0.00%	77.60%
6	Konstrusaun Foun EBF Hotugara Bazarate, Liquica	Milcha Unip Lda	(RFQ:19/029-Q-R)	\$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	\$ 24,910.52	\$ 42,582.17	Parado	Parado	41.01%	0.00%	41.01%
7	Hamos Tangki Estasaun Tratamento Agua Residuals Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	\$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	\$ 12,106.37	\$ 11,072.90	Provezoriam ente servisu paradu hela	Provezoriamente servisu paradu hela	79.42%	0.00%	79.42%
8	New Water Supply of Balros PNTL Liquica	Holuil Unipessoal, Lda	SSS/O54/MI-2019	\$ 58,107.88	Nov. 29, 2019	86.27%	81.96%	\$ 47,623.31	\$ 10,484.57	FHO	FHO	86.27%	0.00%	86.27%
9	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu	MAP-PO2019:19532	\$ 67,927.04	Dec. 5, 2019	82.29	74.06%	\$ 50,309.27	\$ 17,617.77	FHO	FHO	94.12%	0.00%	94.12%
10	New Construction of Laboratory for Covid 19 In Liquica Ministry of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	\$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	\$ 44,268.56	\$ 22,289.34	ON-GOING	Servisu refere sedauk 100%	73.90%	0.00%	73.90%
11	New construction of isolation for covid 19 in Liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	\$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	\$ 212,156.22	\$ 31,211.86	PHO	PHO	96.86%	0.00%	96.86%
12	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Alpele-Liquica	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	\$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	\$ 82,502.69	\$ 16,982.11	PHO	PHO	92.14%	0.00%	92.14%
13	Emergency Project For Tibar River	Sail Magu Unipessoal Lda	RT/067/MOP-2021	\$ 502,473.28	Sept. 20, 2021	72.76%	64.02%	\$ 321,707.56	\$ 180,765.72	PHO	PHO	99.75%	0.00%	99.75%
14	Konstrusaun Edificio Posto Administrativo Bazarate & Moru Haleu	Aquarius Construction Unip,Lda	02/SMA-AMU/PDIM VIII/2021	\$ 154,189.34	Aug. 31, 2021	9.33%	0.00%	\$ -	\$ -		ADN,I.P la hare	9.33%	0.00%	9.33%
15	R4D Rural Road Spot improvement Fahlebo- Bucumera Chainage 0+000-3+000	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	\$ 149,732.87	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	41.45%	0.00%	41.45%
16	R4D Rural Road Spot improvement Fahlebo -Fatumasi Chainage 0+000-2+300 , Liquica Municipality	Hatumeta Oan, Unip.Lda	MOP - CD-RFQ - 21017	\$ 88,852.44	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	19.17%	0.00%	19.17%
17	R4D Rural Road Spot improvement Libaloa- Fahlebo Chainage 0+000-7+000, Liquica Municipality	Hatuleo Unip Lda	MPW-W-210144	\$ 88,425.80	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	60.35%	30.44%	90.80%
18	Rural Road Spot improvement Maumeta- Metagou- Bazarate Chainage 0+000 - 40+000, Liquica Municipality	Craeleki Bercoli Unip,Lda	MPW-W-210145	\$ 62,024.04	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	30.43%	35.37%	65.81%
19	R4D Rural Road Spot improvement Fahlebo - Bucumera Chainage 3+000+6+500) Liquica Municipality	TM Calleba Unip,Lda	MPW-W-210158	\$ 158,465.33	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	44.80%	3.37%	48.17%
20	New construction of fence around for isolation COVID-19 In Liquica Maumeta, Ministerio da Saude Timor Leste	Blamali Unipessoal Lda	RDTL-MS-C19-DNA-DC-21-233	\$ 65,271.32	11/01/2022					ON-GOING	ONGOING	76.00%	21.22%	97.21%
21	Supply and installation connection for isolation and laboratorum Building Maumeta Liquica	ZYC UNIPESOAL Lda	RDTL-MS-C19-DNA-DC-21-228	\$ 58,167.58	11/01/2022					ON-GOING	ONGOING	24.74%	0.00%	24.74%
22	Konstrusaun Foun ESTV Leorema - Liquica	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	\$ 264,260.83	1/11/2021		0.00%	\$ -		ON-GOING	ONGOING	35.45%	0.92%	36.37%
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MEJD PKRIE EPE BAURA	-	\$ 9,072.12	15/10/2021		0.00%	\$ -		ON-GOING	ONGOING	22.03%	9.58%	31.61%



#ANEXO B

PROGRESSU FISIKU FULAN OUTUBRO MUNICIPIO LIQUICA

												Oct-22		
NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVA SAUN	Previous Progress (%)	This Month Progress (%)	Komulative Progress (%)
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MEJD PKRIE EPE ERMETA	-	\$ 86,365.84	15/10/2021		0.00%	\$ -		ON-GOING	ONCOING	17.22%	6.05%	23.28%
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MEJD PKRIE EPE CASSAIT	-	\$ 78,250.89	15/10/2021		0.00%	\$ -		ON-GOING	ONCOING	17.13%	0.83%	17.96%
26	Konstrusaun ka Reabilitasaun ba ESC-Paralelo Bogoro	MEJD PKRIE ESC-PARALELO	-	\$ 115,313.76	15/10/2021		0.00%	\$ -		ON-GOING	ONCOING	16.00%	7.57%	23.57%
27	Meimoramentu no supply energia Elektridade husi Sub Stasaun Liqulisa ba Portu Tibar (Engineering Procurement Construction - Design, Supply, Installation, Testing and Commissioning Extension Transformer Bay Of the Existing 150/20kv Liqulica Substation to Supply Power to Tibar Bay Port)	China Shandong International Economic And Technical Cooperation Group, LTD	RFP/054/MOP-2021	\$ 4,797,600.00	Dec. 16, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING			
28	Supervision Consultant for Construction of Intersection in the Existing Dili - Liqulica Road to Connect Access Road from Tibar Bay Port (National Road - A03) Sta. 0+000 - Sta. 0+620	Lelo Engineering Unipessoal Lda	RFP/072/MOP-2021	\$ 154,000.00	Dec. 14, 2021	95.77%	30.66%	\$ 47,209.03	\$ 106,790.97	ON-GOING	ONCOING			
29	Construction of Intersection in the Existing Dili-Liqulica Road to Connect Access Road from Tibar Bay Port (National Road-A03)	Aitula Construction, Lda	RT/070/MOP-2021	\$ 1,738,869.60	Dec. 1, 2021					ON-GOING	ONCOING	0.00%	28.30%	28.30%
30	Road and Bridge Maintenance Section : Tibar - Liqulica - Maubara (A03) & Carimbala Loes (A03) Municipality Liqulica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	\$ 153,851.88	Dec. 5, 2019	95.23%	81.19%	\$ 124,915.14	\$ 28,936.74	FHO	FHO			
31	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	ECT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REPI/007/MOPTC-2017	\$ 1,394,750.00	May 17, 2017	47.12%	47.12%	\$ 657,275.92	\$ 737,474.08	ON-GOING				
32	R4D Rural Road Periodic Maintenance Albeno - Asumanu Chainage 0+000 - 4+300 Routine Maintenance Dato - Liqulica - Loidahar Chainage 0+000 - 12+300	Nheu	MPW-W-RFO-190093	\$ 55,012.05	Aug. 22, 2019	100%	89.92%	\$ 49,468.35	\$ 5,543.70	FHO	FHO			
33	R4D Rural Road Periodic Maintenance Loidahar - Loidahar Chainage 0+000 & Metagou - Albeno Chainage 0+000 - 7+600 Routine Maintenance Taitabi - Kutulau Chainage 0+000 - 4+300	Goubara Unip Lda	MPW-W-190096	\$ 71,468.49	Aug. 19, 2019	100%	90.00%	\$ 64,321.64	\$ 7,146.85	FHO	FHO			
34	New installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liqulica Municipality	Maferdi, Lda	RTU/MOPTC-VMOPTC/CGI-PEN : 00000399	\$ 593,093.80	Jan. 6, 2017	91.66%	67.45%	\$ 400,036.22	\$ 193,057.58	ON-GOING	ONCOING	92.32%	0.00%	92.32%
35	New installation of mv, lv line and house Connection from Liqulica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, koni Leopa, Alpele, Maumeta, and Leopa - Liqulica Municipality	Busa, Lda	RTU/MOPTC-VMOPTC/CGI-PEN : 00000371	\$ 276,484.00	July 6, 2016	92.77%	83.49%	\$ 230,841.25	\$ 45,642.75	ON-GOING	ONCOING	92.77%	0.00%	92.77%
36	R4D Rural Road Rehabilitation Begoum - Lebokaiako Chainage 0+000 - 5+000 Liqulica Municipality	15 Raeliti Unip. Lda	RT/034/MOP-2019	\$ 452,362.93	Dec. 20, 2019	76.44%	50.38%	\$ 227,897.03	\$ 224,465.90	ON-GOING	ONCOING	97.15%	0.00%	97.15%
37	Manutensaun Kanais Irrigasaun Faulara - Liqulica	Banir Lema Unip, Lda	RTDL 0000	\$ 47,299.32	Aug. 18, 2021	88.95%	80.06%	\$ 37,865.52	\$ 9,433.80	ON-GOING	PHO	88.95%	6.76%	95.71%
38	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	Metalika Unipessoal, Lda	01/SMA-AMU/PDIM VIII/2021	\$ 176,933.50	Aug. 31, 2021	3.83%	0.00%	\$ -	\$ -		ADN, I.P. la hare	3.83%	0.00%	3.83%
39	R4D Rural Road Spot Improvement Beriakuldu-Laberlaka Chainage 0+000-2+600	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	\$ 131,219.62	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	48.18%	0.00%	48.18%
40	R4D Rural Road Spot Improvement Taitabi - Kutulau Chainage 0+000-1+700, Liqulica Municipality	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	\$ 123,631.72	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	61.00%	2.76%	63.76%
41	R4D Rural Road Spot Improvement Metagou - Albeno Chainage 0+000-7+600, Liqulica Municipality	Metalika Unipessoal, Lda	MOP - CD - NCB -R - 21038	\$ 238,739.71	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	40.21%	0.00%	40.21%
42	R4D Rural Road Spot Improvement Dato - Loidahar Chainage 0+000-12+300, Liqulica Municipality	Luquell Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	\$ 188,589.13	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	51.00%	30.67%	81.67%
43	R4D Rural Road Spot Improvement Aibenu - Asumanu - Leurema Chainage 5+000 - 10	Calulu, Unip Lda	MOP - CD - NCB -R - 21035	\$ 162,215.27	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	54.94%	15.40%	70.35%
44	R4D Rural Road Spot Improvement Aibenu - Asumanu-Leurema Chainage 0+000-5+000, Liqulica Municipality	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	\$ 165,363.43	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	45.83%	0.00%	45.83%
45	R4D Rural Road Spot Improvement Beriakuldu - Laberlaka Chainage 2+500-5+600	Claridade Unip, Lda	MPW-W-210163	\$ 167,071.89	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	30.65%	0.00%	30.65%



#ANEXO B

PROGRESSU FISIKU FULAN OUTUBRO MUNICIPIO LIQUICA

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVA SAUN	Oct-22		
												Previous Progress (%)	This Month Progress (%)	Komulative Progress (%)
46	R4D Rural Road Spot Improvement Gunaba - Lukulal Chainage 0+000-2+000	Craeleki Bercoll, Unip Lda	MPW-W-210143	\$ 76,423.05	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	40.74%	0.00%	40.74%
47	Projeitu Konstrusaun foun ESC publico 01 Liquica	Roman Furak Unip,Lda	NCB 16/MEJD/DNA/2021	\$ 167,079.099	Nov. 1, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	47.70%	0.16%	47.86%
48	Roads Maintenance Section : Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chanel Chander Unipessoal Lda	MPW-W-210202	\$ 112,505.280	44543	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	32.14%	0.00%	32.14%
49	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MEJD PKRIE EBC MAUBOQUE	-	\$ 112,530.010	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	17.42%	8.03%	25.45%
50	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MEJD PKRIE EBC 1,2,3 LIQUICA	-	\$ 99,456.040	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	23.22%	0.72%	23.94%
51	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MEJD PKRIE EPE LOIDAHAR	-	\$ 79,735.630	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	25.63%	0.00%	25.63%
52	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclema	MEJD PKRIE EBF 1,2 LACLOLEMA	-	\$ 89,650.660	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	14.62%	8.26%	22.88%
53	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MEJD PKRIE EBF 1,2 TOLEMA	-	\$ 88,407.020	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	22.24%	2.71%	24.95%
54	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculal	MEJD PKRIE EBF 1,2 LUCULAI	-	\$ 5,151.290	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	45.13%	0.00%	45.13%
55	Consultant Services to Supervise EPC Contractor for the Up-Gradation of Liquica 150/20kV Substation to Supply Power to Tibar Bay Port	PT. Artefak Arkindo (Indonesia) JV with Jazcasnu Unipessoal Lda	RFP/054/MOP-2021	\$ 620,500.000	Dec. 16, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING			
56	Addt. Poste Ilga Maubara	Fu Unip,Lda	RDTL - 0000	\$ 13,000.00	Jan. 1, 2016	0.00	0.00%	\$ -	\$ 13,000.00					
57	New installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CCI- PEN : 00000364	\$ 288,760.22	July 6, 2016	83.73%	75.36%	\$ 217,606.07	\$ 71,154.15	ON-GOING	ONGOING	83.73%	0.00%	83.73%
58	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality	Montana Diak Unipessoal, Lda	SSS/126/MOPTC-2017	\$ 1,901,334.67	Sept. 7, 2017	99.98%	89.98%	\$ 1,710,791.24	\$ 190,543.43	ON-GOING	PHO			
59	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	\$ 275,000.00	Dec. 27, 2016	40.00	38.00%	\$ 104,500.00	\$ 170,500.00	ON-GOING	ADN,I.P la hare	40.00%	0.00%	40.00%
60	Konstrusaun ESTV Lisadlia Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM- LIQ/VIII/2019/03	\$ 171,850.61	Aug. 16, 2019	89.17%	80. 25%	\$ 137,915.77	\$ 33,934.84	ON-GOING	Servisu refere sedauk 100%	89.17%	0.00%	89.17%
61	Rehabilitasaun Sistema be'e mos lha aidela Pandevou ho Mau-Uno,Sucu Guico /162	Oceanla Const Unip.Lda	NCB-MOP-190051	\$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	\$ 72,706.50	\$ 98,259.15	ON-GOING	Provizoriamente paradu hela	54.99%	0.00%	54.99%
62	Road network upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara Municipality	Dongsung Engineering Co.,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOPTC/2016	\$ 7,693,101.00	May 3, 2017	75.33%	75.33%	\$ 5,795,051.15	\$ 1,898,049.85	ON-GOING		75.33%	0.00%	75.33%
63	R4D Rural Road Maintenance Barkau - Laberika Chainage 0 + 000 - 5 + 400 Nunuleta - Darulema Chainage 0 + 000 - 4 + 600,Vaululeta - Maubara Chainage 0 + 000 - 4 + 600	Lulana Unip,Lda	MPW-W-190098	\$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	\$ 43,761.73	\$ 6,940.86	PHO	PHO	95.90%	0.00%	95.90%
64	Konstrusaun Moru Haleu no Posto Siguransa ba Edificio Posto Administrativo Maubara	Rafio Unip. Lda	01/AML/SMA- PDIM/VIII/2021	\$ 56,445.70	July 21, 2021	16.32%	0.00%	\$ -	\$ -		ADN,I.P la hare	16.32%	0.00%	16.32%
65	R4D Rural Road Spot Improvement Nunuleta - Darulema Chainage 0 + 000- 2 + 000, Liquica Municipality	Rito - Pu, Unipessoal,Lda	MOP -CD-RFQ - 21013	\$ 67,382.23	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	2.07%	0.00%	2.07%
66	R4D Rural Road Spot improvement Maialsera -Lissadlia Chainage 4 + 800-9 + 600, Liquica Municipality	Malibo, Unipessoal LDA	MOP - CD - NCB-R- 21033	\$ 152,622.90	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	35.83%	0.00%	35.83%
67	R4D Rural Road Spot Improvement Barkau (Vaviquenla)-Maubara Chainage 0 + 000- 4 + 200	Nheu, Unipessoal LDA	MOP - CD - NCB-R- 21027	\$ 173,484.62	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	45.61%	0.00%	45.61%



#ANEXO B

PROGRESSU FISIKU FULAN OUTUBRO MUNICIPIO LIQUICA

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETU	OBSERVAUN	Oct-22		
												Previous Progress (%)	This Month Progress (%)	Komulative Progress (%)
68	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality	Murak, Unipessoal Lda	MOP - CD- NCB-R- 21032	\$ 153,049.65	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	43.43%	0.00%	43.43%
69	R4D Rural Road Spot Improvement Barkau (Vaviquenia) - Maubara Chainage 8+400-12+500	Meta Loe Crae Bau Unip,Lda	MPW-W-210160	\$ 198,698.25	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	44.41%	0.00%	44.41%
70	R4D Rural Road Spot Improvement Samarapo - Gisu Chainage 0+000-2+000	Nazco Unip Lda	MPW-W-210152	\$ 114,789.50	Oct. 01, 2022	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	11.39%	0.00%	11.39%
71	R4D Rural Road Spot Improvement Barkau (Vaviquenia) - Maubara Chainage 4+200-8+400	Lulana Unip,Lda	MPW-W-210161	\$ 213,930.25	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	34.86%	0.00%	34.86%
72	Konstrusaun ka Reabilitasaun ba EBF Gariana	MEJD PKRIE EBF GARIANA	-	\$ 117,902.04	Oct. 15, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	1.98%	0.00%	1.98%
73	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MEJD PKRIE EBF TAPO	-	\$ 100,033.33	Oct. 15, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	10.61%	-0.09%	10.52%
74	Konstrusaun ka Reabilitasaun ba ESC- Paralelo Maubara/Batuvou	MEJD PKRIE ESC- PARALELO	-	\$ 141,660.22	Oct. 15, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	14.14%	6.27%	20.41%
75	Feasibility study for New Construction of Industrial Park In Liquica, Timor Leste	HABERAN UNIPESSOAL LDA (TIMOR LESTE) In Joint Venture with PT ITC TRAVEL & TOUR	RFP/077/MTCI-2021	\$ 225,373.00	March 24, 2022					ON-GOING				
76	Installation foun ba Linha de Media Tensaun, Balxa Tensaun e Balxadas em Liquica - Maubara	Nla construction, Lda	0000	\$ 490,039.81	Dec. 4, 2012	94.93%	85.44%	\$ 418,669.22	\$ 71,370.59	ON-GOING	ONGOING	94.93%	0.00%	94.93%

INSPEKSAUN HUSI,

(Eng. Marcos de Araujo Ximenes)
Engineru ba Projeitu Infrastrutura Transporte
e Irigasaun ADN,I.P

(Eng. Ludovina Maria H. Guterres)
Engineru ba Projeitu Infrastrutura Transporte
e Irigasaun ADN,I.P

(Eng. Juninho Antonio A. da Cruz)
Engineru ba Edificio Publiku Agua e
Saneamento ADN,I.P

(Eng. Antonia de Fatima Moraes Soares)
Engineru ba Edificio Publiku Agua e
Saneamento ADN,I.P

(Eng. Camilo de Jesus)
Engineru ba Projeitu Mekanikal

VERIFIKA HUSI,

(Eng. Remigio da C.S.dos Santos)
Engineru Senior ba Projeitu Infrastrutura Transporte e Irigasaun ADN,I.P

(Arq. Francisco Xavier D D. Jeronimo)
Engineru Senior ba Projeitu Edificio Publiko
no Be'e Saneamento ADN,I.P

(Eng. Deolindo de Fatima Marques)
Chefe Seksaun Mekanikal
e Elektrikal & ITC ADN,I.P

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora da Unidade de Controlo e Validasaun
de Qualidade, ADN,I.P

#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeto Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Data Inspesaun : 27 Outubro 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 40' 43.435", Latetude :

End Point : Long : E 125° 22' 18.833", Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekpa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
Konstrusaun Foun ESTV Leorema
lokaliza iha suku Leorema, Bazartete,
Munisipiu Liquisa projeitu nee kaer
husi kompania U-Rema Unip. Lda.



#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeto Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Iha terenu kompania kuaze finaliza
ona servisu ba item *finishes*,
windows, doors, steel roof, roofing
no painting ba konstrusaun Ca no Cb
nian.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba konstrusaun *teacher office no*
toilet building ninian servisu hirak
neebe kuaze finaliza no lao hela mak
hanesan: *finishes, steel roof, roofing*,
windows no doors.

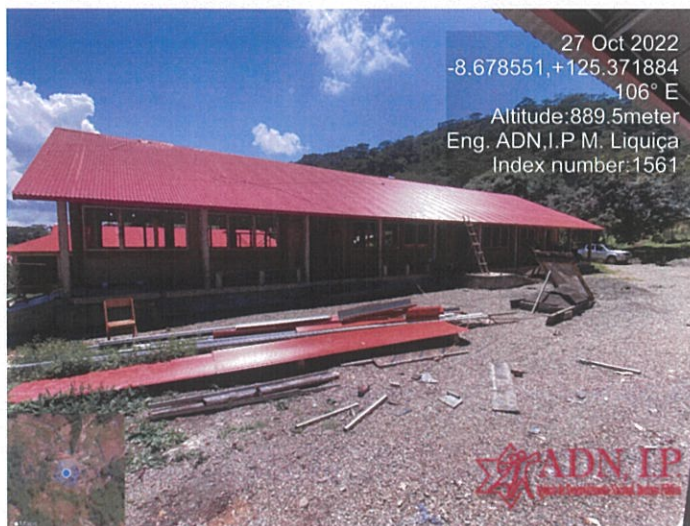



#ANEXU C1 – (BZT24)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Data Inspesaun : 27 Outubro 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 39' 21.442'', Latetude :

End Point : Long : E 125° 22' 51.232'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
foun husi MEJD PKRIE ba
Konstrusaun ka Reabilitasaun EPE
Baura lokaliza iha suku Leorema,
postu Bazartete, Munisipiu Liquisa
projeitu nee kaer husi servisu grupu
komunitariu.

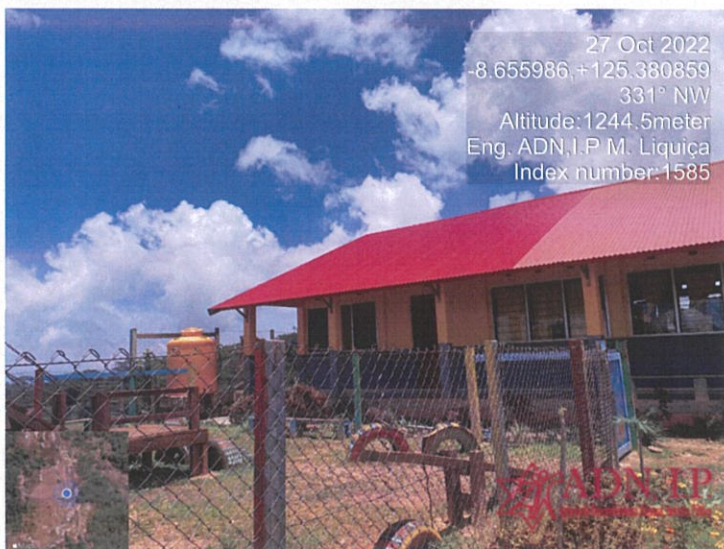

#ANEXU C1 – (BZT24)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Wainhira ekipa enjineiru ADN, IP munisipiu Liquisa halao inspesaun iha terenu ba projeitu refere hatoo husi autoridade/professora sira katak servisu nee remata tiha ona.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Servisu grupu refere nia problema iha terenu maka enjineiru neebe grupu tau fiar atu hare servisu projeitu ida nee nunka marka prezensa iha terenu atu hare progresu servisu real.





#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Data Inspesaun : 20 Outubro 2022

Fatin Inspesaun : Fahilebo - Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 38' 12.154'', Latetude :

End Point : Long : E 125° 24' 35.457'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu foun
husi MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EPE Ermeta Fahilebo iha
suku Fahilebo, postu Bazartete, Liquisa
projeitu nee kaer husi servisu grupu
komunitariu.



#ANEXU C1 – (BZT25)


Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tuir informasaun neebe enjineiru ADN,
IP sira hetan iha terenu katak servisu
projeitu refere lao tarde tanba grupu sei
hein orsamentu ba faze daruak nian hodi
bele sosa material hirak neebe atu lori mai
iha terenu hodi bele continua.

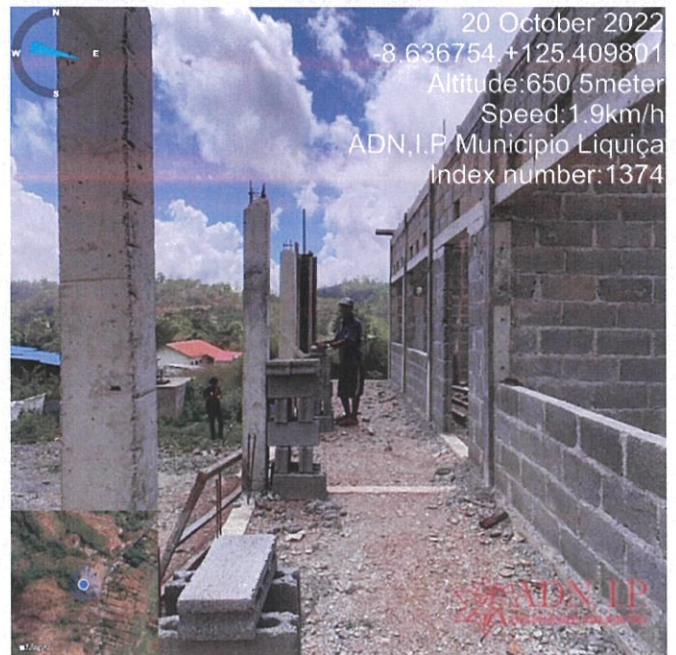

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Dadaun nee servisu projeitu refere atinji
iha servisu item *blockwall* no ba iha
concretework nian too iha servisu ba item
top beam.





#ANEXU C1 – (BZT26)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Cassait
Kompania :
No. kontratu :

Data Inspesaun : 13 Outubro 2022

Fatin Inspesaun : Lauhata - Bazartete, Liquisa

Koordinadas :

Start Point : Long : S 8° 34' 19.391'', Latetude :

End Point : Long : E 125° 27' 52.593'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Moraes Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu Likisa
halao inspesaun ba projeitu foun husi
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EPE Cassait iha suku
Lauhata, Bazartete, Liquisa projeitu nee
kaer husi servisu grupu komunitariu.

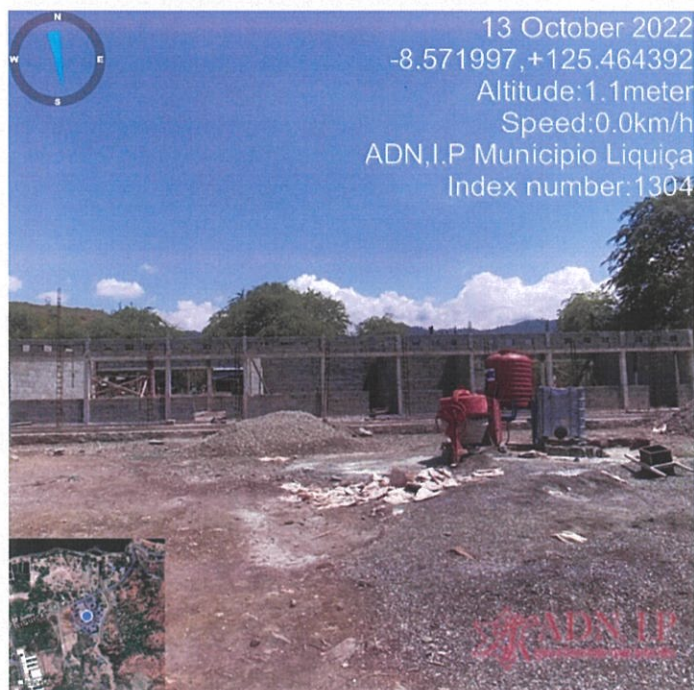

#ANEXU C1 – (BZT26)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Cassait
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Wainhira ekipa enjineiru ADN, IP munisipiu Liquisa nian halao inspesau iha terenu, ladun iha mudansa makas ba progresu fiziku ba projeitu refere.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Problema neebe servisu grupu ida nee hasoru ida maka enjineiru grupu nian neebe ladun ativu atu halo linha koordenasaun ho parte enjineiru projeitu nain ka ADN, IP. No enjineiru mos ladun ativu iha terenu.

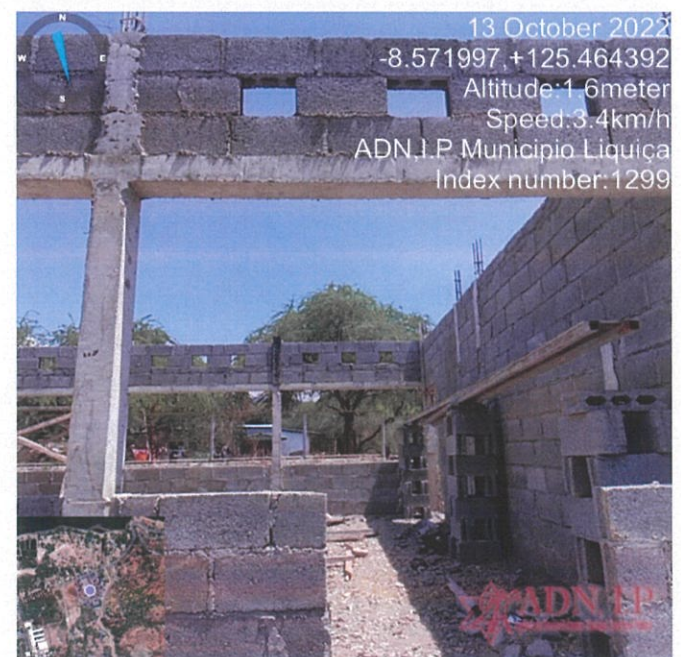



#ANEXU C1 – (BZT27)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE ESG Classe Paralelo Bogoro
Kompania :
No. kontratu :

Data Inspesaun : 20 Outubro 2022

Fatin Inspesaun : Bogoro – Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 36.980", Latetude :

End Point : Long : E 125° 23' 58.119", Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Moraes Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu Foun
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun ESG Classe Paralelo
Bogoro, lokaliza iha suku Bogoro,
Bazartete, Munisipiu Liquisa, neebe kaer
husi servisu Grupu Komunitariu

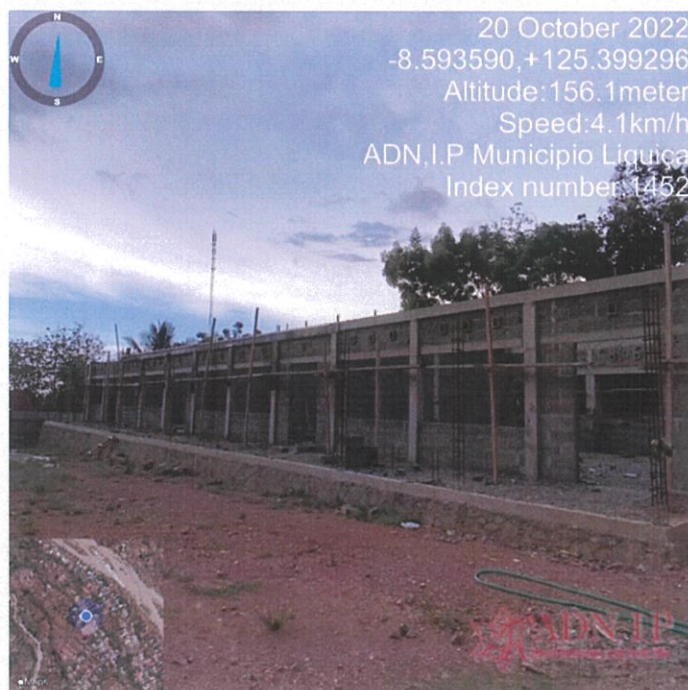

#ANEXU C1 – (BZT27)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE ESG Classe Paralelo Bogoro
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tuir inspesaun neebe enjineiru ADN, IP
sira halao iha terenu hare ba progresu
fiziku atual projeitu refere atinji iha item
blockwall no ba *concretework* ninian
grupu foin finaliza fui betaun ba *top*
beam.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Servisu grupu mos finaliza ona monta
besi tulangan ba item *ringbalk* no
ringbalk samping no kesi ona besi ho
begel molok kontinua servisu monta
bekisting no fui betaun.





#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Data Inspesaun : 13 Outubro 2022

Fatin Inspesaun : Dato, Liquica Vila

Koordinadas :

Start Point : Long : 8.35'21.273"S, Latetude :

End Point : Long : 125.20'1.933"E, Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu husi
Ministeriu Edukasaun Juventude no
Desportu nian ba Konstrusaun Foun
ESG Publico 01-Liquica lokaliza iha
suku Dato, Liquisa Vila, Munisipiu
Liquisa, neebe kaer husi kompania
Roman Furak Unip. Lda.



#ANEXU C1 – (LV20)


Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Ba servisu iha klase C (figura iha sorin)
nia progresu agora daudaun paradu hela
hafoin kompania finaliza servisu item
steel roof no gording ninian.

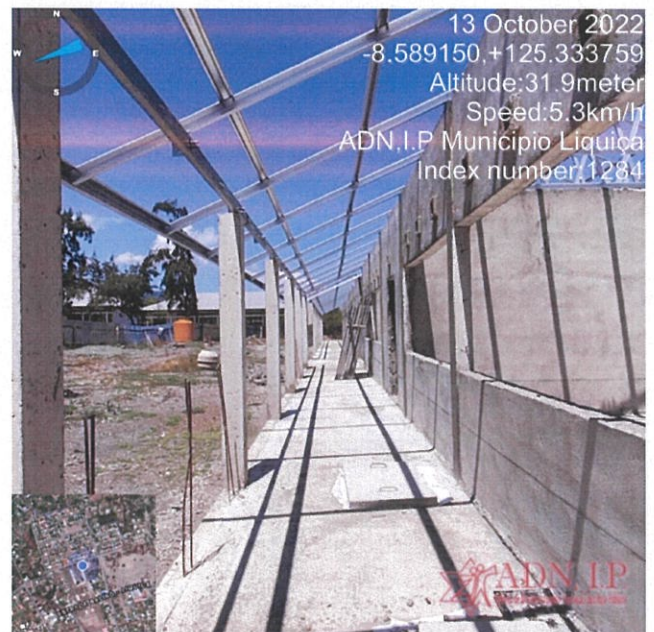

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Servisu kompania nian neebe mak lao
hela ka finaliza tiha ona tan ba projeitu
ida nee maka item *finishes* ka *plesteran*.

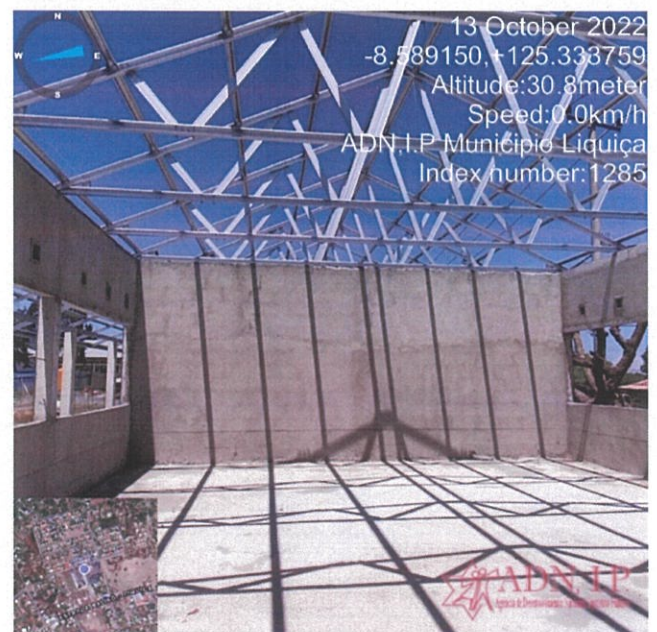

#ANEXU C1 – (LV22)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Data Inspesaun : 12 Outubro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 49.086", Latetude :

End Point : Long : E 125° 18' 51.269", Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa ADN, IP Munisipiu
Liquisa halao inspesaun ba
projeitu husi MEJD PKRIE ba
Konstrusaun ka Reabilitasaun
EBF 1, 2 Mauboque lokaliza
iha suku Dato, Liquisa Vila
Munisipiu Liquisa neebe kaer
husi servisu Grupu
Komunitariu.



#ANEXU C1 – (LV22)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Servisu konstrusaun refere nia
item neebe lao hela maka
hanesan: *concretework (lintel
beam, top beam, ringbalk
samping no ringbalk).*



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Enjineiru ADN, IP mos orienta
ona trabaliador grupu nia
servisu ba item *top beam* neebe
grupu fui ladun diak no tenki
taka tutuir no hadia tutuir.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

#ANEXU C1 – (LV22)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Data Inspesaun : 24 Outubro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 49.086'', Latetude :

End Point : Long : E 125° 18' 51.269'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa ADN, IP Munisipiu
Liquisa halao inspesaun ba
projeitu husi MEJD PKRIE ba
Konstrusaun ka Reabilitasaun
EBF 1, 2 Mauboque lokaliza iha
suku Dato, Liquisa Vila
Munisipiu Liquisa neebe kaer
husi servisu Grupu Komunitariu.



#ANEXU C1 – (LV22)


Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Servisu grupu refere iha terenu
ba item *ringbalk no ringbalk*
sampling kuaze besik finaliza
ona, no hakoi ona plat HD ba iha
tulangan *ringbalk*.

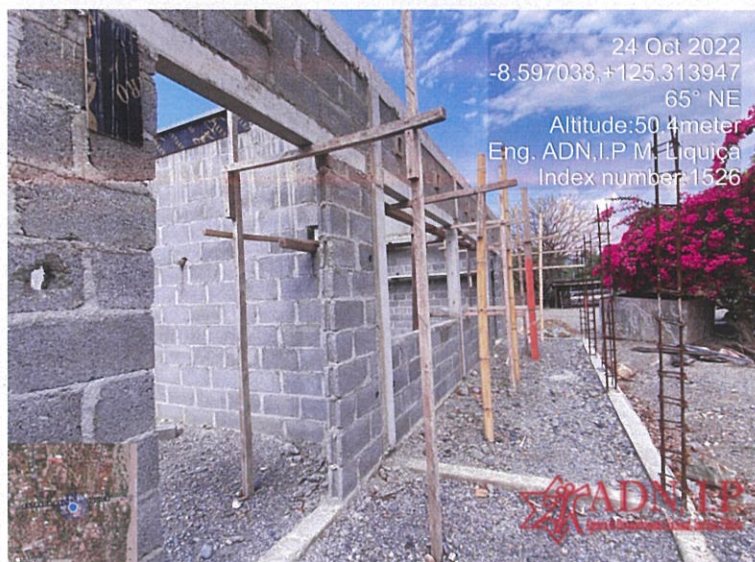

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Enjineiru grupu ladun iha linha
koordinasaun neebe diak ho
enjineiru husi ADN, IP neebe iha
buat falta ruma iha projeitu ida
nee maibe enjineiru seidauk
hasoru ekipa ADN, IP atu koaliala.

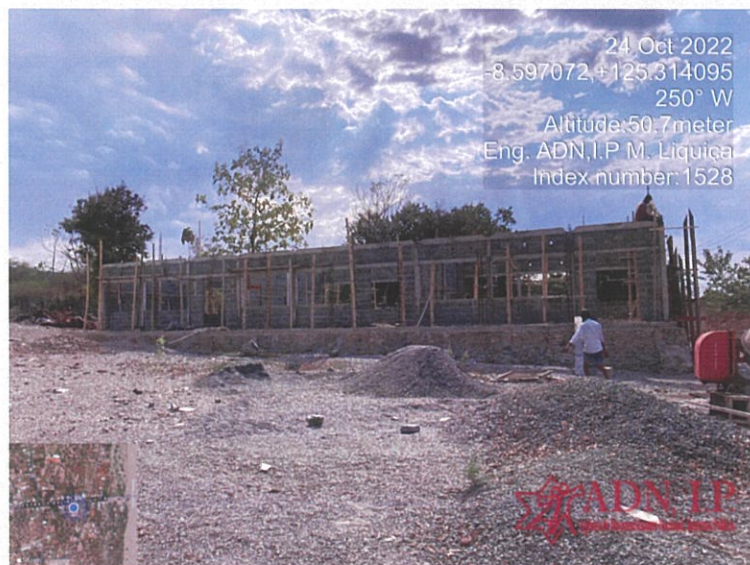



#ANEXU C1 – (LV23)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBC 1,2,3 Liquica
Kompania :
No. kontratu :

Data Inspesaun : 12 Outubro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 32.592'', Latetude :

End Point : Long : E 125° 19' 53.005'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP
Munisipiu Liquisa halao
inspesaun ba projeitu Foun
MEJD PKRIE ba Konstrusaun
ka Reabilitasaun EBC 1, 2, 3
Liquica lokaliza iha suku Dato,
Liquisa Vila munisipiu
Liquisa, neebe kaer husi
servisu Grupu Komunitariu.

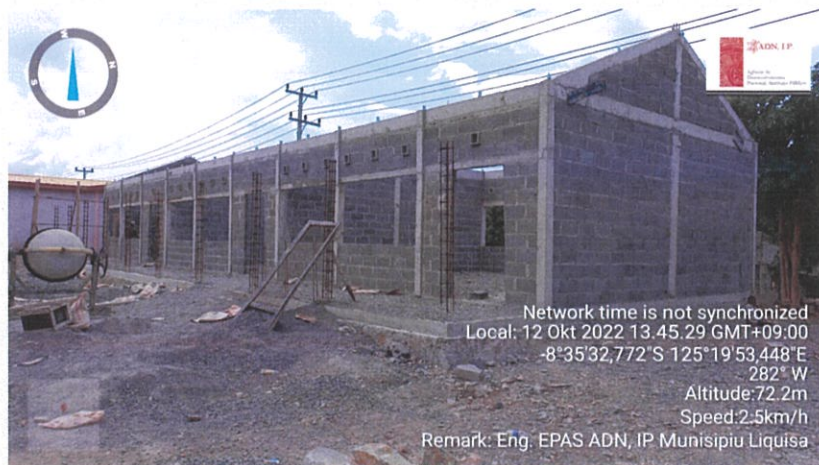

#ANEXU C1 – (LV23)


Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBC 1,2,3 Liquica
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Servisu grupu ba konstrusaun
refere nia progresu atinji too
item *concretework: top beam*.

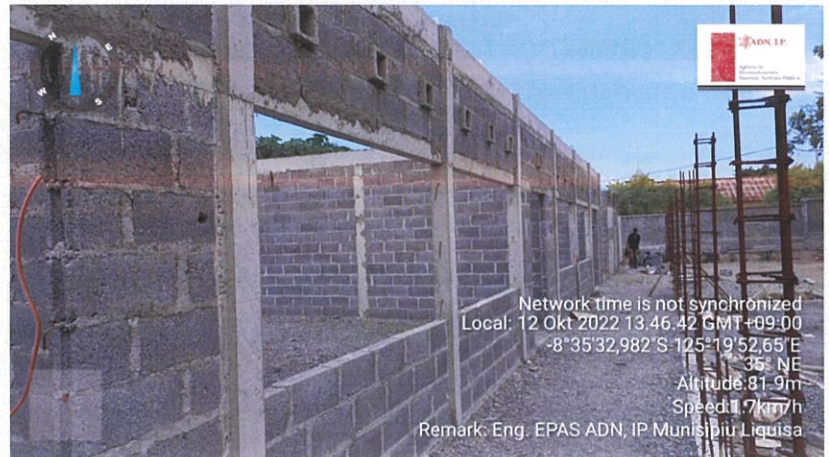

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba servisu item *finishes*:
plesteran bagian dalam nian
mos hahuu lao ona ba
konstrusaun klase nian.

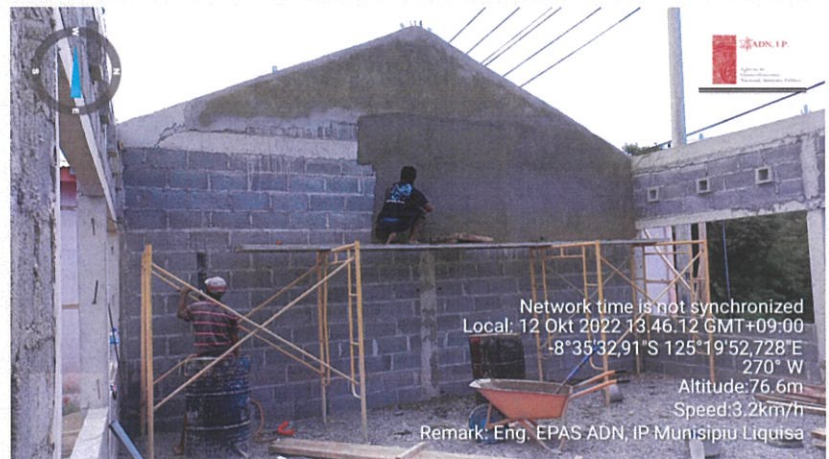



#ANEXU C1 – (LV25)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Laclolema
Kompania :
No. kontratu :

Data Inspesaun : 20 Outubro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 37' 11.666'', Latetude :

End Point : Long : E 125° 18' 55.306'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Moraes Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EBF 1, 2 Laclolema
lokaliza iha suku Dato, Liquisa Vila
munisipiu Liquisa, neebe kaer husi
servisu grupu komunitariu.

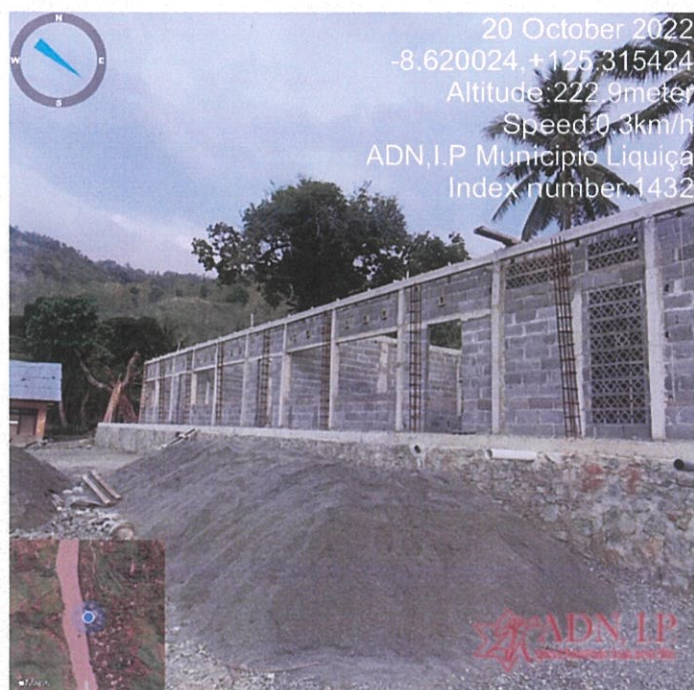

#ANEXU C1 – (LV25)


Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Laclolema
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Servisu konstrusaun grupu refere la hetan koordinasaun diak ho enjineiru grupu tanba enjineiru grupu ladun ativu iha terenu atu hare servisu grupu refere.

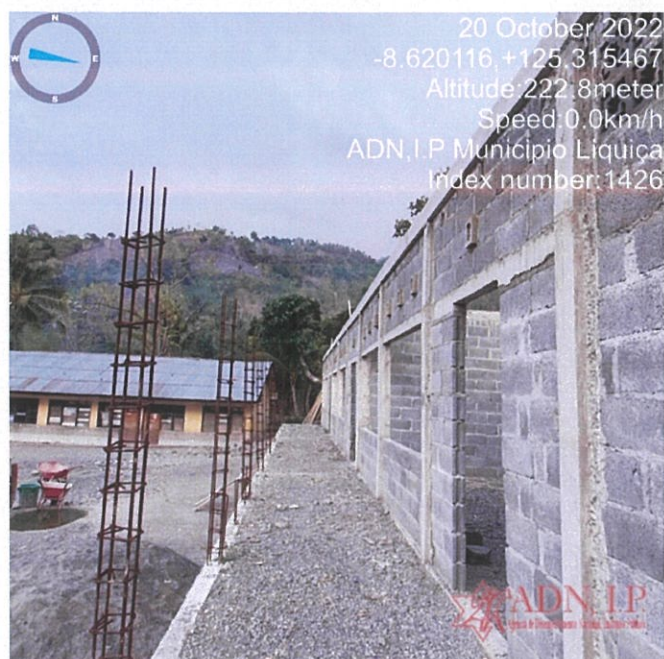

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tekniku ADN, IP foo ona instrusaun ba iha ekipa grupu nian atu hare didiak no tau atensaun ba servisu hada batako nian tanba iha parte balu ladun diak (la rapi/kleuk).

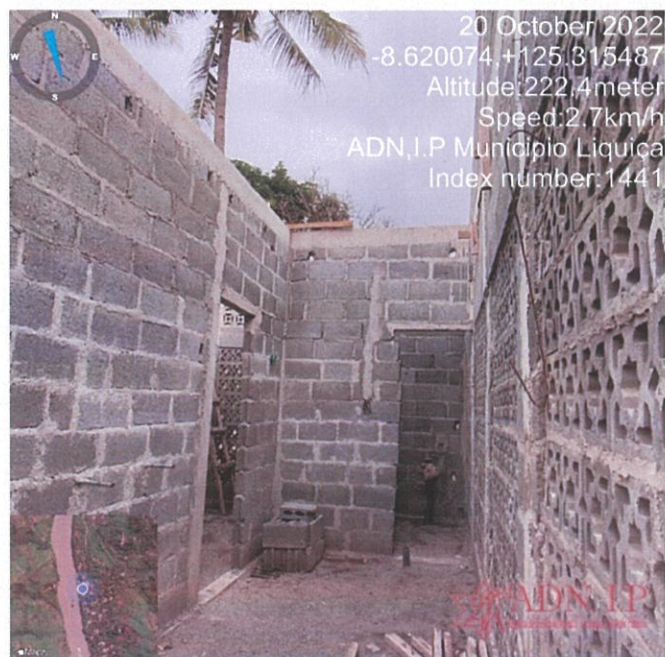

#ANEXU C1 – (LV26)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Tolema
Kompania :
No. kontratu :

Data Inspesaun : 24 Outubro 2022

Fatin Inspesaun : Leotela – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 40' 25. 106'', Latetude :

End Point : Long : E 125° 18' 39. 875'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Moraes Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP
Munisipiu Liquisa halao
inspesaun ba projeitu MEJD
PKRIE ba Konstrusaun ka
Reabilitasaun EBF 1, 2 Tolema
lokaliza iha suku Leotela,
Liquisa Vila munisipiu Liquisa,
neebe kaer husi servisu grupu
komunitariu.

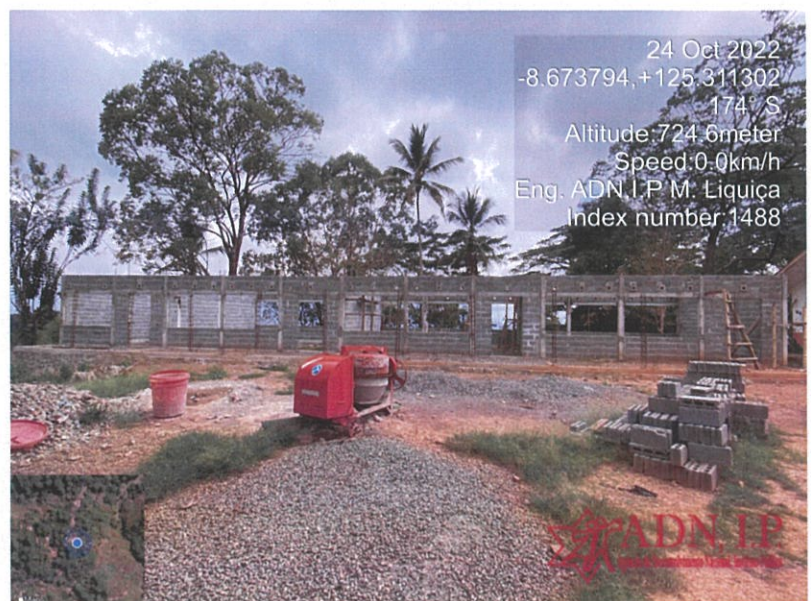

#ANEXU C1 – (LV26)


Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Tolema
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Servisu grupu refere atinji iha
servisu *pembesian tulangan* ba
item *top beam* nian no
trabaliador balu komesa monta
bekisting.

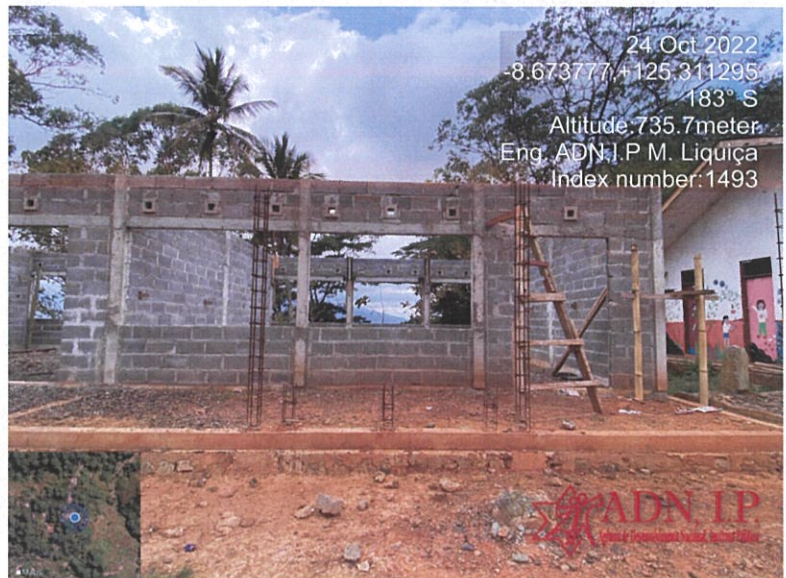

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Enjineiru ADN, IP foo
instrusaun ona ba grupu atu
kontrola no halo koordensaun
diak ho ekipa tekniku sira atu
nunee servisu bele lao tuir mata
dalan neebe loos.

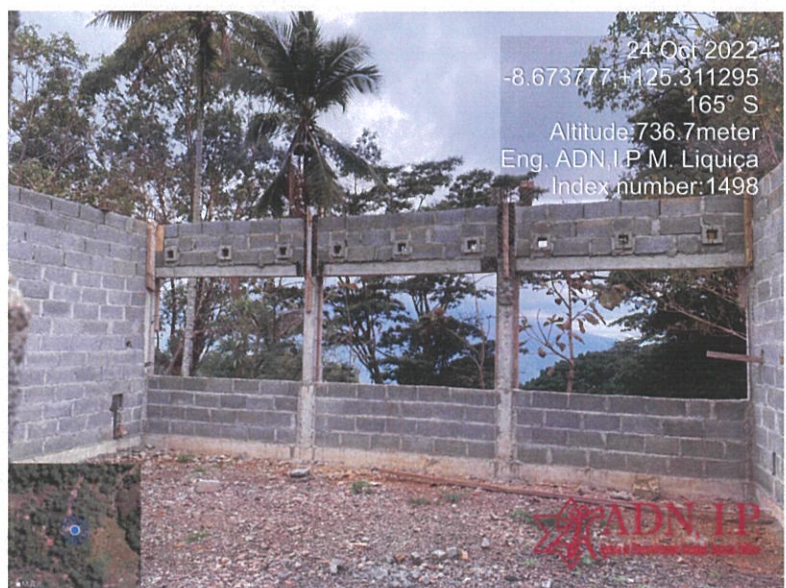



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Data Inspesaun : **24 Outubro 2022**

Fatin Inspesaun : Maubara - Liquica

Koordinadas :

Start Point : Long : S 8° 36' 33.682", Latetude :

End Point : Long : E 125° 13' 5.010", Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia de Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa nian halao inspesaun ba
projeitu MEJD PKRIE –
Konstrusaun Foun ESG Classe
Paralelo Maubara iha suku Maubara,
postu Maubara, munisipiu Liquisa.
Neebe kaer husi servisu Grupu
Komunitariu.

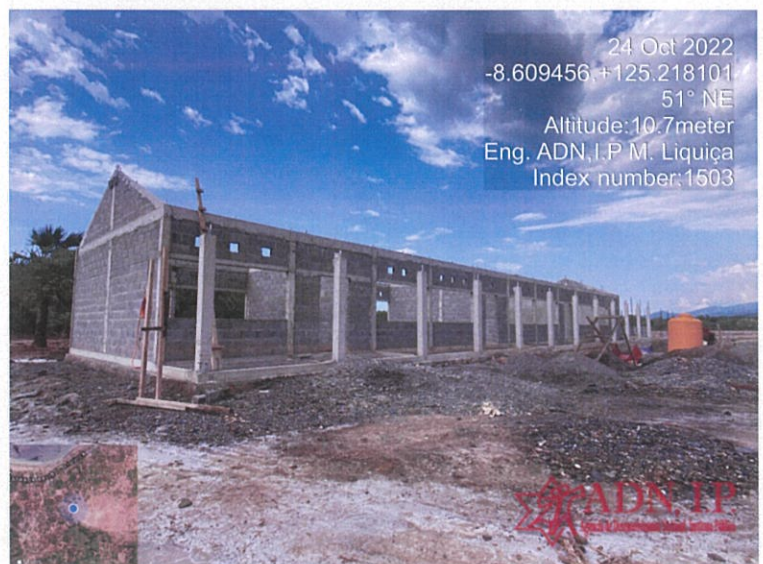



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 – (MBR19)


Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Servisu grupu refere iha terenu atinji
ona servisu ba item *concretework* ba
top beam nian no mos lao ona iha
terenu servisu *plesteran* ba *finishes*.

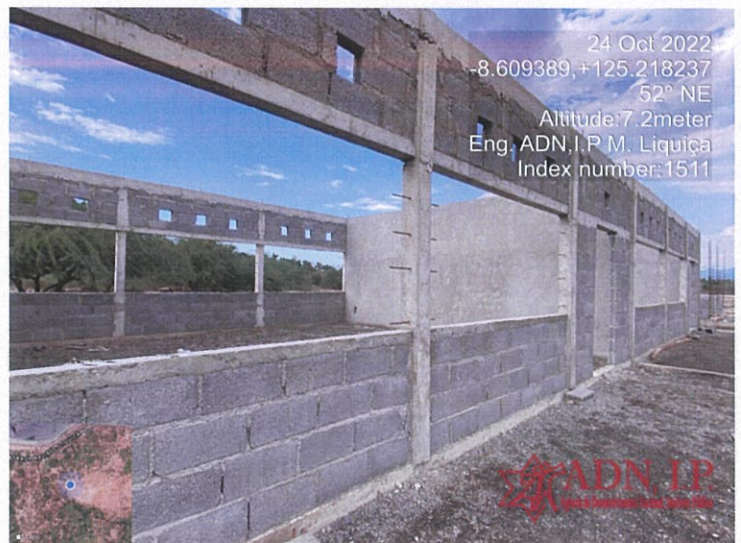

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba servisu konstrusaun Tb nian
grupu finaliza ona servisu
concretework ba *ground beam* no
hahuu servisu *blockwall*.

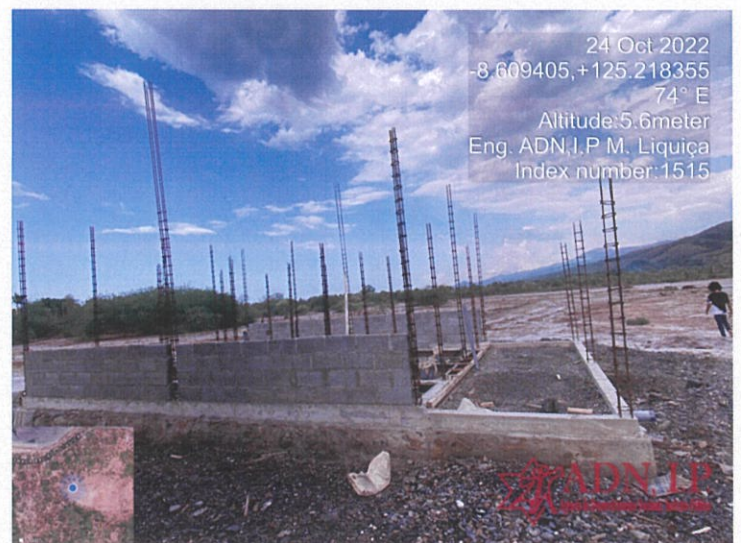

ANEXO C1 (LV13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality
Naran Companhia : Prudencia Unip.Lda
No. kontratu : MOP - CD - NCB-R - 21036

Data Inspeksaun : 12/Outubru/2022

Fatin Inspeksaun : Suco Taltabi - Kutulau

Koordinat :

Start Point : Long : 125.3714575
End Point : Long : 125.3801075


Latetude : - 8.64451919
Latetude : - 8.6527164

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
1 Eng. Luduvina Guterres

Sketch & Foto Desenho

Sketch Item servisu : *Plum Concrete*


Sta, 3+400-3+600



t	L	Distacia	Volume
0.12	3.75	200.00	90.00
Total			90.00 m³

Sketch Item servisu : *Plum Concrete*

Sta, 5+400-5+600



t	L	Distacia	Volume
0.12	3.75	200.00	90.00
Total			90.00 m³

Observasaun iha tereno no Foto Aktual

Companhia halo Plum Concrete iha no Sta, 3+100-3+300



Companhia halo Plum Concrete iha no Sta, 1+200 - 1+300



ANEXO C1 (LV15)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)

No. kontratu : MPW-W-210150

Data Inspeksaun : 12 Outubru 2022

Fatin Inspeksaun : Suco Loidahar

Koordinat :

Start Point : Long : 125°19'36.41779

End Point : Long : 125°19'36.41779

Latetude : - 8°36'46.93352


Latetude : - 8°36'46.93352

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Luduvina M.H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : *Stone Masonry*

Sta.5+300-5+420



Area	Distacia	Volume
0.35	120.00	42.00
Total		42.00 m³


Observasaun iha tereno no Foto Aktual

Companhia halo Line Draen iha Suco Loidahar no Sta, 4+300 - 4+400




Sketch Item servisu : *Stone Masonry*

Sta, 7+500-7+630



Area	Distacia	Volume
0.35	130.00	45.50
Total		45.50 m³



Area	Distacia	Volume
0.35	100.00	35.00
Total		35.00 m³

Companhia halo Line Draen iha Suco Loidahar no Sta, 4+300 - 4+400



ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 25/Outubru/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3469018

Latitude : - 8.680286396

End Point : Long : 125.3739113


Latitude : - 8.684259297

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H. Guterres

Sketch & Foto Desenho

Sketch Item servisu : Gabion

Sta, 1+565 - 1+565

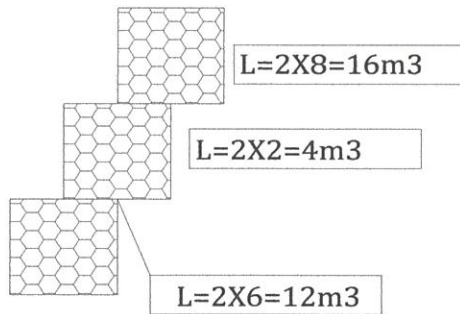


Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Gabion

Sta, 1+565 - 1+565

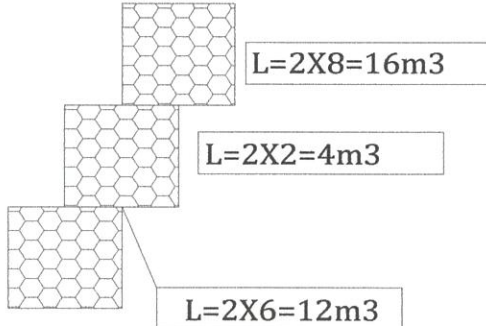

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 25/Outubru/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3469018

Latetude : - 8.680286396

End Point : Long : 125.3739113


Latetude : - 8.684259297

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Luduvina M.H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : Stone Masonry

Sta, 5+100-5+200




Area	Distacia	Volume
0.35	100.00	35.00
Total		35.00 m³

Observasaun iha tereno no Foto Aktual




Sketch Item servisu : Stone Masonry

Sta, 6+100-6+200



Area	Distacia	Volume
0.35	100.00	35.00
Total		35.00 m³

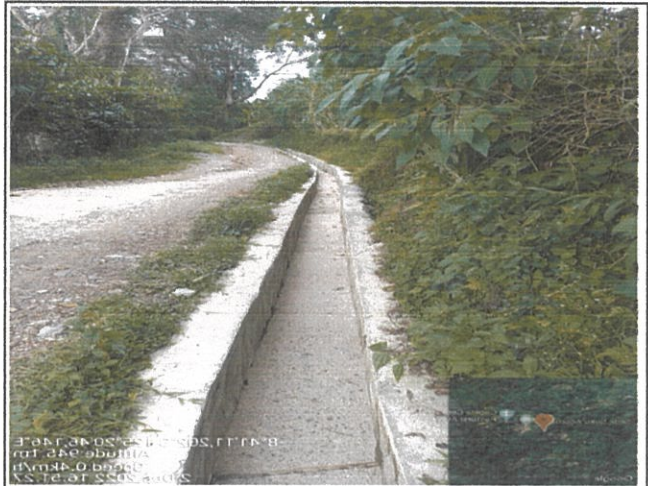

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 25/Outubru/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3469018
End Point : Long : 125.3739113


Latetude : - 8.680286396
Latetude : - 8.684259297

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : Excavation

Sta, 6+300-6+400




T	W	Distacia	Volume
0.12	4	90.00	43.20
Total			43.20 m³

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Excavation

Sta, 4+500-4+600



T	W	Distacia	Volume
0.12	4	120.00	57.60
Total			57.60 m³



ANEXO C1 (LV10)
Back-up Data

Naran Projeto	:	Manutensaun Kanais Irrigasaun Faulara - Liquica
Contractor	:	Banirlema Unip.Lda
No. kontratu	:	2021-G21-015-AG

Data Inspeksaun : 11/Outubru/2022

Fatin Inspeksaun : Suco Lisadila

Koordinat :
Start Point : Long : -8.73011843
End Point : Long : -8.730487275

Latetude : 125.2521963
Latetude : 125.248759050

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Geovanio A. Aleixo

Sketch & Foto Desenho

Sketch Item servisu : Line Drain
STA, 0+000 - 0+500

Companhia Halo htu ona Draenagem Irigasaun iha Tereno, no kondisaun Draenagem kondisaun sei diak nafatin

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Line Drain
STA, 0+000 - 0+500

Companhia Halo itu ona Draenagem Irigasaun iha Tereno, no kondisaun Draenagem kondisaun sei diak nafatin



Sketch Item servisu : Line Drain
STA, 0+000 - 0+500

Companhia Halo itu ona Draenagem Irigasaun iha Tereno, no kondisaun Draenagem kondisaun sei diak nafatin



ANEXO C1 (BZT20)

Naran Projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Contractor : TM.Cailebo Unip.Lda

No. kontratu : MPW-W-210158

Data Inspeksaun : 17/Outubru /2022

Fatin Inspeksaun : Suco Fahilebo -Bucumera

Koordinat :

Start Point : Long : 125.3958511
End Point : Long : 125.3828331


Latetude : - 8.634983018
Latetude : - 8.640302834

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina Guterres

Sketch & Foto Desenho

Sketch Item servisu : Plum Concrete

Sta, 3+200-3+330




T	w	Distacia	Volume
0.12	4.00	130.00	62.40
Total			62.40 m³

Observasaun iha tereno no Foto Aktual




Sketch Item servisu : Plum Concrete

Sta, 3+800-3+900



T	w	Distacia	Volume
0.12	4.00	100.00	48.00
Total			48.00 m³

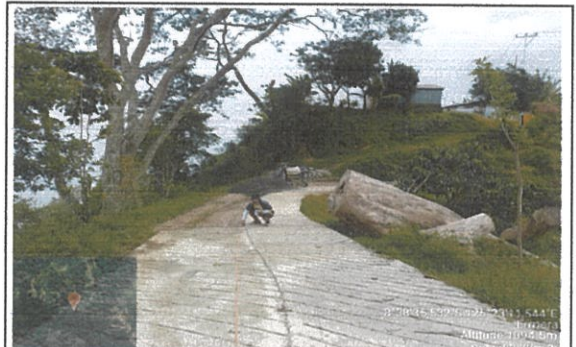

ANEXO C1 (BZT18)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality
Contractor : Hatuleo Unip.Lda
No. kontratu : MPW-W-210144

Data Inspeksaun : 6/Outubru/2022

Fatin Inspeksaun : Suco Libaloa-Fahilebo

Koordinat :

Start Point : Long : 125.43836103
End Point : Long : 125.4135714

Latitude : - 8.64943384


Latitude : - 8.63017393788538

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina Guterres

Sketch & Foto Desenho

Sketch Item servisu : Line Drain

STA, 3+500-3+600




T	W	Distacia	Volume
0.12	2	100.00	24.00
Total			24.00 m³

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Excavation

STA, 4+700-4+800




T	W	Distacia	Volume
0.12	2	100.00	24.00
Total			24.00 m³



Sketch Item servisu : Plum Concrete

STA, 5+100-5+200



T	W	Distacia	Volume
0.12	2	100.00	24.00
Total			24.00 m³



ANEXO C1 (BZT19)

Back-up Data

Naran Projeto : Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000
Contractor : Craeleki Bercoli Unip.Lda
No. kontratu : MPW-W-210145

Data Inspeksaun : 12/Outubru/2022

Fatin Inspeksaun : Suco Maumeta - Metagou

Koordinat :

Start Point : Long : 125.34157891
End Point : Long : 125.38295813

Latetude : - 8.5948749774
Latetude : - 8.62965918


Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Luduvina Guterres

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry

Sta, 3+200

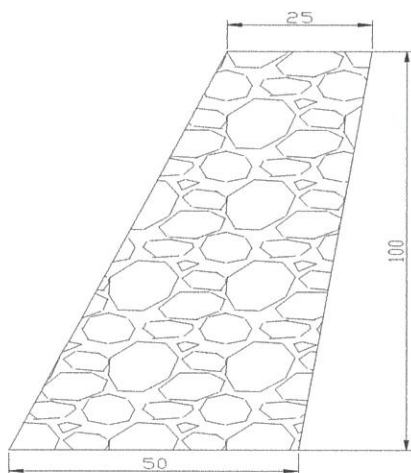


Area	Distacia	Volume
0.375	190.00	71.25
Total		71.25 m³



Sketch Item servisu : Stone Masonry

Sta, 5+150

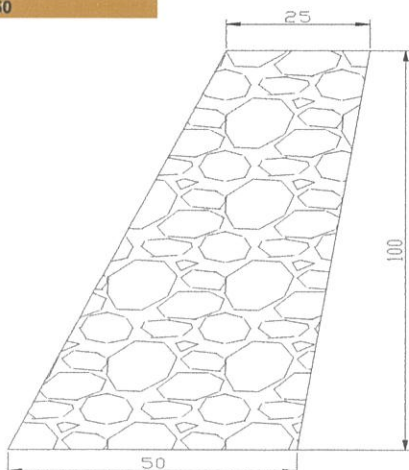

Area	Distacia	Volume
0.375	190.00	71.25
Total		71.25 m³



ANEXO C1 (BZT30)
Back-up Data

Naran Projeto : Construction of Intersection in The Existing Dili - Liquiça Road to Connect Access Road From Tibar Bay Port (National Road-A03)
Contractor : Aitula Unip.Lda
No. kontratu : RT/070/MOP-2021

Data Inspeksaun : 24/Outubru /2022

Fatin Inspeksaun : Tibar

Koordinat :
Start Point : Long : -8.57538396
End Point : Long : -8.57400878


Latetude : - 125.4754456100
Latetude 125.472010710

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina Guterres

Sketch & Foto Desenho

Sketch Item servisu : Removal Pavement, Sidewalk, Curbs, etc

Sta, 0+100 - 0+200



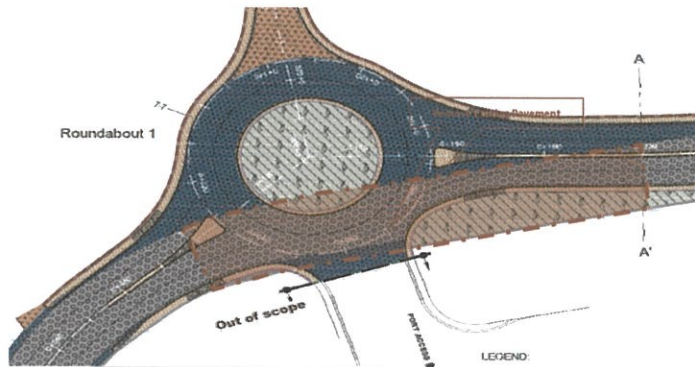


Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Removal Pavement, Sidewalk, Curbs, etc

Sta, 0+380 - 0+480

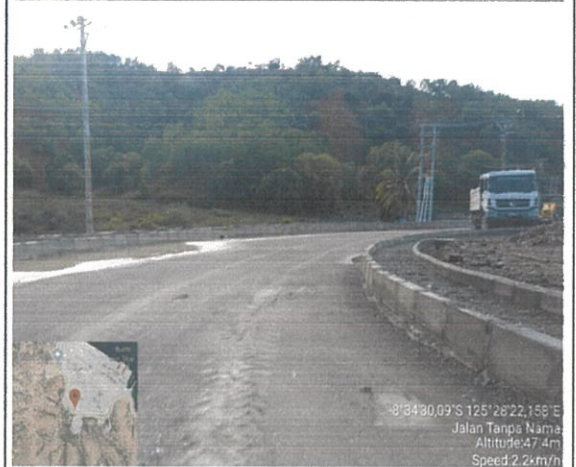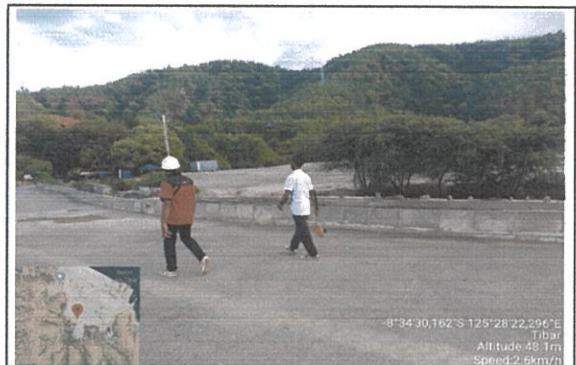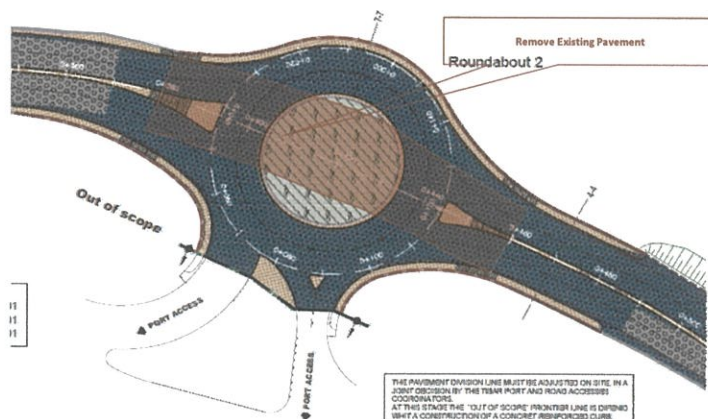

ANEXO C1 (BZT30)

Back-up Data

Naran Projeto : Construction of Intersection in The Existing Dili - Liquiça Road to Connect Access Road From Tibar Bay Port (National Road-A03)
Contractor : Aitula Unip.Lda
No. kontratu : RT/070/MOP-2021

Data Inspeksaun : 24/Outubru /2022

Fatin Inspeksaun : Tibar

Koordinat :
Start Point : Long : -8.57538396
End Point : Long : -8.57400878


Latetude : - 125.4754456100
Latetude 125.472010710

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho

Sketch Item servisu : Retaining Wall (Cyclope)

Sta, 0+100 - 0+200


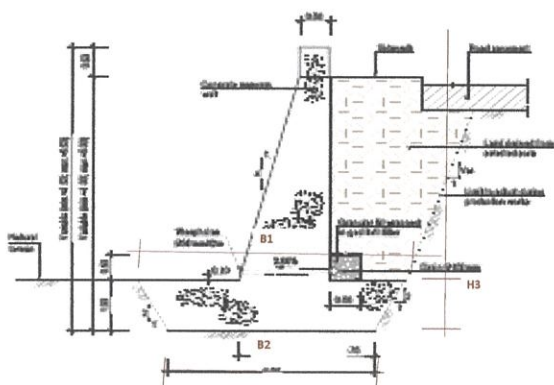


Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Retaining Wall (Cyclope)

Sta, 0+380 - 0+480

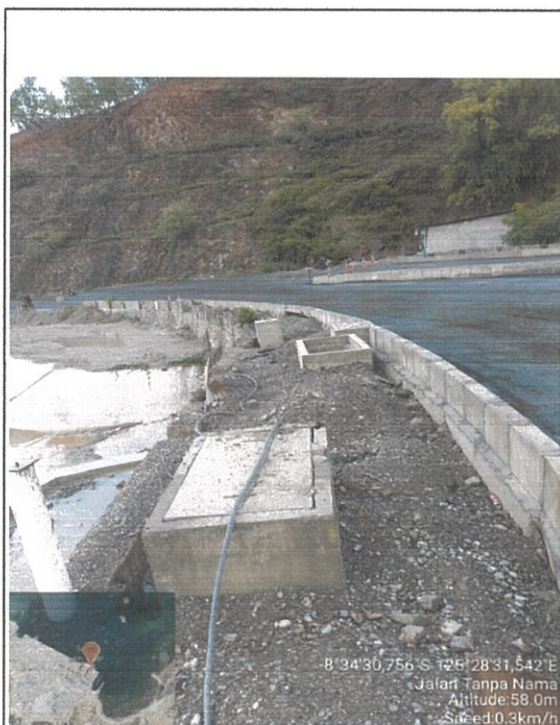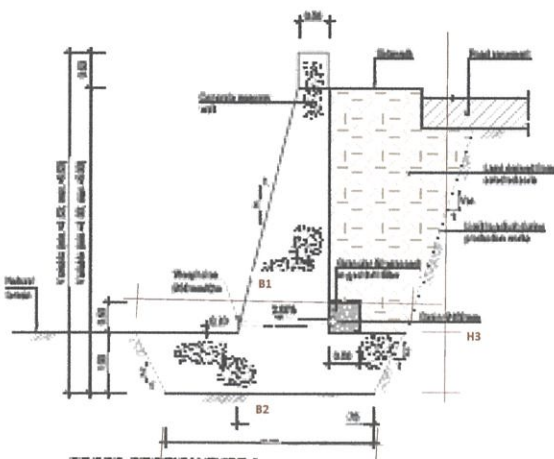



Naran Antónia de Fatima Morais Soares

MUNICIPIO LIQUICA - NO POSTOS							2022																																
Município / Posto	No.	Naran Projeto	Naran Companhia	No. Contrato	Kategoria	Dono do Projeto	Action	Outubro																														OBS	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30		
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	2	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	Nheu Unip. Lda.	MPW-W-RFQ-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	3	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica (162)	Goubara Unip. Lda.	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	4	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda.	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	5	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip. Lda.	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	6	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip. Lda.	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	7	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip. Lda.	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	8	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unip. Lda.	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	9	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip. Lda.	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	10	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip. Lda.		LM	MINISTERIO AGRICULTURA E PESCAS	Plan																																
							Actual																																
	11	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip. Lda.	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	12	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip. Lda.			MINISTERIO DAS OBRAS PUBLICAS	Plan																																
						Actual																																	
13	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
						Actual																																	
14	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip. Lda.	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
						Actual																																	
15					LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
						Actual																																	
16	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip. Lda.	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
						Actual																														On-going			
17	For Roads Maintenance Section Tibar-Liquica-Maubara-Carimbala-Loes (A03)	Chanel Chander Unip. Lda.	MPW-W210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
						Actual																																	
18	MEJD PKRIE EBF Mauboque	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
19	MEJD PKRIE EBC 1,2,3 Liquica	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
20	MEJD PKRIE EPE Loidahar	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
21	MEJD PKRIE EBF 1,2 Laclolema	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
22	MEJD PKRIE EBF 1,2 Tolema	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
23	MEJD PKRIE EBF 1,2 Luculai	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip. Lda.		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																

[illegible]

Note:

Plano Període inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Implementasaun Plano Periode inspesaun iha tereinu

Prepara Husi :

(Eng. Antónia de Fátima Morais Soares)
Eng. ba Edificio Publico Agua e Saneamento Municipio
Liquica ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validação de
Qualidade ADN.I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Ejecutivo ADN.I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng.		Marcos X. de Araujo					2022																																		
Município		MUNICIPIO LIQUICA NO POSTOS																																							
Município / Posto		No. Naran Projeto	Naran Companhia	No. Contrato	Kategoria	Dono do Projeto	Action			OUTUBRO																															OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31			
Municipal	1	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	2	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	3	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	4	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	5	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	6	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	7	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda		LM	MINISTERIO AGRICULTURA E PESCAS	Plan																															PHO			
							Actual																																		
	8	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	9	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	10	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	11	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going			
							Actual																																		
	12	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip.Lda	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip,Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		
							Actual																																		
	2	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		

[Handwritten signature]



Naran Eng.	Marcos X. de Araujo					2022																																	
Município	MUNICIPIO LIQUICA NO POSTOS																																						
Município / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
	1	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	2	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																
							Actual																																
	3	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip Lda	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	4	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	5	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																																
							Actual																																
	6	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																
							Actual																																
	7	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Qeson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																																
							Actual																																
	8	New construction of isolation for covid 19 in chi liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																																
							Actual																																
	9	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTL/MPIE/AND /DA- RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																
							Actual																																
	10	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																PHO
							Actual																																
	11	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan.Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															On Going	
							Actual																																
	12	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan.Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																
	13	R4D Rural Road Spot Improvement Libalao- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																
	14	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																
	15	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																
	16	Construction of Intersection in the Existing Dili-Liquica Road to Connect Acces Road From Tibar Bay Port (Nacional Road-A03)	Aitula.Unip.Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going		
							Actual																																
		TOTAL PROJETO ON-GOING																																					

Note:

Plano Periode inspesaun iha tereinu Relatoriu avaliasuan mensal iha Dili Inspesaun Pagamentu Anual iha tereinu Implementasaun Plano Periode Inspesaun iha tereinu Iha Municipio Liquica

Prepara Husi :

(Eng. Marcos X. de Araujo)

Eng. ba Projeto Infraestrutura, Transportes e Irigasaun
Municipio Liquica ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Vajia Freitas)
Coordenador da Unidade de Controlo e
Validasaun de Qualidade ADN.I.P

As

Aprova Husi :


(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN.I.P



PLANU INSPESAUN

Naran Eng. Juninho António Abrantes da Cruz						2022																																	
Município						MUNICIPIO LIQUICA NO POSTOS																																	
Município / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	Outubro																															OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
Liquica Vila (LV)	1	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip. Lda.	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going	
							Actual																																
	2	MEJD PKRIE EBF Mauboque	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going	
							Actual																															On-going	
	3	MEJD PKRIE EBC 1,2,3 Liquica	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going		
							Actual																															On-going	
	4	MEJD PKRIE EPE Loidahar	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going	
Maubara (MBR)	1	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Pagamentu Seidauk 100%		
							Actual																																
	2	MEJD PKRIE EBF Gariana	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going		
							Actual																																
Bazartete (BZT)	3	MEJD PKRIE EBF 1,2 Tapo Manuhulu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going		
							Actual																																
	4	MEJD PKRIE ESG-Paralelo Maubara	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going		
							Actual																																
	1	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													FHO			
							Actual																																
	2	Konstrusaun Moralha Foun Matadouro Tibar	Manoko Unip. Lda.	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																													Paradu			
							Actual																																
	3	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip. Lda.	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													Paradu			
							Actual																																
	4	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unip. Lda.	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														Pagamentu Seidauk 100%		
							Actual																																
	5	New Water Supply of Bairos PNTL Liquica	Holuli Unip. Lda.	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																														FHO		
							Actual																																
	6	Konstrusaun Armean Foun Matadouro (Bem Servisu)	Naesalobu Unip. Lda.	MAP-PO2019:19532	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																														FHO		
						Actual																																	
7	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Qeson SQ Unip. Lda.	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																														Pagamentu Seidauk 100%			
						Actual																																	
8	New construction of isolation for covid 19 in chi liquica, Timor Leste	Senizu Unip. Lda.	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																														PHO			
						Actual																																	
9	New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta	Biamali Unip. Lda.	RDTL-MS-C19-DNA-DC-21-233	LM	MINISTERIO SAUDE	Plan																														On-going			
						Actual																																	
10	Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica	Zyc Unip. Lda.	RDTL-MS-C19-DNA-DC-21-228	LM	MINISTERIO SAUDE	Plan																														On-going			
						Actual																																	
11	Projeitu Konstrusaun Foun ESTV Leorema - Liquica	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
12	MEJD PKRIE EPE Baura	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
13	MEJD PKRIE EPE Ermeta	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
14	MEJD PKRIE EPE Cassait	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
15	MEJD PKRIE ESG-Paralelo Bogoro	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going			
						Actual																																	
TOTAL PROJETO ON-GOING			26																																	</			

Note: Plano Periode inspesaun iha tereinu Relatorio avaliasuan mensal iha Dili Inspesaun Pagamentu Anual iha Implementasaun Plano Periode inspesaun iha tereinu

Prepara Husi :

 (Eng. Juninho António Abrantes da Cruz)
 Eng. ba Edificio Publico Agua e Saneamento Municipio
 Liquica ADN, I.P

Sertifika Husi :

 (Eng. Emerenciana da Costa Maia Freitas)
 Coordenador da Unidade de Controlo e Validasaun de Qualidade
 ADN.I.P

Aprova Husi :

 (Eng. Januario Maia Guterres)
 Adjunto Director Executivo ADN.I.P

								PLANU INSPESAUN																															
Naran Eng. Camillo de Jesus								2022																															
Município MUNICIPIO LIQUICA NO POSTOS																																							
Município / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	OUTUBRO																															OBS
								Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo								
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
Liquica Vila (LV)	7	New Installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																Pagamentu
	8	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	Busa Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	11	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	PDIM	ESTATAL	Plan																																
							Actual																																Atende Pagamentu
	12	Konstrusaun ka Reabilitasaun ba EPE Baura	EJD PKRIE EPE BAURA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	13	Konstrusaun ka Reabililasaun ba EPE Ermeta	MEJD PKRIE EPE ERMETA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	14	Konstrusaun ka Reabililasaun ba EPE Cassait	MEJD PKRIE EPE CASSAIT		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	15	Konstrusaun ka Reabililasaun ba EBF Gariana	MEJD PKRIE EBF GARIANA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
Maubara (MBR)	2	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	Britas Unip, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																Atende Pagamentu
	5	Novo Konstrusaun Edificio ESTV Lisadila	Aleni Unip, Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	6	Konstrusaun ka Reabililasaun ba EBF Mauboque	MEJD PKRIE EBF MAUBOQUE		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	7	Konstrusaun ka Reabililasaun ba EBC 1.2.3 Liquica	MEJD PKRIE EBC 1.2.3 LIQUIÇA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	8	Konstrusaun ka Reabililasaun ba EBF Tapo Manuhulu	MEJD PKRIE EBF 1.2 TAPO MANUHULU		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	9	Konstrusaun ka Reabililasaun ba EPE Loidahar	MEJD PKRIE EPE LOIDAHAR		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	10	Konstrusaun ka Reabililasaun ba EBF 1.2 Laclema	MEJD PKRIE EBF 1.2 LACLOLEMA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	11	Konstrusaun ka Reabililasaun ba EBF 1.2 Tolema	MEJD PKRIE EBF 1.2 TOLEMA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	12	Konstrusaun ka Reabililasaun ba ESG-Paralelo Maubara/Batuvou	MEJD PKRIE ESG-PARALELO MAUBARA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	13	Konstrusaun ka Reabililasaun ba ESG-Paralelo Bogoro	MEJD PKRIE ESG-PARALELO BOGORO		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu
	14	Konstrusaun ka Reabililasaun ba EBF 1.2 Luculai	MEJD PKRIE EBF 1.2 LUCULAI		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Atende Pagamentu



