



REPÚBLIKA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO
Agência de Desenvolvimento Nacional, Instituto Público



RELATORIU MENSAL
IMPLEMENTASAUN
PROJETUS MUNISIPIU LAUTEM
OUTUBRO 2021



SUMÁRIO

RELATÓRIO


IMPLEMENTAÇÃO DO PROJETO INFRAESTRUTURA IHA MUNICÍPIO LAUTEM

OUTUBRO 2021


Prepara Husi :




(Eng. Inocencio dos Reis Costa Maia)
Eng. ba Porjecto Edificio Publico Beé no
Saneamento Municipio Lautem, ADN, I.P



(Eng. Geovanto M.X.C Aleixo)
Eng. ba Projeto Infraestrutura e
Irigação Municipio Lautem, ADN, I.P




(Eng. Adonis Julio Fernandes)
Eng. ba Projeto ME ADN, I.P




(Eng. Deamantino Henrique Lopes)
Eng. ba Projeto Infraestrutura e
Irigação Municipio Lautem, ADN, I.P

Verifica Husi :



(Arc. Francisco X D D Jeronimo)
Eng. Senior ba Edificio Publico no Beé
Saneamento, ADN, I.P




(Eng. Aniceto da Costa)
Eng. Senior ba Projeto Infraestrutura e
Irigação, ADN, I.P




(Eng. Deolindo de F. Marques)
Chefe Seksaun ba Projeto M.E & ITC, ADN,

Sertifica Husi :



(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de
Qualidade, ADN, I.P

Aprova Husi :



(Mariano Renato Monteiro da Cruz, S. T. M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO.....	1
INDICE	1
I. INTRODUSAUN	2
1.1 Enkuadramentu Legal.....	2
1.2 Perfil Municipio Lautem	2
1.3. Lista Projectos.....	8
II. PROGRESU FISIKU.....	23
2.1 Progreso Fisiku Kada Fulan	23
III. OBSTÁCLO IHA TERENU	24
3.1 Obstáculo Servisu Iha Terenu	24
IV. REKOMENDASAUN IHA TERENU	25
4.1 Rekomendasaun Servisu Iha Terenu	25

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias	4
Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Lautem.....	6
Tabela 1.2 : Lista Asset ADN,I.P Municipio Lautem	6
Tabela 1.3.1 : Projecto Municipio Lautem Por Fundus Finansiamentos	8
Tabela 1.3.2 : Projecto Municipio Lautem Por Sectores.....	11
Tabela 1.3.3 : Projecto Municipio Lautem Por Ministerio.....	17
Tabela 1.4 : Dadus Populasaun Munisipiu Lautem	23

I. INTRODUSAUN

1.1. Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Dekretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekretu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho qualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefísiu ne'ebe razoável no viável.

Depois de Dekretu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizasaun no sertifikasaun qualidade ba projetu sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2. Perfil Municipio Lautem



Mapa hatudu pozisaun jeográfika Administrasaun Munisipal Lautem iha luan 1.702 km2 ho populasau 59.787 tuir Sensus 2010. Tabela 1 hatudu Administrasaun Munisipal Lautem iha Posto Administrativo 5 , Sukus 34 no aldeias 151.

Tabela 1 : Postos Administrativos,Sucos no Aldeias.

Iliomar		Lautém		Lospalos	
Sukus	Aldeias	Sukus	Aldeias	Sukus	Aldeias
Ailebere	4	Baduro	5	Bauro	5
Caenilo	5	Com	6	Cacavei	4
fuat	3	Daudare	8	Fuiloru	11
Iliomar I	5	Euquisi	3	Home	4
Iliomar II	5	lilali	2	Leuro	4
-	3	Maina I	5	Loré I	6
-	3	Maina II	5	Loré II	3
-	-	Pairara	4	Muapiti ne	5
-	-	Parlamento	5	raça	3
-	-	serelau	3	Souro	7
-	-	-	-	-	-
-	-	-	-	-	-
Total	28	-	46	-	52

Data husi: Livro 3 B OJE 2021, pag 58

Luro		Tutuala	
Sukus	Aldeias	sukus	Aldeias
afabubu	2	Mehara	3
Baricafa	3	Tutuala	4
Cotamutu	3	-	
Lacawa	3	-	
Luro	5	-	
Vairoque	5	-	
-	-	-	
-	-	-	
-	-	-	
-	-	-	
-	-	-	
-	-	-	
-	21	-	7

Tabela 1.1: Força de Trabalho ADN, I.P Municipio Lautem.

Força de Trabalho ADN,I.P Municipio Lautem/ Lospalos								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	3					3	
2	Administrasaun no Financas	0					0	
3	Motorista	1					1	
4	Seguransa	0					0	
Total		4					4	

Tabela 1.2 : Lista Asset ADN,I.P Municipio Lautem

ASET ADN,IP MUNICIPIO LAUTEM								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1						
2	Kareta	1						
3	Desktop HP / Monitor	1						
4	Laptop HP	1						
5	Printer Cannon	1						
6	UPS	1						
7	Armario File	2						
8	Armario Tau hena	3						
9	Meja escritorio	1						
10	Meja han	1						

11	Meja TV (kiik)	1						
12	Kadeira escritorio	6						
13	Kadeira han	4						
14	Sofa	1 Set						
15	Springbed +sumasu 4+sprei 3	3 Set						
16	Jeleira	1						
17	Water Dispenser	1						
18	TV + Parabola	1 Set						
19	Kipas Angin	4						
20	Kompor	0						
21	Kompor Gas	1						
22	Rack sepatu	2						
23	Rack Piring	1						
24	Water Pump Sanyo	1						

1.3 : Lista Projectos

Projetu hotu ne'ebe akumulula iha lista ne'e bazeia ba dadus projetu ne'ebe sei lao hela no mos projetu ne'ebe abandona ona tinan barak, projetu hirak ne'e fahe tuir lista 1.3.1 Projeto Por Fundus Finansiamento, 1.3.2 Projeto Por Sector no 1.3.3 Projeto Por Ministerio

1.3.1 : Lista Proyecto Municipio Lautem Por Fundus Finansiamento

NO	POSTO ADMINISTRATIVO	TOTAL FI+Fundo Covid-19+LM-BS+LM-CD+PDIM		
		TOTAL PROJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	Iliomar	3	\$ 685,801.30	76.53%
2	Lautem	6	\$ 12,202,220.98	55.30%
3	Loru	7	\$ 10,357,184.53	87.81%
4	Lospalos	19	\$ 9,027,779.77	45.62%
5	Tutuala	2	\$ 6,113,033.23	21.76%
	Grand Total	37	\$ 38,386,019.81	56.83%

NO	POSTO ADMINISTRATIVO	FI		
		TOTAL PROJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	Iliomar	2	\$ 496,832.66	72.51%
2	Lautem	3	\$ 11,851,338.35	55.99%
3	Loru	3	\$ 9,750,745.44	92.23%
4	Lospalos	4	\$ 4,693,761.44	47.12%
5	Tutuala	2	\$ 6,113,033.23	21.76%
	Grand Total	14	\$ 32,905,711.12	59.35%

NO	POSTO ADMINISTRATIVO	Fundo Covid-19		
		TOTAL PROJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	Iliomar		\$ -	0.00%
2	Lautem		\$ -	0.00%
3	Loru		\$ -	0.00%
4	Lospalos	2	\$ 373,420.03	45.84%
5	Tutuala		\$ -	0.00%
Grand Total		2	\$ 373,420.03	45.84%

NO	POSTO ADMINISTRATIVO	LM-BS		
		TOTAL PROJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	Iliomar		\$ -	0.00%
2	Lautem	1	\$ 85,584.79	82.58%
3	Loru		\$ -	0.00%
4	Lospalos	5	\$ 1,017,957.22	46.27%
5	Tutuala		\$ -	0.00%
Grand Total		6	\$ 1,103,542.01	49.09%

NO	POSTO ADMINISTRATIVO	LM-CD		
		TOTAL PROJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	Iliomar		\$ -	0.00%
2	Lautem	2	\$ 265,297.84	15.67%
3	Loru	4	\$ 606,439.09	16.73%
4	Lospalos	6	\$ 2,545,302.23	49.70%
5	Tutuala		\$ -	0.00%
	Grand Total	12	\$ 3,417,039.16	41.20%

NO	POSTO ADMINISTRATIVO	PDIM		
		TOTAL PROJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	Iliomar	1	\$ 188,968.64	87.09%
2	Lautem		\$ -	0.00%
3	Loru		\$ -	0.00%
4	Lospalos	2	\$ 397,338.85	0.00%
5	Tutuala		\$ -	0.00%
	Grand Total	3	\$ 586,307.49	28.07%

1.3.2 : Lista Projecto Municipio Laudem Por Sector

NO	POR SECTOR	TOTAL MUNICIPIO LAUTEM		
		TOTAL PORJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO	3	\$ 815,564.95	35.07%
2	EDIFICIOS PUBLICOS	5	\$ 1,953,118.89	37.61%
3	EDUKASAUN	1	\$ 66,333.92	86.14%
4	ELETRIFIKASAUN NASIONAL	2	\$ 1,026,193.79	69.98%
5	ESTRADAS	18	\$ 32,857,515.82	57.89%
6	MANUTENSAUN NO REHABILITASAUN	3	\$ 601,385.25	38.04%
7	SAUDE	3	\$ 562,388.67	59.70%
8	SOLIDARIEDADE E SOCIAL	1	\$ 417,933.73	86.66%
9	TURISMO	1	\$ 85,584.79	82.58%
	Grand Total	37	\$ 38,386,019.81	56.83%

NO	POR SECTOR	Iliomar		
		TOTAL PORJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO		\$ -	0.00%
2	EDIFICIOS PUBLICOS		\$ -	0.00%
3	EDUKASAUN		\$ -	0.00%
4	ELETRIFIKASAUN NASIONAL	1	\$ 432,643.32	72.00%
5	ESTRADAS	1	\$ 64,189.34	75.98%
6	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
7	SAUDE	1	\$ 188,968.64	87.09%
8	SOLIDARIEDADE E SOCIAL		\$ -	0.00%
9	TURISMO		\$ -	0.00%
	Grand Total	3	\$ 685,801.30	76.53%

NO	POR SECTOR	Lautem		
		TOTAL PORJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO		\$ -	0.00%
2	EDIFICIOS PUBLICOS		\$ -	0.00%
3	EDUKASAUN		\$ -	0.00%
4	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
5	ESTRADAS	5	\$ 12,116,636.19	55.11%
6	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
7	SAUDE		\$ -	0.00%
8	SOLIDARIEDADE E SOCIAL		\$ -	0.00%
9	TURISMO	1	\$ 85,584.79	82.58%
	Grand Total	6	\$ 12,202,220.98	55.30%

NO	POR SECTOR	Loru		
		TOTAL PORJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO		\$ -	0.00%
2	EDIFICIOS PUBLICOS		\$ -	0.00%
3	EDUKASAUN		\$ -	0.00%
4	ELETRIFIKASAUN NASIONAL	1	\$ 593,550.47	68.51%
5	ESTRADAS	6	\$ 9,763,634.06	88.98%
6	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
7	SAUDE		\$ -	0.00%
8	SOLIDARIEDADE E SOCIAL		\$ -	0.00%
9	TURISMO		\$ -	0.00%
	Grand Total	7	\$ 10,357,184.53	87.81%

NO	POR SECTOR	Lospalos		
		TOTAL PORJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO	3	\$ 815,564.95	35.07%
2	EDIFICIOS PUBLICOS	5	\$ 1,953,118.89	37.61%
3	EDUKASAUN	1	\$ 66,333.92	86.14%
4	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
5	ESTRADAS	4	\$ 4,800,023.00	47.47%
6	MANUTENSAUN NO REHABILITASAUN	3	\$ 601,385.25	38.04%
7	SAUDE	2	\$ 373,420.03	45.84%
8	SOLIDARIEDADE E SOCIAL	1	\$ 417,933.73	86.66%
9	TURISMO		\$ -	0.00%
	Grand Total	19	\$ 9,027,779.77	45.62%

NO	POR SECTOR	Tutuala		
		TOTAL PORJEITO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	AGUA E SANEAMENTO		\$ -	0.00%
2	EDIFICIOS PUBLICOS		\$ -	0.00%
3	EDUKASAUN		\$ -	0.00%
4	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
5	ESTRADAS	2	\$ 6,113,033.23	21.76%
6	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
7	SAUDE		\$ -	0.00%
8	SOLIDARIEDADE E SOCIAL		\$ -	0.00%
9	TURISMO		\$ -	0.00%
	Grand Total	2	\$ 6,113,033.23	21.76%

1.3.3 : Lista Projecto Municipiu Lautem Por Ministerio

NO	POR MINISTERIO	GRAND TOTAL		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	ESTATAL	2	\$ 397,338.85	0.00%
2	MINISTERIO DAS OBRAS PUBLICAS	26	\$ 35,300,659.81	57.38%
3	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 66,333.92	86.14%
4	MINISTERIO FINANCAS	1	\$ 56,783.85	80.85%
5	MINISTERIO PLANU E ORDENAMENTU	1	\$ 788,921.55	49.09%
6	MINISTERIO SAUDE	3	\$ 562,388.67	59.70%
7	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	1	\$ 417,933.73	86.66%
8	PROCURADORIA GERAL DA REPUBLIKA	1	\$ 710,074.64	42.44%
9	SEFOPE	1	\$ 85,584.79	82.58%
	Grand Total	37	\$ 38,386,019.81	56.83%

NO	POR MINISTERIO	Iliomar		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO DAS OBRAS PUBLICAS	2	\$ 496,832.66	72.51%
3	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		\$ -	0.00%
4	MINISTERIO FINANÇAS		\$ -	0.00%
5	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
6	MINISTERIO SAUDE	1	\$ 188,968.64	87.09%
7	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN		\$ -	0.00%
8	PROCURADORIA GERAL DA REPUBLICA		\$ -	0.00%
9	SEFOPE		\$ -	0.00%
Grand Total		3	\$ 685,801.30	76.53%

NO	POR MINISTERIO	Lautem		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO DAS OBRAS PUBLICAS	5	\$ 12,116,636.19	55.11%
3	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		\$ -	0.00%
4	MINISTERIO FINANÇAS		\$ -	0.00%
5	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
6	MINISTERIO SAUDE		\$ -	0.00%
7	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN		\$ -	0.00%
8	PROCURADORIA GERAL DA REPUBLICA		\$ -	0.00%
9	SEFOPE	1	\$ 85,584.79	82.58%
	Grand Total	6	\$ 12,202,220.98	55.30%

NO	POR MINISTERIO	Loru		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO DAS OBRAS PUBLICAS	7	\$ 10,357,184.53	87.81%
3	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		\$ -	0.00%
4	MINISTERIO FINANÇAS		\$ -	0.00%
5	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
6	MINISTERIO SAUDE		\$ -	0.00%
7	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN		\$ -	0.00%
8	PROCURADORIA GERAL DA REPUBLICA		\$ -	0.00%
9	SEFOPE		\$ -	0.00%
	Grand Total	7	\$ 10,357,184.53	87.81%

NO	POR MINISTERIO	Lospalos		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	ESTATAL	2	\$ 397,338.85	0.00%
2	MINISTERIO DAS OBRAS PUBLICAS	10	\$ 6,216,973.20	44.94%
3	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 66,333.92	86.14%
4	MINISTERIO FINANÇAS	1	\$ 56,783.85	80.85%
5	MINISTERIO PLANU E ORDENAMENTU	1	\$ 788,921.55	49.09%
6	MINISTERIO SAUDE	2	\$ 373,420.03	45.84%
7	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	1	\$ 417,933.73	86.66%
8	PROCURADORIA GERAL DA REPUBLICA	1	\$ 710,074.64	42.44%
9	SEFOPE		\$ -	0.00%
Grand Total		19	\$ 9,027,779.77	45.62%

NO	POR MINISTERIO	Tutuala		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAGEM EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO DAS OBRAS PUBLICAS	2	\$ 6,113,033.23	21.76%
3	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		\$ -	0.00%
4	MINISTERIO FINANCAS		\$ -	0.00%
5	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
6	MINISTERIO SAUDE		\$ -	0.00%
7	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN		\$ -	0.00%
8	PROCURADORIA GERAL DA REPUBLIKA		\$ -	0.00%
9	SEFOPE		\$ -	0.00%
	Grand Total	2	\$ 6,113,033.23	21.76%

Tabela 1.4 : Dadus Populasaun Munisipiu Lautem

Posto Administrativo, Suco no Sexu	2021			
	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
	Male	Female	Male	Female
Iliomar	1,679	1,952	1,861	1,945
Lautém	4,308	4,562	3,768	3,729
Lospalos	8,949	9,552	6,942	6,865
Luro	1,960	1,919	1,705	1,678
Tutuala	902	1,000	834	827

Fontes : Projeksaun Populasaun bazeia ba Sensus Populasaun no Umakain 2015,

Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan nia laran, husi lista #anexu B hatudu progresu aktual fulan ida ne'e ho nia prensentagen servisu, montante aktual bazeia ba orsamento ne'ebe hetan husi progresu fulan ida ne'e, ikus liu prentangen aktual fulan ida ne'e hatudu progresu fisiku komulativu husi prosentu antrior no fulan ida ne'e nian, lista kompletu ba detallu bele hare iha #anexu B, detallu ba back-up #anexu C, no Instrusaun Servisu #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

Durante ami nia monitorizasaun ba projecto hotu nebe mak lokaliza iha Munisipio Lautem, ami hasoru obstáclu sira hanesan tuir mai ne'e :

- Rekursu umanu seidauk sufisien (enginheiro,driver,administrasaun).
- Mina La Suficiente
- Ba projecto sira nebe'e ho distancia do'ok no kondisaun estrada mos la dun diak (a'at), hanesan posto administrativo Luro no Iliomar, deficit mai ami atu halo monitorizasaun kada fulan dala tolu ou ha'at
- Ekipamentus apoio servisu sei avaria (Komputador no Laptop).
- Sistema rekolhamentu dados inspeksaun no folder system balun sei dupla hela.
- Kapasidade folder system la to'o atu guarda/save dados inspeksaun tomak ne'ebe barak.
- Kompanhia barak mak servisu la tuir tempo kontratu nebe'e mak iha
- Rekursu umanu ou engenheiro companhia nian la suficiente
- Projeito balun nebe'e mak abandona ou parrado iha tinan barak nia laran

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

Bazeia ba obstákulu ne'ebe iha leten maka ami rekomenda atu :

- Presija aumenta tan rekursu umanu atu bele aselera no fasilita prosesu servisu tomak iha Munisipio.
- Presija Aumenta tan Kupon Mina ba Kareta
- Husu mos ba Superior ADN,I.P atu tolera mos ami hodi halo monitorizasaun ba projeto nebe mak lokaliza iha posto administrativo Luro no Iliomar, se bele kada fulan maksimal dala rua tanba hare ba nia distancia nebe'e mak do'ok no kondisaun Estrada mos a'at
- Presija hadia ka troka ekipamentu apoio servisu ninian hanesan Komputador no Laptop, tamba dala barak sempre avaria/error bainhira ita uja hodi halo servisu.
- Sistema Rekolhamentu dados inspeksaun ninian sei dupla hela, liu liu hanesan site instruction format ne'ebe iha rua (ida ita terrenu no ida fali iha sistema laran).
- Presija minimiza ka halo rezumu ba rekolhamentu dados folder system ne'ebe dupla.
- Presija aumenta tan kapasidade/memory folder system nian halo boot, atu nune'e be'e akumula dados inspeksaun sira hotu ne'ebe iha.
- Husu mos ba Superior A D N I.P atu se bele koordena ho projeito nain sira hodi fo sansaun ka penalidade ba kompanhia sira nebe mak servico atraza ou abandona servico hodi han tempo to'o tinan 2 ba leten

Note: Asinatura Husi Eng. Municipio Lautem

Força de Trabalho ADN,I.P Municipio Lautem						
No	Deskrisaun	Identidade				Asinatura
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	
1	Enjineiru	Inocencio dos Reis Costa Maia	208	Enjineiru EPAS		
		Geovanio M. X. Carlos Aleixo	164	Enjineiru ITI		
		Deamantino Henrique Lopes	213	Enjineiru ITI		

		Adonis Julio Fernandes	152	Enjineiru ME		
2	Enjineira	Olivia Soares	112	Enjineira VEBD		
3	Motorista	Delio Abel Manuel Ferreira	159	Motorista		

#ANEXU C1 (LA-3) Back-up Data

Naran Projeto : **Rural Roads Periodic Maintenance Dasidara Lequidiga 0+000 - 10+000**
Chainage Municipality Lautem (162)
No. kontratu : RDTMPW-W-RTQ-190038

Data Inspesaun : 25/10/2021

Fatin Inspesaun : Dasidara-Lequidiga

Koordinadas :

Start Point : Long : 126.728656, Latetude : 8.413286

End Point : Long : 126.748822, Latetude : 8.476845

Naran Inspector : **1. Geovanio M. X. C. Aleixo**

2. Deamantino Henrique Lopes

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu



ON GOING Maibe servisu iha terreno ba fulan
Outubro laiha.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu

#ANEXU C1 (LA-3) Back-up Data

Naran Projeto : Rural Roads Periodic Maintenance Dasidara Lequidiga 0+000 - 10+000
Chainage Municipality Lautem (162)
No. kontratu : RDTMPW-W-RTQ-190038

ON GOING Maibe serviso iha terreno ba fulan
Outubro laiha.



#ANEXU C1 (LA-2) Back-up Data

Naran Projeto : **Rehabilitation Roads Maina 1 to parlamento 3.916 km**
No. kontratu : **SSS/100/MOPTC-2017**

Data Inspesaun : 29/10/2021

Fatin Inspesaun : Maina I to Parlamento

Koordinadas :

Start Point : Long : 126.9186733, Latetude : 8.351191667

End Point : Long : 126.9239417, Latetude : 8.378418333


Naran Inspector : **1. Geovanio M.X.C. Aleixo**

2. Deamantino Henrique Lopes

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

ON GOING maibe actividade iha terreno ba
fulan Outubro laiha

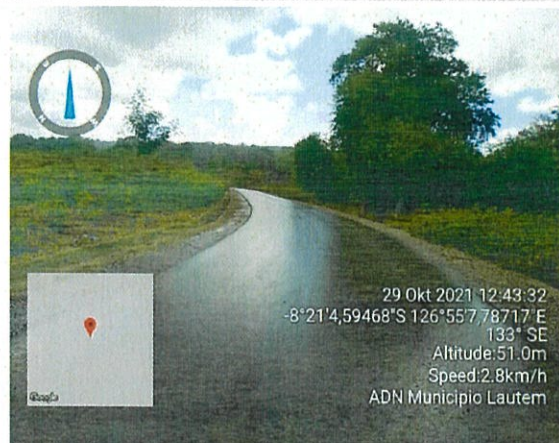

Sketch & Foto Desenho


Observasaun iha tereno no Foto Aktual



#ANEXU C1 (LA-2) Back-up Data

Naran Projeto : **Rehabilitation Roads Maina 1 to parlamento 3.916 km**
No. kontratu : **SSS/100/MOPTC-2017**

ON GOING maibe actividade iha terreno
ba fulan Outubro laiha

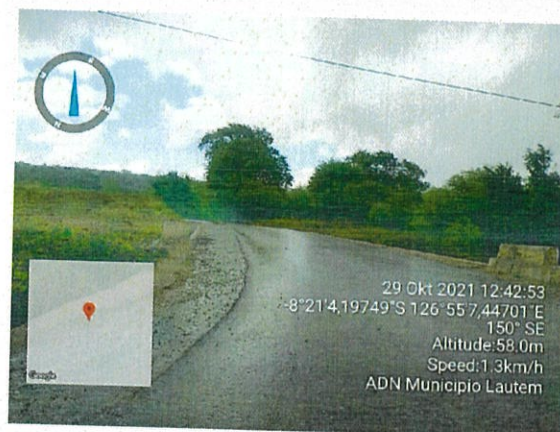



#ANEXU C1 (LA-5) Back-up Data

Naran Projeto : Rehabilitation of Road Jct. Assalaino to Com, Road Section : Jct. Assalaino
to Caicavamoko Sta. 8+000 - 15+200 Lautem Municipality
No. kontratu : SSS/144/MOPTC-2017

Data Inspesaun : 29/10/2021

Fatin Inspesaun : Assalaino to Caicavamoko

Koordinadas :

Start Point : Long : 127.014768, Latetude : 8.380344

End Point : Long : 127.056664, Latetude : 8.355725


Naran Inspector : 1. Geovanio M.X.Carlos Aleixo

2. Deamantino Henrique Lopes

Sketch & Foto Desenho

ON GOING

Observasaun iha tereno no Foto Aktual

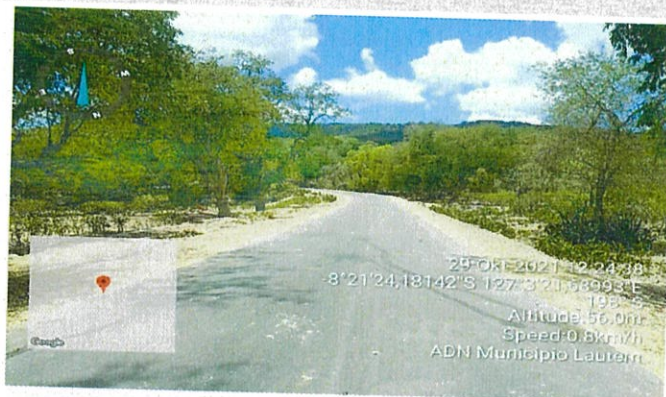




#ANEXU C1 (LA-5) Back-up Data

Naran Projeto : Rehabilitation of Road Jct. Assalaino to Com, Road Section : Jct. Assalaino
to Caicavamoko Sta. 8+000 - 15+200 Lautem Municipality
No. kontratu : SSS/144/MOPTC-2017

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

ON GOING

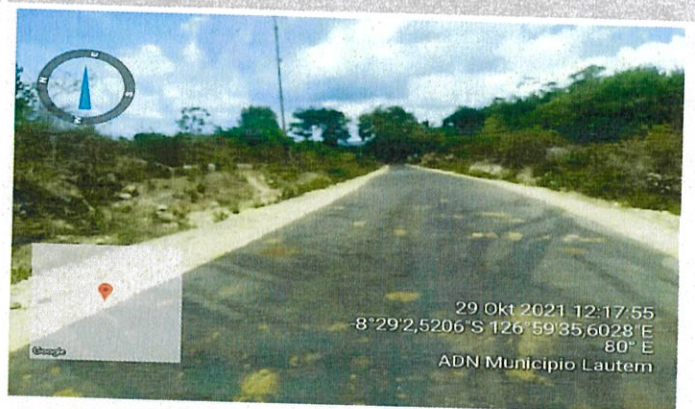

#ANEXU C1 (LO-2)

Back-up Data

Naran Projeto : **Konstrusaun Edifício PGR Municipio Lautem**

No. kontratu : **RDTL-D.FeO/APRO/PGR/19.001/2019**

Data Inspesaun : 29/10/2021

Fatin Inspesaun : Lospalos-Vila

Koordinadas :

Start Point : Long : -8.2946073 Latetude : 126.5929706.

End Point : Long : , Latetude :

Naran Inspector : **1. Inocencio dos Reis Costa Maia**

2.

3.

4.

Sketch & Foto Desenho

Sketch Item servisu

.....

Observasaun iha tereno no Foto Aktual

Progressu servisu ba projeitu
refere iha fulan Outubro nia
laran ne'e maka, servisu
kalkuluk kuaje atu remata
ona, no tuir mai sei tama ba
servisu rangka plafond
ninian.





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL




ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (LO-2)

Back-up Data

Naran Projeto : Konstrusaun Edifício PGR Municipio Lautem
No. kontratu : RDTL-D.FeO/APRO/PGR/19.001/2019

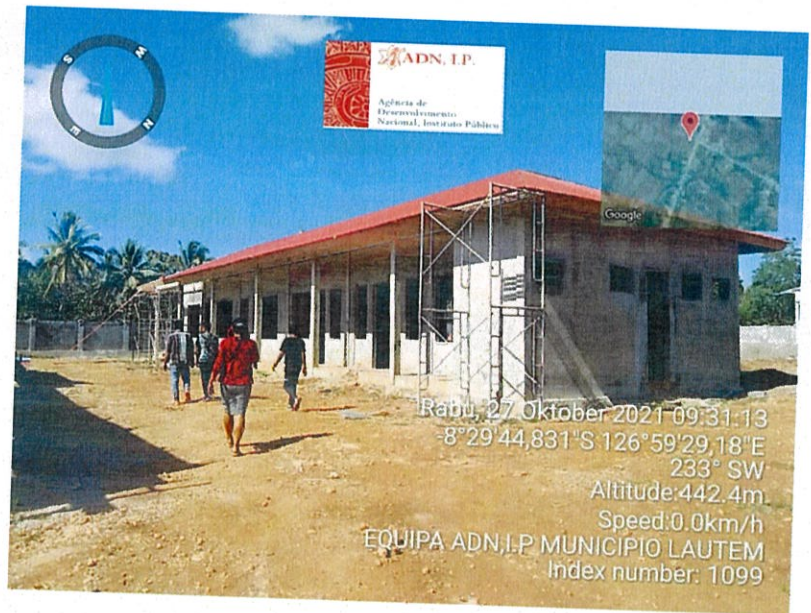

Sketch & Foto Desenho

Sketch Item servisu

.....

Observasaun iha tereno no Foto Aktual



#ANEXU C1 (LO-2)

Back-up Data

Naran Projeto : Konstrusaun Edifício PGR Municipio Lautem
No. kontratu : RDTL-D.FeO/APRO/PGR/19.001/2019



Sketch & Foto Desenho

Sketch Item servisu

.....

Observasaun iha tereno no Foto Aktual





#ANEXU C1 (TU-2) Back-up Data

Naran Projeto : Rehabilitation Road Section : Jct. Tutuala Roads (C2) Package 1 Sta.
3+850 - 7+725 Municipality Lautem
No. kontratu : SSS/083/MOPTC-2017

Data Inspesaun : 12/10/2021

Fatin Inspesaun : Tutuala - Valu

Koordinadas :

Start Point : Long : 127.2821183, Latetude : 8.400788

End Point : Long : 127.2998483, Latetude : 8.412501


Naran Inspector : 1. Geovanio M.X.Carlos Aleixo

2. Deamantino Henrique Lopes

Sketch & Foto Desenho

Servisu ba Item Prime Coat (L/S)

STA. 3 + 850 – 7 + 700 M




Panjang Prime Coat = 3850 m

Lebar Prime Coat = 2.50 m

Area Prime Coat = 3850 m x 2.50 m

= 9625 m²

Observasaun iha tereno no Foto Aktual

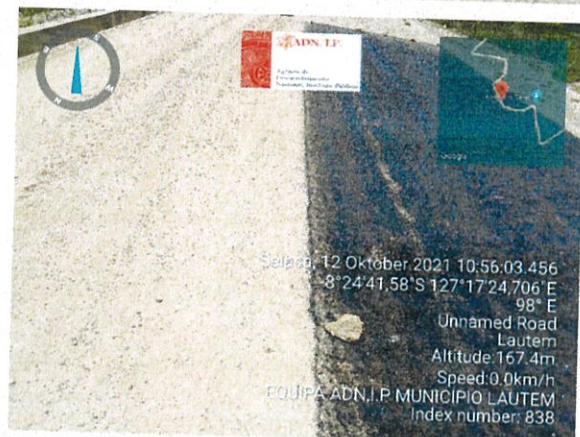


#ANEXU C1 (TU-2) Back-up Data

Naran Projeto : Rehabilitation Road Section : Jct. Tutuala Roads (C2) Package 1 Sta.
3+850 - 7+725 Municipality Lautem
No. kontratu : SSS/083/MOPTC-2017

Sketch & Foto Desenho

Servisu ba Item Prime Coat (L/S)

STA. 3 + 850 – 7 + 700 M




Panjang Prime Coat = 3850 m

Lebar Prime Coat = 2.50 m

Area Prime Coat = 3850 m x 2.50 m
= 9625 m²

Observasaun iha tereno no Foto Aktual





#ANEXU C1 (TU-2) Back-up Data

Naran Projeto : Rehabilitation Road Section : Jct. Tutuala Roads (C2) Package 1 Sta.
3+850 - 7+725 Municipality Lautem
No. kontratu : SSS/083/MOPTC-2017

Data Inspesaun : 29/10/2021

Fatin Inspesaun : Tutuala - Valu

Koordinadas :

Start Point : Long : 127.2821183, Latetude : 8.400788


End Point : Long : 127.2998483, Latetude : 8.412501

Naran Inspector : 1. Geovanio M.X.Carlos Aleixo
2. Deamantino Henrique Lopes

Sketch & Foto Desenho

Servisu ba Item Prime Coat (R/S)

STA. 3 + 850 – 7 + 700 M




Panjang Prime Coat = 3850 m

Lebar Prime Coat = 2.50 m

Area Prime Coat = 3850 m x 2.50 m
= 9625 m²

Observasaun iha tereno no Foto Aktual

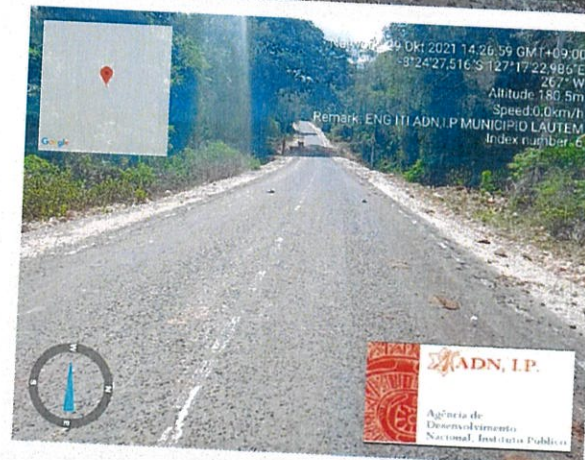


#ANEXU C1 (TU-2) Back-up Data

Naran Projeto : **Rehabilitation Road Section : Jct. Tutuala Roads (C2) Package 1 Sta.
3+850 - 7+725 Municipality Lautem**
No. kontratu : **SSS/083/MOPTC-2017**

Sketch & Foto Desenho

Servisu ba Item Prime Coat (R/S)

STA. 3 +850 – 7 + 700 M



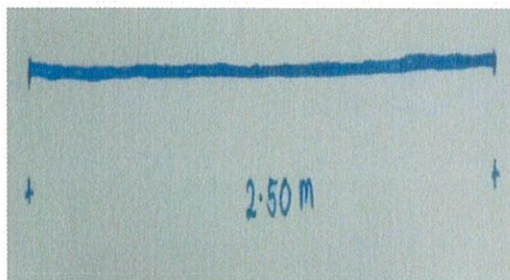


Panjang Prime Coat = 3850 m

Lebar Prime Coat = 2.50 m

Area Prime Coat = 3850 m x 2.50 m
= **9625 m²**

Observasaun iha tereno no Foto Aktual

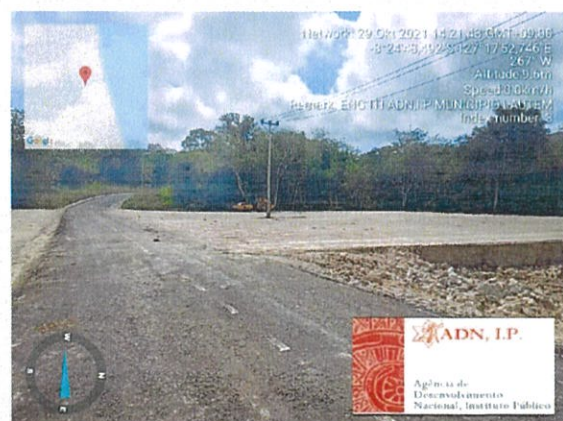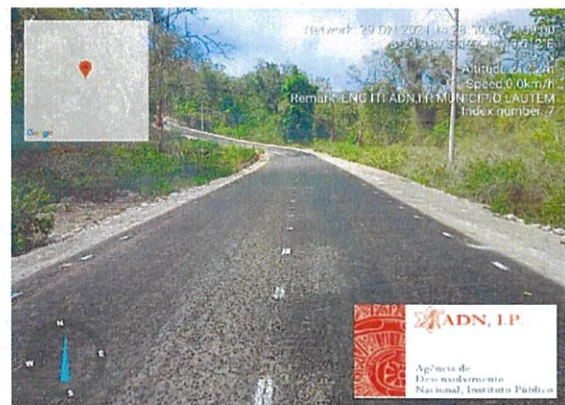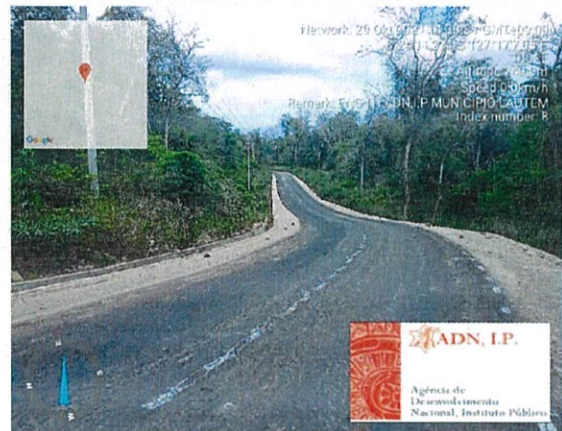



#ANEXU A (LISTA GERAL LAUTEM)

Localizaçao Projeto															
NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	NARAN KONT.	MONT. KONT. (\$)	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	STATUS PROJECTO	OBS
1	Rehabilitation of Laleno Road Project Road Section (Sta. 0+000 - 6+210) Maina 2 in Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lautem	Lautem	Corcorcio Irloyvon, Lda	SSS/117/MOPTC-2016	\$ 4,782,693.68	48.98%	48.98%	\$ 2,342,395.66	\$ 2,440,298.02	ON-GOING	
2	Rehabilitation Roads Maina 1 to parlamento 3.916 km	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lautem	Lautem	Samudra Unip, Lda	SSS/100/MOPTC-2017	\$ 3,039,825.77	71.77%	71.77%	\$ 2,181,690.18	\$ 858,135.59	ON-GOING	
3	Rural Roads Periodic Maintenance Dasidara Lequidiga 0+000 - 10+000 Chainage Municipality Lautem (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lautem	Lautem	Franam Lindo Unip. Lda	MPW-W-RTQ-190038	\$ 84,077.42	49.46%	49.46%	\$ 41,581.46	\$ 42,495.96	ON-GOING	
4	Projectu Konstrusaun Turismu Komunitariu iha COM, Postu Administrativu Lautem	SEFOPE	LM-BS	TURISMO	Lautem	Lautem	Joli Toni Unip Lda	17/CNEFP?XI/2016	\$ 85,584.79	82.58%	82.58%	\$ 70,676.00	\$ 14,908.79	PENDENTE	
5	Rehabilitation of Road Jct. Assalaino to Com, Road Section : Jct. Assalaino to Caicavamoko Sta. 8+000 - 15+200 Lautem Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lautem	Lautem	Fian Const. Unip. Lda	SSS/144/MOPTC-2017	\$ 4,028,818.90	52.41%	52.41%	\$ 2,111,320.44	\$ 1,917,498.46	ON-GOING	
6	R4D RURAL ROAD SPOT IMPROVEMENT DASIDARA - LIQUIDIGA CHAINAGE 0+000-10+500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lautem	Lautem	ILIE CHAO, UNIPESSOAL LDA	MPW - W - 210078	\$ 181,220.42	8.84% ✓	0.00%	\$ -	\$ 181,220.42	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro 8.84%
7	Konstrusaun Monumento Nino Konis Santana no Jardim iha Escola Secundaria Nino Konis Santana Publica LAUTEM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	EDUKASAUN	Lospalos	Lautem	Amor Construction	RDTL 2016	\$ 66,333.92	86.14%	86.14%	\$ 57,143.15	\$ 9,190.77	PENDENTE	
8	Konstrusaun Edificio PGR Municipio Lautem	PROCURADORIA GERAL DA REPUBLICA	LM-CD	EDIFICIOS PUBLICOS	Lospalos	Lautem	Cambota	RDTL-D.FeO/APRO/PGR/19.001/2019	\$ 710,074.64	52.80% ✓	42.44%	\$ 301,355.38	\$ 408,719.26	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 3.36%
9	Rural Road Rehabilitation Fuiloro - Home Chainage 1+200 - 2+500 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Lospalos	Lautem	Paiahara Unipessoal Lda	RT/033/MOP - 2019	\$ 287,376.91	39.02% ✓	30.83%	\$ 88,609.81	\$ 198,767.10	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 0.35%
10	New Construction of Laboratory for Covid 19 at Lautem, Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Lospalos	Lautem	Parapa Bemiziui Star Unipessoal Lda	RDTL-MS-DNA-RBK-20-189	\$ 88,631.06	82.09%	64.43%	\$ 57,104.00	\$ 31,527.06	ON-GOING	
11	Rehabilitation of Road Jct. Assalaino to Com, Road Section : Jct Assalaino to Caicavamoko Sta. 0+000 - 8+000 km municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lospalos	Lautem	Salve, Unip. Lda	SSS/143/MOPTC-2017	\$ 4,092,376.19	48.45%	48.45%	\$ 1,982,788.46	\$ 2,109,587.73	ON-GOING	
12	Routine Maintanance Lospalos - Souro Chainage 0+000 - 5+800, Routine Maintanance Leuro - Sorulua Chainage 0+000 - 3+000	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Lospalos	Lautem	Afabubo f. Unip Lda.	RFQ/222/MOPTC-2016	\$ 49,805.16	78.29%	78.29%	\$ 38,993.47	\$ 10,811.69	PENDENTE	
13	Road Maintenance Sections : Lospalos - Iliomar Section (A082 - 2) Municipality Lautem (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Lospalos	Lautem	Lero Company, Lda	MPW-W-190120	\$ 219,745.45	83.52.%	83.52%	\$ 183,526.66	\$ 36,218.79	PENDENTE	
14	Prefurasaun Sistema Be'e mos iha Suku PA'Papa Postu Adm. Lospalos Vila	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Lospalos	Lautem	Mai Moco	MPWTC-NCB-170007	\$ 140,470.95	72.34%	72.34%	\$ 101,622.87	\$ 38,848.08	PENDENTE	
15	Konstrusaun Edificio CDS Lospalos Inklui Armagem no pavimento	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	LM-CD	SOLIDARIEDADE E SOCIAL	Lospalos	Lautem	Delta Dini	RDTL 15/MSS/DNFALM-DAD/XII/2015	\$ 417,933.73	96.29%	86.66%	\$ 362,176.33	\$ 55,757.40	PENDENTE	

OK.

Cheti gelsaun sin gelsaun Assina



#ANEXU A (LISTA GERAL LAUTEM)

Localizasaun Projeto															
NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	NARAN KONT.	MONT. KONT. (\$)	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	STATUS PROJECTO	OBS
16	Konstrusaun no Instalasaun Sistema Be'e Mos iha Aldeia Homokanu, Foemaa, Nanakuru no EBF Soru Posto Administrativo Lospalos Vila, Municipio Lautem/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Lospalos	Lautem	Paza Conis Unip Lda	NCB-MOP-190063	\$ 255,685.00	25.15%	22.64%	\$ 57,875.81	\$ 197,809.19	PENDENTE	
17	Konstrusaun Be'e Mos Sistema Pompa no Gravitasaun,Tchay Titilary, Nuhalaria, Posto Administrativo Lospalos Vila, Municipio Lautem/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Lospalos	Lautem	Ukat Mape Goll Unip Lda	NCB-MOP-190062	\$ 419,409.00	33.53%	30.18%	\$ 126,557.78	\$ 292,851.22	PENDENTE	
18	Rural Road Rehabilitation Fuloro - Home Chainage 0+000 - 1+200 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Lospalos	Lautem	Paiahara Unipessoal Lda	RT/032/MOP - 2019	\$ 264,203.18	78.06%	38.29%	\$ 101,160.75	\$ 163,042.43	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 2.32%
19	Building Minor Maintenance East Side (Manatuto, Baucau, Lospalos & Viqueque	MINISTERIO FINANÇAS	LM-BS	EDIFICIOS PUBLICOS	Lospalos	Lautem	Prify Unip Lda	01 - Prify - MOF/DGCS.2019	\$ 56,783.85	80.85%	80.85%	\$ 45,907.81	\$ 10,876.04	PENDENTE	
20	Rural Roads Periodic Maintenance Lospalos Soru Chainage 0 + 000 - 2 + 500, Lautem Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lospalos	Lautem	Ulau Unip. Lda	MPW-W: 190110	\$ 216,252.57	80.83%	52.01%	\$ 112,482.53	\$ 103,770.04	ON-GOING	
21	Konstrusaun Fatin Izolamentu iha CHC Lospalos Municipiu Lautem	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Lospalos	Lautem	RICS Unipessoal Lda	RDTL-MS-DNA-DC-20-253	\$ 284,788.97	59.13%	40.05%	\$ 114,064.48	\$ 170,724.49	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 2.45%
22	New Construction Of Houses For Veterant 8 Unit	MINISTERIO PLANU E ORDENAMENTU	LM-CD	EDIFICIOS PUBLICOS	Lospalos	Lautem	Davinci	001/RDTL/MP/IE/AN/D/DIL/VI/2016	\$ 788,921.55	49.09%	49.09%	\$ 387,253.22	\$ 401,668.33	PENDENTE	
23	R4D RURAL ROADS SPOT IMPROVEMENT LEURO - SOURULUA CHAINAGE 0+000-2+650	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lospalos	Lautem	KOMI ARA UNIPESSOAL LDA	MPW - W -210080	\$ 271,648.79	2.64%	0.00%	\$ -	\$ -	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro 2.64%
24	Konstrusaun Murru Haleu Edifisiu Administasaun Munisipiu no Jardim Municipiu Lautem	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Lospalos	Lautem	Marvong Construction Unip.Lda	02/KML-PDIM/SMA/X2021	\$ 145,363.15	0.00%	0.00%	\$ -	\$ -	ON-GOING	
25	Rehabilitasaun Residencia Adminitrador + Murru no Jardim Municipio Lautem	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Lospalos	Lautem	Marvong Construction Unip.Lda	01/KML-PDIM/SMA/X/2021	\$ 251,975.70	0.00%	0.00%	\$ -	\$ -	ON-GOING	
26	New Installation MV, LV Line and House Connection from Wanira to Wairoke, Ulukisi, Ailembere, and Liarafa, Luro - Lautem Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Loru	Lautem	Vairoque Unip., Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000432	\$ 593,550.47	68.51%	68.51%	\$ 406,628.69	\$ 186,921.78	ON-GOING	
27	Rehabilitation of Road Laivai - Vairoque - Liarava Roads Sta. 0+000 - 7+250 (7.25 km) Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Loru	Lautem	Hoven II, Unip. Lda	SSS/140/MOPTC-2017	\$ 4,207,194.97	100.00%	89.84%	\$ 3,779,720.19	\$ 427,474.78	PHO	Ongoing
28	Rural Roads Periodic Maintenance Luro - Barikafa Chainage 0+000 - 7+000 Municipality Lautem (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loru	Lautem	Perekiki Mori Unip. Lda	MPW-W-NVB-R-190041	\$ 161,431.38	37.70%	37.70%	\$ 60,858.29	\$ 100,573.09	PENDENTE	
29	Rehabilitation of Luro - Buihomau Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Loru	Lautem	Consorcio ASCEM "CACM" Lda"	MPW-W-13-005	\$ 4,950,000.00	97.11%	97.11%	\$ 4,806,765.20	\$ 143,234.80	PENDENTE	
30	Road Maintenance Periodic Luro - Kota Mutu - Lakawa Sta. 0+000 6+500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loru	Lautem	Cambota	MPW-W:190095	\$ 62,781.36	75.93%	64.69%	\$ 40,614.46	\$ 22,166.90	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 4.02%



#ANEXU A (LISTA GERAL LAUTEM)

Localizasaun Projeto															
NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	NARAN KONT.	MONT. KONT. (\$)	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	STATUS PROJECTO	OBS
31	R4D RURAL ROAD SPOT IMPROVEMENT LURO - BARIKAFA CHAINAGE 0+000+7+000 LAUTEM MUNICIPALITY	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loru	Lautem	Lili Unip. Lda.	MPW - W 210079	\$ 249,614.09	3.92% ✓	0.00%	\$ -	\$ -	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro 3.92%
32	R4D RURAL ROAD SPOT IMPROVEMENT LURO - KOTAMUTU - LAKAWA CHAINAGE 0+000-6+500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loru	Lautem	ILIE CHAO, UNIPESSOAL LDA	MPW - W - 210077	\$ 132,612.26	7.04% ✓	0.00%	\$ -	\$ -	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro 7.04%
33	New Installation MV, LV Line and House Connection from Ailebere to Pujiara, Arafalun and Ledo Ira, Iliomar - Lautem Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Iliomar	Lautem	Lor Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000363	\$ 432,643.32	72.00%	72.00%	\$ 311,503.19	\$ 121,140.13	ON-GOING	
34	Aditonal Emergency Iliomar Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Iliomar	Lautem	Resister Unip.Lda	SSS/140/MOPTC-2016	\$ 64,189.34	86.34%	75.98%	\$ 48,771.30	\$ 15,418.04	PENDENTE	
35	Konstrusaun Postu Saude no Rezidencia ba Mediki iha Iradarate	MINISTERIO SAUDE	PDIM	SAUDE	Iliomar	Lautem	Diroma Unip. Lda	18/A.M.LAUTEM/XI/2019	\$ 188,968.64	87.09%	87.09%	\$ 164,564.78	\$ 24,403.86	ON-GOING	
36	Road Rehabilitation From Tutuala to Valu Chainage 0+000 - 3+850 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Tutuala	Lautem	Consortio Vacu-Hiamoinu Lda	SSS/063/MOPTC-2017	\$ 3,104,481.77	38.64% ✓	24.22%	\$ 751,811.30	\$ 2,352,670.47	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 1.14%
37	Rehabilitation Road Section : Jct. Tutuala Roads (C2) Package 1 Sta. 3+850 - 7+725 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Tutuala	Lautem	Hamutuk Unipessoal, Lda	SSS/083/MOPTC-2017	\$ 3,008,551.46	34.08% ✓	19.23%	\$ 578,491.43	\$ 2,430,060.03	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Outubro Aumenta 1.59%
TOTAL									\$ 38,386,019.81			\$ 21,816,015.08	\$ 15,518,790.74		

1. Eng. Inocencio da Costa Maia
Eng. ba Projecto Edificio Publico Beé no Saneamento Municipiu Lautem, ADN, I.P.

4. Eng. Adonis Julio Fernandes
Eng. ba Projecto ME, ADN, I.P.

Prepara Husi :

2. Eng. Gerardo M.X.C. Aleixo
Eng. ba Projecto Infrastrutura e Irigasaun Municipiu Lautem, ADN, I.P.

3. Eng. Deolindo Henrique Lopes
Eng. ba Projecto Infrastrutura e Irigasaun Municipiu Lautem, ADN, I.P.

Verifika Husi :

Eng. Aniceto da Costa
Eng. Senior ba Projecto Infrastrutura e Irigasaun, ADN, I.P.

Eng/Arch. Francisco Xavier de D. Jeronimo
Senior Engenheiro ba Projecto Edificio Publico Beé no Saneamento ADN, I.P.

Eng. Deolindo de Fatima Marques
ChefeSaksaun ME& ITC, ADN, I.P.

Certifika Husi :

Eng. Emerenciana da Costa M.Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN, I.P.

#ANEXU B

PROGRESSU FISIKU KADA FULAN



LOKALIZASAUN PROJETU											Sep-21	Oct-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Kumulativo Progress	Previous Progress	This Month Progress	Kumulativo Progress
1	Rehabilitation of Laleno Road Project Road Section (Sta. 0+000 - 6+210) Maina 2 in Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lautem	Lautem	Corcorcio Irloyvon, Lda	SSS/117/MOPTC-2016	\$ 4,782,693.68	July 25, 2016	87.20%	87.20%	0.00%	87.20%
2	Rehabilitation Roads Maina 1 to parlamento 3.916 km	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lautem	Lautem	Samudra Unip, Lda	SSS/100/MOPTC-2017	\$ 3,039,825.77	Sept. 12, 2017	82.22%	82.22%	0.00%	82.22%
3	Rural Roads Periodic Maintenance Dasidara Lequidiga 0+000 - 10+000 Chainage Municipality Lautem (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Lautem	Lautem	Franam Lindo Unip. Lda	MPW-W-RTQ-190038	\$ 84,077.42	Oct. 29, 2013	56.05%	56.05%	0.00%	56.05%
4	Projectu Konstrusaun Turizmu Komunitariu iha COM, Postu Administrativu Lautem	SEFOPE	LM	TURISMO	Lautem	Lautem	Joli Toni Unip Lda	17/CNEFP?XI/2016	\$ 85,584.79	Nov. 3, 2016	91.76%	91.76%	0.00%	91.76%
5	Rehabilitation of Road Jct. Assalaino to Com, Road Section : Jct. Assalaino to Caicavamoko Sta. 8+000 - 15+200 Lautem Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lautem	Lautem	Fian Const. Unip. Lda	SSS/144/MOPTC-2017	\$ 4,028,818.90	Sept. 12, 2017	93.03%	93.03%	0.00%	93.03%
6	R4D RURAL ROAD SPOT IMPROVEMENT DASIDARA - LIQUIDIGA CHAINAGE 0+000-10+500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lautem	Lautem	ILIE CHAO, UNIPESOAAL LDA	MPW - W - 210078	\$ 181,220.42	16-Jul-21	0.00%	0.00%	8.84%	8.84%
7	Konstrusaun Monumento Nino Konis Santana no Jardim iha Escola Secundaria Nino Konis Santana Publica LAUTEM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM	EDUKASAUN	Lospalos	Lautem	Amor Construction	RDTL 2016	\$ 66,333.92	Dec. 16, 2016	95.58%	95.58%	0.00%	95.58%
8	Konstrusaun Edificio PGR Municipio Lautem	PROCURADORIA GERAL DA REPUBLICA	LM	EDIFICIOS PUBLICOS	Lospalos	Lautem	Cambota	RDTL- D.FeO/APRO/PGR/19.001/20 19	\$ 710,074.64	Oct. 17, 2019	49.45%	49.45%	3.36%	52.80%
9	Rural Road Rehabilitation Fuiloro - Home Chainage 1+200 - 2+500 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Lospalos	Lautem	Paiahara Unipessoal Lda	RT/033/MOP - 2019	\$ 287,376.91	Jan. 22, 2020	38.67%	38.67%	0.35%	39.02%
10	New Construction of Laboratory for Covid 19 at Lautem, Ministry of Health, Timor Leste	MINISTERIO SAUDE	LM	SAUDE	Lospalos	Lautem	Parapa Bemiziuu Star Unipessoal Lda	RDTL-MS-DNA-RBK-20-189	\$ 88,631.06	Nov. 1, 2021	82.09%	82.09%	0.00%	82.09%
11	Rehabilitation of Road Jct. Assalaino to Com, Road Section : Jct Assalaino to Caicavamoko Sta. 0+000 - 8+000 km municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lospalos	Lautem	Salve, Unip. Lda	SSS/143/MOPTC-2017	\$ 4,092,376.19	Sept. 12, 2017	92.22%	92.22%	0.00%	92.22%
12	Routine Maintanance Lospalos - Souro Chainage 0+000 - 5+800, Routine Maintanance Leuro - Sorulua Chainage 0+000 - 3+000	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Lospalos	Lautem	Afabubo f. Unip Lda.	RFQ/222/MOPTC-2016	\$ 49,805.16	July 11, 2016	86.99%	86.99%	0.00%	86.99%
13	Road Maintenance Sections : Lospalos - Iliomar Section (A082 - 2) Municipality Lautem (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Lospalos	Lautem	Lero Company, Lda	MPW-W-190120	\$ 219,745.45	Sept. 16, 2019	92.80%	92.80%	0.00%	92.80%
14	Prefurasau Sistema Be'e mos iha Suku PA'Papa Postu Adm. Lospalos Vila	MINISTERIO DAS OBRAS PUBLICAS	LM	AGUA E SANEAMENTO	Lospalos	Lautem	Mai Moco	MPWTC-NCB-170007	\$ 140,470.95	Aug. 25, 2017	80.38%	80.38%	0.00%	80.38%
15	Konstrusaun Edificio CDS Lospalos Inklui Armagem no pavimento	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	LM	SOLIDARIEDADE E SOCIAL	Lospalos	Lautem	Delta Dini	RDTL 15/MSS/DNFALM-DAD/XII/2015	\$ 417,933.73	July 20, 2015	96.29%	96.29%	0.00%	96.29%

16	Konstrusaun no Instalasaun Sistema Be'e Mos iha Aldeia Homokanu, Foemaa, Nanakuru no EBF Soru Posto Administrativo Lospalos Vila, Municipio Lautem/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM	AGUA E SANEAMENTO	Lospalos	Lautem	Paza Conis Unip Lda	NCB-MOP-190063	\$ 255,685.00	Dec. 1, 2019	25.15%	25.15%	0.00%	25.15%
17	Konstrusaun Be'e Mos Sistema Pompa no Gravitasaun,Tchay Titilary, Nuhalanta, Posto Administrativo Lospalos Vila, Municipio Lautem/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM	AGUA E SANEAMENTO	Lospalos	Lautem	Ukat Mape Goll Unip Lda	NCB-MOP-190062	\$ 419,409.00	Dec. 1, 2019	33.53%	33.53%	0.00%	33.53%
18	Rural Road Rehabilitation Fuloro - Home Chainage 0+000 - 1+200 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Lospalos	Lautem	Paiahara Unipessoal Lda	RT/032/MOP - 2019	\$ 264,203.18	Jan. 22, 2020	75.74%	75.74%	2.32%	78.06%
19	Building Minor Maintenance East Side (Manatuto, Baucau, Lospalos & Viqueque	MINISTERIO FINANÇAS	LM	EDIFICIOS PUBLICOS	Lospalos	Lautem	Prify Unip Lda	01 - Prify - MOF/DGCS.2019	\$ 56,783.85	Jan. 15, 2019	80.85%	80.85%	0.00%	80.85%
20	Rural Roads Periodic Maintenance Lospalos Soru Chainage 0 + 000 - 2 + 500, Lautem Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Lospalos	Lautem	Ulau Unip. Lda	MPW-W: 190110	\$ 216,525.57	March 9, 2019	80.83%	80.83%	0.00%	80.83%
21	Konstrusaun Fatin Izolamentu iha CHC Lospalos Municipiu Lautem	MINISTERIO SAUDE	LM	SAUDE	Lospalos	Lautem	RICS Unipessoal Lda	RDTL-MS-DNA-DC-20-253	\$ 284,788.97	Dec. 9, 2020	56.69%	56.69%	2.45%	59.13%
22	New Construction Of Houses For Veteran 8 Unit	MINISTERIO PLANU E ORDENAMENTU	LM-CD	EDIFICIOS PUBLICOS	Lospalos	Lautem	Davinci	001/RDTL/MPIE/AND/DIL/VI/2 016	\$ 788,921.55	Aug. 06, 2016	54.54%	54.54%	0.00%	54.54%
23	R4D RURAL ROADS SPOT IMPROVEMENT LEURO - SOURULUA CHAINAGE 0+000-2+650	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lospalos	Lautem	KOMI ARA UNIPESSOAL LDA	MPW - W -210080	\$ 271,648.79	16-Jul-21	0.00%	0.00%	2.64%	2.64%
24	Konstrusaun Murru Haleu Edifisiu Administasaun Munisipiu no Jardim Municipiu Lautem	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Lospalos	Lautem	Marvong Construction Unip.Lda	02/KML-PDIM/SMA/X2021	\$ 145,363.15	8-Jul-21	0.00%	0.00%	0.00%	0.00%
25	Rehabilitasaun Residencia Adminitrador + Murru no Jardim Municipio Lautem	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Lospalos	Lautem	Marvong Construction Unip.Lda	01/KML-PDIM/SMA/X/2021	\$ 251,975.70	8-Jul-21	0.00%	0.00%	0.00%	0.00%
26	New Installation MV, LV Line and House Connection from Wanira to Wairoke, Ulukisi, Ailembere, and Liarafa, Luro - Lautem Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Loru	Lautem	Vairoque Unip., Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000432	\$ 593,550.47	Sept. 1, 2016	81.25%	81.25%	0.00%	81.25%
27	Rehabilitation of Road Laivai - Vairoque - Liarava Roads Sta. 0+000 - 7+250 (7.25 km) Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Loru	Lautem	Hoven II, Unip. Lda	SSS/140/MOPTC-2017	\$ 4,207,194.97	Sept. 7, 2017	99.82%	99.82%	0.00%	99.82%
28	Rural Roads Periodic Maintenance Luro - Barikafa Chainage 0+000 - 7+000 Municipality Lautem (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Loru	Lautem	Perekiki Mori Unip. Lda	MPW-W-NVB-R-190041	\$ 161,431.38	Aug. 22, 2013	45.00%	45.00%	0.00%	45.00%
29	Rehabilitation of Luro - Buihomau Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Loru	Lautem	Consortio ASCEM "CACM" Lda"	MPW-W-13-005	\$ 4,950,000.00	Oct. 1, 2012	97.11%	97.11%	0.00%	97.11%
30	Road Maintenance Periodic Luro - Kota Mutu - Lakawa Sta. 0+000 6+500	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Loru	Lautem	Cambota	MPW-W:190095	\$ 62,781.36	Sept. 6, 2019	71.91%	71.91%	4.02%	75.93%
31	R4D RURAL ROAD SPOT IMPROVEMENT LURO - BARIKAFA CHAINAGE 0+000+7+000 LAUTEM MUNICIPALITY	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loru	Lautem	Lili Unip. Lda.	MPW - W 210079	\$ 249,614.09	16-Jul-21	0.00%	0.00%	3.92%	3.92%
32	R4D RURAL ROAD SPOT IMPROVEMENT LURO - KOTAMUTU - LAKAWA CHAINAGE 0+000-6+500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loru	Lautem	ILIE CHAO, UNIPESSOAL LDA	MPW - W - 210077	\$ 132,612.26	16-Jul-21	0.00%	0.00%	7.04%	7.04%
33	New Installation MV, LV Line and House Connection from Ailebere to Pujiara, Arafalun and Ledo Ira, Iliomar - Lautem Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Iliomar	Lautem	Lor Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000363	\$ 432,643.32	July 6, 2016	82.15%	82.15%	0.00%	82.15%
34	Aditonal Emergency Iliomar Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Iliomar	Lautem	Resister Unip.Lda	SSS/140/MOPTC-2016	\$ 64,189.34	Nov. 7, 2016	86.34%	86.34%	0.00%	86.34%

35	Konstrusaun Postu Saude no Rezidencia ba Mediku iha Iradarate	MINISTERIO SAUDE	PDIM	SAUDE	Iliomar	Lautem	Diroma Unip. Lda	18/A.M.LAUTEM/XI/2019	\$ 188,968.64	Nov. 4, 2019	96.76%	96.76%	0.00%	96.76%
36	Road Rehabilitation From Tutuala to Valu Chainage 0+000 - 3+850 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Tutuala	Lautem	Consortio Vacu-Hiamoinu Lda	SSS/063/MOPTC-2017	\$ 3,104,481.77	Aug. 25, 2017	37.50%	37.50%	1.14%	38.64%
37	Rehabilitation Road Section : Jct. Tutuala Roads (C2) Package 1 Sta. 3+850 - 7+725 Municipality Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Tutuala	Lautem	Hamutuk Unipessoal, Lda	SSS/083/MOPTC-2017	\$ 3,008,551.46	Aug. 28, 2017	32.50%	32.50%	1.59%	34.08%

Inspeksaun Husi :


1. Eng. Inocencio doa Reis Costa Maia
Eng. ba Porjecto Edificio Publico Beé no Saneamento Municipio Lautem,ADN,I.P



4. Eng. Adonis Julio Fernandes
Eng. ba Projeito ME, ADN, I.P


2. Eng. Geovanhio M.X.C. Aleixo
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Lautem, ADN, I.P


3. Eng. Beamantino Henrique Lopes
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Lautem, ADN, I.P

Verifika Husi :


Eng. Aniceto da Costa
Eng. Senior ba Projeito Insfrasturctura e Irigasaun, ADN, I.P


Eng/Arch.Francisco Xavier de D. Jeronimo
Senior Engineer ba Porjecto Edificio Publico Beé no Saneamento,ADN,I.P


Eng. Deolindo de Fatima Marques
ChefeSeksau ME& ITC, ADN, I.P


Eng. Emerenciana da Costa
M.Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN,I.P
