




REPÚBLIKA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATORIU MENSAL
IMPLEMENTASAUN
PROJETUS MUNISIPIU AILEU

DEZEMBRO 2021

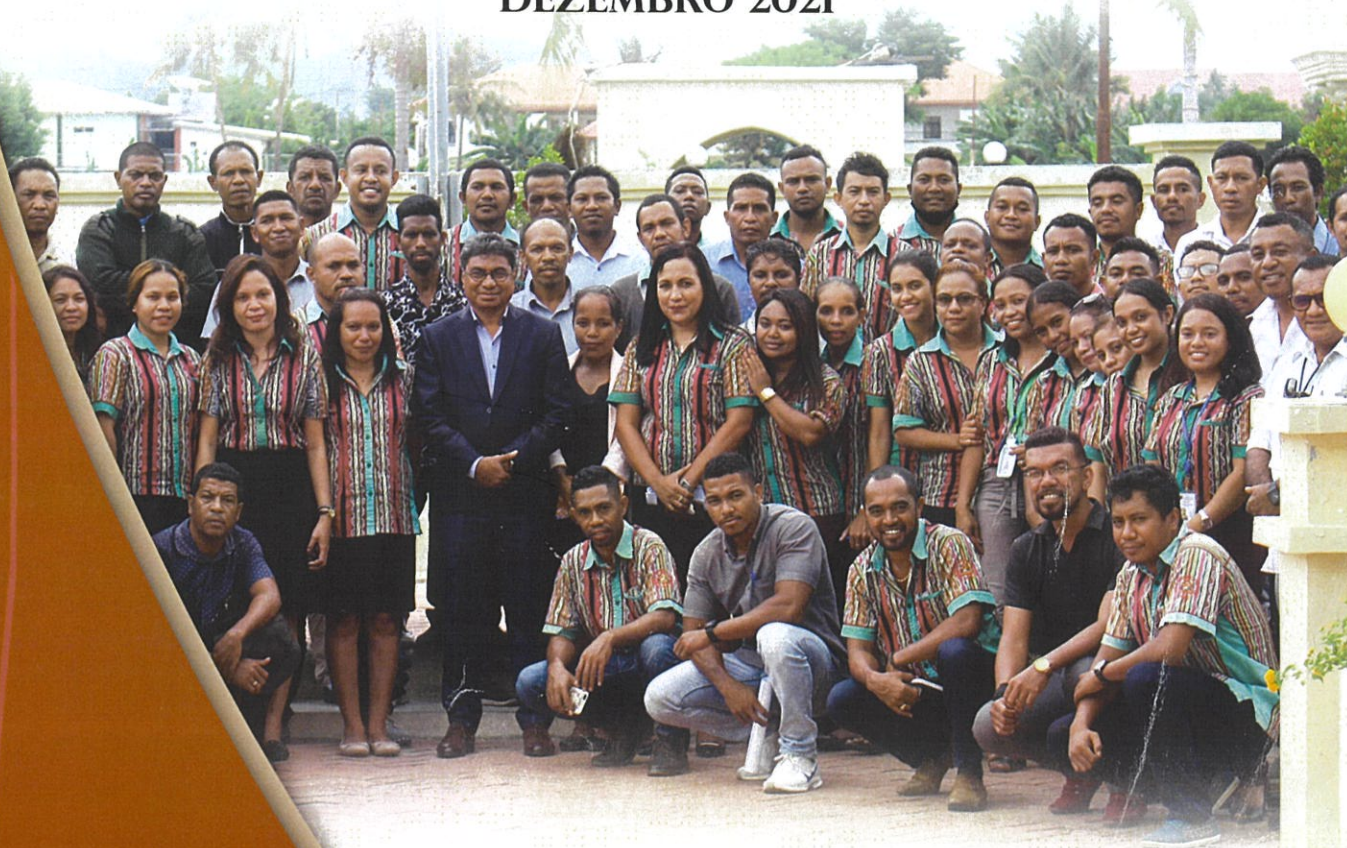

SUMÁRIO
RELATÓRIO
IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO
AILEU
DESEMBRO 2021

Prepara Husi :


(Eng. Merinho Cuco Lopes de Araújo)
Eng. ba Edifício Público no Beé Saneamento,
Município Aileu ADN, I.P


(Silvino D R R Soares)
Eng. M & E, Município Aileu ADN, I.P


(Eng. Rui Lopes)
Eng. ba Projeto Infraestrutura, Transporte e
Irigação, Município Aileu ADN, I.P


(Eng. Marcelino Amaral)
Eng. ba Projeto Infraestrutura, Transporte e
Irigação, Município Aileu ADN, I.P

Verifica Husi :


(Arc. Francisco X D D Jeronimo)
Eng. Senior ba Edifício Público no Beé
Saneamento, ADN, I.P


(Eng. Aniceto da Costa)
Eng. Senior ba Projeto Infraestrutura,
Transporte e Irigação, ADN, I.P


(Deolindo de F Marques)
Chefe Sek. Projeto M.E & ITC, ADN,

Sertifica Husi :


(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade,
ADN, I.P

Aprova Husi :


(Mariano Renato Monteiro da Cruz, S. T. M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO	1
INDICE	1
I. INTRODUSAUN	3
1.1 Enkuadramentu Legal.....	3
1.2 Perfil Municipio Aileu.....	3
1.3. Lista Projectos	6
II. PROGRESU FISIKU	13
2.1 Progreso Fisiku Kada Fulan	13
III. OBSTÁCLO IHA TERENU	13
3.1 Obstáculo Servisu Iha Terenu	13
IV. REKOMENDASAUN IHA TERENU	15
4.1 Rekomendasaun Servisu Iha Terenu.....	15

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias	4
Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Aileu.....	4
Tabela 1.2 : Lista Asset ADN,I.P Municipio Aileu	5
Tabela 1.3.1 : Projecto Municipio Aileu Por Fundus Finansiamentos	6
Tabela 1.3.2 : Projecto Municipio Aileu Por Sectores.....	8
Tabela 1.3.3 : Projecto Municipio Aileu Por Ministerio.....	10
Tabela 1.4 : Dadus Populasaun Munisipiu Aileu	13

I. INTRODUSAUN


1.1 Enkuadramentu Legal

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho qualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefisiu ne'ebe razoável no viável.

Depois de Dekretu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizaun no sertifikasaun qualidade ba projetu sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Aileu

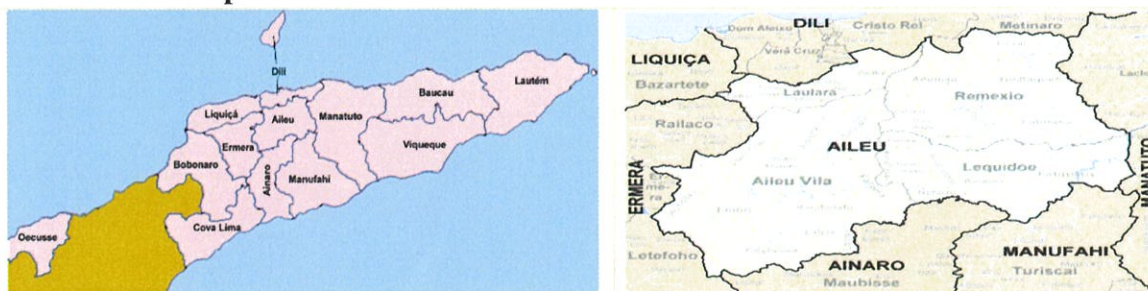

Administrasaun Munisipal Aileu lokalizadu iha parte sul Dili, kapital paiz no mapa 1 hatudu pozisaun jeográfika Munisipiu Aileu ne'ebé ho luan hamutuk 729 km² ho populasau ema

na'in 44,325 no densidade demografika ema 50.6 ba km2 , tuir Sensus 2015. Topografia Munisipiu Aileu ne'ebé foho dominante liu ho a'as entre 350 m to'o 1,500 m sukat husi tasi. Kapitál maka Aileu Vila iha foho Mota Mantane ho altitude 913 m. Administrasaun Munisipal Aileu iha Postos Administrativos 4, Sukus 31 no aldeias 139.

Tabela 1 : Postos Administrativos, Sucos No Aldeias

Aileu villa		Laulara		Lequidoe		Remexio	
Sukus	Aldeias	Sukus	Aldeias	Sukus	Aldeias	Sukus	Aldeias
Aissirimou	5	Fatisei	5	Aculitofo	3	Acumau	3
Bandudato	3	Cotolau	5	Bereleu	5	Fadabloco	7
Fahiria	6	Madabeno	5	Betulau	3	Fahiso	3
Fatubossa	7	Talitu	4	Fahiso	3	Faturas	4
Hoholau	5	Tohumeta	3	Faturilau	2	Hautoho	3
Lahane	5	-	-	Manucasa	2	Suco Liurai	3
Lausi	4	-	-	Namolesso	4	Maumeta	3
Suco Liurai	8	-	-	-	-	Tulataqueo	7
Seloi Malere	6	-	-	-	-	-	-
Saburia	3	-	-	-	-	-	-
Seloi Craik	10	-	-	-	-	-	-
Total	62	-	22	-	22		33

Data husi: Livro 3 B OJE 2021, pag 17

Tabela 1.1 : Força de Trabalho ADN, I.P Municipio Aileu

Força de Trabalho ADN,I.P Municipio Aileu								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	3					3	
2	Administrasaun no Financas	0					0	
3	Motorista	1					1	
4	Seguransa	0					0	
Total		4					4	

Tabela 1.2 : Lista Asset ADN,I.P Municipio Aileu

ASET ADN, I.P MUNICIPIO AILEU								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1					1	
2	Kareta	1					1	
3	Desktop HP / Monitor	1					1	
4	Laptop HP	1					1	Port ba USB fatin la diak , operaun labtop Todan
5	Printer Cannon	1					1	
6	UPS	1					1	
7	Armario File	2					1	
8	Armario Tau hena	3					3	
9	Meja escritorio	1					1	
10	Meja han	1					1	
11	Meja TV (kiik)	1					1	
12	Kadeira escritorio	4					4	
13	Kadeira han	4					4	
14	Sofa	1 Set					1	
15	Springbed +sumasu 4+sprei 3	3 Set					1	Springbed ida Nakles, Sumaso la Iha ba Kuarto Tolu
16	Jeleira	1					1	
17	TV + Parabola	1 Set					1	Reciver hosi Parabola la Utilija
18	Kipas Angin	5					5	Ida Kondisaun att
19	Kompor	1					1	
20	Kompor Gas	1					1	Kondisaun Att no la bele uja
21	Rack sepatu	3					3	
22	Rack Piring	1					1	
23	Lampu	11					11	Rua mak att, nebe monta iha Veranda Uma oin no Veranda Kotuk ho Marka Philip
24	Water Pump Sanyo	1					1	

1.3. Lista Projectos

Projetu hotu neébe akumula iha lista neé bazeia ba dados projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamiento, tabela 1.3.2 Projetu por Sector no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabela 1.3.1 : Projecto Municipio Aileu Por Fundus Finansiamiento

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM - CD + PDIM + LM - BS + LM - TP + Fundo Covid-19		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	21	\$ 45,227,712.91	86.70%
2	Laulara	9	\$ 32,269,244.55	54.63%
3	Lequidoe	6	\$ 1,653,948.80	65.22%
4	Remexio	2	\$ 3,061,889.99	35.99%
	Grand Total	38	\$ 82,212,796.25	71.79%

NO	POSTO ADMINISTRATIVO	FI		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	6	\$ 42,290,763.92	90.08%
2	Laulara	7	\$ 32,002,953.24	54.56%
3	Lequidoe	1	\$ 240,048.46	84.76%
4	Remexio	1	\$ 2,567,345.51	30.98%
	Grand Total	15	\$ 77,101,111.13	73.35%

NO	POSTO ADMINISTRATIVO	LM-CD		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	4	\$ 1,397,856.77	33.22%
2	Laulara	2	\$ 266,291.31	63.74%
3	Lequidoe	4	\$ 863,100.34	56.74%
4	Remexio			
	Grand Total	10	\$ 2,527,248.42	44.46%

NO	POSTO ADMINISTRATIVO	PDIM		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	6	\$ 445,124.22	0.00%
2	Laulara			
3	Lequidoe			
4	Remexio			
Grand Total		6	\$ 445,124.22	0.00%

NO	POSTO ADMINISTRATIVO	LM-BS		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	2	\$ 522,720.63	25.09%
2	Laulara			
3	Lequidoe	1	\$ 550,800.00	70.00%
4	Remexio	1	\$ 494,544.48	62.04%
Grand Total		4	\$ 1,568,065.11	52.52%

NO	POSTO ADMINISTRATIVO	LM-TP		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	1	\$ 227,981.87	82.08%
2	Laulara			
3	Lequidoe			
4	Remexio			
Grand Total		1	\$ 227,981.87	82.08%

NO	POSTO ADMINISTRATIVO	Fundu-Covid-19		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aileu-Vila	2	\$ 343,265.50	89.27%
2	Laulara			
3	Lequidoe			
4	Remexio			
Grand Total		2	\$ 343,265.50	89.27%

Dadus detallu kada projetu: #Anexu A

Tabela 1.3.2 : Projecto Municipio Aileu Por Sectores

NO	SECTOR PROJECTO	TOTAL MUNICIPIO AILEU		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Agua E Saneamento	2	\$ 862,274.82	8.64%
2	Edificios Publicos	4	\$ 754,094.60	57.21%
3	Eletrifikasaun Nasional	3	\$ 1,001,069.36	75.97%
4	Estradas	9	\$ 17,144,407.17	76.67%
5	Imprestimo	3	\$ 137,301.98	0.00%
6	Flood Control	5	\$ 59,210,769.19	72.66%
7	Manutensaun No Rehabilitasaun	5	\$ 1,320,533.03	56.62%
8	Preparasaun Desenhos No Supervisaun -Novos Projectos	2	\$ 1,025,800.00	47.11%
9	Saude	2	\$ 362,073.90	30.68%
10	Solidariedade E Social	2	\$ 166,490.33	20.05%
11	Turismo	1	\$ 227,981.87	95.18%
Grand Total		38	\$ 82,212,796.25	71.79%

NO	SECTOR PROJECTO	Aileu-Vila		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Agua E Saneamento	2	\$ 862,274.82	8.64%
2	Edificios Publicos	4	\$ 754,094.60	57.21%
3	Eletrifikasaun Nasional			
4	Estradas	2	\$ 469,908.84	85.87%
5	Imprestimo	3	\$ 137,301.98	0.00%
6	Flood Control	4	\$ 41,355,467.92	90.94%
7	Manutensaun No Rehabilitasaun	1	\$ 717,064.23	41.26%
8	Preparasaun Desenhos No Supervisaun -Novos Projectos	1	\$ 475,000.00	20.58%
9	Saude	1	\$ 62,128.32	85.95%
10	Solidariedade E Social	2	\$ 166,490.33	20.05%
11	Turismo	1	\$ 227,981.87	95.18%
Grand Total		21	\$ 45,227,712.91	86.70%

NO	SECTOR PROJECTO	Laulara		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Agua E Saneamento			
2	Edificios Publicos			
3	Eletrifikasaun Nasional	2	\$ 761,020.90	73.19%
4	Estradas	5	\$ 13,612,608.34	85.50%
5	Imprestimo			
6	Flood Control	1	\$ 17,855,301.27	30.32%
7	Manutensaun No Rehabilitasaun	1	\$ 40,314.04	49.04%
8	Preparasaun Desenhos No Supervisaun -Novos Projectos			
9	Saude			
10	Solidariedade E Social			
11	Turismo			
Grand Total		9	\$ 32,269,244.55	54.63%

NO	SECTOR PROJECTO	Lequidoe		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Agua E Saneamento			
2	Edificios Publicos			
3	Eletrifikasaun Nasional	1	\$ 240,048.46	84.76%
4	Estradas			
5	Imprestimo			
6	Flood Control			
7	Manutensaun No Rehabilitasaun	3	\$ 563,154.76	76.72%
8	Preparasaun Desenhos No Supervisaun -Novos Projectos	1	\$ 550,800.00	70.00%
9	Saude	1	\$ 299,945.58	19.23%
10	Solidariedade E Social			
11	Turismo			
Grand Total		6	\$ 1,653,948.80	65.22%

NO	SECTOR PROJECTO	Remexio		
		TOTAL PROJECTO	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Agua E Saneamento			
2	Edificios Publicos			
3	Eletrifikasaun Nasional			
4	Estradas	2	\$ 3,061,889.99	35.99%
5	Imprestimo			
6	Flood Control			
7	Manutensaun No Rehabilitasaun			
8	Preparasaun Desenhos No Supervisaun -Novos Projectos			
9	Saude			
10	Solidariedade E Social			
11	Turismo			
Grand Total		2	\$ 3,061,889.99	35.99%

Dadus detallu kada projetu: #Anexu A

Tabela 1.3.3 : Projecto Municipio Aileu Por Ministerios

NO	DONO DO PROJECTO	GRAND TOTAL		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatal	5	\$ 410,259.40	0.00%
2	Ministerio Da Justica	1	\$ 200,000.00	89.19%
3	Ministerio Das Obras Publicas	25	\$ 80,089,853.57	72.59%
4	Ministerio Ensino Superior Ciencia E Cultura	1	\$ 475,000.00	20.58%
5	Ministerio Para Os Assuntos Dos Combatentes Da Libertacao Nacional	1	\$ 118,769.70	0.00%
6	Ministerio Saude	3	\$ 643,211.08	56.61%
7	Ministerio Solidariedade Social E Inklusaun	1	\$ 47,720.63	69.97%
8	Sefope	1	\$ 227,981.87	95.18%
Grand Total		38	\$ 82,212,796.25	71.79%

NO	DONO DO PROJECTO	Aileu-Vila		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatul	5	\$ 410,259.40	0.00%
2	Ministerio Da Justica	1	\$ 200,000.00	89.19%
3	Ministerio Das Obras Publicas	9	\$ 43,404,715.81	88.42%
4	Ministerio Ensino Superior Ciencia E Cultura	1	\$ 475,000.00	20.58%
5	Ministerio Para Os Assuntos Dos Combatentes Da Libertacao Nacional	1	\$ 118,769.70	0.00%
6	Ministerio Saude	2	\$ 343,265.50	89.27%
7	Ministerio Solidariedade Social E Inklusaun	1	\$ 47,720.63	69.97%
8	Sefope	1	\$ 227,981.87	95.18%
Grand Total		21	\$ 45,227,712.91	86.70%

NO	DONO DO PROJECTO	Laulara		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatul			
2	Ministerio Da Justica			
3	Ministerio Das Obras Publicas	9	\$ 32,269,244.55	54.63%
4	Ministerio Ensino Superior Ciencia E Cultura			
5	Ministerio Para Os Assuntos Dos Combatentes Da Libertacao Nacional			
6	Ministerio Saude			
7	Ministerio Solidariedade Social E Inklusaun			
8	Sefope			
Grand Total		9	\$ 32,269,244.55	54.63%

NO	DONO DO PROJECTO	Lequidoe		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Ministerio Da Justica			
3	Ministerio Das Obras Publicas	5	\$ 1,354,003.22	75.41%
4	Ministerio Ensino Superior Ciencia E Cultura			
5	Ministerio Para Os Assuntos Dos Combatentes Da Libertacao Nacional			
6	Ministerio Saude	1	\$ 299,945.58	19.23%
7	Ministerio Solidariedade Social E Inklusaun			
8	Sefope			
Grand Total		6	\$ 1,653,948.80	65.22%

NO	DONO DO PROJECTO	Remexio		
		TOTAL PROJETU	MONTANTE KONTRATU (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Ministerio Da Justica			
3	Ministerio Das Obras Publicas	2	\$ 3,061,889.99	35.99%
4	Ministerio Ensino Superior Ciencia E Cultura			
5	Ministerio Para Os Assuntos Dos Combatentes Da Libertacao Nacional			
6	Ministerio Saude			
7	Ministerio Solidariedade Social E Inklusaun			
8	Sefope			
Grand Total		2	\$ 3,061,889.99	35.99%

Dadus detallu kada projetu: #Anexu A

Tabela 1.4 : Dadus populasau Munisipiu Aileu

Posto Administrativu, Suku no Sexu	2021				
	Total	Idade Poduktivu (idade 15-64)		Idade la Produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Aileu Vila	27,669	8392	7814	6008	5455
Laulara	8,184	2373	2291	1807	1713
Lequidoe	7,764	2362	2149	1667	1587
Remexio	12,625	3320	3376	2984	2945

Fontes : Projeksaun Populasau bazeia ba Sensus Populasau no Umakain 2015,
Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu progresu actual fulan ida ne'e ho nia porsentagen servisu, montante actual bazeia ba orsamentu ne'ebe hetan husi progresu fulan ida ne'e, ikus liu porsentagen actual fulan ida ne'e hatudu progressu fisiku komulativu husi porsentu anterior no fulan ida ne'e nian, lista kompletu ba detallu bele hare'e iha #Anexu B, detallu ba Back-up Fotografia #Anexu C1, detallu ba Back-up BoQ #Anexu C2 no Instrusaun Servisu bele hare'e #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

1. Iha Municipio Aileu Kompania balun sira nia Enjineiru laiha Terenu, no Enjineiru husi Dono do Projeto mos la activu iha terenu.
2. Komposisi betaun ne'ebe fo husi Laboratorio Nacional maibe bainhira halo trail iha terenu husi kompanha kontaktu sira parte Laboratorio Nacional maibe laiha resposta ne'ebe fixu ba iha kompania sira. Maibe liu tiha loron balun husi parte Laboratorio Nacional kontaktu fali sira hodi foti rasik sample.

3. Iha Municipiu Aileu kompania/empreza sira infrenta problema ba rekursu finanseiru nune'e fo inpaktu ba serbisu konstrusaun nian hodi difikulta progress serbisu iha terenu.
4. Mudansa *Schedule* la tuir kontratu ho razaun pagamentu tarde, situasaun nebe'e ita hotu la espera ho covid-19 nebe'e invade Timor-Leste sai difikuldade mos ba kompania/empreza sira la halo serbisu tuir planu refere.
5. Tekniku AND,I.P halo observasaun/monitorizasaun direktamente iha terenu hodi hare'e serbisu kompania/empreza sira, maibe sira laiha Site Engineering.
6. Iha projectu balun ne'ebe maka kompania/empreza ladun koopera di'ak ho tekniku AND.IP no tekniku husi Dono projectu, tamba instrusaun nebe'e mak ita fo hanesan prepara *time schedule* hadia *direksi keet* maibe kompania/empreza la halo tuir orientasaun.
7. Bazeia ba planu inspesaun ne'ebe ami halo balun nia implementasaun la tuir planu nebee mak aprova husi DE. AND.IP, tamba iha difikuldade transporte, maibe ami nafatin tenta ka fahe tempo hodi halo monitorizasaun ba projetu hotu ne'ebe iha Municipiu Aileu.
8. Ba projectu ne'ebe mak abandona no parado ami halo monitorizasaun dala 2 tamba laiha progresu fiziku ne'ebe mak halo iha terenu tuir planu ne'ebe tekniku AND.IP halo Monitorizasaun.

➤ Obstaclo parte Eletricidade

1. Durante halo monitorizasaun ba projeto ne'ebe mak mensiona iha lista projetu Eng. M & E, ADN – I.P, la hasoru kontraktor sira tamba televomel fora da area hotu.
2. Eng. M & E, ADN – I.P, nunka hasoru tekniku husi kompania no parte kompania sempre delega tekniku ne'ebe ba hein iha terenu, maibe tekniku ne'e rasik laiha konesimentu klean ho orbra refere.
3. Seksaun M & E, AND – I.P, la bele kontrola projeto ho maximu tamba Eng. M & E ida hodi
kontrola Projeto Linha Electricidade ho Edifisio Publik Iha Municipio Ha'at (4).

4. Projeto eletricidade barak maka espasu ba lina laiha ona, hodi kompanha sira mos la halo servisu kontinuasaun.
5. Motorista menus difikulta ami nia servisu.

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Husu Superior ADN.IP atu bele hatu'o ba projectu nain konaba projetu hirak ne'ebe maka abandona no parado husi kompania/empresa ne'ebe iha responsabilidade ba projectu ne'e rasik atu bele foti medidas ruma hanesan *Black list* ou Penalidade ba kompania.
2. Ami husi tekniku/engineiru Municipiu AND.IP husu ba Dono Projectu refere, ba oin kompania/empresa ne'ebe maka laiha responsabilidade no abandona projetu/obra ne'ebe sira halo, husu Governo la bele fo tan oportunidade ba kompania hirak ne'e hodi kaer fali obra seluk.
3. Ami husi Engineiru Municipiu AND.IP sujere ba superior AND.IP atu bele prepara transporte hanesan motorizada hodi nune'e bele fasilita ami halo monitorizasaun ba projectu ne'ebe ho nia lokalizasaun besik.

➤ Recomendação parte Eletricidade

1. Husu ba parte ITC, ADN – I.P bele kria Folder Sistem ba Seksaun M & E, ADN – I.P.
2. Husu atu aumenta tan rekursu iha Seksaun M & E, ADN – I.P.

Note: Asinatura husi Eng Municipio Aileu

Força de Trabalho ADN, I.P Municipio Aileu						
No	Deskrisaun	Identidade				
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	Asinatura
1	Engineiro	Rui Lopes	077	Enjineiru ITI		
		Merinho Cuco L. de Araujo	189	Enjineiru EPAS		
		Marcelino Amaral	222	Enjineiru ITI		
		Silvino D. R. R. Soares	177	Enjineiru METIC		

2	Enjineira	Tifania Clotaria G. Ornai	201	Enjineira VEBD		
3	Motorista	João Pedro Cortereal		Motorista		



ANEXU A

MUNICIPIO AILEU (LISTA GERAL)

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
1	Rehabilitation of Sloi Tocoluli roads Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Aileu-Vila	Aileu	Mendith UnipLda	SSS/061/MOPTK-2015	\$ 218,231.77	Nov. 14, 2014	100.00%	88.00%	\$ 192,043.96	\$ 26,187.81	PENDENTE	Projeito refere falta 10% rekomendasaun ikus iha tinan 2019
2	Rehabilitasaun Estrada Rural R4D Taliforleu - Kolihoho Chainage 0+000 - 8+000 Munisiupi Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Aileu-Vila	Aileu	Caviq Unipessoal Lda in joint venture with Sunnines Unip. Lda	NCB/020/MOP-2019	\$ 717,064.23	Dec. 20, 2019	45.85%	41.26%	\$ 295,880.00	\$ 421,184.23	ON-GOING	
3	Road Climate Resilience project (RCRP) upgrading project and maintainance of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Chongqing International Construction Corporation	ICB/010/MPW-2013	\$ 28,823,606.10	April 10, 2014	97.44%	97.19%	\$ 28,012,563.34	\$ 811,042.76	ON-GOING	Maintanance
4	Consultant Design & Supervision Lot 3	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Katahira and Engineers International	SSS/043/MPW-2014	\$ 4,069,793.04	Sept. 15, 2014	80.11%	80.11%	\$ 3,260,234.80	\$ 809,558.24	ON-GOING	
5	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Kunhwa Engineering & Consulting Co., Ltd JV with Dongsung Engineering Co.,Ltd	RFP/020/MOPTC/2017	\$ 2,626,077.78	April 27, 2018	63.53%	61.16%	\$ 1,606,091.72	\$ 1,019,986.06	ON-GOING	
6	Emergency Dili to Aileu Maubisse Roads	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Aileu-Vila	Aileu	My Friend Unip. Lda	MPW-W-014054	\$ 251,677.07	Oct. 5, 2014	100.00%	84.02%	\$ 211,462.39	\$ 40,214.68	ON-GOING	
7	Rehabilitation of MSS Office in Aileu	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	LM-BS	SOLIDARIEDADE E SOCIAL	Aileu-Vila	Aileu	Borudo Matak	RDTL:47/MSS/DNP FAL-DAD/X/2016	\$ 47,720.63	Oct. 24, 2016	77.74%	69.97%	\$ 33,389.23	\$ 14,331.40	PENDENTE	
8	Programma Turismo Komunitario 2014 Seloi / Malere	SEFOPE	LM-TP	TURISMO	Aileu-Vila	Aileu	Miror Raefusa	RDTL/SEFOPE/DNA/DNE/2013-0003	\$ 227,981.87	May 5, 2014	91.20%	95.18%	\$ 217,004.28	\$ 10,977.59	PENDENTE	
9	Preparation of Master Plan For Municipal Capitals Water Supply and Sanitation (Aileu-Gleno-Liquica) /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Aileu-Vila	Aileu	Jurutera Perunding Zaaba Sdn. Bhd (Malaysia)	MPW-CS-200028	\$ 827,410.00	May 1, 2020	10.00%	9.00%	\$ 74,466.90	\$ 752,943.10	ON-GOING	
10	Realization of the Detailed Engeneering Design (DED) includes Reparation of Feasibility Study of the University of Aileu (Bem Serviso)	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA	LM-BS	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Aileu-Vila	Aileu	Bernabad Arquitectura SLP	MPW-S-200024	\$ 475,000.00	March 31, 2020	9.16%	20.58%	\$ 97,736.23	\$ 377,263.77	ON-GOING	
11	New Construction of laboratory for covid 19 at CHC Aileu Vila	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Aileu-Vila	Aileu	Jomy Unipessoal Lda	RDTL-MS-DNA-DC-20-257	\$ 62,128.32	Nov. 4, 2020	9.16%	85.95%	\$ 53,402.35	\$ 8,725.97	ON-GOING	
12	Konstrusaun, Vedasaun no Jardim ba Edificio DTPSC	Ministerio da Justica	LM-CD	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Kablaki Engineering Unip. Lda		\$ 200,000.00	1-Jul-12	89.19%	89.19%	\$ 178,371.29	\$ 21,628.71	PENDENTE	
13	Consultancy services for National Road No. 1 - Upgrading Project	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Philcoei International, Inc. In JV with Luis and Associates, Co	nn	\$ 5,835,991.00	Jan. 18, 2013	83.00%	81.01%	\$ 4,727,833.53	\$ 1,108,157.47	ON-GOING	
14	New Construction of Isolation Building	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Mortiles Unip.Lda	RDTL-MS-DNA-DC-20-255	\$ 281,137.18	Nov. 04, 2020	90.47%	90.00%	\$ 253,023.47	\$ 28,113.71	ON-GOING	
15	New Construction of Campas, Gate And Leveling	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTACAO NACIONAL	LM-CD	SOLIDARIEDADE E SOCIAL	Aileu-Vila	Aileu	Caramé Unip. Lda	No.: 37/MACLN/IX/2021	\$ 118,769.70	1-Sep-21	44.58%	0.00%	\$ -	\$ 118,769.70	ON-GOING	



ANEXU A

MUNICIPIO AILEU (LISTA GERAL)

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
16	Perfurasau Bee Mos Iha Selo Ba Fatin Turismo Komunitariu	MINISTERIO DAS OBRAS PUBLICAS	PDIM	AGUA E SANEAMENTO	Aileu-Vila	Aileu	Alenta Unip. Lda	48/SMA/AM-AIL/VIII/2021	\$ 34,864.82	Aug. 6, 2021	19.05%	0.00%	\$ -	\$ 34,864.82	ON-GOING	
17	Konstrusaun Intake inklui Bareira Protege Lagoa Selo Kraik iha Aileu Vila	ESTATAL	PDIM	FLOOD CONTROL	Aileu-Vila	Aileu	Aisel Girasol Unip. Lda	004/MAE/AM-AIL/SMA/IX/2021	\$ 26,311.39	Aug. 6, 2021	22.84%	0.00%	\$ -	\$ 26,311.39	ON-GOING	
18	Konstrusaun Edificio Posto Administrativo Lequidoe	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Fitun Foun, Unip Lda	002/MAE/AM-AIL/SMA/IX/2021	\$ 128,221.80	Aug. 6, 2021	14.98%	0.00%	\$ -	\$ 128,221.80	ON-GOING	
19	Konstrusaun Edifisiu Posto Administrativo Aileu Vila	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Diborna Unip. Lda	001/MAE/AM-AIL/SMA/IX/2021	\$ 144,735.62	Aug. 6, 2021	23.75%	0.00%	\$ -	\$ 144,735.62	ON-GOING	
20	Konstrusaun Bronjong Proteje Uma Comunidade no Uma Madres Caridade Inklui Toós Comunidade	ESTATAL	PDIM	FLOOD CONTROL	Aileu-Vila	Aileu	JOHIJEMAR Unip,Lda	005/MAE/AM-AIL/SMA/IX/2021	\$ 61,880.06	Aug. 6, 2021	30.18%	0.00%	\$ -	\$ 61,880.06	ON-GOING	
21	Konstrusaun Bronjong Proteje Igreja Assembleia de Deus no Uma Comunidade	ESTATAL	PDIM	FLOOD CONTROL	Aileu-Vila	Aileu	Padua Unip. Lda	006/MAE/AM-AIL/SMA/IX/2021	\$ 49,110.53	Aug. 6, 2021	84.81%	0.00%	\$ -	\$ 49,110.53	ON-GOING	
22	New Install New Transformer & Extend LV Line & New distribution Line from Madabeno to Sarlala Aileu District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laulara	Aileu	Aldepo Murak Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000162	\$ 462,154.02	Aug. 22, 2013	81.19%	73.07%	\$ 337,695.10	\$ 124,458.92	PENDENTE	Progresu Fisiku nafatin deit tamba laiha ona espasu atu kontinua tan obra ne'e.
23	Installation New MV Line,transformer & Extend LV Line & distribution Line from Lebukuku to Besilau and Fatuk Hun - Aileu District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laulara	Aileu	osxavijoneli unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000179	\$ 298,866.88	Aug. 22, 2013	81.53%	73.38%	\$ 219,311.16	\$ 79,555.72	PENDENTE	Progresu Fisiku nafatin deit tamba laiha ona espasu atu kontinua tan obra ne'e.
24	Rehabilitation of Beducu Sarlala Roads (Ex. Japan) Sta. 6+300 - Sta. 8+968.45	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Mejori, Lda	SSS/0103/MOPTC-2016	\$ 4,451,281.98	Sept. 5, 2016	98.97%	82.89%	\$ 3,689,601.06	\$ 761,680.92	ON-GOING	
25	Road Rehabilitation project, Sarlala - Bemós - Manleuana - Timor block link, Package 1: Sta. 0+000 - Sta. 2+800	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Aspalink Unip Lda	SSS/120/MOPTC-2015	\$ 4,128,651.62	Dec. 11, 2015	100.00%	87.43%	\$ 3,609,489.52	\$ 519,162.10	ON-GOING	Projeito Refere falta 10% rekomendasaun ikus iha tinan Desembro 2020
26	Road Rehabilitation project, Sarlala - Bemós - Manleuana - Timor block link, Package 1: Sta. 2+800 - Sta. 6+300	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Jonize Construction, Unip. Lda	SSS/121/MOPTC-2015	\$ 4,645,457.43	Dec. 11, 2015	100.00%	87.12%	\$ 4,046,912.38	\$ 598,545.05	ON-GOING	Projeito Refere falta 10% rekomendasaun ikus iha tinan Desembro 2020
27	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620) Municipality Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Laulara	Aileu	CINA WU YI CO.LTD	ICB/018/MOPTC-2017	\$ 17,855,301.27	May 31, 2019	79.61%	30.32%	\$ 5,413,917.86	\$ 12,441,383.41	ON-GOING	Responsavel Eng. ADN Imprestimo



ANEXU A

MUNICIPIO AILEU (LISTA GERAL)

NU.	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
28	Rural Roads Maintenance Fahisohi - Fadabloco Sta 0+000-8+200, Hotoho - Liquica Sta 0+000 - 2+500 and Laulara - Ornai Sta 0+000 - 7+500 in Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Laulara	Aileu	Remexio Furak Unip Lda	MPWTC-CD-170004	\$ 40,314.04	July 20, 2017	100.00%	49.04%	\$ 19,768.44	\$ 20,545.60	ON-GOING	Rekomenadasun Ikus 2018
29	R4D Rural Roads Periodic Maintenance Laulara - Ornai Chainage 0+000 - 8+000 Routine Maintenance Madabeno - Lisimori Chainage 0+000 - 4+900 and Acumau - Aicorema Chainage 0+000 - 2+000 Municipality Aileu / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laulara	Aileu	Fin Los unip.Lda	MPW-W190086	\$ 225,977.27	Aug. 16, 2019	73.71%	66.37%	\$ 149,975.81	\$ 76,001.46	ON-GOING	
30	Laulara Solerema Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Marino Enterprises, Lda	SSS/115/MOPTC-2017	\$ 161,240.04	Sept. 7, 2017	100.00%	88.85%	\$ 143,267.06	\$ 17,972.98	ON-GOING	Projeito refere Atinji deit progreso 98.73% baseia ba Rekomendasaun ikus 2017. no agora Projeito Impristimo mak halo fali konstrusaun foun
31	Rural Road Periodik Maintenance Hero - Remexio Star 0+000 -10+400 Dili & Aileu Municipality / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Remexio	Aileu	Nautetu I, II Unipessoal Lda	MPW.W-1900081	\$ 494,544.48	Aug. 16, 2019	68.90%	62.04%	\$ 306,821.03	\$ 187,723.45	ON-GOING	
32	Road Rehabilitation of Remexio to Lacio Sta 0+000-20+000 Package I Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Remexio	Aileu	Mendith UnipLda	SSS/139/MOPTC-2017	\$ 2,567,345.51	Sept. 12, 2017	34.94%	30.98%	\$ 795,306.18	\$ 1,772,039.33	ON-GOING	
33	New MV Line ,Install New transformer & Extend LV line & New distribution Line from Simpang Tiga Lequidoe Tursai Aileu District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Lequidoe	Aileu	Cadila Supplie Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000163	\$ 240,048.46	Aug. 22, 2013	94.17%	84.76%	\$ 203,456.68	\$ 36,591.78	PENDENTE	Progresu Fisiku nafatin deit tamba laiha ona espasu atu kontinua tan obra ne'e.
34	R4D MPW Rural Roads rehabilitation Project in Aileu Bereleu manucasa Package 2 Sta. 3+500-13+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Lequidoe	Aileu	Seiara Irapiti Unip. Lda	MPWTC-W-015016	\$ 248,750.72	Sept. 7, 2015	97.45%	87.70%	\$ 218,159.90	\$ 30,590.82	ON-GOING	Projeito refere Atinji deit progreso 97.45% baseia ba Rekomendasaun ikus 2017. no agora Projeito Impristimo mak halo fali konstrusaun foun
35	R4D Rural Road Maintenance Fahisoi - Fadabloco Chainage 0+000 - 8+200, Namalesu - Faturilau Chainage 0+000 - 12+500, Fahisoi - Dairlouta Chainage 0+000 - 2+600 and Hautoho - Lequica Chainage 0+000 - 2+500 Municipality Aileu / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Lequidoe	Aileu	Emmanuel Milenial	MPW-W-190103	\$ 171,685.42	Aug. 21, 2019	64.64%	58.18%	\$ 99,884.64	\$ 71,800.78	ON-GOING	
36	Rural Roads Periodic Maintenance Aituhularan - Manufoni Chainage 0+000 - 1+000 and Daisoli - Fatubosa Chainage 0+000 - 7+300, Routine Maintenance Coula Udo Kirlelo Chainage 0+000 - 7+000 Municipality Aileu / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Lequidoe	Aileu	LNG Unip. Lda	MPW-W-190174	\$ 142,718.62	Nov. 25, 2019	92.82%	79.86%	\$ 113,980.68	\$ 28,737.94	ON-GOING	
37	For Preparation of Detailed Engineering Design For Rehabilitation of "municipio Roads" Package 8 : (Be' Cluru) to Lequidoe Town (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Lequidoe	Aileu	Team Consulting Engineering & Management Co., Ltd JV ATT Consultants Co., Ltd & Triangle Architech Consultant., Lda	MPW-CS-2000021	\$ 550,800.00	March 26, 2020	40.00%	70.00%	\$ 385,560.00	\$ 165,240.00	ON-GOING	



ANEXU A

MUNICIPIO AILEU (LISTA GERAL)

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVAUN
38	New Construction of Health Post and Doctor's House Buiding in Aileu, Lequidoe / Fatuberli, Timor Leste	MINISTERIO SAUDE	LM-CD	SAUDE	Lequidoe	Aileu	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-073	\$ 299,945.58	Sept. 6, 2021	21.36%	19.23%	\$ 57,670.93	\$ 242,274.65	ON-GOING	
TOTAL									\$ 82,212,796.25			71.79%	\$ 59,024,281.92	\$ 23,188,514.33		

Prepara Husi :

(Eng. Marcelino Amaral)
Engenheiro ba Projetu Insfrastuctura, Transportes e
Irigasaun Municipio Aileu,

(Eng. Merinho Cúco L. de Araujo)
Eng. ba Edificio Publiku no Be'e Saneamento
Municipio Aileu
ADN, I.P.

(Eng. Rui Lopes)
Engenheiro ba Projetu Insfrastuctura, Transportes e Irigasaun Municip
Aileu,
ADN .IP.

(Silvino D. R. R. Soares)
Eng. M & E, Municipiu Aileu, ADN, I.P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU AILEU

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Cumulative Progress (%)
1	Rehabilitation of Sloi Tocoluli roads Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Aileu-Vila	Aileu	Mendith UnipLda	SSS/061/MOPTK-2015	\$ 218,231.77	Nov. 14, 2014	100.00%	0.00%	100.00%
2	Rehabilitasaun Estrada Rural R4D Taliforleu - Kolihoho Chainage 0+000 - 8+000 Munisipiu Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Aileu-Vila	Aileu	Caviq Unipessoal Lda in joint venture with Sunnines Unip. Lda	NCB/020/MOP-2019	\$ 717,064.23	Dec. 20, 2019	45.85%	0.00%	45.85%
3	Road Climate Resilience Project (RCRP) Upgrading and Maintenance of Dili - ainaro Road (Lot 3 : Solerema - Bandudatu Section (Km 34+620 - 64+000)) Municipality Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Chongqing International Construction Corporation	ICB/010/MPW-2013	\$ 28,823,606.10	April 10, 2014	97.44%	0.00%	97.44%
4	Consultant Design & Supervision Lot 3	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Katahira and Engineers International	SSS/043/MPW-2014	\$ 4,069,793.04	Sept. 15, 2014	80.11%	0.00%	80.11%
5	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Aileu-Vila	Aileu	Kunhwa Engineering & Consulting Co., Ltd JV with Dongsung Engineering Co.,Ltd	RFP/020/MOPTC/2017	\$ 2,626,077.78	April 27, 2018	63.53%	0.00%	63.53%
6	Emergency Dili to Aileu Maubisse Roads	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Aileu-Vila	Aileu	My Friend Unip. Lda	MPW-W-014054	\$ 251,677.07	Oct. 5, 2014	100.00%	0.00%	100.00%
7	Rehabilitation of MSS Office in Aileu	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	LM-BS	SOLIDARIEDADE E SOCIAL	Aileu-Vila	Aileu	Borudo Matak	RDTL:47/MSS/DNPFA L-DAD/X/2016	\$ 47,720.63	Oct. 24, 2016	77.74%	0.00%	77.74%
8	Programma Turismo Komunitario 2014 Seloi / Malere	SEFOPE	LM-TP	TURISMO	Aileu-Vila	Aileu	Mirror Raefusa	RDTL/SEFOPE/DNA/D NE/2013-0003	\$ 227,981.87	May 5, 2014	91.20%	0.00%	91.20%
9	Preparation of Master Plan For Municipal Capitals Water Supply and Sanitation (Aileu-Gleno-Liquica) /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Aileu-Vila	Aileu	Jurutera Perunding Zaaba Sdn. Bhd (Malaysia)	MPW-CS-200028	\$ 827,410.00	May 1, 2020	10.00%	0.00%	10.00%
10	Realization of the Detailed Engeneering Design (DED) includes Reparation of Feasibility Study of the University of Aileu (Bem Serviso)	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA	LM-BS	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Aileu-Vila	Aileu	Bernabad Arquitectura SLP	MPW-S-200024	\$ 475,000.00	March 31, 2020	9.16%	0.00%	9.16%
11	New Construction of laboratory for covid 19 at CHC Aileu Vila	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Aileu-Vila	Aileu	Jomy Unipessoal Lda	RDTL-MS-DNA-DC-20-257	\$ 62,128.32	Nov. 4, 2020	94.67%	0.00%	94.67%
12	Konstrusaun, Vedasaun no Jardim ba Edificio DTPSC	Ministerio da Justica	LM-CD	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Kablaki Engineering Unip. Lda		\$ 200,000.00	1-Jul-12	89.19%	0.00%	89.19%
13	Consultancy services for National Road No. 1 - Upgrading Project	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA-IMPRESTIMO	Aileu-Vila	Aileu	Philcoei International, Inc. In JV with Luis and Associates, Co	nn	\$ 5,835,991.00	Jan. 18, 2013	83.00%	0.00%	83.00%
14	New Construction of Isolation Building	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Mortiles Unip.Lda	RDTL-MS-DNA-DC-20-255	\$ 281,137.18	Nov. 04, 2020	90.47%	0.00%	90.47%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU AILEU

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Comulative Progress (%)
15	New Construction of Campas, Gate And Leveling	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTACAO NACIONAL	LM-CD	SOLIDARIEDADE E SOCIAL	Aileu-Vila	Aileu	Caramé Unip, Lda	No.: 37/MACLN/IX/2021	\$ 118,769.70	9/1/2021	0.00%	44.58%	44.58%
16	Perfurasun Bee Mos Iha Selo Ba Fatin Turismo Komunitariu	MINISTERIO DAS OBRAS PUBLICAS	PDIM	AGUA E SANEAMENTO	Aileu-Vila	Aileu	Alenta Unip. Lda	48/SMA/AM-AIL/VIII/2021	\$ 34,864.82	Aug. 6, 2021	7.66%	11.39%	19.05%
17	Konstrusaun Intake inklui Bareira Protege Lagoa Selo Kraik iha Aileu Vila	ESTATAL	PDIM	FLOOD CONTROL	Aileu-Vila	Aileu	Aisel Girasol Unip. Lda	004/MAE/AM-AIL/SMA/IX/2021	\$ 26,311.39	Aug. 6, 2021	22.84%	0.00%	22.84%
18	Konstrusaun Edificio Posto Administrativo Lequidoe	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Fitun Foun, Unip Lda	002/MAE/AM-AIL/SMA/IX/2021	\$ 128,221.80	Aug. 6, 2021	14.98%	0.00%	14.98%
19	Konstrusaun Edifisiu Posto Administrativu Aileu Vila	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Aileu-Vila	Aileu	Diborna Unip. Lda	001/MAE/AM-AIL/SMA/IX/2021	\$ 144,735.62	Aug. 6, 2021	20.74%	3.00%	23.75%
20	Konstrusaun Bronjong Proteje Uma Comunidade no Uma Madres Caridade Inklui Toós Comunidade	ESTATAL	PDIM	FLOOD CONTROL	Aileu-Vila	Aileu	JOHIJEMAR Unip,Lda	005/MAE/AM-AIL/SMA/IX/2021	\$ 61,880.06	Aug. 6, 2021	30.18%	0.00%	30.18%
21	Konstrusaun Bronjong Protege Igreja Assembleia de Deus no Uma Comunidade	ESTATAL	PDIM	FLOOD CONTROL	Aileu-Vila	Aileu	Padua Unip. Lda	006/MAE/AM-AIL/SMA/IX/2021	\$ 49,110.53	Aug. 6, 2021	84.81%	0.00%	84.81%
22	New Install New Transformer & Extend LV Line & New distribution Line from Madabeno to Sarlala Aileu District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laulara	Aileu	Aldepo Murak Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000162	\$ 462,154.02	Aug. 22, 2013	81.19%	0.00%	81.19%
23	Installation New MV Line,transformer & Extend LV Line & distribution Line from Lebukuku to Besilau and Fatuk Hun - Aileu District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laulara	Aileu	osxavijoneli unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000179	\$ 298,866.88	Aug. 22, 2013	81.53%	0.00%	81.53%
24	Rehabilitation of Beducu Sarlala Roads (Ex. Japan) Sta. 6+300 - Sta. 8+968.45	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Mejori, Lda	SSS/0103/MOPTC-2016	\$ 4,451,281.98	Sept. 5, 2016	94.19%	4.78%	98.97%
25	Road Rehabilitation project, Sarlala - Bemós - Manleuana - Timor block link, Package 1: Sta. 0+000 - Sta. 2+800	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Aspalink Unip Lda	SSS/120/MOPTC-2015	\$ 4,128,651.62	Dec. 11, 2015	100.00%	0.00%	100.00%
26	Road Rehabilitation project, Sarlala - Bemós - Manleuana - Timor block link, Package 1: Sta. 2+800 - Sta. 6+300	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Jonize Construction, Unip. Lda	SSS/121/MOPTC-2015	\$ 4,645,457.43	Dec. 11, 2015	100.00%	0.00%	100.00%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU AILEU													
LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Comulative Progress (%)
27	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620) Municipality Aileu	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Laulara	Aileu	CINA WU YI CO.LTD	ICB/018/MOPTC-2017	\$ 17,855,301.27	May 31, 2019	79.61%	0.00%	79.61%
28	Rural Roads Maintenance Fahisohi - Fadabloko Sta 0+000-8+200, Hotoho - Liquica Sta 0+000 - 2+500 and Laulara - Ornai Sta 0+000 - 7+500 in Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Laulara	Aileu	Remexio Furak Unip Lda	MPWTC-CD-170004	\$ 40,314.04	July 20, 2017	100.00%	0.00%	100.00%
29	R4D Rural Roads Periodic Maintenance Laulara - Ornai Chainage 0+000 - 8+000 Routine Maintenance Madabeno - Lisimori Chainage 0+000 - 4+900 and Acumau - Aicorema Chainage 0+000 - 2+000 Municipality Aileu / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laulara	Aileu	Fin Los unip.lida	MPW-W190086	\$ 225,977.27	Aug. 16, 2019	61.68%	12.03%	73.71%
30	Laulara Solerema Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Laulara	Aileu	Marino Enterprises, Lda	SSS/115/MOPTC-2017	\$ 161,240.04	Sept. 7, 2017	100.00%	0.00%	100.00%
31	Rural Road Periodik Maintenance Hero - Remexio Star 0+000 -10+400 Dili & Aileu Municipality / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Remexio	Aileu	Nautetu I, II Unipessoal Lda	MPW.W-1900081	\$ 494,544.48	Aug. 16, 2019	51.03%	17.87%	68.90%
32	Road Rehabilitation of Remexio to Lacro Sta 0+000-20+000 Package I Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Remexio	Aileu	Mendith UnipLda	SSS/139/MOPTC-2017	\$ 2,567,345.51	Sept. 12, 2017	34.94%	0.00%	34.94%
33	New MV Line ,Install New transformer & Extend LV line & New distribution Line from Simpang Tiga Lequidoe Tursai Aileu District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Lequidoe	Aileu	Cadila Supplie Unip,Lda	RDTL/MOP-SEE/CGI-PEN : 0000163	\$ 240,048.46	Aug. 22, 2013	94.17%	0.00%	94.17%
34	R4D MPW Rural Roads rehabilitation Project in Aileu Bereleu manucasa Package 2 Sta. 3+500-13+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Lequidoe	Aileu	Seiara Irapiti Unip. Lda	MPWTC-W-015016	\$ 248,750.72	Sept. 7, 2015	97.45%	0.00%	97.45%
35	R4D Rural Road Maintenance Fahisoi - Fadabloko Chainage 0+000 - 8+200, Namalesu - Faturilau Chainage 0+000 - 12+500, Fahisoi - Dairilouta Chainage 0+000 - 2+600 and Hautoho - Lequica Chainage 0+000 - 2+500 Municipality Aileu / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Lequidoe	Aileu	Emmanuel Milenial	MPW-W-190103	\$ 171,685.42	Aug. 21, 2019	64.64%	0.00%	64.64%
36	Rural Roads Periodic Maintenance Aituhaularan - Manufoni Chainage 0+000 - 1+000 and Daisoli - Fatubosa Chainage 0+000 - 7+300, Routine Maintenance Coula Udo Kirelo Chainage 0+000 - 7+000 Municipality Aileu / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Lequidoe	Aileu	LNG Unip. Lda	MPW-W-190174	\$ 142,718.62	Nov. 25, 2019	92.82%	0.00%	92.82%
37	For Preparation of Detailed Engineering Design For Rehabilitation of "municipio Roads" Package 8 : (Be' Cluru) to Lequidoe Town (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Lequidoe	Aileu	Team Consulting Engineering & Management Co., Ltd JV ATT Consultants Co., Ltd & Triangle Architech Consultant., Lda	MPW-CS-2000021	\$ 550,800.00	March 26, 2020	40.00%	0.00%	40.00%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU AILEU													
LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Comulative Progress (%)
38	New Construction of Health Post and Doctor's House Buiding in Aileu, Lequidoe / Fatuberli, Timor Leste	MINISTERIO SAUDE	LM-CD	SAUDE	Lequidoe	Aileu	Kartini Unipessoal Lda	RDTL-MS-DNA-ICB-21-073	\$ 299,945.58	Sept. 6, 2021	0.00%	21.36%	21.36%

Prepara Husi :

(Eng. Marcelino Amaral)

Engineiro ba Projetu Insfrastuctura, Transportes e Irigasaun Municipio Aileu, ADN .IP.

(Eng. Rui Lopes)

Engineiro ba Projetu Insfrastuctura, Transportes e Irigasaun Municipio Aileu, ADN .IP.

(Eng. Merinho Cúco L. de Araujo)

Eng. ba Edifício Publiku no Be'e Saneamento Municipio Aileu ADN, I.P.

(Silvino D. R. R. Soares)

Eng. M & E, Municipio Aileu, ADN, I.P.

(Eng. Aniceto da Costa)

Engenheiro Senior ba Projecto Infraestrutura, Transportes e Irigasaun, ADN I.P.

(Deolindo de F. Marques)

Chefe Sec. Projeto M.E & ITC, ADN, I.P.

(Arch Francisco Xavier de Deus Jeronimo)
Engenheiro Senior ba Edifício Publiku no Be'e Saneamento ADN, I.P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)

Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.
