



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL
IMPLEMENTASAUN
PROJETUS MUNISÍPIU LIQUICA

NOVEMBRO 2022




SUMÁRIO

RELATÓRIO


IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO LIQUICA NOVEMBRO 2022


Prepara Husi :


(Eng. Juninho Antonio A. Da Cruz)
Eng. ba Edifício Público no Beé Saneamento,
Município Liquica ADN, I.P



(Eng. Antonia de Fatima Moraes)
Eng. ba Edifício Público no Beé Saneamento,
Município Liquica ADN, I.P



(Eng. Marcus Ximenes de Araujo)
Eng. ba Projeto Infraestrutura, Transporte e
Irigação, Município Liquica ADN, I.P



(Eng. Geovanio M.X. Carlos Aleixo)
Eng. ba Projeto Infraestrutura, Transporte e
Irigação, Município Liquica ADN, I.P


(Eng. Camilio de Jesus)
Eng. ba Projeto ME Município Liquica
ADN, I.P

Verifica Husi :


(Arc. Francisco X D D Jeronimo)
Eng. Senior ba Edifício Público no Beé
Saneamento, ADN, I.P


(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba Projeto Infraestrutura e
Irigação, ADN, I.P


(Deolindo de Fatima Marques)
Chefe Seksaun ba Projeto M. E & ITC, ADN, I.P

Sertifica Husi :


(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade,
ADN, I.P

Aprova Husi :


(Mariano Renato Monteiro da Cruz, S. T. M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO	1
I. INTRODUSAUN.....	3
1.1 Enkuadramentu Legal.....	3
1.2 Perfil Municipio Liquica	3
1.3 Lista Projecto	7
II. PROGRESU FISIKU	18
2.1 Progreso Fisiku Kada Fulan	18
III OBSTÁKLU IHA TERENU	18
3.1 Obstáculo Servisu Iha Terenu.....	18
VI. REKOMENDASAUN IHA TERENU	19
4.1 Rekomendasaun Servisu iha Terenu	19

INDICE TABELA

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica	5
Tabela 1. 2: Lista Asset ADN,I.P Municipio Liquica	5
Tabela 1.3. 1 Projecto Municipio Liquica Por Fundus Financiamento.....	7
Tabela 1.3. 2 Projecto Municipio Liquica Por Sectores.....	9
Tabela 1.3. 3 Projecto Municipio Liquica Por Ministerios.....	14
Tabela 4. 1 Dadus Populasaun Munisipiu Liquica	18

I. INTRODUSAUN.


1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu aseguira katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefisiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizaun no sertifikasaun kualidade ba Projeto sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Liquica

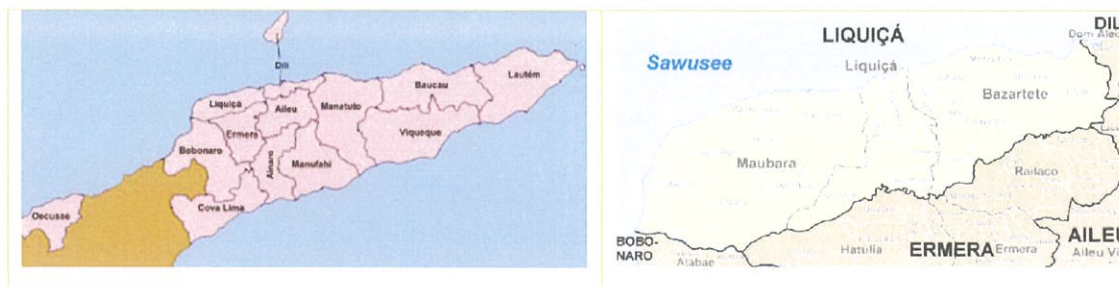

Mapa hatudu pozisaun Administrasaun Munisipal Liquica iha luan area 543 km² ho populasau nain – 63.403 tuir Sensus 2010. Administrasaun Munisipal Liquica iha Postu Administrativu tolu (3) , Sukus 23 no aldeias 134, mak hanesan hatudu iha Tabela 1

Tabela 1: Postos Administrativos, Sucos no Aldeias.

Bazartete		Liquica		Maubara	
sukus	Aldeias	Sukus	Aldeias	Sukus	Aldeias
Fahilelo	3	Açumano	4	Gugleur	11
Fatumasi	4	Darulete	4	Guiço	5
Lauhata	5	Dato	10	Lissadila	7
Leorema	10	Hatuquesi	8	Maubaralissa	5
Maumeta	4	Leotala	5	Vatuboro	5
Metagou	3	Loidahar	4	Vatuvou	10
Motaulun	3	Luculai	4	Vaviquinia	7
Tibar	4	-	-	-	-
Ulmera	9	-	-	-	-
Total	45	-	39	-	50

Data husi: Livro 3B OJE 2021, pag 58

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica

Força de Trabalho ADN, I.P Municipio Liquica								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro		2				2	
2	Administrasaun no Financas		0				0	
3	Motorista		1				1	
4	Seguransa		0				0	
Total			3				3	

Tabela 1. 2 : Lista Asset ADN,I.P Municipio Liquica

ASSET ADN,IP MUNICIPIO LIQUICA								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio		1					
2	Kareta		1					
3	Desktop HP / Monitor		1					
4	Laptop HP		1					
5	Printer Cannon		1					
6	UPS		1					
7	Armario File		1					
8	Armario Tau hena		3					
9	Meja escritorio		1					
10	Meja han		1					
11	Meja TV (kiik)		1					
12	Kadeira escritorio		6					
13	Kadeira han		4					

14	Sofa		1 Set					
15	Springbed +sumasu 4+sprei 3		3 Set					
16	Jeleira		1					
17	Water Dispenser		1					Aát
18	TV + Parabola		1 Set					
19	AC		4					
20	Kipas Angin		1					
21	Kompor		1					
22	Kompor Gas		1					
23	Rack sepatu		3					
24	Rack Piring		1					
25	Lampu		11					
26	Water Pump Sanyo		0					

1.3 Lista Projecto

Projeto hotu ne'ebe akumula iha lista ne'e bazeia ba dadus Projeto nebe sei lao hela no mos Projeto nebe abandona ona iha tinan barak nia laran, Projeto hirak ne'e fahe tuir lista tabela 1.3.1 Projeto Por Fundus Financiamento, Tabela 1.3.2 Projeto Por Sector no tabela 1.3.3 Projeto Por Ministerio, no lista detallu kada Projeto bele hare iha #Aneksu A.

Tabela 1.3. 1 Projeto Municipio Liquica Por Fundus Financiamento



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM (CD + BS + TP + FUNDO COVID etc..) + EMERGENCY + PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	29	\$10,522,091.43	\$2,514,948.69	23.90%
2	LIQUICA VILA	27	\$6,542,041.94	\$2,970,589.17	45.41%
3	MAUBARA	21	\$12,770,126.24	\$9,190,085.35	71.97%
	Grand Total	77	\$29,834,259.61	\$14,675,623.21	49.19%

NO	POSTO ADMINISTRATIVO	FI			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	5	\$7,247,828.32	\$580,057.84	8.00%
2	LIQUICA VILA	6	\$4,029,707.85	\$2,101,349.13	52.15%
3	MAUBARA	7	\$10,886,608.70	\$8,562,990.98	78.66%
	Grand Total	18	\$22,164,144.87	\$11,244,397.95	50.73%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	LM -CD			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	7	\$834,783.75	\$259,426.98	31.08%
2	LIQUICA VILA	11	\$1,528,099.12	\$512,692.60	33.55%
3	MAUBARA	7	\$951,175.37	\$285,257.70	29.99%
	Grand Total	25	\$3,314,058.24	\$1,057,377.28	31.91%

NO	POSTO ADMINISTRATIVO	LM -BS			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	6	\$897,734.42	\$717,903.81	79.97%
2	LIQUICA VILA	3	\$332,370.82	\$241,807.82	72.75%
3	MAUBARA	2	\$344,450.27	\$175,003.84	50.81%
	Grand Total	11	\$1,574,555.51	\$1,134,715.47	72.07%

NO	POSTO ADMINISTRATIVO	LM -TP			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	\$289,002.61	\$47,279.70	16.36%
2	LIQUICA VILA	6	\$474,930.65	\$114,739.62	24.16%
3	MAUBARA	3	\$359,595.59	\$28,917.06	8.04%
	Grand Total	13	\$1,123,528.85	\$190,936.38	16.99%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	FUNDO - COVID			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	\$433,364.88	\$313,531.42	72.35%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	4	\$433,364.88	\$313,531.42	72.35%

NO	POSTO ADMINISTRATIVO	EMERGENCY			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	1	\$ 502,473.28	\$ 441,060.32	87.78%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	1	\$ 502,473.28	\$ 441,060.32	87.78%

NO	POSTO ADMINISTRATIVO	PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	2	\$ 316,904.17	\$155,688.62	49.13%
2	LIQUICA VILA	1	\$ 176,933.50		
3	MAUBARA	2	\$ 228,296.31	\$137,915.77	60.41%
	Grand Total	5	\$ 722,133.98	\$293,604.39	40.66%

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 2 Projeto Municipio Liquica Por Sectores



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA	2	\$91,877.21	\$80,662.08	87.79%
2	AGUA E SANEAMENTO	3	\$293,629.77	\$167,315.56	56.98%
3	EDIFICIOS PUBLICOS	2	\$210,635.04	\$-	0.00%
4	EDUKASAUN	19	\$2,649,444.03	\$580,570.33	21.91%
5	ELÉTRICIDADE	8	\$7,578,728.67	\$2,137,054.62	28.20%
6	ESTRADAS E PONTES	29	\$15,553,331.56	\$9,716,655.22	62.47%
7	MANUTENSAUN NO REHABILITASAUN	6	\$1,070,017.57	\$867,928.26	81.11%
8	PORTOS	1	\$1,394,750.00	\$657,275.92	47.12%
9	SAUDE	4	\$433,364.88	\$313,531.42	72.35%
10	SEGURANCA NASIONAL	1	\$58,107.88	\$50,129.80	86.27%
11	TURISMO	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		77	\$29,834,259.61	\$14,675,623.21	49.19%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA	2	\$91,877.21	\$80,662.08	87.79%
2	AGUA E SANEAMENTO	2	\$122,664.12	\$94,609.06	77.13%
3	EDIFICIOS PUBLICOS	1	\$154,189.34	\$-	
4	EDUKASAUN	7	\$783,470.96	\$227,878.84	29.09%
5	ELÉCTRICIDADE	2	\$5,296,850.84	\$449,325.76	8.48%
6	ESTRADAS E PONTES	9	\$3,016,113.87	\$742,093.93	24.60%
7	MANUTENSAUN NO REHABILITASAUN	1	\$565,452.33	\$556,717.80	98.46%
8	PORTOS				
9	SAUDE	4	\$433,364.88	\$313,531.42	72.35%
10	SEGURANCA NASIONAL	1	\$58,107.88	\$50,129.80	86.27%
11	TURISMO				
Grand Total		29	\$10,522,091.43	\$2,514,948.69	23.90%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA				
2	AGUA E SANEAMENTO				
3	EDIFICIOS PUBLICOS				
4	EDUKASAUN	8	\$1,334,526.87	\$185,858.66	13.93%
5	ELETRIFIKASAUN NASIONAL	3	\$1,490,077.80	\$1,051,453.57	70.56%
6	ESTRADA- IMPRESTIMO	10	\$1,818,122.03	\$764,790.56	42.06%
7	ESTRADAS	5	\$504,565.24	\$311,210.46	61.68%
8	FLOOD CONTROL	1	\$1,394,750.00	\$657,275.92	47.12%
9	MANUTENSAUN NO REHABILITASAUN				
10	PORTOS				
11	SAUDE				
	Grand Total	27	\$6,542,041.94	\$2,970,589.17	45.41%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	SECTOR	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	AGRICULTURA				
2	AGUA E SANEAMENTO	1	\$170,965.65	\$72,706.50	42.53%
3	EDIFICIOS PUBLICOS	1	\$56,445.70		
4	EDUKASAUN	4	\$531,446.20	\$166,832.83	31.39%
5	ELETRIFIKASAUN NASIONAL	3	\$791,800.03	\$636,275.29	80.36%
6	ESTRADA- IMPRESTIMO	10	\$10,719,095.66	\$8,209,770.73	76.59%
7	ESTRADAS				
8	FLOOD CONTROL				
9	MANUTENSAUN NO REHABILITASAUN				
10	PORTOS				
11	SAUDE	2	\$500,373.00	\$104,500.00	20.88%
	Grand Total	21	\$12,770,126.24	\$9,190,085.35	71.97%

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 3 Projeto Municipio Liquica Por Ministerios



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	3	\$387,568.54	\$ -	0.00%
2	MINISTERIO AGRICULTURA E PISCAS	3	\$139,176.53	\$118,527.60	85.16%
3	MINISTERIO DAS OBRAS PUBLICAS	43	\$24,171,989.95	\$12,768,585.45	52.82%
4	MINISTERIO DO INTERIOR	1	\$58,107.88	\$50,129.80	86.27%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	19	\$2,649,444.03	\$580,570.33	21.91%
6	MINISTERIO PLANU E ORDENAMENTU	1	\$99,484.80	\$82,502.69	82.93%
7	MINISTERIO SAUDE	4	\$433,364.88	\$313,531.42	72.35%
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN	1	\$1,394,750.00	\$657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		77	\$29,834,259.61	\$14,675,623.21	49.19%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	1	\$154,189.34	\$-	
2	MINISTERIO AGRICULTURA E PESCAS	2	\$91,877.21	\$80,662.08	87.79%
3	MINISTERIO DAS OBRAS PUBLICAS	13	\$8,901,596.36	\$1,760,243.86	19.77%
4	MINISTERIO DO INTERIOR	1	\$58,107.88	\$50,129.80	86.27%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	\$783,470.96	\$227,878.84	29.09%
6	MINISTERIO PLANU E ORDENAMENTU	1	\$99,484.80	\$82,502.69	82.93%
7	MINISTERIO SAUDE	4	\$433,364.88	\$313,531.42	72.35%
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
Grand Total		29	\$10,522,091.43	\$2,514,948.69	23.90%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	1	\$176,933.50		
2	MINISTERIO AGRIKULTURA E PESCAS	1	\$47,299.32	\$37,865.52	80.06%
3	MINISTERIO DAS OBRAS PUBLICAS	16	\$3,588,532.25	\$2,089,589.07	58.23%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	\$1,334,526.87	\$185,858.66	13.93%
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN	1	\$1,394,750.00	\$657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
Grand Total		27	\$6,542,041.94	\$2,970,589.17	45.41%

Dados Detallu Kada Projeto #Anexu A



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU (\$)	MONTANTE EZEKUSAUN (\$)	PERCENTAGEM EZEKUSAUN (\$)
1	ESTATAL	1	\$56,445.70	\$-	0.00%
2	MINISTERIO AGRICULTURA E PISCAS				
3	MINISTERIO DAS OBRAS PUBLICAS	14	\$11,681,861.34	\$8,918,752.52	76.35%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	4	\$531,446.20	\$166,832.83	31.39%
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANSPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$500,373.00	\$104,500.00	20.88%
Grand Total		21	\$12,770,126.24	\$9,190,085.35	71.97%

Dados Detallu Kada Projeto #Anexu A

Tabela 4. 1 : Dadus Populasaun Munisipiu Liquica

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Bazartete	31,983	9,158	9,039	7,089	6,697
Liquiça	25,334	6,978	7,348	5,672	5,337
Maubara	25,234	7,088	6,802	5,766	5,578

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi Progressu servisu nebe kompanha sira atinji iha fulan neé nia laran, husi lista nebe iha #Anexu B hatudu progressu aktual fulan ida neé ho nia persentagen servisu, montante aktual bazeia ba orsamento nebe hetan husi progressu fulan ida neé, ikus liu persentagen aktual fulan ida neé hatudu progressu fisiku komulativa husi porsento anterior no fulan ida neé nian, lista kompletu ba detalho bele hare iha #Anexu B, detallu ba Backup Fotografia #Anexu C1, Detallu ba Backup BoQ #Anexu C2 no Instrusaun servisu bele hare #Anexu D

III. OBSTÁKLU IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

Durante iha Fulan ida nia laran, problema nebe ami enjineiru municipio hasoru mak hanesan :

1. Projeto lao tarde
2. Companhia balun servisu la tuir spesifikasaun
3. Companhia balun servisu la iha Site Engineer
4. Difikuldade ba Ekpa ADN M.Liquica hasoru susar ba Be'e mos

VI. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu iha Terenu

1. Rekomenda ba Kompanhia sira servisu tuir spesifikasaun nebe iha ona
2. Rekomenda ba Kompanhia sira tenke iha Site Engineer iha terenu

Rekomenda ba ADN.I.P. Nacional liu-liu ba Superior sira hodi hare ba Edificio ADN.I.P.

Note : Assinatura Husi Enjineiru Municipio Liquica

Força de Trabalho ADN,I.P Municipio Liquica					
No	Deskrisaun	Identidade			
		Naran Kompletu e Asinatura	Nu. ID Card	Pozisaun	Fotografia
1	Enjineiru	 Juninho António A. Da Cruz	216	Enjineiru EPAS	
		 Marcus Ximenes de Araujo	172	Enjineiru ITI	
		 Geovânio M.X. Carlos. Aleixo	164	Enjineira ITI	

		 Antonia de Fatima Morais	241	Enjineira EPAS	
		 Camilio de Jesus	061	Enjineiru METIC	
2	Enjineira	 Nencia F.Ö. do Rêgo	173	Enjineira VEBD	
3	Motorista	 Rui Antonio Gaio	029	Motorista	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Novembro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVASAUN
1	New Installation MV/LV Line and House Connection for Bazartete Vila to Leorema -Bazartete Sub District-Liquica District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	BAZARTETE	LIQUICA	Mina Petro Leste Unip. Lda	RDTL-11004589	\$ 499,250.84		100.00%	90.00%	\$ 449,325.76	\$ 49,925.08	ABANDONA	
2	Rural Road Rehabilitation Metagou Bazartete 0+ 000 -3+ 000 & Periodic Maintenance Maumeta - Metagou Sta. 0+ 000 -7+ 000 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Banir Lema	MPW-W-190097	\$ 565,452.33	Aug. 14, 2019	100.00%	98.46%	\$ 556,717.80	\$ 8,734.53	FHO	Progreso Físico 100% e hela pagamento retensaun 10%
3	Novo Konstrusaun Edifício Escola Técnico Vocational (ES-TECVOC) Maumeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	BAZARTETE	LIQUICA	Vida Diak Unip. Lda	OD/600/PDIM/AM-LIQ/VIII/2019/02	\$ 162,714.83	Aug. 16, 2019	95.66%	95.66%	\$ 155,688.62	\$ 7,026.21	FHO	FHO iha Agosto 2022
4	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+ 000 -7+ 000 & Fahilebo - Fatumasi Chainage 0+ 000 -2+ 300 Routine Maintenance Fahilebo Bucumera Chainage 0+ 000 -5+ 500 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Lep Laco Dato	MPW-W-190111	\$ 73,270.51	Sept. 5, 2019	100.00%	97.90%	\$ 71,729.53	\$ 8,712.25	FHO	Progresu fizicamente 100 % e sei falta pagamento ba retensaun
5	Konstrusaun Morilha Foun Matadouro Tibar	MINISTERIO AGRICULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Manoko Unip. Lda	RDTL-MAP-PO2019-19726	\$ 23,950.17	Dec. 5, 2019	77.60%	69.84%	\$ 16,726.74	\$ 7,223.43	ON-GOING	Provezoramente servisu paradu hela
6	Konstrusaun Foun EBF Holugara Bazartete, Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	EDUKASAUN	BAZARTETE	LIQUICA	Milcha Unip Lda	(RFQ/19/029-Q-R)	\$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	\$ 24,910.52	\$ 42,582.17	ON-GOING	
7	Hamos Tangki Estasaun Tratamento Agua Residuals Elar Tibar / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Quloco Unipessoal Lda	Contract No. MOP-W-190184	\$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	\$ 12,106.37	\$ 11,072.90	ON-GOING	Provezoramente servisu paradu hela
8	New Water Supply of Bairos PNLT Liquica	MINISTERIO DO INTERIOR	FI	SEGURANCA NASIONAL	BAZARTETE	LIQUICA	Holuli Unipessoal, Lda	SSS/054/MI-2019	\$ 58,107.88	Nov. 29, 2019	86.27%	86.27%	\$ 50,129.80	\$ 10,484.57	FHO	
9	Konstrusaun Armagen Foun Matadouro	MINISTERIO AGRICULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Nasasobu	MAP-PO2019-19532	\$ 67,927.04	Dec. 5, 2019	94.12%	94.12%	\$ 63,935.34	\$ 17,617.77	FHO	Progresu fizicamente remata ona
10	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	\$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	\$ 44,268.56	\$ 22,289.34	ON-GOING	ongoing
11	New construction of isolation for covid 19 in liquica, Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	SENIZU UNIPESSOAL LDA	MS-DNA-NCB-20-163	\$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	\$ 212,156.22	\$ 31,211.86	PHO	Projeto refere hela retensaun (10%) e Fisiku iha Tereno atinji deit 96.86%
12	Kanalizasaun Be Mosho Sistema Gravitasaun Iha Aipelo-Liquica	MINISTERIO PLANU E ORDENAMENTU	LM-CD	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTAMENT	\$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	\$ 82,502.69	\$ 16,982.11	ON-GOING	Falla retensaun
13	Emergency Project For Tibar River	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Sali Magu Unipessoal Lda	RT/067/MOP-2021	\$ 502,473.28	Sept. 20, 2021	99.75%	87.78%	\$ 411,060.32	\$ 61,412.96	ON-GOING	ON-GOING
14	Konstrusaun Edifício Posto Administrativo Bazartete & Moru Haleu	ESTATAL	PDIM	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	Aquarius Construction Unip. Lda	02/SMA-AMU/PDIM VIII/2021	\$ 154,189.34	Aug. 31, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	
15	R4D Rural Road Spot Improvement Fahilebo- Bucumera Chainage 0+ 000-3+ 000	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Hatumeta Oan, Unip. Lda	MOP - CD-NCB-R-21030	\$ 149,732.87	Oct. 01, 2021	41.45%	29.06%	\$ 43,507.04	\$ 106,225.83	ON-GOING	
16	R4D Rural Road Spot Improvement Fahilebo - Fatumasi Chainage 0+ 000-2+ 300 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Hatumeta Oan, Unip. Lda	MOP - CD-RFQ - 21017	\$ 88,852.44	Oct. 01, 2021	19.17%	13.35%	\$ 11,862.47	\$ 76,989.97	ON-GOING	
17	R4D Rural Road Spot Improvement Libaloa - Fahilebo Chainage 0+ 000-7+ 000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Hatuleo Unip Lda	MPW-W-210144	\$ 88,425.80	Oct. 01, 2021	60.35%	35.54%	\$ 31,422.82	\$ -	ON-GOING	
18	Rural Road Spot Improvement Maumeta-Metagou- Bazartete Chainage 0+ 000 - 10+ 000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	CRAELEKI BEROOLI UNIPESSOAL LDA	MPW-W-210145	\$ 62,024.04	Oct. 01, 2021	30.43%	24.93%	\$ 15,463.72	\$ 46,560.32	ON-GOING	SEIDAIK REGISTO IHA SISTEMA
19	R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+ 000+ 6+ 500) Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	BAZARTETE	LIQUICA	TM Calleba Unip. Lda	MPW-W-210158	\$ 158,465.33	Oct. 01, 2021	44.80%	29.31%	\$ 46,445.75	\$ 112,019.58	ON-GOING	SEIDAIK REGISTO IHA SISTEMA
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Biamali Unipessoal Lda	RDTL-MS	\$ 65,271.32		97.21%	87.49%	\$ 57,106.64	\$ 8,164.68	ON-GOING	
21	Supply and Installation Connection for Isolation and Laboratory Building Maumeta Liquica	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	ZYC UNIPESSOAL LDA	RDTL-MS-C19-DNA-DC-21-228	\$ 58,167.58	1/11/2022	24.74%	0.00%	\$ -		ON-GOING	
22	Konstrusaun Foun ESTV Leorema - Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	BAZARTETE	LIQUICA	U-Rema Unip. Lda	NCB-15/MEID/DNA/2021	\$ 264,260.83	11/1/2021	35.45%	0.00%	\$ -		ON-GOING	
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJD PKRE EPE BAURA	-	\$ 9,072.12	10/15/2021	22.03%	0.00%	\$ -		ON-GOING	
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJD PKRE EPE ERMETA	-	\$ 86,365.84	10/15/2021	17.22%	23.28%	\$ 20,102.04	\$ 66,263.80	ON-GOING	
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJD PKRE EPE CASSAIT	-	\$ 78,250.89	10/15/2021	17.13%	0.00%	\$ -		ON-GOING	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Novembro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVASAUN
26	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	MEJO PKRE ESG-PARALELO	-	\$ 115,313.76	10/15/2021	16.00%	23.57%	\$ 27,177.66	\$ 88,136.10	ON-GOING	
27	Melhoramento no Supply Energia Elektridade husi Sub Stasaun Liquica ba Portu Tibar (Engineering Procurement Construction - Design, Supply, Installation, Testing and Commissioning Extension Transformer Bay Of the Existing 150/20kV Liquica Substation to Supply Power to Tibar Bay Port)	MINISTERIO DAS OBRAS PUBLICAS	FI	ELECTRICIDADE	BAZARTETE	LIQUICA	China Shandong International Economic And Technical Cooperation Group, LTD	RFP/054/MOP-2021	\$ 4,797,600.00	Dec. 16, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	
28	Supervision Consultant for Construction of Intersection in the Existing Dili - Liquica Road to Connect Access Road from Tibar Bay Port (National Road - A03) Sta. 0+ 000 - Sta. 0+ 620	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Lelo Engineering Unipessoal Lda	RFP/072/MOP-2021	\$ 154,000.00	Dec. 14, 2021	95.77%	52.34%	\$ 80,602.28	\$ 73,397.72	ON-GOING	
29	Construction of Intersection in the Existing Dili - Liquica Road to Connect Access Road from Tibar Bay Port (National Road-A03)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	BAZARTETE	LIQUICA	Aitula Construction, Lda	RT/070/MOP-2021	\$ 1,738,869.60	Dec. 1, 2021					ON-GOING	
30	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Naroman Mosu Dadaun Unip. Lda	MPW-W/190250	\$ 153,851.88	Dec. 5, 2019	100.00%	95.49%	\$ 146,911.62	\$ 6,940.26	FHO	Servisu iha Tereno remata tiha ona, sei hein kompanha Amenda kontratu nebe mate tiha ona
31	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	MINISTERIO TRANSPORTES E KOMUNIKASAUN	FI	PORTOS	LIQUICA VILA	LIQUICA	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	\$ 1,394,750.00	May 17, 2017	100%	47.12%	\$ 657,275.92	\$ 737,474.08	ON-GOING	
32	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+ 000 - 4+ 300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+ 000 - 12+ 300 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Nheu	MPW-W/RFO-190093	\$ 55,012.05	Aug. 22, 2019	100%	99.91%	\$ 54,964.83	\$ 5,543.70	FHO	Projeto refere hela retensaun (10%) e Fisku iha Tereno atinji deit 99.91%
33	Rural Roads Periodic Gunaba - Lukulai Chainage 0+ 000 & Metagou - Aibenu Chainage 0+ 000 - 7+ 600 Rutine Maintenance Taltabi - Kutulau Chainage 0+ 000 - 1+ 700 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Goubara Unip Lda	MPW-W-190096	\$ 71,468.49	Aug. 19, 2019	92.32%	100.00%	\$ 71,468.49	\$ 7,146.85	FHO	
34	New Installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELECTRICIDADE	LIQUICA VILA	LIQUICA	Maferdi, Lda	RD/L/MOPTC-V/MOPTC/CG-PEN : 00000399	\$ 593,093.80	Jan. 6, 2017	92.77%	95.29%	\$ 565,173.15	\$ 27,920.65	FHO	
35	New Installation of MV, LV Line and House Connection from Liquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELECTRICIDADE	LIQUICA VILA	LIQUICA	Busa Lda	RD/L/MOPTC-V/MOPTC/CG-PEN : 00000371	\$ 276,484.00	July 6, 2016	80.84%	83.49%	\$ 230,841.25	\$ 45,642.75	ON-GOING	
36	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+ 000 - 5+ 000 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	15 Raelli Unip. Lda	RT/034/MOP-2019	\$ 452,362.93	Dec. 20, 2019	97.15%	86.79%	\$ 392,619.64	\$ 59,743.29	ON-GOING	
37	Manutensaun Kanais Irrigasaun Faulara - Liquica	MINISTERIO AGRICULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Banir Lema Unip.Lda	RD/L 0000	\$ 47,299.32	Aug. 18, 2021	88.95%	80.06%	\$ 37,865.52	\$ 9,433.80	PHO	
38	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	01/SMA-AMU/PDIM VIII/2021	\$ 176,933.50	Aug. 31, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	
39	R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chainage 0+ 000-2+ 500	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	\$ 131,219.62	Oct. 01, 2021	48.18%	43.46%	\$ 57,030.68	\$ 74,188.94	ON-GOING	
40	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+ 000-1+ 700, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	\$ 123,631.72	Oct. 01, 2021	61.00%	34.51%	\$ 42,662.88	\$ 80,968.84	ON-GOING	
41	R4D Rural Road Spot Improvement Metagou - Aibenu Chainage 0+ 000-7+ 600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	MOP - CD - NCB - R - 21038	\$ 238,739.71	Oct. 01, 2021	40.21%	0.00%	\$ -	\$ -	ON-GOING	
42	R4D Rural Road Spot Improvement Dato - Loidahar Chainage 0+ 000-12+ 300, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Luqueli Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	\$ 188,589.13	Oct. 01, 2021	51.00%	34.78%	\$ 65,594.85	\$ 122,994.28	ON-GOING	
43	R4D Rural Road Spot Improvement Aibenu - Asumanu - Leurema Chainage 5+ 000 - 10 + 000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Calulu, Unip Lda	MOP - CD - NCB - R - 21035	\$ 162,215.27	Oct. 01, 2021	54.94%	26.60%	\$ 43,152.43	\$ 119,062.84	ON-GOING	
44	R4D Rural Road Spot Improvement Aibenu - Asumanu-Leorema Chainage 0+ 000-5+ 000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	\$ 165,363.43	Oct. 01, 2021	45.83%	39.81%	\$ 65,827.42	\$ 99,536.01	ON-GOING	
45	R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chainage 2+ 500-5+ 400	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Qaridade Unip.Lda	MPW-W-210163	\$ 167,071.89	Oct. 01, 2021	30.65%	23.41%	\$ 39,104.89	\$ 127,967.00	ON-GOING	
46	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+ 000-2+ 000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Craeleki Bercoli, Unip Lda	MPW-W-210143	\$ 76,423.05	Oct. 01, 2021	40.74%	34.35%	\$ 26,250.43	\$ 50,172.62	ON-GOING	
47	Projeto Konstrusaun foun ESG publico 01 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	LIQUICA VILA	LIQUICA	Roman Furak Unip.Lda	NCB 16/MEJD/DNA/2021	\$ 167,079.099	Nov. 1, 2021	47.70%	42.57%	\$ 71,119.04	\$ 95,960.05	ON-GOING	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Novembro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVASAUN
48	For Roads Maintenance Section : Tibar - Liquica - Maubara, Carimbala - Loes (A03)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	LIQUICA VILA	LIQUICA	Chanel Chander Unipessoal Lda	MPW-W-210202	\$ 112,505.280	12/13/2021	32.14%	28.93%	\$ 32,547.34	\$ 79,957.94	ON-GOING	
49	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRE EBC MAUBOQUE	-	\$ 112,530.010	10/15/2021	17.42%	25.45%	\$ 28,640.50	\$ 83,889.51	ON-GOING	
50	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRE EBC 1,2,3 LIQUICA	-	\$ 99,456.040	10/15/2021	23.22%	23.22%	\$ 23,094.93	\$ 76,361.11	ON-GOING	
51	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRE EPE LOIDAHAR	-	\$ 79,735.630	10/15/2021	25.63%	25.63%	\$ 20,432.50	\$ 59,303.13	ON-GOING	
52	Konstrusaun ka Reabilitasaun ba EBF 1,2 Lactolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRE Ebf 1,2 LACTOLEMA	-	\$ 89,650.660	10/15/2021	14.62%	22.88%	\$ 20,511.00	\$ 69,139.66	ON-GOING	
53	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRE EBF 1,2 TOLEMA	-	\$ 88,407.020	10/15/2021	22.24%	24.95%	\$ 22,060.69	\$ 66,346.33	ON-GOING	
54	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	MEJD PKRE EBF 1,2 LUCULAI	-	\$ 5,151.290	10/15/2021	45.13%	0.00%	\$ -	\$ -	ON-GOING	
55	Consultant Services to Supervise EPC Contractor for the Up-Gradation of Liquica 150/20kV Substation to Supply Power to Tibar Bay Port	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	LIQUICA VILA	LIQUICA	PT. Artefak Arkindo (Indonesia) JV with Jazcasnu Unipessoal Lda	RFP/054/MOP-2021	\$ 620,500.000	Dec. 16, 2021	23.33%	41.17%	\$ 255,439.17	\$ 365,060.83	ON-GOING	
56	New Construction of "Escola CAPE" Building at Liquica Municipality	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	LIQUICA VILA	LIQUICA	RCS Unipessoal Lda	NCB/138/MEJD-2021	\$ 692,517.120	June 8, 2022						
57	Addt. Poste liga Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	MAUBARA	LIQUICA	Fu Unip. Lda	RDTL - 0000	\$ 13,000.00	Jan. 1, 2016	0.00%	0.00%	\$ -	\$ 13,000.00	ON-GOING	Kontratu ladaukiha no fiziku la eziste
58	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	MAUBARA	LIQUICA	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/OG-PEN : 00000364	\$ 288,760.22	July 6, 2016	83.73%	75.36%	\$ 217,606.07	\$ 71,154.15	ON-GOING	
59	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	MAUBARA	LIQUICA	Montana Diak, Unipessoal, Lda	SSS/126/MOPTC-2017	\$ 1,901,334.67	Sept. 7, 2017	99.98%	99.98%	\$ 1,900,879.16	\$ 455.51	PHO	
60	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	\$ 275,000.00	Dec. 27, 2016	0.00%	0.00%	\$ 104,500.00	\$ 170,500.00	ON-GOING	ADN, I.P la hare
61	Novo Konstrusaun Edificio ESTV Lisadila	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	MAUBARA	LIQUICA	Aleni Unip. Lda	OD/600/DPIM/AM-LIQ/VIII/2019/03	\$ 171,850.61	Aug. 16, 2019	89.17%	80.25%	\$ 137,915.77	\$ 33,934.84	ON-GOING	
62	Rehabilitasaun Sistema be'le mosiha aldeia Pandevou ho Mau-Uno, Sucu Guico /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	MAUBARA	LIQUICA	Oceania Const Unip. Lda	NCB-MOP-190051	\$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	\$ 72,706.50	\$ 98,259.15	ON-GOING	Provizoriamente paradu hela
63	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS E PONTES	MAUBARA	LIQUICA	Dongsung Engineering Co.,Ltd JV with Kunhwa Engineering and Consulting Co.,Ltd.	RFP/038/MOPTC/2016	\$ 7,693,101.00	May 3, 2017	76.97%	76.97%	\$ 5,921,336.53	\$ 1,771,764.47	ON-GOING	
64	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+ 000 - 5+ 400 Nunuleta - Darulema Chainage 0+ 000 - 1+ 600 Vaviquina - Maubalisa Chainage 0+ 000 - 12+ 500	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Luliana Unip. Lda	MPW-W-190098	\$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	\$ 43,761.73	\$ 6,940.86	PHO	
65	Konstrusaun Moru Haleu no Posto Sguransa ba Edificio Posto Administrativo Maubara	ESTATAL	PDIM	EDIFICIOS PUBLICOS	MAUBARA	LIQUICA	Rafio Unip. Lda	01/AMU/SMA-PDIM/VIII/2021	\$ 56,445.70	July 21, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ADN, I.P La Hare
66	R4D Rural Road Spot Improvement Nunuleta - Darulema Chainage 0+ 000-2+ 000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Rito -Pu, Unipessoal Lda	MOP -CD-RFO - 21013	\$ 67,382.23	Oct. 01, 2021	2.07%	0.00%	\$ -	\$ -	ON-GOING	
67	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 4+ 800-9+ 600	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Malibo, Unipessoal LDA	MOP - CD - NCB-R- 21033	\$ 152,622.90	Oct. 01, 2021	35.83%	25.75%	\$ 39,294.58	\$ 113,328.32	ON-GOING	
68	R4D Rural Road Spot Improvement Barkau (Vaviquina)-Maubalisa Chainage 0+ 000-4+ 200	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS E PONTES	MAUBARA	LIQUICA	Nheu, Unipessoal LDA	MOP - CD - NCB-R- 21027	\$ 173,484.62	Oct. 01, 2021	45.61%	58.97%	\$ 102,297.34	\$ 71,187.28	ON-GOING	
69	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+ 000-4+ 800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Murak, Unipessoal Lda	MPW-W-210157	\$ 153,049.85	Oct. 01, 2021	43.43%	27.12%	\$ 41,501.12	\$ 111,548.53	ON-GOING	
70	R4D Rural Road Spot Improvement Barkau (Vaviquina) - Maubalisa, Chainage 8+ 400-12+ 500)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Meta Lee Crae Bau Unip. Lda	MPW-W-210160	\$ 198,698.25	Oct. 01, 2021	44.41%	39.89%	\$ 79,267.01	\$ 119,431.24	ON-GOING	
71	R4D Rural Road Spot Improvement Samarapo - Gsu Chainage 0+ 000-2+ 000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Nazico Unip. Lda	-	\$ 114,789.50	Oct. 01, 2021	11.39%	24.71%	\$ 28,362.37	\$ 86,427.13	ON-GOING	
72	R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubalisa Chainage 4+ 200-8+ 400)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS E PONTES	MAUBARA	LIQUICA	Luliana Unip. Lda	MPW-W-210161	\$ 213,930.25	Oct. 01, 2021	34.86%	24.81%	\$ 53,070.89	\$ 160,859.36	ON-GOING	



#ANEXO A

Lista Geral Projeto On-going Municipio Liquica - Novembro 2022

NU	NARAN PROJETO	DONO PROJETO	KATEGORIA PROJETO	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJECT	OBSERVA SAUN
73	Konstrusaun ka Reabilitasaun ba EBF Galiana	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	MEJD PKRIE EBF GARIANA	-	\$ 117,902.04	Oct. 15, 2021	1.98%	0.00%	\$ -	\$ -	ON-GOING	
74	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	MEJD PKRIE EBF TAPO MANUHULU	-	\$ 100,033.33	Oct. 15, 2021	10.61%	0.00%	\$ -	\$ -	ON-GOING	
75	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	MEJD PKRIE ESG-PARALELO MAUBARA/BATUVOU	-	\$ 141,660.22	Oct. 15, 2021	14.14%	20.41%	\$ 28,917.06	\$ 112,743.16	ON-GOING	
76	Feasibility study for New Construction of Industrial Park in Liquica, Timor Leste	MINISTERIO TURISMO KOMERGO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	HABERAN UNIPESSOAL LDA (TIMOR LESTE) in Joint Venture with PT ITS TEKNO SAINS (INDONESIA)	RFP/077/MTQ-2021	\$ 225,373.00	March 24, 2022					ON-GOING	
77	Installation foun ba Linha de Media Tensaun, Baixa Tensaun e Baixadas em Liquica - Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELÉCTRICIDADE	MAUBARA	LIQUICA	Nia construction, Lda	0000	\$ 490,039.81	Dec. 4, 2012	94.93%	85.44%	\$ 418,669.22	\$ 71,370.59	ON-GOING	
TOTAL									\$ 29,834,259.61				\$ 14,675,623.21	49.19%		

PREPARA HUSI,

(Eng. Marcus Ximeres de Araujo)
Eng. ba Projeto Infraestrutura Transporte e Irigasaun, ADN, I.P.

VERIFIKA HUSI,

(Eng. Remigio da C.S.dos Santos)
Engineru Senior ba Projeto Infraestrutura Transporte e Irigasaun ADN, I.P.

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

(Eng. Juninho Antonio A. da Cruz)
Eng. ba Edificio Publiku Agua e

(Arg. Francisco Xavier D. D. Jeronimo)
Engineru Senior ba Projeto Edificio Publiko no Be'e Saneamento ADN, I.P.

(Eng. Deolinda de Fatima Marques)
Chefe Seksaun Mekanikal e Elektrikal & ITC ADN, I.P.

(Eng. Antónia de Fatima Moraes Soares)
Engineru ba Edificio Publiku Agua e Saneamento ADN, I.P.

(Eng. Ludovina Maria Helena Guterres)
Engineru ba Projeto Infraestrutura Transporte e Irigasaun ADN, I.P.

(Eng. Camilio de Jesus)
Eng. Mekanikal e Elektrikal ADN, I.P.



#ANEXO B

PROGRESSU FISIKU FULAN NOVEMBRO MUNICIPIO LIQUICA

												Nov-22		
NU	NARAN PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVASAUN			
1	New Installation MV, LV Line and House Connection for Bazartete Vila to Leorema -Bazartete Sub District-Liquica District	Mina Petro Leste Unip. Lda	RDTL-11004589	\$ 499,250.84	Oct. 1, 2020	100.00%	90.00%	\$ 449,325.76	\$ 49,925.08	ABANDONA				
2	Rural Road Rehabilitation Metagou Bazartete 0 + 000 - 3 + 000 & Periodic Maintenance Maumeta - Metagou Sta. 0 + 000 - 7 + 000 Municipality Liquica	Banir Lema	MPW-W-190097	\$ 565,452.33	Aug. 14, 2019	100.00%	88.61%	\$ 501,046.02	\$ 64,406.31	PHO	PHO			
3	Novo Konstrusaun Edifício Escola Técnico Vocacional (ES-TECVOC) Maumeta)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	\$ 162,714.83	Aug. 16, 2019	95.68%	86.11%	\$ 140,119.76	\$ 22,595.07	ON-GOING	PHO	95.68%	0.00%	95.68%
4	R4D Rural Road Periodic Maintenance Libaloa - Fahliebo Chainage 0 + 000 - 7 + 000 & Fahliebo - Fatumasi Chainage 0 + 000 - 2 + 300 Routine Maintenance Fahliebo Bucumera Chainage 0 + 000 - 6 + 500 Municipality Liquica	Lep Laco Dato	MPW-W-190111	\$ 73,270.51	Sept. 5, 2019	100.00%	88.11%	\$ 64,558.26	\$ 8,712.25	PHO	PHO			
5	Konstrusaun Moraiha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019-19726	\$ 23,950.17	Dec. 5, 2019	77.60%	69.84%	\$ 16,726.74	\$ 7,223.43	ON-GOING	Provezoriamente servisu paradu hela	77.60%	0.00%	77.60%
6	Konstrusaun Foun EBF Hotugara Bazartete, Liquica	Milcha Unip Lda	(RFQ-19/029-Q-R)	\$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	\$ 24,910.52	\$ 42,582.17	Parado	Parado	41.01%	0.00%	41.01%
7	Hamos Tangki Estasaun Tratamento Agua Residuals Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	\$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	\$ 12,106.37	\$ 11,072.90	Provezoriam ente servisu paradu hela	Provezoriamente servisu paradu hela	79.42%	0.00%	79.42%
8	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal Lda	SSS/054/MI-2019	\$ 58,107.88	Nov. 29, 2019	86.27%	81.96%	\$ 47,623.31	\$ 10,484.57	PHO	PHO	86.27%	0.00%	86.27%
9	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesaliobu	MAP-PO2019-19532	\$ 67,927.04	Dec. 5, 2019	82.29	74.06%	\$ 50,309.27	\$ 17,617.77	PHO	PHO	94.12%	0.00%	94.12%
10	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Queson SO Unipessoal Lda	MS-DNA-RBK-20-178	\$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	\$ 44,268.56	\$ 22,289.34	ON-GOING	Servisu refere sedauk 100%	73.90%	0.00%	73.90%
11	New construction of Isolation for covid 19 in liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	\$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	\$ 212,156.22	\$ 31,211.86	PHO	PHO	96.86%	0.00%	96.86%
12	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquica	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	\$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	\$ 82,502.69	\$ 16,982.11	PHO	PHO	92.14%	0.00%	92.14%
13	Emergency Project For Tibar River	Sail Magu Unipessoal Lda	RT/067/MOP-2021	\$ 502,473.28	Sept. 20, 2021	72.76%	64.02%	\$ 321,707.56	\$ 180,765.72	PHO	PHO	99.75%	0.00%	99.75%
14	Konstrusaun Edifício Posto Administrativo Bazartete & Moru Haleu	Aquarius Construction Unip.Lda	02/SMA-AML/PDIM VIII/2021	\$ 154,189.34	Aug. 31, 2021	9.33%	0.00%	\$ -	\$ -		ADN,I.P la hare	9.33%	0.00%	9.33%
15	R4D Rural Road Spot Improvement Fahliebo-Bucumera Chainage 0 + 000-3 + 000	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	\$ 149,732.87	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	41.45%	0.00%	41.45%
16	R4D Rural Road Spot Improvement Fahliebo -Fatumasi Chainage 0 + 000-2 + 300 , Liquica Municipality	Hatumeta Oan, Unip.Lda	MOP - CD-RFQ - 21017	\$ 88,852.44	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	19.17%	0.00%	19.17%
17	R4D Rural Road Spot Improvement Libaloa-Fahliebo Chainage 0 + 000-7 + 000, Liquica Municipality	Hatuleo Unip Lda	MPW-W-210144	\$ 88,425.80	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	90.80%	0.00%	90.80%
18	Rural Road Spot Improvement Maumeta-Metagou-Bazartete Chainage 0 + 000 - 10 + 000, Liquica Municipality	Craeleki Bercoil Unip.Lda	MPW-W-210145	\$ 62,024.04	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	65.81%	0.00%	65.81%
19	R4D Rural Road Spot Improvement Fahliebo - Bucumera Chainage 3 + 000 + 6 + 500) Liquica Municipality	TM Calieba Unip.Lda	MPW-W-210158	\$ 158,465.33	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	48.17%	0.00%	48.17%
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	Blamail Unipessoal Lda	RDTL-MS-C19-DNA-DC-21-233	\$ 65,271.32	11/01/2022					ON-GOING	ONCOING	97.21%	0.00%	97.21%
21	Supply and Installation connection for Isolation and laboratorium Building Maumeta Liquica	ZYC UNIPESOAL LDA	RDTL-MS-C19-DNA-DC-21-228	\$ 58,167.58	11/01/2022					ON-GOING	ONCOING	24.74%	0.00%	24.74%
22	Konstrusaun Foun ESTV Leorema - Liquica	U-Rema Unip. Lda.	NCB-15/MEI/DNA/2021	\$ 264,260.83	1/11/2021		0.00%	\$ -		ON-GOING	ONCOING	36.37%	27.13%	63.50%



#ANEXO B

PROGRESSU FISIKU FULAN NOVEMBRO MUNICIPIO LIQUICA

NU	NARAN PROJETU	NARAN COMPANHIA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVASAUN	Nov-22		
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MEJD PKRIE EPE BAURA	-	\$ 9,072.12	15/10/2021		0.00%	\$ -		ON-GOING	ONGOING	31.61%	0.00%	31.61%
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MEJD PKRIE EPE ERMETA	-	\$ 86,365.84	15/10/2021		0.00%	\$ -		ON-GOING	ONGOING	23.28%	1.20%	24.47%
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MEJD PKRIE EPE CASSAIT	-	\$ 78,250.89	15/10/2021		0.00%	\$ -		ON-GOING	ONGOING	17.96%	5.36%	23.32%
26	Konstrusaun ka Reabilitasaun ba ESC-Paralelo Bogoro	MEJD PKRIE ESC-PARALELO	-	\$ 115,313.76	15/10/2021		0.00%	\$ -		ON-GOING	ONGOING	23.57%	0.56%	24.13%
27	Meiohoramento no Suply Energia Elektridade husi Sub Stasaun Liquica ba Portu Tibar (Engineering Procurement Construction - Design, Suply, Instalation, Testing and Commissioning Extension Transformer Bay Of the Existing 150/20kV Liquica Substation to Supply Power to Tibar Bay Port)	China Shandong International Economic And Technical Cooperation Group, LTD	RFP/054/MOP-2021	\$ 4,797,600.00	Dec. 16, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING			
28	Supervision Consultant for Construction of Intersection In the Existing Dili - Liquica Road to Connect Access Road from Tibar Bay Port (National Road - A03) Sta. 0 + 000 - Sta. 0 + 620	Leio Engineering Unipessoal Lda	RFP/072/MOP-2021	\$ 154,000.00	Dec. 14, 2021	95.77%	30.66%	\$ 47,209.03	\$ 106,790.97	ON-GOING	ONGOING			
29	Construction of Intersection In the Existing Dili-Liquica Road to Connect Access Road from Tibar Bay Port (National Road-A03)	Altua Construction, Lda	RT/070/MOP-2021	\$ 1,738,869.60	Dec. 1, 2021					ON-GOING	ONGOING	28.30%	0.00%	28.30%
30	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	\$ 153,851.88	Dec. 5, 2019	95.23%	81.19%	\$ 124,915.14	\$ 28,936.74	FHO	FHO			
31	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	\$ 1,394,750.00	May 17, 2017	47.12%	47.12%	\$ 657,275.92	\$ 737,474.08	ON-GOING		47.12%	0.00%	47.12%
32	R4D Rural Road Periodic Maintenance Albenu - Asumanu Chainage 0 + 000 - 4 + 300 Rutine Maintenance Dato - Liquica - Loldahar Chainage 0 + 000 - 12 + 300 Municipality Liquica	Nheu	MPW-W-RFQ-190093	\$ 55,012.05	Aug. 22, 2019	100%	89.92%	\$ 49,468.35	\$ 5,543.70	FHO	FHO			
33	Rural Roads Periodic Gunaba - Lukuai Chainage 0 + 000 & Metagou - Albenu Chainage 0 + 000 - 7 + 600 Rutine Maintenance Taitabi - Kutulau Chainage 0 + 000 - 1 + 700 Municipality Liquica	Goubara Unip Lda	MPW-W-190096	\$ 71,468.49	Aug. 19, 2019	100%	90.00%	\$ 64,321.64	\$ 7,146.85	FHO	FHO			
34	New Installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	Maferdi, Lda	RD/L/MOPTC-VMOPTC/CGI-PEN : 00000399	\$ 593,093.80	Jan. 6, 2017	91.66%	67.45%	\$ 400,036.22	\$ 193,057.58	ON-GOING	ONGOING	92.32%	0.00%	92.32%



#ANEXO B

PROGRESSU FISIKU FULAN NOVEMBRO MUNICIPIO LIQUICA

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVASAUN	Nov-22		
35	New Installation of MV, LV Line and House Connection from Liquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuieno, Koni Leopa, Alpeio, Maumeta, and Leopa - Liquica Municipality	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	\$ 276,484.00	July 6, 2016	92.77%	83.49%	\$ 230,841.25	\$ 45,642.75	ON-GOING	ONGOING	92.77%	0.00%	92.77%
36	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raeliti Unip. Lda	RT/034/MOP-2019	\$ 452,362.93	Dec. 20, 2019	76.44%	50.38%	\$ 227,897.03	\$ 224,465.90	ON-GOING	ONGOING	97.15%	0.00%	97.15%
37	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda	RDTL 0000	\$ 47,299.32	Aug. 18, 2021	88.95%	80.06%	\$ 37,865.52	\$ 9,433.80	ON-GOING	PHO	95.71%	0.00%	95.71%
38	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	\$ 176,933.50	Aug. 31, 2021	3.85%	0.00%	\$ -	\$ -		ADN,I.P ia hare			
39	R4D Rural Road Spot Improvement Beriakuldu-Laberiaka Chainage 0+000-2+500	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	\$ 131,219.62	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	48.18%	0.00%	48.18%
40	R4D Rural Road Spot Improvement Taitabi - Kutulau Chainage 0+000-1+700, Liquica Municipality	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	\$ 123,631.72	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	63.76%	0.00%	63.76%
41	R4D Rural Road Spot Improvement Metagou - Albenu Chainage 0+000-7+600, Liquica Municipality	Metalika Unipessoal, Lda	MOP - CD - NCB - R - 21038	\$ 238,739.71	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	40.21%	0.00%	40.21%
42	R4D Rural Road Spot Improvement Dato - Loidahar Chainage 0+000-12+300, Liquica Municipality	Luquell Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	\$ 188,589.13	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	81.67%	0.00%	81.67%
43	R4D Rural Road Spot Improvement Albenu - Asumanu - Leurema Chainage 5+000 - 10+000, Liquica Municipality	Calulu, Unip Lda	MOP - CD - NCB - R - 21035	\$ 162,215.27	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	70.35%	0.00%	70.35%
44	R4D Rural Road Spot Improvement Albenu-Asumanu-Leurema Chainage 0+000-5+000, Liquica Municipality	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	\$ 165,363.43	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	45.83%	42.02%	87.85%
45	R4D Rural Road Spot Improvement Beriakuldu - Laberiaka Chainage 2+500-5+400	Claridade Unip.Lda	MPW-W-210163	\$ 167,071.89	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	30.65%	17.55%	48.21%
46	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000	Craeleki Bercoil, Unip Lda	MPW-W-210143	\$ 76,423.05	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	40.74%	15.79%	56.53%
47	Projeltu Konstrusaun foun ESC publico 01 Liquica	Roman Furak Unip.Lda	NCB 16/MEJD/DNA/2021	\$ 167,079.099	Nov. 1, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	47.86%	0.11%	47.97%
48	Roads Maintenance Section : Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chanel Chander Unipessoal Lda	MPW-W-210202	\$ 112,505.280	44543	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	32.14%	0.00%	32.14%
49	Konstrusaun ka Rehabilitasaun ba EBF Mauboque	MEJD PKRIE EBC MAUBOQUE	-	\$ 112,530.010	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	25.45%	0.71%	26.16%
50	Konstrusaun ka Rehabilitasaun ba EBC 1,2,3 Liquica	MEJD PKRIE EBC 1,2,3 LIQUICA	-	\$ 99,456.040	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	23.94%	0.77%	24.71%
51	Konstrusaun ka Rehabilitasaun ba EPE Loidahar	MEJD PKRIE EPE LOIDAHAR	-	\$ 79,735.630	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	25.63%	1.15%	26.77%
52	Konstrusaun ka Rehabilitasaun ba EBF 1,2 Laclema	MEJD PKRIE Ebf 1,2 LACLEMA	-	\$ 89,650.660	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	22.88%	0.91%	23.79%
53	Konstrusaun ka Rehabilitasaun ba EBF 1,2 Tolema	MEJD PKRIE EBF 1,2 TOLEMA	-	\$ 88,407.020	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	24.95%	1.16%	26.11%
54	Konstrusaun ka Rehabilitasaun ba EBF 1,2 Luculai	MEJD PKRIE EBF 1,2 LUCULAI	-	\$ 5,151.290	44484	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING	45.13%	5.35%	50.48%
55	Consultant Services to Supervise EPC Contractor for the Up-Grading of Liquica 150/20KV Substation to Supply Power to Tibar Bay Port	PT. Artefak Arkindo (Indonesial JV with Jazicasnu Unipessoal Lda	RFP/054/MOP-2021	\$ 620,500.000	Dec. 16, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONGOING			
56	New Construction of "Escola CAFE" Building at Liquica Municipality	RICS Unipessoal Lda	NCB/138/MEJD-2021	\$ 692,517.120	June 8, 2022							0.00%	0.00%	0.00%
57	Addt. Poste Iiga Maubara	Fu Unip.Lda	RDTL - 0000	\$ 13,000.00	Jan. 1, 2016	0.00	0.00%	\$ -	\$ 13,000.00					
58	New Installation MV, LV Line and House Connection from Kuiau to Maubara - Liquica Municipality	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	\$ 288,760.22	July 6, 2016	83.73%	75.36%	\$ 217,606.07	\$ 71,154.15	ON-GOING	ONGOING			
59	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	Montana Diak Unipessoal, Lda	SSS/126/MOPTC-2017	\$ 1,901,334.67	Sept. 7, 2017	99.98%	89.98%	\$ 1,710,791.24	\$ 190,543.43	ON-GOING	PHO			
60	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	Bernabud Arquitectura SLP	RFP/147/MTAC/2016	\$ 275,000.00	Dec. 27, 2016	40.00	38.00%	\$ 104,500.00	\$ 170,500.00	ON-GOING	ADN,I.P ia hare			
61	Konstrusaun ESTV Lisadila Maubara-Liquica (CA + CBI)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	\$ 171,850.61	Aug. 16, 2019	89.17%	80.25%	\$ 137,915.77	\$ 33,934.84	ON-GOING	Servisu refere sedauk 100%	89.17%	0.00%	89.17%



#ANEXO B

PROGRESSU FISIKU FULAN NOVEMBRO MUNICIPIO LIQUICA

												Nov-22		
NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO (\$)	BALANSU (\$)	STATUS PROJETO	OBSERVASAUN			
62	Rehabilitasaun Sistema be'e mos lina aldeia Pandevou ho Mau-Uno, Sucu Guico /162	Oceania Const Unip.Lda	NCB-MOP-190051	\$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	\$ 72,706.50	\$ 98,259.15	ON-GOING	Provizoriamente paradu nela	54.99%	0.00%	54.99%
63	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOPTC/2016	\$ 7,693,101.00	May 3, 2017	75.33%	75.33%	\$ 5,795,051.15	\$ 1,898,049.85	ON-GOING				
64	R4D Rural Road Maintenance Berikuilidu - Laberiaka Chainage 0 + 000 - 5 + 400 Nunuleta - Darulema Chainage 0 + 000 - 1 + 600 Vaviquinia - Maubaralisa Chainage 0 + 000 - 12 + 500	Luliana Unip.Lda	MPW-W-190098	\$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	\$ 43,761.73	\$ 6,940.86	PHO	PHO			
65	Konstrusaun Moru Haleu no Posto Siguransa ba Edifício Posto Administrativo Maubara	Raflo Unip. Lda	01/AML/SMA-PDIM/VIII/2021	\$ 56,445.70	July 21, 2021	16.32%	0.00%	\$ -	\$ -		ADN,I.P la hare			
66	R4D Rural Road Spot Improvement Nunulete - Darulema Chainage 0 + 000-2 + 000, Liquica Municipality	Rito - Pu, Unipessoal,Lda	MOP - CD-RFQ - 21013	\$ 67,382.23	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	2.07%	23.27%	25.33%
67	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 4 + 800-9 + 600, Liquica Municipality	Mailbo, Unipessoal LDA	MOP - CD - NCB-R- 21033	\$ 152,622.90	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	35.83%	19.66%	55.49%
68	R4D Rural Road Spot Improvement Barkau (Vaviquenia)-Maubaralisa Chainage 0 + 000-4 + 200	Nheu, Unipessoal LDA	MOP - CD - NCB-R- 21027	\$ 173,484.62	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	45.61%	54.39%	100.00%
69	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 0 + 000-4 + 800, Liquica Municipality	Murak, Unipessoal Lda	MOP - CD - NCB-R- 21032	\$ 153,049.65	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	43.43%	25.57%	68.99%
70	R4D Rural Road Spot Improvement Barkau (Vaviquenia) - Maubaralisa - Chainage 8 + 400-12 + 500	Meta Loe Crae Bau Unip.Lda	MPW-W-210160	\$ 198,698.25	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING			
71	R4D Rural Road Spot Improvement Samarapo - Gisu Chainage 0 + 000-2 + 000	Nazico Unip Lda	MPW-W-210152	\$ 114,789.50	Oct. 01, 2022	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING			
72	R4D Rural Road Spot Improvement Barkau (Vaviquina) - Maubaralisa Chainage 4 + 200-8 + 400	Luliana Unip,Lda	MPW-W-210161	\$ 213,930.25	Oct. 01, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING			
73	Konstrusaun ka Rehabilitasaun ba EBF Gariana	MEJD PKRIE EBF GARIANA	-	\$ 117,902.04	Oct. 15, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	1.98%	18.03%	20.01%
74	Konstrusaun ka Rehabilitasaun ba EBF Tapo Manuhulu	MEJD PKRIE EBF TAPO	-	\$ 100,033.33	Oct. 15, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	10.52%	12.37%	22.89%
75	Konstrusaun ka Rehabilitasaun ba ESC-Paralelo Maubara/Batuvo	MEJD PKRIE ESC-PARALELO	-	\$ 141,660.22	Oct. 15, 2021	0.00%	0.00%	\$ -	\$ -	ON-GOING	ONCOING	20.41%	0.45%	20.86%
76	Feasibility study for New Construction of Industrial Park in Liquica, Timor Leste	HABERAN UNIPESOAAL LDA (TIMOR LESTE) in Joint Venture with PT ITS TEKNO SAINS (INDONESIA)	RFP/077/MTCI-2021	\$ 225,373.00	March 24, 2022					ON-GOING				
77	Installation foun ba Linha de Media Tensaun, Baixa Tensaun e Baixadas em Liquica - Maubara	Nla construction, Lda	0000	\$ 490,039.81	Dec. 4, 2012	94.93%	85.44%	\$ 418,669.22	\$ 71,370.59	ON-GOING	ONCOING	94.93%	0.00%	94.93%

INSPEKSAUN HUSI,

(Eng. Marcos de Araújo Ximenes)

Engineru ba Projeitu Infrastrutura Transporte e Irigasaun ADN,I.P

(Eng. Geovanto M. X. C. Aleixo)

Engineru ba Projeitu Infrastrutura Transporte e Irigasaun ADN,I.P

(Eng. Juninho Antonio A. da Cruz)

Engineru ba Edifício Público Água e Saneamento ADN,I.P

(Eng. Antonia de Fatima Moraes Soares)

Engineru ba Edifício Público Água e Saneamento ADN,I.P

(Eng. Camilo de Jesus)

Engineru ba Projeitu Mekanikal

VERIFIKA HUSI,

(Eng. Remigio da C.S.dos Santos)

Engineru Senior ba Projeitu Infrastrutura Transporte e Irigasaun ADN,I.P

(Arg. Francisco Xavier D.D. Jeronimo)

Engineru Senior ba Projeitu Edifício Público no Be'e Saneamento ADN,I.P

(Eng. Deolindo de Fatima Marques)

Chefe Seksaun Mekanikal e Elektrikal & ITC ADN,I.P

SERTIFIKA HUSI,

(Eng. Emerenciano da Costa M.Freitas)

Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeto Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Data Inspesaun : 30 Novembro 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 40' 43.435'', Latetude :

End Point : Long : E 125° 22' 18.833'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekiba tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
Konstrusaun Foun ESTV Leorema
lokaliza iha suku Leorema,
Bazartete, Munisipiu Liquisa projeitu
nee kaer husi kompania U-Rema
Unip. Lda.



#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeto Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tuir rezultadu inspesaun enjineiru
ADN, IP iha terenu hare ba progresu
fiziku iha terenu atinji on aba servisu
item *painting* ba konstrusaun klase


Ca no Cb.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba servisu progresu iha konstrusaun
teacher office atinji ona servisu ba
item *roofing* ba monta *rangka*
plafond ninian.

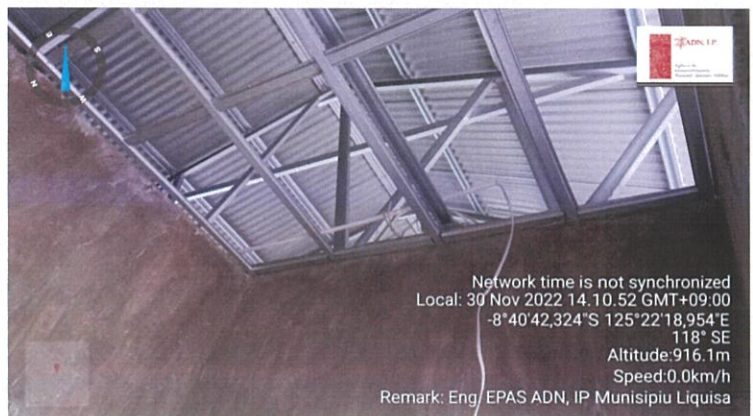



#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Data Inspesaun : 30 Novembro 2022

Fatin Inspesaun : Fahilebo - Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 38' 12.154'', Latetude :

End Point : Long : E 125° 24' 35.457'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekpa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
foun husi MEJD PKRIE ba
Konstrusaun ka Reabilitasaun EPE
Ermeta Fahilebo iha suku Fahilebo,
postu Bazartete, Liquisa projeitu nee
kaer husi servisu grupu komunitariu.



#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo

Kompania :

No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Tuir rezultadu inspesaun neebe halao husi ekipa enjineiru ADN, IP iha terenu, progresu fiziku atinji ona servisu item *windows frame* ninian ba konstrusaun klase C.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Grupu mos hahuu ona servisu ba item *finishes plesteran* iha parte klase balu.

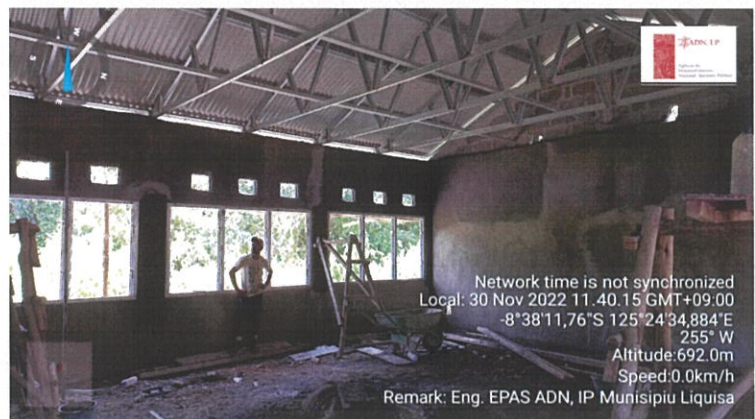



#ANEXU C1 – (BZT26)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Cassait
Kompania :
No. kontratu :

Data Inspesaun : 22 Novembro 2022

Fatin Inspesaun : Lauhata - Bazartete, Liquisa

Koordinadas :

Start Point : Long : S 8° 34' 19.391'', Latetude :

End Point : Long : E 125° 27' 52.593'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Ekpa tekniku ADN, IP Munisipiu
Likisa halao inspesaun ba projeitu
foun husi MEJD PKRIE ba
Konstrusaun ka Reabilitasaun EPE
Cassait iha suku Lauhata, Bazartete,
Liquisa projeitu nee kaer husi servisu
grupu komunitariu.

Observasaun iha tereno no Foto Aktual



#ANEXU C1 – (BZT26)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Cassait
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Wainhira ekipa tekniku ADN, IP
halao inspesaun iha terenu servisu
projeitu refere paradu hela, hatoo
husi autoridade sira katak trabaliador
no tekniku grupu sira servisu loron
balu deit.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tekniku grupu presija halo
justifikasaun konaba item neebe
grupu atu sosa ka stock mai iha
terenu tanba tuir informasaun katak
grupu hola sala ona item fiu nian balu
neebe la hanesan ho design ka
mensiona iha BoQ.





#ANEXU C1 – (BZT27)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE ESG Classe Paralelo Bogoro
Kompania :
No. kontratu :

Data Inspesaun : 24 Novembro 2022

Fatin Inspesaun : Bogoro – Bazartete, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 36.980", Latetude :

End Point : Long : E 125° 23' 58.119", Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
Foun MEJD PKRIE ba Konstrusaun
ka Reabilitasaun ESG Classe Paralelo
Bogoro, lokaliza iha suku Bogoro,
Bazartete, Munisipiu Liquisa, neebe
kaer husi servisu Grupu Komunitariu



#ANEXU C1 – (BZT27)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE ESG Classe Paralelo Bogoro
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba servisu konstrusaun klase *Ca*
(figura iha sorin) nia progresu iha
terenu atinji ona servisu *top beam*.
Grupu deklara katak sei kontinua
servisu wainhira stock material iha
terenu.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba iha servisu konstrusaun *toilet building Tb* nian grupu finaliza ona
servisu betaun ba iha kolom pendek
nian tuir kompozisaun husi Obras
Nasional no grupu mos hadia ona
begel tuir tekniku ADN, IP nia
instrusaun.





#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Data Inspesaun : **24 Novembro 2022**

Fatin Inspesaun : Dato, Liquica Vila

Koordinadas :

Start Point : Long : 8.35'21.273"S, Latetude :

End Point : Long : 125.20'1.933"E, Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia De Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
husi Ministeriu Edukasaun
Juventude no Desportu nian ba
Konstrusaun Foun ESG Publico 01-
Liquica lokaliza iha suku Dato,
Liquisa Vila, Munisipiu Liquisa,
neebe kaer husi kompania Roman
Furak Unip. Lda.

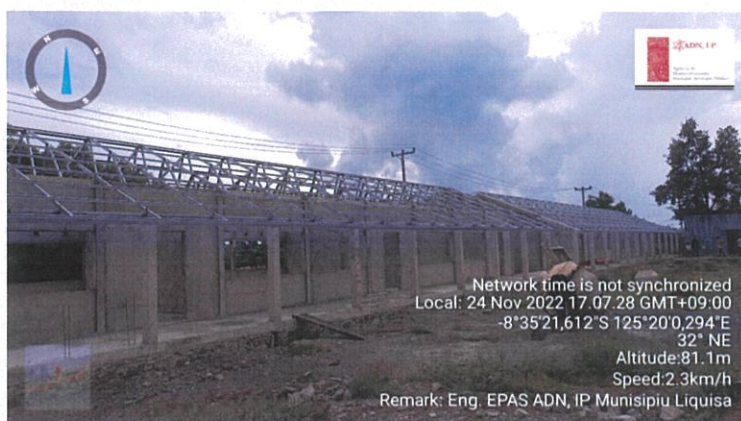

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Sketch & Foto Desenho

Ba servisu iha klase *C* (figura iha sorin) nia progresu iha terenu atinji ona item servisu ba *Steel Roof/Gording* kuase hatur no instala ona, servisu ba item fui beton lantain nian mos lao ona tuir diamentru nebe mentiona iha BOQ (50mm).


Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho

Iha klase *Cb* (figura iha sorin) trabaliador kompania finaliza servisu instala *Gording*. Ba iha servisu konstrusaun toilet nian hahuu ona plester.

Observasaun iha tereno no Foto Aktual

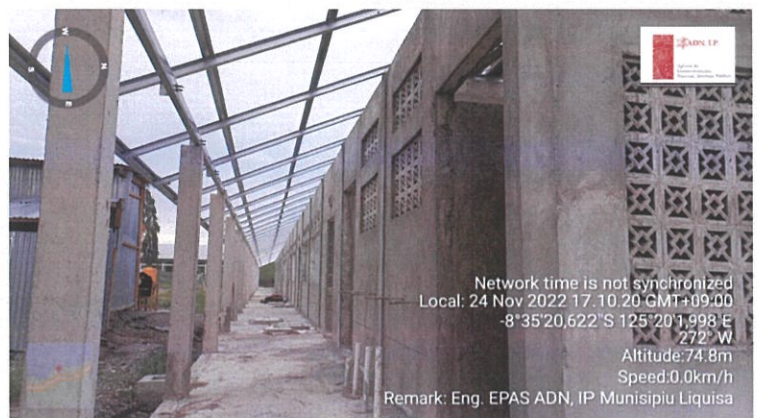

#ANEXU C1 – (LV22)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Data Inspesaun : 16 Novembro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 49.086", Latetude :

End Point : Long : E 125° 18' 51.269", Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia De Fatima Moraes Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa ADN, IP Munisipiu Liquisa
halao inspesaun ba projeitu husi
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EBF 1, 2 Mauboque
lokaliza iha suku Dato, Liquisa Vila
Munisipiu Liquisa neebe kaer husi
servisu Grupu Komunitariu.



#ANEXU C1 – (LV22)


Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba servisu konstrusaun klase *Cdl*
(figura iha sorin) enjineiru ADN, IP
foo ona instrusaun atu monta *bekisting*
ba koluna nian no hahuu fui ona
betaun molok kontinua ba servisu
item *steel roof*.

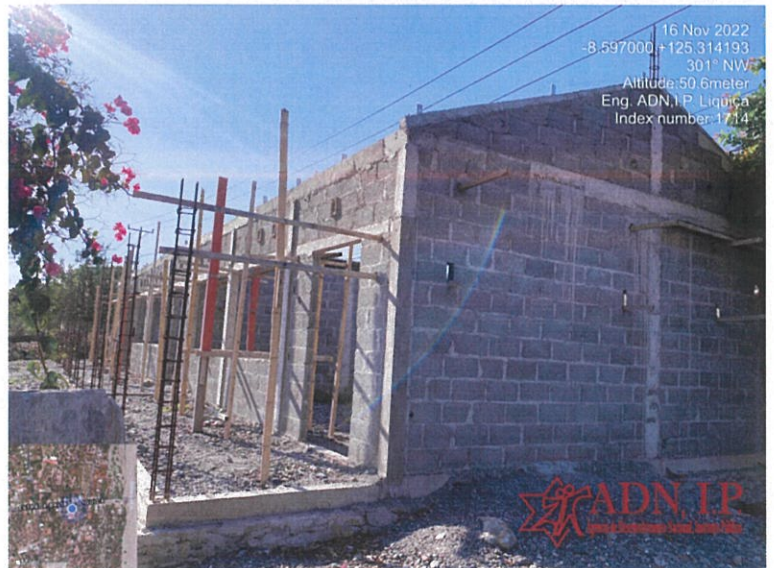

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekupa hato'o ona ba grupu atu aselera
servisu nebe tuir ona planu iha
terrenu, servisu refere quase lao *lento*
(neneik loos).



#ANEXU C1 – (LV23)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBC 1,2,3 Liquica
Kompania :
No. kontratu :

Data Inspesaun : 17 Novembro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 32. 592'', Latetude :

End Point : Long : E 125° 19' 53. 005'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
Foun MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EBC 1, 2, 3 Liquica
lokaliza iha suku Dato, Liquisa Vila
munisipiu Liquisa, neebe kaer husi
servisu Grupu Komunitariu.

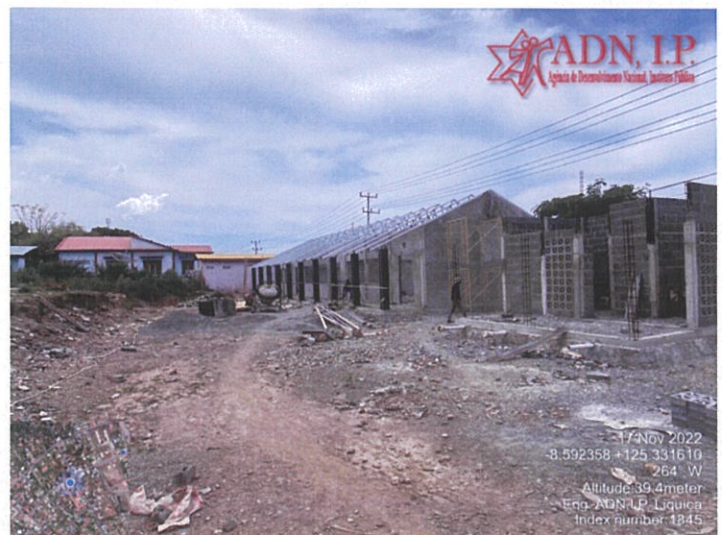

#ANEXU C1 – (LV23)


Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBC 1,2,3 Liquica
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tuir observasaun neebe enjineiru ADN,
IP Munisipiu Liquisa hare iha terenu
tuir progresu fiziku konstrusaun refere
atinji ona servisu monta *bekisting* ba
koluna klase oin.

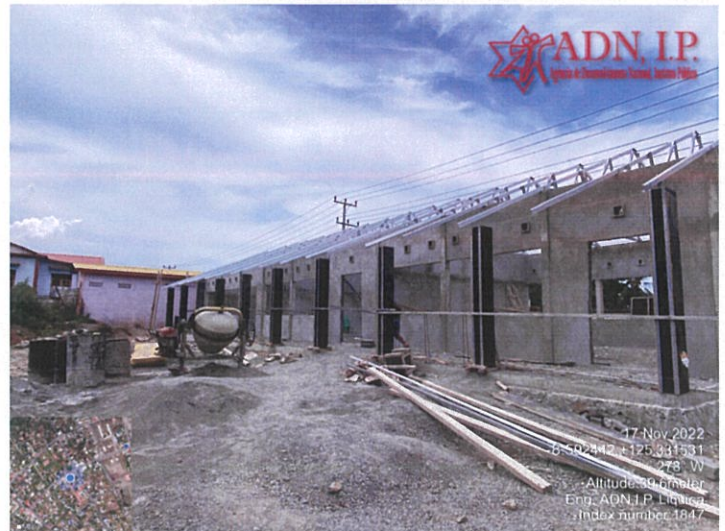

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekupa relata ona ba grupu atu ativu iha
terenu hodi bele aselera servisu refere
tuir planu neebe iha ona.



#ANEXU C1 – (LV24)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EPE Loidahar
Kompania :
No. kontratu :

Data Inspesaun : 17 Novembro 2022

Fatin Inspesaun : Loidahar - Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 32. 592'', Latetude :

End Point : Long : E 125° 19' 53. 005'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
Foun MEJD PKRIE ba
Konstrusaun ka Reabilitasaun EPE
Loidahar lokaliza iha suku
Loidahar, Liquisa Vila munisipiu
Liquisa, neebe kaer husi servisu
Grupu Komunitariu.



#ANEXU C1 – (LV24)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EPE Loidahar
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekiba tekniku ADN, I.P. Munisipiu
Liquisa observa servisu iha terenu
atinji parte sevisu item *Gording/
Kuda-kuda*.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tekniku ADN, I.P. mos husu ona
grupo atu hatama relatoriu
progresu servisu iha terenu tuir
progresu neebe grupu atinji ona.



#ANEXU C1 – (LV25)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Laclolema
Kompania :
No. kontratu :

Data Inspesaun : 30 Novembro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 37' 11.666", Latetude :

End Point : Long : E 125° 18' 55.306", Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekpa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EBF 1, 2 Laclolema
lokaliza iha suku Dato, Liquisa Vila
munisipiu Liquisa, neebe kaer husi
servisu grupu komunitariu.



#ANEXU C1 – (LV25)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Laclolema
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Ba servisu konstrusaun klase *Cb*
(figura iha sorin) ba projeitu refere
servisu lao hela maka *Gording/Kuda-*
kuda no hahuu ona lao servisu item
finishes.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Grupu hadia ona servisu neebe
enjineiru ADN, IP foo instrusaun ba
iha parte *toilet building* nian neebe
servisu item *blockwall* halai kleuk.

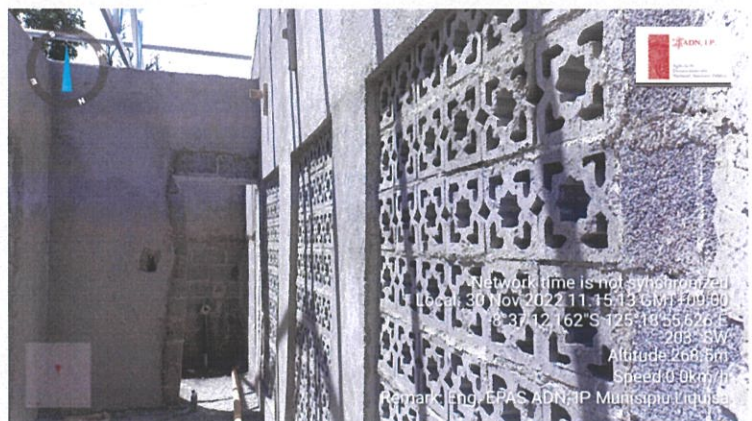

#ANEXU C1 – (LV26)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Tolema
Kompania :
No. kontratu :

Data Inspesaun : 30 Novembro 2022

Fatin Inspesaun : Leotela – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 40' 25. 106'', Latetude :

End Point : Long : E 125° 18' 39. 875'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EBF 1, 2 Tolema
lokaliza iha suku Leotela, Liquisa
Vila munisipiu Liquisa, neebe kaer
husi servisu grupu komunitariu.



#ANEXU C1 – (LV26)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Tolema
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tuir observasaun neebe enjineiru
ADN, IP halao iha terenu nota katak
servisu konstrusaun refere lao tarde,
no hatoo ona ba autoridade eskola
nian atu toma atensaun ba grupu nia
servisu.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tekniku ADN, IP presija konsulta ho
tekniku grupu hodi aselera servisu
refere.



#ANEXU C1 – (LV27)

Back-up Data

Naran Projeto : Rehabilitasaun MEJD PKRIE EBF 1,2 Luculai
Kompania :
No. kontratu :

Data Inspesaun : 17 Novembro 2022

Fatin Inspesaun : Luculai – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 38' 31.068", Latetude :

End Point : Long : E 125° 21' 20.97", Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
MEJD PKRIE ba Konstrusaun ka
Reabilitasaun EBF 1, 2 Luculai lokaliza
iha suku Luculai, Liquisa Vila munisipiu
Liquisa, neebe implementa husi servisu
grupu komunitariu.

Observasaun iha tereno no Foto Aktual



#ANEXU C1 – (LV27)

Back-up Data

Naran Projeto : Rehabilitasaun MEJD PKRIE EBF 1,2 Luculai
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Enjineiru ADN, IP Munisipiu Liquisa
nafatin tenta ho enjineiru grupu
konstrusaun refere atu hasoru malu iha
terenu maibe seidauk posivel.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Projeitu refere konaba rehabilitasaun parte
eskola EBF Luculai nia kotuk hodi
monta *gabion*, no *stone masonry* hodi sai
protesaun ba eskola refere.



#ANEXU C1 – (LV29)

Back-up Data

Naran Projeto : New Construction of “Escola Café” Building at Liquica Municipality
Kompania : RICS Unip. Lda.
No. kontratu : NCB/138/MEJD-2021

Data Inspesaun : 17 Novembro 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 37.38'', Latetude :

End Point : Long : E 125° 19' 40.752'', Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia De Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
New Construction of “Escola Café”
Building lokaliza iha suku Dato,
Liquisa Vila munisipiu Liquisa, neebe
implementa husi kompania RICS Unip.
Lda.

Observasaun iha tereno no Foto Aktual

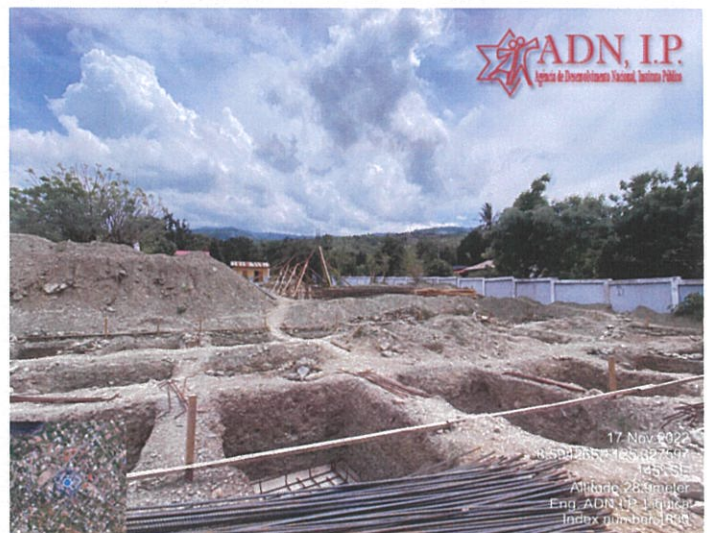

#ANEXU C1 – (LV29)

Back-up Data

Naran Projeto : New Construction of “Escola Café” Building at Liquica Municipality
Kompania : RICS Unip. Lda.
No. kontratu : NCB/138/MEJD-2021

Sketch & Foto Desenho

Ekipa enjineiru ADN, IP Munisipiu
Liquisa hatoo iha instrusaun ba
kompania konaba dezeniu tulangan
footing ba tipu C1 no C2 atu korderna
ho uluk lai ho projeitu nain.


Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho

Ekipa husu ba kompania atu prepara
dokumentus despaisu ba lisensa teste
betaun nian ba item saida deit molok
implementa.

Observasaun iha tereno no Foto Aktual

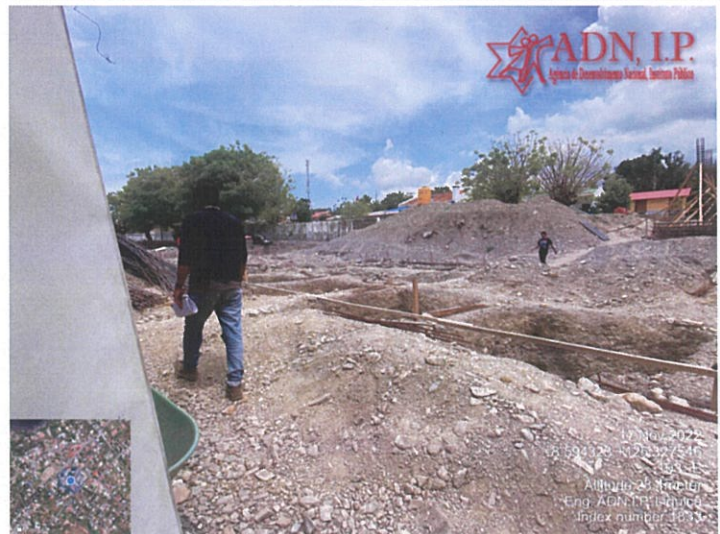

#ANEXU C1 – (MBR17)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1, 2 Gariana
Kompania :
No. kontratu :

Data Inspesaun : 10 Novembro 2022

Fatin Inspesaun : Fatubou - Maubara, Liquica

Koordinadas :

Start Point : Long : S 8° 35' 32.592'', Latetude :

End Point : Long : E 125° 19' 53.005'', Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa halao inspesaun ba projeitu
Foun MEJD PKRIE ba Konstrusaun
ka Reabilitasaun EBF 1, 2 Gariana
lokaliza iha suku Fatubou, Maubara
munisipiu Liquisa, neebe kaer husi
servisu Grupu Komunitariu.

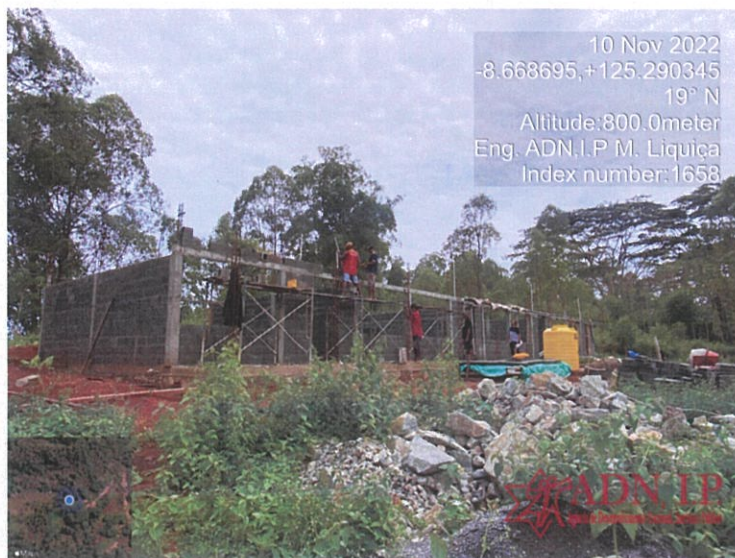

#ANEXU C1 – (MBR17)


Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1, 2 Gariana
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP halao
inspesaun ba konstrusaun projeitu
refere hahuu kontinua halao fali
servisu tanba material foin desloka
mai terenu.

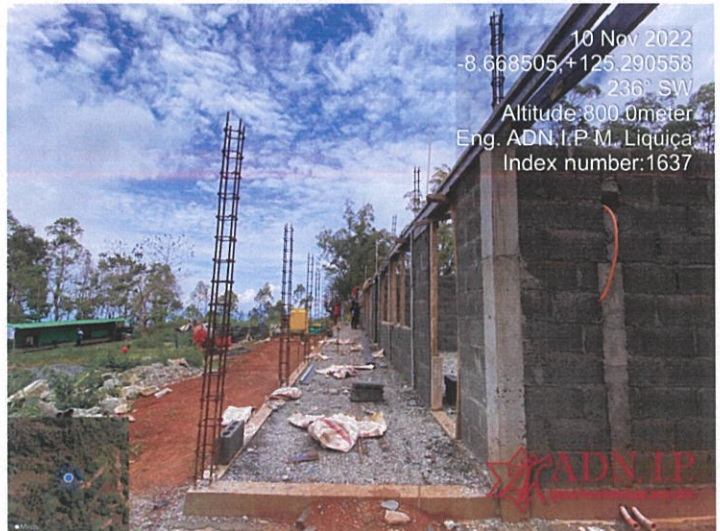

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa ADN, IP hatu'o ba grupu
trabalhadores atu aktivu iha terenu
hodi aselera servisu refere.



#ANEXU C1 – (MBR18)

Back-up Data

Naran Projeto : **Konstrusaun Foun EBF 1,2 Tapo Manuhulu**
Kompania :
No. kontratu :

Data Inspesaun : 11 Novembro 2022

Fatin Inspesaun : Gugleur, Maubara - Liquica

Koordinadas :

Start Point : Long : S 8° 43' 42. 194", Latetude :

End Point : Long : E 125° 9' 12. 256", Latetude :

Naran Inspector : **1. Juninho António Abrantes da Cruz**

2. Antónia De Fatima Morais Soares

3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu
Liquisa nian halao inspesaun ba
projeitu MEJD PKRIE –
Konstrusaun Foun EBF 1,2 Tapo
Manuhulu lokaliza iha suku
Gugleur, postu Maubara, munisipiu
Liquisa. Neebe kaer husi servisu
Grupú Komunitariu.



#ANEXU C1 – (MBR18)

Back-up Data


Naran Projeto : **Konstrusaun Foun EBF 1,2 Tapo Manuhulu**
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Tuir observasaun ekipa enjineiru
ADN, IP iha terenu hare ba projeitu
nia progresu fiziku atinji iha monta
bekisting ba iha item *lintel beam*.


No kada tulangan foo ona
instrusaun atu kesi *selimut beton*.

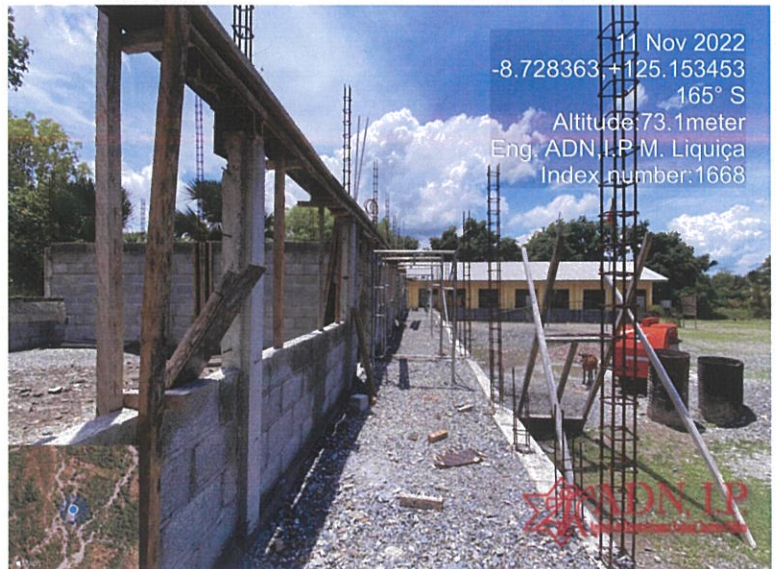

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Iha konstrusaun klase C sira nee
mos foo ona instrusaun husi
enjineiru ADN, IP atu komesa halo
pemadatan ona molok hakat ba
servisu sira seluk.

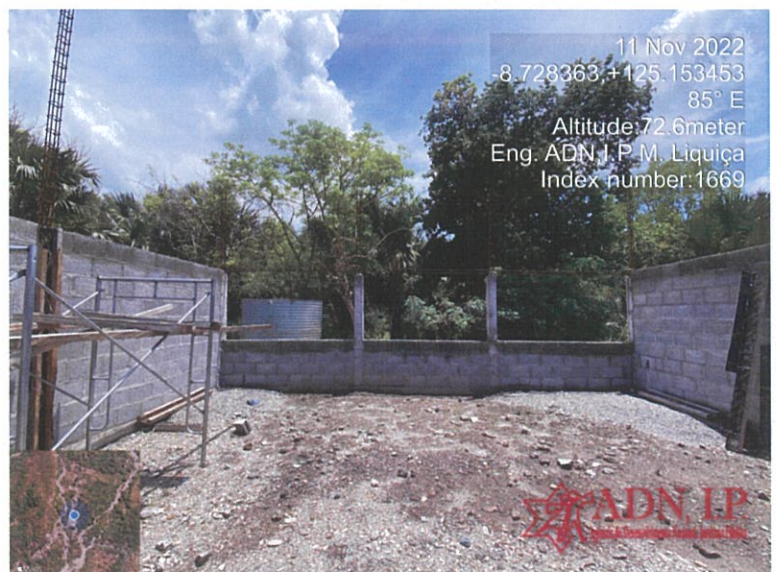



#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : Konstrusaun Foun ESG Classe Paralelo Maubara
Kompania :
No. kontratu :

Data Inspesaun : 11 Novembro 2022

Fatin Inspesaun : Maubara - Liquica

Koordinadas :

Start Point : Long : S 8° 36' 33.682", Latetude :

End Point : Long : E 125° 13' 5.010", Latetude :

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antónia de Fatima Morais Soares


3.

4.

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu Liquisa nian halao inspesaun ba projeitu MEJD PKRIE – Konstrusaun Foun ESG Classe Paralelo Maubara iha suku Maubara, postu Maubara, munisipiu Liquisa. Neebe kaer husi servisu Grupu Komunitariu.

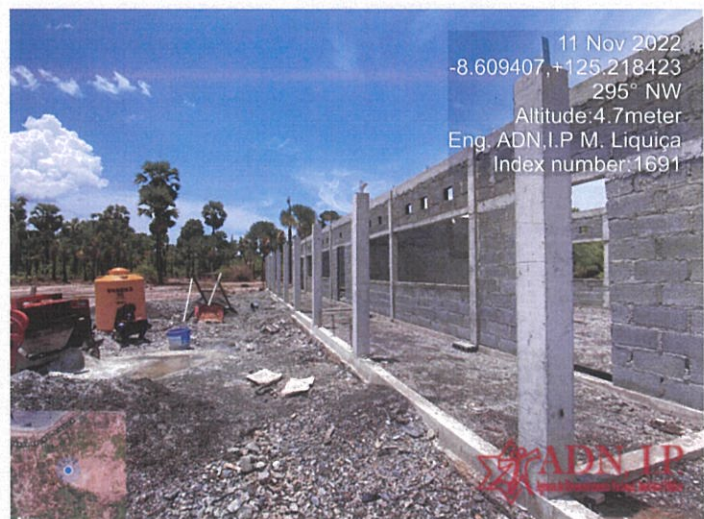



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 – (MBR19) Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual


Servisu hirak neebe lao tiha ona iha terenu
kuaze finaliza ona no grupu hein stock
deit material ba item *steel roof* ninian
molok kontinua ba instalasaun.



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Ba servisu item betaun sira mos foo ona
instrusaun ba grupu atu nunee prepara
karta lisensa ka foti amostra nee tenki
inklui ADN, IP.

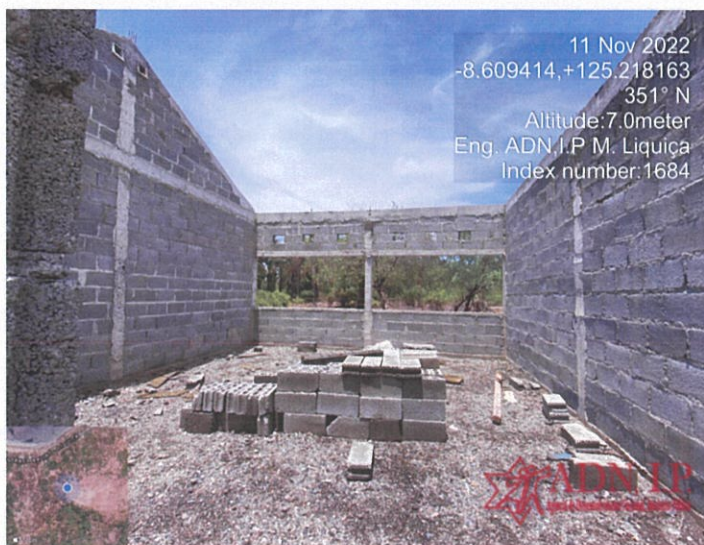

#ANEXO C2 (MBR10)

Naran Projeto : R4D Rural Road Spot Improvemrnt Nunulete - Darulema Chainage 0+000-2+000, Liquica Municipality
Contractor : Rito-Pu Unip.Lda
No. kontratu : MOP-CD-RFQ - 21013

Data Inspeksaun : 3/Novembru/2022

Fatin Inspeksaun : Suco Nunuleta - Darulema

Koordinat :

Start Point : Long : 125.19399353
End Point : Long : 125.19758718


Latetude : - 8.66031911
Latetude : - 8.652363510

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Geovanio A. Aleixo

Sketch & Foto Desenho

Sketch Item servisu : *Stone Masonry*


STA, 0+000 - 2+000

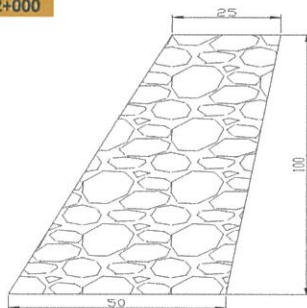


Area	Distacia	Volume
0.375	50.00	18.75
Total		18.75 m³

Sketch Item servisu : *Gabion*

STA, 0+000 - 2+000

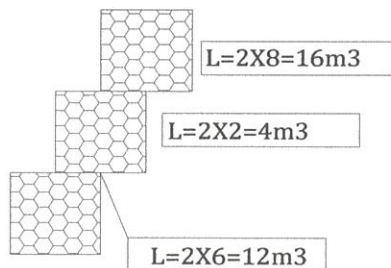

STA, 0+000 - 1+050



Area	Distacia	Volume
0.35	100.00	35.00
Total		35.00 m³

Observasaun iha tereno no Foto Aktual



ANEXO C1 (MBR12)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Barkau (VaVIQUENIA) - Maubalarisa Chainage 0+000-4+200, Liquica Municipality
Contractor : Nheu Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21027

Data Inspeksaun : 14/Novembru/2022

Fatin Inspeksaun : Suco Vaviquenia-Maubalarisa

Koordinat :

Start Point : Long : 125.21124422
End Point : Long : 125.2281181


Latitude : -8.61803763

Latitude : -8.632661686

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Geovanio A. Aleixo

Sketch & Foto Desenho

Sketch Item servisu : Stone Masonry
STA, 3+920 - 4+020




T	W	Distacia	Volume
0.12	4	500.00	240.00
Total			240.00 m³

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Stone Masonry


STA, 3+920 - 4+020



T	W	Distacia	Volume
0.12	4	500.00	240.00
Total			240.00 m³

Sketch Item servisu : Stone Masonry

STA, 3+920 - 4+020



T	W	Distacia	Volume
0.12	4	500.00	240.00
Total			240.00 m³



ANEXO C1 (MBR13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemnt Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality
Contractor : Murak Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21032

Data Inspeksaun : 22 Novembru 2022

Fatin Inspeksaun : Suco Maubalarisa

Koordinat :

Start Point : Long : 125.22682227
End Point : Long : 125.2382274

Latitude : -8.644211521


Latitude : -8.672448189

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Geovanio A. Aleixo

Sketch & Foto Desenho

Sketch Item servisu : Stone Masonry

STA, 1+050-1+150




<i>t</i>	<i>w</i>	<i>Distacia</i>	<i>Volume</i>
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Stone Masonry

STA, 1+100-1+220




<i>t</i>	w	<i>Distacia</i>	<i>Volume</i>
0.40	0.25	120.00	24.00
0.15	1.00		18
Total			42.00 m3



Sketch Item servisu : Gabion

STA, 1+300-1+420

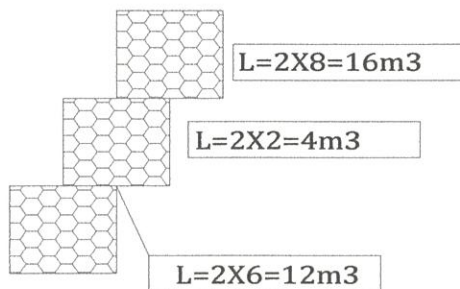

ANEXO C1 (MBR13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemmt Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality
Contractor : Murak Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21032

Data Inspeksaun : 22 Novembru 2022

Fatin Inspeksaun : Suco Maubaralisa


Koordinat :
Start Point : Long : 125.22682227
End Point : Long : 125.2382274

Latetude : -8.644211521
Latetude : -8.672448189

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Eng. Geovanio A. Aleixo

Sketch & Foto Desenho

Sketch Item servisu : Plum Concrete
STA, 2+100-2+320




t	L	Distacia	Volume
0.12	2.00	120.00	28.80
Total			28.80 m³

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Plum Concrete

STA, 2+400-2+460




t	L	Distacia	Volume
0.12	2.00	60.00	14.40
Total			14.40 m³



Sketch Item servisu : Plum Concrete

STA, 3+400-3+470



t	L	Distacia	Volume
0.12	2.00	70.00	16.80
Total			16.80 m³



ANEXO C1 (MBR11)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemrnt Malaísera - Lissadila Chainage 0+000-4+800, Liquica Municipality
Contractor : Murak Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21032

Data Inspeksaun : 8/Novembru/2022

Fatin Inspeksaun : Suco Lisadila

Koordinat :
Start Point : Long : 125.23822736
End Point : Long : 125.2291648


Latetude : -8.672448189
Latetude : -8.693159140

Naran Inspektor :
1 Eng. Marcos Ximenes de Araujo
2 Geonavio A.Aleixo

Sketch & Foto Desenho

Sketch Item servisu : Plum Concrete

STA, 4+100-4+200




T	W	Distacia	Volume
0.12	2	100.00	24.00
Total			24.00 m³

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : Plum Concrete

STA, 4+500-4+600




T	W	Distacia	Volume
0.12	2	100.00	24.00
Total			24.00 m³



Sketch Item servisu : Plum Concrete

STA, 4+600-4+700



T	W	Distacia	Volume
0.12	2	100.00	24.00
Total			24.00 m³





ANEXO C1 (LV17)

Naran Projeto : R4D Rural Road Spot Improvement Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality

Contractor : Vicaroman Unip.Lda

No. kontratu : MOP - CD NCB - R - 21034

Data Inspeksaun : 09/Novembro/2022

Fatin Inspeksaun : Suco Asu-Manu


Koordinat :

Start Point : Long : 125.3416468
End Point : Long : 125.3469018


Latetude : - 8.65444508
Latetude : - 8.680286396

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Geovanio A.Aleixo

Sketch & Foto Desenho

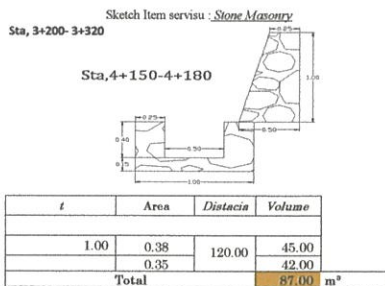

Observasaun iha tereno no Foto Aktual

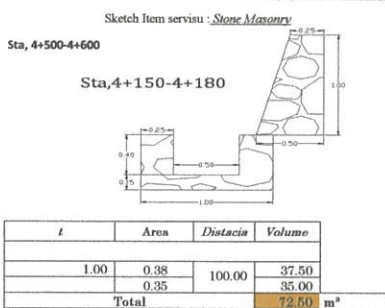

Naran Projeto : R4D Rural Road Spot Improvement Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality

Contractor : Vicaroman Unip.Lda

No. kontratu : MOP - CD NCB - R - 21034

Data Inspeksaun : 09/Novembro/2022

Fatin Inspeksaun : Suco Asu-Manu


Koordinat :

Start Point : Long : 125.34165
End Point : Long : 125.3469


Latetude : - 8.65444508
Latetude : - 8.680286396

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Geovanio A.Aleixo

Sketch Item servisu : *Stone Masonry*

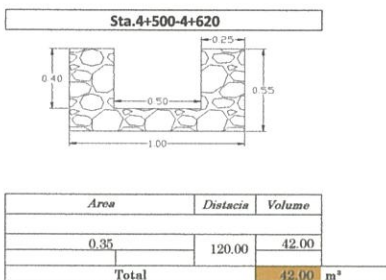

Observasaun iha tereno no Foto Aktual

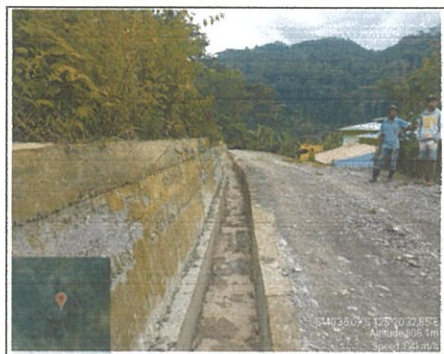

#ANEXO C2 (LV18)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400
Contractor : Claridade Unip.Lda
No. kontratu : MPW-W-210163

Data Inspeksaun : 16/Novembru/2022

Fatin Inspeksaun : Suco Berlakuidu - Laberlaka

Koordinat :

Start Point : Long : 125.29520251
End Point : Long : 125.30192345

Latetude : - 8.63329600


Latetude : - 8.641753681

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Geovanio A.Aleixo

Sketch & Foto Desenho

Sketch Item servisu : Plum Concrete

STA,3+100-3+160

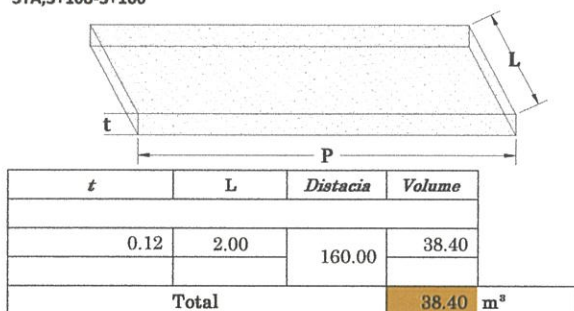


Observasaun iha tereno no Foto Aktual




Sketch Item servisu : Plam Concrete

STA, 3+700-3+800

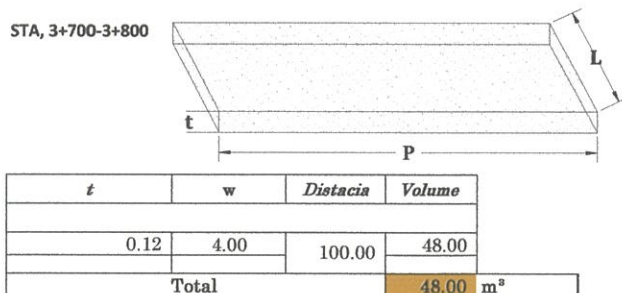

STA, 2+800-2+920

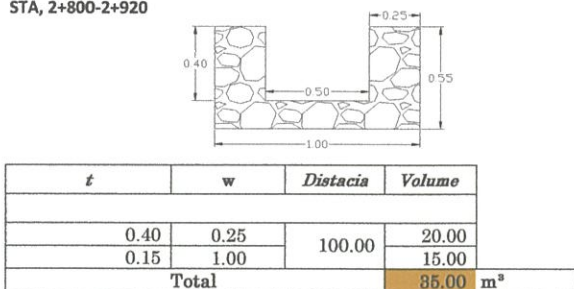

ANEXO C1 (LV19)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000
Contractor : Craeleki Bercoli Unip.Lda
No. kontratu : MPW-W-210143

Data Inspeksaun : 23 Novembru 2022

Fatin Inspeksaun : Suco Gunaba - Lukulai

Koordinat :

Start Point : Long : 125.36314054
End Point : Long : 125.35645402


Latitude : - 8.65021033
Latitude : - 8.640334040

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Geovanio A. Aleixo

Sketch & Foto Desenho

Sketch Item servisu : *Plum Concrete*

STA, 1+100-1+200




t	L	Distacia	Volume
0.12	4.00	100.00	48.00
Total			48.00

Observasaun iha tereno no Foto Aktual



Sketch Item servisu : *Plum Concrete*


STA, 1+060 - 1+085



t	L	Distacia	Volume
0.12	4.00	25.00	12.00
Total			12.00



STA, 1+400 - 1+443




t	L	Distacia	Volume
0.12	4.00	43.00	20.64
Total			20.64




STA, 1+600-1+630

Sketch Item servisu : *Line Drain*



T	w	Distacia	Volume
0.40	0.25	30.00	6.00
0.15	1.00		4.5
Total			10.50 m³





Naran Eng. Marcos X. de Araujo		2022																																				
Municipio	MUNICIPIO LIQUICA NO POSTOS																																					
Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	NOVEMBRU																														OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
	1	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going		
							Actual																													On Going		
	2	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going			
							Actual																													On Going		
	3	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going			
							Actual																													On Going		
	4	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going			
							Actual																													On Going		
	5	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going			
							Actual																													On Going		
	6	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going			
							Actual																													On Going		
7	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																												PHO				
						Actual																													On Going			
8	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
						Actual																													On Going			
9	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
						Actual																													On Going			
10	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
						Actual																													On Going			
11	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan</																																

Naran Eng. Marcos X. de Araujo						2022																															
Município	MUNICIPIO LIQUICA NO POSTOS																																				
Município / Posto	No. Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	1	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	2	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																														
							Actual																														
	3	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip Lda	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	4	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	5	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																														
							Actual																														
	6	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																														
							Actual																														
	7	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																														
							Actual																														
	8	New construction of isolation for covid 19 in chi liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																														
							Actual																														
	9	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTLMPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																														
							Actual																														
	10	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														PHO
							Actual																														
	11	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan.Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																														
	12	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan.Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going	
							Actual																														
	13	R4D Rural Road Spot Improvement Libaloe- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going	
							Actual																														
	14	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going	
							Actual																														
	15	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going	
							Actual																														
	16	Construction of Intersection in the Existing Dili-Liquica Road to Connect Acces Road From Tibar Bay Port (Nacional Road-A03)	Aitula.Unip.Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													On Going	
							Actual																														
TOTAL PROJETO ON-GOING																																					

Note:

Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspeasaun Pagamentu Anual iha tereinu

Implementasaun Plano Periode Inspeasaun iha tereinu

Iha Municipio Liquica

Prepara Husi :



(Eng. Marcos X. de Araujo)
Eng. ba Projeto Infraestrutura, Transportes e Irigasaun
Municipio Liquica ADN, I.P

Sertifika Husi :



(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e
Validasaun de Qualidade ADN.I.P

Aprova Husi :



(Eng. Januario Maia Guteres)
Adjunto Director Executivo ADN.I.P

 MINISTERIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL		 ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público		PLANU INSPESAUN																															
Naran Eng. Juninho António Abrantes da Cruz								2022																											
Município								MUNICIPIO LIQUICA NO POSTOS																											
Município / Posto								Novembro																							OBS				
Liquica Vila (LV)	No.	Naran Projeto		Naran Kompanha		No. Contrato		Kategoria		Dono do Projeto		Action																							
	1		Projeitu Konstrusaun Foun ESG Publico 01-Liquica		Roman Furak Unip. Lda.		NCB/16/MEJD/DNA/2021		LM		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going
	2		Konstrusaun ka Reabilitasaun ba EBF Mauboque		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going
	3		Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going
	4		Konstrusaun ka Reabilitasaun ba EPE Loidahar		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going
	5		Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclelema		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going
	6		Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going
	7		Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going
	8		New Construction of "Escola Café" Building at Liquica Municipality		RICS Unip. Lda.		NCB/138/MEJD-2021		FI		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						Foun
	Maubara (NBR)	1		Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)		Aleni Unip. Lda.		CID/600/PDIM/AM-LI/VIII/2019/03		PDIM		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																					
2		Konstrusaun ka Reabilitasaun ba EBF Gariana		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going	
3		Konstrusaun ka Reabilitasaun ba EBF 1,2 Tapo Manuhulu		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going	
4		Konstrusaun ka Reabilitasaun ESG-Paralelo Maubara		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going	
Bazartete (BZT)	1		Konstrusaun ESTV Maumeta - Liquisa (CA + CB)		Vida Diak Unip. Lda.		CID/600/PDIM/AM-LI/VIII/2019/02		PDIM		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						FHO
	2		Konstrusaun Moralha Foun Matadouro Tibar		Manoko Unip. Lda.		RDTL-MAP-PO2019:19726		LM		MINISTERIO AGRIKULTURA E PESCAS		Actual																						Paradu
	3		Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)		Milcha Unip. Lda.		(RFQ/19/029-Q-R)		LM		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						Paradu
	4		Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162		Culoco Unip. Lda.		Contract No.MOP-W-190184		LM		MINISTERIO DAS OBRAS PUBLICAS		Actual																						Pagamentu Seidauk 100%
	5		New Water Supply of Bairos PNTL Liquica		Holuli Unip. Lda.		SSS/054/MI-2019		FI		MINISTERIO DO INTERIOR		Plan																						FHO
	6		Konstrusaun Armagen Foun Matadouro (Bem Servisu)		Naesalobu Unip. Lda.		MAP-P02019:19532		LM		MINISTERIO AGRIKULTURA E PESCAS		Actual																						FHO
	7		New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste		Queson SQ Unip. Lda.		MS-DNA-RBK-20-178		LM		MINISTERIO SAUDE		Plan																						Pagamentu Seidauk 100%
	8		New Construction of Isolation for Covid 19 in Chi Liquica, Timor Leste		Senizu Unip. Lda.		MS-DNA-NCB-20-163		LM		MINISTERIO SAUDE		Actual																						PHO
	9		Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa		Tinocya Unip. Lda.		022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT		LM		MINISTERIO PLANU E ORDENAMENTU		Plan																						PHO
	10		New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta		Biamali Unip. Lda.		RDTL-MS-C19-DNA-DC-21-233		LM		MINISTERIO SAUDE		Actual																						On-going
	11		Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica		Zyc Unip. Lda.		RDTL-MS-C19-DNA-DC-21-228		LM		MINISTERIO SAUDE		Plan																						On-going
	12		Projeitu Konstrusaun Foun ESTV Leorema - Liquica		U-Rema Unip. Lda.		NCB/15/MEJD/DNA/2021		LM		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going
	13		Konstrusaun ka Reabilitasaun ba EPE Baura		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going
	14		Konstrusaun ka Reabilitasaun ba EPE Ermeta		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going
	15		Konstrusaun ka Reabilitasaun ba EPE Cassait		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Plan																						On-going
	16		Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro		Grupú Komunitariu				LM - TP		MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		Actual																						On-going
TOTAL PROJETO ON-GOING																																			

Note:

Plano Periode inspesaun iha tereinu

Relatoriu avaliasaun mensal iha Dili

Inspesaun Pagamentu Anual iha

Implementasaun Plano Periode inspesaun iha tereinu

Prepara Husi :

(Eng Juninho António Abrantes da Cruz)

Eng. ba Edificio Publico Agua e Saneamento Municipio Liquica ADN, I.P

Sertifika Husi :

(Eng Emerenciana da Costa Maia Freitas)

Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN, I.P

Aprova Husi :

(Eng Januario Maia Guterres)

Adjunto Director Executivo ADN, I.P

PLANU INSPESAUN																																				
Naran Eng. Antonia de Fatima Morais						2022																														
MUNICIPIO LIQUICA NO POSTOS																																				
						Novembro																								OBS						
						1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
Liquica Vila (LV)	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action																													
	1	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip. Lda.	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
	2	Konstrusaun ka Reabilitasaun ba EBF Mauboque	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
	3	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
	4	Konstrusaun ka Reabilitasaun ba EPE Loidahar	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
Maubara (MBR)	5	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclelema	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
	6	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
	7	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
	8	New Construction of "Escola Café" Building at Liquica Municipality	RICS Unip. Lda.	NCB/138/MEJD-2021	FI	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								Foun					
							Actual																													
	Bazartete (BZT)	1	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								Pagamentu Seidauk 100%				
							Actual																													
2		Konstrusaun ka Reabilitasaun ba EBF Gariana	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
3		Konstrusaun ka Reabilitasaun ba EBF 1,2 Tapo Manuhulu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
4		Konstrusaun ka Reabilitasaun ESG-Paralelo Maubara	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going					
							Actual																													
1		Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								FHO					
							Actual																													
2		Konstrusaun Morilha Foun Matadoro Tibar	Manoko Unip. Lda.	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																								Paradu					
							Actual																													
3		Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip. Lda.	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								Paradu					
							Actual																													
4		Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unip. Lda.	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																								Pagamentu Seidauk 100%					
							Actual																													
5		New Water Supply of Bairos PNTL Liquica	Holuli Unip. Lda.	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																								FHO					
							Actual																													
6		Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu Unip. Lda.	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																								FHO					
							Actual																													
7		New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Queson SQ Unip. Lda.	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																								Pagamentu Seidauk 100%					
							Actual																													
8		New Construction of Isolation for Covid 19 in Chi Liquica, Timor Leste	Senizu Unip. Lda.	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																								PHO					
							Actual																													
9	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya Unip. Lda.	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																								PHO						
						Actual																														
10	New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta	Biamali Unip. Lda.	RDTL-MS-C19-DNA-DC-21-233	LM	MINISTERIO SAUDE	Plan																								On-going						
						Actual																														
11	Supply and Installation Connection for Isolation and Labororium Building Maumeta Liquica	Zyc Unip. Lda.	RDTL-MS-C19-DNA-DC-21-228	LM	MINISTERIO SAUDE	Plan																								On-going						
						Actual																														
12	Projeitu Konstrusaun Foun ESTV Leorema - Liquica	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going						
						Actual																														
13	Konstrusaun ka Reabilitasaun ba EPE Baura	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going						
						Actual																														
14	Konstrusaun ka Reabilitasaun ba EPE Ermeta	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going						
						Actual																														
15	Konstrusaun ka Reabilitasaun ba EPE Cassait	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going						
						Actual																														
16	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																								On-going						
						Actual																														
TOTAL PROJETO ON-GOING																																				
28																																				

Note: ☐ Plano Periode inspesaun iha tercinu ☐ Relatoriu avaliasuan mensal iha Dili ☐ Inspesaun Pagamentu Anual iha ☐ Implementasaun Plano Periode inspesaun iha tercinu

Prepara Husi :

 (Eng. Antonia de Fatima Morais)
 Eng. ba Edificio Publico Agua e Saneamento Municipio
 Liquica ADN, I.P

Sertifika Husi :
