



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATÓRIU MENSÁL
IMPLEMENTASAUN
PROJETUS MUNISÍPIU MANATUTO

DEZEMBRO 2022




SUMÁRIO
RELATÓRIO
IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICIPIO
MANATUTO
DESEMBRO 2022

Prepara Husi :



(Eng. Fabiano F.M Madeira)
Eng. ba Projecto Edificio Publico Beé no
Saneamento Municipio Manatuto, ADN, I.P



(Eng. Jose R. Carlos Gusmão)
Eng. ba Projecto Insfrasturctura e
Irigasaun Municipiu Manatuto, ADN, I.P



(Eng. Adonis Julio Fernandes)
Eng. ba Projecto ME, ADN, I.P



(Eng Domingos da Costa e Silva)
Eng. ba Projecto Insfrasturctura e
Irigasaun Municipiu Manatuto, ADN, I.P

Verifika Husi :



(Arc. Francisco X D D Jeronimo)
**Eng. Senior ba Edificio Publiku no Beé
Saneamentu, ADN, I.P**



(Eng. Remigio da C. S. dos Santos)
**Eng. Senior ba Projetu Infraestrutura e
Irigasaun, ADN, I.P**



(Eng. Deolindo de F. Marques)
Chefe Seksaun ba Projetu M.E & ITC, ADN, I.P

Sertifika Husi :




(Eng. Emerenciana da Costa Maia Freitas)
**Coordenadora Unidade de Controlo e Validação de Qualidade,
ADN, I.P**

Aprova Husi :



(Mariano Renato Monteiro da Cruz, S. T, M. Eng)
Director Executivo, ADN, I.P



INDICE

SUMÁRIO	1
INDICE	3
I. INTRODUSAUN	3
1.1 Enkuadramentu Legal	3
1.2 Perfil Municipio Manatuto	3
1.3. Lista Projectos	7
II. PROGRESU FISIKU	25
2.1 Progreso Fisiku Kada Fulan	25
III. OBSTÁCLO IHA TERENU	26
3.1 Obstáculo Servisu Iha Terenu	26
IV. REKOMENDASAUN IHA TERENU	27
4.1 Rekomendasaun Servisu Iha Terenu	27

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias	4
Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Manatuto	4
Tabela 1.2 : Lista Asset ADN,I.P Municipio Manatuto	6
Tabela 1.3.1 : Projecto Municipio Manatuto Por Fundus Finansiamientos	7
Tabela 1.3.2 : Projecto Municipio Manatuto Por Sectores	11
Tabela 1.3.3 : Projecto Municipio Manatuto Por Ministerio	18
Tabela 1.4 : Dadus Populasaun Munisipiu Manatuto	25

I. INTRODUSAUN.

1.1.Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Presidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho qualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefísiu ne'ebe razoável no viável.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvementu nian.
2. Halo fiskalizaun no sertifikasaun qualidade ba projetu sira iha programa Kapital Desenvolvementu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liuhusi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria

1.2. Perfil Municipio Manatuto



Mapa 2 hatudu pozisaun jeográfika Administrasaun Munisipal Manatuto iha luan 1,706 km² ho populasaun nain 42,742 tuir Sensus 2010. Administrasaun Munisipal Manatutoiha Postos Administrativos nen (6), Sukus 29 no aldeias 99 , mak hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos, Sucos no Aldeias.

Natarbora		Laclo		Laklubar		Laleia	
Sukus	Aldeia	Sukus	Aldei	Suku	Aldeia	Sukus	Aldeias
Aubeon	2	Hohorai	4	Batara	4	Cairui	7
Barique	2	Locomesak	5	Hatu ma quere k	3	Hatulara n	3
Fatuwaque	2	Uma kaduak	3	Funar	4	Lifau	3
Manehat	3	Uma naruk	4	Mane lima	6		
Uma Boco	2			-	8		
				Sanan a Na'i	4		
Total	11		18		30		13

Data husi: Livro 3 B OJE 2021, pag 69

Manatuto		Soibada	
sukus	Aldeia	sukus	aldeias
Ailili	2	Fatuma querek	2
Aitekas	4	Leo-hat	2
Cribas	5	Manlala	2
Iliheu	5	Maun Fahe	2
Ma'abat	2	Somoro	2
Sau	2		
	22		10

Tabela 1.1: Forca de Trabalho ADN, I.P Municipio Manatuto

Forca de Trabalho ADN,I.P Municipio Manututu								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	3	3				3	
2	Administrasau n no Financas	0	0				0	
3	Motorista	1	1				1	
4	Seguransa	0	0				0	
Total		4					4	

Tabela 1.2 : Lista Asset ADN,I.P Municipio Manatuto.

ASET ADN,IP MUNICIPIO MANATUTO								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1	1					
2	Kareta	1	1					
3	Desktop HP / Monitor	1	1					
4	Laptop HP	1	1					
5	Printer Cannon	1	1					
6	UPS	1	1					
7	Armario File	2	2					
8	Armario Tau hena	3	3					
9	Meja escritorio	1	1					
10	Meja han	1	1					
11	Meja TV (kiik)	1	1					
12	Kadeira escritorio	6	6					
13	Kadeira han	4	4					
14	Sofa	1 Set	1 Set					
15	Springbed +sumasu 4+sprei 3	3 Set	3 Set					
16	Jeleira	1	1					
17	Water Dispenser	1	1					
18	TV + Parabola	1 Set	1 Set					
19	AC	4	4					
20	Kipas Angin	4	4					
21	Kompor	1	1					
22	Kompor Gas	1	1					

23	Rack sepatu	3	3					
24	Rack Piring	1	1					
25	Lampu	11	11					
26	Water Pump Sanyo	1	1					

1.3 : Lista Projectos

Projetu hotu ne'ebe akumulula iha lista ne'e bazeia ba dadus projetu ne'ebe sei lao hela no mos projeto ne'ebe abandona ona tinan barak, projeto hirak ne'e fahe tuir lista 1.3.1 Projeto Por Fundus Finansiamientos, 1.3.2 Projeto Por Sectors no 1.3.3 Projeto Por Ministerios.

1.3.1 : Lista Projectos Municipio Manatuto Por Fundus Finansiamientos

NO	POSTO ADMINISTRATIVU	TOTAL FI+Fundu Covid -19+LM-BE+LM-CD+LM-TP+PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique	11	\$ 2,476,084.64	44.42%
2	Laclo	9	\$ 49,767,971.56	87.65%
3	Laclubar	11	\$ 36,930,495.47	86.10%
4	Laleia	4	\$ 534,417.22	35.39%
5	Manatuto Villa	21	\$ 45,928,020.17	82.15%
6	Soibada	7	\$ 4,470,048.98	86.06%
	Grand Total	63	\$ 140,107,038.04	84.43%

NO	POSTO ADMINISTRATIVU	FI		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique		\$ -	0.00%
2	Laclo	3	\$ 48,698,873.04	87.85%
3	Laclubar	2	\$ 35,075,150.37	88.18%
4	Laleia		\$ -	0.00%
5	Manatuto Villa	7	\$ 44,188,670.20	82.95%
6	Soibada	1	\$ 3,553,954.20	93.93%
	Grand Total	13	\$ 131,516,647.81	86.46%

NO	POSTO ADMINISTRATIVU	Fundo Covid-19		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique		\$ -	0.00%
2	Laclo		\$ -	0.00%
3	Laclubar		\$ -	0.00%
4	Laleia		\$ -	0.00%
5	Manatuto Villa	4	\$ 665,658.27	86.96%
6	Soibada		\$ -	0.00%
	Grand Total	4	\$ 665,658.27	86.96%

NO	POSTO ADMINISTRATIVU	LM-BS		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique	2	\$ 404,938.08	54.93%
2	Laclo	1	\$ 50,745.00	34.95%
3	Laclubar	2	\$ 675,432.39	40.19%
4	Laleia		\$ -	0.00%
5	Manatuto Villa	1	\$ 29,275.84	15.92%
6	Soibada		\$ -	0.00%
	Grand Total	6	\$ 1,160,391.31	44.49%

NO	POSTO ADMINISTRATIVU	LM-CD		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique	7	\$ 1,876,648.24	38.63%
2	Laclo	2	\$ 646,243.79	84.96%
3	Laclubar	2	\$ 661,982.34	55.55%
4	Laleia	2	\$ 305,588.74	8.32%
5	Manatuto Villa	1	\$ 175,266.63	98.51%
6	Soibada	4	\$ 630,201.31	47.08%
	Grand Total	18	\$ 4,295,931.05	49.74%

NO	POSTO ADMINISTRATIVU	LM-TP		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique		\$ -	0.00%
2	Laclo	1	\$ 98,147.27	23.56%
3	Laclubar	2	\$ 202,223.29	25.59%
4	Laleia	1	\$ 86,883.29	25.06%
5	Manatuto Villa	5	\$ 382,490.63	15.84%
6	Soibada	1	\$ 102,512.31	27.56%
	Grand Total	10	\$ 872,256.79	21.27%

NO	POSTO ADMINISTRATIVU	PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	Barique	2	\$ 194,498.32	78.34%
2	Laclo	2	\$ 273,962.46	91.17%
3	Laclubar	3	\$ 315,707.08	56.94%
4	Laleia	1	\$ 141,945.19	100.00%
5	Manatuto Villa	3	\$ 486,658.60	52.57%
6	Soibada	1	\$ 183,381.16	100.00%
	Grand Total	12	\$ 1,596,152.81	72.87%

1.3.2 : Lista Projectos Municipio Manatuto Por Sectors

NO	POR SECTOR	TOTAL MUNICIPIO MANATUTO		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA	1	\$ 370,511.25	15.83%
2	AGUA E SANEAMENTO	1	\$ 162,377.94	41.85%
3	COMERCIO	1	\$ 153,942.39	84.29%
4	EDIFICIOS PUBLICOS	9	\$ 1,430,360.48	62.95%
5	EDUKASAUN	12	\$ 1,236,740.28	43.43%
6	ELETRIFIKASAUN NASIONAL	2	\$ 1,076,003.44	78.57%
7	ESTRADAS	19	\$ 13,102,209.38	72.95%
8	FLOOD CONTROL	1	\$ 242,560.14	63.68%
8	IMPRESTIMO	4	\$ 115,112,106.35	86.96%
9	JUVENTUDE NO DESPORTU	1	\$ 2,362,976.44	76.00%
10	MANUTENSAUN NO REHABILITASAUN	2	\$ 157,560.52	41.96%
11	PONTES	1	\$ 3,553,954.20	93.93%
12	SAUDE	7	\$ 840,178.96	77.51%
13	TURISMO	2	\$ 305,556.27	28.66%
Grand Total		63	\$ 140,107,038.04	84.43%

NO	POR SECTOR	Barique		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA	1	\$ 370,511.25	15.83%
2	AGUA E SANEAMENTO	1	\$ 162,377.94	41.85%
3	COMERCIO		\$ -	0.00%
4	EDIFICIOS PUBLICOS	1	\$ 408,460.73	78.09%
5	EDUKASAUN		\$ -	0.00%
6	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
7	ESTRADAS	3	\$ 940,115.74	29.92%
8	FLOOD CONTROL	1	\$ 242,560.14	63.68%
8	IMPRESTIMO		\$ -	0.00%
9	JUVENTUDE NO DESPORTU		\$ -	0.00%
10	MANUTENSAUN NO REHABILITASAUN	2	\$ 157,560.52	41.96%
11	PONTES		\$ -	0.00%
12	SAUDE	2	\$ 194,498.32	78.34%
13	TURISMO		\$ -	0.00%
	Grand Total	11	\$ 2,476,084.64	44.42%

NO	POR SECTOR	Laclo		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		\$ -	0.00%
2	AGUA E SANEAMIENTO		\$ -	0.00%
3	COMERCIO	1	\$ 153,942.39	84.29%
4	EDIFICIOS PUBLICOS	2	\$ 170,765.07	80.67%
5	EDUKASAUN	1	\$ 98,147.27	23.56%
6	ELETRIFIKASAUN NASIONAL	1	\$ 380,582.61	72.08%
7	ESTRADAS	3	\$ 649,558.35	84.99%
8	FLOOD CONTROL		\$ -	0.00%
8	IMPRESTIMO	1	\$ 48,314,975.87	87.98%
9	JUVENTUDE NO DESPORTU		\$ -	0.00%
10	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
11	PONTES		\$ -	0.00%
12	SAUDE		\$ -	0.00%
13	TURISMO		\$ -	0.00%
Grand Total		9	\$ 49,767,971.56	87.65%

NO	POR SECTOR	Laclubar		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		\$ -	0.00%
2	AGUA E SANEAMENTO		\$ -	0.00%
3	COMERCIO		\$ -	0.00%
4	EDIFICIOS PUBLICOS		\$ -	0.00%
5	EDUKASAUN	2	\$ 202,223.29	25.59%
6	ELETRIFIKASAUN NASIONAL	1	\$ 695,420.83	82.11%
7	ESTRADAS	4	\$ 1,337,414.73	47.79%
8	FLOOD CONTROL		\$ -	0.00%
8	IMPRESTIMO	1	\$ 34,379,729.54	88.30%
9	JUVENTUDE NO DESPORTU		\$ -	0.00%
10	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
11	PONTES		\$ -	0.00%
12	SAUDE	3	\$ 315,707.08	56.94%
13	TURISMO		\$ -	0.00%
	Grand Total	11	\$ 36,930,495.47	86.10%

NO	POR SECTOR	Laleia		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		\$ -	0.00%
2	AGUA E SANEAMENTO		\$ -	0.00%
3	COMERCIO		\$ -	0.00%
4	EDIFICIOS PUBLICOS	2	\$ 419,275.62	33.85%
5	EDUKASAUN	1	\$ 86,883.29	25.06%
6	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
7	ESTRADAS	1	\$ 28,258.31	90.00%
8	FLOOD CONTROL		\$ -	0.00%
8	IMPRESTIMO		\$ -	0.00%
9	JUVENTUDE NO DESPORTU		\$ -	0.00%
10	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
11	PONTES		\$ -	0.00%
12	SAUDE		\$ -	0.00%
13	TURISMO		\$ -	0.00%
	Grand Total	4	\$ 534,417.22	35.39%

NO	POR SECTOR	Manatuto Villa		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		\$ -	0.00%
2	AGUA E SANEAMIENTO		\$ -	0.00%
3	COMERCIO		\$ -	0.00%
4	EDIFICIOS PUBLICOS	3	\$ 364,960.55	72.47%
5	EDUKASAUN	6	\$ 563,592.96	40.61%
6	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
7	ESTRADAS	5	\$ 9,583,559.45	81.39%
8	FLOOD CONTROL		\$ -	0.00%
8	IMPRESTIMO	2	\$ 32,417,400.94	84.01%
9	JUVENTUDE NO DESPORTU	1	\$ 2,362,976.44	76.00%
10	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
11	PONTES		\$ -	0.00%
12	SAUDE	2	\$ 329,973.56	96.69%
13	TURISMO	2	\$ 305,556.27	28.66%
	Grand Total	21	\$ 45,928,020.17	82.15%

NO	POR SECTOR	Soibada		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		\$ -	0.00%
2	AGUA E SANEAMIENTO		\$ -	0.00%
3	COMERCIO		\$ -	0.00%
4	EDIFICIOS PUBLICOS	1	\$ 66,898.51	55.80%
5	EDUKASAUN	2	\$ 285,893.47	74.03%
6	ELETRIFIKASAUN NASIONAL		\$ -	0.00%
7	ESTRADAS	3	\$ 563,302.80	46.05%
8	FLOOD CONTROL		\$ -	0.00%
8	IMPRESTIMO		\$ -	0.00%
9	JUVENTUDE NO DESPORTU		\$ -	0.00%
10	MANUTENSAUN NO REHABILITASAUN		\$ -	0.00%
11	PONTES	1	\$ 3,553,954.20	93.93%
12	SAUDE		\$ -	0.00%
13	TURISMO		\$ -	0.00%
	Grand Total	7	\$ 4,470,048.98	86.06%

1.3.3 : Lista Projectos Municipio Manatuto Por Ministerios

NO	POR MINISTERIO	GRAND TOTAL		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	4	\$ 567,521.53	61.59%
2	MINISTERIO AGRIKULTURA E PESCAS	1	\$ 370,511.25	15.83%
3	MINISTERIO DA JUSTICA	1	\$ 29,275.84	15.92%
4	MINISTERIO DAS OBRAS PUBLICAS	30	\$ 133,406,771.97	85.55%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	13	\$ 1,303,638.79	44.07%
6	MINISTERIO PLANU E ORDENAMENTU	1	\$ 277,330.43	0.00%
7	MINISTERIO SAUDE	9	\$ 1,175,863.67	77.48%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$ 204,687.39	72.06%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 408,460.73	78.09%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	1	\$ 2,362,976.44	76.00%
Grand Total		63	\$ 140,107,038.04	84.43%

NO	POR MINISTERIO	Barique		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO AGRICULTURA E PISCAS	1	\$ 370,511.25	15.83%
3	MINISTERIO DA JUSTICA		\$ -	0.00%
4	MINISTERIO DAS OBRAS PUBLICAS	7	\$ 1,502,614.34	37.92%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		\$ -	0.00%
6	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
7	MINISTERIO SAUDE	2	\$ 194,498.32	78.34%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0.00%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	\$ 408,460.73	78.09%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0.00%
Grand Total		11	\$ 2,476,084.64	44.42%

NO	POR MINISTERIO	Laclo		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	\$ 120,020.07	100.00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0.00%
3	MINISTERIO DA JUSTICA		\$ -	0.00%
4	MINISTERIO DAS OBRAS PUBLICAS	5	\$ 49,345,116.83	87.81%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 98,147.27	23.56%
6	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
7	MINISTERIO SAUDE		\$ -	0.00%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	\$ 204,687.39	72.06%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0.00%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0.00%
	Grand Total	9	\$ 49,767,971.56	87.65%

NO	POR MINISTERIO	Laclubar		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0.00%
3	MINISTERIO DA JUSTICA		\$ -	0.00%
4	MINISTERIO DAS OBRAS PUBLICAS	6	\$ 36,412,565.10	86.69%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	2	\$ 202,223.29	25.59%
6	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
7	MINISTERIO SAUDE	3	\$ 315,707.08	56.94%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0.00%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0.00%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0.00%
	Grand Total	11	\$ 36,930,495.47	86.10%

NO	POR MINISTERIO	Laleia		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	\$ 141,945.19	100.00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0.00%
3	MINISTERIO DA JUSTICA		\$ -	0.00%
4	MINISTERIO DAS OBRAS PUBLICAS	1	\$ 28,258.31	90.00%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	\$ 86,883.29	25.06%
6	MINISTERIO PLANU E ORDENAMENTU	1	\$ 277,330.43	0.00%
7	MINISTERIO SAUDE		\$ -	0.00%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0.00%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0.00%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0.00%
	Grand Total	4	\$ 534,417.22	35.39%

NO	POR MINISTERIO	Manatuto Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	2	\$ 305,556.27	28.66%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0.00%
3	MINISTERIO DA JUSTICA	1	\$ 29,275.84	15.92%
4	MINISTERIO DAS OBRAS PUBLICAS	7	\$ 42,000,960.39	83.41%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	6	\$ 563,592.96	40.61%
6	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
7	MINISTERIO SAUDE	4	\$ 665,658.27	86.96%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0.00%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0.00%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	1	\$ 2,362,976.44	76.00%
Grand Total		21	\$ 45,928,020.17	82.15%

NO	POR MINISTERIO	Soibada		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		\$ -	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		\$ -	0.00%
3	MINISTERIO DA JUSTICA		\$ -	0.00%
4	MINISTERIO DAS OBRAS PUBLICAS	4	\$ 4,117,257.00	87.38%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	\$ 352,791.98	70.57%
6	MINISTERIO PLANU E ORDENAMENTU		\$ -	0.00%
7	MINISTERIO SAUDE		\$ -	0.00%
8	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		\$ -	0.00%
9	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		\$ -	0.00%
10	SECRETARIADO ESTADO JUVENTUDE E DESPORTU		\$ -	0.00%
	Grand Total	7	\$ 4,470,048.98	86.06%

1.4. Dadus Populasaun Munisipiu Manatuto

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0- 14+65 ba leten)	
		Male	Female	Male	Female
Barique	5,833	1,924	1,617	1,183	1,109
Laclo	8,193	2,250	2,185	1,919	1,838
Laclubar	12,777	3,445	3,571	2,924	2,836
Laleia	3,930	1,181	1,189	817	743
Manatuto	15,446	4,741	4,609	3,109	2,987
Soibada	3,511	237	213	239	259

Fontes : Projeksaun Populasaun bazea ba Census Populasaun no Umakain 2015,

Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1. Progressu Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan nia laran, husi lista #anexu B hatudu progresu aktual fulan ida ne'e ho nia presentagen servisu, montante aktual bazeia ba orsamento ne'ebe hetan husi progresu fulan ida ne'e, ikus liu prentangen aktual fulan ida ne'e hatudu progresu fisiku komulativu husi prosentun anterior no fulan ida ne'e nian, lista kompletu ba detallu bele hare iha #anexu B, detallu ba back-up #anexu C, no Instrusaun Servisu #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1. Obtáclo Servisu iha Terenu

Observasaun geral ba projeito hirak nebe mak implementa iha Munisipio Manatuto

1. Projeito Lao la tuir tempo nebee asina entre parte rua
2. Laiha tekniko supervisaun husi projeito nain atu halo kontrolo diaramente
3. Tekniko kompanha la iha tereno
4. Skill badaen neebe mak la dun professional

Obstalku teknik A.D.N hasoru

1. Distansia ne'ebe dook difikulta teknik atu servisu lalais
2. Kondisaun estrada neébe a'at
3. Kontraktor sira ne'ebe mak servisu iha terreno barak mak la tuir Spesifikasaun ne'ebe iha kontartu laran.
4. Planu Mapamentu Enginheiro Munisipiu la konsege realiza tuir planu tamba hare hosi nia distansia ne'ebe dook.
5. Sistema dropbox iha Munisipiu dala ruma iha problema lina internet

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Presija tebes atu aumenta ema iha Munisipiu atu nune bele halo servisu ba administrasaun ne'ebe efetivo.
2. Sebele sistema dropbox tau mos iha dekstop Munisipiu para la bele atraja ami nia servisu.

Note: Asinatura Husi Eng. Municipio Manatuto

Força de Trabalho ADN,I.P Municipio Manatuto						
No	Deskrisaun	Identidade				Asinatura
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	
1	Enjineiru	Fabiano F.M Madeira	235	Enjineiru EPAS		
		José R. Carlos Gusmão	168	Enjineiru ITI		
		Domingos da Costa e Silva	250	Enjineiru ITI		

		Adonis Julio Fernandes	152	Enjineiru ME		
2	Enjineira	Olivia Soares	112	Enjineira VEBD		
3	Motorista	Timoteo da Silva Morais	120	Motorista		

#ANEXU A

23,983,565.18

MUNICIPIO MANATUTO (LISTA GERAL)

Localizasaun Projeto

NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	MONT. KONT. (\$)	DATA KONT.	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	Status Projecto	OBS
1	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	\$ 2,561,405.06	Aug. 25, 2018	63.80%	57.33%	\$ 1,468,479.04	\$ 1,092,926.02	ON-GOING	
2	Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Nananiu, Unip. Lda JV Ina Forek, Lda	\$ 3,029,514.40	Aug. 25, 2017	89.20%	79.82%	\$ 2,418,275.38	\$ 611,239.02	ON-GOING	
3	Construção de novo Estádio de Futebol em Manatuto	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Manatuto Villa	Manatuto	Obrai Unipessoal, Lda	\$ 2,362,976.44	June 30, 2015	82.08%	76.00%	\$ 1,795,843.89	\$ 567,132.55	ON-GOING	
4	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	R.D Interior Junior Construction / Hebei Road and Bridge Group	\$ 28,011,854.94	Feb. 10, 2014	94.91%	85.62%	\$ 23,983,565.18	\$ 4,028,289.76	ON-GOING	
5	Consultant Supervision (M-L & L-N)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	Sinotech Engineering Consultant	\$ 4,405,546.00	Sept. 3, 2014	73.76%	73.76%	\$ 3,249,684.75	\$ 1,155,861.25	ON-GOING	
6	Konstrusaun ESTV Beadi-Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Manatuto Villa	Manatuto	Ralan Unip. Lda	\$ 181,102.33	Oct. 10, 2019	92.91%	92.91%	\$ 168,257.35	\$ 12,844.98	FHO	
7	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Unip. Lda	\$ 79,155.54	Dec. 18, 2019	88.07%	79.26%	\$ 62,737.67	\$ 16,417.87	ON-GOING	
8	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Lda	\$ 226,400.73	Dec. 18, 2019	43.70%	10.97%	\$ 24,834.32	\$ 201,566.41	ON-GOING	
9	Servisu Manutensaun Edifisiu CRC Munisipiu Manatuto	MINISTERIO DA JUSTICA	LM-BS	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Baboe Unip Lda	\$ 29,275.84	March 1, 2020	15.92%	15.92%	\$ 4,660.85	\$ 24,614.99	ON-GOING	
10	New Construction of Laboratory for Covid 19 at Manatuto, Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Manatuto Villa	Manatuto	Kartini Unipessoal Lda	\$ 66,989.91	Jan. 7, 2021	95.34%	94.75%	\$ 63,474.73	\$ 3,515.18	FHO	Projecto ne Finaliza ona
11	New Construction of Gabion wall in Somasi River	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Forte, Unip. Lda	\$ 1,486,885.83	Sept. 7, 2017	100.00%	98.72%	\$ 1,467,902.28	\$ 18,983.55	FHO	Projecto ne Finaliza ona
12	Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu, Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Ilalun, Lda	\$ 2,330,487.53	July 25, 2016	97.52%	97.52%	\$ 2,272,774.64	\$ 57,712.89	FHO	Progresso Fisiko iha Tereno ba Fulan Dezembro Aumenta 1.11%
13	Konstrusaun Fatin Isolamentu iha Municipiu Manatuto, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Manatuto Villa	Manatuto	Talamori Unip.Lda	\$ 262,983.65	09-Dec-20	100.00%	97.19%	\$ 255,587.87	\$ 7,395.78	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Dezembro Aumenta 8.03%
14	New Construction of Gabions Tower No. 4 Section Manatuto - Baucau Municipality Manatuto	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Manatuto Villa	Manatuto	Giovania Unip. Lda	\$ 175,266.63		98.51%	98.51%	\$ 172,646.46	\$ 2,620.17	FHO	
15	New Construction of Fence at Isolation Covid-19 in Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	K-6, UNIPESOAAL LDA	\$ 257,748.51	Jan. 12, 2022	88.89%	74.56%	\$ 192,164.43	\$ 65,584.08	ON-GOING	
16	Supply and Instalition Main Power For Isolation and Laboratorium Building Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Fraternity Unipessoal Lda	\$ 77,936.20	Jan. 12, 2022	92.28%	86.81%	\$ 67,657.50	\$ 10,278.70	ON-GOING	
17	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE ESG KAY RALA	\$ 62,996.83	Oct. 15, 2021	31.90%	24.62%	\$ 15,507.66	\$ 47,489.17	ON-GOING	
18	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF RENTAU	\$ 64,383.50	Oct. 15, 2021	28.55%	24.73%	\$ 15,921.64	\$ 48,461.86	ON-GOING	
19	Konstrusaun ka Rehabilitasaun ba PE Rembor	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE PE REMBOR	\$ 88,918.34	Oct. 15, 2021	22.77%	0.00%	\$ -	\$ 88,918.34	ON-GOING	
20	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF OBRATO	\$ 66,144.65	Oct. 15, 2021	38.17%	22.03%	\$ 14,570.40	\$ 51,574.25	ON-GOING	

NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	MONT. KONT. (\$)	DATA KONT.	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	Status Projeto	OBS
21	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF BAHADIK	\$ 100,047.31	Oct. 15, 2021	14.58%	14.58%	\$ 14,590.20	\$ 85,457.11	ON-GOING	
22	Rehabilitasaun Kampu Foteboll iha Postu Administrativu Laleia	MINISTERIO PLANU E ORDENAMENTU	LM-CD	EDIFICIOS PUBLICOS	Laleia	Manatuto	DCO Unip.Lda	\$ 277,330.43	July 18, 2019	0.00%	0.00%	\$ -	\$ 277,330.43	ON-GOING	
23	Konstrusaun Edificio Posto Administrativo Laleia	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Laleia	Manatuto	Hare Unip.Lda	\$ 141,945.19	Oct. 8, 2019	100.00%	100.00%	\$ 141,945.19	\$ -	FHO	Projecto ne Finaliza ona
24	R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laleia	Manatuto	As Jazesia Unipessoal Lda	\$ 28,258.31	June 10, 2021	99.86%	90.00%	\$ 25,432.48	\$ 2,825.83	ON-GOING	
25	Konstrusaun ka Rehabilitasaun ba EP Cairui	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laleia	Manatuto	MEJD PKRIE EP CAIRUI	\$ 86,883.29	Oct. 15, 2021	28.43%	25.06%	\$ 21,771.04	\$ 65,112.25	ON-GOING	
26	New Installation Mv, Lv Line & House Connection From Laclubar Vila to Funar And Fatuk Manu - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laclubar	Manatuto	Tasibala III Unip. Lda	\$ 695,420.83	June 7, 2016	91.52%	82.11%	\$ 571,034.27	\$ 124,386.56	ON-GOING	
27	Road Network Upgrading Sector Project (RNUSP)Upgrading and Maintenance of Laclubar Junction - Natarbora Road (Sta. 100+360 - Sta. 144+995)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Laclubar	Manatuto	China Nuclear Industry 22ND Construction Co; LTD	\$ 34,379,729.54	Nov. 20, 2014	92.04%	88.30%	\$ 30,356,507.52	\$ 4,023,222.02	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Dezembro Aumenta 0.38%
28	Konstrusaun Posto Saude Iha iha Suku Funar - Laklubar	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Ladiama Unip. Lda	\$ 112,967.53	Sept. 23, 2019	22.06%	19.85%	\$ 22,429.62	\$ 90,537.91	ON-GOING	
29	Konstrusaun Rezidencia Pesoal Iha iha Suku Funar - Laklubar	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Tonijo Unip. Lda	\$ 81,776.84	Oct. 8, 2019	100.00%	97.56%	\$ 79,782.68	\$ 1,994.16	FHO	Projecto ne Finaliza ona
30	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Hatuwari Unip. Lda	\$ 481,029.67	Aug. 25, 2020	54.37%	11.80%	\$ 126,501.30	\$ 354,528.37	ON-GOING	
31	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Ryzena Unipessoal Lda	\$ 194,402.72	Dec. 20, 2019	82.83%	74.55%	\$ 144,924.09	\$ 49,478.63	ON-GOING	
32	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Sun Rise Golden Construction 02 Lda	\$ 448,209.39	June 10, 2021	95.04%	82.05%	\$ 367,756.59	\$ 80,452.80	ON-GOING	
33	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Adahiak Orlao Unipessoal Lda	\$ 213,772.95	June 10, 2021	7.12%	0.00%	\$ -	\$ 213,772.95	ON-GOING	
34	Kontinuasaun Konst. Postu Saude Iha Suku Fatumakerek	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Hatuwari Unip. Lda	\$ 120,962.71	July 28, 2019	71.23%	64.11%	\$ 77,547.51	\$ 43,415.20	ON-GOING	
35	Konstrusaun ka Rehabilitasaun ba EBF Batara	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF BATARA	\$ 102,060.99	Oct. 15, 2021	25.60%	25.60%	\$ 26,125.75	\$ 75,935.24	ON-GOING	
36	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF AISIU-UM	\$ 100,162.30	Oct. 15, 2021	25.60%	25.59%	\$ 25,626.77	\$ 74,535.53	ON-GOING	
37	Construction of New Steel Bridge 100m in Milotu Sahe river, jct.Fatucamanau, Soibada, Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Soibada	Manatuto	FIRDO UNIPESOAAL LDA	\$ 3,553,954.20	Feb. 27, 2017	100.00%	93.93%	\$ 3,338,377.84	\$ 215,576.36	ON-GOING	
38	Konstrusaun ESTV Soibada Manatuto (CA + CB)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 183,381.16	Sept. 23, 2019	100.00%	100.00%	\$ 183,381.18	\$ (0.02)	FHO	Projecto ne Finaliza ona
39	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 10 Soibada to Soibada Town	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	\$ 164,154.00	March 25, 2020	70.00%	70.00%	\$ 114,907.80	\$ 49,246.20	ON-GOING	
40	R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 203,036.57	June 10, 2021	48.43%	41.78%	\$ 84,819.65	\$ 118,216.92	ON-GOING	
41	R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Ryzena Unipessoal Lda	\$ 196,112.23	June 10, 2021	50.20%	30.42%	\$ 59,662.31	\$ 136,449.92	ON-GOING	
42	Projetu Rehabilitasaun Ensina Sekundariu Tekniku Vokasional Soibada, Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDIFICIOS PUBLICOS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 66,898.51	Nov. 26, 2021	78.97%	55.80%	\$ 37,330.95	\$ 29,567.56	ON-GOING	
43	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Soibada	Manatuto	MEJD PKRIE EBC WEAIHUDIK	\$ 102,512.31	Oct. 15, 2021	31.76%	27.56%	\$ 28,253.89	\$ 74,258.42	ON-GOING	
44	Construction of Sahen Bridge Approach Protection (A14) Manatuto (MPW-W-190157) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	FLOOD CONTROL	Barique	Manatuto	Yoku Unipessoal Lda	\$ 242,560.14	Oct. 24, 2019	70.75%	63.68%	\$ 154,455.92	\$ 88,104.22	ON-GOING	

NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNI.	NARAN COMP.	MONT. KONT. (\$)	DATA KONT.	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. (\$)	BAL. (\$)	Status Projecto	OBS
45	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	MINISTERIO AGRICULTURA E PESCAS	LM-CD	AGRICULTURA	Barique	Manatuto	Tasibala II Const	\$ 370,511.25	Sept. 13, 2016	17.59%	15.83%	\$ 58,645.87	\$ 311,865.38	Abandona	Abandona
46	Rural Roads Routine Maintenance Uma Boco - Aubeon, Sta. 0+000 - 6+000, Manututo Municipality (Manutensaun)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Zenobia Diak Unip.Lda	\$ 15,875.56	Jan. 7, 2017	100.00%	87.26%	\$ 13,853.09	\$ 2,022.47	ON-GOING	
47	Konstrusaun Postu Saude Aimeta Laran-Barique	MINISTERIO SAUDE	PDIM	SAUDE	Barique	Manatuto	Malack II Unip. Lda	\$ 116,914.88	Sept. 23, 2019	71.10%	63.99%	\$ 74,817.23	\$ 42,097.65	ON-GOING	
48	Construction of Residence for Health Staff in Suku Aimeta Laran-Barique	MINISTERIO SAUDE	PDIM	SAUDE	Barique	Manatuto	Macucuren Unip. Lda	\$ 77,583.44	Oct. 8, 2019	99.96%	99.96%	\$ 77,556.13	\$ 27.31	FHO	Projecto ne Finaliza ona
49	Konstrusaun Sistema Bee Mos Iha Suco Aubeon no Aimetalan /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Barique	Manatuto	Malaca Unip Lda	\$ 162,377.94	Oct. 8, 2019	46.50%	41.85%	\$ 67,961.57	\$ 94,416.37	ON-GOING	
50	R4D Rural Periodic Maintenance Kaen Laran - Barique Chainage 0+000 - 9+000 & Routine, Hatularan-Cairui Chainage 0+000-9+800 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Manufahi Kiik Unip. Lda	\$ 141,684.96	Aug. 25, 2019	41.78%	36.88%	\$ 52,260.01	\$ 89,424.95	ON-GOING	
51	R4D Rural Road Spot Improvement Agriculture Center - Aubeon Chainage 3+000-6+200	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	We"coi Unipessoal Lda	\$ 343,111.47	June 10, 2021	44.80%	21.97%	\$ 75,370.79	\$ 267,740.68	ON-GOING	
52	R4D Rural Road Spot Improvement Uma Boco - Agriculture Center Chainage 0+000 - 3+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Linoel	\$ 296,211.81	June 10, 2021	18.83%	15.96%	\$ 47,266.94	\$ 248,944.87	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Dezembro Aumenta 17.73%
53	R4D Rural Road Spot Improvement Kaen-Laran - Barique Chainage 0+000-9+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Gimso Brothers Unip. Lda	\$ 300,792.46	July 10, 2021	88.60%	52.76%	\$ 158,690.94	\$ 142,101.52	ON-GOING	
54	New construction of Gapura and gabion wall protection no jardim de herois de Natarbora	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Barique	Manatuto	Senizu	\$ 408,460.73	Oct. 18, 2021	84.16%	78.09%	\$ 318,953.66	\$ 89,507.07	ON-GOING	
55	New Installation MV, LV Line and House Connection from Lado to Mantane - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Lado	Manatuto	Anopa Electrical Unip. Lda	\$ 380,582.61	Sept. 1, 2016	95.99%	72.08%	\$ 274,330.03	\$ 106,252.58	ON-GOING	
56	Emergency Rehabilitation Project in Subao Boo, Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lado	Manatuto	Sahan I Unip.Lda	\$ 3,314.56	Sept. 27, 2016	100.00%	90.00%	\$ 2,983.11	\$ 331.45	ON-GOING	
57	Konstrusaun Edificio Posto Administrativo Lado	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Lado	Manatuto	Ailii Const. Unip. Lda	\$ 120,020.07	Oct. 8, 2019	100.00%	100.00%	\$ 120,019.88	\$ 0.19	FHO	Projecto ne Finaliza ona
58	For Roads & Bridges Maintenance Section : Mantanen Lado, Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lado	Manatuto	Egana, Unip. Lda	\$ 223,843.79	Dec. 13, 2019	68.89%	56.58%	\$ 126,647.74	\$ 97,196.05	ON-GOING	
59	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 9 : Lado to Lado Town Road	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lado	Manatuto	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	\$ 422,400.00	April 25, 2020	100.00%	100.00%	\$ 422,400.00	\$ -	ON-GOING	
60	Rehabilitation of Behau Mini Tradisional Food	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Lado	Manatuto	Esa-Un	\$ 50,745.00	May 2, 2016	38.83%	34.95%	\$ 17,736.12	\$ 33,008.88	PENDENTE	
61	Konstrusaun Mercado Komunitaria Kikan Ilmano	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	COMERCIO	Lado	Manatuto	Surprise Unip. Lda	\$ 153,942.39	Sept. 12, 2016	97.16%	84.29%	\$ 129,753.97	\$ 24,188.42	ON-GOING	
62	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Lado	Manatuto	Sinohydro Corporation Limited	\$ 48,314,975.87	May,3, 2016	87.98%	87.98%	\$ 42,506,027.78	\$ 5,808,948.09	ON-GOING	
63	Konstrusaun ka Rehabilitasaun ba EBC Remanarun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Lado	Manatuto	MEJD PKRIE EBC REMANARUN	\$ 98,147.27	Oct. 15, 2021	23.59%	23.56%	\$ 23,122.26	\$ 75,025.01	ON-GOING	
	TOTAL							\$ 140,107,038.04				\$ 118,286,107.71	\$ 21,820,930.33		


1. Eng. Aleixo da Costa Andrade
Eng. ba Projecto Edificio Publico Beé no Saneamento Municipio Manatuto, ADN, I.P


2. Eng. Jose Roberto C. Gusmão
Eng. ba Projecto Insfrasturctura e Irigasaun Municipiu Manatuto, ADN, I.P


3. Eng. Domingos D.X. Silva
Eng. ba Projecto Insfrasturctura e Irigasaun Municipiu Manatuto, ADN, I.P


4. Eng. Febian Fitalis Maria Madeira
Eng. ba Projecto Insfrasturctura e Irigasaun Municipiu Manatuto, ADN, I.P


5. Eng. Adonis Julia Fernandes
Eng. ba Projecto ME, ADN, I.P


Certifika Husi:
Eng. Emerenciana da Costa Maia Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN, I.P

LISTA #ANEXU B

PROGRESSU FISIKU KADA FULAN



					LOKALIZASAUN PROJETU					Dec-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativo Progress
1	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	\$ 2,561,405.06	Aug. 25, 2018	63.80%		63.80%
2	Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Nananiu, Unip. Lda JV Ina Forek, Lda	\$ 3,029,514.40	Aug. 25, 2017	89.20%		89.20%
3	Construção de novo Estadio de Futebol em Manatuto	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Manatuto Villa	Manatuto	Obrai Unipessoal, Lda	\$ 2,362,976.44	June 30, 2015	82.08%		82.08%
4	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	R.D Interior Junior Construction / Hebel Road and Bridge Group	\$ 28,011,854.94	Feb. 10, 2014	94.91%		94.91%
5	Consultant Supervision (M-L & L-N)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Manatuto Villa	Manatuto	Sinotech Engineering Consultant	\$ 4,405,546.00	Sept. 3, 2014	73.76%		73.76%
6	Konstrusaun ESTV Beadi-Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Manatuto Villa	Manatuto	Ralan Unip. Lda	\$ 181,102.33	Oct. 10, 2019	92.91%		92.91%
7	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Unip. Lda	\$ 79,155.54	Dec. 18, 2019	88.07%		88.07%
8	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	ESTATAL	PDIM	TURISMO	Manatuto Villa	Manatuto	Carya Timor Leste Lda	\$ 226,400.73	Dec. 18, 2019	43.70%		43.70%
9	Servisu Manutensaun Edifisru CRC Munisipiu Manatuto	MINISTERIO DA JUSTICA	LM-BS	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Baboe Unip Lda	\$ 29,275.84	March 1, 2020	15.92%		15.92%
10	New Construction of Laboratory for Covid 19 at Manatuto, Ministry of Helath, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Manatuto Villa	Manatuto	Kartini Unipessoal Lda	\$ 66,989.91	Jan. 7, 2021	95.34%		95.34%
11	Sumase River	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Forté, Unip. Lda	\$ 1,486,885.83	Sept. 7, 2017	100.00%		100.00%
12	Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu, Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Manatuto Villa	Manatuto	Ilatun, Lda	\$ 2,330,487.53	July 25, 2016	96.42%	1.11%	97.52%
13	Konstrusaun Fatin Isolamentu iha Municipiu Manatuto, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Manatuto Villa	Manatuto	Talamori Unip.Lda	\$ 262,983.65	09-Dec-20	91.97%	8.03%	100.00%
14	New Construction of Gabions Tower No. 4 Section Manatuto - Baucau Municipality Manatuto	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Manatuto Villa	Manatuto	Giovania Unip. Lda	\$ 175,266.63	02-Aug-21	98.51%		98.51%
15	New Construction of Fence at Isolation Covid-19 in Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	K-6, UNIPESOAL LDA	\$ 257,748.51	Jan. 12, 2022	88.89%		88.89%
16	Supply and Installtion Main Power For Isolation and Laboratorium Building Ma'abat Manatuto Municipality	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Manatuto Villa	Manatuto	Fraternity Unipessoal Lda	\$ 77,936.20	Jan. 12, 2022	92.28%		92.28%
17	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE ESG KAY RALA	\$ 62,996.83	Oct. 15, 2021	31.90%		31.90%
18	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF RENTAU	\$ 64,383.50	Oct. 15, 2021	28.55%		28.55%
19	Konstrusaun ka Rehabilitasaun ba PE Rembor	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE PE REMBOR	\$ 88,918.34	Oct. 15, 2021	22.77%		22.77%
20	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF OBRATO	\$ 66,144.65	Oct. 15, 2021	38.17%		38.17%
21	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Manatuto Villa	Manatuto	MEJD PKRIE EBF BAHADIK	\$ 100,047.31	Oct. 15, 2021	14.58%		14.58%
22	Rehabilitasaun Kampu Foteboll iha Postu Administrativu Laleia	MINISTERIO PLANU E ORDENAMENTU	LM-CD	EDIFICIOS PUBLICOS	Laleia	Manatuto	DCO Unip.Lda	\$ 277,330.43	July 18, 2019	0.00%		0.00%
23	Konstrusaun Edificio Posto Administrativo Laleia	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Laleia	Manatuto	Hare Unip.Lda	\$ 141,945.19	Oct. 8, 2019	100.00%		100.00%
24	R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laleia	Manatuto	As Jazesia Unipessoal Lda	\$ 28,258.31	June 10, 2021	99.86%		99.86%
25	Konstrusaun ka Rehabilitasaun ba EP Cairui	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laleia	Manatuto	MEJD PKRIE EP CAIRUI	\$ 86,883.29	Oct. 15, 2021	28.43%		28.43%
26	New Installation Mv, Lv Line & House Connection From Laclubar Vila to Funar And Fatuk Manu - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Laclubar	Manatuto	Tasibala III Unip. Lda	\$ 695,420.83	June 7, 2016	91.52%		91.52%
27	Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Laclubar	Manatuto	China Nuclear Industry 22ND Construction Co; LTD	\$ 34,379,729.54	Nov. 20, 2014	91.66%	0.38%	92.04%
28	Konstrusaun Posto Saude Iha iha Suku Funar - Laklubar	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Ladiama Unip. Lda	\$ 112,967.53	Sept. 23, 2019	22.06%		22.06%
29	Konstrusaun Rezidencia Pesoa Iha iha Suku Funar - Laklubar	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Tonijo Unip. Lda	\$ 81,776.84	Oct. 8, 2019	100.00%		100.00%
30	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Hatuwari Unip. Lda	\$ 481,029.66	Aug. 25, 2020	54.37%		54.37%
31	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laclubar	Manatuto	Ryzena Unipessoal Lda	\$ 194,402.72	Dec. 20, 2019	82.83%		82.83%
32	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Sun Rise Golden Construction 02 Lda	\$ 448,209.39	June 10, 2021	95.04%		95.04%
33	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laclubar	Manatuto	Adahiak Orlao Unipessoal Lda	\$ 213,772.95	June 10, 2021	7.12%		7.12%
34	Kontinuasaun Konst. Postu Saude Iha Suku Fatumakerek	MINISTERIO SAUDE	PDIM	SAUDE	Laclubar	Manatuto	Hatuwari Unip. Lda	\$ 120,962.71	July 28, 2019	71.23%		71.23%
35	Konstrusaun ka Rehabilitasaun ba EBF Batara	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF BATARA	\$ 102,060.99	Oct. 15, 2021	25.60%		25.60%
36	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laclubar	Manatuto	MEJD PKRIE EBF AISIU-UM	\$ 100,162.30	Oct. 15, 2021	25.60%		25.60%
37	Construction of New Steel Bridge 100m in Milotu Sahe river, jct.Fatucamanau, Soibada, Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Soibada	Manatuto	FIRDO UNIPESOAL LDA	\$ 3,384,214.14	Feb. 27, 2017	100.00%		100.00%
38	Konstrusaun ESTV Soibada Manatuto (CA + CB)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 183,381.16	Sept. 23, 2019	100.00%		100.00%
39	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 10 Soibada to Soibada Town	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	\$ 164,154.00	March 25, 2020	70.00%		70.00%
40	R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 203,036.57	June 10, 2021	48.43%		48.43%
41	R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Soibada	Manatuto	Ryzena Unipessoal Lda	\$ 196,112.23	June 10, 2021	26.63%	23.57%	50.20%
42	Projetu Rehabilitasaun Ensnu Sekundariu Tekniku Vokasional Soibada, Manatuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDIFICIOS PUBLICOS	Soibada	Manatuto	Manufahi Kiik Unip. Lda	\$ 66,898.51	Nov. 26, 2021	78.97%		78.97%
43	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Soibada	Manatuto	MEJD PKRIE EBC WEAIHUDIK	\$ 102,512.31	Oct. 15, 2021	31.76%		31.76%
44	Construction of Sahen Bridge Approach Protection (A14) Manatuto (MPW-W-190157) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	FLOOD CONTROL	Barique	Manatuto	Yoku Unipessoal Lda	\$ 242,560.14	Oct. 24, 2019	70.75%		70.75%
45	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	MINISTERIO AGRICULTURA E PESCAS	LM-CD	AGRICULTURA	Barique	Manatuto	Tasibala II Const	\$ 370,511.25	Sept. 13, 2016	17.59%		17.59%
46	Rural Roads Routine Maintenance Uma Boco - Aubeon, Sta. 0+000 - 6+000, Manututo Municipality (Manutensaun)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Zenobia Diak Unip.Lda	\$ 15,875.56	Jan. 7, 2017	100.00%		100.00%

LISTA #ANEXU B

PROGRESSU FISIKU KADA FULAN

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	LOKALIZASAUN PROJETU		NARAN COMPANHA	MONTANTE KONTRATU (\$)	DATA KONTRATU	Dec-22		
					POSTO ADMINISTRATIVO	MUNISIPIU				Previous Progress	This Month Progress	Kumulativo Progress
47	Konstrusaun Postu Saude Aimeta Laran-Barique	MINISTERIO SAUDE	PDIM	SAUDE	Barique	Manatuto	Malack II Unip. Lda	\$ 116,914.88	Sept. 23, 2019	71.10%		71.10%
48	Construction of Residence for Health Staff in Suku Aimeta Laran-Barique	MINISTERIO SAUDE	PDIM	SAUDE	Barique	Manatuto	Macucuren Unip. Lda	\$ 77,583.44	Oct. 8, 2019	99.96%		99.96%
49	Konstrusaun Sistema Bee Mos Iha Suco Aubeon no Aimetalan /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Barique	Manatuto	Malaca Unip Lda	\$ 162,377.94	Oct. 8, 2019	46.50%		46.50%
50	R4D Rural Periodic Maintenance Kaen Laran - Barique Chainage 0+000 - 9+000 & Routine, Hatularan-Cairui Chainage 0+000-9+800 (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Barique	Manatuto	Manufahi Kiik Unip. Lda	\$ 141,684.96	Aug. 25, 2019	41.78%		41.78%
51	R4D Rural Road Spot Improvement Agriculture Center - Aubeon Chainage 3+000-6+200	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	We"coi Unipessoal Lda	\$ 343,111.47	June 10, 2021	44.80%		44.80%
52	R4D Rural Road Spot Improvement Uma Boco - Agriculture Center Chainage 0+000 - 3+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Linoel	\$ 296,211.82	June 10, 2021	1.10%	17.73%	18.83%
53	R4D Rural Road Spot Improvement Kaen-Laran - Barique Chainage 0+000-9+000	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Barique	Manatuto	Gimso Brothers Unip. Lda	\$ 300,792.46	July 10, 2021	88.60%		88.60%
54	New construction of Gapura and gabion wall protection no jardim de herois de Natarbora	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTACAO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Barique	Manatuto	Senizu	\$ 408,460.73		84.16%		84.16%
55	New Installation MV, LV Line and House Connection from Lacio to Mantane - Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Lacio	Manatuto	Anopa Electrical Unip. Lda	\$ 380,582.61	Sept. 1, 2016	95.99%		95.99%
56	Emergency Rehabilitation Project in Subao Boo, Municipio Manatuto	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lacio	Manatuto	Sahan I Unip.Lda	\$ 3,314.56	Sept. 27, 2016	100.00%		100.00%
57	Konstrusaun Edificio Posto Administrativo Lacio	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Lacio	Manatuto	Ailli Const. Unip. Lda	\$ 120,020.07	Oct. 8, 2019	100.00%		100.00%
58	Routine Roads Maintenance - Lacio, Manatuto Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lacio	Manatuto	Egana, Unip. Lda	\$ 223,836.50	Dec. 13, 2019	68.89%		68.89%
59	For Preparation of Detailed Engineering Design for Rehabilitation of "Municipio Roads" Package 9 : Lacio to Lado Town Road	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Lacio	Manatuto	PT. Bikarma Jv Aureum Solis Consultant Unip Lda	\$ 422,400.00	April 25, 2020	100.00%		100.00%
60	Rehabilitation of Behau Mini Tradisional Food	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Lacio	Manatuto	Esa-Un	\$ 50,745.00	May 2, 2016	38.83%		38.83%
61	Konstrusaun Mercado Komunitaria Kikan Ilmano	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	COMERCIO	Lacio	Manatuto	Surprise Unip. Lda	\$ 153,942.39	Sept. 12, 2016	97.16%		97.16%
62	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Lacio	Manatuto	Sinohydro Corporation Limited	\$ 48,314,975.87	May.3, 2016	87.98%		87.98%
63	Konstrusaun ka Rehabilitasaun ba EBC Remanarun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Lacio	Manatuto	MEJD PKRIE EBC REMANARUN	\$ 98,147.27	Oct. 15, 2021	23.59%		23.59%

Prepara Husi:

1. Eng. Aleixo da Costa Andrade
Eng. ba Projecto Edificio Publico Beé no Saneamento Municipio Manatuto,ADN,I.P

3. Eng. Adonis Julio Fernandes
Eng. ba Projecto ME, ADN, I.P

2. Eng. Jose R.C. Gasmão
Eng. ba Projecto Infrastrutura e Irigasaun Municipiu Manatuto, ADN, I.P

4. Eng. Domingos D.X. Silva
Eng. ba Projecto Infrastrutura e Irigasaun Municipiu Manatuto, ADN, I.P

5. Eng. Fabiano Fitalis Maria Madeira
Eng. ba Projecto Infrastrutura e Irigasaun Municipiu Manatuto, ADN, I.P

Verifica Husi :

Eng. Remigio da c.s dos Santos
Eng. Senior ba Projecto Infrastrutura e Irigasaun, ADN, I.P

Eng./Arch. Francisco Xavier de D. Jeronimo
Eng. Senior ba Projecto Edificio Publico Beé no Saneamento,ADN,I.P

Eng. Decindo de Fatima Marques
ChefeSeksau ME& ITC, ADN, I.P

Certifica Husi :

Eng. Emerenciana da Costa M.Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN,I.P



ANEXU C1 (BA-9)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Uma Boco - Agriculture Center
Chainage 0+000 - 3+000
No. kontratu : MPW-W-210061

Data Inspesaun : 24/ 11/ 2022

Fatin Inspesaun : Natarbora - Uma Boco- Aubeon

Koordinadas :

Start Point : Long : -8.996666°, Latetude : 126.084966°

End Point : Long : -9.004681°, Latetude : 126.061377°

Naran Inspector : 1.Eng. Jose R. Carlos Gusmão,
2. Eng. Domingos D.X. Silva

Sketch & Foto Desenho

Projetu ne'e paradu kleur ona. Equipa dala barak halo inspesaun iha terenu maibe la hetan tekniku ruma no nain ba kompania. Equipa kontaktu ona nain ba kompania mas la garantia atu hahu bainhira.(tamba projetu refere tama kategoria Abandona.

Observasaun iha tereno no Foto Aktual





ANEXU C1 (BA-9)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Uma Boco - Agriculture Center
Chainage 0+000 - 3+000
No. kontratu : MPW-W-210061

Sketch & Foto Desenho

Sketch Item la iha tamba Projeitu ne'e paradu kleur ona. Equipa dala barak halo inspesaun iha terenu maibe la hetan tekniku ruma no nain ba kompania. Equipa kontaktu ona nain ba kompania mas la garantia atu hahu bainhira.(tamba projeitu refere tama kategoria Abandona.

Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho

Sketch Item la iha tamba Projeitu ne'e paradu kleur ona. Equipa dala barak halo inspesaun iha terenu maibe la hetan tekniku ruma no nain ba kompania. Equipa kontaktu ona nain ba kompania mas la garantia atu hahu bainhira.(tamba projeitu refere tama kategoria Abandona.

Observasaun iha tereno no Foto Aktual





#ANEXU C2 (BA - 9)

Naran Projeto : RD4 RURAL ROAD ROUTINE MAINTENANCE
No. kontratu : MPW-W-210055
Postu : Natarbora
Suku : Aubeon
Naran Companhia : Linoel Unip, Lda

SUMMARY								
SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	PROGRESS PAYMENT BY A D N					
		(US\$)	PREVIOUS BILLING (USD)	PERECENT PREVIOUS	THIS BILLING (USD)	PERCENT THIS	TOTAL TO DATE (USD)	% TO DATE
				BILLING		MONTH		
R-01	General	\$ 2,440.90	\$ 600.00	0.20%	\$ 950.00	0.32%	\$ 1,550.00	0.52%
R-05	Earth work	\$ 23,170.60	\$ 584.63	0.20%	\$ 17,457.52	5.89%	\$ 18,042.15	6.09%
R-07	Sub-base, Base and Pavement	\$ 56,064.54	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
R-08	Bituminous pavement	\$ 134,733.55	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
R-10	Structures	\$ 16,458.42	\$ 378.53	0.13%	\$ 11,616.88	3.92%	\$ 11,995.41	4.05%
R-11	Dayworks	\$ 182.00	\$ 105.00	0.04%	\$ -	0.00%	\$ 105.00	0.04%
R-15	Routine maintenance	\$ 5,357.00	\$ -	0.00%	\$ 4,057.00	1.37%	\$ 4,057.00	1.37%
R-15	Provisional sum	\$ 200.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
A	Construction Cost	\$ 238,607.02	\$ 1,668.16	0.56%	\$ 34,081.40	11.51%	\$ 35,749.56	12.07%
B	Profit & Over Head (10% x A)	\$ 23,860.70	\$ 166.82	0.06%	\$ 3,408.14	1.15%	\$ 3,574.96	1.21%
C	Generals item	\$ 27,936.02	\$ 1,360.00	0.46%	\$ 13,999.50	4.73%	\$ 15,359.50	5.19%
D	Tax 2 % x (A+B+C)	\$ 5,808.07	\$ 63.90	0.02%	\$ 1,029.78	0.35%	\$ 1,093.68	0.37%
E	GRAND/GROSS TOTAL	\$ 296,211.81	\$ 3,258.88	1.10%	\$ 52,518.82	17.73%	\$ 55,777.70	18.83%

Inspeksaun Husi:

Verifika Husi :

Sertifika husi :

1. (José R. Carlos Gusmão)
Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Manatuto, ADN.I.P

Eng. Remigio da c.s dos Santos
Eng. Senior ba Projeto Insfrasturctura e Irigasaun,
ADN, I.P

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de
Qualidade, ADN.I.P

2. (Domingos D.X. Silva)
Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Manatuto, ADN.I.P`

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					INSTRUSAUN / REKOMENDASAUN		
Naran projeto : R4D Rural Road Spot Improvement Uma Boco - Agriculture Center Chainage 0+000 - 3+000							
Kompanha : Linoel							
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	24/11/2022	Manatuto/ Barique	1. Jose R. Carlos Gusmão	Eng. Ba Projeitu ITI Munisipiu Manatuto, ADN.I.P	1	Projetu ne'e paradu kleur ona. Equipa dala barak halo inspesaun iha terenu maibe la hetan tekniku ruma no nain ba kompania. Equipa kontaktu ona nain ba kompania mas la garantia atu hahu bainhira.(tamba projetu refere tama kategoria Abandona.	
					2	Teknik A.D.N.I.P halo monitorija tuir planu tekniku nia Compania la halo atividade ruma iha tereinu	
					3	Tuir observaun teknik A.D.N.I.P Compania abandona servisu iha tereinu	
					4	Teknik A.D.N.I.P halo monitorija tuir planu tekniku nia, maibe dalaruma ami hasoru deit Security.	
			2. Domingos D.X. Silva		1	Projetu ne'e paradu kleur ona. Equipa dala barak halo inspesaun iha terenu maibe la hetan tekniku ruma no nain ba kompania. Equipa kontaktu ona nain ba kompania mas la garantia atu hahu bainhira.(tamba projetu refere tama kategoria Abandona.	
					2	Teknik A.D.N.I.P halo monitorija tuir planu tekniku nia Compania la halo atividade ruma iha tereinu	
					3	Tuir observaun teknik A.D.N.I.P Compania abandona servisu iha tereinu	
					4	Teknik A.D.N.I.P halo monitorija tuir planu tekniku nia, maibe dalaruma ami hasoru deit Security.	



#ANEXU C1 (LAC-3)

Back-up Data

Naran Projeto : Road Network Upgrading Project (RNUP) for Laclubar - natarbora
(ADB Loan)

No. kontratu : ICB/04/MPW-2014

Data Inspesaun : 06/12/2022

Fatin Inspesaun : Laclubar-Natarbora

Koordinadas :


Start Point : Long : -8,749,216, Latetude : 125,971,366

End Point : Long : -8,976,984, Latetude : 126,042,458

Naran Inspector : 1. Eng. Vidal Guterres

2. Eng. Domingos X. da C. Silva

3. Eng. Augusta da Costa Ferreira

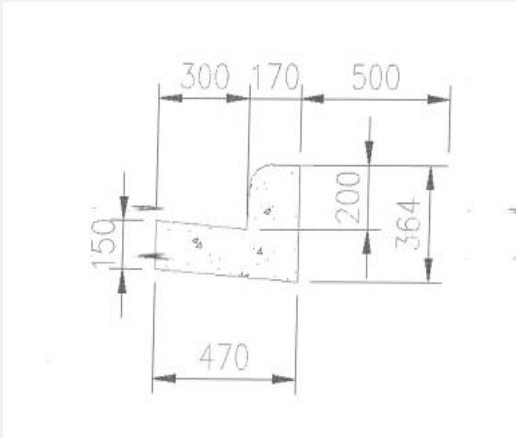Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Skecth Item servisu Curb and Guter  Volume= 1,328.01 m	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual




#ANEXU C1 (LAC-3)

Back-up Data

Naran Projeto : Road Network Upgrading Project (RNUP) for Laclubar - natarbora
(ADB Loan)

No. kontratu : ICB/04/MPW-2014

Skecth Item servisu Stone Masonry Line Ditch

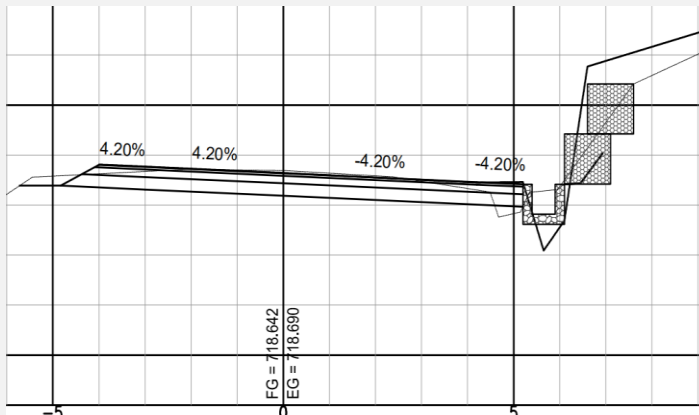

Volume= 3,243.42 m3





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (LAC-3)



Back-up Data

Naran Projeto

: Road Network Upgrading Project (RNUP) for Laclubar - natarbora
(ADB Loan)

No. kontratu

: ICB/04/MPW-2014





#ANEXU C2 (LAC- 3)

Project Name: Upgrading and Maintenance of Laclubar Junction-Natarbora Road(Sta.100+360 to
Contractor : China Nuclear Industry 22nd Construction Co., Lda.

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
100	GENERAL REQUIREMENTS	\$ 2,876,362.43	\$ 3,658,056.59	10.64%	\$ -	0.00%	\$ 3,658,056.59	10.64%	\$ (781,694.16)
200	EARHWORKS	\$ 2,196,247.04	\$ 2,292,965.43	6.67%	\$ -	0.00%	\$ 2,292,965.43	6.67%	\$ (96,718.39)
300	SUBBASE AND BASE COURSES	\$ 8,645,516.40	\$ 8,235,866.98	23.96%	\$ -	0.00%	\$ 8,235,866.98	23.96%	\$ 409,649.42
400	SURFACE COURSE	\$ 8,484,452.55	\$ 8,293,287.46	24.12%	\$ -	0.00%	\$ 8,293,287.46	24.12%	\$ 191,165.09
500	BRIDGE CONSTRUCTION	\$ 2,716,589.87	\$ 2,361,649.00	6.87%	\$ -	0.00%	\$ 2,361,649.00	6.87%	\$ 354,940.87
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	\$ 5,757,775.65	\$ 7,177,906.99	20.88%	\$ -	0.00%	\$ 7,177,906.99	20.88%	\$ (1,420,131.34)
700	MISCELLANEOUS STRUCTURES	\$ 678,108.08	\$ 911,811.69	2.65%	\$ -	0.00%	\$ 911,811.69	2.65%	\$ (233,703.61)
800	BIO ENGINEERING	\$ 236,159.60	\$ 83,037.24	0.24%	\$ -	0.00%	\$ 83,037.24	0.24%	\$ 153,122.36
DW	DAYWORKS	\$ 743,149.42	\$ 243,658.75	0.71%	\$ -	0.00%	\$ 243,658.75	0.71%	\$ 499,490.67
	PROVISIONAL SUM AND CONTINGENCY	\$ 1,410,954.90	\$ 324,317.46	0.94%	\$ -	0.00%	\$ -	0.94%	\$ 1,410,954.90
	TOTAL =	\$ 33,745,315.94	\$ 33,582,557.58	97.68%	\$ -	0.00%	\$ 33,258,240.12	97.68%	\$ 487,075.82
	PERFORMANCE BASED MAINTENANCE WORKS	\$ 634,413.60	\$ -	0.00%	\$ 131,752.73	0.38%	\$ 131,752.73		\$ 502,660.87
	CONTRACT AMOUNT	\$ 34,379,729.54	\$ 33,582,557.58	97.68%	\$ -	0.38%	\$ 33,258,240.12	98.06%	\$ 1,121,489.42
	GRAND TOTAL	\$ 34,379,729.54	\$ 33,582,557.58	97.68%	\$ -	0.38%	\$ 33,258,240.12	98.06%	\$ 1,121,489.42

Inspeksaun Husi:

(Eng. Jose R Carlos Gusmão)
Eng. ba Projecto Infraestrutura Transporte
e Irrigação Munisipiu Manatuto, ADN.I.P

(Eng. Domingos da C. X. Silva)
Eng. ba Projecto Infraestrutura Transporte
e Irrigação Munisipiu Manatuto, ADN.I.P

(Eng. Vidal Guterres)
Eng. PMU ba Projecto (Imprestimo),
ADN.I.P

(Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projecto (Imprestimo),
ADN.I.P

Verifika Husi :

(Eng. Aniceto da Costa)
Eng. Senior ba projeito Infraestrutura,
Transporte e Irigasaun, ADN.I.P

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN.I.P

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					#ANEXU D (LAC-3) INSTRUSAUN / REKOMENDASAUN Naran projeto : Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan) Kompanha : China Nuclear Industry 22ND Construction Co; LTD		
No	Data inspesaun	Municípiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12/06/2022	Laclubar/ Natarbora	Vidal Guterres	Eng. PMU ba Projetu (Imprestimo), ADN.I.P	1		
					2		
					3		
II	12/06/2022	Laclubar/ Natarbora	Domingos da C.X e Silva	Eng. Ba Projetu ITI Munisípiu Manatuto, ADN,I.P.	1		
					2		
					3		
III	12/06/2022	Laclubar/ Natarbora	Augusta da Costa Ferreira	Eng. PMU ba Projetu (Imprestimo), ADN.I.P	1		
					2		
					3		
IV	12/06/2022	Laclubar/ Natarbora			1		
					2		
					3		



#ANEXU C1 (MV-12)

Back-up Data

Naran Projeto : **Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu, Manatuto Municipality**

No. kontratu : **SSS/115/MOPTC-2016**

Data Inspesaun : **12/ 12/2022**

Fatin Inspesaun : **Manatuto Villa**

Koordinadas :

Start Point : Long : 126,021,108, Latetude : -8,518,339

End Point : Long : 126,003,775, Latetude : -8,517,000

Naran Inspector : **1. Eng. José Roberto, C. Gusmão**

2. Eng. Domingos DX. Silva

Sketch & Foto Desenho

Sketch Item: Rekomendasaun pagamento
ikus 100% no Retensaun 10%.

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (MV-12)


Back-up Data

Naran Projeto

: Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu,
Manatuto Municipality

No. kontratu

: SSS/115/MOPTC-2016





#ANEXU C2 (MAV- 2)

Projeitu : Fundus de Infrastruturas (F I)
Titulo Projeitu : Rehabilitation of Roads Monumento Laclubar, Mercado Huo - Lu, Manatuto Municipality
Fatin Projeitu : Posto Administrstivo Manatuto Villa, Municipio Manatuto
Contraktor : Ilatun Unip. Lda
No. kontratu : SSS/062/MOPTC-2017

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST (US\$)	PROGRESS PAYMENT BY A D N					
			PREVIOUS BILLING (USD)	PERECENT PREVIOUS BILLING	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
100	GENERAL REQUIREMENTS	\$ 15,850.00	\$ 15,850.00	0.68%	\$ -	0.00%	\$ 15,850.00	0.68%
200	EARTHWORKS	\$ 185,933.55	\$ 80,055.14	3.44%	\$ 23,008.97	0.99%	\$ 103,064.11	4.42%
300	SUB BASE AND BASE COURSE	\$ 209,427.60	\$ 427,989.94	18.36%	\$ -	0.00%	\$ 427,989.94	18.36%
400	SURFACE COURSE	\$ 1,189,573.72	\$ 1,051,863.33	45.13%	\$ -	0.00%	\$ 1,051,863.33	45.13%
500	BRIDGE CONSTRUCTION	\$ 2,514.67	\$ 70,444.04	3.02%	\$ -	0.00%	\$ 70,444.04	3.02%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	\$ 369,960.49	\$ 261,446.59	11.22%	\$ -	0.00%	\$ 261,446.59	11.22%
700	MISCELLANEOUS STRUCTURES	\$ 103,823.33	\$ 94,987.98	4.08%	\$ -	0.00%	\$ 94,987.98	4.08%
A	Construction Cost	\$ 2,077,083.36	\$ 2,002,637.01	85.93%	\$ 23,008.97	0.99%	\$ 2,025,645.98	86.92%
B	Profit (10% x A)	\$ 207,708.34	\$ 200,263.70	8.59%	\$ 2,300.90	0.10%	\$ 202,564.60	8.69%
C	Tax 2 % x (A+B)	\$ 45,695.83	\$ 44,058.01	1.89%	\$ 506.20	0.02%	\$ 44,564.21	1.91%
D	GRAND/GROSS TOTAL	\$ 2,330,487.53	\$ 2,246,958.73	96.42%	\$ 25,816.06	1.11%	\$ 2,272,774.79	97.52%

Inspeksaun Husi:

Verifika Husi :

Sertifika husi :

1. (Eng. José R Carlos Gusmão)
Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Matatuto, ADN.I.P

Eng. Remigio da c.s dos Santos
Eng. Senior ba Projeito Insfrasturctura e

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de
Qualidade, ADN.I.P

2. (Eng. Domingos D,X,Silva)
Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Matatuto, ADN.I.P

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público					INSTRUSAUN / REKOMENDASAUN		
					Naran projeto : Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu, Manatuto Municipality		
					Kompanha : Ilatun, Lda		
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12 de Dezembro 2022	Manatuto Villa	José R.Carlos Gusmão	Eng.	1	Iha data 12 de Dezembro 2022 Tekniku A.D.N.I.P inspeksaun konjuntu entre teknik kompania ba pagamento 100% no Retensaun 10%.	
					2	Iha data 12 de Dezembro 2022 Tekniku A.D.N.I.P orienta kedan teknik kompania atu hadia defeitus tamba iha balu hanesan item line draine ne'ebe nakonu ho sedimentasaun iha tereinu no kompania presija hamos antes prosesa pagamento final.	
					3	Tekniku A.D.N.I.P orienta kompania atu hamos linedraine ninin no tembok penahan (Retaning wall) teknik oreinta kompania atu hamos durante loron 2 molok teknik A.D.N.I.P prosesa pagamento.	
II	12 de Dezembro 2022	Manatuto Villa	Domingos X.D. Silva	Eng.	1	Iha data 12 de Dezembro 2022 Tekniku A.D.N.I.P inspeksaun konjuntu entre teknik kompania ba pagamento 100% no Retensaun 10%.	
					2	Iha data 12 de Dezembro 2022 Tekniku A.D.N.I.P orienta kedan teknik kompania atu hadia defeitus tamba iha balu hanesan item line draine ne'ebe nakonu ho sedimentasaun iha tereinu no kompania presija hamos antes prosesa pagamento final.	
					3	Tekniku A.D.N.I.P orienta kompania atu hamos linedraine ninin no tembok penahan (Retaning wall) teknik oreinta kompania atu hamos durante loron 2 molok teknik A.D.N.I.P prosesa pagamento.	



#ANEXU C1 (MV- 4)

Back-up Data

Naran Projeto : RNUSP / Upgrading and Maintenance of Manatuto - Laclubar Junction Road
(sta.65+235 to Sta 100+355)

No. kontratu : ICB/023/MPW-2013

Data Inspesaun : 04/ 10/ 2022

Fatin Inspesaun : Manatuto-Laclubar

Koordinadas :

Start Point : Long : -84310383, Latetude : 125.5843077

End Point : Long : -8373105, Latetude : 125.5915918


Naran Inspector : 1. Eng. Domingos X. da C. Silva

2. Eng. Vidal Guterres

Sketch & Foto Desenho

Sketch Item servisu laiha tanba servisu
Fiziku 100%

Observasaun iha tereno no Foto Aktual

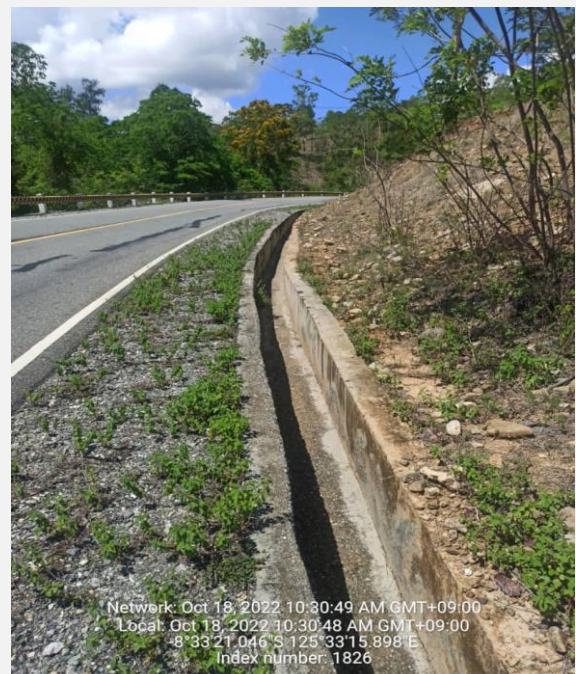



#ANEXU C1 (MV- 4)

Back-up Data

Naran Projeto : RNUSP / Upgrading and Maintenance of Manatuto - Laclubar Junction Road
(sta.65+235 to Sta 100+355)

No. kontratu : ICB/023/MPW-2013

Sketch & Foto Desenho

Sketch Item servisu laiha tanba servisu
Fiziku 100%

Observasaun iha tereno no Foto Aktual



Network: Oct 18, 2022 10:29:59 AM GMT+09:00
Local: Oct 18, 2022 10:29:58 AM GMT+09:00
Index number: 1824



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (MV- 4)

Back-up Data

Naran Projeto : **RNUSP / Upgrading and Maintenance of Manatuto - Laclubar Junction Road**
(sta.65+235 to Sta 100+355)

No. kontratu : ICB/023/MPW-2013





#ANEXU C2 (MV- 4)

Project Name : RNUSP / Upgrading and Maintenance of Manatuto - Laclubar Junction Road(sta.65+235 to Sta 100+355)

Contractor : R.D. Interior Junior Construction/Hebei Road and Bridges Group Co. Ltd. (JV)

IPC no. : IPC no.Final Payment (November, 26 2018-Decemeber 24, 2018)

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
100	GENERAL REQUIREMENTS	\$ 1,832,315.90	\$ 1,769,896.73	6.32%	\$ -	0.00%	\$ 1,769,896.73	6.32%	\$ 62,419.18
200	EARHWKRS	\$ 4,582,442.48	\$ 4,051,855.40	14.46%	\$ 164,392.44	0.59%	\$ 4,216,247.83	15.05%	\$ 366,194.64
300	SUBBASE AND BASE COURSES	\$ 3,815,952.12	\$ 3,766,624.61	13.45%	\$ -	0.00%	\$ 3,766,624.61	13.45%	\$ 49,327.51
400	SURFACE COURSE	\$ 6,906,466.41	\$ 6,806,708.10	24.30%	\$ -	0.00%	\$ 6,806,708.10	24.30%	\$ 99,758.31
500	BRIDGE CONSTRUCTION	\$ 1,532,360.99	\$ 1,532,185.97	5.47%	\$ -	0.00%	\$ 1,532,185.97	5.47%	\$ 175.03
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	\$ 6,212,247.57	\$ 5,663,263.57	20.22%	\$ 58,974.73	0.21%	\$ 5,722,238.30	20.43%	\$ 490,009.26
700	MISCELLANEOUS STRUCTURES	\$ 1,958,295.38	\$ 1,941,390.20	6.93%	\$ -	0.00%	\$ 1,941,390.20	6.93%	\$ 16,905.18
800	BIO ENGINEERING	\$ 173,496.50	\$ 143,962.95	0.51%	\$ 3,522.63	0.01%	\$ 147,485.57	0.53%	\$ 26,010.93
DW	DAYWORKS	\$ 54,389.06	\$ 54,389.06	0.19%	\$ -	0.00%	\$ 54,389.06	0.19%	\$ -
	PROVISIONAL SUM AND CONTINGENCY	\$ 343,891.70	\$ 61,499.72	0.22%	\$ -	0.00%	\$ 61,499.72	0.22%	\$ 282,391.98
	TOTAL =	\$ 27,411,858.12	\$ 25,791,776.32	92.07%	\$ 226,889.79	0.81%	\$ 26,018,666.11	92.88%	\$ 1,393,192.02
	PERFORMANCE BASED MAINTENANCE WORKS	\$ 599,996.82	\$ 543,705.31	1.94%		0.00%	\$ 543,705.31	1.94%	\$ 56,291.51
	CONTRACT AMOUNT	\$ 28,011,854.94	\$ 543,705.31	94.02%		0.00%	\$ 543,705.31	94.83%	\$ 27,468,149.63
	GRAND TOTAL	\$ 28,011,854.94	\$ 26,335,481.63	94.02%	\$ 226,889.79	0.81%	\$ 26,562,371.42	94.83%	\$ 1,449,483.53

Inspeksaun Husi:

Verifika Husi :

Sertifika husi :

1. (Eng. Jose R. Carlos Gusmão)
Eng. ba Projecto Infraestrutura
Transporte e Irrigação Munisipiu
Manatuto, ADN.I.P


(Eng. Remigio da C.S. dos Santos)
Eng. Senior ba projeto Infraestrutura,
Transporte e Irigasaun, ADN.I.P

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN.I.P

2. (Domingos X. daC. Silva)
Eng. ba Projetu Infraestrutura
Transporte e Irrigasaun Munisuipiu
Manatuto ADN, I.P.

3. (Eng. Augusta da Costa Ferreira)
Eng. ba Projecto PMU (Impréstimo)
ADN.I.P

4.(Eng. Vidal Guterres)
Eng. ba Projecto PMU (Impréstimo)
ADN.I.P

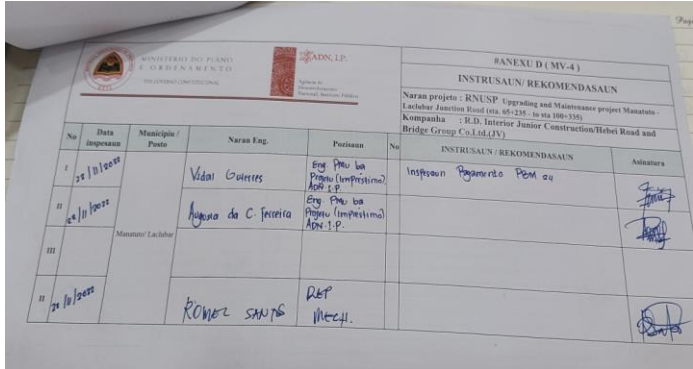 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público #ANEXU D (MV-4) INSTRUSAUN/ REKOMENDASAUN Naran projeto : RNUSP Upgrading and Maintenance project Manatuto - Laclubar Junction Road (sta. 65+235 - to sta 100+335) Kompanha : R.D. Interior Junior Construction/Hebei Road and Bridge Group Co.Ltd.(JV)							
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	24/11/2022	Manatuto/ Laclubar	Eng. Augusta da Costa Ferreira	Eng. PMU ba Projetu Imprestimo,ADN.I.P	1	Inspesaun pagametnto PBM IPC. 24	
II			Eng. Vidal Guterres	Eng. PMU ba Projetu Imprestimo,ADN.I.P			



#ANEXU C1 (SO - 4)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada
Chainage 0+000-2+000
No. kontratu : MPW-W-210059

Data Inspesaun : 18/10/2022

Fatin Inspesaun : Soibada, Buah Rahun

Koordinadas :

Start Point : Long : 8,8399S Latetude: 125,9171E

End Point : Long : 8,82990S Latetude: 125,9223E

Naran Inspector : 1. Eng. Jose Roberto Carlos Gusmão
2. Eng. Domingos D.X Silva

Sketch & Foto Desenho

Sketch Item servisu plum concrete ho
distansia 75 m

$P = 2 \times 75 \times 0.12$

$V = 18 \text{ m}^3$

Observasaun iha tereno no Foto Aktual





#ANEXU C1 (SO - 4)



Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada
Chainage 0+000-2+000
No. kontratu : MPW-W-210059

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu Routine maintenance -
wet season

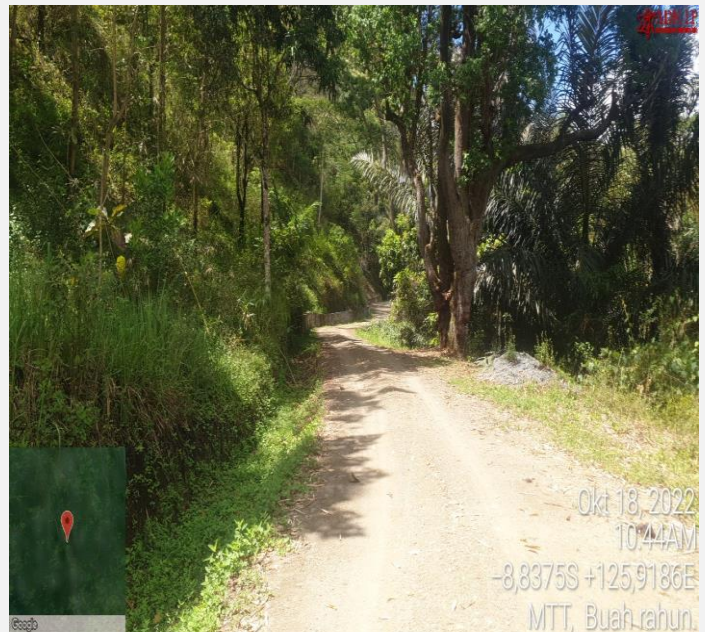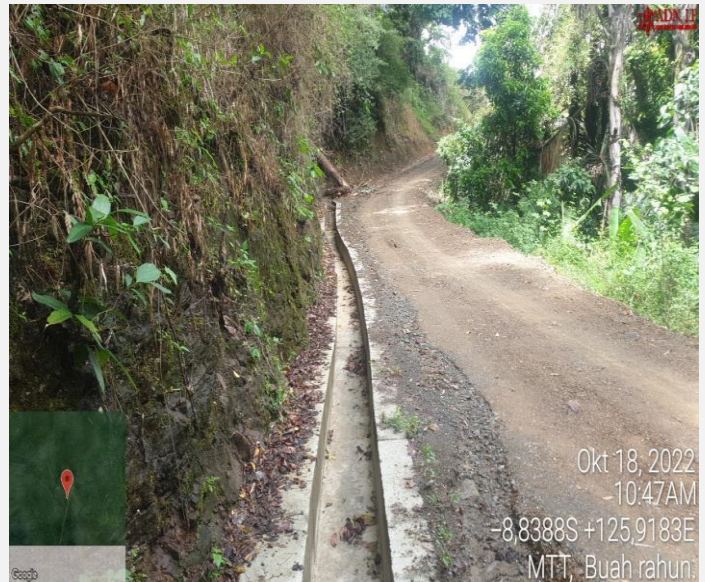



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SO - 4)


Back-up Data

Naran Projeto

: R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada
Chainage 0+000-2+000

No. kontratu

: MPW-W-210059

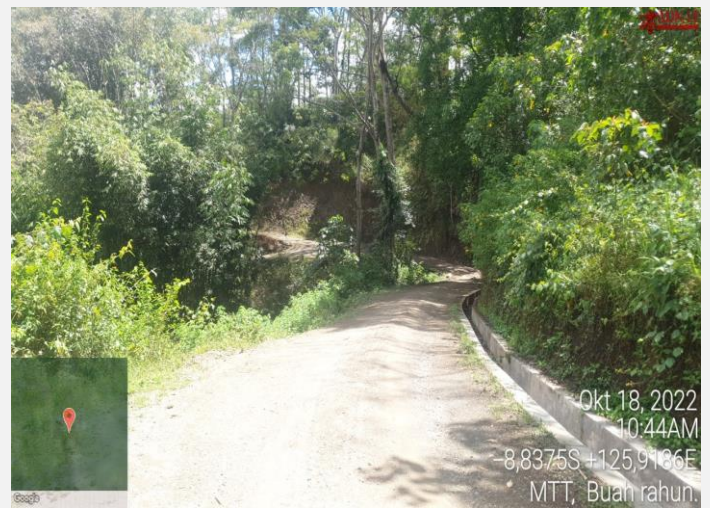



#ANEXU C2 (SO - 4)

Road Name : Manlala(Manufahi Kiik) - Soibada Chainage start 0 + 000
Municipality : Manatuto Chainage end 2+000
Postu : Soibada Length 2.0 Km
Sukos : Manufahi Kiik

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	PROGRESS PAYMENT BY A D N					
			PREVIOUS BILLING (USD)	PERECENT PREVIOUS BILLING	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
		(US\$)						
R-01	General	\$ 2,990.00	\$ 2,970.00	1.46%	\$ -	0.00%	\$ 2,970.00	1.46%
R-03	Earth work	\$ 11,037.21	\$ 12,532.73	6.17%	\$ -	0.00%	\$ 12,532.73	6.17%
R-05	Sub-base, Base and Pavament	\$ 13,353.74	\$ 12,473.94	6.14%	\$ -	0.00%	\$ 12,473.94	6.14%
R-08	Structures	\$ 121,257.00	\$ 34,991.55	17.23%	\$ -	0.00%	\$ 34,991.55	17.23%
R-10	Dayworks	\$ 1,750.00	\$ -	0.00%	\$ 175.00	0.09%	\$ 175.00	0.09%
R-11	Routine maintenance	\$ 4,205.00	\$ 3,131.00	1.54%	\$ 1,074.00	0.53%	\$ 4,205.00	2.07%
R-15	Provisional sum	\$ 200.00	\$ -	0.00%	\$ 200.00	0.10%	\$ 200.00	0.10%
A	Construction Cost	\$ 154,792.95	\$ 66,099.22	32.56%	\$ 1,449.00	0.7%	\$ 67,548.22	33.3%
B	Profit & Over Head (10% x A)	\$ 15,479.29	\$ 6,609.92	3.26%	\$ 144.90	0.07%	\$ 6,754.82	3.33%
C	General Item	\$ 28,783.23	\$ 19,005.00	9.36%	\$ 1,606.00	0.79%	\$ 20,611.00	10.15%
D	Tax 2 % x (A+B)	\$ 3,981.11	\$ 1,834.28	0.90%	\$ 64.00	0.03%	\$ 1,898.28	0.93%
E	GRAND/GROSS TOTAL	\$ 203,036.57	\$ 93,548.42	46.02%	\$ 3,263.90	1.61%	\$ 96,812.32	47.63%

Inspeksaun Husi:

Verifika Husi :

Sertifika husi :

1. (Eng. Domingos D.X. Silva)
Eng. ba Projecto Infraestrutura Transporte e
Irigação Munisipiu Manatuto, ADN.I.P

(Eng. Remigio da C.S. dos Santos)
Eng. Senior ba projeto Infraestrutura,
Transporte e Irigasaun, ADN.I.P

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e
Validação de Qualidade, ADN.I.P

2. (Eng. Jose R. Carlos Gusmão)
Eng. ba Projecto Infraestrutura Transporte e
Irigação Munisipiu Manatuto, ADN.I.P

 MINISTÉRIO DO PLANO E ORDENAMENTO VIII GOVERNO CONSTITUCIONAL  Agência de Desenvolvimento Nacional, Instituto Público						#ANEXU D (SO - 4)	
						INSTRUSAUN / REKOMENDASAUN	
						Naran projeto : R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada Chainage 0+000-2+000 Kompanha : Manufahi Kiik Unip. Lda	
No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	18/10/2022	Manatuto/ Soibada	Jose Roberto Carlos Gusmão	Eng. Ba Projetu ITI Munispiu Manatuto, AND.I.P	1	Teknik A.D.N.I.P la prenze buku tamu ho rajaun tamba kompania la servisu iha tereinu.	
II	18/10/2022	Manatuto/ Soibada	Domingos D,X Silva	Eng. Ba Projetu ITI Munispiu Manatuto, AND.I.P	2	Teknik A.D.N.I.P la prenze buku tamu ho rajaun tamba kompania la servisu iha tereinu.	



#ANEXU C1 (SO-5)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage
8+000-10+700

No. kontratu : MPW-W-210057

Data Inspesaun : 22/ 11 /2022

Fatin Inspesaun : Soibada, Fatuk Makerek

Koordinadas :

Start Point : Long : 8,8510S Latetude : 125,8697E

End Point : Long : 8,8683S Latetude : 125,8736E

Naran Inspector : 1. Eng. Jose R. C. Gusmão

2. Eng. Domingos DX. Silva

Sketch & Foto Desenho

Sketch Item servisu tamba kompania hahu servisu
fali ona iha tereinu no komesa hamos item
Routine maintenance - dry season

Observasaun iha tereno no Foto Aktual





#ANEXU C1 (SO-5)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage
8+000-10+700**
No. kontratu : **MPW-W-210057**

Sketch & Foto Desenho

Sketch Item servisu tamba kompania hahu servisu
fali ona iha tereinu no komesa hamos ba dry
season, wet- season

Observasaun iha tereno no Foto Aktual





#ANEXU C2 (SO - 5)

PROJECT NAME : R4D RURAL ROAD SPOT IMROVEMET, SOIBADA - FATUMAKEREK CHAINAGE 8+000 - 10+700
CONT.NUMBER : MPW - W - 210060
SUCO SASAHI - FATUMAQUEREC

SUMMARY

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST (US\$)	PROGRESS PAYMENT BY A D N					
			PREVIOUS BILLING (USD)	PERECENT PREVIOUS BILLING	THIS BILLING (USD)	PERCENT THIS MONTH	TOTAL TO DATE (USD)	% TO DATE
R-01	General	\$ 3,040.00	\$ 1,300.00	0.66%	\$ 250.00	0.13%	\$ 1,550.00	0.79%
R-03	Earth Work	\$ 9,242.27	\$ 1,516.37	0.77%	\$ 21,569.27	11.00%	\$ 23,085.64	11.77%
R - 05	Sub-base, Base and Pavement	\$ 12,677.94	\$ 5,762.70	2.94%	\$ 127.89	0.07%	\$ 5,890.59	3.00%
R - 08	Structure	\$ 119,043.38	\$ 23,675.42	12.07%	\$ 5,139.99	2.62%	\$ 28,815.41	14.69%
R-10	Dayworks	\$ 1,750.00	\$ 420.00	0.21%	\$ 70.00	0.04%	\$ 490.00	0.25%
R-11	Routine Maintenance	\$ 5,800.25	\$ 10,438.00	5.32%	\$ 881.00	0.45%	\$ 11,319.00	5.77%
R-15	Provisional Sum	\$ 200.00	\$ -	0.00%	\$ -	0.00%	\$ -	0.00%
A	Construction Cost	\$ 151,753.84	\$ 43,112.49	21.98%	\$ 28,038.15	14.30%	\$ 71,150.63	36.3%
B	Profit (10% x A)	\$ 15,175.38	\$ 4,311.25	2.20%	\$ 2,803.81	1.43%	\$ 7,115.06	3.63%
C	General Item	\$ 25,337.67	\$ 3,773.50	1.92%	\$ 14,479.20	7.38%	\$ 18,252.70	9.31%
D	Tax 2 % x (A+B)	\$ 3,845.34	\$ 948.47	0.52%	\$ 906.42	0.46%	\$ 1,930.37	0.98%
E	GRAND/GROSS TOTAL	\$ 196,112.23	\$ 52,145.71	26.63%	\$ 46,227.58	23.57%	\$ 98,448.76	50.20%

Inspeksaun Husi:

Verifika Husi :

Sertifika husi :

1. (Eng. Jose R Carlos Gusmão)
Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Manatuto, ADN.I.P

Eng. Aniceto da Costa
Eng. Senior ba projeto Infraestrutura,
Transporte e Irigasaun, ADN.I.P

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e
Validação de Qualidade, ADN.I.P

2. (Eng. Augusta da Costa Ferreira)
Eng. ba Projecto Infraestrutura Transporte e
Irrigação Munisipiu Manatuto, ADN.I.P



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU D (SO- 5)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700

Kompanha : Ryzena Unipessoal Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura	
I	27/12/2022	Manatuto/ Soibada	José Roberto Carlos Gusmão	Eng. Ba Projetu ITI Munisipiu Manatuto	1	Ba General Item presiza anexa nota Orijinal		
					2	Item servisu tamba kompania hahu servisu fali ona iha tereinu no komesa hamos item Routine maintenance - dry season		
II	27/12/2022	Manatuto/ Soibada	Domingos D.X.Silva	Eng. Ba Projetu ITI Munisipiu Manatuto	1	Ba General Item presiza anexa nota Orijinal		
					2	Item servisu tamba kompania hahu servisu fali ona iha tereinu no komesa hamos item Routine maintenance - dry season		



Desembro

Naran Eng.	Vidal Guterres								2022																															
Município	MUNICIPIO DILI NO POSTOS																																						Observasaun	
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		Desembro																																
								Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa									
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																												FHO					
							Actual																																	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																											halo Relatorio Pagamento						
							Actual																																	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan																												halo Relatorio Pagamento					
							Actual																																	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan																												halo Relatorio Pagamento					
							Actual																																	
	6	Road Network Upgrading Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																												halo Relatorio Pagamento					
							Actual																																	
	7	Road Climate Resilience project (RCRP) upgrading project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																												FHO					
							Actual																																	
	8	Road Climate Resilience project (RCRP) upgrading and maintenance of Dili- Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																												FHO					
							Actual																																	
	9	Road Climate Resilience project (RCRP) upgrading and maintenance of Dili- Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																												FHO					
							Actual																																	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co.Ltd JV with Kunlwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Pagamento ba Konsultan IPC 57,58,59.					
							Actual																																	
11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.Ltd JV with Kunlwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Pagamento ba Konsultan IPC 57,58,59.						
						Actual																																		
12	Upgrading and Maintenance of Laclubar Jet Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																												Inspecsaun Pagamento, PBM 01,02,03,04,05,06,07. no first half Retention Money						
						Actual																																		
13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunlwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd, and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Pagamento ba Konsultan, IPC 32, A. no 33						
						Actual																																		
14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (Km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Relatorio						
						Actual																																		
15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Philis. (Icp) Inc. (Philippines) (As Sub-Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Relatorio						
						Actual																																		
16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																												Halo Recomendasaun Pagamento IPC 11						
						Actual																																		
17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																												Recomendasaun Pagamento IPC 12						
						Actual																																		



2022

IMPRESTIMO





2022



Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		Desembro																														
								Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Selo - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																															
							Actual																															
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Muti Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																															
							Actual																															
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																															
							Actual																															
	21	For Preparation of detailed engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																															
							Actual																															
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																															
							Actual																															
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																															
							Actual																															
	24	Preparation of detailed Design for Rahabilitation municipio Roads Package 4 : turiscat to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Intercontinental Unip Lda	MPW- CS 2000028	LM		Plan																															
							Actual																															
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																															
							Actual																															
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																															
							Actual																															
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																															
							Actual																															
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana utulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																															
							Actual																															
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultani Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																															
							Actual																															
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																															
							Actual																															
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																															
							Actual																															
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																
						Actual																																
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																
						Actual																																
34	Konsultan Suprevisi for Konstruction Suprevison of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																
						Actual																																
35	Suprevison Consultant for Construction of Intersection in the Existing Dili-Liquisa Road to Connect Access Road from Tibar Bay port (National Road)	Lelo Unipessoal Lda.		LM	MOP	Plan																																
						Actual																																
36	Preparation of Detailed Engineering Design (DED) For New Cable Stayed Bridge Over the Becusse River, in Dili Total Length +	TPT Timor Unip Lda		LM	MOP	Plan																																
						Actual																																
TOTAL PROJETO ON-GOING																																						
Note:																																						
Planu Periode inspesaun iha tereinu																																						
Prepara Husi :																																						
(Eng. Teresa Gomes)																																						
Eng. PMU ba Projetu (Impréstimo), ADN, I.P.																																						
Sertifika Husi :																																						
(Eng. Emerenciana da Costa Maia Freitas)																																						
Coordenadora da Unidade de Controlo e Validação de Qualidade, ADN, I.P.																																						
Aprova Husi :																																						
(Eng. Januario Maia Guterres)																																						
Adjunto Director Executivo, ADN, I.P.																																						

SERVISU BA
KONSULTAN DESIGN
SEI AJUSTA TUIR
PLANO HUSI
PROJECTO NAIN .OU
BAZEIA BA
DOKUMENTOS
KONSULTAN NIAN
NEBE SUPMETE MAI
HUSI PROJECTO
NAIN.

FHO

Konsultan la serviso ona
iha tereno,maibe
pagamento seidauk hotu



MINISTERIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL



ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

PLANU INSPEAUN


Naran Eng.		Tito Edgar F.N. de Jesus						2022																																Observasaun
Município	MUNICIPIO DILI NO POSTOS																																							
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		Desembro																																
								Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa	Su	Mo	Tu	We	Th	Fri	Sa		
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd / Chongqing Road Engineering (Group)Co.,Ltd (Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd / Chongqing Road Engineering (Group)Co.,Ltd (Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	6	Road Network Upgrading Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	7	Road Climate Resilience project (RCRP) upgrading project and maintainace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	8	Road Climate Resilience project (RCRP) upgrading and maintainace of Dili- Ainaro Road, Lot 4 Bandudatu-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	9	Road Climate Resilience project (RCRP) upgrading and maintainace of Dili- Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no. 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co.Ltd JV with Kunlwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																																	
							Actual																																	
11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.Ltd JV with Kunlwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																																		
						Actual																																		
12	Upgrading and Maintenance ofLaclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																																		
						Actual																																		
13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunlwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																																		
						Actual																																		
14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																																		
						Actual																																		

[Handwritten signature]

REPÚBLICA DE TIMOR-LESTE MINISTÉRIO DO PLANO E ORDENAMENTO VIA GOVERNO CONSTITUCIONAL ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público							PLANU INSPESAUN																																
Naran Eng.	Adonis Julio Fernandes						2022																																
Município	MUNICIPIO MANATUTO NO POSTOS																																						
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	DESEMBRO																															OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
MANATUTO VILA (MV)	1	Konstrusaun ka Rehabilitasaun ba EBF Batara	MEJD PKRIE EBF BATARA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
	2	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MEJD PKRIE EBF AISIU-UM	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
	3	Konstrusaun ka Rehabilitasaun ba EBC Remanarun	MEJD PKRIE EBC REMANARUN	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
	4	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MEJD PKRIE EBC WEAIHUDIK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
	5	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MEJD PKRIE EBF RENTAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
	6	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MEJD PKRIE ESG KAY RALA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
	7	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MEJD PKRIE EBF OBRATO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																															Lakonsege hare tamba Okupadu ho Pagamento	
8	Construção de novo Estadio de Futebol em Manatuto	Obral Unipesoal, Lda	ICB/0128/SEJD-2014	FI	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	Plan																																	
						Actual																															Lakonsege hare tamba Okupadu ho Pagamento		
9	Konstrusaun ESTV Beadi-Manatuto	Ralan Unip. Lda	03/PDIM-I/MNTT/IX/2019	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
						Actual																															Projeitu Refere FHO ona		
10	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	Carya Timor Leste Unip. Lda	08/PDIM-I/MNTT/XII/2019	PDIM	ESTATAL	Plan																																	
						Actual																															Lakonsege hare tamba Okupadu ho Pagamento		
11	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	Carya Timor Leste Lda	01/PDIM-I/MNTT/XII/2019	PDIM	ESTATAL	Plan																																	
						Actual																															Lakonsege hare tamba Okupadu ho Pagamento		
12	Costrusaun Fatin Isolamento Iha Municipio Manatuto	Talamori Unip.Lda	RDTL-MS-DNA-DC-20-254	LM	SAUDE	Plan																																	
						Actual																															Lakonsege hare tamba Okupadu ho Pagamento		
13	Supplay and installation Main Power for Isolation and Laboratorium Building Maabat Manatuto	Fraternity Unip.Lda	RDTL-MS-C19-DNA-DC-21-229	LM	MINISTERIO DA SAUDE	Plan																																	
						Actual																															Lakonsege hare tamba Okupadu ho Pagamento		
14	New Construction of Laboratory for Covid 19 at Manatuto, Ministry of Helath, Timor Leste	Kartini Unipessoal Lda	RDTL-MS-DNA-RBK-20-186	LM	MINISTERIO DA SAUDE	Plan																														Projeitu Refere FHO ona			
						Actual																																	
LALEIA (LAL)	1	Konstrusaun ka Rehabilitasaun ba EP Cairui	MEJD PKRIE EP CAIRUI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																														Lakonsege hare tamba Okupadu ho Pagamento		
	2	Rehabilitasaun Kampu Foteboll iha Postu Administrativo Laleia	DCO Unip.Lda	011LM/AND/MP/E/VII/DILI/2019/EDIFI CIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																
							Actual																																
LALEIA (LAL)	3	Konstrusaun Edificio Posto Administrativo Laleia	Hare Unip.Lda	02/PDIM-I/MNTT/IX/2019	PDIM	ESTATAL	Plan																													Projeitu Refere FHO ona			
							Actual																																
AC)	1	New Installation Mv, Lv Line & House Connection From Laclubar Vila to Funar And Fatuk Manu - Manatuto Municipality	Tasibala III Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000412	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																														Lakonsege hare tamba okupado ho Pagamento		

Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	DESEMBRO																															OBS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
LACLUBAR (L)	2	Konstrusaun Posto Saude Iha iha Suku Funar - Lakilubar	Ladiama Unip. Lda	04/PDIM I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									</

Note:



Plano Periode inspesaun iha tereinu



Implementasaun Plano Periode inspesaun iha tereinu



Relatoriu avaliasuan mensal iha Dili



Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Adenis Julio Fernandes)
Eng. Electricidade, ADN, I.P

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo,ADN, I.P

Naran Eng.		Domingos D. X. e Silva						2022																															
Município		Manatuto																																					
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Decembro																															OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
MANATUTO VILA (MV)	1	Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto	Maran-Dai, Lda JV Adam Motor, Unip. Lda	SSS/062/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												Progressu Fíziku 100%				
							Actual																																
	2	Rehabilitacao Estrada Urbanas Jot, Ma'abat - Manatuto Vila - Sau Ponte (4.88 km) in Manatuto Municipio Manatuto	Nananui, Unip. Lda JV Ina Forek, Lda	SSS/061/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												Progressu Fíziku 100%				
							Actual																																
	4	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R,D Interior Junior Construction / Hebei Road and Bridge Group	ICB/023/MPW-2013	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
							Actual																																
	6	Manatuto to Laclubar (Ortiua Bridge)	Manu Aman Unip.Lda	nn	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													PHO			
							Actual																																
	12	Sumase River	Forte, Unip. Lda	SSS/113/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													Progressu Fíziku terrenu 100.00%			
							Actual																																
	13	Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu, Manatuto Municipality	Ilalun, Lda	SSS/115/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													Progressu Fíziku terrenu 97.52%			
							Actual																																
14	New Const. of Gabion Tower No,04 Section Manatuto - Baucau	Geovanio Unip. Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													Progressu Fíziku terrenu 98.51%				
						Actual																																	PHO
LALEIA (LAL)	3	R4d Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800	As Jazesia Unipessoal Lda	MPW-W-210055	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												Progressu Fíziku 100%				
							Actual																																
LACLUBAR (LAC)	2	Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan)	China Nuclear Industry 22ND Construction Co, LTD	ICB/04/MPW-2014	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
							Actual																																
	5	Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)	Hatuwari Unip. Lda	MPW-W-NCB-R-190035	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going					
							Actual																																
	6	Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)	Ryzena Unipessoal Lda	MOP/DGOP/DNEPCC/0871-VIII/2020	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going					
							Actual																																
	7	R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000	Sun Rise Golden Construction 02 Lda	MPW-W-210057	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On going				
							Actual																																
	8	R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000	Adahiak Orfao Unipessoal Lda	MPW-W-210056	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
							Actual																																
	SOIBADA (SO)	1	Construction of New Steel Bridge 100m in Mlotu Sahe river, jct.Fatucamanau, Soibada, Timor Leste	FIRDO UNIPESSOAL LDA	SSS/013/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																											Progressu Fíziku 100%				
								Actual																															
4		R4D Rural Road Spot Improvement Manlala (Manufahi Kiik) - Soibada Chainage 0+000-2+000	Manufahi Kiik Unip. Lda	MPW-W-210059	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																											On Going					
							Actual																																
5		R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700	Ryzena Unipessoal Lda	MPW-W-210060	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																												On Going				
							Actual																																

[illegible]

 MINISTERIO DO PLANO E ORDENAMENTO SECRETARIA DE PLANEJAMENTO E ORÇAMENTO ADN, L.P. Agência de Planejamento Nacional - Instituto Público							PLANU INSPESAUN																														
Naran Eng. Jose Roberto Carlos Gusmão							2022																														
Município																																					
Manatuto																																					
Município / Posto																																					
No.																																					
Naran Projeto																																					
Naran Companhia																																					
No Contrato																																					
Categoria																																					
Dono do Projeto																																					
Action																																					
							Decembro																														
							1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31																														
							OBS																														
MANATUTO VILA (MV)							1		Rehabilitation Estrada Urbanas Manatuto Vila (3.72 km) area in Manatuto Municipality Manatuto		Maran-Dai, Lda JV Adam Motor, Unip. Lda		SSS/062/MOPTC-2017		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku 100%		
									Actual																Relatoria Fulan Novembro Eng. Município Manatuto la halo Inpesaun la Maximo tamba projeto refere finaliza 100% ona ita tereno, no kompania hein rekomendaduan ita hui DNFFCC (MOP). Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional												
							2		Rehabilitacao Estrada Urbanas Jct. Ma'abat - Manatuto Vila - Sau Ponte (4.68 km) in Manatuto Município Manatuto		Nananlu, Unip. Lda JV Ina Forek, Lda		SSS/061/MOPTC-2017		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku 100%		
									Actual																Relatoria Fulan Novembro Eng. Município Manatuto la halo Inpesaun la Maximo tamba projeto refere finaliza 100% ona ita tereno, no kompania hein rekomendaduan ita hui DNFFCC (MOP). Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional												
							4		Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)		R.D Interior Junior Construction / Hebei Road and Bridge Group		ICB/023/MPW-2013		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going		
									Actual																Relatoria Fulan Nov Eng. Município Manatuto la halo Inpesaun Maximo tamba durante ne'e Eng Dñ mak reponabizira inspeksaun ba projeto Imprestima (ADB) Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional												
							6		Manatuto to Laclubar (Orhua Bridge)		Manu Aman Unip.Lda		nn		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																PHO		
									Actual																PHO												
							12		Sumase River		Forte, Unip. Lda		SSS/113/MOPTC-2017		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku terrenu 100.00%		
									Actual																PHO												
							13		Rehabilitation of Roads Monumento - Laclubar, Mercado Hua-Lu, Manatuto Municipality		Ilatun, Lda		SSS/115/MOPTC-2016		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku terrenu 97.52%		
									Actual																PHO												
							14		New Const. of Gabion Tower No.04 Section Manatuto - Baucau		Geovario Unip. Lda				LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku terrenu 98.51%		
									Actual																PHO												
LALEI A (LAL)		3		R4D Rural Road Routine Maintenance Haturalan - Cairui Chainage 0+000-9+800		As Jazesia Unipessoal Lda		MPW-W-210055		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku 100%							
														Actual																PHO							
LACLUBAR (LAC)		2		Road Network Upgrading Project (RNUP) for Laclubar - natarbora (ADB Loan)		China Nuclear Industry 22ND Construction Co; LTD		ICB/04/MPW-2014		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going							
														Actual																Relatoria Fulan Nov Eng. Município Manatuto la halo Inpesaun Maximo tamba durante ne'e Eng Dñ mak reponabizira inspeksaun ba projeto Imprestima (ADB) Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
		5		Rural Roads (R4D) Periodic Maintenance Laclubar Fatumakerek Chainage 0+000 - 27+000 (162)		Hatuwari Unip. Lda		MPW-W-NCB-R-190035		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going							
														Actual																Relatoria Fulan Nov Eng. Município la realiza Maximo tamba, projeto refere kompania sei kontinua servisu ita tereno tamba ne'e teknik Município la halo monitoria ita tereno ho rajuan tamba koutan tempo no relasan pagamentu Annual Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
		6		Routine Roads Maintenance - JCTA09 Laclubar (C15) Manatuto Municipality (162)		Ryzena Unipessoal Lda		MOP/DGOP/DNEPCC/0871-VIII/2020		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going							
														Actual																Relatoria Fulan Nov Eng. Município la realiza Maximo tamba, projeto refere kompania la servisu ona ita tereno tamba ne'e kompania ita kontinua volume remate ona mabe lokalizadun teknik volunente sedak aragat 100% tamba ita defete Dimensuan excavasion ho ida ne'e volume sei meno ita tereno, tamba ne'e teknik Município la halo monitoria ita tereno tamba projeto refere kategori Abandona Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
		7		R4D Rural Road Spot Improvement Funar - Fatumakerek Chainage 12+000 - 27+000		Sun Rise Golden Construction 02 Lda		MPW-W-210057		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																On going							
														Actual																Relatoria Fulan Nov Eng. Município la bele realiza monitoring tamba projeto refere lokaliza ita Fatumakerek balaz entre Turseca tamba a'1 belot taka estrada laran hodi diffidulu Eng Município la bele areu ata manatuto projeto kark Eng Município atu monitoria projeto refere teknik ulupapa la hui Sane Poste Administrativa Turical Vila Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
		8		R4D Rural Road Spot Improvement Laclubar - Funar Chainage 0+000 - 12+000		Adahiak Orfao Unipessoal Lda		MPW-W-210056		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going							
														Actual																Relatoria Fulan Novembro Eng. Município Manatuto la halo Inpesaun maksimu tamba relasan pagamentu anual projeto refere kompania kontinuasun servisu hela ita tereno, mabe ita mos mudasa lokaliza projeto refere no agora dadun kompania servisu hela ita tereno posto Laclubar Vila, atu informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
SOIBADA (SO)		1		Construction of New Steel Bridge 100m in Mitou Sahe river, jct.Fatucamanau, Soibada, Timor Leste		FIRDO UNIPESOAAL LDA		SSS/013/MOPTC-2017		FI		MINISTERIO DAS OBRAS PUBLICAS		Plan																Progressu Fízku 100%							
														Actual																Relatoria Fulan Novembro Eng. Município Manatuto halo Inpesaun ita tereno ba pagamentu anual, projeto refere kategori fani (PHO), tamba ne'e ita mos mudasa progressu anterior 100%, mabe hui parte teknik halo dedakasan ba item AC-WC tamba menua ita tereno tur rejuladu inspeksaun pagamentu progressu fali ataja dot 99.93% ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
		4		R4D Rural Road Spot Improvement Marlala (Manufahi Kikik) - Soibada Chainage 0+000-2+000		Manufahi Kikik Unip. Lda		MPW-W-210059		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going							
														Actual																Relatoria Fulan Nov Eng. Município la realiza Maximo tamba, projeto refere kompania sei kontinua servisu ita tereno tamba ne'e teknik Município la monitoria maksimu monitoria ita tereno ho rajuan tamba koutan tempo no relasan pagamentu Annual Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							
		5		R4D Rural Road Spot Improvement Soibada - Fatumakerek Chainage 8+000-10+700		Ryzena Unipessoal Lda		MPW-W-210060		LM		MINISTERIO DAS OBRAS PUBLICAS		Plan																On Going							
														Actual																Relatoria Fulan Novembro Eng. Município Manatuto la halo Inpesaun Maximo tamba koutan tempo no udan Projeto refere kompania hui servisu fali ona ita tereno Atu Informa mos katak ita fulan28 de Novembro de 2022 leron Independensia Timor Leste lokaliza ita Manatuto Vila tamba ne'e Teknik la halo Monitoria maksimu tamba apoa Tekniku Nasional							

2022

PLANU INSPESAUN

Naran Eng. Fabiano Fitalis Maria Madeira							2022																																	
Municipio	MUNICIPIO MANATUTO NO POSTOS						Action	Dezembro																															OBS	
Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		
MANATUTO VILA (MV)	3	Construção de novo Estadio de Futebol em Manatuto	Obrai Unipesoal, Lda	ICB/0128/SEJD-2014	FI	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	Plan	■							■																									On Going
							Actual																																	
	6	Konstrusaun ESTV Beadi-Manatuto	Ralan Unip. Lda	03/PDIM-IIMNTT/IX/2019	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																FHO	
							Actual																																	
	7	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	Carya Timor Leste Unip. Lda	08/PDIM-IMNTT/XII/2019	PDIM	ESTATAL	Plan	■							■																								On Going	
							Actual																																	
	8	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	Carya Timor Leste Lda	01/PDIM-IMNTT/XII/2019	PDIM	ESTATAL	Plan	■							■																									On Going
							Actual																																	
	9	Servisu Manutensaun Edifisiu CRC Munisipiu Manatuto	Baboe Unip Lda	019/Janeiro/2020	LM	MINISTERIO DA JUSTICA	Plan																																	FHO
							Actual																																	
	10	New Construction of Laboratory for Covid 19 at Manatuto, Ministry of Helath, Timor Leste	Karlini Unipessoal Lda	RDTL-MS-DNA-RBK-20-186	LM	MINISTERIO SAUDE	Plan																																	FHO
							Actual																																	
	13	Konstrusaun Fatin Isolamentu iha Munisipiu Manatuto	Talamori Unip,Lda	RDTL-MS-DNA-DC-20-254	LM	MINISTERIO SAUDE	Plan	■								■																								On Going
							Actual																																	
	15	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MEJD PKRIE ESG KAY RALA	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	■								■																								On Going
							Actual																																	
	16	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MEJD PKRIE EBF RENTAU	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	■								■																								On Going
							Actual																																	
	17	Konstrusaun ka Rehabilitasaun ba PE Rembor	MEJD PKRIE PE REMBOR	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	■								■																								On Going
							Actual																																	
	18	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MEJD PKRIE EBF OBRATO	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	■								■																								On Going
Actual																																								
19	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MEJD PKRIE EBF BAHADIK	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	■								■																								Sedauk Implementa	
						Actual																																		
20	Supplay and Installation Main Power For Isolation an Laboratorium Building Maabat Manatuto	MINISTERIO SAUDE	RDTL-MS-C19-DNA-DC-21-229	FI	MINESTERIO SAUDE	Plan	■								■																								PHO	
						Actual																																		
21	New Construction of Fence at Islation	MINISTERIO SAUDE	RDTL-MS-C19-DNA-DC-21-227		MINESTERIO SAUDE	Plan	■								■	■																							On Going	
						Actual																																		

Naran Eng. Fabiano Fitalis Maria Madeira							2022																																	
Município	MUNICIPIO MANATUTO NO POSTOS																																							
Município / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Dezembro																															OBS	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		
LALÉA (LAL)	1	Rehabilitasaun Kampu Foteboll Iha Postu Administrativu Laleia	DCO Unip.Lda	011LM/AND/MPIE/VI/DILU/2019/ED IFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																Pendenti	
							Actual																																	
	2	Konstrusaun Edifício Posto Administrativo Laleia	Hare Unip.Lda	02/PDIM-IMNTT/X/2019	PDIM	ESTATAL	Plan																																FHO	
							Actual																																	
	4	Konstrusaun ka Rehabilitasaun ba EP Cairui	MEJD PKRIE EP CAIRUI	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	On Going
							Actual																																	
LACLUBAR (LAC)	3	Konstrusaun Posto Saude Iha Iha Suku Funar - Laklubar	Ladiama Unip. Lda	04/PDIM IMNTT/X/2019	PDIM	MINISTERIO SAUDE	Plan																																Kontrato Remata Ona	
							Actual																																	
	4	Konstrusaun Rezidencia PesoaI Iha Iha Suku Funar - Laklubar	Tonijo Unip. Lda	05/PDIM-IMNTT/X/2019	PDIM	MINISTERIO SAUDE	Plan																																FHO	
							Actual																																	
	9	Kontinuasaun Konst. Postu Saude Iha Suku Fatumakerek	Hatuwari Unip. Lda	02/PDD-II/MNTT/VI/2015	PDIM	MINISTERIO SAUDE	Plan																																On Going	
							Actual																																	
	10	Konstrusaun ka Rehabilitasaun ba EBF Batara	MEJD PKRIE EBF BATARA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	On Going
							Actual																																	
	11	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MEJD PKRIE EBF AISIU-UM		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	On Going
							Actual																																	
	SOIBADA (SO)	2	Konstrusaun ESTV Soibada Manatuto (CA + CB)	Manufahi Kik Unip. Lda	01/PDIM-IMNTT/X/2019	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																FHO
								Actual																																
3		Projetu Rehabilitasaun Ensinu Sekundariu Tekniku Vokasional Soibada, Manatuto	Manufahi Kik Unip. Lda	-	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																On Going	
							Actual																																	
7	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MEJD PKRIE EBF WEAIHUDIK		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
						Actual																																		
BARIQUE (BA)	2	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	Tasibala II Const	RDTL/PO:2016-11272	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																																Abandona	
							Actual																																	
	4	Konstrusaun Postu Saude Aimeta Laran-Barique	Malack II Unip. Lda	03/PDIM-IMNTT/X/2019	PDIM	MINISTERIO SAUDE	Plan																															On Going		
							Actual																																	
	5	Construction of Residense for Health Staff in Suku Aimeta Laran-Barique	Macucuren Unip. Lda	03/PDIM-IMNTT/X/2019	PDIM	MINISTERIO SAUDE	Plan																															FHO		
							Actual																																	
	6	Konstrusaun Sistema Bee Mos Iha Suco Aubeon no Aimetalaran /162	Malaca Unip Lda	No. Kontratu : MOP-W-190233	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Projeitu BTL:EP		
							Actual																																	
	11	New Contruction of Gapura and Gabion Wall Protection no Jardim de Herois de Natarbora	Senizu Unip. Lda	215/MACLN/X/2021	LM	MACLN	Plan																																On Going	
							Actual																																	

