



REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público



RELATORIU MENSAL
IMPLEMENTASAUN
PROJETUS MUNISIPIU COVALIMA
DEZEMBRO 2021



SUMÁRIO

RELATÓRIO


IMPLEMENTAÇÃO PROJETO INFRAESTRUTURA IHA MUNICÍPIO COVALIMA

DESEMBRO 2021

Prepara Husi :


(Eng. Madelino D J Magno)
Eng. ba Edifício Público no Beé Saneamento,
Município Covalima ADN, I.P


(Eng. Domingos Soares Martins)
Eng. ba Projeto Infraestrutura, Transporte e
Irigação, Município Covalima ADN, I.P


(Eng. Prezenzio L C D Ximenes)
Eng. ba Edifício Público no Beé Saneamento,
Município Covalima ADN, I.P


(Eng. Bosco Dinis de Sousa)
Eng. ba Projeto Infraestrutura, Transporte e
Irigação, Município Covalima ADN, I.P


(Silvino D R R Soares)
Eng. M & E, Município Covalima ADN, I.P

Verifica Husi :


(Arc. Francisco X D D Jeronimo)
Eng. Senior ba Edifício Público no Beé
Saneamento, ADN, I.P


(Eng. Aniceto da Costa)
Eng. Senior ba Projeto Infraestrutura,
Transporte e Irrigação, ADN, I.P


(Deolindo de F Marques)
Chefe Sek. Projeto M.E & ITC, ADN, I.P

Sertifica Husi :


(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade,
ADN, I.P

Aprova Husi :


(Mariano Renato Monteiro da Cruz, S. T. M. Eng.)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO	1
INDICE	2
I. INTRODUSAUN	3
1.1 Enkuadramentu Legal.....	3
1.2 Perfil Municipio Covalima.....	3
1.3. Lista Projectos.....	6
II. PROGRESU FISIKU	21
2.1 Progreso Fisiku Kada Fulan.....	21
III. OBSTÁCLO IHA TERENU	21
3.1 Obstáculo Servisu Iha Terenu	21
IV. REKOMENDASAUN IHA TERENU	22
4.1 Rekomendasaun Servisu Iha Terenu	22

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias.....	4
Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Covalima.....	5
Tabela 1.2 : Lista Asset ADN,I.P Municipio Covalima	5
Tabela 1.3.1 : Projecto Municipio Covalima Por Fundus Finansiamentos	7
Tabela 1.3.2 : Projecto Municipio Covalima Por Sectores.....	11
Tabela 1.3.3 : Projecto Municipio Covalima Por Ministerio.....	16
Tabela 1.4 : Dadus Populasaun Munisipiu Covalima	21


I. INTRODUSAUN

1.1 Enkuadramentu Legal

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ho Misaun ADN nian maka atu aseguza katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho qualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análise kustu-benefisiu ne'ebe razoável no viável. Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Público (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimento nian.
2. Halo fiskalizasaun no sertifikasaun qualidade ba projetu sira iha programa Kapital Desenvolvimento nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Covalima

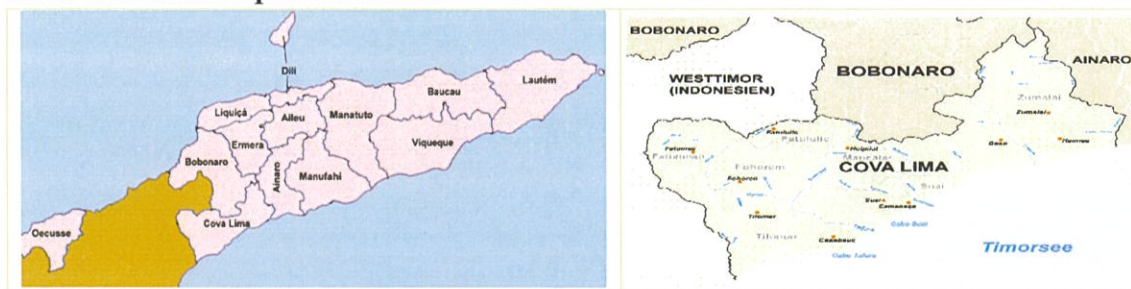

Hatudu pozisaun jeográfika Administrasaun Munisipal Covalima iha area luan 1,226 km², ho populasau emá nain – 59,455 tuir Sensus 2010. Munisipiu Covalima iha Posto Administrativo 7, Sukus 30 no aldeias 148 ne'ebé hatudu iha Tabela 1. Posto

Administrativo Zumalai iha Sukus barak liu kompara ho Sukus seluk iha Administrasaun Munisipal Cova-Lima.

Tabela 1 : Postos Administrativos,Sucos no Aldeias

Fatululik		Fohorem		Zumalai		Maucatar	
Sukus	Aldeia	Sukus	Aldeia	Suku	Aldeia	Sukus	Aldeia
Fatululik	3	Dato 2	3	Tashilin	4	Belecassac	7
Taroman	5	Dato 3	3	fatutetu	5	Holpilat	6
		Fohorem	5	lepo	5	Matai	4
		Lactos	4	Lour	7	Ogues	5
				Mape	3		
				Raimea	4		
				Ucecai	2		
				Zulo	4		
Total	8		15		34		22
Suai		Timolar		Fatumean			
sukus	Aldeia	sukus	Aldeia	Suku	Aldeia		
Beco	11	Beiseuk	7	Belulik leten	4		
Debos	9	lalawa	6	fatumean	4		
Camnaça	4	Maudemo	7	Nunu	4		
Labarai	5	Casabauk	3				
Suai Loro	5						
	43		23		12		

Data husi: Livro 3 B OJE 2021, pag 39

Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Covalima

Forca de Trabalho ADN,I.P Municipio Covalima/Suai								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	4					4	
2	Administrasaun no Financas	0					0	
3	Motorista	1					1	
4	Seguransa	0					0	
Total		5					5	

Tabela 1.2. : Lista Asset ADN,I.P Municipio Covalima

ASET ADN,IP MUNICIPIO COVALIMA								
No	Deskrisaun	Total Aset Kada Tinan					Total	OBS
		2021	2022	2023	2024	2025		
1	Edificio	1					1	Eletricidade, odamatan, janela, ho plumbing presija hadia no pinta foun
2	Kareta	1					1	
3	Desktop HP / Monitor	1					1	Diak
4	Laptop HP	1					1	Presija Troka no aumenta 1
5	Printer HP (Kiik hitam&Mutin)	1					1	Aat presija troka (A3 warna)
6	UPS	1					0	
7	Armario File	2					2	1 Aat
8	Armario Tau hena	3					3	Diak
9	Meja escritorio	1					1	Diak
10	Meja han	1					1	Diak

11	Meja TV (kiik)	1					1	Diak
12	Kadeira han	6					6	Diak
13	Kadeira Rotan + Massa	6					6	Diak
14	Sofa	1 Set					1	Aat presija troka
15	Springbed +sumasu 4+sprei 3	3 Set					3	Sprei presija troka
16	Jeleira	1					1	Diak
17	Water Dispenser	1					1	Aat
18	TV + Parabola	1 Set					1	Aat
19	AC	4					4	1 aat, 3 presija manutensaun
20	Kompor	1					1	Aat
21	Kompor Gas	1					1	Aat
22	Rack Piring	1					1	Diak
23	Water Pump Sanyo	1					1	Diak

1.3. Lista Projectos

Projetu hotu neébe akumulá iha lista neé bazeia ba dados projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamento, tabela 1.3.2 Projetu por Sector no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabela 1.3.1 : Projecto Municipio Covalima Por Fundus Finansiamentos

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM-CD + PDIM + LM-BS + LM-TP + FUNDU COVID-19		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik	2	\$ 2,745,409.37	81.02%
2	Fatumea	3	\$ 3,801,173.06	78.03%
3	Fohorem	5	\$ 7,566,532.36	93.34%
4	Maucatar	3	\$ 1,363,085.95	63.82%
5	Multy Posto	5	\$ 5,614,470.32	81.98%
6	Suai Villa	21	\$ 96,931,858.33	91.23%
7	Tilomar	7	\$ 1,560,769.70	63.40%
8	Zumalai	17	\$ 26,875,795.89	67.02%
Grand Total		63	\$ 146,459,094.98	85.46%

NO	POSTO ADMINISTRATIVO	FI		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik	1	\$ 2,445,005.95	86.59%
2	Fatumea	1	\$ 3,407,674.66	78.79%
3	Fohorem	4	\$ 7,282,268.51	95.05%
4	Maucatar	1	\$ 955,722.62	78.02%
5	Multy Posto	3	\$ 5,471,153.29	83.57%
6	Suai Villa	11	\$ 95,135,977.91	91.79%
7	Tilomar	2	\$ 806,244.40	80.14%
8	Zumalai	9	\$ 23,357,166.45	66.57%
Grand Total		32	\$ 138,861,213.79	86.82%

NO	POSTO ADMINISTRATIVO	LM-CD		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik			
2	Fatumea			
3	Fohorem	1	\$ 284,263.85	49.47%
4	Maucatar			
5	Multy Posto	2	\$ 143,317.03	21.06%
6	Suai Villa	5	\$ 930,887.00	57.99%
7	Tilomar	3	\$ 534,590.93	32.71%
8	Zumalai	3	\$ 1,039,111.25	54.20%
Grand Total		14	\$ 2,932,170.06	49.41%

NO	POSTO ADMINISTRATIVO	PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik			
2	Fatumea	1	\$ 228,246.62	89.92%
3	Fohorem			
4	Maucatar	1	\$ 164,861.91	0.00%
5	Multy Posto			
6	Suai Villa	1	\$ 115,587.75	95.72%
7	Tilomar	1	\$ 186,843.31	77.43%
8	Zumalai	3	\$ 558,116.96	94.92%
Grand Total		7	\$ 1,253,656.55	79.00%

NO	POSTO ADMINISTRATIVO	LM-BS		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik	1	\$ 300,403.42	35.69%
2	Fatumea	1	\$ 165,251.78	45.79%
3	Fohorem			
4	Maucatar	1	\$ 242,501.42	51.26%
5	Multy Posto			
6	Suai Villa	1	\$ 226,245.45	39.84%
7	Tilomar	1	\$ 33,091.06	72.00%
8	Zumalai	1	\$ 724,741.23	58.96%
Grand Total		6	\$ 1,692,234.36	50.14%

NO	POSTO ADMINISTRATIVO	LM-TP		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik			
2	Fatumea			
3	Fohorem			
4	Maucatar			
5	Multy Posto			
6	Suai Villa			
7	Tilomar			
8	Zumalai	1	\$ 1,196,660.00	78.70%
Grand Total		1	\$ 1,196,660.00	78.70%

NO	POSTO ADMINISTRATIVO	FUNDU COVID-19		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Fatululik			
2	Fatumea			
3	Fohorem			
4	Maucatar			
5	Multy Posto			
6	Suai Villa	3	\$ 523,160.22	70.19%
7	Tilomar			
8	Zumalai			
	Grand Total	3	\$ 523,160.22	70.19%

Dadus detallu kada projetu: #Anexu A

Tabela 1.3.2 : Projecto Municipio Covalima Por Sectores

NO	SECTOR PROYECTO	TOTAL MUNICIPIO COVALIMA		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos	3	\$ 72,526,168.60	92.85%
2	Agua E Saneamento	6	\$ 1,950,202.36	53.72%
3	Edificios Publicos	8	\$ 2,229,994.58	58.72%
4	Edukasaun	2	\$ 293,218.52	90.51%
5	Eletrifikasaun Nasional	5	\$ 2,730,729.02	61.19%
6	Estradas	22	\$ 54,501,632.01	78.60%
7	Flood Control	2	\$ 769,063.25	48.16%
8	Juventude No Desportu	1	\$ 136,718.09	99.86%
9	Manutensaun No Rehabilitasaun	7	\$ 1,507,681.83	62.76%
10	Pontes	2	\$ 8,755,658.60	95.58%
11	Saude	5	\$ 1,058,028.12	82.29%
Grand Total		63	\$ 146,459,094.98	85.46%

NO	SECTOR PROYECTO	Fatululik		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos			
2	Agua E Saneamento			
3	Edificios Publicos			
4	Edukasaun			
5	Eletrifikasaun Nasional			
6	Estradas	1	\$ 300,403.42	35.69%
7	Flood Control			
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun			
10	Pontes	1	\$ 2,445,005.95	86.59%
11	Saude			
Grand Total		2	\$ 2,745,409.37	81.02%

NO	SECTOR PROYECTO	Fatumea		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos			
2	Agua E Saneamento	1	\$ 165,251.78	45.79%
3	Edificios Publicos			
4	Edukasaun			
5	Eletrifikasaun Nasional			
6	Estradas	1	\$ 3,407,674.66	78.79%
7	Flood Control			
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun			
10	Pontes			
11	Saude	1	\$ 228,246.62	89.92%
	Grand Total	3	\$ 3,801,173.06	78.03%

NO	SECTOR PROYECTO	Fohorem		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos			
2	Agua E Saneamento	1	\$ 284,263.85	49.47%
3	Edificios Publicos			
4	Edukasaun			
5	Eletrifikasaun Nasional			
6	Estradas			
7	Flood Control			
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun	3	\$ 971,615.86	68.98%
10	Pontes	1	\$ 6,310,652.65	99.06%
11	Saude			
	Grand Total	5	\$ 7,566,532.36	93.34%

NO	SECTOR PROYECTO	Maucatar		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeropertos			
2	Agua E Saneamento			
3	Edificios Publicos	1	\$ 164,861.91	0.00%
4	Edukasaun			
5	Eletrifikasaun Nasional			
6	Estradas	1	\$ 955,722.62	78.02%
7	Flood Control			
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun	1	\$ 242,501.42	51.26%
10	Pontes			
11	Saude			
Grand Total		3	\$ 1,363,085.95	63.82%

NO	SECTOR PROYECTO	Multy Posto		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeropertos			
2	Agua E Saneamento			
3	Edificios Publicos			
4	Edukasaun			
5	Eletrifikasaun Nasional			
6	Estradas	3	\$ 5,430,116.11	82.93%
7	Flood Control			
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun	2	\$ 184,354.21	53.84%
10	Pontes			
11	Saude			
Grand Total		5	\$ 5,614,470.32	81.98%

NO	SECTOR PROYECTO	Suai Villa		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos	3	\$ 72,526,168.60	92.85%
2	Agua E Saneamento	3	\$ 775,945.50	52.06%
3	Edificios Publicos	3	\$ 410,001.02	54.04%
4	Edukasaun	1	\$ 115,587.75	95.72%
5	Eletrifikasaun Nasional	2	\$ 1,218,543.47	34.52%
6	Estradas	7	\$ 21,486,441.90	91.50%
7	Flood Control			
8	Juventude No Desportu	1	\$ 136,718.09	99.86%
9	Manutensaun No Rehabilitasaun			
10	Pontes			
11	Saude	1	\$ 262,452.00	55.51%
	Grand Total	21	\$ 96,931,858.33	91.23%

NO	SECTOR PROYECTO	Tilomar		
		TOTAL PROYECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos			
2	Agua E Saneamento			
3	Edificios Publicos	3	\$ 458,471.65	31.90%
4	Edukasaun			
5	Eletrifikasaun Nasional	1	\$ 323,539.34	87.54%
6	Estradas	1	\$ 482,705.06	75.18%
7	Flood Control			
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun	1	\$ 109,210.34	48.01%
10	Pontes			
11	Saude	1	\$ 186,843.31	77.43%
	Grand Total	7	\$ 1,560,769.70	63.40%

NO	SECTOR PROJECTO	Zumalai		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Aeroportos			
2	Agua E Saneamento	1	\$ 724,741.23	58.96%
3	Edificios Publicos	1	\$ 1,196,660.00	78.70%
4	Edukasaun	1	\$ 177,630.77	87.11%
5	Eletrifikasaun Nasional	2	\$ 1,188,646.21	81.35%
6	Estradas	8	\$ 22,438,568.24	65.85%
7	Flood Control	2	\$ 769,063.25	48.16%
8	Juventude No Desportu			
9	Manutensaun No Rehabilitasaun			
10	Pontes			
11	Saude	2	\$ 380,486.19	98.57%
	Grand Total	17	\$ 26,875,795.89	67.02%

Dadus detallu kada projetu: #Anexu A

Tabela 1.3.3 : Projecto Municipio Covalima Por Ministerio

NO	DONO DO PROJECTO	GRAND TOTAL		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat	1	\$ 164,861.91	0.00%
2	Gabinete Do Primeiro Ministro	1	\$ 1,196,660.00	78.70%
3	Ministerio Agrikultura E Pescas	1	\$ 260,523.18	35.26%
4	Ministerio Da Justica	1	\$ 149,292.80	0.00%
5	Ministerio Das Obras Publicas	42	\$ 69,690,062.09	78.76%
6	Ministerio Do Petroleo E Recursos Minerais	1	\$ 95,176.06	94.04%
7	Ministerio Edukasaun Juventude E Desportu	2	\$ 293,218.52	90.51%
8	Ministerio Planu E Ordenamentu	2	\$ 401,099.89	99.95%
9	Ministerio Saude	9	\$ 1,744,116.93	69.64%
10	Ministerio Tranportes E Komunikaun	2	\$ 72,430,992.54	92.84%
11	Ministerio Turismo Komercio E Industria	1	\$ 33,091.06	72.00%
Grand Total		63	\$ 146,459,094.98	85.46%

NO	DONO DO PROJECTO	Fatululik		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	2	\$ 2,745,409.37	81.02%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu			
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude			
10	Ministerio Tranportes E Komunikaun			
11	Ministerio Turismo Komercio E Industria			
	Grand Total	2	\$ 2,745,409.37	81.02%
NO	DONO DO PROJECTO	Fatumea		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	2	\$ 3,572,926.44	77.27%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu			
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude	1	\$ 228,246.62	89.92%
10	Ministerio Tranportes E Komunikaun			
11	Ministerio Turismo Komercio E Industria			
	Grand Total	3	\$ 3,801,173.06	78.03%

NO	DONO DO PROJECTO	Fohorem		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	5	\$ 7,566,532.36	93.34%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu			
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude			
10	Ministerio Tranportes E Komunikasaun			
11	Ministerio Turismo Komercio E Industria			
	Grand Total	5	\$ 7,566,532.36	93.34%
NO	DONO DO PROJECTO	Maucatar		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat	1	\$ 164,861.91	0.00%
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	2	\$ 1,198,224.04	72.60%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu			
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude			
10	Ministerio Tranportes E Komunikasaun			
11	Ministerio Turismo Komercio E Industria			
	Grand Total	3	\$ 1,363,085.95	63.82%

NO	DONO DO PROJECTO	Multy Posto		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	5	\$ 5,614,470.32	81.98%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu			
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude			
10	Ministerio Tranportes E Komunikasaun			
11	Ministerio Turismo Komercio E Industria			
Grand Total		5	\$ 5,614,470.32	81.98%
NO	DONO DO PROJECTO	Suai Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica	1	\$ 149,292.80	0.00%
5	Ministerio Das Obras Publicas	11	\$ 23,216,549.07	87.09%
6	Ministerio Do Petroleo E Recursos Minerais	1	\$ 95,176.06	94.04%
7	Ministerio Edukasaun Juventude E Desportu	1	\$ 115,587.75	95.72%
8	Ministerio Planu E Ordenamentu	2	\$ 401,099.89	99.95%
9	Ministerio Saude	3	\$ 523,160.22	70.19%
10	Ministerio Tranportes E Komunikasaun	2	\$ 72,430,992.54	92.84%
11	Ministerio Turismo Komercio E Industria			
Grand Total		21	\$ 96,931,858.33	91.23%

NO	DONO DO PROJECTO	Tilomar		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro			
3	Ministerio Agrikultura E Pescas			
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	3	\$ 915,454.74	76.31%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu			
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude	3	\$ 612,223.90	43.63%
10	Ministerio Tranportes E Komunikasaun			
11	Ministerio Turismo Komercio E Industria	1	\$ 33,091.06	72.00%
Grand Total		7	\$ 1,560,769.70	63.40%
NO	DONO DO PROJECTO	Zumalai		
		TOTAL PROJECTO	MONTANTE KONTRATO (\$)	PERSENTAGEM EXECUSAUN (%)
1	Estatat			
2	Gabinete Do Primeiro Ministro	1	\$ 1,196,660.00	78.70%
3	Ministerio Agrikultura E Pescas	1	\$ 260,523.18	35.26%
4	Ministerio Da Justica			
5	Ministerio Das Obras Publicas	12	\$ 24,860,495.75	66.16%
6	Ministerio Do Petroleo E Recursos Minerais			
7	Ministerio Edukasaun Juventude E Desportu	1	\$ 177,630.77	87.11%
8	Ministerio Planu E Ordenamentu			
9	Ministerio Saude	2	\$ 380,486.19	98.57%
10	Ministerio Tranportes E Komunikasaun			
11	Ministerio Turismo Komercio E Industria			
Grand Total		17	\$ 26,875,795.89	67.02%

Dadus detallu kada projetu: #Anexu A

Tabela 1.4 : Dadus Populasaun Munisipiu Covalima

Posto Administrativu, Suku no Sexu	2021				
	Total	Idade Produktivu (idade 15-64)		Idade la Produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Fatululic	2,149	1,816	1,952	1,876	1,779
Fatumean	3,488	820	887	920	861
Fohorem	4,402	1,199	1,266	977	960
Maucatar	9,656	2,833	2,842	2,054	1,927
Suai	27,929	8,582	8,280	5,585	5,481
Tilomar	8,431	2,357	2,239	1,963	1,872
Zumalai	14,139	3,864	3,895	3,257	3,123

Fontes : Projeksaun Populasaun bazeia ba Sensus Populasaun no Umakain 2015,

Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu progresu actual fulan ida ne'e ho nia porsentagen servisu, montante actual bazeia ba orsamentu ne'ebe hetan husi progresu fulan ida ne'e, ikus liu porsentagen actual fulan ida ne'e hatudu progressu fisiku komulativu husi porsentu anterior no fulan ida ne'e nian, lista kompletu ba detallu bele hare'e iha #Anexu B, detallu ba Back-up Fotografia #Anexu C1, detallu ba Back-up BoQ #Anexu C2 no Instrusaun Servisu bele hare'e #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáculo Servisu Iha Terenu

1. Durante Equipa ADN, I.P. Covalima halo monitorizasaun no Inspekasaun hasoru obstaklo sira iha Terreno mak hanesan:

- Dokumentos sira dala ruma *owner* sumbmete barak liu iha fulan Dezembro, maske kompanhia submete ba *owner* iha fulan Setembro ou Outubro.
- Projeto balu parado liu husi fulan ida ona maibe *owner* la iha desizaun ruma ba kompanhia refere.
- Dalaruma ami nia actividade de Kontrolo Projetu la hanesan ho plano ne'ebe Trasa ona tamba iha fulan Dezembro tempo barak liu halo rekomendasaun pagamento iha Nasional tamba liga ho obstaklo iha numero primeiro.

2. Durante Equipa ADN, I.P. Covalima halo servisu Iha Eskritorio ADN, I.P. Municipio hasoru obstaklo sira mak hanesan:

- Ami nafatin hasoru difikuldade ba Printer, tamba printer ne'ebe iha at no la funsiona ona.
- Ate a data Ami seidauk bele asesu ba informasaun *Via Drop Box*, tamba *Memory Drop Box Full*.

➤ Obstacle parte Eletricidade

1. Iha Fulan Setembro nia laran ami labele ba halo inspeksaun ba Munisipiu, tamba transporte ne'ebe atu lori ami mak laiha.


IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

- Rekomenda ba Superior sira atu fo hela informasaun ba kada Lina Ministerial katak labele halo dokumentos kleur liu iha *owner* nia fatin.
- Rekomenda ba Superior sira atu informa hela ba superior sira husi projeto nain atu kontrola sira nia projeto ne'ebe durante ne parado hodi foti desizaun

- Karik ami nia realizasaun aktividade la hanesan ho Plano ne'ebe trasa ona husu ba Superior sira atu tetu no fo solusaun mai ami.
 - Husu ba Parte ITC atu Prepara Printer ida ba Municipio Covalima hodi nune bele Fasilita servisu iha Municipio
 - Husu mos ba Parte ITC atu aumenta *memory* ba *Drop Box* Hodi nune bale akumulada dados barak.
-
- Rekomendasaun parte Eletricidade
 1. Husu ba Parte superior atu bele hare ba kestaun hirak ne'e tamba susar mai ami atu desloka ba munisipiu hodi hare / inspeksaun ba projetu hirak ne'ebe presija ba halo monitorizasaun.

Note: Asinatura husi Eng Municipio Covalima

Força de Trabalho ADN,I.P Municipio Covalima/Suai						
No	Deskrisaun	Identidade				Asinatura
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	
1	Enjineiru	Madelino Deonizo José Magno	170	Enjineiru EPAS		
		Domingos Soares Martins	160	Enjineiru ITI		
		Prezenzio Legorio do Carmo Dias Ximenes	212	Enjineiru EPAS		
		Bosco Dinis de Sousa	215	Enjineiru ITI		
		Silvino D. R. R. Soares	177	Enjineiru METIC		

2	Enjineira	Tifania Clotaria G. Ornai	201	Enjineira VEBD		
3	Motorista	Agustinho Amaral	068	Motorista		



ANEXU A

MUNICIPIO COVALIMA (LISTA GERAL)

MUNICIPIO COVALIMA (LISTA GERAL)																
LOKALIZASAUN PROJETU																
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
1	The Undergrading of existing Suai Airport at Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Suai Villa	Covalima	Divita Unip. Lda	RDTL/MOP-SEE/CGI-PEN:000052	\$ 230,560.12	July 18, 2017	100.00%	90.00%	\$ 207,504.11	\$ 23,056.01	ON-GOING	Projeto ida ne iha Fase Retensaun
2	New Installation MV, LV Line and House Connection from Suai Vila to Suai Debos Office District, Tabaklot, Matai, Kiar Laran, Audian, Aldeia Halihun, MDGS, Matai, MDGS Halihun - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Suai Villa	Covalima	Eron Power, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000435	\$ 987,983.35	Sept. 1, 2016	24.00%	21.57%	\$ 213,139.22	\$ 774,844.13	ON-GOING	Projeto ida ne Parado Hela
3	Upgrading of Existing Suai Airport, Suai, Timor Leste	MINISTERIO TRANSPORTES E KOMUNIKASAUN	FI	AEROPORTOS	Suai Villa	Covalima	PT Waskita Karya (Persero) Tbk	ICB/035/TGAP-2013	\$ 67,687,412.46	April 24, 2014	100.00%	92.65%	\$ 62,709,401.97	\$ 4,978,010.49	PHO	Inspeksaun geral ba pagamentu retensaun, devolve dokumentus tamba sei iha defeitus nebe'e seidauk hadia husi contractor.
4	Construction Supervision for the Upgrading of Existing Suai Airport	MINISTERIO TRANSPORTES E KOMUNIKASAUN	FI	AEROPORTOS	Suai Villa	Covalima	Jurutera Perunding Zaaba Sdn, Bhd (Malaysia)	ICB/035/TGAP-2013	\$ 4,743,580.08	May 30, 2014	100.00%	95.67%	\$ 4,538,294.94	\$ 205,285.14	PHO	
5	New construction of drainage in Suai Loro 1 (Bebusa to Suai Loro)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Consortio Naroman Covalima, Group Lda	SSS/266/MOPTC-2016	\$ 1,223,216.12	July 10, 2016	62.09%	51.65%	\$ 631,782.25	\$ 591,433.87	ON-GOING	On Progress
6	Emergency new construction of bridge, gabions and normalization in Busakukun	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Consortio Zemo Lda	SSS/346/MOPTC-2016	\$ 970,974.30	Dec. 12, 2016	74.13%	74.13%	\$ 719,783.67	\$ 251,190.63	Abandona	Abandona servisu iha tinan 2017 to agora, la iha informaun klaru husi kompanhia konaba continuidade servisu iha tereno.
7	Rehabilitation of Road From Haemano Bridge to Zumalai Jct. Phase II 5+020 - 10+140 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Nobre Labadai Unipessoal, Lda	SSS/051/MOPTC-2017	\$ 3,802,446.29	Sept. 11, 2017	100.00%	88.95%	\$ 3,382,301.17	\$ 420,145.12	PHO	Fisiku 100%, PHO.
8	Rehabilitation Estrada urbanas Covalima I (0+00-7+750) CH-01 - CH-02	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Jonize Construction, Unip. Lda	SSS/123/MOPTC-2017	\$ 4,487,106.16	Aug. 25, 2017	100.00%	99.85%	\$ 4,480,350.63	\$ 6,755.53	FHO	FHO, Inspeksaun pagamentu 10%, balansu fila ba kofre estado
9	Rehabilitation Estrada urbanas Covalima II (0+00-7+575) CH-03 - CH-07	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Mejori, Lda	SSS/127/MOPTC-2017	\$ 3,301,268.19	Aug. 25, 2017	100.00%	99.35%	\$ 3,279,934.33	\$ 21,333.86	FHO	FHO, Inspeksaun pagamentu 10%, balansu fila ba kofre estado
10	Rehabilitation Estrada urbanas Covalima III (0+00-9+541)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Nananiu Unipessoal Lda	SSS/124/MOPTC-2017	\$ 4,255,553.24	Sept. 7, 2017	100.00%	99.58%	\$ 4,237,792.31	\$ 17,760.93	FHO	FHO, Inspeksaun pagamentu 10%, balansu fila ba kofre estado
11	Kontinuasaun Fase II Construsaun Reservatorio, Installasaun Kanu Transmissaun e Distribuissau iha Multy Aldeia Suku Debos - Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Suai Villa	Covalima	Kevina	MPWTC-NCB-170005	\$ 285,318.25	Nov. 30, 2017	19.26%	17.33%	\$ 49,447.74	\$ 235,870.51	PENDENTE	Projeto ida ne abandona hela, no pertense ona ba responsabilidade BTL.EP nian
12	Melhoramento Kanu Transmissaun no Distribuissau iha Asumaten Lokeu Munisipiu Covalima / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Suai Villa	Covalima	Maun Alin Suai Unip Lda	MOP-W-190168	\$ 226,245.45	Dec. 1, 2019	66.31%	39.84%	\$ 90,135.57	\$ 136,109.88	ON-GOING	Projeto ida ne agora pertense ona ba responsabilidade BTL.EP nian
13	Prefurasaun No Kanalizasaun Bee Mos Iha Aldeia Gala	MINISTERIO PLANU E ORDENAMENTU	LM-CD	AGUA E SANEAMENTO	Suai Villa	Covalima	Paya's Sisters	002.LM/RDTL/MPIE/A.D.N/Da Rfq/VI/2019/EDIFICIO DEPARTMENT	\$ 264,381.80	July 3, 2019	100.00%	100.00%	\$ 264,381.80	\$ -	FHO	Projeto ida nee halo ona pagamento retensaun balu, tuir CPV nebe parte finansas ADN,I.P Prepara, no balansu \$ 1,398.61 sei halo tan pagamento iha tinan 2022
14	Konstrusaun Kampo Multifunsaun Iha Lakonak-Covalima	MINISTERIO PLANU E ORDENAMENTU	LM-CD	JUVENTUDE NO DESPORTU	Suai Villa	Covalima	Damalelo	001./RDTL/LM/MPIE/A.D.N/DILI/IV/2019/EDIFICIO DEPARTMENT	\$ 136,718.09	May 15, 2019	100.00%	99.86%	\$ 136,532.71	\$ 185.38	FHO	Projeto ida ne halo pagamento retensaun ona. (FHO), no balansu \$ 185.38 Fila ba Kofre estado
15	Konstrusaun Edifisiu EBF Audian - Camenaca - Suai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Suai Villa	Covalima	Feto Lima Unip. Lda	07/A.M.Coalima/KDM-AMP/VII/2019	\$ 115,587.75	Oct. 14, 2019	95.72%	95.72%	\$ 110,639.86	\$ 4,947.89	FHO	Projeto ida ne rekomenda ona pagamento Retensaun no balansu osan fila fali ba Kofre Estado
16	New Construction Fencing, Stonee Masonry Wall and Chapel for Cemetery in Airport Area in Covalima Municipality	MINISTERIO DO PETROLEO E RECURSOS MINERAIS	LM-CD	AEROPORTOS	Suai Villa	Covalima	Joia Camenasa Unip. Lda	RFQ/049/MPRN-2019	\$ 95,176.06	Feb. 11, 2020	94.04%	94.04%	\$ 89,502.38	\$ 5,673.68	FHO	Projeto ida ne halo ona pagamento Retensaun (FHO) no Balansu Osan Fila ba Kofre Estado
17	New Construction of ICU ROOM in Covalima, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Suai Villa	Covalima	Giovania	RDTL-MS-DNA-NCB-20-150	\$ 189,960.54	Sept. 1, 2020	95.44%	85.89%	\$ 163,162.64	\$ 26,797.90	PHO	Projeto ida nee agora iha fase retensaun



ANEXU A

MUNICIPIO COVALIMA (LISTA GERAL)

MUNICIPIO COVALIMA (LISTA GERAL)																
					LOKALIZASAUN PROJETU											
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
18	New Construction of Isolamento for covid-19 Suai Referral Hospital, Covalima, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Suai Villa	Covalima	Roman Junior Unipessoal, Lda	RDTL-MS-DNA-NCB-20-166	\$ 262,452.00	Sept. 23, 2020	61.89%	55.51%	\$ 145,679.52	\$ 116,772.48	ON-GOING	Tuir Observasaun ikus ADN ,IP. Iha dia06-12-2021 Projeto refere parado hela
19	New Construction of Laboratory for Covid 19 at Suai Referral Hospital, Ministry of Health Timor-Leste	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Suai Villa	Covalima	Manu Bey Unip Lda	RDTL-MS-DNA-RBK-20-184	\$ 70,747.68	Jan. 11, 2021	91.69%	82.52%	\$ 58,383.19	\$ 12,364.49	PHO	Projeto ida nee agora iha fase retensaun
20	Rehabilitation of Road From Haemano Bridge - Zumalai Jct. Phase I 0+000 - 5+020 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	WTJ Contraction Unipessoal Lda	SSS/322/MOPTC-2016	\$ 3,445,877.60	Nov. 21, 2016	100.00%	84.95%	\$ 2,927,308.63	\$ 518,568.97	PHO	Fisiku 100%, PHO.
21	New Construsaun of Interior Fence for Prison in Suai Municipality	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	Suai Villa	Covalima	Fraternity Unipessoal Lda	MJ-062/OUTUBRO/2021	\$ 149,292.80	Sept. 19, 2021	22.54%	0.00%	\$ -	\$ 149,292.80	ON-GOING	Projeto ida ne agora lao hela
22	New Installation of MV, LV Line and House Connection from Suco Sadahur to Posto Administrativo Tilomar - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Tilomar	Covalima	Lalenok Fronteira, unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000366	\$ 323,539.34	July 6, 2016	97.00%	87.54%	\$ 283,223.74	\$ 40,315.60	ON-GOING	Projeto ida ne remata ona no la iha tan item seluk atu kontinua
23	River normalization and protection in Fatuk Oan	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Tilomar	Covalima	Consortio Lorico Covalima	SSS/263/MOPTC-2016	\$ 482,705.06	July 10, 2016	75.18%	75.18%	\$ 362,886.49	\$ 119,818.57	Abandona	Projecto refere abandona kleur ona husi companhia ate agora la iha aktividade servisu iha tereno.
24	Rehabilitasaun Merkadu Tradisional iha Fronteira Salele-Sua- Covalima	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Tilomar	Covalima	Ota Gelor	RDTL:73/GMTAC/XI/2 015	\$ 33,091.06	Aug. 8, 2014	80.00%	72.00%	\$ 23,825.57	\$ 9,265.49	ON-GOING	Projeto ida ne agora rehabilita fali ona ba fatin karantina
25	Construction of Health Post and Residence for Health Staff in Suku Beiseuk	MINISTERIO SAUDE	PDIM	SAUDE	Tilomar	Covalima	Joia Camenasa Unip. Lda	06/A.M.Covalima/KDM-AMP/IX/2019	\$ 186,843.31	Sept. 16, 2019	86.04%	77.43%	\$ 144,679.23	\$ 42,164.08	ON-GOING	Projeto ida ne remata ona, osan resto no osan Externa Works owner sei orineta atu halo tan servisu balu.
26	Lookeu Chainage 0+000 - 6+000, Casabau 008 Chainage 0+000 - 3+000, Casabau 012 Chainage 0+000 - 3+500, Casabau 018 Chainage 0+000 - 2+700, Naguidal - Lour Chainage 0+000 - 4+000, Boardikun - Mape Chainage 0+000 - 8+000, Data - Tolu Chainage 0+000 - 9+600 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Tilomar	Covalima	Futuro Mane Mesak Unip. Lda	RDTL	\$ 109,210.34	Aug. 13, 2019	72.42%	48.01%	\$ 52,437.14	\$ 56,773.20	ON-GOING	Projeto ne'e parado hela, husi fulan Abril 2021 to agora, Halo ona konfirmasaun ho companhia, resposta katak sira nia servisu remata ona iha fulan Marsu 2021, prosesu husu pagamentu maka seidaik realiza
27	Rehabilitation of Mini Mercado Mota Masin in Suai Covalima Ministry of Health, Timor Leste	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Tilomar	Covalima	Figelato Unip. Lda	RDTL-MS-DNA-NCB-20-217	\$ 129,595.17	Abr. 21, 2021	77.50%	69.75%	\$ 90,394.32	\$ 39,200.85	ON-GOING	Projeto ida ne lao hela
28	New Construction of Health Post and Doctor House Buiding in Beisuk, Tilomar, Covalima, Timor Leste (Niquir)	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Tilomar	Covalima	Caramé Unip Lda	RDTL-MS-DNA-ICB-21-071	\$ 295,785.42	Aug. 18, 2021	12.19%	10.82%	\$ 32,018.72	\$ -	ON-GOING	Projeto ida ne lao hela
29	R4D Rural Road Rehabilitation Data - Tolu Chainage 9+600 - 11+100 Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Fohorem	Covalima	Unidade Unip Lda	RT/027/MOP-2019	\$ 284,245.59	Dec. 20, 2019	100.00%	89.64%	\$ 254,811.22	\$ 29,434.37	PHO	Projecto ne'e PHO tia ona ba dono projecto
30	R4D Rural Road Rehabilitation Dato- Tolu Chainage 11+100 - 12+600 Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Fohorem	Covalima	Verde Caisahe Lda	NCB/057/MOP-2019	\$ 283,833.62	March 1, 2020	100.00%	90.00%	\$ 255,450.25	\$ 28,383.37	PHO	Progresu Fisiku 100%, PHO.
31	Installasaun Be'e mos iha Aldeia Aitos, Suco Datorua, Posto Administrativo Fohorem, Municipio Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Fohorem	Covalima	Abata	MPWTC-NCB-170004	\$ 284,263.85	Aug. 10, 2017	56.67%	49.47%	\$ 140,613.69	\$ 143,650.16	ON-GOING	Projeto ida ne agora kontinua fali servisu ona, no pertense ona responsabilidade BTL.EP nian
32	Construction, Rehabilitation and Installation of Clean Water with System Gravitation in Suco Fohorem Villa	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Fohorem	Covalima	Loro Metan Unipesola. Lda	SSS/293/MOPTC-2016	\$ 403,536.65	Nov. 22, 2016	45.05%	39.65%	\$ 159,993.44	\$ 243,543.21	PENDENTE	Projeto ida ne abandona hela



ANEXU A

MUNICIPIO COVALIMA (LISTA GERAL)

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	LOKALIZASAUN PROJETU		NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
					POSTO ADMINISTRATIVO	MUNISIPIU										
33	Construction of Baer Bridge	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Fohorem	Covalima	PT. Duta Graha	RDTL- 120002189	\$ 6,310,652.65	23-May-10	100.00%	99.06%	\$ 6,251,415.94	\$ 59,236.71	PENDENTE	Projeto refere atinge 100% iha tinan 7 liu ba kotuk, balansu nebe'e iha presija halo konfirmasaun ho dono projeto e nomos hare fila fali iha pagamentu anterior nian, hodi nune bele hatene los osamentu nebe'e sei iha balansu nia disposizaun
34	Construction Open New Road Belulic Leten to Belulic Craic for Patrolling the Border Sta. 0+000 - Sta. 9+160	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatumea	Covalima	Be'e horis, Unip. Lda	SSS/103/MOPTC-2017	\$ 3,407,674.66	Sept. 15, 2017	90.63%	78.79%	\$ 2,685,016.49	\$ 722,658.17	ON-GOING	On Progress,Projecto refere atinge ona 100% iha tereno, maibe seidauk iha aprovasaun variation order tamba ne'e bazeia hela ba kontrato original hodi aplika ba porsentu seidauk 100%
35	Construction of Health Post and Residence for Health Staff in Suku Nanu	MINISTERIO SAUDE	PDIM	SAUDE	Fatumea	Covalima	Unidade Unip Lda	05/A.M.Covalima/KDM-AMP/II/2019	\$ 228,246.62	Sept. 16, 2019	99.91%	89.92%	\$ 205,240.23	\$ 23,006.39	PHO	Projeto ida ne iha fase retensaun, no tempo retensaun remata ona seidauk bele prosesa pagamento tamba sei hein desizaun konaba rai halai
36	Rehabilitasaun Sistema Be mos Multy Aldeia Iha Dacolo Suco Nanu, Posto Administrativo Fatumea Municipio Covalima / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Fatumea	Covalima	Carisan Bonansa Unip Lda	MOP-W-190168	\$ 165,251.78	Dec. 1, 2019	51.00%	45.79%	\$ 75,663.22	\$ 89,588.56	ON-GOING	Projeto ida ne agora pertense ona ba responsabilidade BTL.EP nian
37	Road Maintenance Section Taroman - Datorua - Fatumeta (A016) 13.15 Km Section Covalima Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Fatululik	Covalima	Jufado	NCB-MOP-190014	\$ 300,403.42	Oct. 8, 2019	39.66%	35.69%	\$ 107,214.96	\$ 193,188.46	Parado	kondisaun aktual agora iha tereno parado hela tamba companhia la iha finaseiru nebe'e suficiente hodi apoiu aktividade servisu iha tereno
38	Construction of Taroman Bridge	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Fatululik	Covalima	Ensul Engenharia, S.A.	RDTL- 11005004	\$ 2,445,005.95	Nov. 10, 2011	100.00%	86.59%	\$ 2,117,121.82	\$ 327,884.13	PENDENTE	Projeto refere atinge 100% iha tinan 7 liu ba kotuk, balansu nebe'e iha presija halo konfirmasaun ho dono projeto e nomos hare fila fali iha pagamentu anterior nian, hodi nune bele hatene los osamentu nebe'e sei iha balansu nia disposizaun
39	Rehabilitation of Roads 5.400 Km (0+000-5+400) Aldeia Leogore to Aldeia iha Roads Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Maucatar	Covalima	Maun Alin Suai Unip Lda	SSS/135/MOPTC-2016	\$ 955,722.62	July 29, 2016	97.84%	78.02%	\$ 745,653.07	\$ 210,069.55	ON-GOING	Projecto lao hela iha tereno,maibe dezenho seidauk hetan aprovasaun husi dono projecto.
40	Rebidding of Project Road Maintenance Sections ; Suai, Maucatar - Lelaus Municipality Covalima (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Maucatar	Covalima	Verde Caisahe Lda	NCB-MOP-190010	\$ 242,501.42	Dec. 15, 2019	56.96%	51.26%	\$ 124,309.81	\$ 118,191.61	Parado	kondisaun aktual agora iha tereno parado hela tamba companhia la iha finaseiru nebe'e suficiente hodi apoiu aktividade servisu iha tereno
41	Konstrusaun Edifisiu Posto Administrativo Maucatar	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Maucatar	Covalima	Sabudoj Unip. Lda	RDTL/01/A.M.COVALI MA/X/2021	\$ 164,861.91	Aug. 25, 2021	0.00%	0.00%	\$ -	\$ 164,861.91	ON-GOING	Projeto ida si iha problema wituan konaba kondisaun rai
42	New Installation MV, LV Line and House Connection from Bulo to Zulo - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Zumalai	Covalima	Foho Rua Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000404	\$ 466,841.13	July 6, 2016	82.01%	73.80%	\$ 344,551.37	\$ 122,289.76	ON-GOING	Projeto ida ne remata ona no la iha tan item seluk atu kontinua
43	New Installation Mv, Lv Line & House Connection From Bulo to Lepo and Hohopu, Zumalai - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Zumalai	Covalima	Mania Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000427	\$ 721,805.08	Sept. 1, 2016	96.00%	86.24%	\$ 622,455.90	\$ 99,349.18	ON-GOING	Projeto ida ne remata ona no la iha tan item seluk atu kontinua
44	Upgrading of Cassa-Zumalai Roads Jct. Zumalai-Harekain Road (Km 00+000-Km 04+000), Municipality of Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Clardel Interprice Unip Lda	SSS/227/MOPTC-2016	\$ 3,026,312.56	Sept. 13, 2016	70.39%	60.64%	\$ 1,835,036.16	\$ 1,191,276.40	Parado	Obra ne'e sei iha balansu osamentu ba fisiku kontrusaun nian, maibe obra ne'e parado iha tinan 2019 to agora la iha informasaun rumu husi companhia konaba continuidade obra refere.
45	Rehabilitation of Road From Haemanu Bridge Zumalai Junction (0+000 - 20+316) Phase III Sta. 10+140 - 15+180 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Star Suai, Lda	SSS/050/MOPTC-2017	\$ 3,461,708.40	Sept. 7, 2017	96.79%	89.51%	\$ 3,098,636.12	\$ 363,072.28	ON-GOING	Fisiku 100%, seidauk PHO.



ANEXU A

MUNICIPIO COVALIMA (LISTA GERAL)

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	LOKALIZASAUN PROJETU		NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)			STATUS PROJECTO	OBSERVASAUN
					POSTO ADMINISTRATIVO	MUNISIPIU						PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)		
46	Reh. Of Road from Haemanu Bridge Jct Zumalai sta. 15+180-20+316	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Aitula Construction, Lda	SSS/081/MOPTC-2017	\$ 3,898,396.71	Sept. 7, 2017	100.00%	99.88%	\$ 3,893,706.39	\$ 4,690.32	FHO	Projectu ne'e termina FHO ba ona dono projectu, no hetan ona rekomendasaun pagamentu 10% retensaun nian, no balassu husi \$4,690.32 fila ba kofre estado
47	Rehabilitation of be'e mean roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Roman Junior Unipessoal, Lda	SSS/049/MOPTC-2017	\$ 3,645,870.73	Sept. 5, 2017	100.00%	92.75%	\$ 3,381,632.29	\$ 264,238.44	PHO	Hein prosesu pagamentu 100%,no halo PHO ba dono projecto
48	Emergency Bebora Zumalai Roads Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Zumalai	Covalima	Delta Nova Junior unip lda	162926	\$ 270,048.00	June 16, 2013	100.00%	71.41%	\$ 192,843.00	\$ 77,205.00	PENDENTE	Projectu remata ona iha tinan hitu ba kotuk, no halo ona rekomendasaun pagamentu fisiku tur item sira nebe'e instala ona iha tereno, Presija halo konfirmasaun ho dono projectu ba balansu nebe'e iha .tamba to agora la iha konstrusaun foun ida mak halo husi kompanhia iha tereno (ABANDONA)
49	Konstrusaun Igreja Paroquia Zumalai	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	Zumalai	Covalima	Aitula Construction, Lda	002/NC-ZC/VII/2015	\$ 1,196,660.00	Aug. 1, 2015	87.44%	78.70%	\$ 941,722.09	\$ 254,937.91	PENDENTE	Projeto ida remata ona no ate a data kompanhia seidaok submete pagamento final
50	Konstrusaun Eskola Tekniko Professional Zumalai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Zumalai	Covalima	Sabudoi Unip. Lda	03/A.M.Covalima/KDM-AMP/VII/2019	\$ 177,630.77	July 15, 2019	96.79%	87.11%	\$ 154,742.01	\$ 22,888.76	PHO	Projeto ida nee agora iha fase retensaun
51	Konstrusaun Edifisiu Postu Saude no Konstrusaun Residencia Mediki Lepo	MINISTERIO SAUDE	PDIM	SAUDE	Zumalai	Covalima	Titor Unip. Lda	08/A.M.Covalima/KDM-AMP/X/2019	\$ 190,500.47	Oct. 14, 2019	98.76%	98.76%	\$ 188,135.99	\$ 2,364.48	FHO	Projeto ida ne halo ona pagamento Retensaun (FHO) no Balansu Osan Fila ba Kofre Estado
52	Construction of Health Post and Residence for Health Staff in Suku Fatuleto - Zumalai	MINISTERIO SAUDE	PDIM	SAUDE	Zumalai	Covalima	Lifran Unip. Lda	04/A.M.Covalima/KDM-AMP/VII/2019	\$ 189,985.72	Aug. 5, 2019	98.38%	98.38%	\$ 186,901.47	\$ 3,084.25	FHO	Projeto ida ne halo ona pagamento Retensaun (FHO) no Balansu Osan Fila ba Kofre Estado
53	Melhoramento be mos Sistema Gravitasau iha Bulo Pelet suko Lour, Suko Fatu Leto, Suko Zulo Phase I Posto Administrativo Zumalai, Municipio Covalima / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Zumalai	Covalima	Delta Nova Junior unip lda	NCB-MOP-190057	\$ 724,741.23	Dec. 1, 2019	65.51%	58.96%	\$ 427,315.44	\$ 297,425.79	ON-GOING	Projeto ida ne agora pertense ona ba responsabilidade BTL.EP nian
54	New Construction of Wall Protection Tower No.31 Section Area Cassa - Suai Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	FLOOD CONTROL	Zumalai	Covalima	SKF Unipessoal Lda & Chacalala Joint Venture	NCB-MOP-1900075	\$ 508,540.07	Dec. 1, 2019	89.98%	54.77%	\$ 278,546.50	\$ 229,993.57	ON-GOING	Fisiku 100%, seidaok PHO. Pertensi ona ba EDTL.EP
55	Rural Roads Periodik Maintenance Lepo - Lour Chainage 0+000-3+000	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Futuro Mane Mesak Unip. Lda	MPW-W-190260	\$ 73,033.49	Dec. 19, 2019	84.51%	38.51%	\$ 28,127.77	\$ 44,905.72	ON-GOING	Obra ne'e remata ona 100%,iha fulan Junho 2021 hein submissaun pagamentu husi kompanhia ba dono projecto
56	Rehabilitation of Roads A12 Jct A12 Maliana - Jct A02 Zumalai Road Section 8 : Zulo - Jct Zumalai (30+100 - 35+120 km) Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Octogono Constr. Unip. Lda	SSS/067/MOPTC-2017	\$ 3,748,915.76	Sept. 7, 2017	41.69%	30.95%	\$ 1,160,430.04	\$ 2,588,485.72	ON-GOING	On Progress, Kontinua servisu Base-Course
57	Rehabilitation of Roads A12 Jct A12 Maliana - Jct A02 Zumalai (50+900 km), Road Section : Jct A16 Uele'o - Jct A02 Zumalai (35+120) Road Section 7 : Fatulito - Zulo (25+800 - 30+100) Municipality Bobonaro - Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Marino Enterprises, Lda	SSS/065/MOPTC-2017	\$ 4,314,282.59	Sept. 12, 2017	39.95%	27.46%	\$ 1,184,893.23	\$ 3,129,389.36	ON-GOING	On Progress, Kontinua servisu Base-Course
58	Manutensaun no Konstrusaun Kanais Irrigasaun iha Oebaba - Covalima	MINISTERIO AGRICULTURA E PISCAS	LM-CD	FLOOD CONTROL	Zumalai	Covalima	Lifran Unip. Lda	RDTL-2021-15595	\$ 260,523.18	Oct. 5, 2021	56.46%	35.26%	\$ 91,856.83	\$ 168,666.35	ON-GOING	On Progress



ANEXU A

MUNICIPIO COVALIMA (LISTA GERAL)

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	LOKALIZASAUN PROJETU		NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU (\$)	BALANSU (\$)	STATUS PROJECTO	OBSERVASAUN
					POSTO ADMINISTRATIVO	MUNISIPIU										
59	Design and Construction Supervision Services Emergency Package Project for the year 2013 Municipalities of Covalima, Ainaro and Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Multy Posto	Covalima	Maun Alin Suai Unip Lda	SSS/029/MOPTC-2017	\$ 379,631.20	July 7, 2017	100.00%	84.10%	\$ 319,270.12	\$ 60,361.08	ON-GOING	
60	Rehabilitation of Mota Masin to Haemanu Roads Sta. 17+500-23+800	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Multy Posto	Covalima	Expres Distribution Services Unip. Lda	SSS/318/MOPTC-2016	\$ 4,941,274.57	Dec. 9, 2016	100.00%	84.68%	\$ 4,184,042.48	\$ 757,232.09	ON-GOING	Obra ne'e remata ona 100%, iha tinan 2019 hein submisaun pagamentu husi kompanhia ba dono projecto, nomos iha problema adisional nebe'e seidauk iha aprovasaun husi dono do projetu.
61	Manutensaun Estrada Lookeu. Sta. 0+000-6+000, Manutensaun Estrada Lepo-Lour. Sta. 0+000-3+000, Manutensaun Estrada Naquidal-Lour. Sta. 0+000-4+200-Municipal of Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Multy Posto	Covalima	Manu Bey Unip Lda	RT/079/MOPTC-2016	\$ 150,247.52	Aug. 19, 2016	51.08%	45.97%	\$ 69,074.95	\$ 81,172.57	Abandona	Projecto refere abandona / parado iha tinan 2019 ate agora tamba problema menus financeiro, Agora dadaun iha ona projetu foun halo manutensaun ba lokasaun refere husi ILO-R4D nebeé implementa hela husi kompania Futuru Manemesak
62	Rural Roads Routine Maintenance Lepo-Lour Sta 0+000-3+000, Naguidal - Lour Sta 0+000-5+000, Boardikun - Mape Sta 0+000-8+000 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Multy Posto	Covalima	Futuro Mane Mesak Unip Lda	MPWTC-CD-170015	\$ 34,106.69	Jan. 8, 2017	88.48%	88.48%	\$ 30,176.89	\$ 3,929.80	PENDENTE	Agora dadaun iha ona projetu foun halo manutensaun ba lokasaun refere husi ILO-R4D nebeé implementa hela husi kompania Futuru Manemesak, ho kontratu foun
63	Rural Roads Routine Maintenance Dato Tolu Cha 0+000 - 9+600, Lookeu Cha 0+000 - 6+000, Casabauc 008 Cha 0+000 - 3+000, Casabauc 012 Cha 0+000 - 3+500, Casabauc 018 Cha 0+000 - 2+700, Lalawa Cha 0+000 - 3+500, Boraikun Mape Cha 0+000 - 8+000, Naguidal Lepo Cha 0+000 - 4+000 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multy Posto	Covalima	Lufi Raica Unip Lda	MPW/WNCB/R/190048	\$ 109,210.34	Aug. 13, 2019	0.00%	0.00%	\$ -	\$ 109,210.34	Seidauk Implementa	Projetu ne'e seidauk implementa iha tereno, no iha ona projetu foun husi R4D implementa ona area fefere husi kompanhia Futuru-Manemesak.
TOTAL									\$ 146,459,094.98			85.46%	\$ 125,161,525.03	\$ 21,033,803.25		

Prepara Husi :

(Eng. Madelino D J Magno)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Covalima ADN, I.P.

(Eng. Prezenzio L C D Ximenes)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Covalima ADN, I.P.

(Eng. Domingos Soares Martins)
Eng. ba Projetu Infraestrutura, Transportes e Irigasaun, Municipio Covalima ADN, I.P.

(Eng. Bosco Dinis de Sousa)
Eng. ba Projetu Infraestrutura, Transportes e Irigasaun, Municipio Covalima ADN, I.P.

(Silvino D R R Soares)
Eng. M & E, Municipio Covalima ADN, I.P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validação de Qualidade, ADN, I.P.



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU COVALIMA

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Cumulative Progress (%)
1	The Undergrading of existing Suai Airport at Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Suai Villa	Covalima	Divita Unip. Lda	RDTL/MOP-SEE/CGI-PEN:000052	\$ 230,560.12	July 18, 2017	100.00%	0.00%	100.00%
2	New Installation MV, LV Line and House Connection from Suai Vila to Suai Debos Office District, Tabaklot, Matai, Kiar Laran, Audian, Aldeia Halihun, MDGS, Matai, MDGS Halihun - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Suai Villa	Covalima	Eron Power, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000435	\$ 987,983.35	Sept. 1, 2016	24.00%	0.00%	24.00%
3	Upgrading of Existing Suai Airport, Suai, Timor Leste	MINISTERIO TRANSPORTES E KOMUNIKASAUN	FI	AEROPORTOS	Suai Villa	Covalima	PT Waskita Karya (Persero) Tbk	ICB/035/TGAP-2013	\$ 67,687,412.46	April 24, 2014	100.00%	0.00%	100.00%
4	Construction Supervision for the Upgrading of Existing Suai Airport	MINISTERIO TRANSPORTES E KOMUNIKASAUN	FI	AEROPORTOS	Suai Villa	Covalima	Jurutera Perunding Zaaba Sdn. Bhd (Malaysia)	ICB/035/TGAP-2013	\$ 4,743,580.08	May 30, 2014	100.00%	0.00%	100.00%
5	New construction of drainage in Suai Loro 1 (Bebusa to Suai Loro)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Consortio Naroman Covalima, Group Lda	SSS/266/MOPTC-2016	\$ 1,223,216.12	July 10, 2016	62.09%	0.00%	62.09%
6	Emergency new construction of bridge, gabions and normalization in Busakukun	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Consortio Zemo Lda	SSS/346/MOPTC-2016	\$ 970,974.30	Dec. 12, 2016	74.13%	0.00%	74.13%
7	Rehabilitation of Road From Haemano Bridge to Zumalai Jct. Phase II 5+020 - 10+140 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Nobre Labadai Unipessoal, Lda	SSS/051/MOPTC-2017	\$ 3,802,446.29	Sept. 11, 2017	100.00%	0.00%	100.00%
8	Rehabilitation Estrada urbanas Covalima I (0+00-7+750) CH-01 -CH-02	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Jonize Construction, Unip. Lda	SSS/123/MOPTC-2017	\$ 4,487,106.16	Aug. 25, 2017	100.00%	0.00%	100.00%
9	Rehabilitation Estrada urbanas Covalima II (0+00-7+575) CH-03 -CH-07	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Mejori, Lda	SSS/127/MOPTC-2017	\$ 3,301,268.19	Aug. 25, 2017	100.00%	0.00%	100.00%
10	Rehabilitation Estrada urbanas Covalima III (0+00-9+541)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	Nananiu Unipessoal Lda	SSS/124/MOPTC-2017	\$ 4,255,553.24	Sept. 7, 2017	100.00%	0.00%	100.00%
11	Kontinuasaun Fase II Construsaun Reservatorio, Installasaun Kanu Transmisaun e Distribuisaun iha Multy Aldeia Suku Debos - Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Suai Villa	Covalima	Kevina	MPWTC-NCB-170005	\$ 285,318.25	Nov. 30, 2017	19.26%	0.00%	19.26%
12	Melhoramento Kanu Transmisaun no Distribuisaun iha Asumaten Lokeu Munisipiu Covalima / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Suai Villa	Covalima	Maun Alin Suai Unip Lda	MOP-W-190168	\$ 226,245.45	Dec. 1, 2019	66.31%	0.00%	66.31%
13	Prefurasaun No Kanalizasaun Bee Mos Iha Aldeia Gala	MINISTERIO PLANU E ORDENAMENTU	LM-CD	AGUA E SANEAMENTO	Suai Villa	Covalima	Paya's Sisters	002.LM/RDTL/MPIE/A.D .N/Da Rfq/VI/2019/EDIFICIO DEPARTMENT	\$ 264,381.80	July 3, 2019	100.00%	0.00%	100.00%
14	Konstrusaun Kampo Multifunsaun Iha Lakonak-Covalima	MINISTERIO PLANU E ORDENAMENTU	LM-CD	JUVENTUDE NO DESPORTU	Suai Villa	Covalima	Damalelo	001./RDTL/LM/MPIE/A. D.N/DILI/IV/2019/EDIFI CIO DEPARTMENT	\$ 136,718.09	May 15, 2019	100.00%	0.00%	100.00%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU COVALIMA

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Cumulative Progress (%)
15	Konstrusaun Edifisiu EBF Audian - Camenaca - Suai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Suai Villa	Covalima	Feto Lima Unip. Lda	07/A.M.Covalima/KDM-AMP/VII/2019	\$ 115,587.75	Oct. 14, 2019	95.72%	0.00%	95.72%
16	New Construction Fencing, Stonee Massonry Wall and Chapel for Cemetery in Airport Area in Covalima Municipality	MINISTERIO DO PETROLEO E RECURSOS MINERAIS	LM-CD	AEROPORTOS	Suai Villa	Covalima	Joia Camenasa Unip. Lda	RFQ/049/MPRN-2019	\$ 95,176.06	Feb. 11, 2020	94.04%	0.00%	94.04%
17	New Construction of ICU ROOM in Covalima, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Suai Villa	Covalima	Giovanio	RD TL-MS-DNA-NCB-20-150	\$ 189,960.54	Sept. 1, 2020	92.68%	2.76%	95.44%
18	New Construction of Isolamento for covid-19 Suai Referral Hospital, Covalima, Timor Leste	MINISTERIO SAUDE	Fundo Covid-19	SAUDE	Suai Villa	Covalima	Roman Junior Unipessoal, Lda	RD TL-MS-DNA-NCB-20-166	\$ 262,452.00	Sept. 23, 2020	61.89%	0.00%	61.89%
19	New Construction of Laboratory for Covid 19 at Suai Referral Hospital, Ministry of Health Timor-Leste	MINISTERIO SAUDE	Fundo Covid-19	EDIFICIOS PUBLICOS	Suai Villa	Covalima	Manu Bey Unip Lda	RD TL-MS-DNA-RBK-20-184	\$ 70,747.68	Jan. 11, 2021	84.60%	7.09%	91.69%
20	Rehabilitation of Road From Haemano Bridge - Zumalai Jct. Phase I 0+000 - 5+020 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Suai Villa	Covalima	WTJ Contraction Unipessoal Lda	SSS/322/MOPTC-2016	\$ 3,445,877.60	Nov. 21, 2016	100.00%	0.00%	100.00%
21	New Construsaun of Interior Fence for Prison in Suai Municipality	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	Suai Villa	Covalima	Fraternity Unipessoal Lda	MJ-062/OUTUBRO/2021	\$ 149,292.80	Sept. 19, 2021	22.54%	0.00%	22.54%
22	New Installation of MV, LV Line and House Connection from Suco Sadahur to Posto Administrativo Tilomar - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Tilomar	Covalima	Lalenok Fronteira, unip.lda	RD TL/MOPTC-VMOPTC/CGI-PEN : 00000366	\$ 323,539.34	July 6, 2016	97.00%	0.00%	97.00%
23	River normalization and protection in Fatuk Oan	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Tilomar	Covalima	Consorcio Lorico Covalima	SSS/263/MOPTC-2016	\$ 482,705.06	July 10, 2016	75.18%	0.00%	75.18%
24	Rehabilitasaun Merkadu Tradisional iha Fronteira Salele- Sua- Covalima	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Tilomar	Covalima	Ota Gelor	RD TL:73/GMTAC/XI/2015	\$ 33,091.06	Aug. 8, 2014	80.00%	0.00%	80.00%
25	Construction of Health Post and Residence for Health Staff in Suku Beiseuk	MINISTERIO SAUDE	PDIM	SAUDE	Tilomar	Covalima	Joia Camenasa Unip. Lda	06/A.M.Covalima/KDM-AMP/IX/2019	\$ 186,843.31	Sept. 16, 2019	84.02%	2.02%	86.04%
26	Lookeu Chainage 0+000 - 6+000, Casabau 008 Chainage 0+000 - 3+000, Casabau 012 Chainage 0+000 - 3+500, Casabau 018 Chainage 0+000 - 2+700, Naguidal - Lour Chainage 0+000 - 4+000, Boardikun - Mape Chainage 0+000 - 8+000, Data - Tolu Chainage 0+000 - 9+600 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Tilomar	Covalima	Futuro Mane Mesak Unip. Lda	RD TL	\$ 109,210.34	Aug. 13, 2019	72.42%	0.00%	72.42%
27	Rehabilitation of Mini Mercado Mota Masin in Suai Covalima Ministry of Health, Timor Leste	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Tilomar	Covalima	Figelato Unip. Lda	RD TL-MS-DNA-NCB-20-217	\$ 129,595.17	Abr. 21, 2021	73.17%	4.33%	77.50%
28	New Construction of Health Post and Doctor House Buiding in Beisuk, Tilomar, Covalima, Timor Leste (Niquir)	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Tilomar	Covalima	Caramé Unip Lda	RD TL-MS-DNA-ICB-21-071	\$ 295,785.42	Aug. 18, 2021	4.91%	7.28%	12.19%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU COVALIMA

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Cumulative Progress (%)
29	R4D Rural Road Rehabilitation Data - Tolu Chainage 9+600 - 11+100 Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Fohorem	Covalima	Unidade Unip Lda	RT/027/MOP-2019	\$ 284,245.59	Dec. 20, 2019	100.00%	0.00%	100.00%
30	R4D Rural Road Rehabilitation Dato- Tolu Chainage 11+100 - 12+600 Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Fohorem	Covalima	Verde Caisahe Lda	NCB/057/MOP-2019	\$ 283,833.62	March 1, 2020	100.00%	0.00%	100.00%
31	Installasaun Be'e mos iha Aldeia Aitos, Suco Datorua, Posto Administrativo Fohorem, Municipio Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Fohorem	Covalima	Abata	MPWTC-NCB-170004	\$ 284,263.85	Aug. 10, 2017	56.67%	0.00%	56.67%
32	Construction, Rehabilitation and Installation of Clean Water with System Gravitation in Suco Fohorem Villa	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Fohorem	Covalima	Loro Metan Unipesola. Lda	SSS/293/MOPTC-2016	\$ 403,536.65	Nov. 22, 2016	45.05%	0.00%	45.05%
33	Construction of Baer Bridge	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Fohorem	Covalima	PT. Duta Graha	RDTL- 120002189	\$ 6,310,652.65	23-May-10	100.00%	0.00%	100.00%
34	Construction Open New Road Belulic Leten to Belulic Craic for Patrolling the Border Sta. 0+000 - Sta. 9+160	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Fatumea	Covalima	Be'e horis, Unip. Lda	SSS/103/MOPTC-2017	\$ 3,407,674.66	Sept. 15, 2017	90.63%	0.00%	90.63%
35	Construction of Health Post and Residence for Health Staff in Suku Nanu	MINISTERIO SAUDE	PDIM	SAUDE	Fatumea	Covalima	Unidade Unip Lda	05/A.M.Covalima/KDM-AMP/VII/2019	\$ 228,246.62	Sept. 16, 2019	99.91%	0.00%	99.91%
36	Rehabilitasaun Sistema Be mos Multy Aldeia Iha Dacolo Suco Nanu, Posto Administrativo Fatumea Municipio Covalima / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Fatumea	Covalima	Carisan Bonansa Unip Lda	MOP-W-190168	\$ 165,251.78	Dec. 1, 2019	51.00%	0.00%	51.00%
37	Road Maintenance Section Taroman - Datorua - Fatumeta (A016) 13.15 Km Section Covalima Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Fatululik	Covalima	Jufado	NCB-MOP-190014	\$ 300,403.42	Oct. 8, 2019	39.66%	0.00%	39.66%
38	Construction of Taroman Bridge	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Fatululik	Covalima	Ensul Engenharia, S.A.	RDTL- 11005004	\$ 2,445,005.95	Nov. 10, 2011	100.00%	0.00%	100.00%
39	Rehabilitation of Roads 5.400 Km (0+000-5+400) Aldeia Leogore to Aldeia iha Roads Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Maucatar	Covalima	Maun Alin Suai Unip Lda	SSS/135/MOPTC-2016	\$ 955,722.62	July 29, 2016	97.84%	0.00%	97.84%
40	Rebidding of Project Road Maintenance Sections ; Suai, Maucatar - Lelaus Municipality Covalima (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Maucatar	Covalima	Verde Caisahe Lda	NCB-MOP-190010	\$ 242,501.42	Dec. 15, 2019	56.96%	0.00%	56.96%
41	Konstrusaun Edifisiu Posto Administrativo Maucatar	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Maucatar	Covalima	Sabudoir Unip. Lda	RDTL/01/A.M.COVALIM A/X/2021	\$ 164,861.91	Aug. 25, 2021	0.00%	0.00%	0.00%
42	New Installation MV, LV Line and House Connection from Bulo to Zulo - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Zumalai	Covalima	Foho Rua Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000404	\$ 466,841.13	July 6, 2016	54.00%	28.05%	82.01%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU COVALIMA

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Cumulative Progress (%)
43	New Installation Mv, Lv Line & House Connection From Bulo to Lepo and Hohopu, Zumalai - Covalima Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Zumalai	Covalima	Mania Unip, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000427	\$ 721,805.08	Sept. 1, 2016	96.00%	0.00%	96.00%
44	Rehabilitation of Roads A12 Jct A12 Maliana - Jct A02 Zumalai Road Section 8 : Zulo - Jct Zumalai (30+100 - 35+120 km) Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Octogono Constr. Unip. Lda	SSS/067/MOPTC-2017	\$ 3,748,915.76	Sept. 7, 2017	41.69%	0.00%	41.69%
45	Rehabilitation of Roads A12 Jct A12 Maliana - Jct A02 Zumalai (50+900 km), Road Section : Jct A16 Uele'o - Jct A02 Zumalai (35+120) Road Section 7 : Fatulito - Zulo (25+800 - 30+100) Municipality Bobonaro - Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Marino Enterprises, Lda	SSS/065/MOPTC-2017	\$ 4,314,282.59	Sept. 12, 2017	39.95%	0.00%	39.95%
46	Upgrading of Cassa-Zumalai Roads Jct. Zumalai-Harekain Road (Km 00+000-Km 04+000), Municipality of Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Clardel Interprice Unip Lda	SSS/227/MOPTC-2016	\$ 3,026,312.56	Sept. 13, 2016	70.39%	0.00%	70.39%
47	Rehabilitation of Road From Haemanu Bridge Zumalai Junction (0+000 - 20+316) Phase III Sta. 10+140 - 15+180 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Star Suai, Lda	SSS/050/MOPTC-2017	\$ 3,461,708.40	Sept. 7, 2017	96.79%	0.00%	96.79%
48	Reh. Of Road from Haemanu Bridge Jct Zumalai sta. 15+180-20+316	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Zumalai	Covalima	Aitula Construction, Lda	SSS/081/MOPTC-2017	\$ 3,898,396.71	Sept. 7, 2017	100.00%	0.00%	100.00%
49	Rehabilitation of be'e mean roads	MINISTERIO DAS OBRAS PUBLICAS	LM-TP	ESTRADAS	Zumalai	Covalima	Roman Junior Unipessoal, Lda	SSS/049/MOPTC-2017	\$ 3,645,870.73	Sept. 5, 2017	100.00%	0.00%	100.00%
50	Emergency Bebora Zumalai Roads Covalima	MINISTERIO DAS OBRAS PUBLICAS	PDIM	ESTRADAS	Zumalai	Covalima	Delta Nova Junior unip lda	162926	\$ 270,048.00	June 16, 2013	100.00%	0.00%	100.00%
51	Konstrusaun Igreja Paroquia Zumalai	GABINETE DO PRIMEIRO MINISTRO	PDIM	EDIFICIOS PUBLICOS	Zumalai	Covalima	Aitula Construction, Lda	002/NC-ZC/VII/2015	\$ 1,196,660.00	Aug. 1, 2015	87.44%	0.00%	87.44%
52	Konstrusaun Eskola Tekniko Professional Zumalai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Zumalai	Covalima	Sabudo Unip. Lda	03/A.M.Coalima/KDM-AMP/VII/2019	\$ 177,630.77	July 15, 2019	96.79%	0.00%	96.79%
53	Konstusaun Edifisiu Postu Saude no Konstrusaun Residencia Mediku Lepo	MINISTERIO SAUDE	LM-BS	SAUDE	Zumalai	Covalima	Titor Unip. Lda	08/A.M.Coalima/KDM-AMP/X/2019	\$ 190,500.47	Oct. 14, 2019	98.76%	0.00%	98.76%
54	Construction of Health Post and Residence for Health Staff in Suku Fatuleto - Zumalai	MINISTERIO SAUDE	LM-CD	SAUDE	Zumalai	Covalima	Lifran Unip. Lda	04/A.M.Coalima/KDM-AMP/VII/2019	\$ 189,985.72	Aug. 5, 2019	98.38%	0.00%	98.38%
55	Melhoramento be mos Sistema Gravitasau iha Bulo Pelet suko Lour, Suko Fatu Leto, Suko Zulo Phase I Posto Administrativo Zumalai, Municipio Covalima / 162	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	Zumalai	Covalima	Delta Nova Junior unip lda	NCB-MOP-190057	\$ 724,741.23	Dec. 1, 2019	65.51%	0.00%	65.51%
56	New Construction of Wall Protection Tower No.31 Section Area Cassa - Suai Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	FLOOD CONTROL	Zumalai	Covalima	SKF Unipessoal Lda & Chacalala Joint Venture	NCB-MOP-1900075	\$ 508,540.07	Dec. 1, 2019	89.98%	0.00%	89.98%



ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU COVALIMA

LOKALIZASAUN PROJETU											Dec-21		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU (\$)	DATA KONTRATU	Previous Progress (%)	This Month Progress (%)	Comulative Progress (%)
57	Rural Roads Periodik Maintenance Lepo - Lour Chainage 0+000-3+000	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Zumalai	Covalima	Futuro Mane Mesak Unip. Lda	MPW-W-190260	\$ 73,033.49	Dec. 19, 2019	84.51%	0.00%	84.51%
58	Manutensaun no Konstrusaun Kanais Irrigasaun iha Oebaba - Covalima	MINISTERIO AGRICULTURA E PESCAS	LM-CD	FLOOD CONTROL	Zumalai	Covalima	Lifran Unip. Lda	RDTL-2021-15595	\$ 260,523.18	Oct. 5, 2021	20.39%	36.07%	56.46%
59	Design and Construction Supervision Services Emergency Package Project for the year 2013 Municipalities of Covalima, Ainaro and Manufahi	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Multy Posto	Covalima	Maun Alin Suai Unip Lda	SSS/029/MOPTC-2017	\$ 379,631.20	July 7, 2017	100.00%	0.00%	100.00%
60	Rehabilitation of Mota Masin to Haemanu Roads Sta. 17+500-23+800	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Multy Posto	Covalima	Expres Distribution Services Unip. Lda	SSS/318/MOPTC-2016	\$ 4,941,274.57	Dec. 9, 2016	100.00%	0.00%	100.00%
61	Manutensaun Estrada Lookeu. Sta. 0+000-6+000, Manutensaun Estrada Lepo-Lour. Sta. 0+000-3+000, Manutensaun Estrada Naquidal-Lour. Sta. 0+000-4+200-Municipal of Covalima	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Multy Posto	Covalima	Manu Bey Unip Lda	RT/079/MOPTC-2016	\$ 150,247.52	Aug. 19, 2016	51.08%	0.00%	51.08%
62	Rural Roads Routine Maintenance Lepo-Lour Sta 0+000-3+000, Naguidal - Lour Sta 0+000-5+000, Boardikun - Mape Sta 0+000-8+000 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Multy Posto	Covalima	Futuro Mane Mesak Unip Lda	MPWTC-CD-170015	\$ 34,106.69	Jan. 8, 2017	88.48%	0.00%	88.48%
63	Rural Roads Routine Maintenance Dato Tolu Cha 0+000 - 9+600, Lookeu Cha 0+000 - 6+000, Casabauc 008 Cha 0+000 - 3+000, Casabauc 012 Cha 0+000 - 3+500, Casabauc 018 Cha 0+000 - 2+700, Lalawa Cha 0+000 - 3+500, Boraikun Mape Cha 0+000 - 8+000, Naguidal Lepo Cha 0+000 - 4+000 Municipality Covalima	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multy Posto	Covalima	Lufi Raica Unip Lda	MPW/WNCB/R/190048	\$ 109,210.34	Aug. 13, 2019	0.00%	0.00%	0.00%

Prepara Husi :

(Eng. Madelino D J Magno)

Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Covalima
ADN, I.P.

(Eng. Prezenzio L C D Ximenes)

Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Covalima
ADN, I.P.

(Silvino D R R Soares)

Eng. M & E, Municipio Covalima ADN, I.P.

(Eng. Domingos Soares Martins)

Eng. ba Projetu Infraestrutura, Transportes e Irigasaun, Municipio Covalima
ADN, I.P.

(Eng. Bosco Dinis de Sousa)

Eng. ba Projetu Infraestrutura, Transportes e Irigasaun, Municipio
Covalima
ADN, I.P.

Verifika Husi :

(Arc. Francisco X D D Jeronimo)

Eng. Senior ba Edificio Publiku no Beé Saneamentu,
ADN, I.P.

(Eng. Aniceto da Costa)

Eng. Senior ba Projetu Infraestrutura, Transportes e
Irigasaun,
ADN, I.P.

(Deolindo de F Marques)

Chefe Sek. Projetu M.E & ITC, ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade,
ADN, I.P.



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SV-2)

Back-up Data

Naran Projeto : New Installation MV, LV Line and House Connection from Suai Vila to Suai Debos Office District, Tabaklot, Matai, Kiar Laran, Audian, Aldeia Halihun, MDGS, Matai, MDGS Halihun - Covalima Municipality

No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000435

Data Inspesaun : 2/12/2021

Fatin Inspesaun : Suai Vila

Koordinadas :

Start Point : Long : -9,88.59.27 Latetude: 125,16.54.04

End Point : Long : -9,58.57.96, Latetude: 125,15.26.25

Naran Inspector : 1. Silvino D. R. Rebelo Soares

Sketch & Foto Desenho

Sketch Item servisu

Laiha Aktividade Iha Tereno

Observasaun iha tereno no Foto Aktual





MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SV-2)

Back-up Data

Naran Projeto : New Installation MV, LV Line and House Connection from Suai Vila to Suai Debos Office District, Tabaklot, Matai, Kiar Laran, Audian, Aldeia Halihun, MDGS, Matai, MDGS Halihun - Covalima Municipality

No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000435

Sketch & Foto Desenho

Sketch Item servisu


Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho

Sketch Item servisu

Observasaun iha tereno no Foto Aktual

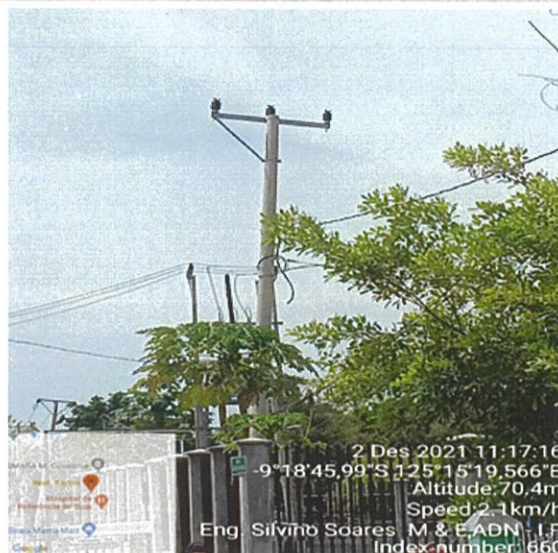



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C1 (SV-2)

Back-up Data

Naran Projeto : New Installation MV, LV Line and House Connection from Suai Vila to Suai Debos Office District, Tabaklot, Matai, Kiar Laran, Audian, Aldeia Halihun, MDGS, Matai, MDGS Halihun - Covalima Municipality

No. kontratu : RDTL/MOPTC-VMOPTC/CGI-PEN : 00000435

Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

Sketch Item servisu

