REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público

A.D.N. I.P.
Agência de Desenvolvimento Nacional, Instituto Público

RELATÓRIU MENSÁL IMPLEMENTASAUN PROJETUS MUNISÍPIU LIQUICA

ABRIL 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTASAUN PROJETO INFRAESTRUTURA IHA MUNICIPIO LIQUICA ABRIL 2022

Prepara Husi :

(Eng. Juninho Antonio A. Da Cruz)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Liquica ADN, I.P

(Eng. Marcus Ximenes de Araujo)
Eng. ba Projeto Infraestrutura,Transporte e Irigasaun, Municipio Liquica ADN, I.P

(Eng. Camilio de Jesus)
Eng. ba Projeto ME Municipio Liquica ADN, I.P

Verifika Husi :

(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edificio Publiku no Beé Saneamentu, ADN, I.P

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba Projeto Infraestrutura e Irigasaun, ADN, I.P

(Deolindo de Fatima Marques)
Chefe Seksaun ba Projeto M. E & ITC, ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :

(Mariano Renato Monteiro da Cruz, S. T, M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO..... 1

I. INTRODUSAUN. 3

1.1 Enkuadramentu Legal..... 3

1.2 Perfil Municipio Liquica 3

1.3 Lista Projecto..... 7

II. PROGRESU FISIKU 18

2.1 Progresso Fisiku Kada Fulan..... 18

III OBSTÁKLU IHA TERENU..... 18

3.1 Obstáclo Servisu Iha Terenu 18

VI. REKOMENDASAUN IHA TERENU 19

4.1 Rekomendasaun Servisu iha Terenu..... 19

INDICE TABELA

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica 5

Tabela 1. 2: Lista Asset ADN,I.P Municipio Liquica..... 5

Tabela 1.3. 1 Projecto Municipio Liquica Por Fundus Financimento 7

Tabela 1.3. 2 Projecto Muncipio Liquica Por Sectores 9

Tabela 1.3. 3 Projecto Municipio Liquica Por Ministerios 14

Tabela 4. 1 : Dadus populasaun Munisipiu Liquica 18

I. INTRODUSAUN.

1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análize kustu-benefísiu ne'ebe razoável no viavél.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimentu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba Projeto sira iha programa Kapital Desenvolvimentu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Liquica





Mapa hatudu pozisaun Administrasaun Munisipal Liquica iha luan area 543 km² ho populasaun nain – 63.403 tuir Sensus 2010. Administrasaun Munisipal Liquica iha Postu Administrativu tolu (3) , Sukus 23 no aldeias 134, mak hanesan hatudu iha Tabela 1

Tabela 1: Postos Administrativos, Sucos no Aldeias.

Bazartete		Liquica		Maubara	
sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**
Fahilelo	3	Açumano	4	Gugleur	11
Fatumasi	4	Darulete	4	Guiço	5
Lauhata	5	Dato	10	Lissadila	7
Leorema	10	Hatuquesi	8	Maubaralissa	5
Maumeta	4	Leotala	5	Vatuboro	5
Metagou	3	Loidahar	4	Vatuvou	10
Motaulun	3	Luculai	4	Vaviquinia	7
Tibar	4	-	-	-	-
Ulmera	9	-	-	-	-
Total	**45**	-	**39**	-	**50**

Data husi: Livro 3 B OJE 2021, pag 58

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica

Forca de Trabalho ADN,I.P Municipio Liquica								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro		2				2	
2	Administrasaun no Financas		0				0	
3	Motorista		1				1	
4	Seguransa		0				0	
Total			**3**				**3**	

Tabela 1. 2 : Lista Asset ADN,I.P Municipio Liquica

ASSET ADN,IP MUNICIPIO LIQUICA								
No	**Deskrisaun**	**Total Aset Kada Tinan**					**Total**	**OBS**
		2021	**2022**	**2023**	**2024**	**2025**		
1	Edificio		1					
2	Kareta		1					
3	Desktop HP / Monitor		1					
4	Laptop HP		1					
5	Printer Cannon		1					
6	UPS		1					
7	Armario File		1					
8	Armario Tau hena		3					
9	Meja escritorio		1					
10	Meja han		1					
11	Meja TV (kiik)		1					
12	Kadeira escritorio		6					
13	Kadeira han		4					

14	Sofa		1 Set					
15	Springbed +sumasu 4+sprei 3		3 Set					
16	Jeleira		1					
17	Water Dispenser		1					Aát
18	TV + Parabola		1 Set					
19	AC		4					
20	Kipas Angin		1					
21	Kompor		1					
22	Kompor Gas		1					
23	Rack sepatu		3					
24	Rack Piring		1					
25	Lampu		11					
26	Water Pump Sanyo		0					

1.3 Lista Projecto

Projeto hotu ne'ebe akumula iha lista neé bazeia ba dadus Projeto nebe sei lao hela no mos Projeto nebe abandona ona iha tinan barak nia laran, Projeto hirak ne'e fahe tuir lista tabela 1.3.1 Projeto Por Fundus Finansiamento, Tabela 1.3.2 Projeto Por Sector no tabela 1.3.3 Projeto Por Ministerio, no lista detallu kada Projeto bele hare iha #Aneksu A.

Tabela 1.3. 1 Projeto Municipio Liquica Por Fundus Financiamento

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM (FUNDO COVID + CD + BS + TP etc..) + PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	26	$3,831,621.83	$2,163,182.92	56.46%
2	LIQUICA VILA	25	$5,229,024.82	$1,798,117.55	34.39%
3	MAUBARA	19	$12,054,713.43	$8,272,420.38	68.62%
	Grand Total	**70**	**$21,115,360.08**	**$12,233,720.85**	**57.94%**

NO	POSTO ADMINISTRATIVO	FI			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	2	$557,358.72	$496,949.07	89.16%
2	LIQUICA VILA	4	$2,716,690.73	$1,516,050.42	55.81%
3	MAUBARA	5	$10,171,195.89	$8,018,036.38	78.83%
	Grand Total	**11**	**$13,445,245.34**	**$10,031,035.87**	**74.61%**

Dados Detallu Kada Projeto #Anexu A

NO	POSTO ADMINISTRATIVO	FUNDO COVID			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	$433,364.88	$256,424.78	59.17%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	**4**	**$433,364.88**	**$256,424.78**	**59.17%**

NO	POSTO ADMINISTRATIVO	LM -CD			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	8	$1,222,729.07	$595,292.54	48.69%
2	LIQUICA VILA	11	$1,546,813.46	$119,286.47	7.71%
3	MAUBARA	8	$1,124,659.99	$43,761.73	3.89%
	Grand Total	**27**	**$3,894,202.52**	**$758,340.74**	**19.47%**

Dados Detallu Kada Projeto #Anexu A

NO	POSTO ADMINISTRATIVO	LM-BS			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	6	$1,012,262.38	$674,396.77	66.62%
2	LIQUICA VILA	3	$313,656.48	$162,780.66	51.90%
3	MAUBARA	1	$170,965.65	$72,706.50	42.53%
	Grand Total	10	$1,496,884.51	$909,883.93	60.79%

NO	POSTO ADMINISTRATIVO	LM-TP			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	$ 289,002.61		
2	LIQUICA VILA	6	$ 474,930.65		
3	MAUBARA	3	$ 359,595.59		
	Grand Total	13	$ 1,123,528.85		

NO	POSTO ADMINISTRATIVO	PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	2	$316,904.17	$140,119.76	44.22%
2	LIQUICA VILA	1	$176,933.50		
3	MAUBARA	2	$228,296.31	$137,915.77	60.41%
	Grand Total	5	$722,133.98	$278,035.53	38.50%

Tabela 1.3. 2 Projeto Municipio Liquica Por Sectores



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

NO	SECTOR	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA	2	$91,877.21	$80,662.08	87.79%
2	AGUA E SANEAMENTO	3	$293,629.77	$167,315.56	56.98%
3	EDIFICIOS PUBLICOS	2	$210,635.04		
4	EDUKASAUN	18	$1,956,926.91	$302,946.05	15.48%
5	ELETRIFIKASAUN NASIONAL	5	$1,670,588.86	$1,297,809.30	77.69%
6	ESTRADA- IMPRESTIMO	1	$7,693,101.00	$5,795,051.15	75.33%
7	ESTRADAS	24	$5,012,524.75	$2,016,370.42	40.23%
8	FLOOD CONTROL	1	$502,473.28	$441,060.32	87.78%
9	MANUTENSAUN NO REHABILITASAUN	7	$1,522,380.50	$1,066,681.96	70.07%
10	PORTOS	1	$1,394,750.00	$657,275.92	47.12%
11	SAUDE	4	$433,364.88	$256,424.78	59.17%
12	SEGURANCA NO DEFESA	1	$58,107.88	$47,623.31	81.96%
13	TURISMO	1	$275,000.00	$104,500.00	38.00%
	Grand Total	**70**	**$21,115,360.08**	**$12,233,720.85**	**57.94%**

Dados Detallu Kada Projeto #Anexu A

NO	SECTOR	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA	2	$91,877.21	$80,662.08	87.79%
2	AGUA E SANEAMENTO	2	$122,664.12	$94,609.06	77.13%
3	EDIFICIOS PUBLICOS	1	$154,189.34		
4	EDUKASAUN	7	$783,470.96	$165,030.28	21.06%
5	ELETRIFIKASAUN NASIONAL	1	$499,250.84	$449,325.76	90.00%
6	ESTRADA- IMPRESTIMO				
7	ESTRADAS	6	$620,770.99	$71,729.53	11.55%
8	FLOOD CONTROL	1	$502,473.28	$441,060.32	87.78%
9	MANUTENSAUN NO REHABILITASAUN	1	$565,452.33	$556,717.80	98.46%
10	PORTOS				
11	SAUDE	4	$433,364.88	$256,424.78	59.17%
12	SEGURANCA NO DEFESA	1	$58,107.88	$47,623.31	81.96%
13	TURISMO				
	Grand Total	**26**	**$3,831,621.83**	**$2,163,182.92**	**56.46%**

Dados Detallu Kada Projeto #Anexu A

NO	SECTOR	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA				
2	AGUA E SANEAMENTO				
3	EDIFICIOS PUBLICOS				
4	EDUKASAUN	7	$642,009.75		
5	ELETRIFIKASAUN NASIONAL	2	$869,577.80	$630,877.47	72.55%
6	ESTRADA- IMPRESTIMO				
7	ESTRADAS	9	$1,365,759.10	$-	
8	FLOOD CONTROL				
9	MANUTENSAUN NO REHABILITASAUN	6	$956,928.17	$509,964.16	53.29%
10	PORTOS	1	$1,394,750.00	$657,275.92	47.12%
11	SAUDE				
12	SEGURANCA NO DEFESA				
13	TURISMO				
	Grand Total	**25**	**$5,229,024.82**	**$1,798,117.55**	**34.39%**

Dados Detallu Kada Projeto #Anexu A

NO	SECTOR	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA				
2	AGUA E SANEAMENTO	1	$170,965.65	$72,706.50	42.53%
3	EDIFICIOS PUBLICOS	1	$56,445.70		
4	EDUKASAUN	4	$531,446.20	$137,915.77	25.95%
5	ELETRIFIKASAUN NASIONAL	2	$301,760.22	$217,606.07	72.11%
6	ESTRADA- IMPRESTIMO	1	$7,693,101.00	$5,795,051.15	75.33%
7	ESTRADAS	9	$3,025,994.66	$1,944,640.89	64.26%
8	FLOOD CONTROL				
9	MANUTENSAUN NO REHABILITASAUN				
10	PORTOS				
11	SAUDE				
12	SEGURANCA NO DEFESA				
13	TURISMO	1	$275,000.00	$104,500.00	38.00%
	Grand Total	**19**	**$12,054,713.43**	**$8,272,420.38**	**68.62%**

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 3 Projeto Municipio Liquica Por Ministerios



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

NO	DONO DO PROJETO	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	3	$387,568.54		
2	MINISTERIO AGRIKULTURA E PESCAS	3	$139,176.53	$118,527.60	85.16%
3	MINISTERIO DAS OBRAS PUBLICAS	38	$16,370,980.54	$10,663,920.50	65.14%
4	MINISTERIO DO INTERIOR	1	$58,107.88	$47,623.31	81.96%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	18	$1,956,926.91	$302,946.05	15.48%
6	MINISTERIO PLANU E ORDENAMENTU	1	$99,484.80	$82,502.69	82.93%
7	MINISTERIO SAUDE	4	$433,364.88	$256,424.78	59.17%
8	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$1,394,750.00	$657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$275,000.00	$104,500.00	38.00%
	Grand Total	**70**	**$21,115,360.08**	**$12,233,720.85**	**57.94%**

Dados Detallu Kada Projeto #Anexu A

NO	DONO DO PROJETO	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	1	$154,189.34		
2	MINISTERIO AGRIKULTURA E PESCAS	2	$91,877.21	$80,662.08	87.79%
3	MINISTERIO DAS OBRAS PUBLICAS	10	$2,211,126.76	$1,530,939.78	69.24%
4	MINISTERIO DO INTERIOR	1	$58,107.88	$47,623.31	81.96%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	$783,470.96	$165,030.28	21.06%
6	MINISTERIO PLANU E ORDENAMENTU	1	$99,484.80	$82,502.69	82.93%
7	MINISTERIO SAUDE	4	$433,364.88	$256,424.78	59.17%
8	MINISTERIO TRANPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
	Grand Total	**26**	**$3,831,621.83**	**$2,163,182.92**	**56.46%**

Dados Detallu Kada Projeto #Anexu A

NO	DONO DO PROJETO	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EM EZEKUSAUN ($)
1	ESTATAL	1	$176,933.50		
2	MINISTERIO AGRIKULTURA E PESCAS	1	$47,299.32	$37,865.52	80.06%
3	MINISTERIO DAS OBRAS PUBLICAS	15	$2,968,032.25	$1,102,976.11	37.16%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	$642,009.75		
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$1,394,750.00	$657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
	Grand Total	**25**	**$5,229,024.82**	**$1,798,117.55**	**34.39%**

Dados Detallu Kada Projeto #Anexu A

NO	DONO DO PROJETO	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	1	$56,445.70		
2	MINISTERIO AGRIKULTURA E PESCAS				
3	MINISTERIO DAS OBRAS PUBLICAS	13	$11,191,821.53	$8,030,004.61	71.75%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	4	$531,446.20	$137,915.77	25.95%
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$275,000.00	$104,500.00	38.00%
	Grand Total	**19**	**$12,054,713.43**	**$8,272,420.38**	**68.62%**

Dados Detallu Kada Projeto #Anexu A

Tabela 4. 1 : Dadus Populasaun Munisipiu Liquica

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Bazartete	31,983	9,158	9,039	7,089	6,697
Liquiça	25,334	6,978	7,348	5,672	5,337
Maubara	25,234	7,088	6,802	5,766	5,578

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan refere hetan husi Progressu servisu nebe kompanha sira atinji iha fulan neé nia laran, husi lista nebe iha #Anexu B hatudu progressu aktual fulan ida neé ho nia persentagen servisu, montante aktual bazeia ba orsamento nebe hetan husi progressu fulan ida neé, ikus liu persentagen aktual fulan ida neé hatudu progressu fisiku komulativa husi porsento anterior no fulan ida neé nian, lista kompletu ba detailho bele hare iha #Anexu B, detallu ba Backup Fotografia #Anexu C1, Detallu ba Backup BoQ #Anexu C2 no Instrusaun servisu bele hare #Anexu D

III. OBSTÁKLU IHA TERENU

3.1 Obstáclo Servisu Iha Terenu

Durante iha Fulan ida nia laran, problema nebe ami enjineiru municipio hasoru mak hanesan :

1. Projeto lao tarde
2. Companhia balun servisu la tuir spesifikasaun
3. Companhia balun servisu la iha Site Engineer
4. Difikulidade ba Ekipa ADN M.LIQUICA hasoru susar ba Be'e mos

VI. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu iha Terenu

1. Rekomenda ba Kompanhia sira servisu tuir spesifikasaun nebe iha ona
2. Rekomenda ba Kompanhia sira tenke iha Site Engineer iha terenu

Rekomenda ba ADN.I.P. Nacional liu-liu ba Superior sira hodi hare ba Edificio ADN.I.P.

Note : Assinatura Husi Enjineiru Municipio Liquica

Força de Trabalho ADN,I.P Municipio Liquica					
No	**Deskrisaun**	**Identidade**			
		Naran Kompletu e Asinatura	**Nu. ID Card**	**Pozisaun**	**Fotografia**
1	Enjineiru	Juninho António A. Da Cruz	216	Enjineiru EPAS	
		Marcus Ximenes de Araujo	172	Enjineiru ITI	

		Camilio de Jesus	061	Enjineiru METIC	
2	Enjineira	Nencia F.O. do Rêgo	173	Enjineira VEBD	
3	Motorista	Rui Antonio Gaio	029	Motorista	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica Abril 2022

NU	NARAN PROJETU	DONO PROJETO	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESIO FISIKU (%)	PROGRESIO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
1	New Installation MV,LV Line and House Connection for Bazartete Vila to Leorema -Bazartete Sub District-Liquica District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	BAZARTETE	LIQUICA	Mina Petro Leste Unip, Lda	RDTL-11004589	$ 499,250.84		100.00%	90.00%	$ 449,325.76	$ 49,925.08	ABANDONA	
2	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Banir Lema	MPW-W-190097	$ 565,452.33	Aug. 14, 2019	100.00%	98.46%	$ 556,717.80	$ 64,406.31	PHO	Progresio Fisiko 100% e hela pagamento retensaun 10%
3	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	BAZARTETE	LIQUICA	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	$ 162,714.83	Aug. 16, 2019	95.68%	86.11%	$ 140,119.76	$ 22,595.07	ON-GOING	Progresu fizikamente remata ona no hein retensaun
4	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Lep Laco Dato	MPW-W-190111	$ 73,270.51	Sept. 5, 2019	100.00%	97.90%	$ 71,729.53	$ 8,712.25	PHO	Progresu fizikamente 100 % e sei falta pagamento ba retensaun
5	Konstrusaun Moraiha Foun Matadoro Tibar	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	$ 23,950.17	Dec. 5, 2019	77.60%	69.84%	$ 16,726.74	$ 7,223.43	ON-GOING	Provezorlamente servisu paradu hela
6	Konstrusaun Foun EBF Hotugara Bazartete, Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	EDUKASAUN	BAZARTETE	LIQUICA	Milcha Unip Lda	(RFQ:19/029-O-R)	$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	$ 24,910.52	$ 42,582.17	ON-GOING	
7	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Culoco Unipessoal Lda	Contract No.MOP-W-190184	$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	$ 12,106.37	$ 11,072.90	ON-GOING	Provezorlamente servisu paradu hela
8	New Water Supply of Bairos PNTL Liquica	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	BAZARTETE	LIQUICA	Holuli Unipessoal, Lda	SSS/054/MI-2019	$ 58,107.88	Nov. 29, 2019	86.27%	81.96%	$ 47,623.31	$ 10,484.57	ON-GOING	
9	Konstrusaun Armagen Foun Matadouro	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Naesalobu	MAP-P02019:19532	$ 67,927.04	Dec. 5, 2019	82.29	94.12%	$ 63,935.34	$ 17,617.77	ON-GOING	Progresu fizikamente remata ona
10	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	$ 44,268.56	$ 22,289.34	ON-GOING	ongoing
11	New construction of Isolation for covid 19 in liquica, Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Senizu	MS-DNA-NCB-20-163	$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	$ 212,156.22	$ 31,211.86	PHO	Projetu refere hela retensaun (10%) e Fisiku iha Tereno atinji deit 96.86%
12	Kanalizasaun Be Mos ho Sistema Gravitasaun iha Alpelo-Liquisa	MINISTERIO PLANU E ORDENAMENTU	LM -CD	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	$ 82,502.69	$ 16,982.11	ON-GOING	Falta retensaun
13	Emergency Project For Tibar River	MINISTERIO DAS OBRAS PUBLICAS	Emergency	FLOOD CONTROL	BAZARTETE	LIQUICA	Sali Magu Unipessoal Lda	RT/067/MOP-2021	$ 502,473.28	Sept. 20, 2021	99.75%	87.78%	$ 441,060.32	$ 180,765.72	ON-GOING	ON-GOING
14	Konstrusaun Edifício Posto Administrativo Bazartete & Moru Haleu	ESTATAL	PDIM	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	Aquarius Construction Unip,Lda	02/SMA-AML/PDIM VIII/2021	$ 154,189.34	Aug. 31, 2021	9.33%	0.00%	$ -	$ -	New	
15	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000	MINISTERIO DAS OBRAS PUBLICAS	LM -BS	ESTRADAS	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	$ 149,732.87	Oct. 01, 2021	6.61%	0.00%	$ -	$ -	New	
16	R4D Rural Road Spot Improvement Fahilebo - Fatumasi Chainage 0+000-2+300 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-RFQ - 21017	$ 88,852.44	Oct. 01, 2021	3.29%	0.00%	$ -	$ -	New	
17	R4D Rural Road Spot Improvement Libaloa - Fahilebo Chainage 0+000-7+000, liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatuleo Unip Lda	MPW-W-210144	$ 88,425.80	Oct. 01, 2021	12.46%	0.00%	$ -	$ -	New	
18	Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Craeleki Bercoli Unip,Lda	MPW-W-210145	$ 62,024.04	Oct. 01, 2021	6.85%	0.00%	$ -	$ -	New	SEIDAUK REGISTO IHA SISTEMA
19	R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500i Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	TM Calleba Unip,Lda	MPW-W-210158	$ 158,465.33	Oct. 01, 2021	5.21%	0.00%	$ -	$ -	New	SEIDAUK REGISTO IHA SISTEMA
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	Biamali Unipessoal Lda	RDTL-MS	$ 65,271.32		20.25%	0.00%	$ -		On going	
21	Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica	MINISTERIO SAUDE	Fundo Covid	SAUDE	BAZARTETE	LIQUICA	ZYC UNIPESSOAL LDA	RDTL-MS-C19-DNA-DC-21-228	$ 58,167.58	11/01/2022	11.30%	0.00%	$ -			
22	Konstrusaun Foun ESTV Leorema - Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	BAZARTETE	LIQUICA	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	$ 264,260.83	1/11/2021	0.00%	0.00%	$ -		New	
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 9,072.12	15/10/2021	10.86%	0.00%	$ -		New	
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 86,365.84	15/10/2021	0.00%	0.00%	$ -		New	
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 78,250.89	15/10/2021	9.37%	0.00%	$ -		New	
26	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 115,313.76	15/10/2021	5.24%	0.00%	$ -		New	
27	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	$ 153,851.88	Dec. 5, 2019	95.77%	81.19%	$ 124,915.14	$ 28,936.74	ON-GOING	Servisu iha Tereno remata tiha ona, sei hein kompanha Amenda kontratu nebe mate tiha ona
28	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	MINISTERIO TRANPORTES E KOMUNIKASAUN	FI	PORTOS	LIQUICA VILA	LIQUICA	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	$ 1,394,750.00	May 17, 2017	47.12%	47.12%	$ 657,275.92	$ 737,474.08	ON-GOING	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica Abril 2022

NU	NARAN PROJETU	DONO PROJETO	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESIO FISIKU (%)	PROGRESIO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
29	R4D Rural Road Periodic Maintenance Albenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Nheu	MPW-W-RFQ-190093	$ 55,012.05	Aug. 22, 2019	100%	99.91%	$ 54,964.83	$ 5,543.70	PHO	Projetu refere hela retensaun (10%) e Fisiku lha Tereno atinji deit 99.91%
30	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Albenu Chainage 0+000 - 7+600 Rutine Maintenance Taitabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Goubara Unip Lda	MPW-W-190096	$ 71,468.49	Aug. 19, 2019	100%	90.00%	$ 64,321.64	$ 7,146.85	PHO	Projetu ida neé Remata ona, no hela Retensaun 10% e pagamento atinji 100%
31	New Installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	LIQUICA VILA	LIQUICA	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	$ 593,093.80	Jan. 6, 2017	91.66%	67.45%	$ 400,036.22	$ 193,057.58	ON-GOING	
32	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	LIQUICA VILA	LIQUICA	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	$ 276,484.00	July 6, 2016	92.77%	83.49%	$ 230,841.25	$ 45,642.75	ON-GOING	
33	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	15 Raelti Unip. Lda	RT/034/MOP-2019	$ 452,362.93	Dec. 20, 2019	79.93%	50.38%	$ 227,897.03	$ 224,465.90	ON-GOING	
34	Manutensaun Kanais Irrigasaun Faulara - Liquica	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Banir Lema Unip,Lda	RDTL 0000	$ 47,299.32	Aug. 18,2021	88.95%	80.06%	$ 37,865.52	$ 9,433.80	ON-GOING	
35	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	$ 176,933.50	Aug. 31, 2021	3.83%	0.00%	$ -	$ -	New	
36	R4D Rural Road Spot Improvement Berlakuldu-Laberlaka Chainage 0+000-2+500	MINISTERIO DAS OBRAS PUBLICAS	LM -BS	ESTRADAS	LIQUICA VILA	LIQUICA	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	$ 131,219.62	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New	
37	R4D Rural Road Spot Improvement Taitabi - Kutulau Chainage 0+000-1+700, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	$ 123,631.72	Oct. 01, 2021	5.34%	0.00%	$ -	$ -	New	
38	R4D Rural Road Spot Improvement Metagou - Albenu Chainage 0+000-7+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	MOP - CD - NCB -R - 21038	$ 238,739.71	Oct. 01, 2021	14.72%	0.00%	$ -	$ -	New	
39	R4D Rural Road Spot Improvement Dato - Loidahar Chainage 0+000-12+300, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Luqueli Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	$ 188,589.13	Oct. 01, 2021	3.36%	0.00%	$ -	$ -	New	
40	R4D Rural Road Spot Improvement Albenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Caiulu, Unip Lda	MOP - CD - NCB -R - 21035	$ 162,215.27	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New	
41	R4D Rural Road Spot Improvement Albenu - Asumanu - Leurema Chainage 5+000-10+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	$ 165,363.43	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New	
42	R4D Rural Road Spot Improvement Berlakuldu - Laberlaka Chainage 2+500-5+400	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Claridade Unip,Lda	MPW-W-210163	$ 167,071.89	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New	
43	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Craeleki Bercoil, Unip Lda	MPW-W-210143	$ 76,423.05	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New	
44	Projeitu Konstrusaun foun ESG publico 01 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM -CD	EDUKASAUN	LIQUICA VILA	LIQUICA	Roman Furak Unip,Lda	NCB 16/MEJD/DNA/2021	$ 167,079.099	Nov. 1, 2021	18.23%	0.00%	$ -	$ -	New	
45	Tibar - Liquica - Maubara - Carimbala - Loes (A03)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	LIQUICA VILA	LIQUICA	Chanel Chander Unipessoal Lda	MPW-W-210202	$ 112,505.280	13/12/2021	2.40%	0.00%	$ -	$ -		
46	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 112,530.010	15/10/2021	9.48%	0.00%	$ -	$ -		
47	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 99,456.040	15/10/2021	8.55%	0.00%	$ -	$ -		
48	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 79,735.630	15/10/2021	0.00%	0.00%	$ -	$ -		
49	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laciolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 89,650.660	15/10/2021	9.25%	0.00%	$ -	$ -		
50	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 88,407.020	15/10/2021	0.00%	0.00%	$ -	$ -		
51	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 5,151.290	15/10/2021	0.00%	0.00%	$ -	$ -		
52	Addt. Poste liga Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	MAUBARA	LIQUICA	Fu Unip,Lda	RDTL - 0000	$ 13,000.00	Jan. 1, 2016	0.00	0.00%	$ -	$ 13,000.00	New	
53	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	MAUBARA	LIQUICA	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	$ 288,760.22	July 6, 2016	83.73%	75.36%	$ 217,606.07	$ 71,154.15	ON-GOING	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica Abril 2022

NU	NARAN PROJETU	DONO PROJETO	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESIO FISIKU (%)	PROGRESIO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
54	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	MAUBARA	LIQUICA	Montana Diak, Unipessoal, Lda	SSS/126/MOPTC-2017	$ 1,901,334.67	Sept. 7, 2017	99.98%	99.98%	$ 1,900,879.16	$ 190,543.43	ON-GOING	
55	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	$ 275,000.00	Dec. 27, 2016	40.00	38.00%	$ 104,500.00	$ 170,500.00	ON-GOING	
56	Novo Konstrusaun Edificio ESTV Lisadila	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	MAUBARA	LIQUICA	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	$ 171,850.61	Aug. 16, 2019	89.17%	80. 25%	$ 137,915.77	$ 33,934.84	ON-GOING	
57	Rehabilitasaun Sistema be'e mos iha aldeia Pandevou ho Mau-Uno,Sucu Guico /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	MAUBARA	LIQUICA	Oceania Const Unip.Lda	NCB-MOP-190051	$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	$ 72,706.50	$ 98,259.15	ON-GOING	Provizoriamente paradu hela
58	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	MAUBARA	LIQUICA	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co Ltd.	RFP/038/MOPTC/2016	$ 7,693,101.00	May 3, 2017	75.33%	75.33%	$ 5,795,051.15	$ 1,898,049.85	ON-GOING	
59	R4D Rural Road Maintenance Beriakulidu - Laberlaka Chainage 0+000 - 5+400 Nunulete - Darulema Chainage 0+000 - 1+600 Vaviquinia - Maubaralisa Chainage 0+000 - 12+500	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-190098	$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	$ 43,761.73	$ 6,940.86	ON-GOING	
60	Konstrusaun Moru Haleu no Posto Siguransa ba Edificio Posto Administrativo Maubara	ESTATAL	PDIM	EDIFICIOS PUBLICOS	MAUBARA	LIQUICA	Rafio Unip. Lda	01/AML/SMA-PDIM/VIII/2021	$ 56,445.70	July 21, 2021	16.32%	0.00%	$ -	$ -	New	
61	R4D Rural Road Spot Improvement Nunulete - Darulema Chainage 0+000-2+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Rito - Pu, Unipessoal,Lda	MOP -CD-RFQ - 21013	$ 67,382.23	Oct. 01, 2021	2.07%	0.00%	$ -	$ -	New	
62	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 4+800-9+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Malibo, Unipessoal LDA	MOP - CD- NCB-R- 21033	$ 152,622.90	Oct. 01, 2021	3.81%	0.00%	$ -	$ -	New	
63	R4D Rural Road Spot Improvement Barkau (Vaviquenia-Maubaralisa Chainage 0+000-4+200	MINISTERIO DAS OBRAS PUBLICAS	LM -BS	ESTRADAS	MAUBARA	LIQUICA	Nheu, Unipessoal LDA	MOP - CD- NCB-R- 21027	$ 173,484.62	Oct. 01, 2021	21.18%	0.00%	$ -	$ -	New	
64	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+000-4+800	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Murak, Unipessoal Lda	MPW-W-210157	$ 153,049.65	Oct. 01, 2021	5.87%	0.00%	$ -	$ -	New	
65	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa, Chainage 8+400-12+500)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Meta Loe Crae Bau Unip,Lda	MPW-W-210160	$ 198,698.25	Oct. 01, 2021	5.70%	0.00%	$ -	$ -	New	
66	R4D Rural Road Spot Improvement Samarapo - Gisu Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Nazico Unip Lda	-	$ 114,789.50	Oct. 01, 2021	2.18%	0.00%	$ -	$ -	New	
67	R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubaralisa Chainage 4+200-8+400)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-210161	$ 213,930.25	Oct. 01, 2021	2.25%	0.00%	$ -	$ -	New	
68	Konstrusaun ka Reabilitasaun ba EBF Gariana	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 117,902.04	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	New	
69	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 100,033.33	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	New	
70	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 141,660.22	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	New	
	TOTAL								$ 21,115,360.08				$ 12,233,720.85	57.94%		

PREPARA HUSI,

(Eng. Marcus Ximenes de Araujo)
Eng. ba Projetu Infrastutura Transporte e Irigasaun, ADN,I.P

(Eng. Juninho Antonio A. da Cruz)
Eng. ba Edificio Publiku Agua e Saneamento, ADN,I.P

(Eng. Camilio de Jesus)
Eng. Mekanikal e Electrikal ADN,I.P

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO B

PROGRESSU FISIKU FULAN ABRIL MUNICIPIO LIQUICA

					LOKALIZASAUN PROJETO											Apr-22		
NU	NARAN PROJETU	DONO PROJETO	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJETO	OBSERVASAUN	Previous Progress (%)	This Month Progress (%)	Komulative Progress (%)
1	New Installation MV,LV Line and House Connection for Bazartete Vila to Leorema - Bazartete Sub District-Liquica District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	BAZARTETE	LIQUICA	Mina Petro Leste Unip, Lda	RDTL-11004589	$ 499,250.84	Oct. 1, 2020	100.00%	90.00%	$ 449,325.76	$ 49,925.08	ABANDONA				
2	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Banir Lema	MPW-W-190097	$ 565,452.33	Aug. 14, 2019	100.00%	88.61%	$ 501,046.02	$ 64,406.31	PHO	Progresio Fisiko 100% e hela pagamento retensaun 10%			
3	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	BAZARTETE	LIQUICA	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	$ 162,714.83	Aug. 16, 2019	95.68%	86.11%	$ 140,119.76	$ 22,595.07	ON-GOING	Progresu fizikamente remata ona no hein retensaun			
4	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Lep Laco Dato	MPW-W-190111	$ 73,270.51	Sept. 5, 2019	100.00%	88.11%	$ 64,558.26	$ 8,712.25	PHO	Progresu fizikamente 100 % e sei falta pagamento ba retensaun			
5	Konstrusaun Moralha Foun Matadoro Tibar	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	$ 23,950.17	Dec. 5, 2019	77.60%	69.64%	$ 16,726.74	$ 7,223.43	ON-GOING	Provezoriamente servisu paradu hela			
6	Konstrusaun Foun EBF Hotugara Bazartete, Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	EDUKASAUN	BAZARTETE	LIQUICA	Milcha Unip Lda	(RFQ:19/029-Q-R)	$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	$ 24,910.52	$ 42,582.17	ON-GOING				
7	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Culoco Unipessoal Lda	Contract No.MOP-W-190184	$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	$ 12,106.37	$ 11,072.90	ON-GOING	Provezoriamente servisu paradu hela			
8	New Water Supply of Bairos PNTL Liquica	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	BAZARTETE	LIQUICA	Holuli Unipessoal, Lda	SSS/054/MI-2019	$ 58,107.88	Nov. 29, 2019	86.27%	81.96%	$ 47,623.31	$ 10,484.57	ON-GOING				
9	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Naesalobu	MAP-P02019:19532	$ 67,927.04	Dec. 5, 2019	82.29	74.06%	$ 50,309.27	$ 17,617.77	ON-GOING	Progresu fizikamente remata ona			
10	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	MINISTERIO SAUDE	FUNDO COVID	SAUDE	BAZARTETE	LIQUICA	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	$ 44,268.56	$ 22,289.34	ON-GOING	ongoing			
11	New construction of isolation for covid 19 in liquica, Timor Leste	MINISTERIO SAUDE	FUNDO COVID	SAUDE	BAZARTETE	LIQUICA	Senizu	MS-DNA-NCB-20-163	$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	$ 212,156.22	$ 31,211.86	PHO	Projetu refere hela retensaun (10%) e Fisiku iha Tereno atinji deit 96.86%			
12	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	MINISTERIO PLANU E ORDENAMENTU	LM -CD	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	$ 82,502.69	$ 16,982.11	ON-GOING	Falta retensaun			
13	Emergency Project For Tibar River	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	FLOOD CONTROL	BAZARTETE	LIQUICA	Sali Magu Unipessoal Lda	RT/067/MOP-2021	$ 502,473.28	Sept. 20, 2021	72.76%	64.02%	$ 321,707.56	$ 180,765.72	ON-GOING	ON-GOING			
14	Konstrusaun Edificio Posto Administrativo Bazartete & Moru Haleu	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Aquarius Construction Unip,Lda	02/SMA-AML/PDIM VIII/2021	$ 154,189.34	Aug. 31, 2021	9.33%	0.00%	$ -	$ -	New				
15	R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	$ 149,732.87	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		6.61%	6.47%	13.08%
16	R4D Rural Road Spot Improvemrnt Fahilebo -Fatumasi Chainage 0+000-2+300 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-RFQ - 21017	$ 88,852.44	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
17	R4D Rural Road Spot Improvemrnt Libaloa - Fahilebo Chainage 0+000-7+000, liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatuleo Unip Lda	MPW-W-210144	$ 88,425.80	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		12.46%	8.88%	21.34%
18	Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Craeleki Bercoli Unip,Lda	MPW-W-210145	$ 62,024.04	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		6.85%	5.86%	12.71%
19	R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	TM Caileba Unip,Lda	MPW-W-210158	$ 158,465.33	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		5.21%	9.83%	15.05%
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	MINISTERIO DA SAUDE	Fundo Covid	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	Biamali Unipessoal Lda	RDTL-MS-C19-DNA-DC-21-233	$ 65,271.32	11/01/2022					New		20.25%	33.38%	53.64%
21	Supply and installation connection for isolation and laboratorium Building Maumeta Liquica	MINISTERIO DA SAUDE	Fundo Covid	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	ZYC UNIPESSOAL LDA	RDTL-MS-C19-DNA-DC-21-228	$ 58,167.58	11/01/2022					New		11.30%	2.90%	14.20%
22	Konstrusaun Foun ESTV Leorema - Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM -BS	EDUKASAUN	BAZARTETE	LIQUICA	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	$ 264,260.83	01/11/2021		0.00%	$ -		New		0.00%	15.98%	15.98%
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 9,072.12	15/10/2021		0.00%	$ -		New		10.86%	0.00%	10.86%
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 86,365.84	15/10/2021		0.00%	$ -		New		0.00%	8.70%	8.70%
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 78,250.89	15/10/2021		0.00%	$ -		New				
26	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 115,313.76	15/10/2021		0.00%	$ -		New				
27	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	$ 153,851.88	Dec. 5, 2019	95.23%	81.19%	$ 124,915.14	$ 28,936.74	ON-GOING	Servisu iha Tereno remata tiha ona, sei hein kompanha Amenda kontratu nebe mate tiha ona			
28	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	MINISTERIO TRANPORTES E KOMUNIKASAUN	FI	PORTOS	LIQUICA VILA	LIQUICA	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	$ 1,394,750.00	May 17, 2017	47.12%	47.12%	$ 657,275.92	$ 737,474.08	ON-GOING				
29	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Nheu	MPW-W-RFQ-190093	$ 55,012.05	Aug. 22, 2019	100%	89.92%	$ 49,468.35	$ 5,543.70	PHO	Projetu refere hela retensaun (10%) e Fisiku iha Tereno atinji deit 99.91%			
30	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Goubara Unip Lda	MPW-W-190096	$ 71,468.49	Aug. 19, 2019	100%	90.00%	$ 64,321.64	$ 7,146.85	PHO	Projetu ida neé Remata ona, no hela Retensaun 10% e pagamento atinji 100%			
31	New Installation MV, LV Line and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	LIQUICA VILA	LIQUICA	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	$ 593,093.80	Jan. 6, 2017	91.66%	67.45%	$ 400,036.22	$ 193,057.58	ON-GOING				
32	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	LIQUICA VILA	LIQUICA	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	$ 276,484.00	July 6, 2016	92.77%	83.49%	$ 230,841.25	$ 45,642.75	ON-GOING				
33	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	15 Raelti Unip. Lda	RT/034/MOP-2019	$ 452,362.93	Dec. 20, 2019	76.44%	50.38%	$ 227,897.03	$ 224,465.90	ON-GOING				
34	Manutensaun Kanais Irrigasaun Faulara - Liquica	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Banir Lema Unip,Lda	RDTL 0000	$ 47,299.32	Aug. 18,2021	88.95%	80.06%	$ 37,865.52	$ 9,433.80	ON-GOING				
35	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	$ 176,933.50	Aug. 31, 2021	3.83%	0.00%	$ -	$ -	New				
36	R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-2+500, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	$ 131,219.62	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		1.16%	8.19%	9.35%
37	R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	$ 123,631.72	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		5.34%	8.49%	13.83%
38	R4D Rural Road Spot Improvemrnt Metaqou - Aibenu Chainage 0+000-7+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	MOP - CD - NCB -R - 21038	$ 238,739.71	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		14.72%	3.80%	18.53%
39	R4D Rural Road Spot Improvemrnt Dato - Liodahar Chainage 0+000-12+300, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Luqueli Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	$ 188,589.13	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		3.36%	4.52%	7.88%

40	R4D Rural Road Spot Improvemnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Caiulu, Unip Lda	MOP - CD - NCB -R - 21035	$ 162,215.27	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New			6.32%	6.32%
41	R4D Rural Road Spot Improvemnt Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	$ 165,363.43	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		1.48%	3.80%	5.29%
42	R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chainage 2+500-5+400	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Claridade Unip,Lda	MPW-W-210163	$ 167,071.89	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New		0.93%	7.01%	7.94%
43	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Craeleki Bercoli, Unip Lda	MPW-W-210143	$ 76,423.05	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
44	Projeitu Konstrusaun foun ESG publico 01 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM -CD	EDUKASAUN	LIQUICA VILA	LIQUICA	Roman Furak Unip,Lda	NCB 16/MEJD/DNA/2021	$ 167,079.099	Nov. 1, 2021	0.00%	0.00%	$ -	$ -	New				
45	Roads Maintenance Section : Tibar - Liquica - Maubara - Carimbala - Loes (A03)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	LIQUICA VILA	LIQUICA	Chanel Chander Unipessoal Lda	MPW-W-210202	$ 112,505.280	44543	0.00%	0.00%	$ -	$ -	New				
46	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 112,530.010	44484	0.00%	0.00%	$ -	$ -	New				
47	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 99,456.040	44484	0.00%	0.00%	$ -	$ -	New				
48	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 79,735.630	44484	0.00%	0.00%	$ -	$ -	New				
49	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 89,650.660	44484	0.00%	0.00%	$ -	$ -	New				
50	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 88,407.020	44484	0.00%	0.00%	$ -	$ -	New				
51	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 5,151.290	44484	0.00%	0.00%	$ -	$ -	New				
52	Addt. Poste liga Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	MAUBARA	LIQUICA	Fu Unip,Lda	RDTL - 0000	$ 13,000.00	Jan. 1, 2016	0.00	0.00%	$ -	$ 13,000.00	New				
53	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	MAUBARA	LIQUICA	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	$ 288,760.22	July 6, 2016	83.73%	75.36%	$ 217,606.07	$ 71,154.15	ON-GOING				
54	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	MAUBARA	LIQUICA	Montana Diak Unipessoal, Lda	SSS/126/MOPTC-2017	$ 1,901,334.67	Sept. 7, 2017	99.98%	89.98%	$ 1,710,791.24	$ 190,543.43	ON-GOING				
55	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	$ 275,000.00	Dec. 27, 2016	40.00	38.00%	$ 104,500.00	$ 170,500.00	ON-GOING				
56	Novo Konstrusaun Edificio ESTV Lisadila	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	MAUBARA	LIQUICA	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	$ 171,850.61	Aug. 16, 2019	89.17%	80. 25%	$ 137,915.77	$ 33,934.84	ON-GOING				
57	Rehabilitasaun Sistema be'e mos iha aldeia Pandevou ho Mau-Uno,Sucu Guico /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	MAUBARA	LIQUICA	Oceania Const Unip.Lda	NCB-MOP-190051	$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	$ 72,706.50	$ 98,259.15	ON-GOING	Provizoriamente paradu hela			
58	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	MAUBARA	LIQUICA	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOPTC/2016	$ 7,693,101.00	May 3, 2017	75.33%	75.33%	$ 5,795,051.15	$ 1,898,049.85	ON-GOING				
59	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000 - 1+600 Vaviquinia - Maubaralisa Chainage 0+000 - 12+500	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-190096	$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	$ 43,761.73	$ 6,940.86	ON-GOING				
60	Konstrusaun Moru Haleu no Posto Siguransa ba Edificio Posto Administrativo Maubara	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	MAUBARA	LIQUICA	Rafio Unip. Lda	01/AML/SMA-PDIM/VIII/2021	$ 56,445.70	July 21, 2021	16.32%	0.00%	$ -	$ -	New				
61	R4D Rural Road Spot Improvement Nunulete - Darulema Chainage 0+000-2+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Rito - Pu, Unipessoal,Lda	MOP -CD-RFQ - 21013	$ 67,382.23	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
62	R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Malibo, Unipessoal LDA	MOP - CD- NCB-R- 21033	$ 152,622.90	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
63	R4D Rural Road Spot Improvement Barkau (VaVIQUENIA) - Maubaralisa Chainage 0+000-4+200, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Nheu, Unipessoal LDA	MOP - CD- NCB-R- 21027	$ 173,484.62	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
64	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Murak, Unipessoal Lda	MOP - CD- NCB-R- 21032	$ 153,049.65	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
65	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa, Chainage 8+400-12+500)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Meta Loe Crae Bau Unip,Lda	MPW-W-210160	$ 198,698.25	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
66	R4D Rural Road Spot Improvement Samarapo -Gisu Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Nazico Unip Lda	MPW-W-210152	$ 114,789.50	Oct. 01, 2022	0.00%	0.00%	$ -	$ -	New				
67	R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubaralisa Chainage 4+200-8+400)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-210161	$ 213,930.25	Oct. 01, 2021	0.00%	0.00%	$ -	$ -	New				
68	Konstrusaun ka Reabilitasaun ba EBF Gariana	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 117,902.04	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	New				
69	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 100,033.33	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	New				
70	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 141,660.22	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	New		0.00%	8.05%	8.05%

INSPEKSAUN HUSI,

(Eng. Marcos de Araujo Ximenes)
Engineru ba Projetu Infrastrutura Transporte e Irigasaun ADN,I.P

(Eng. Juninho Antonio A. da Cruz)
Engineru ba Edificio Publiku Agua e Sanéamento ADN,I.P

(Eng. Camilo de Jesus)
Engineru ba Projetu Mekanikal e Elektrikal ADN,I.P

VERIFIKA HUSI,

(Eng. Remigio da C.S.dos Santos)
Engineru Senior ba Projetu Infrastutura Transporte e Irigasaun ADN,I.P

(Arq. Francisco Xavier D D. Jeronimo)
Engineru Senior ba Projetu Edificio Publiko no Be'e Sanéamento ADN,I.P

(Eng. Deolindo de Fatima Marques)
Chefe Seksaun Mekanikal e Elektrikal & ITC ADN,I.P

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

#ANEXO C2 (LV18)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400
Contractor : Claridade Unip.Lda
No. kontratu : MPW-W-210163

Data Inspeksaun : 25/Abril/2022

Fatin Inspeksaun : Suco Berlakulidu - Laberlaka

Koordinat :

Start Point : Long : 125.29520251 Latetude : - 8.63329600
End Point : Long : 125.30192345 Latetude : - 8.641753681


Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual


Sketch Item servisu : ***Gabios***

STA, 1+620

Sta, 5+900




Sta, 1+620





Sketch Item servisu : ***CMG leader***


STA, 0+000 - 2+220



t	w	*Distacia*	*Volume*
0.55	1.00	130.00	71.50
Total			71.50 m³



STA, 0+000 - 2+420



t	w	*Distacia*	*Volume*
0.40	0.25	130.00	26.00
0.15	1.00		19.50
Total			45.50 m³



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (LV18)

INSTRUSAUN / REKOMENDASAUN KADA PROJETO

Naran projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400

Naran Kompanha : Claridade Unipessoal.Lda

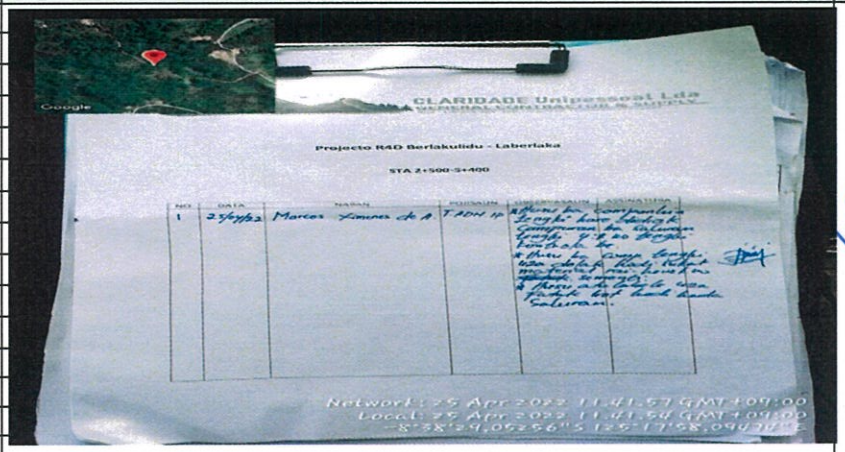No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	25/Abril/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO C2 (LV18)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400
Contractor : Claridade Unip.Lda
No. kontratu : MPW-W-210163

SUMMARY											
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP			RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,700.00				$ 1,300.00	0.78%			$ 1,300.00	0.78%
R-02	Drainage	$ 319.00									
R-03	Earth work	$ 6,484.77						$ 801.90	0.48%	$ 801.90	0.48%
R-05	Sub-base, base and pavement	$ 2,196.00									
R-08	Structures	$ 109,034.33						$ 5,992.45	3.59%	$ 5,992.45	3.59%
R-10	Dayworks	$ 140.00									
R-11	Routine maintenance	$ 5,440.50				$ 91.00	0.05%	$ 182.00	0.11%	$ 273.00	0.16%
R-15	Provisional sum	$ 1,000.00									
	GENERAL ITEM										
G-01	Security	$ 2,760.00						$ 920.00	0.55%	$ 920.00	0.55%
G-02	Project team	$ 12,180.00						$ 2,880.00	1.72%	$ 2,880.00	1.72%
G-03	Safety and protection	$ 2,513.00									
G-05	Meetings	$ 100.00									
G-06	Ceremonial costs	$ 200.00									
G-07	Mineral fees	$ 5,996.91									
A	**Construction cost**	**$ 127,314.60**				**$ 1,391.00**	**0.83%**	**$ 6,976.35**	**4.18%**	**$ 8,367.35**	**5.01%**
B	Contractor Fee (A x 10%)	$ 12,731.46				$ 139.10	0.08%	$ 697.64	0.42%	$ 836.74	0.50%
C	General items	$ 23,749.91				$ -	0.00%	$ 3,800.00	2.27%	$ 3,800.00	2.27%
D	Construction tax (A+B+C x 2%)	$ 3,275.92				$ 30.60	0.02%	$ 229.48	0.14%	$ 260.08	0.16%
E	**Total**	**$ 167,071.89**				**$ 1,560.70**	**0.93%**	**$ 11,703.46**	**7.01%**	**$ 13,264.17**	**7.94%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura, Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade, ADN I.P.

ANEXO C1 (LV14)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)

No. kontratu : MPW-W-210151

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Metagou - Aibeno

Koordinat :


Start Point : Long : 125.36544444 Latetude : - 8.66332014
End Point : Long : 125.3416468 Latetude : - 8.65444508

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry

STA, 0+090 - 0+900



Keterangan :

w1	***0.25***
w2	***0.80***
w3	***1.00***
t1	***1.50***
t2	***0.50***
L	***15.00***


		Distacia	*Volume*
Wall	0.79	15.00	11.81
Foundation	0.50		7.5
	Total		19.31 m3

Moru Protesaun nebe halo husi kompanhia



Sketch Item servisu : Stone Masonry

STA, 0+250-0+900



Keterangan :

w1	***0.25***
w2	***0.80***
w3	***1.00***
t1	***1.50***
t2	***0.50***
L	***15.00***

		Distacia	*Volume*
Wall	0.79	15.00	11.81
Foundation	0.50		7.5
	Total		19.31 m3





ANEXO C1 (LV14)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)

No. kontratu : MPW-W-210151

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Metagou - Aibeno

Koordinat :


Start Point : Long : 125.36544444 Latetude : - 8.66332014
End Point : Long : 125.3416468 Latetude : - 8.65444508

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Plum Concrete

STA, 0+090 - 0+900



t	L	*Distacia*	*Volume*
0.12	4.00	80.00	38.40
Total			38.40


Fotografia terreno hatudo katak companhia halo hela pengecoran Plum Concrete





Sketch Item servisu : *Plum Concrete*

STA, 0+250-0+900

t	L	*Distacia*	*Volume*
0.12	4.00	80.00	38.40
Total			38.40



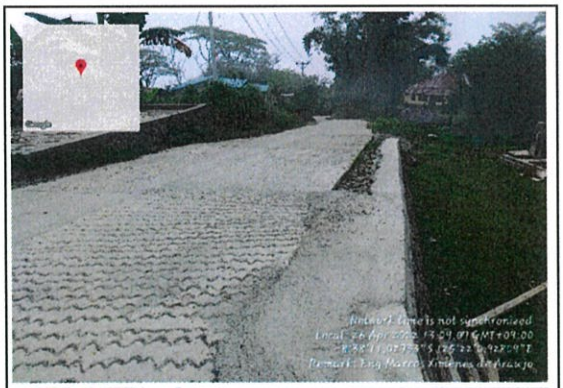

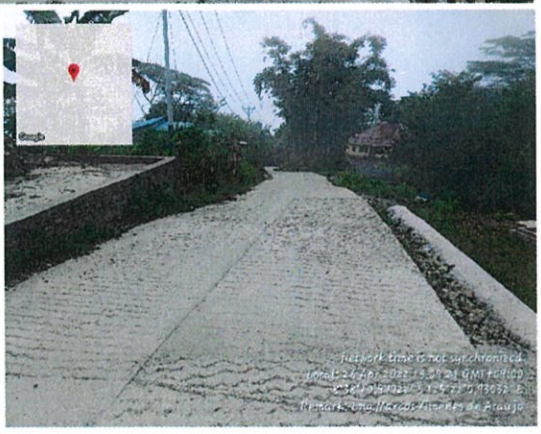

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV14)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvemrnt Metaqou - Aibenu Chainage 0+000-7+600, Liquica Municipality

Kompanha : Metalika Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Monitorizasaun iha Terreno teknik kompanhia laiha	
					2	Rekomenda Mandor atu fo hatene ba teknik Companhia tengki iha terreno	
					3	Husu ba Companha servisu tuir orentasaun nebe fo ona	
					4		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV14)

Naran Projeto :R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)
Contractor : Metalika Unip.Lda
No. kontratu :MPW-W-210151

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 3,400.00					$ 250.00	0.10%	$ -	0.00%	$ 250.00	0.10%
R-02	Drainage	$ 244.30										
R-03	Earth work	$ 5,301.97										
R-05	Sub-base, base and pavement	$ 3,356.64										
R-08	Structures	$ 159,824.15					$ 28,082.16	11.76%	$ 4,992.38	2.09%	$ 33,074.54	13.85%
R-11	Routine maintenance	$ 16,538.40					$ 196.00	0.08%	$ 196.00	0.08%	$ 392.00	0.16%
R-15	Provisional sum	$ 250.00										
GENERAL ITEM												
G-01	Security	$ 1,380.00					$ 230.00	0.10%	$ 345.00	0.14%	$ 575.00	0.24%
G-02	Project team	$ 13,660.00					$ 2,850.00	1.19%	$ 2,850.00	1.19%	$ 5,700.00	2.39%
G-03	Safety and protection	$ 3,062.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 200.00										
G-07	Mineral fees	$ 7,849.54										
A	**Construction cost**	**$ 188,915.45**					**$ 28,528.16**	**11.95%**	**$ 5,188.38**	**2.17%**	**$ 33,716.54**	**14.12%**
B	**Contractor Fee (A x 10%)**	**$ 18,891.55**					**$ 2,852.82**	**1.19%**	**$ 518.84**	**0.22%**	**$ 3,371.65**	**1.41%**
C	**General items**	**$ 26,251.54**					**$ 3,080.00**	**1.29%**	**$ 3,195.00**	**1.34%**	**$ 6,275.00**	**2.63%**
D	**Construction tax (A+B+C x 2%)**	**$ 4,681.17**					**$ 689.22**	**0.29%**	**$ 178.04**	**0.07%**	**$ 867.26**	**0.36%**
E	**Total**	**$ 238,739.71**					**$ 35,150.20**	**14.72%**	**$ 9,080.27**	**3.80%**	**$ 44,230.46**	**18.53%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto
Infraestructura,Transporte e irigaaun Municipio

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (LV15)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)

No. kontratu : MPW-W-210150

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Loidahar

Koordinat :

Start Point : Long : 125°19'36.41779 Latetude : - 8°36'46.93352


End Point : Long : 125°19'36.41779 Latetude : - 8°36'46.93352

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho

Sketch Item servisu : *Stone Masonry*

Sta, 3+150 - 3+150



t	L	*Distacia*	*Volume*
0.12	4.00	50.00	24.00
Total			24.00 m³


Observasaun iha tereno no Foto Aktual

Companhia halo Line drain iha Suco Loidahar no Sta, 3+250 - 3+300




Sketch Item servisu : *Stone Masonry*


Sta, 3+600 - 3+650




t	L	*Distacia*	*Volume*
0.12	4.00	50.00	24.00
Total			24.00 m³

Companhia halo Line drain iha Suco Loidahar no Sta, 3+600 - 3+650

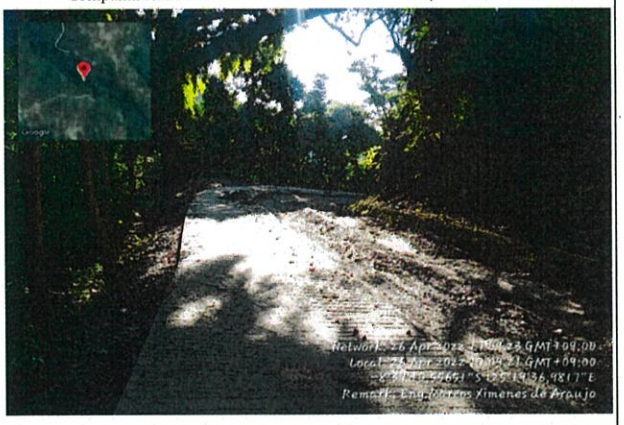



t	L	*Distacia*	*Volume*
0.12	4.00	50.00	24.00
Total			24.00 m³

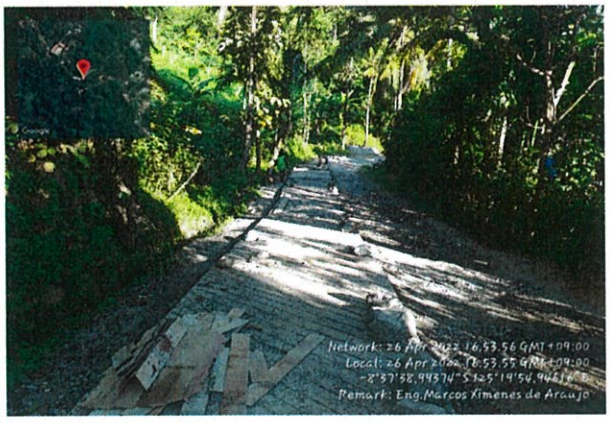

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV15)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)

Kompanha : Luqueli Oan Unip.Lda

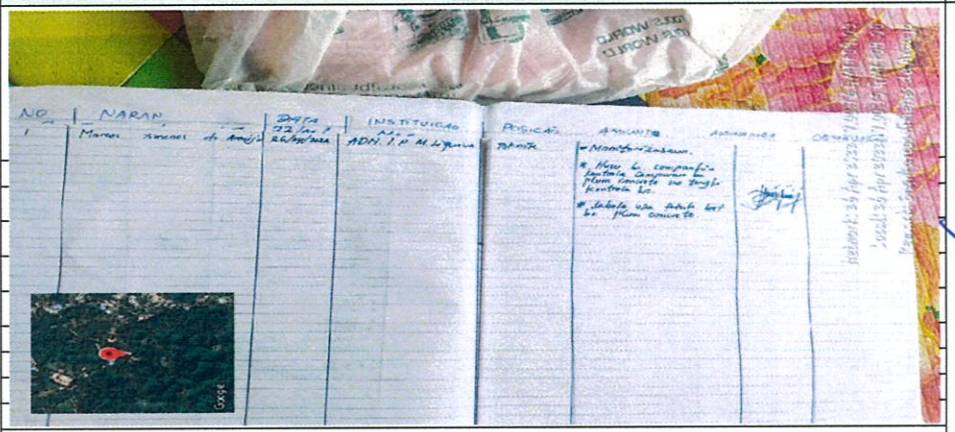No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II					1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV15)

Name of Roads : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)
Contract No : MPW-W-210150
Contractor : Luqueli Oan Unipessoal.Lda

SUMMARY

NO	DESCRIPTION	CONTRAC ORIGINAL	RESULTADO INSPEKSAUN MOP			RESULTADO INSPEKSAUN ADN.					
			PREVIOUS BILLING	THIS BILLING	TO DATE	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,300.00				$ 150.00	0.08%	$ -	0.00%	$ 150.00	0.08%
R-02	Drainage	$ 1,905.47									
R-03	Earth work	$ 19,160.19									
R-05	Sub-base, base and pavement	$ 5,007.60									
R-08	Structures	$ 97,539.20				$ 3,675.00	1.95%	$ 6,337.21	3.36%	$ 10,012.21	5.31%
R-11	Routine maintenance	$ 18,278.00				$ 140.00	0.07%	$ 140.00	0.07%	$ 280.00	0.15%
R-15	Provisional sum	$ 250.00									
	Sub Total	**$ 143,440.46**				**$ 3,965.00**	**2.10%**	**$ 6,477.21**	**3.43%**	**$ 10,442.21**	**5.54%**
	General items										
G-01	Security	$ 1,680.00				$ 560.00	0.30%	$ 280.00	0.15%	$ 840.00	0.45%
G-02	Project team	$ 9,960.00				$ 1,290.00	0.68%	$ 860.00	0.46%	$ 2,150.00	1.14%
G-03	Safety and protection	$ 6,094.50									
G-05	Meetings	$ 100.00									
G-06	Ceremonial costs	$ 175.00						$ 87.50	0.05%	$ 87.50	0.05%
G-07	Mineral fees	$ 9,097.30									
	Sub Total	**$ 27,106.80**				**$ 1,850.00**		**$ 1,227.50**	**0.65%**	**$ 3,077.50**	
A	**CONSTRUCTION COST**	**$ 143,440.46**				**$ 3,965.00**	**2.10%**	**$ 6,477.21**	**3.43%**	**$ 10,442.21**	**5.54%**
B	**PROFIT 10% x A**	**$ 14,344.05**				**$ 396.50**	**0.21%**	**$ 647.72**	**0.34%**	**$ 1,044.22**	**0.55%**
C	**OVERHEAD**	**$ 27,106.80**				**$ 1,850.00**	**0.98%**	**$ 1,227.50**	**0.65%**	**$ 3,077.50**	**1.63%**
D	**TAX 2% (A+B+C)**	**$ 3,697.83**				**$ 124.23**	**0.07%**	**$ 167.05**	**0.09%**	**$ 291.28**	**0.15%**
E	**GRAND TOTAL (A+B+C)**	***$ 188,589.13***				***$ 6,335.73***	**3.36%**	***$ 8,519.48***	**4.52%**	***$ 14,855.21***	**7.88%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (LV12)
Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)
Contractor : Goubara Unip.Lda
No. kontratu : MPW-W-210162

Data Inspeksaun : 25/Abril/2022

Fatin Inspeksaun : Suco Berlakuliado-Laberlaka

Koordinat :


Start Point : Long : 125.29724167 Latetude : - 8.60635641
End Point : Long : 125.2952025 Latetude : - 8.62329599714

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Plum Concrete

2+300 - 2+400




t	L	*Distacia*	*Volume*
0.12	3.75	100.00	45.00
Total			45.00 m³

Fotografia terreno hatudo katak companhia halo hela Plum concrete



Sketch Item servisu : Plum Concrete

2+300 - 2+400



t	L	*Distacia*	*Volume*
0.12	3.75	100.00	45.00
Total			45.00 m³



ANEXO C1 (LV12)
Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)
Contractor : Goubara Unip.Lda
No. kontratu : MPW-W-210162

Data Inspeksaun : 25/Abril/2022

Fatin Inspeksaun : Suco Berlakuliado-Laberlaka

Koordinat :


Start Point : Long : 125.29724167 Latetude : - 8.60635641
End Point : Long : 125.2952025 Latetude : - 8.62329599714

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry (Line Drain)

2+300 - 2+400




T	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m³

Fotografia terreno hatudo katak companhia halo hela Saluran



Sketch Item servisu : *Stone Masonry (Line Drain)*

2+300 - 2+400



t	L	*Distacia*	*Volume*
0.12	1.85	100.00	22.20
Total			22.20





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV12)

INSTRUSAUN / REKOMENDASAUN

Naran projeto :R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-2+500, Liquica Municipality

Kompanha : Goubara Unip.Lda

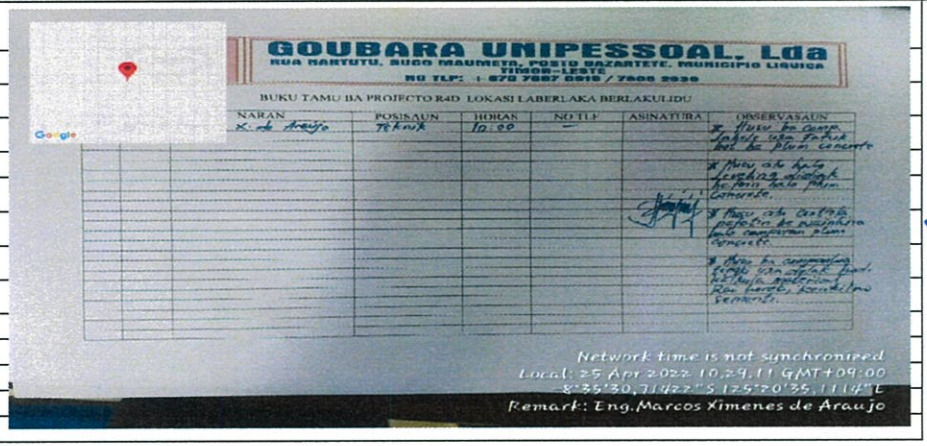No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	25/Abril/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II					1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV12)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)

Contractor : Goubara Unip.Lda

No. kontratu :MPW-W-210162

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,300.00							$ 250.00	0.19%	$ 250.00	0.19%
R-02	Drainage	$ 171.01										
R-03	Earth work	$ 4,699.77							$ 157.85	0.12%	$ 157.85	0.12%
R-05	Sub-base, base and pavement	$ 2,653.56										
R-08	Structures	$ 81,840.38					$ 1,358.65	1.04%	$ 6,161.02	4.70%	$ 7,519.67	5.73%
R-10	Dayworks	$ 105.00										
R-11	Routine maintenance	$ 5,957.00							$ 196.00	0.15%	$ 196.00	0.15%
R-15	Provisional sum	$ 775.00										
	General items											
G-01	Security	$ 690.00							$ 345.00	0.26%	$ 345.00	0.26%
G-02	Project team	$ 11,700.00							$ 2,750.00	2.10%	$ 2,750.00	2.10%
G-03	Safety and protection	$ 2,949.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 200.00										
G-07	Mineral fees	$ 4,655.79										
A	**Construction cost**	**$ 98,501.72**					**$ 1,358.65**	**1.04%**	**$ 6,764.87**	**5.16%**	**$ 8,123.52**	**6.19%**
B	**Contractor Fee (A x 10%)**	**$ 9,850.17**					**$ 135.86**	**0.10%**	**$ 676.49**	**0.52%**	**$ 812.35**	**0.62%**
C	**General items**	**$ 20,294.79**					**$ -**	**0.00%**	**$ 3,095.00**	**2.36%**	**$ 3,095.00**	**2.36%**
D	**Construction tax (A+B+C x 2%)**	**$ 2,572.93**					**$ 29.89**	**0.02%**	**$ 210.73**	**0.16%**	**$ 240.62**	**0.18%**
E	**Total**	**$ 131,219.62**					**$ 1,524.40**	***1.16%***	**$ 10,747.09**	***8.19%***	**$ 12,271.49**	***9.35%***

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura, Transportes e

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade, ADN I.P.

ANEXO C1 (LV13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality

No. kontratu : MOP - CD - NCB-R - 21036

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Taltabi - Kutulau

Koordinat :

Start Point : Long : 125.3714575 Latetude : - 8.64451919


End Point : Long : 125.3801075 Latetude : - 8.6527164

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Plum Concrete*

Sta, 1+150 - 1+200




t	L	*Distacia*	*Volume*
0.12	3.75	100.00	45.00
Total			45.00 m³

Companhia halo Plum Concrete iha no Sta, 1+150 - 1+200



Sketch Item servisu : *Plum Concrete*

Sta, 1+150 - 1+200



t	L	*Distacia*	*Volume*
0.12	3.75	100.00	45.00
Total			45.00 m³

Companhia halo Plum Concrete iha no Sta, 1+150 - 1+200





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV13)

INSTRUSAUN / REKOMENDASAUN

Naran projeto :R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality

Kompanha : Prudencia Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	16/Marco/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Monitorizasaun iha Terreno teknik kompanhia laiha	
					2	Rekomenda Mandor atu fo hatene ba teknik Companhia tengki iha terreno	
					3	Husu ba Companha servisu tuir orentasaun nebe fo ona	
					4		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV13)

Name of Roads :R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality
Contract No : MOP - CD - NCB-R - 21036
Contractor : Prudencia Construction Unipessoal.Lda

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,550.00					$ 250.00	0.20%	$ -	0.00%	$ 250.00	0.20%
R-03	Earth work	$ 6,216.90										
R-05	Sub-base, base and pavement	$ 2,205.60										
R-08	Structures	$ 69,266.99					$ 1,352.16	1.09%	$ 5,070.60	4.10%	$ 6,422.76	5.20%
R-11	Routine maintenance	$ 3,842.00					$ 280.00	0.23%	$ 280.00	0.23%	$ 560.00	0.45%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 15.00					$ 2.50	0.00%	$ 3.75	0.00%	$ 6.25	0.01%
G-02	Project team	$ 21,600.00					$ 4,400.00	3.56%	$ 4,400.00	3.56%	$ 8,800.00	7.12%
G-03	Safety and protection	$ 2,816.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 150.00										
G-07	Mineral fees	$ 4,861.93										
A	Construction cost	$ 83,331.49					$ 1,882.16	1.52%	$ 5,350.60	4.33%	$ 7,232.76	5.85%
B	Contractor Fee (A x 10%)	$ 8,333.15					$ 188.22	0.15%	$ 535.06	0.43%	$ 723.28	0.59%
C	General items	$ 29,542.93					$ 4,402.50	3.56%	$ 4,403.75	3.56%	$ 8,806.25	7.12%
D	Construction tax (A+B+C x 2%)	$ 2,424.15					$ 129.46	0.10%	$ 205.79	0.17%	$ 335.25	0.27%
E	Total	$ 123,631.72					$ 6,602.33	5.34%	$ 10,495.20	8.49%	$ 17,097.53	13.83%

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (LV17)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality

Contractor : Vicaroman Unip.Lda

No. kontratu : MOP - CD NCB - R - 21034

Data Inspeksaun : 26/Abril/2022



Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3416468 Latetude : - 8.65444508

End Point : Long : 125.3469018 Latetude : - 8.680286396

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : *Gabion* **Sta, 4+670** 	
Sketch Item servisu :Gabion **Sta, 4+670** 	

ANEXO C1 (LV17)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality

Contractor : Vicaroman Unip.Lda

No. kontratu : MOP - CD NCB - R - 21034

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3416468 Latetude : - 8.65444508


End Point : Long : 125.3469018 Latetude : - 8.680286396

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Stone Masonry*

Sta, 4+600 - 4+650




t	area	*Distacia*	*Volume*
1.00	0.38	50.00	18.75
Total			18.75 m³

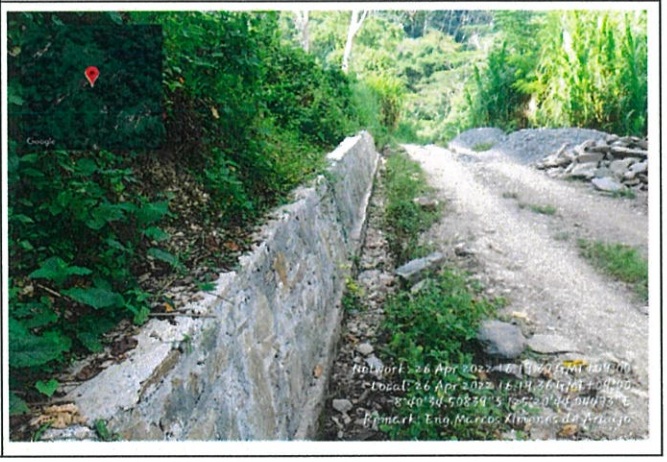

Sketch Item servisu : *Stone Masonry*

Sta, 4+600 - 4+650



t	Area	*Distacia*	*Volume*
1.00	0.38	50.00	18.75
Total			18.75 m³



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV17)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)

Kompanha : Vicaroman Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/04/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Monitorizasaun ba Terreno laiha ema servisu	
					2	Teknik Kompanhia Laiha Terreno	
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV17)

Name of Roads : R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)
Contract No : MPW-W-210155
Contractor : Vicaroman Unip.Lda

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,750.00							$ 250.00	0.15%	$ 250.00	0.15%
R-02	Drainage	$ 37.00										
R-03	Earth work	$ 13,233.46										
R-05	Sub-base, base and pavement	$ 8,729.99										
R-08	Structures	$ 82,879.01					$ 2,182.40	1.32%	$ 2,416.83	1.46%	$ 4,599.23	2.78%
R-11	Routine maintenance	$ 8,882.00							$ 200.00	0.12%	$ 200.00	0.12%
R-15	Provisional sum	$ 250.00										
	General Items											
G-01	Security	$ 1,380.00							$ 345.00	0.21%	$ 345.00	0.21%
G-02	Project team	$ 17,520.00							$ 2,670.00	1.61%	$ 2,670.00	1.61%
G-03	Safety and protection	$ 6,501.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 200.00										
G-07	Mineral fees	$ 8,290.40										
A	**Construction cost**	**$ 115,761.46**					**$ 2,182.40**	**1.32%**	**$ 2,866.83**	**1.73%**	**$ 5,049.23**	**3.05%**
B	**Contractor Fee (A x 10%)**	**$ 11,576.15**					**$ 218.24**	**0.13%**	**$ 286.68**	**0.17%**	**$ 504.92**	**0.31%**
C	**General items**	**$ 33,991.40**					**$ -**	**0.00%**	**$ 3,015.00**	**1.82%**	**$ 3,015.00**	**1.82%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,226.58**					**$ 48.01**	**0.03%**	**$ 123.37**	**0.07%**	**$ 171.38**	**0.10%**
E	**Total**	**$ 165,363.43**					**$ 2,448.65**	**1.48%**	**$ 6,291.88**	**3.80%**	**$ 8,740.53**	**5.29%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remegio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :


Start Point :	Long :	125.3469018	Latetude	: - 8.680286396
End Point :	Long :	125.3739113	Latetude	: - 8.684259297

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Stone Masonry*


Sta, 2+800 - 2+900

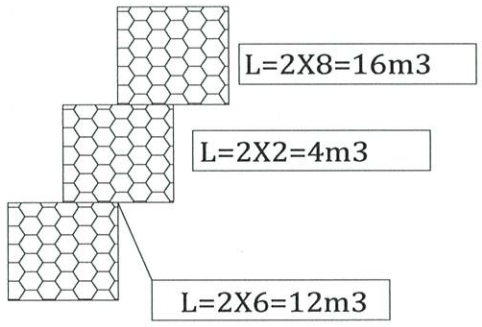



Sketch Item servisu :Gabion

Sta, 2+700

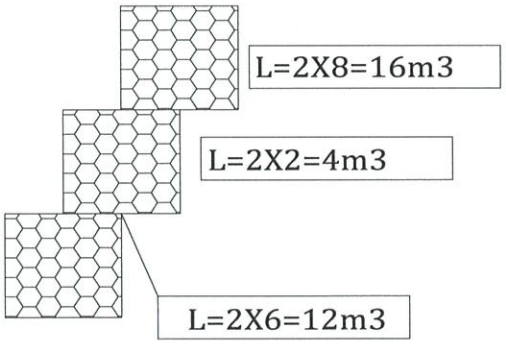



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3469018 Latetude : - 8.680286396


End Point : Long : 125.3739113 Latetude : - 8.684259297

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Excavation*

Sta, 2+530 - 2+630




T	w	*Distacia*	*Volume*
0.55	1.00	100.00	55.00
Total			55.00 m³




Sketch Item servisu : *Excavation*

Sta, 2+530 - 2+630



T	w	*Distacia*	*Volume*
0.55	1.00	100.00	55.00
Total			55.00 m³

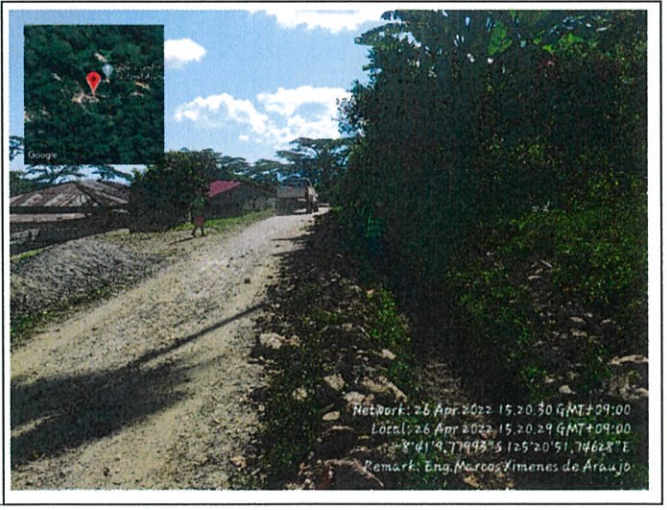

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV16)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)

Kompanha : Caiulu Unip.Lda

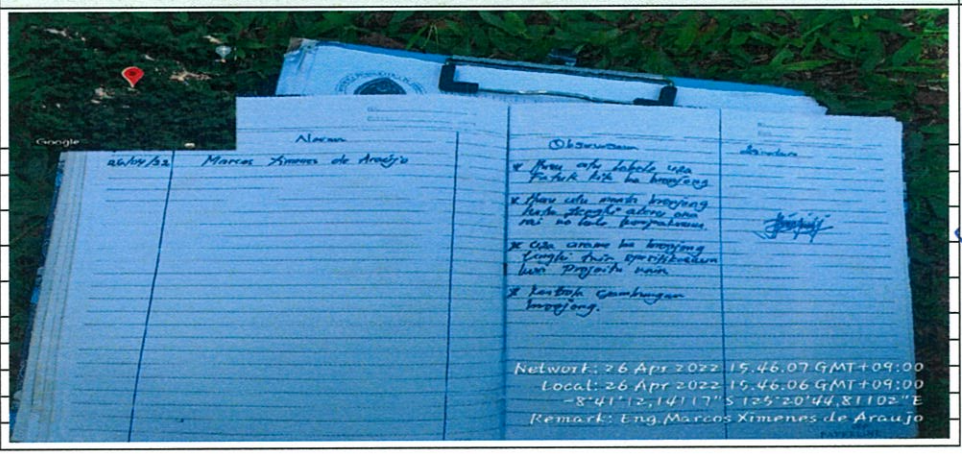No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II					1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV16)

Name of Roads : R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)
Contract No : MPW-W-210154
Contractor : Caiulu Unipessoal.Lda

SUMMARY										
Itime	**DESCRIPTION**	**CONTRACT ORIGINAL**	**RESULTADO INSPEKSAUN MOP**			**RESULTADO INSPEKSAUN ADN.IP**				
			PREVIOUS BILLING	**THIS BILLING**	**TO DATE**	**PREVIOUS BILDING**	**THIS BILLING**	**%**	**TO DATE**	**%**
R-01	General works	$ 1,700.00					$ 375.00	0.23%	$ 375.00	0.23%
R-02	Drainage	$ 174.10								
R-03	Earth work	$ 11,371.21					$ 215.05	0.13%	$ 215.05	0.13%
R-05	Sub-base, base and pavement	$ 8,458.48								
R-08	Structures	$ 82,977.14					$ 4,862.44	3.00%	$ 4,862.44	3.00%
R-11	Routine maintenance	$ 11,409.50					$ 280.00	0.17%	$ 280.00	0.17%
R-15	Provisional sum	$ 250.00								
	General items									
G-01	Security	$ 1,800.00					$ 450.00	0.28%	$ 450.00	0.28%
G-02	Project team	$ 15,900.00					$ 3,300.00	2.03%	$ 3,300.00	2.03%
G-03	Safety and protection	$ 4,618.00								
G-05	Meetings	$ 100.00								
G-06	Ceremonial costs	$ 200.00								
G-07	Mineral fees	$ 8,442.11								
A	**Construction cost**	**$ 116,340.43**					**$ 5,732.49**		**$ 5,732.49**	**3.53%**
B	**Contractor Fee (A x 10%)**	**$ 11,634.04**					**$ 573.25**		**$ 573.25**	**0.35%**
C	**General items**	**$ 31,060.11**					**$ 3,750.00**		**$ 3,750.00**	**2.31%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,180.69**					**$ 201.11**		**$ 201.11**	**0.12%**
E	**Total**	**$ 162,215.27**					**$ 10,256.85**		**$ 10,256.85**	**6.32%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (BZT19)

Back-up Data

Naran Projeto : Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000
Contractor : Craeleki Bercoli Unip.Lda
No. kontratu : MPW-W-210145


Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Maumeta - Metagou

Koordinat :

Start Point : Long : 125.34157891 Latetude : - 8.5948749774
End Point : Long : 125.38295813 Latetude : - 8.62965918

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

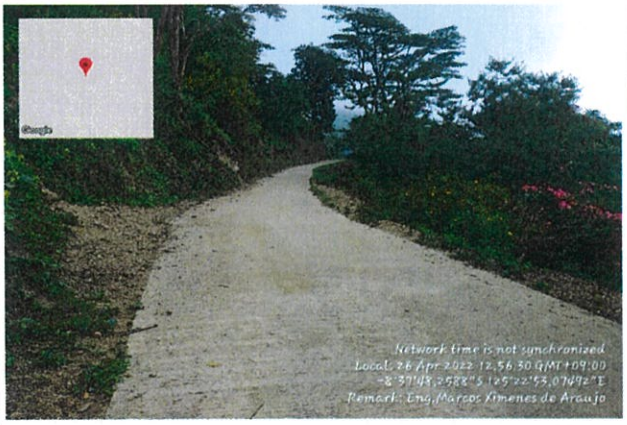Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : *CMG* **Sta, 6+200** Servisu Item CMG Leader nebe kompanhia kontinua hamos no taka dalan koak iha terreno	
Sketch Item servisu :*CMG* **Sta, 6+200** Servisu Item CMG Leader nebe kompanhia kontinua hamos no taka dalan koak iha terreno	

ANEXO C1 (BZT19)

Back-up Data

Naran Projeto : Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000
Contractor : Craeleki Bercoli Unip.Lda
No. kontratu : MPW-W-210145

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Maumeta - Metagou

Koordinat :


Start Point : Long : 125.34157891 Latetude : - 8.5948749774
End Point : Long : 125.38295813 Latetude : - 8.62965918

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Stone Masonry*

Sta, 7+160




T	w1 w2	*Distacia*	*Area*	*Volume*
1.00	0.30	10.00	0.55	5.50
	0.80			
Total				5.50 m³



Sketch Item servisu : *Stone Masonry*

Sta, 7+160



T	w1 w2	*Distacia*	*Area*	*Volume*
1.00	0.30	10.00	0.55	5.50
	0.80			
Total				5.50 m³



ANEXO D (BZT19)

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN **KADA**
PROJETO

Naran projeto : Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000

Naran Kompanha : Craeleki Bercoli Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Monitorizasaun iha terreno maibe buku tamu laiha	
					2	Teknik Kompanhia laiha tereno	
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (BZT19)
Back-up Data

Naran Projeto : Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000
Contractor : Craeleki Bercoli Unip.Lda
No.Kontrac : MPW-W-210145

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 700.00					$ 550.00	0.89%	$ -	0.00%	$ 550.00	0.89%
R-03	Earth work	$ 2,472.64										
R-05	Sub-base, base and pavement	$ 1,997.60										
R-08	Structures	$ 15,124.71					$ 527.94	0.85%	$ 414.81	0.67%	$ 942.75	1.52%
R-11	Routine maintenance	$ 17,562.00					$ 300.00	0.48%	$ 300.00	0.48%	$ 600.00	0.97%
R-15	Provisional sum	$ 250.00										
GENERAL ITEM												
G-01	Security	$ 1,500.00					$ 250.00	0.40%	$ 375.00	0.60%	$ 625.00	1.01%
G-02	Project team	$ 11,550.00					$ 2,400.00	3.87%	$ 2,400.00	3.87%	$ 4,800.00	7.74%
G-03	Safety and protection	$ 2,293.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 150.00										
G-08	Mineral fees	$ 3,297.24										
		$ 18,890.24					$ 2,650.00					
A	**Construction cost**	**$ 38,106.95**					**$ 1,377.94**	**2.22%**	**$ 714.81**	**1.15%**	**$ 2,092.75**	**3.37%**
B	**Contractor Fee (A x 10%)**	**$ 3,810.70**					**$ 137.79**	**0.22%**	**$ 71.48**	**0.12%**	**$ 209.28**	**0.34%**
C	**General items**	**$ 18,890.24**					**$ 2,650.00**	**4.27%**	**$ 2,775.00**	**4.47%**	**$ 5,425.00**	**8.75%**
D	**Construction tax (A+B+C x 2%)**	**$ 1,216.16**					**$ 83.31**	**0.13%**	**$ 71.23**	**0.11%**	**$ 154.54**	**0.25%**
E	**Total**	**$ 62,024.04**					**$ 4,249.05**	**6.85%**	**$ 3,632.52**	**5.86%**	**$ 7,881.57**	**12.71%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (BZT18)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality

No. kontratu : MPW-W-210144

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Libaloa-Fahilebo

Koordinat :

Start Point : Long : 125.43836103 Latetude : - 8.64943384

End Point : Long : 125.4135714 Latetude : - 8.63017393788538


Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

2

Sketch & Foto Desenho

Sketch Item servisu : Gabion

STA, 2+750

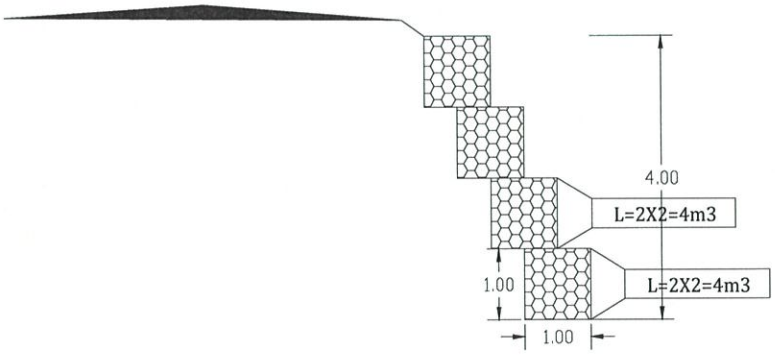


Observasaun iha tereno no Foto Aktual




Sketch Item servisu : *Plum Concrete*


STA, 2+350-2+450



T	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m³



Fotografia foti iha terreno wainhira trabalhador sira halo hela Drainagem

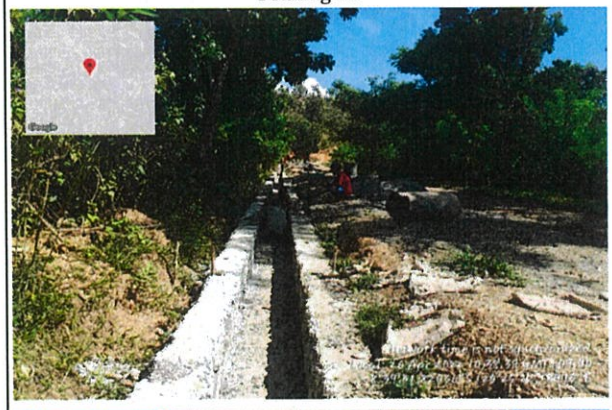



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (BZT18)

INSTRUSAUN / REKOMENDASAUN **KADA PROJETO**

Naran projeto : R4D Rural Road Spot Improvement Libaloa-Fahilebo Chainage 0+000-7+000) Liquica Municipality

Naran Kompanha : Hatuleo Unipessoal.Lda

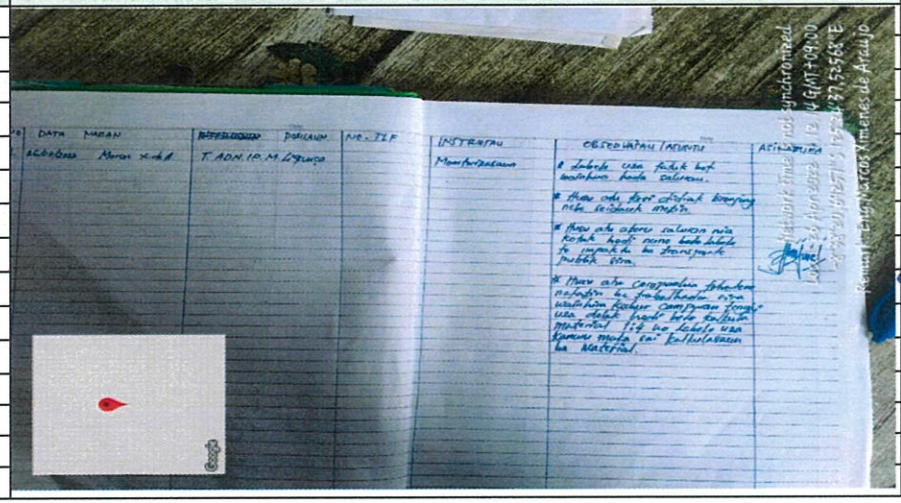No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4 5		
II					1 2 3 4 5		
III					1 2 3 4 5		

ANEXO C2 (BZT18)

Naran Projeto : R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality

No. kontratu :MPW-W-210144

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,250.00					$ 150.00	0.17%			$ 150.00	0.17%
R-02	Drainage	$ 121.86										
R-03	Earth work	$ 3,188.68										
R-05	Sub-base, base and pavement	$ 6,285.96										
R-08	Structures	$ 26,959.42					$ 6,288.77	7.11%	$ 3,669.42	4.15%	$ 9,958.19	11.26%
R-11	Routine maintenance	$ 12,699.00					$ 200.00	0.23%	$ 150.00	0.17%	$ 350.00	0.40%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 1,200.00					$ 200.00	0.23%	$ 200.00	0.23%	$ 400.00	0.45%
G-02	Project team	$ 14,700.00					$ 3,300.00	3.73%	$ 3,300.00	3.73%	$ 6,600.00	7.46%
G-03	Safety and protection	$ 5,886.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 175.00										
G-07	Mineral fees	$ 8,800.55										
A	**Construction cost**	**$ 50,754.92**					**$ 6,638.77**	**7.51%**	**$ 3,819.42**	**4.32%**	**$ 10,458.19**	**11.83%**
B	**Contractor Fee (A x 10%)**	**$ 5,075.49**					**$ 663.88**	**0.75%**	**$ 381.94**	**0.43%**	**$ 1,045.82**	**1.18%**
C	**General items**	**$ 30,861.55**					**$ 3,500.00**	**3.96%**	**$ 3,500.00**	**3.96%**	**$ 7,000.00**	**7.92%**
D	**Construction tax (A+B+C x 2%)**	**$ 1,733.84**					**$ 216.05**	**0.24%**	**$ 154.03**	**0.17%**	**$ 370.08**	**0.42%**
E	**Total**	**$ 88,425.80**					**$ 11,018.70**	**12.46%**	**$ 7,855.39**	***8.88%***	**$ 18,874.08**	***21.34%***

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto
Infraestructura,Transporte e irigaaun
Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes
e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (BZT16)

Naran Projeto :R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000

Contractor : Hatumeta Oan Unip.Lda

No. kontratu :MOP - CD-NCB-R -21030

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Libaloa -Bucumera

Koordinat :

Start Point : Long : 125.3931986 Latetude : - 8.63674152


End Point : Long : 125.3833257 Latetude : - 8.63314678

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual


Sketch Item servisu : *Stone Masonry*

Sta, 0+400 - 0+200




T	w	*Distacia*	*Volume*
0.40	0.25	53.60	10.72
0.15	1.00		8.04
Total			18.76 m³

Companhia halo Line drain iha Suco Libaloa no Sta, 0+400 - 0+200

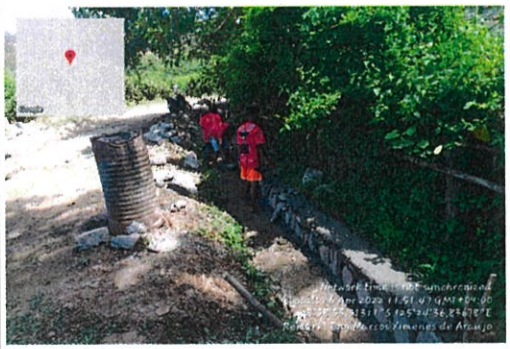

Sketch Item servisu : *Stone Masonry*

Sta, 0+400 - 0+200



T	w	*Distacia*	*Volume*
0.40	0.25	200.00	40.00
0.15	1.00		30
Total			70.00 m³

Companhia halo Line drain iha Suco Libaloa no Sta, 0+400 - 0+200



ANEXO C1 (BZT16)

Naran Projeto :R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000
Contractor : Hatumeta Oan Unip.Lda
No. kontratu :MOP - CD-NCB-R -21030

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Libaloa -Bucumera

Koordinat :


Start Point :	Long :	125.3931986	Latetude	: - 8.63674152
End Point :	Long :	125.3833257	Latetude	: - 8.63314678

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho

Sketch Item servisu : *Excavation*

Sta, 0+400 - 0+200



T	w	*Distacia*	*Volume*
0.55	1.00	200.00	110.00
Total			110.00 m³


Observasaun iha tereno no Foto Aktual

Companhia halo Line drain iha Suco Libaloa no Sta, 0+400 - 0+200



Sketch Item servisu : *Excavation*

Sta, 0+400 - 0+200



T	w	*Distacia*	*Volume*
0.55	1.00	200.00	110.00
Total			110.00 m³

Companhia halo Line drain iha Suco Libaloa no Sta, 0+400 - 0+200



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (BZT16)

INSTRUSAUN / REKOMENDASAUN **KADA PROJETO**

Naran projeto : R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000

Naran Kompanha : Hatumeta Oan Unipessoal.Lda

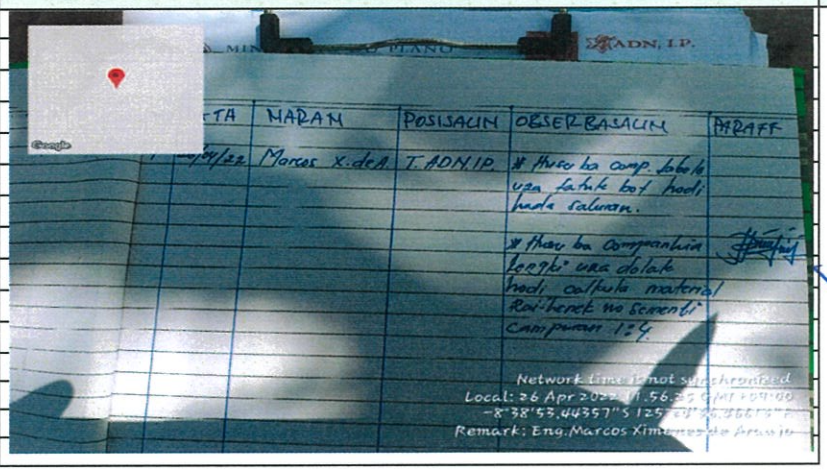No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4 5		
II					1 2 3 4 5		
III					1 2 3 4 5		

ANEXO C2 (BZT16)

Naran Projeto :R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000

Contractor : Hatumeta Oan Unip.Lda

No. kontratu :MOP - CD-NCB-R -21030

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,000.00					$ 150.00	0.10%	$ -	0.00%	$ 150.00	0.10%
R-02	Drainage	$ 97.72										
R-03	Earth work	$ 4,936.60					$ 453.71	0.30%	$ 451.00	0.30%	$ 904.71	0.60%
R-05	Sub-base, base and pavement	$ 793.80										
R-08	Structures	$ 97,039.43					$ 5,141.36	3.43%	$ 5,110.70	3.41%	$ 10,252.06	6.85%
R-11	Routine maintenance	$ 7,192.50					$ 168.00	0.11%	$ 168.00	0.11%	$ 336.00	0.22%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 1,380.00					$ 345.00	0.23%	$ 345.00	0.23%	$ 690.00	0.46%
G-02	Project team	$ 12,150.00					$ 2,850.00	1.90%	$ 2,850.00	1.90%	$ 5,700.00	3.81%
G-03	Safety and protection	$ 4,103.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 200.00										
G-07	Mineral fees	$ 5,091.88										
A	**Construction cost**	**$ 112,310.04**					**$ 5,913.07**	**3.95%**	**$ 5,729.70**	**3.83%**	**$ 11,642.77**	**7.78%**
B	**Contractor Fee (A x 10%)**	**$ 11,231.00**					**$ 591.31**	**0.39%**	**$ 572.97**	**0.38%**	**$ 1,164.28**	**0.78%**
C	**General items**	**$ 23,024.88**					**$ 3,195.00**	**2.13%**	**$ 3,195.00**	**2.13%**	**$ 6,390.00**	**4.27%**
D	**Construction tax (A+B+C x 2%)**	**$ 2,931.32**					**$ 193.99**	**0.13%**	**$ 189.95**	**0.13%**	**$ 383.94**	**0.26%**
E	**Total**	**$ 149,732.87**					**$ 9,893.36**	**6.61%**	**$ 9,687.62**	**6.47%**	**$ 19,580.99**	**13.08%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto
Infraestructura, Transporte e irigaaun
Municipio Liquica, ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Infrastructura, Transportes e Irigasaun,
ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade, ADN I.P.

ANEXO C1 (BZT20)

Naran Projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Contractor : TM.Cailebo Unip.Lda

No. kontratu : MPW-W-210158

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Fahilebo -Bucumera

Koordinat :

Start Point : Long : 125.3958511 Latetude : - 8.634983018


End Point : Long : 125.3828331 Latetude : - 8.640302834

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Stone Masonry*

Sta, 2+800 - 2+900




T	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m³



Sketch Item servisu :Gabion

Sta, 3+400 - 3+400

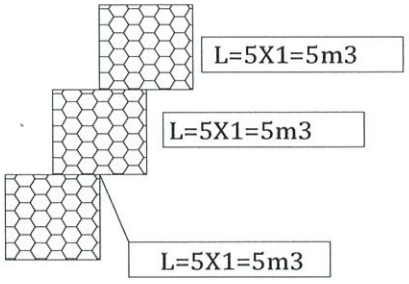





ANEXO C1 (BZT20)

Naran Projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Contractor : TM.Cailebo Unip.Lda

No. kontratu : MPW-W-210158

Data Inspeksaun : 26/Abril/2022

Fatin Inspeksaun : Suco Fahilebo -Bucumera

Koordinat :

Start Point : Long : 125.3958511 Latetude : - 8.634983018


End Point : Long : 125.3828331 Latetude : - 8.640302834

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Excavation*

Sta, 2+800 - 2+900




T	w	*Distacia*	*Volume*
0.55	1.00	100.00	55.00
Total			**55.00** m³



Sketch Item servisu : *Excavation*

Sta, 2+800 - 2+900



T	w	*Distacia*	*Volume*
0.55	1.00	100.00	55.00
Total			**55.00** m³





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (BZT20)

INSTRUSAUN / REKOMENDASAUN **KADA PROJETO**

Naran projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Naran Kompanha : TM Caileba Unip,Lda

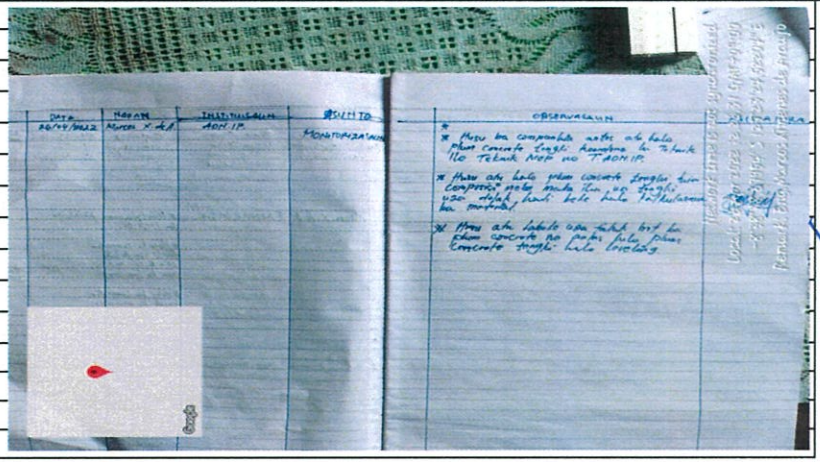No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Abril/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (BZT20)

Naran Projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Contractor : TM.Cailebo Unip.Lda

No. kontratu :MPW-W-210158

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,500.00					$ 150.00	0.09%	$ -	0.00%	$ 150.00	0.09%
R-02	Drainage	$ 164.55										
R-03	Earth work	$ 6,714.14					$ 445.50	0.28%	$ 891.00	0.56%	$ 1,336.50	0.84%
R-05	Sub-base, base and pavement	$ 2,216.25										
R-08	Structures	$ 102,616.19					$ 3,869.60	2.44%	$ 9,985.85	6.30%	$ 13,855.45	8.74%
R-11	Routine maintenance	$ 6,427.50					$ 182.00	0.11%	$ 182.00	0.11%	$ 364.00	0.23%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 1,440.00					$ 240.00	0.15%	$ 360.00	0.23%	$ 600.00	0.38%
G-02	Project team	$ 11,700.00					$ 2,750.00	1.74%	$ 2,750.00	1.74%	$ 5,500.00	3.47%
G-03	Safety and protection	$ 3,735.00										
G-05	Meetings	$ 100.00										
G-06	Ceremonial costs	$ 200.00										
G-07	Mineral fees	$ 4,974.69										
A	**Construction cost**	**$ 120,888.63**					**$ 4,647.10**	**2.93%**	**$ 11,058.85**	**6.98%**	**$ 15,705.95**	**9.91%**
B	**Contractor Fee (A x 10%)**	**$ 12,088.86**					**$ 464.71**	**0.29%**	**$ 1,105.89**	**0.70%**	**$ 1,570.60**	**0.99%**
C	**General items**	**$ 22,149.69**					**$ 2,990.00**	**1.89%**	**$ 3,110.00**	**1.96%**	**$ 6,100.00**	**3.85%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,102.54**					**$ 162.04**	**0.10%**	**$ 305.49**	**0.19%**	**$ 467.53**	**0.30%**
E	**Total**	**$ 158,465.33**					**$ 8,263.85**	**5.21%**	**$ 15,580.23**	**9.83%**	**$ 23,844.08**	**15.05%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Instrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

#ANEXU C1 – (BZT21)

Back-up Data

Naran Projeto : New Construction Fence Around for Isolation Covid 19 in Maumeta Liquica
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Data Inspesaun : 08 Abril 2022

Fatin Inspesaun : Maumeta – Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 33. 072''**, Latetude : .....

End Point : Long : **E 125º 20' 28. 881''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP munisipiu Likisa halao inspesaun ba projeitu Foun Konstrusaun Moru Haleu ba Isolamentu Covid 19 iha Liquica no kaer husi kompania Biamali Unip. Lda.	

#ANEXU C1 – (BZT21)

Back-up Data

Naran Projeto Liquica : New Construction Fence Around for Isolation Covid 19 in Maumeta
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania servisu ona too iha item plester ka reboka didin hafoin remata servisu hada batako (1 pc : 4 ps) no fui sinta leten.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu besi hollow nian mos kompania halo ona, ba instalasaun besi hollow vertikal (40 x 40 x 2mm) no besi hollow horizontal (80 x 40 x 2mm).	

#ANEXU C1 – (BZT21)


Back-up Data

Naran Projeto : New Construction Fence Around for Isolation Covid 19 in Maumeta Liquica
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

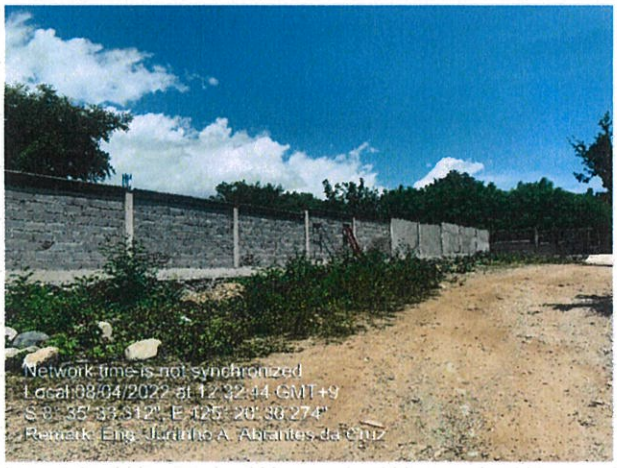

#ANEXU C1 – (BZT21)

Back-up Data

Naran Projeto : New Construction Fence Around for Isolation Covid 19 in Maumeta Liquica
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Data Inspesaun : 27 Abril 2022

Fatin Inspesaun : Maumeta – Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 33. 072''**, Latetude : .....

End Point : Long : **E 125º 20' 28. 881''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP munisipiu Likisa halao inspesaun ba projeitu Foun Konstrusaun Moru Haleu ba Isolamentu Covid 19 iha Liquica no kaer husi kompania Biamali Unip. Lda.	

#ANEXU C1 – (BZT21)

Back-up Data

Naran Projeto Liquica : New Construction Fence Around for Isolation Covid 19 in Maumeta
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP halao inspesaun ba pagamentu husi projeitu refere, rezultadu husi inspesaun iha loron nee mak sei sai rezultadu ba pedidu pagamentu neebe hatama ona husi kompania no projeitu nain.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu iha terenu kuaze remata tiha ona, no hela item balu deit maka sei lao hela no balu neebe presiza hadia halo diak fali. Hanesan ho dalan sai (exit gate) nia sementi balun neebe nakloke, tekniku ADN, IP foo ona instrusaun atu halo diak fali.	

#ANEXU C1 – (BZT21)

Back-up Data

Naran Projeto Liquica : New Construction Fence Around for Isolation Covid 19 in Maumeta
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Entry gate nia servisu maka seidauk remata, no kompania nia trabaliador sira hetan ona instrusaun atu finaliza lalais ba item nee molok sira hadia exit gate nian.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu pintura moru nian mos kuaze atu finaliza ona hela deit parte balu maka sei pinta hela husi kompania, no backfill ba rai hirak uluk neebe kee, mos sei hein finaliza pinta hotu maka kompania finaliza servisu item nee.	

#ANEXU C1 – (BZT21)

Back-up Data

Naran Projeto : New Construction Fence Around for Isolation Covid 19 in Maumeta Liquica
Kompania : Biamali Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-233

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PROJECT TITLE : NEW CONSTRUCTION FENCE AROUND FOR ISOLATION COVID-19
LOCATION : MAUMETA - LIQUICA MUNICIPALITY - TIMOR LESTE
PROJECT OWNER : MINISTRY OF HEALTH

SUMMARY

# ANEXU C2 - (BZT 21)			VERIFIED BY A D N , I P									
No	DESCRIPTION	AMOUNT (USD)	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
			FULAN KOTUK	%	FULAN NEE	%						
I	PREPARATION WORKS	$ 2,255.00	$ 1,127.50	1.73%	$ -	0.00%			$ 1,127.50	1.73%	$ 1,127.50	1.73%
II	FUNDATION WORKS	$ 11,000.46	$ 5,500.23	8.43%	$ 1,118.38	1.71%			$ 6,618.61	10.14%	$ 6,618.61	10.14%
III	CONCRETE WORKS	$ 15,907.15	$ 1,665.83	2.55%	$ 7,153.99	10.96%			$ 8,819.82	13.51%	$ 8,819.82	13.51%
IV	WALL INSTALLATION AND PLESTERING	$ 15,764.38	$ 3,371.20	5.16%	$ 7,882.19	12.08%			$ 11,253.39	17.24%	$ 11,253.39	17.24%
V	OTHER WORKS	$ 1,312.60	$ 118.03	0.18%	$ 694.58	1.06%			$ 812.60	1.24%	$ 812.60	1.24%
VI	PAINTING WORKS	$ 3,380.40	$ -	0.00%	$ 1,565.20	2.40%			$ 1,565.20	2.40%	$ 1,565.20	2.40%
VII	FINAL CLEARING	$ 100.00	$ -	0.00%	$ -	0.00%			$ -	0.00%	$ -	0.00%
A	**GRAND TOTAL**	**$ 49,719.99**	**$ 11,782.78**	**18.05%**	**$ 18,414.33**	**28.21%**			**$ 30,197.11**	**46.26%**	**$ 30,197.11**	**46.26%**
B	**FEE CONTRACTOR (10% x A)**	**$ 4,972.00**	**$ 1,178.28**	**1.81%**	**$ 1,841.43**	**2.82%**			**$ 3,019.71**	**4.63%**	**$ 3,019.71**	**4.63%**
C	**OVERHEAD**	**$ 4,425.00**	**$ -**	**0.00%**	**$ 1,106.25**	**1.69%**			**$ 1,106.25**	**1.69%**	**$ 1,106.25**	**1.69%**
D	**TAX (2% x(A+B+C)**	**$ 1,182.34**	**$ 259.22**	**0.40%**	**$ 427.24**	**0.65%**			**$ 686.46**	**1.05%**	**$ 686.46**	**1.05%**
E	**CONTIGENCY**	**$ 4,972.00**	**$ -**	**0.00%**	**$ -**	**0.00%**			**$ -**	**0.00%**	**$ -**	**0.00%**
F	**TOTAL PROJECT COST (A +B + C + D + E)**	**$ 65,271.32**	**$ 13,220.28**	**20.25%**	**$ 21,789.26**	**33.38%**			**$ 35,009.54**	**53.64%**	**$ 35,009.54**	**53.64%**

Inspeksaun Husi :

Eng. Juninho Antonio Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu
Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU D - (BZT21)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta

Kompanha : Biamali Unipessoal Lda

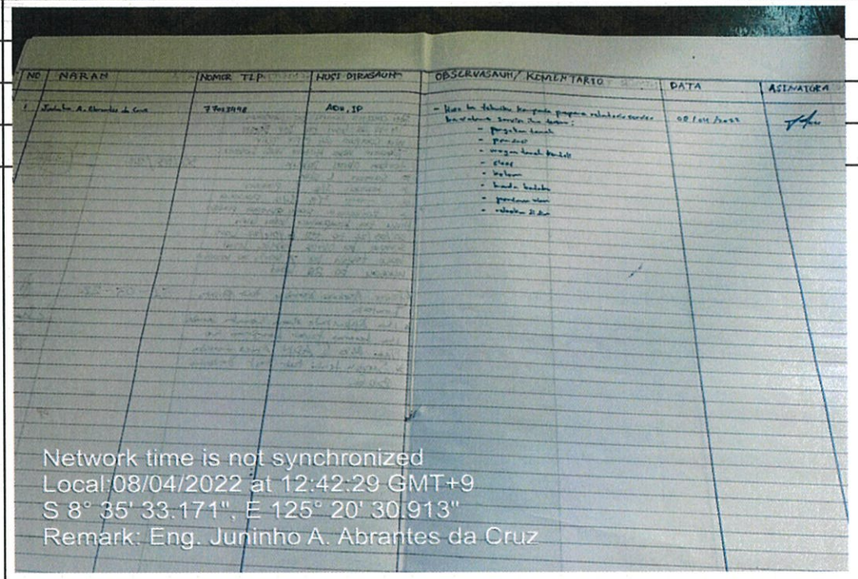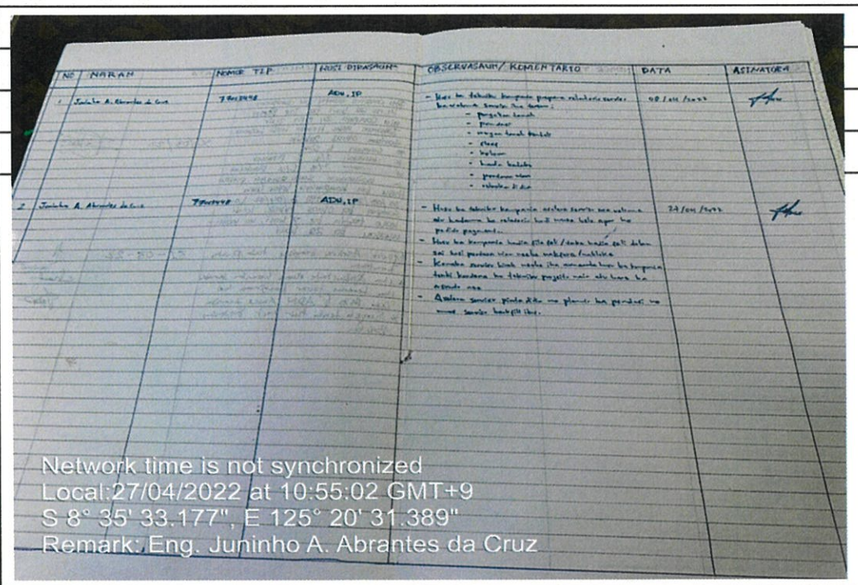No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/04/2022	Maumeta, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		
II	27/04/2022	Maumeta, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		

#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

Data Inspesaun : 08 Abril 2022

Fatin Inspesaun : Maumeta – Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 33. 307''**, Latetude : .....

End Point : Long : **E 125º 20' 30. 962''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa ADN, IP Munisipiu Likisa halao inspesaun dahuluk ba projeitu Foun Supply and Installation Connection for Isolation and Laboratorium Building iha Liquica, obra husi Ministeriu Saude husi fundu Covid no kaer husi kompania Zyc Unip. Lda.	

#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania finaliza ona servisu fui betaun ba item, kolom 15/15 (19,3 Mpa) no top beam 15/15 (19,3 Mpa). No hahuu kontinua fali ona servisu kontinuasaun ba leten nian (kuda-kuda).	

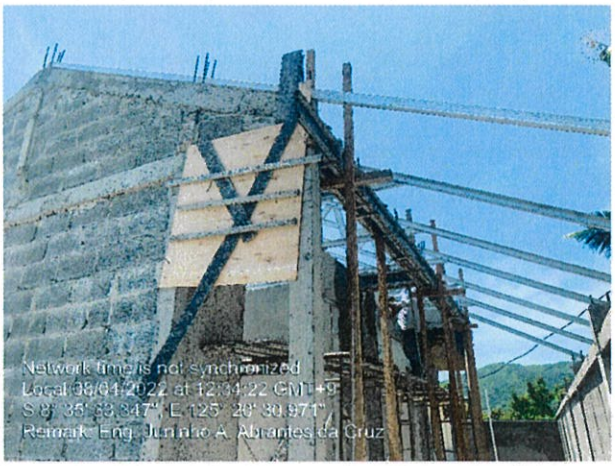Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania iha failansu ituan wainhira fui betaun top beam 15/15 tanba kompania haluha hakoi/monta plat HD iha top beam nia laran molok hatur kuda-kuda. Tan nee kordena ona ho projeitu nain no hetan ona solusaun ba problema nee.	

#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

Data Inspesaun : 27 Abril 2022

Fatin Inspesaun : Maumeta – Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 33. 307''**, Latetude : .....


End Point : Long : **E 125º 20' 30. 962''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

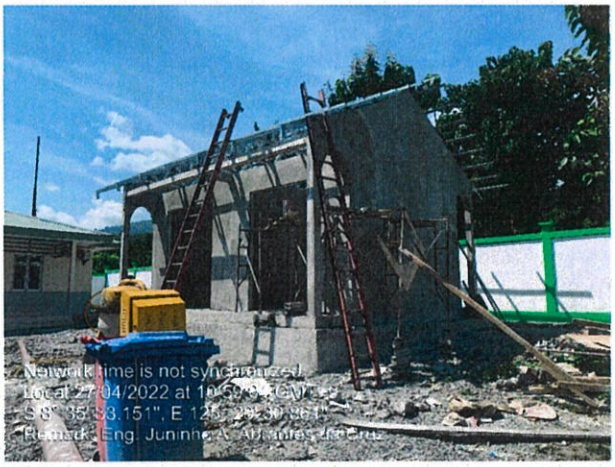Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa ADN, IP Munisipiu Likisa halao inspesaun dahuluk ba projeitu Foun Supply and Installation Connection for Isolation and Laboratorium Building iha Liquica, obra husi Ministeriu Saude husi fundu Covid no kaer husi kompania Zyc Unip. Lda.	

#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania servisu hotu ona ba item hada batako (40 x 20 x 10) (1pc : 4pc), no iha terenu trabaliador sira komesa ona reboka haleu uma tuir design (1pc : 3 sand) mahar 15mm.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku kompania ho tekniku projeitu nain kordena hamutuk ona, no hetan ona solusaun ba problema plat HD nian neebe foin dadauk la hakoi husi laran, no rezolve ona ba kestaun ida nee tuir design neebe husi projeitu nain nia tekniku.	

#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

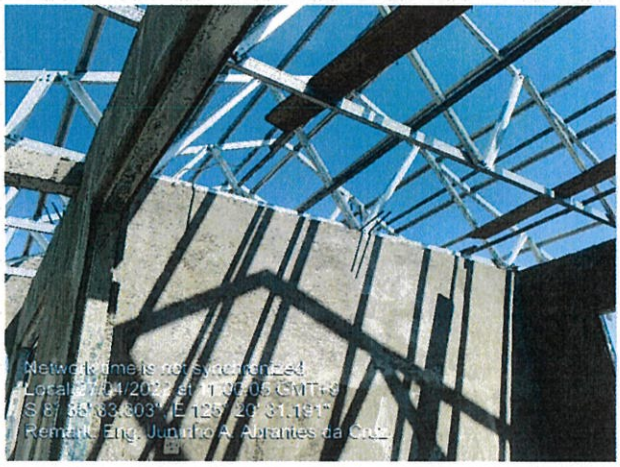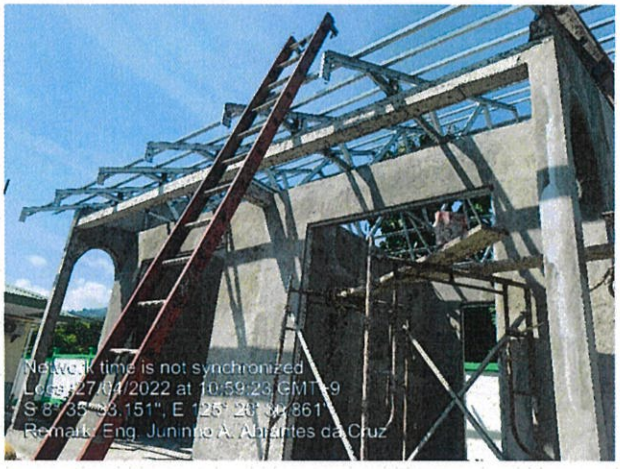Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu atap nian, iha terenu instala ona item Rangka Atap (Trusses Channels C 75 x 40 x 1 mm). No hahu instala ona item Baja Purlin V (Steel Purlin Channel V 45 x 35 x 0,75 mm).	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Material iha terenu maka sei insufisienti/menus liu ba trabaliador sira atu aselera servisu, tanba kompania rasik ladun iha terenu hodi hare sira nia servisu, so husi deit tekniku kompania.	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Project Name : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Location : Liquica Municipality - Timor Leste
Project Owner : Ministry of Health

#ANEXU C2 - (BZT22)			VERIFIED BY A D N , I P									
NO	DESCRIPTION	Amount (USD)	PREVIOUS	% BILLED	THIS BILLING	% BILLED	TO DATE	% BILLED	PROGRESU IHA TERENU				TOTAL %
									FULAN KOTUK	%	FULAN NEE	%	
I	PREPARATION WORKS	$ 4,200.00							$ 2,100.00	3.61%	$ -	0.00%	3.61%
II	NEW INSTALLATION LOW VOLTAGE (LV) LINE	$ 1,044.00							$ -	0.00%	$ -	0.00%	0.00%
III	MAIN CONNECTION TO ISOLATION INCLUDE PROVIDE GENSET	$ 22,726.44							$ -	0.00%	$ -	0.00%	0.00%
IV	CONSTRUCTION HOUSE FOR GENSET	$ 15,040.67							$ 3,760.17	6.46%	$ 1,504.07	2.59%	9.05%
V	FINAL CLEARING	$ 1,000.00							$ -	0.00%	$ -	0.00%	0.00%
A	GRAND TOTAL	$ 44,011.11							$ 5,860.17	10.07%	$ 1,504.07	2.59%	12.66%
B	Fee Contractor(10% x A)	$ 4,401.11							$ 586.02	1.01%	$ 150.41	0.26%	1.27%
C	Overhead	$ 4,300.00							$ -	0.00%	$ -	0.00%	0.00%
D	TAX 2% x (A + B + C)	$ 1,054.24							$ 128.92	0.22%	$ 33.09	0.06%	0.28%
E	CONTIGENCY (10% x A)	$ 4,401.11							$ -	0.00%	$ -	0.00%	0.00%
F	TOTAL PROJECT COST (A + B + C + D + E)	$ 58,167.58							$ 6,575.11	11.30%	$ 1,687.56	2.90%	14.20%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU D - (BZT22)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica

Kompanha : Zyc Unipessoal Lda

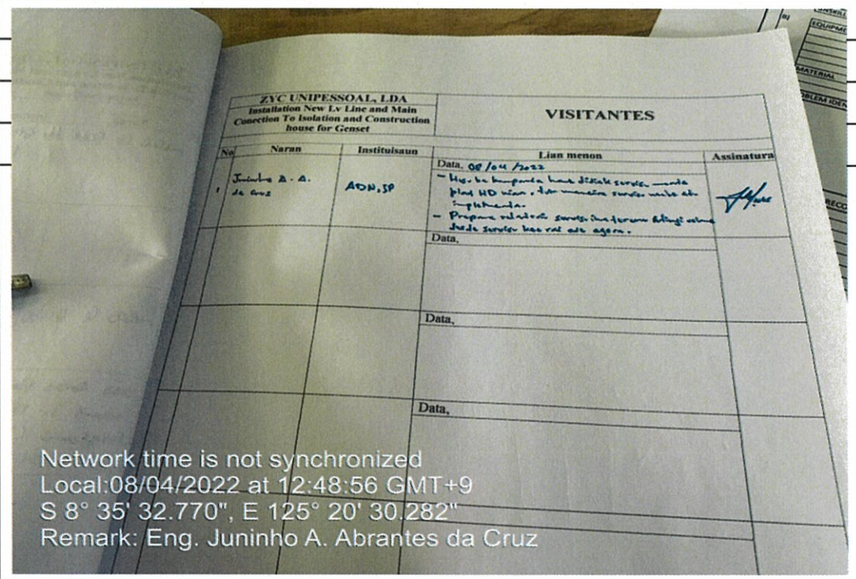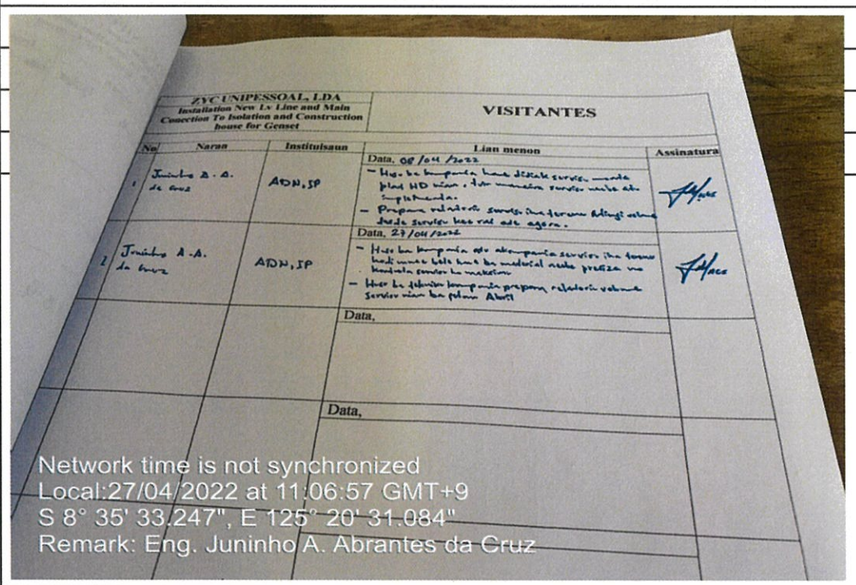No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/04/2022	Maumeta, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		
II	27/04/2022	Maumeta, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		

#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Data Inspesaun : 26 Abril 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 40' 43. 435''**, Latetude : .....

End Point : Long : **E 125º 22' 18. 833''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....


4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu Konstrusaun Foun ESTV Leorema lokaliza iha suku Leorema, Bazartete, Munisipiu Likisa projeitu nee kaer husi kompania U-Rema Unip. Lda.	

#ANEXU C1 – (BZT23)
Back-up Data


Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Hafoin kompania servisu remata item hada fatuk pondasi no hatur besi beton ulir diametru 12mm ba sloof okos (ground beam) diametru entre tulangan ho sengkang tuir ona design neebe hatoo iha BoQ, kompania hahuu fali monta bekisting ba sloof nian.	

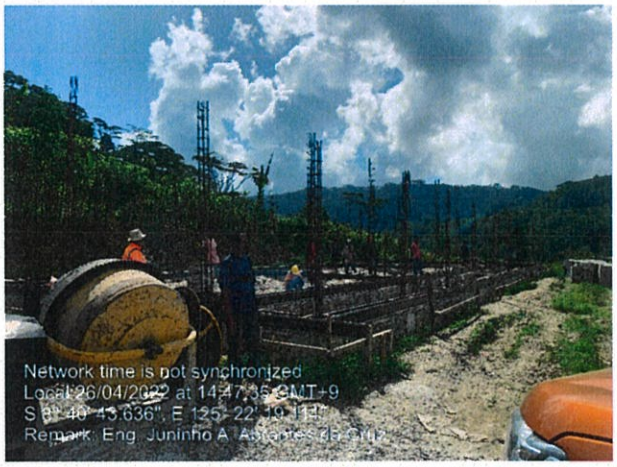Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu besi beton polos begel ho diametru 8mm ba sloof mos kesi ona husi kompania, ba item reinforcement nian. No kompania hatoo ona karta despaisu atu ekipa tekniku Laboratorium bele foti amostra betaun ba sloof nian.	

#ANEXU C1 – (BZT23)
Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

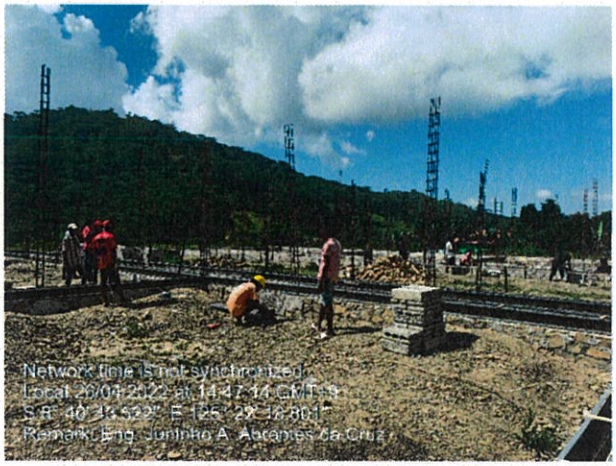Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania mos hatoo katak iha mudansa konaba item hakoi pipa hodi dada fiu eletrisidade husi tulangan sloof nia laran, tuir ekipa Infraestrutura nian katak tenki monta fali husi liur tanba tauk dampak ba iha kekuatan beton ground beam nian.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Area klase C sorin nian trabaliador sira foin komesa servisu kesi besi, no hafoin sira remata klase iha sorin maka sei komesa fali ba klase ida nee.	

#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Data Inspesaun : 28 Abril 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 40' 43. 435''**, Latetude : .....

End Point : Long : **E 125º 22' 18. 833''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu Konstrusaun Foun ESTV Leorema lokaliza iha suku Leorema, Bazartete, Munisipiu Likisa projeitu nee kaer husi kompania U-Rema Unip. Lda.	

#ANEXU C1 – (BZT23)
Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa kordena ho ekipa tekniku Laboratorium ADN, IP no ekipa tekniku projeitu nain munisipiu Likisa nian, akompania hamutuk no foti amostra hamutuk ba servisu pengecoran sloof okos (ground beam) (mutu beton 25 Mpa).	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba kompozisaun servisu betaun sloof okos nian foti no teste husi Laboratorium Obras Nasional, no hetan ona lisensa atu kontinua servisu pengecoran ba item refere iha terenu mantein tuir kompozisaun neebe iha ona.	

#ANEXU C1 – (BZT23)
Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania hahuu servisu pengecoran ba sloof okos (ground beam) nian iha terenu ba iha area klase hirak neebe monta ona besi no bekisting. Kompania prepara mos ho vibrator atu uza hodi bele hetan rezultadu neebe maksimu.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Rezultadu husi slump test neebe hetan husi kompozisaun neebe Laboratorium Obras Nasional foo sai maka = 8 cm.	

#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA TECNICA VOCASIONAL LEOREMA
FATIN PROJEITO : LEOREMA , BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (BZT23)			VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
			FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	$ 3,035.00			$ 1,517.50	0.57%					$ 1,517.50	0.57%
II	CLASSROOM BUILDING C 2 UNIT (2 X 56653.93)	$ 113,269.89			$ 28,317.47	10.72%					$ 28,317.47	10.72%
III	TEACHER OFFICE	$ 77,944.01			$ 7,794.40	2.95%					$ 7,794.40	2.95%
IV	TOILET BUILDING	$ 30,577.69			$ -	0.00%					$ -	0.00%
V	PROVISIONAL SUM FOR SITE WORKS	$ 6,000.00			$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST	$ 230,826.59			$ 37,629.37	14.24%					$ 37,629.37	14.24%
B	PROFIT 10% X A	$ 23,082.66			$ 3,762.94	1.42%					$ 3,762.94	1.42%
C	OVERHEAD	$ 5,170.00			$ -	0.00%					$ -	0.00%
D	TAX 2% X (A + B + C)	$ 5,181.58			$ 827.85	0.31%					$ 827.85	0.31%
E	CONTIGENCY	$ 4,500.00			$ -	0.00%					$ -	0.00%
F	GRAND TOTAL	$ 264,260.83			$ 42,220.16	15.98%					$ 42,220.16	15.98%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU D - (BZT23)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN ESTV LEOREMA

Kompania : U-REMA UNIP. LDA.

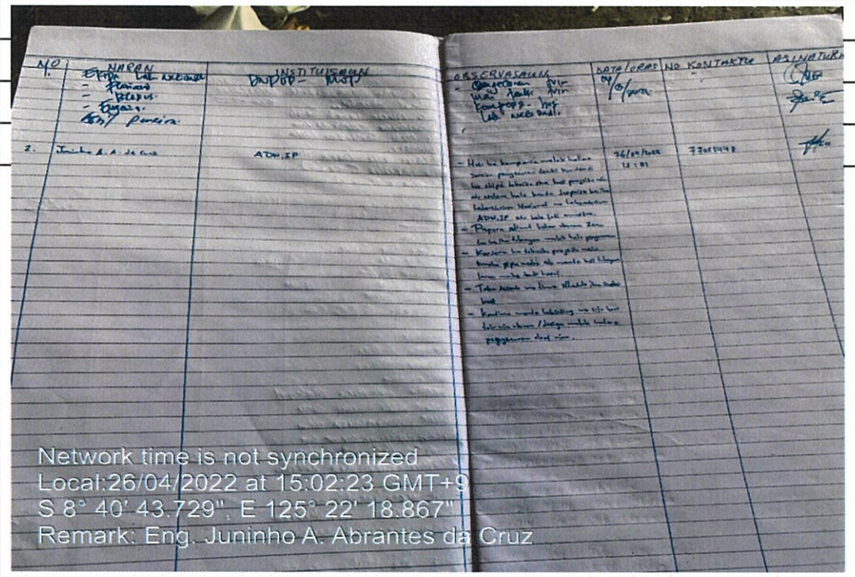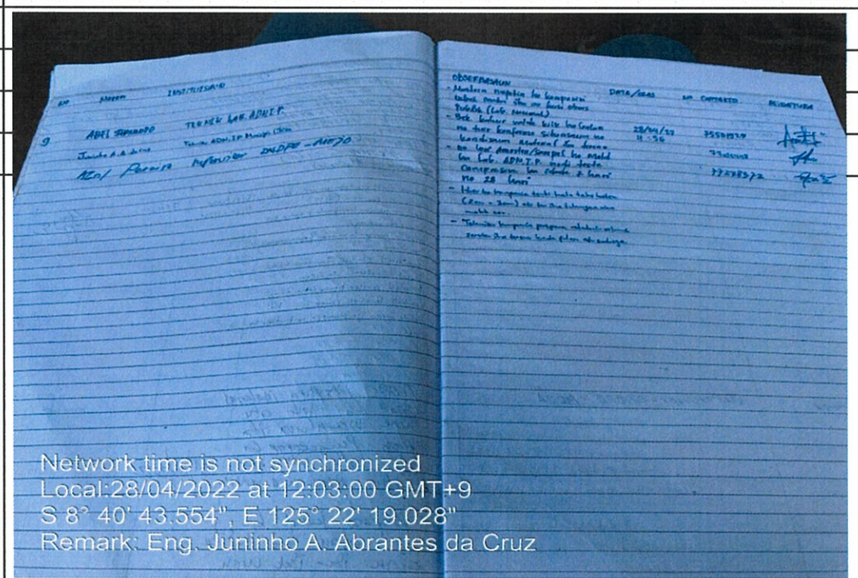No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/04/2022	Leorema, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		
II	28/04/2022	Leorema, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		

#ANEXU C1 – (BZT24)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Data Inspesaun : 26 Abril 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 39' 21. 442''**, Latetude : .....


End Point : Long : **E 125º 22' 51. 232''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

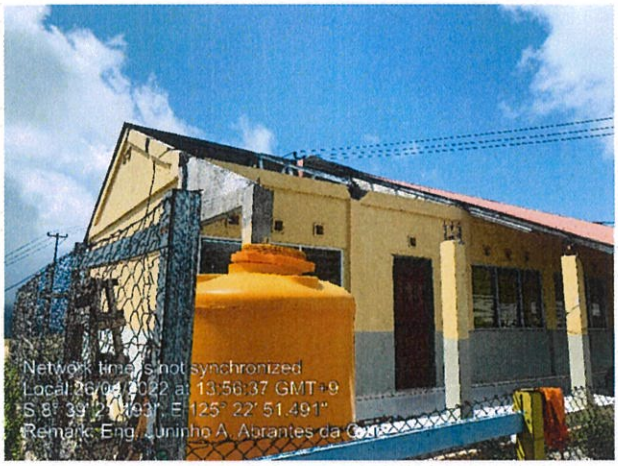Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu foun husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Baura lokaliza iha Leorema, Bazartete, Munisipiu Likisa projeitu nee kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (BZT24)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Wainhira ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun iha terenu, hatoo husi trabaliador/seguransa grupu nian katak servisu iha terenu paradu hela.	


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
	

#ANEXU C1 – (BZT24)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
	

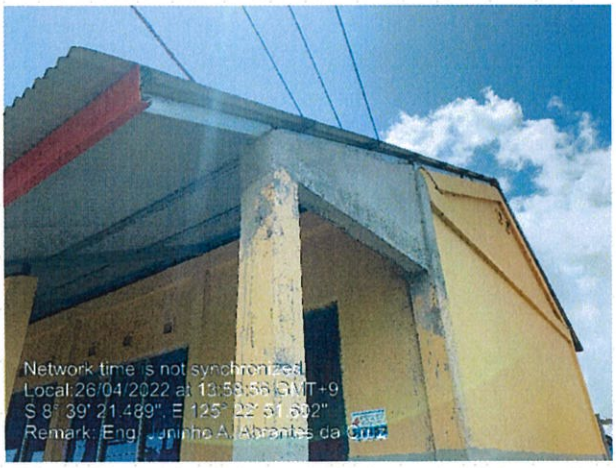Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
	

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : REHABILITAÇÃO ESCOLA PRE-ESCOLAR BAURA
FATIN PROJEITO : LEOREMA , BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (BZT24)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 1,970.00	$ 985.00	10.86%	$ -	0.00%					$ 985.00	10.86%
II	CLASSROOM BUILDING RF	RF/21	(i)	US$	$ 4,102.12	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 6,072.12	$ 985.00	10.86%	$ -	0.00%					$ 985.00	10.86%
B	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	GRAND TOTAL			US$	$ 9,072.12	$ 985.00	10.86%	$ -	0.00%					$ 985.00	10.86%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edifício Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edifício Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Data Inspesaun : 13 Abril 2022

Fatin Inspesaun : Fahilebo - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 38' 12. 154''**, Latetude : .....

End Point : Long : **E 125º 24' 35. 457''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu foun husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Ermeta Fahilebo iha suku Fahilebo, postu Bazartete, Likisa projeitu nee kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Iha loron neebe ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu refere, trabaliador grupu sira no ekipa grupu sira laiha terenu no laiha servisu iha terenu tanba iha aktividade relijioza suku nian.	


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tuir inspesaun neebe halo hamutuk ho tekniku projeitu nain munisipiu Likisa nian katak servisu lao kuaze too ona iha hada fatuk pondasi no mos pemadatan tanah kembali ba area klase nian.	

#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

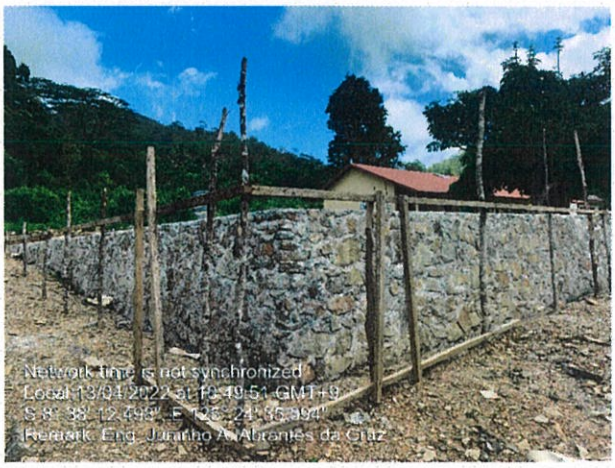

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



#ANEXU C1 – (BZT25)
Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Data Inspesaun : 26 Abril 2022

Fatin Inspesaun : Fahilebo - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 38' 12. 154''**, Latetude : .....

End Point : Long : **E 125º 24' 35. 457''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu foun husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Ermeta Fahilebo iha suku Fahilebo, postu Bazartete, Likisa projeitu nee kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (BZT25)
Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu grupu iha terenu lao ona too iha kesi besi (besi beton ulir 12 mm no besi beton polos 8 mm), hafoin grupu finaliza pengecoran ba kolom pendek. Iha mos mudansa ba diametru pondasi neebe la tuir dezeniu tanba tuir kondisaun iha terenu.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku grupu konsulta ho ekipa tekniku sira konaba design pipa hodi dada fiu eletrisidade neebe hatama husi tulangan nia laran, no tanba sira tauk dampak nee ba iha kekuatan beton, grupu mos sei kordena lai ho ekipa projeitu nain konaba asuntu nee.	

#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual



#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Data Inspesaun : 12 Abril 2022

Fatin Inspesaun : Maubara - Liquica

Koordinadas :

Start Point : Long : S 8° 36' 33. 682", Latetude : .....

End Point : Long : E 125° 13' 5. 010", Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa nian halao inspesaun ba projeitu MEJD PKRIE – Konstrusaun Foun ESG Classe Paralelo Maubara iha suku Maubara, postu Maubara, munisipiu Liquica. Neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (MBR19)

Back-up Data


Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa kordena ho tekniku projeitu nain munisipiu Likisa halao inspesaun ba projeitu MEJD PKRIE refere iha Maubara. Tanba kestaun rai projeitu ida nee lao tarde ituan.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu kee rai nian iha terenu tanba rai masin (area iha los Mota Masin Maubara), ho ida nee tekniku grupu ho nia trabaliador sira servisu ho kuidadu no detailiu liu ba servisu kee rai ninian.	

#ANEXU C1 – (MBR19)
Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

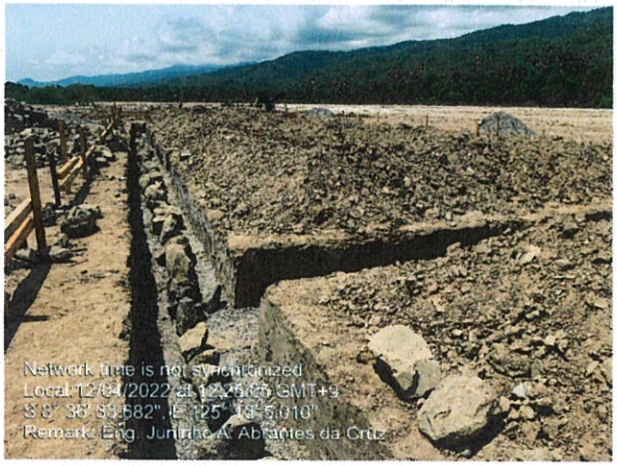Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu kee rai nian tuir design labele tun liu metru 1 ba fondasi lajur, no servisu urugan pasir kembali iha pondasi okos ho diametru 50mm sei uza stamper hodi halo pemadatan molok hatur fatuk pondasi.	
Ba servisu iha area haris fatin nian (toilet) nian mos grupu kee ona no iha instrusaun husi tekniku grupu lao tuir nia design.	

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA PRE-ESCOLAR ERMETA FAHILEBO
FATIN PROJEITO : FAHILEBO, BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (BZT25)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	BILLED %	THIS BILLING	BILLED %	TOTAL TO DATE	BILLED %
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00			$ 1,537.50	1.78%					$ 1,537.50	1.78%
II	CLASSROOM BUILDING C2	C2/47	(i)	US$	$ 59,793.47			$ 5,979.35	6.92%					$ 5,979.35	6.92%
III	PROVISIONAL SUM FOR SITE WORKS	SW/23	(i)	US$	$ 14,157.37			$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 77,025.84			$ 7,516.85	8.70%					$ 7,516.85	8.70%
B	OVERHEAD			US$	$ 6,340.00			$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00			$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 86,365.84			$ 7,516.85	8.70%					$ 7,516.85	8.70%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU D - (BZT25)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EPE ERMETA FAHILEBO

GRUPU KOMUNITARIU

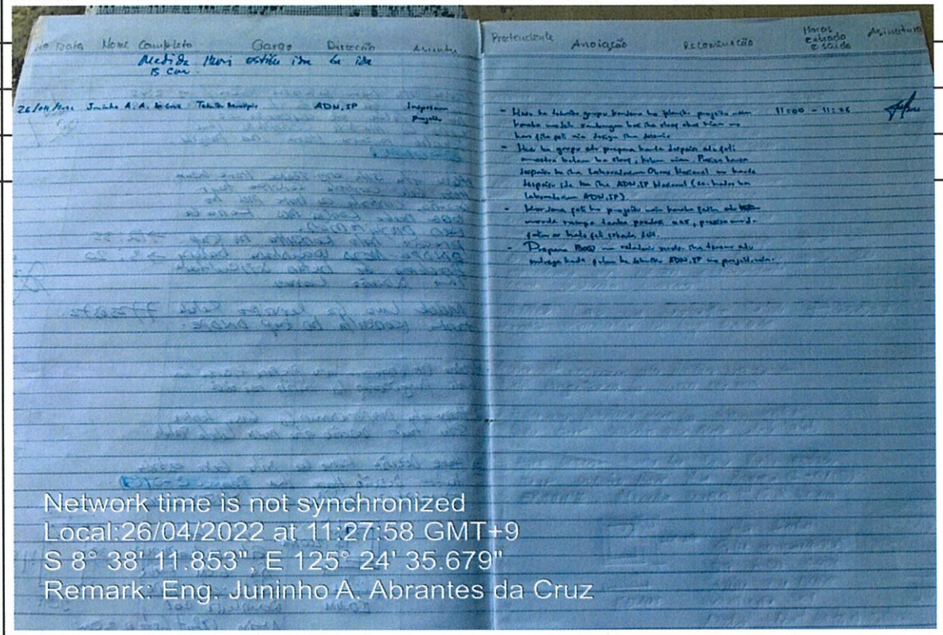No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/04/2022	Fahilebo, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5		

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Data Inspesaun : 12 Abril 2022

Fatin Inspesaun : Dato, Liquica

Koordinadas :

Start Point : Long : 8.35'21.273"S, Latetude : .....

End Point : Long : 125.20'1.933"E, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu husi Ministeriu Edukasaun Juventude no Desportu nian ba Konstrusaun Foun ESG Publico 01-Liquica lokaliza iha suku Dato, Liquica Vila, Munisipiu Likisa, neebe kaer husi kompania Roman Furak Unip. Lda.



#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu ba projeitu refere atinji ona iha servisu hada batako ho diametru (390 x 190mm) ho perbandingan pasangan 1:4. Ba servisu monta pipa (toilet) neebe halai husi rai okos no balu husi tulangan laran nian mos halo ona husi kompania.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu kesi besi ka monta besi ba beton polos diametru 8mm no besi beton ulir diametru 12mm, diametru ka jarak tulangan no sengkang nian mos tuir ona nia design.	

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

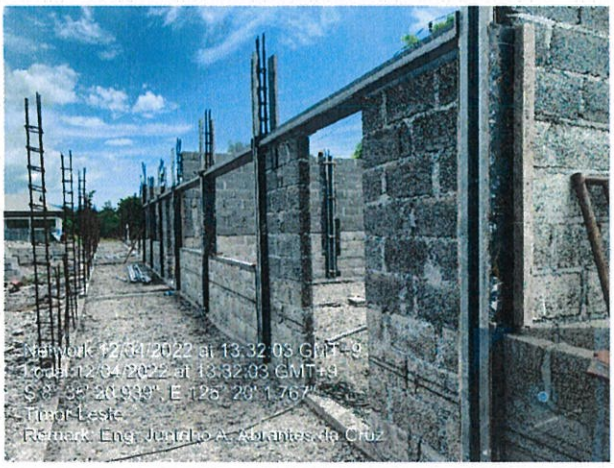Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Kompania mos monta ona bekisting ba kolom no sinta leten neebe halai husi area odamatan no janela. Bekisting ba lintel beam neebe cor iha kolom C4 nia leten mos monta ona.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba area klase C nian kompania atu finishing ona ba servisu pemadatan tanah kembali ba area klase laran nian. No sei kontinua ba servisu monta bekisting.	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

SUMMARY

Naran Projeitu : NOVA CONSTRUÇÃO ESCOLA SECUNDÁRIA GERAL LIQUIÇA
Fatin Projeitu : CAIMEO VILA, SUCO DATO
Projeitu Nain : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

ANEXU C2 - (LV20)			VERIFIED BY A D N , I P									
NO.	WORK DESCRIPTION	AMOUNT (USD)	PREVIOUS	BILLED (%)	THIS BILLING	BILLED (%)	TO DATE	BILLED (%)	PROGRESU IHA TERENU				BILLED (%)
									Fulan Kotuk	%	Fulan Ida Nee	%	
I	PRELIMINARIES	$ 2,870.00							$ 1,435.00	0.86%	$ -	0.00%	0.86%
II	CLASSROOM BUILDING C	$ 53,423.84							$ 10,684.77	6.40%	$ -	0.00%	6.40%
III	CLASSROOM BUILDING CB	$ 75,136.99							$ 15,027.40	8.99%	$ 11,270.55	6.75%	15.74%
IV	PROVISIONAL SUM FOR SITEWORKS	$ 13,000.00							$ -	0.00%	$ -	0.00%	0.00%
A	**CONSTRUCTION COST**	**$ 144,430.83**							**$ 27,147.17**	**16.25%**	**$ 11,270.55**	**6.75%**	**22.99%**
B	**CONTRACTOR FEE (10% x A)**	**$ 14,443.08**							**$ 2,714.72**	**1.62%**	**$ 1,127.05**	**0.67%**	**2.30%**
C	**OVERHEAD**	**$ 4,930.00**							**$ -**	**0.00%**	**$ -**	**0.00%**	**0.00%**
D	**TAX (2% x (A+B+C))**	**$ 3,276.08**							**$ 597.24**	**0.36%**	**$ 247.95**	**0.15%**	**0.51%**
E	**CONTIGENCY**	**$ -**							**$ -**	**0.00%**	**$ -**	**0.00%**	**0.00%**
F	**TOTAL COST (A+B+C+D)**	**$ 167,079.99**							**$ 30,459.12**	**18.23%**	**$ 12,645.56**	**7.57%**	**25.80%**

Inspeksaun Husi :

Eng, Juninho António Abrantes da Cruz
Engineru ba Edifisiu Publiku Agua Saneamentu, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineer ba Projeitu
Edificio Publiku Agua Saneamento
ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ
ADN, I.P.

#ANEXU D - (LV20)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran Projeitu: Projeitu Konstrusaun Foun ESG Publico 01-Liquica

Kompanha : ROMAN FURAK Unip. Lda.

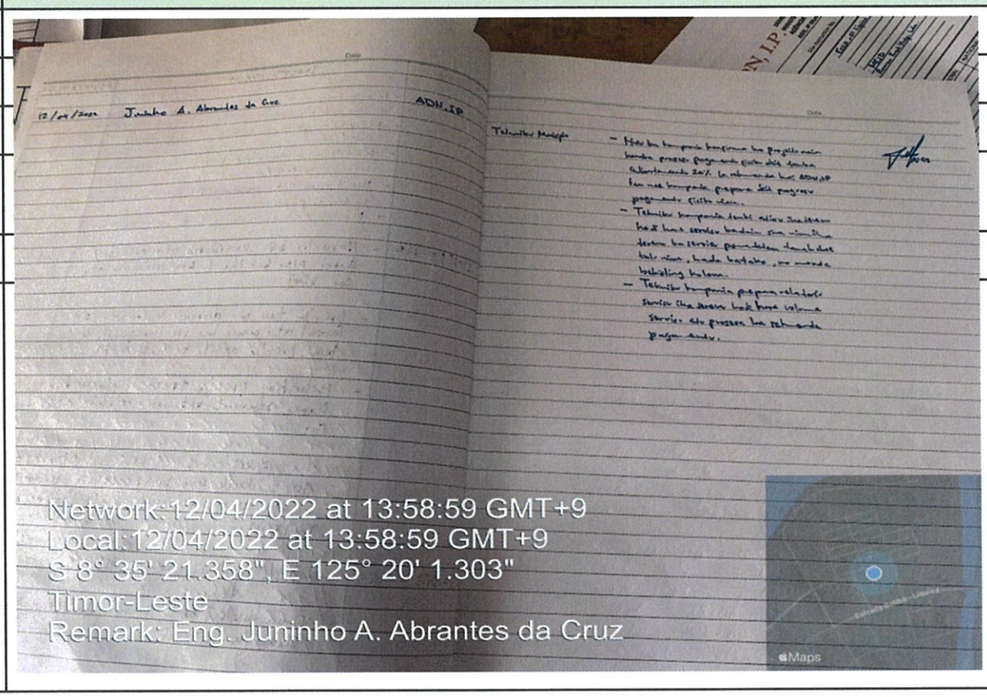No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12/04/2022	Dato, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquica	1 2 3 4 5 6		

#ANEXU C1 – (MBR18)

Back-up Data

Naran Projeto : **Konstrusaun Foun EBF 1,2 Tapo Manuhulu**
Kompania :
No. kontratu :

Data Inspesaun : 12 Abril 2022

Fatin Inspesaun : Gugleur, Maubara - Liquica

Koordinadas :

Start Point : Long : S 8° 43' 42. 194", Latetude : .....

End Point : Long : E 125° 9' 12. 256", Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa nian halao inspesaun ba projeitu MEJD PKRIE – Konstrusaun Foun EBF 1,2 Tapo Manuhulu lokaliza iha suku Gugleur, postu Maubara, munisipiu Liquica. Neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (MBR18)
Back-up Data

Naran Projeto : **Konstrusaun Foun EBF 1,2 Tapo Manuhulu**
Kompania :
No. kontratu :


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu grupu neebe lokaliza iha suku Gugleur lao ona durante semana ida ho balu, no konsisti husi Prezidenti Grupu, tekniku Grupu no estrutura seluk tan. Ekipa tekniku ADN, IP Munisipiu Likisa kordena ho tekniku projeitu nain munisipiu Likisa hodi halao inspesaun.	


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu grupu iha terenu ba kee rai nian kuaze finaliza ona, maibe iha problema ituan ho maneira servisu ba item urugan pasir kembali nian tanba grupu uza deit stamper manual neebe ladun foo rezultadu maksimu. Tan nee foo ona instrusaun atu uza stamper mesin molok kontinua servisu.	

#ANEXU C1 – (MBR18)

Back-up Data

Naran Projeto : **Konstrusaun Foun EBF 1,2 Tapo Manuhulu**
Kompania :
No. kontratu :

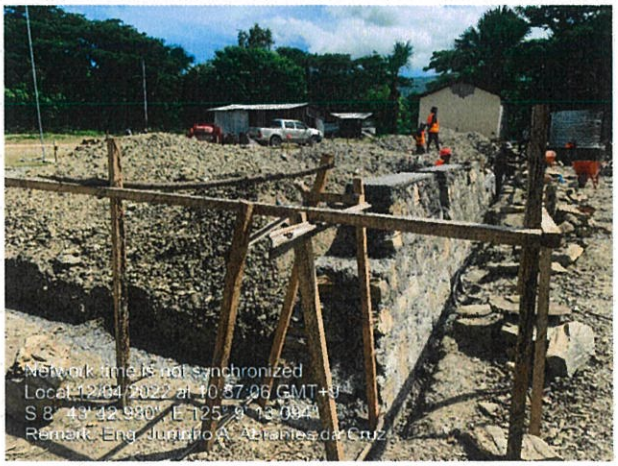Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu hada batako nian mos tenki para lai molok stamper mesin nian mai no halo tiha pemadatan ba urugan pasir 50mm nian. Tanba iha area balu hada ona batako, tekniku projeitu nain orienta ona grupu atu finaliza deit parte rohan nee.	

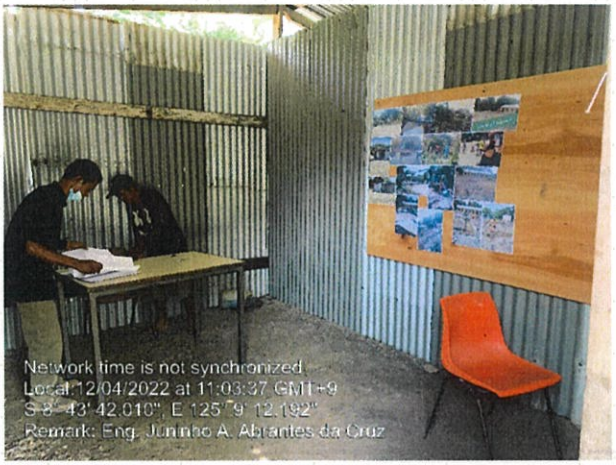Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa mos foo ona orientasaun ba grupu atu sira nia tekniku tenki ativu iha terenu, no atu monta/taka dezeniu no time schedule iha sira nia direksi site keet/site office.	

#ANEXU D - (MBR 18)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Konstrusaun Foun EBF 1,2 Tapo Manuhulu

Grupu Komunitariu

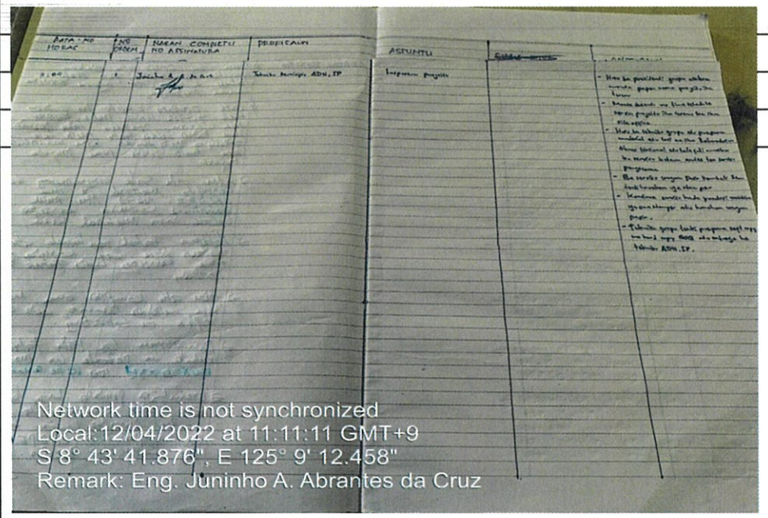No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12/04/2022	Gugleur, Maubara, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquica	1		
					2		
					3		
					4		
					5		

#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Data Inspesaun : 12 Abril 2022

Fatin Inspesaun : Maubara - Liquica

Koordinadas :

Start Point : Long : S 8º 36' 33. 682", Latetude : .....

End Point : Long : E 125º 13' 5. 010", Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Ekipa tekniku ADN, IP Munisipiu Likisa nian halao inspesaun ba projeitu MEJD PKRIE – Konstrusaun Foun ESG Classe Paralelo Maubara iha suku Maubara, postu Maubara, munisipiu Liquica. Neebe kaer husi servisu Grupu Komunitariu.



#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa kordena ho tekniku projeitu nain munisipiu Likisa halao inspesaun ba projeitu MEJD PKRIE refere iha Maubara. Tanba kestaun rai projeitu ida nee lao tarde ituan.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu kee rai nian iha terenu tanba rai masin (area iha los Mota Masin Maubara), ho ida nee tekniku grupu ho nia trabaliador sira servisu ho kuidadu no detailiu liu ba servisu kee rai ninian.	

#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

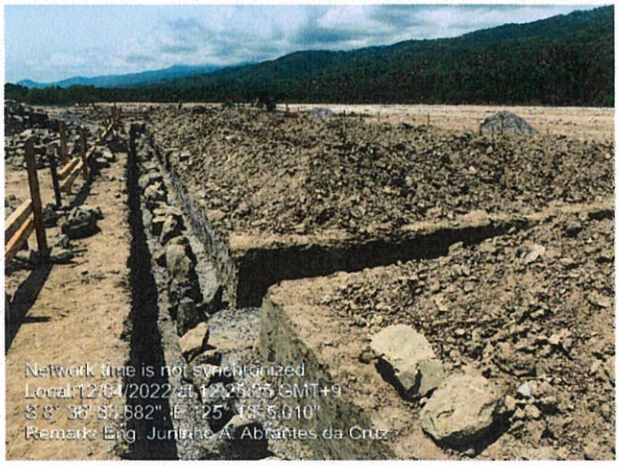Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Servisu kee rai nian tuir design labele tun liu metru 1 ba fondasi lajur, no servisu urugan pasir kembali iha pondasi okos ho diametru 50mm sei uza stamper hodi halo pemadatan molok hatur fatuk pondasi.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu iha area haris fatin nian (toilet) nian mos grupu kee ona no iha instrusaun husi tekniku grupu lao tuir nia design.	

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA SECUNDARIA GERAL PARALELO MAUBARA
FATIN PROJEITO : VAVIQUINA, MAUBARA
DONO DO PROJEITO : MINISTÉRIO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

ANEXU C2 - (MBR 19)						VERIFIED BY A D N , I P							
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	BILLED %	THIS BILLING	BILLED %	TOTAL TO DATE	BILLED %
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ -	0.00%	$ 1,537.50	1.09%					$ 1,537.50	1.09%
III	CLASSROOM BUILDING CA	CA/39	(i)	US$	$ 67,673.42	$ -	0.00%	$ 6,767.34	4.78%					$ 6,767.34	4.78%
IV	TOILET BUILDING Tb	TB/39	(i)	US$	$ 31,055.68	$ -	0.00%	$ 3,105.57	2.19%					$ 3,105.57	2.19%
V	PROVISIONAL SUM FOR SITE WORKS	SW/28	(i)	US$	$ 30,516.12	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 132,320.22	$ -	0.00%	$ 11,410.41	8.05%					$ 11,410.41	8.05%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 141,660.22	$ -	0.00%	$ 11,410.41	8.05%					$ 11,410.41	8.05%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edifisiu Publiku Agua Saneamentu, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku Agua Saneamentu, ADN, I.P

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P

#ANEXU D - (MBR 19)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Konstrusaun Foun ESG Classe Paralelo Maubara

Grupu Komunitariu

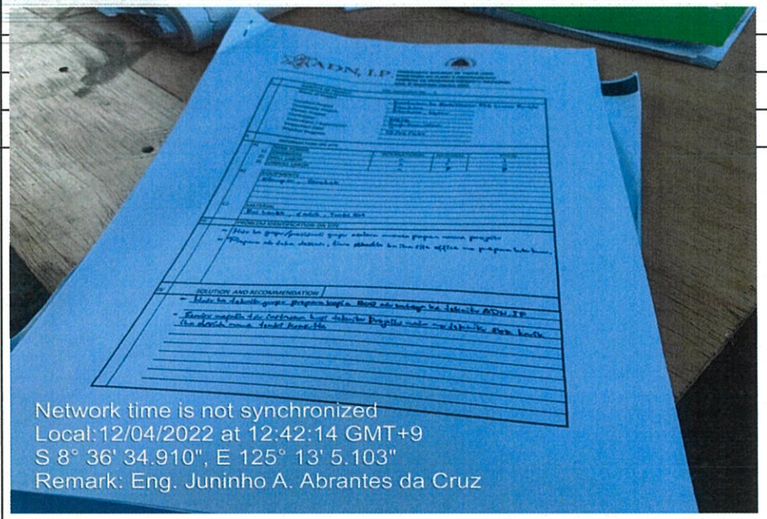No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12/04/2022	Maubara, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquica	1		
					2		
					3		
					4		
					5		

MINISTERIU INFRAESTRUTURA

ADN, I.P

PLANU INSPESAUN

Naran Eng. Marcos Ximenes de Araujo

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

ABRIL

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono de Projeto	Action	4	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Sector - Tibar - Liquica - Manleuana - Aileu (A04) & Caranbola - Loes (A03) Municipality Liquica 162	Naroman Motu Dadaun Unip Lda	MPW-W1/0250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													Pagamentu sedauk 100%
							Actual																												
	2	R4D Rural Road Periodic Maintenance Aileu - Asemana Chainage 0+000 - 4+300 Routine Maintenance Dato - Liquica - Loulidar Chainage 0+000 - 12+300 Municipality Liquica	Nheu	MPW-W-RFQ-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														PHO
							Actual																												
	3	Rural Roads Periodic Gasuba - Iskalai Chainge 0+000 & Metagou - Aberta Chainge 0+000 - 7+600 Rutine Maintenance Talitabi - Kabalau Chainge 0+000 - 16+700 Municipality Liquica (162)	Goubara Unip Lda	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														PHO
							Actual																												
	4	R4D Rural Road Rehabilitation Behasori - Tebekdak - Chainage 0+000 - 8+000 Liquica Municipality	15 Raofi Unip Lda	RT 034/MOP/2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	5	R4D Rural Road Spot Improvement Dato-Loulidar Chainage 0+000-12+300)	Luquefi Dan Unip Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	6	R4D Rural Road Spot Improvement Aileutu-Asantana Chainage 5+000-10+000)	Cailu Unip Lda	MPW-W-210134	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	7	R4D Rural Road Spot Improvement Aileutu-Asantana Chainage 0+000-5+000)	Victoriman Unip Lda	MPW-W-210135	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	8	R4D Rural Road Spot Improvement Metagou-Aberta Chainage 0+000-7+600)	Matelika Unipessoal Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	9	R4D Rural Road Spot Improvement Talitabi - Kabalau Chainage 0+000-16+700)	Prudencia Construction Unip Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	10	Manutensaun Kanale Irigasaun Faulara - Liquica	Banir Lema Unip Lda		LM	MINISTERIO AGRICULTURA E PESCAS	Plan																														EHO
							Actual																												
	11	R4D Rural Road Spot Improvement Berlakutalu-Laberlaku Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	12	R4D Rural Road Spot Improvement Berlakutalu-Laberlaku Chainage 2+500-5+000)	Claridade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	13	R4D Rural Road Spot Improvement Gasuba- Iskalai Chainge 0+000-2+000)	Craeleki Bercoli Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	14	Road Maintenance Sector a Tibar - Liquica - Manleuana - Caranbala - Loes (A03)	Chantel Chander Unip Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	15				LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																												
	16	Projetu Konstrusaun Foun ESG Fulbiku 01-Liquica	Roman Furak Unip Lda	NCB 16-MEJD-DNA-2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																												
	17	Tye Roads Maintenance Sector Tibar-Liquica-Manleuana-Caranbala-Loes (A03)	Chanel Chander Unip Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	4	Asfalt Frente Igue Manleuana	Fu Unip Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																												
	5	Road Link Corridor Rua Metinaro - Manatuto - Natarbora - Laclubar - Soibada - Same - Betano - Lospalos - Iliomar - Viqueque - Beacu - Suai - Cova Lima - Tilomar - Fatumean - Tasitolu - Dili - Manleuana - Liquica	Mahkana Dunk Unipessoal Lda	SNS 156/MOPTC/2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														Selvisu ba Tarefas 100% mas ho hein Fatin Pagamentu
							Actual																												
	3	Construcsaun ESTV Tasitolu - Manbaru Liquica (CA + CB)	Aloni Unip Lda	CBD 600 PDIM AM-LIQ VIII 2019 03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																												
	4	RNESP - Road Link No. A01 - 03 - Upgrading and Maintenance of Manbaru - Karambala Road (Km 49.7 to Km 54.1 and Km 58.1 to Km 62.6)and Aileu - Maubisse Road (Km 0.3 to Km 114.2)	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	RTB 077 MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														Ekipa ADN IP nebe maka tomia lotta Preciso IMPRESTIMO
							Actual																												
	5	R4D Rural Road Maintenance Berlakutalu - Laberlaku Chainage 0+000 - 4+400 Nemaleta - Darulema Chainage 0+000-14+600 Verugantu-Manbaru Chainage 0+000-12+300)	Luluna Unip Lda	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														PHO
							Actual																												
	6	R4D Rural Road Spot Improvement Berlakutalu - Laberlaku Chainage 0+000-4+500)	Nheu Unip Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	7	R4D Rural Road Spot Improvement Bandeira - Darulema Chainage 0+000-2+000 Liquica Municipality	Rito-Pu Unip Lda	MPW-W-210148	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	8	R4D Rural Road Spot Improvement Maloreca-Lesadila Chainage 0+000-5+000)	Malibu Unip Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	9	R4D Rural Road Spot Improvement Maloreca-Lesadila Chainage 0+000-14+600)	Murak Unip Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	10	R4D Rural Road Spot Improvement Berlaku - Verugantu - Maubisse - Chainage 8+000-12+500)	Mesa Lee Urae Baa Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	11	R4D Rural Road Spot Improvement Samaro-Goa Chainage 0+000-2+000)	Nazico Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	12	R4D Rural Road Spot Improvement Berlaku - Verugantu - Maubisse - Chainage 4+200-8+000)	Luluna Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	1	Rural Road Rehabilitation Metagou-Beasoleu 0+000 - 7+000 & Periodic Maintenance Maumeta - Metagou Sta 0+000 - 7+000 Municipality Liquica (162)	Banir Lema	MPW-W-190097	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														PHO
							Actual																												
	2	Konstruksaun CSTV Manleuana - Liquica (CA + CB)	Vida Diak Unip Lda	CBD 600 PDIM AM-LIQ VIII 2019 07	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																												
	3	R4D Rural Road Periodic Maintenance Tabilebo - Tahilebo Chainage 0+000 - 7+000 & Tahilebo - Laramasi Chainage 0+000 - 2+300 Routine Maintenance Laberlaku Bucumere Chainage 0+000 - 6+500 Municipality Liquica	Lep Leco Dato	MPW-W-190111	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																												
	4	Konstruksaun Meruhia Foun Manatuto - Tibar	Manoko Unip Lda	RDIT-MAP-PO2019/19726	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																														
							Actual																												
	5	Konstruksaun Foun EBE Hospital Referrale, Liquica (162)	Micha Unip Lda	(RFQ 19/029/Q-IR)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																												
	6	Hamaa Tasipi Tubuan Tratamento Agua Residuu Fatr Tibar - 162	Culoco Unipessoal Lda	Contract No MOP-W-190384	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																												
	7	New Water Supply of Bairos PNH Liquica	Holula Unipessoal Lda	SSS/054/MI-2019	IT	MINISTERIO DO INTERIOR	Plan																														
							Actual																												
	8	Konstruksaun Armagen Foun Mutuklauro (Hein Servisu)	Naesalobu	MAP-PO2019/19532	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																														
							Actual																												
	9	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																														
							Actual																												
	10	New construction of Isolation for covid 19 on the liquica Timor Leste	Senzu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																														
							Actual																												
	11	Kanalizasaun Be Mosu ba Sistema Oan-tasaun Ba Aipelo-Liquica	Tinoya	022/UM/RDTL/MPE-ASD/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																														
							Actual																												
	12	Emergency Project For Tibar River	Salu-Magu Unip Lda	RT 067/MOP/2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	13	R4D Rural Road Spot Improvement Tahilebo-Bucumere Chainage 0+000-3+000)	Hatumeta Oan Unip Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	14	R4D Rural Road Spot Improvement Tahilebo-Tatamasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan Unip Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	15	R4D Rural Road Spot Improvement Ububleu-Tahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	16	Routine Maintenance Maumeta-Metagou-Baurtete Chainage 0+000-D+000	Craeleki Bercoli Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
	17	R4D Rural Road Spot Improvement Tahilebo-Bucumere Chainage 3+000-6+500) Liquica Municipality	TM Caleba Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														On Going
							Actual																												
		TOTAL PROJETO ON-GOING																																		

Note:

Plano Periode inspesaun iha tereinu

Relatoriu avaliasaun mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Implementasaun Plano Periode inspesaun iha tereinu

Prepara Husi :

(Eng Marcos Ximenes de Araujo)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun Municipio

Sertifika Husi :

(Eng Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.I.P

Aprova Husi :

(Eng Januario Maia Guteres)
Adjunto Director Executivo ADN.I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERSO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Marcos Ximenes de Araujo
Municipio MUNICIPIO LIQUICA NO POSTOS

2022

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	ABRIL 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		Pagamentu seidauk 100%
							Actual		
	2	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	Nheu	MPW-W-RFQ-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		PHO
							Actual		
	3	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica (162)	Goubara Unip Lda	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		PHO
							Actual		
	4	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	5	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	6	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	7	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	8	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	9	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	10	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan		FHO
							Actual		
	11	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	12	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	13	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	14	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	15				LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	16	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip.Lda	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		
							Actual		
	17	For Roads Maintenance Section Tibar-Liquica-Maubara-Carimabala-Loes (A03)	Chanel Chander Unip.Lda	MPW-W210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip,Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	2	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	Montana Diak, Unipessoal, Lda	SSS/126/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		Setrvisu iha Tereno 100% ona no hein Pedido Pagamentu
							Actual		
	3	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		
							Actual		
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		Ekipa ADN.I.P nebe maka toma konta Projeito IMPRESTIMO
							Actual		
	5	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000-1+600 Vaviquinia-Maubaralisa Chainage 0+000-12+500	Luliana Unip.Lda	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		PHO
							Actual		
	6	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 0+000-4+200)	Nheu.Unip.Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	7	R4D Rural Road Spot Improvement Nunuleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip.Lda	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	8	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 4+800-9+600)	Malibo Unip.Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	9	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+000-4+800)	Murak.Unip.Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	10	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 8+400-12+500)	Meta Loe Crae Bau.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	11	R4D Rural Road Spot Improvement Samarapo-Gisu Chainage 0+000-2+000)	Nazico.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	12	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 4+200-8+400)	Luliana Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
Bazartete (BZT)	1	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica (162)	Banir Lema	MPW-W-190097	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		PHO
							Actual		
	2	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		
							Actual		
	3	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	Lep Laco Dato	MPW-W-190111	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		PHO
							Actual		
	4	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan		
							Actual		
	5	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip Lda	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan		
							Actual		
	6	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	7	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan		
							Actual		
	8	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan		
							Actual		
	9	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan		
							Actual		
	10	New construction of isolation for covid 19 in chi liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan		
							Actual		
	11	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan		
							Actual		
	12	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	13	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan.Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	14	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan.Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	15	R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	16	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
	17	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		On Going
							Actual		
TOTAL PROJETO ON-GOING									

Note:

Plano Periode inspesaun iha tereinu | Relatoriu avaliasuan mensal iha Dili | Inspesaun Pagamentu Anual iha tereinu | Implementasaun Plano Periode inspesaun iha tereinu | Iha Edifisio Municipio Liquica

Prepara Husi :

(Eng.Marcos Ximenes de Araujo)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun Municipio

Sertifika Husi :

(Eng.Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.I.P

Aprova Husi :

(Eng.Januario Maia Guteres)
Adjunto Director Executivo ADN.I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Juninho António Abrantes da Cruz
Municipio MUNICIPIO LIQUICA NO POSTOS
Municipio / Posto

2022

ABRIL

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Monu Dadaun Unip. Lda.	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	2	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	Nheu Unip. Lda.	MPW-W-RFQ-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	3	Rural Roads Periodic Gunaba - Lakulai Chainage 0+000 & Motagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica (162)	Goubara Unip. Lda.	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	4	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raohi Unip. Lda.	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	5	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luquoli Oan Unip. Lda.	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	6	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip. Lda.	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	7	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip. Lda.	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	8	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unip. Lda.	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	9	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip. Lda.	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	10	Manitensaun Kanais Irigasaun Faulara - Liquica	Banir Loma Unip. Lda.		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																													
							Actual																													
	11	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip. Lda.	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	12	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip. Lda.			MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	13	R4D Rural Road Spot Improvement Gunaba- Lakulai Chainage 0+000-2+000)	Craeleki Bercoli Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	14	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip. Lda.	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	15				LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	16	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip. Lda.	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													Iha loron 4 fulan nee la ba inspesaun tanba sei iha Nasional prepara relatoria. Iha loron 18 fulan nee feriadu. Iha loron 25 fulan nee la ba inspesaun tanba hatama relatoria fulan Marsu.
							Actual																													
	17	For Roads Maintenance Section Tibar-Liquica-Maubara-Carimbala-Loes (A03)	Chanel Chander Unip. Lda.	MPW-W210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	18	MEJD PKRIE EBF Mauboque	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	19	MEJD PKRIE EBC 1,2,3 Liquica	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	20	MEJD PKRIE EPE Loidahar	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	21	MEJD PKRIE EBF 1,2 Laoleroma	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	22	MEJD PKRIE EBF 1,2 Tolema	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	23	MEJD PKRIE EBF 1,2 Loculai	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip. Lda.		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	2	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	Montana Diak Unip. Lda.	SSS/126/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	3	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													On-going
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	5	R4D Rural Road Maintenance Berlakuidu - Laberlaka Chainage 0+000 - 5+400 Numuleta - Darulema Chainage 0+000-1+600 Vavisquinia-Maubaralisa Chainage 0+000-12+500	Luliana Unip. Lda.	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	6	R4D Rural Road Spot Improvement Barkau (Vavisquenia - Maubaralisa Chainage 0+000-4+200)	Nheu Unip. Lda.	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	7	R4D Rural Road Spot Improvement Numuleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip. Lda.	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	8	R4D Rural Road Spot Improvement Malaisera-Lisadila Chainage 4+800-9+600)	Malibo Unip. Lda.	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	9	R4D Rural Road Spot Improvement Malaisera-Lisadila Chainage 0+000-4+800)	Murak Unip. Lda.	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	10	R4D Rural Road Spot Improvement Barkau (Vavisquenia - Maubaralisa Chainage 8+400-12+500)	Meta Loe Crae Bau Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	11	R4D Rural Road Spot Improvement Samarapo-Giuu Chainage 0+000-2+000)	Nazico Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	12	R4D Rural Road Spot Improvement Barkau (Vavisquenia - Maubaralisa Chainage 4+200-8+400)	Luliana Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	13	MEJD PKRIE EBF Gariana	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	14	MEJD PKRIE EBF 1,2 Tapo Manubulu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	15	MEJD PKRIE ESG-Paraleio Maubara	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
Bazartete (BZT)	1	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica (162)	Banir Loma Unip. Lda.	MPW-W-190097	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	2	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													PHO
	3	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	Lep Laco Dato Unip. Lda.	MPW-W-190111	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	4	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda.	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																													
							Actual																													Paradu
	5	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip. Lda.	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Paradu
	6	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Cidoco Unip. Lda.	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													Pagamentu Seidauk 100%
	7	New Water Supply of Bairos PNTL Liquica	Hohuli Unip. Lda.	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																													
							Actual																													PHO
	8	Konstrusaun Armagem Foun Matadouro (Bem Servisu)	Naosalobu Unip. Lda.	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																													
							Actual																													Pagamentu Seidauk 100%
	9	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Quosson SQ Unip. Lda.	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																													
							Actual																													Pagamentu Seidauk 100%
	10	New construction of isolation for covid 19 in chi liquica, Timor Leste	Soniziu Unip. Lda.	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																													
							Actual																													PHO
	11	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Timocya Unip. Lda.	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDP/CIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																													
							Actual																													PHO
	12	Emergency Project For Tibar River	Sali-Magu Unip. Lda.	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	13	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan Unip. Lda.	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	14	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan Unip. Lda.	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	15	R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip. Lda.	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	16	Routine Maintenance Maumeta-Motagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	17	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba Unip. Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																													
	18	New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta	Biamali Unip. Lda.	RDTL-MS-C19-DNA-DC-21-233	LM	MINISTERIO SAUDE	Plan																													
							Actual																													Iha loron 11 no 13 fulan nee la ba inspesaun tanba hadia relatoriu no inspesaun ba fali projeitu PKRIE foun. Iha loron 18 fulan nee feriadu.
	19	Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica	Zyc Unip. Lda.	RDTL-MS-C19-DNA-DC-21-228	LM	MINISTERIO SAUDE	Plan																													
							Actual																													Iha loron 11 no 13 fulan nee la ba inspesaun tanba hadia relatoriu no inspesaun ba fali projeitu PKRIE foun. Iha loron 18 fulan nee feriadu.
	20	Projeitu Konstrusaun Foun ESTV Loorema - Liquica	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Iha loron 7 fulan nee la ba inspesaun tanba lisensa. Iha loron 14 no 21 fulan nee la ba inspesaun tanba kareta la ba munisipiu.
	21	MEJD PKRIE EPE Baura	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	22	MEJD PKRIE EPE Ermeta	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	23	MEJD PKRIE EPE Cassait	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
	24	MEJD PKRIE ESG-Paraldo Bogoro	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																													Foun
TOTAL PROJETO ON-GOING																																			

Note:

Plano Periode inspesaun iha tereinu | Relatoriu avaliasaun mensal iha Dili | Inspesaun Pagamentu Anual iha tereinu | Implementasaun Plano Periode inspesaun iha tereinu

Prepara Husi :

(Eng Juninho António Abrantes da Cruz)
Eng. ba Edifício Publico Agua e Saneamento Municipio Liquica
ADN, I.P

Sertifika Husi :

(Eng Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun do Qualidade ADN.I.P

Aprova Husi :

(Eng Januario Maia Guterres)
Adjunto Diretor Executivo ADN.I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
V.T GOVERNO CONSTITUCIONAL

PLANU INSPESAUN

Naran Eng. Juninho António Abrantes da Cruz

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

ABRIL

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	OBS
Liquica Vila (LLV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naromas Mono Dadaun Unip. Lda.	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	2	R4D Rural Road Periodic Maintenance Albern - Asumanu Chainage 0+000 - 4+300 Ruline Maintenance Dato - Liquica - Loidahar Chainge 0+000 - 12+300 Municipality Liquica	Nhoe Unip. Lda.	MPW-W-RFQ-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	3	Rural Roads Periodic Gasabu - Lukulai Chainage 0+000 & Metagou - Albern Chainage 0+000 - 7+600 Rotine Maintenance Talbabi - Kutulau Chainge 0+000 - 1+700 Municipality Liquica (162)	Goubara Unip. Lda.	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	4	R4D Rural Road Rehabilitation Bibadiri - Labakalaku Chainge 0+000 - 5+000 Liquica Municipality	15 Raebi Unip. Lda.	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	5	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Liquchi Oan Unip. Lda.	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	6	R4D Rural Road Spot Improvement Albern- Asumanu Chainage 5+000-10+000)	Cadia Unip. Lda.	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	7	R4D Rural Road Spot Improvement Albern- Asumanu-Laupasa Chainage 0+000-5+000)	Vicenotmo Unip. Lda.	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	8	R4D Rural Road Spot Improvement Metagou-Albern Chainage 0+000-7+600)	Modifica Unip. Lda.	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	9	R4D Rural Road Spot Improvement Talbabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip. Lda.	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	10	Manutensaun Kanais Irigatasn Faulara - Liquica	Basic Lorsa Unip. Lda.		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																														
							Actual																														
	11	R4D Rural Road Spot Improvement Borlaksida-Laberlaka Chainage 0+000-2+500)	Goubara Unip. Lda.	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	12	R4D Rural Road Spot Improvement Borlaksida-Laberlaka Chainage 2+500-5+400)	Claridade Unip. Lda.			MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	13	R4D Rural Road Spot Improvement Gusabu- Lukulai Chainage 0+000-2+000)	Cruciobi Borcoli Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	14	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chandor Unip. Lda.	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	15				LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	16	Projeito Konstrusaun Foun ESG Publico 01-Liquica	Romana Fursk Unip. Lda.	NCB/16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going
							Actual																														
	17	For Roads Maintenance Section Tibar-Liquica-Maubara-Carimbala-Loes (A03)	Chanel Chandor Unip. Lda.	MPW-W/210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	18	MEJD PKRIE EBF Mauboque	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	19	MEJD PKRIE EBC 1,2,3 Liquica	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	20	MEJD PKRIE EPE Loidahar	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	21	MEJD PKRIE EBF 1,2 Lecleleena	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	22	MEJD PKRIE EBF 1,2 Tolama	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	23	MEJD PKRIE EBF 1,2 Lisculai	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
Maubara (MBR)	1	Addt. Ponte liga Maubara	Fu Unip. Lda.		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	2	Road and Drainage Rehabilitation Project Emergency Road at Tibulau and Karimbala Liquica Municipality Liquica	Montana Diak Unip. Lda.	SSS/126/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	3	Konstrusaun ESTV Lisadida Maubara-Liquica (CA + CB)	Akosi Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														On-going
							Actual																														
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km 54.1 and Km.58.1 to Km. 62.6)and Atabae - Motu Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Ltd Jv Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	5	R4D Rural Road Maintenance Borlaksida - Laberlaka Chainage 0+000 - 5+400 Nunoleta - Darulema Chainage 0+000-1+600 Vaviquinia-Maubaralau Chainage 0+000-12+500	Lulisna Unip. Lda.	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	6	R4D Rural Road Spot Improvement Barkau (Vaviquonia - Maubaralau Chainage 0+000-4+200)	Nhoe Unip. Lda.	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	7	R4D Rural Road Spot Improvement Nunoleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip. Lda.	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	8	R4D Rural Road Spot Improvement Malaisera-Lisadida Chainage 4+800-9+600)	Malibo Unip. Lda.	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	9	R4D Rural Road Spot Improvement Malaisera-Lisadida Chainage 0+000-4+800)	Morok Unip. Lda.	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	10	R4D Rural Road Spot Improvement Barkau (Vaviquonia - Maubaralau Chainage 8+400-12+500)	Meta Loc Crac Bau Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	11	R4D Rural Road Spot Improvement Sumarapo-Gisa Chainage 0+000-2+000)	Nezico Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	12	R4D Rural Road Spot Improvement Barkau (Vaviquonia - Maubaralau Chainage 4+200-8+400)	Lulisna Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	13	MEJD PKRIE EBF Gariana	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	14	MEJD PKRIE EBF 1,2 Tapo Manubulu	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
	15	MEJD PKRIE ESG-Puraldo Maubara	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														
Bazartete (BZT)	1	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica (162)	Banir Lorsa Unip. Lda.	MPW-W-190097	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	2	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda.	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														PHO
							Actual																														
	3	R4D Rural Road Periodic Maintenance Libelen - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Clwinage 0+000 - 6+500 Municipality Liquica	Lep Laco Dato Unip. Lda.	MPW-W-190111	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	4	Konstrusaun Moralha Foun Matadoro Tibar	Maneku Unip. Lda.	RDTL-MAP-F02019/19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																														
							Actual																														
	5	Konstrusaun Foun EBF Hotugau Bazartete, Liquica (162)	Mikiba Unip. Lda.	(RFQ/19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	6	Hanoo Tangki Estasun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unip. Lda.	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														Pagamentu Seidauk 100%
							Actual																														
	7	New Water Supply of Bairos PNTL Liquica	Holuli Unip. Lda.	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																														PHO
							Actual																														
	8	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesaloba Unip. Lda.	MAP-F02019/19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																														Pagamentu Seidauk 100%
							Actual																														
	9	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Queson SQ Unip. Lda.	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																														Pagamentu Seidauk 100%
							Actual																														
	10	New construction of isolation for covid 19 in chi liquica, Timor Leste	Seniru Unip. Lda.	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																														PHO
							Actual																														
	11	Kanalizasaun Ba Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya Unip. Lda.	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																														PHO
							Actual																														
	12	Emergency Project For Tibar River	Sidi-Magu Unip. Lda.	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	13	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hahameta Oan Unip. Lda.	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	14	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatimeta Oan Unip. Lda.	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	15	R4D Rural Road Spot Improvement Libelou- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip. Lda.	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	16	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+600	Craolcki Borcoli Unip. Lda.		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	17	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Cailoba Unip. Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	18	New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta	Bianuli Unip. Lda.	RDTL-MS-C19-DNA-DC-21-233	LM	MINISTERIO SAUDE	Plan																														Foun
							Actual																														
	19	Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica	Zye Unip. Lda.	RDTL-MS-C19-DNA-DC-21-228	LM	MINISTERIO SAUDE	Plan																														Foun
							Actual																														
	20	Projeito Konstrusaun Foun ESTV Leorema - Liquica	U-Rana Unip. Lda.	NCB/15/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														Foun
							Actual																														

21	MEJD PKRIE EPE Ilaura	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan Actual		Foun
22	MEJD PKRIE EPE Ermera	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan Actual		Foun
23	MEJD PKRIE EPE Cassait	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan Actual		Foun
24	MEJD PKRIE ESG-Paraiclo Bogoro	Grupu Komunitariu		LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan Actual		Foun
	TOTAL PROJETO ON-GOING							

Note:

Plano Periode Inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Implementasaun Plano Periode Inspesaun iha tereinu

Prepara Husi :

(Eng Juninho Antônio Abrantes da Cruz)
Eng. ba Edifício Publico Agua e Saneamento Municipio Liquica
ADN, I.P

Sertifika Husi :

(Eng.Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.I.P

Aprova Husi :

(Eng.Januario Vania Guteres)
Adjunto Director Executivo ADN.I.P

ANEXO

Back-up Data

Naran Projeto : Fatin Ceremonia Tomada de Pose Presidente Republica de Timor Leste, dia 20 de Maio 2022 - Dili Municipality

No. kontratu :

Data Inspesaun : Fulan Abril & Maiu

Fatin Inspesaun : Tasi Tolu - Dili Municipality

Start Point : Long : , Latetude :

End Point : Long : ....., Latetude : .....


Naran Inspector : 1.Camilio De Jesus

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

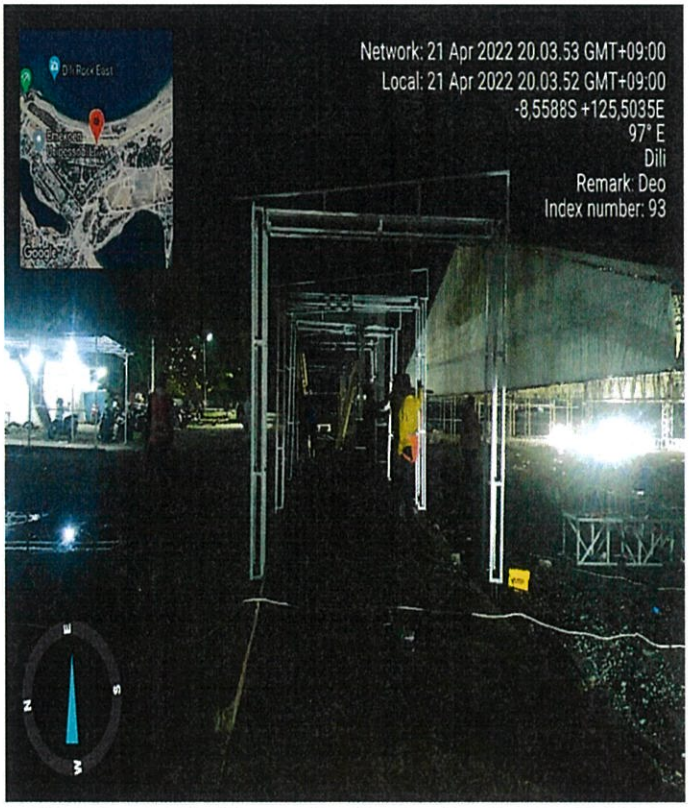

ANEXO

Back-up Data

Naran Projeto : Fatin Ceremonia Tomada de Pose Presidente Republica de Timor Leste, dia 20 de Maio 2022 - Dili Municipality

No. kontratu :



Kompanhia Instala Ligting




Kompanhia Instala Kabel Power

ANEXO


Back-up Data

Naran Projeto : Fatin Ceremonia Tomada de Pose Presidente Republica de Timor Leste, dia 20 de Maio 2022 - Dili Municipality

No. kontratu :

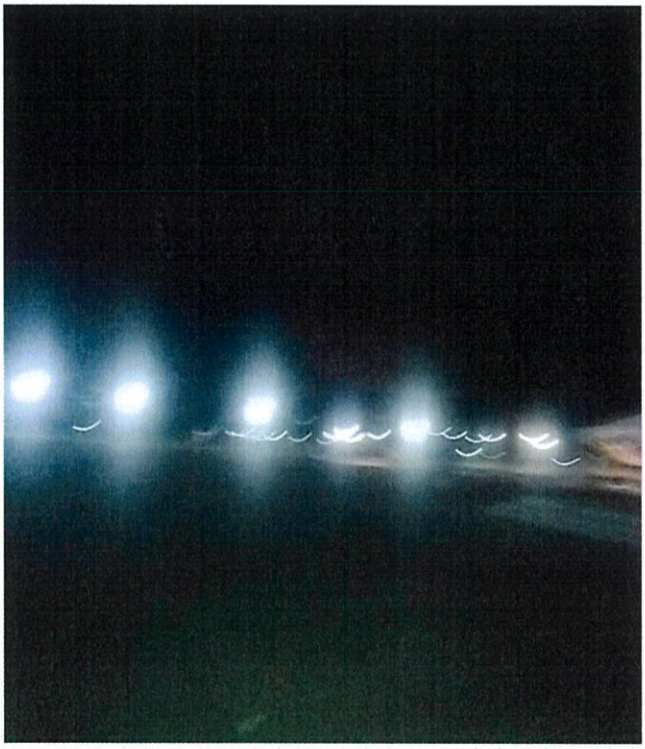

Kompanhia Instala Street Light

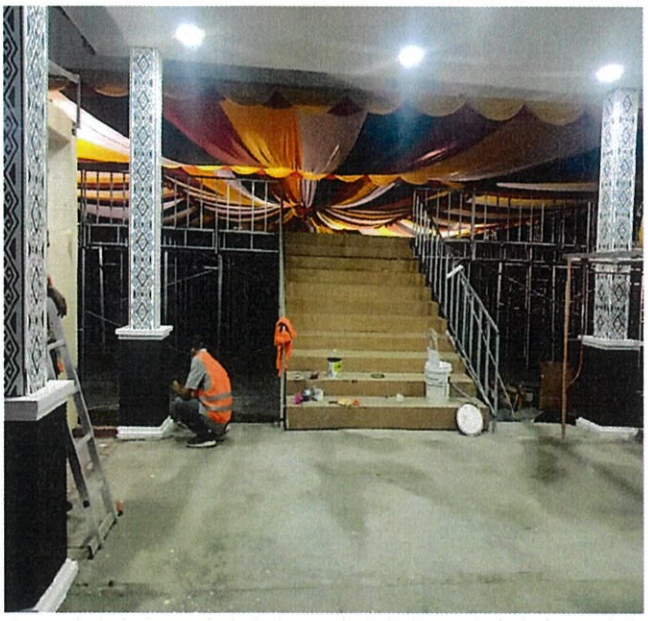

Kompanhia Insta dowlight Coridor VIP

ANEXO

Back-up Data

Naran Projeto : Fatin Ceremonia Tomada de Pose Presidente Republica de Timor Leste, dia 20 de Maio 2022 - Dili Municipality

No. kontratu :



Kompanhia Insta dowlight Coridor VIP



Kompanhia Insta dowlight Coridor VIP

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOV. BNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng.	Camilio de Jesus
Municipio	MUNICIPIO LIQUICA NO POSTOS

2022

ABRIL

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	fr 29	Sa 30	OBS
Liquica Vila (LV)	8	New Installation MV, LV LIne and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	9	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	10	Konstrusaun ka Reabilitasaun ba EPE Baura	EJD PKRIE EPE BAURA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	11	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MEJD PKRIE EPE ERMETA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	12	Konstrusaun ka Reabilitasaun ba EPE Cassait	MEJD PKRIE EPE CASSAIT		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	13	Konstrusaun ka Reabilitasaun ba EBF Gariana	MEJD PKRIE EBF GARIANA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
Maubara(MBR)	2	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	3	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MEJD PKRIE EBF MAUBOQUE		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba
							Actual																														
	4	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MEJD PKRIE EBC 1,2,3 LIQUIÇA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	5	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MEJD PKRIE EBF 1,2 TAPO MANUHULU		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba
							Actual																														
	6	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MEJD PKRIE EPE LOIDAHAR		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
Bazartete (BA)	1	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclolema	MEJD PKRIE EBF 1,2 LACLOLEMA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	2	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MEJD PKRIE EBF 1,2 TOLEMA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba
							Actual																														
	3	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MEJD PKRIE ESG-PARALELO MAUBARA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	4	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MEJD PKRIE ESG-PARALELO BOGORO		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
	5	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MEJD PKRIE EBF 1,2 LUCULAI		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														La ba halo monitorisasaun tamba actividade iha tasi Tolu konaba preparasaun 20 Mei 2022
							Actual																														
TOTAL PROJETO ON-GOING																																				

Note:

Plano Periode Inspesaun iha tereinu | Relatoriu avaliasuan mensal iha Dili | Implementasaun Plano Periode Inspesaun iha tereinu | Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Camilio de Jesus)
Tekniku M& E ADN.IP

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.IP

Aprova Husi :

(Eng Januario Maia Guterres)
Adjuntu Director Executivo ADN.IP

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Camilio de Jesus

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	ABRIL																												OBS
								fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
Liquica Vila (LV)	8	New Installation MV, LV LIne and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	9	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	10	Konstrusaun ka Reabilitasaun ba EPE Baura	EJD PKRIE EPE BAURA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	11	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MEJD PKRIE EPE ERMETA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	12	Konstrusaun ka Reabilitasaun ba EPE Cassait	MEJD PKRIE EPE CASSAIT		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	13	Konstrusaun ka Reabilitasaun ba EBF Gariana	MEJD PKRIE EBF GARIANA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
Maubara(MBR)	2	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	3	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MEJD PKRIE EBF MAUBOQUE		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	4	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MEJD PKRIE EBC 1,2,3 LIQUIÇA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	5	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MEJD PKRIE EBF 1,2 TAPO MANUHULU		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	6	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MEJD PKRIE EPE LOIDAHAR		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
Bazartete (BA)	1	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclolema	MEJD PKRIE EBF 1,2 LACLOLEMA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	2	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MEJD PKRIE EBF 1,2 TOLEMA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	3	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MEJD PKRIE ESG-PARALELO MAUBARA		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	4	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MEJD PKRIE ESG-PARALELO BOGORO		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
	5	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MEJD PKRIE EBF 1,2 LUCULAI		LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															
TOTAL PROJETO ON-GOING																																				

Note:

Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Implementasaun Plano Periode inspesaun iha tereinu

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Camilio de Jesus)
Tekniku M&E ADN.IP

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.IP

Aprova Husi :

(Eng Januario Maia Guterres)
Adjuntu Director Executivo ADN.IP
