REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE

MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público

A.D.N, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

RELATÓRIU MENSÁL IMPLEMENTASAUN PROJETUS MUNISÍPIU BAUCAU

JULHO 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTASAUN PROJETU INFRAESTRUTURA IHA MUNICIPIO BAUCAU

JULHO 2022

Prepara Husi :

(Eng. Agustinho Aranda)
Eng. ba Porjecto Edificio Publico Beé no Saneamento Municipio Baucau, ADN,I.P.

(Eng. Jacob da Costa Camoês)
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Baucau, ADN, I.P.

(Eng. Jerry Gil M. Pereira)
Eng. ba Porjecto Edificio Publico Beé no Saneamento Municipio Baucau,ADN, I.P.

(Eng. Leonito Pereira)
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Baucau, ADN, I.P.

(Eng. Adonis Julio Fernades)
Eng. ba Projeito ME, ADN, I.P.

Verifika Husi :

(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edificio Publiku no Beé Saneamentu, ADN, I.P.

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba Projetu Infraestrutura e Irigasaun, ADN, I.P.

(Eng. Deolindo de F. Marques)
Chefe Seksaun ba Projetu M.E & ITC, ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P.

Aprova Husi :

(Mariano Renato Monteiro da Cruz, ST., M. Eng)
Director Executivo, ADN, I.P.

INDICE

SUMÁRIO 1

INDICE 3

I. INTRODUSAUN 3

1.1 Enkuadramentu Legal 3

1.2 Perfil Municipio Baucau 3

1.3. Lista Projectos 8

II. PROGRESU FISIKU 28

2.1 Progresso Fisiku Kada Fulan 28

III. OBSTÁCLO IHA TERENU 29

3.1 Obstáclo Servisu Iha Terenu 29

IV. REKOMENDASAUN IHA TERENU 30

4.1 Rekomendasaun Servisu Iha Terenu 30

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias 4

Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Baucau 6

Tabela 1.2 : Lista Asset ADN,I.P Municipio Baucau 6

Tabela 1.3.1 : Projecto Municipio Baucau Por Fundus Finansiamentos 8

Tabela 1.3.2 : Projecto Municipio Baucau Por Sectores 12

Tabela 1.3.3 : Projecto Municipio Baucau Por Ministerio 20

Tabela 1.4 : Dadus Populasaun Munisipiu Baucau 28

I. INTRODUSAUN.

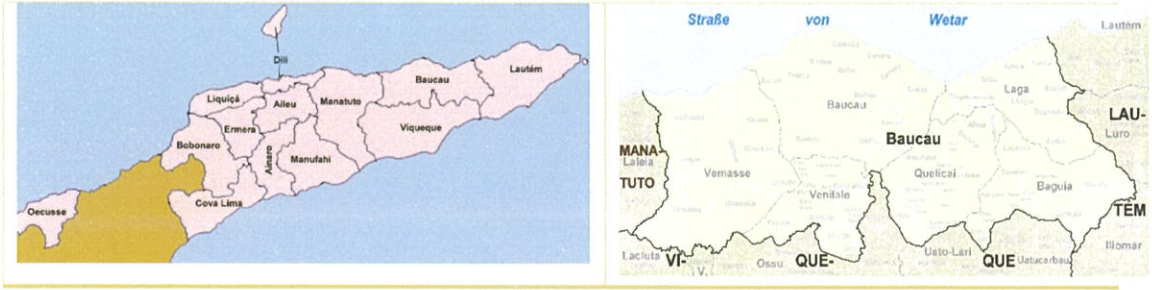
1.1.Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análize kustu-benefísiu ne'ebe razoável no viavél.

Depois de Dekretu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimentu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projetu sira iha programa Kapital Desenvolvimentu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2. Perfil Municipio Baucau



Mapa 3 hatudu pozisaun jeográfika Autoridade Munisipal Baucau ne'ebé ho luan área hamutuk 1,494 km² ho populasaun 111,694 tuir Sensus 2010. Autoridade Munisipal Baucau iha Posto Administrativo neen (6) ho 59 Sukus no 282 Aldeias hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos,Sucos no Aldeias.

Baguia		Baucau		Laga		Quelicai	
Sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**
Afaloicai	4	Bahu	5	Atelari	10	Abafala	3
Alaua craic	5	Bucoli	6	Libagua	5	Abo	4
Alaua leten	5	Buibau	6	Nunira	5	Afaca	3
Defa-uassi	4	Buruma	4	Saelari	9	Baguia	3
Haeconi	6	Caibada(Uaima)	7	Sagadati	11	Bualale	2
Larisula	7	Gariuai	8	Samalari	7	Guruca	5
Lavateri	5	Samalari	4	Soba	6	lacoliu	3
Osso huna	3	Seiçal	5	Tequi naumata	5	Laisoro Lai de baixo	4
Samalari	4	Trilolo	6	-	-	Laisorolai De cima	3
Uacala	4	Triloca	4	-	-	lelalai	4
-	-	Ualili	10	-	-	Letemumo	5
-	-	-	-	-	-	Macalaco	3
-	-	-	-	-	-	Maluro	4
-	-	-	-	-	-	Namanei	4
-	-	-	-	-	-	Uaitame	4
Total	**48**		**65**		**58**		**54**

Vemasse		Venilale	
sukus	**Aldeia**	**Suku**	**Aldeia**
Caicua	2	Bado-Ho'o	5
Loilubo	3	Baha Mori	6
Ossouala	5	Fatulia	4
Ostico	3	Uailaha	4
Uaigae	2	Uai-Oli	4
Uatulari	3	Uatu Hoco	4
Vemasse	4	Uma AnaUlo	4
-	-	Uma Ana Ico	4
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
	22		**35**

Tabela 1.1: Forca de Trabalho ADN, I.P Municipio Baucau

Forca de Trabalho ADN,I.P **Municipio Baucau**							
No	Deskrisaun	Total Membros Kada Tinan					
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	**3**	**2**				**3**	
2	Administrasaun no Financas	**0**	**0**				**0**	
3	Motorista	**1**	**1**				**1**	
4	Seguransa	**0**	**0**				**0**	
Total		**4**					**4**	

Tabela 1.2 : Lista Asset ADN,I.P Municipio Baucau.

ASET ADN,IP MUNICIPIO BAUCAU								
No	**Deskrisaun**	**Total Aset Kada Tinan**					**Total**	**OBS**
		2021	**2022**	**2023**	**2024**	**2025**		
1	Edificio	1	1				**1**	
2	Kareta	1	1					
3	Desktop HP / Monitor	0	0					
4	Laptop HP	2	2					
5	Printer Cannon	1	1					
6	UPS	0	0					
7	Armario File	1	1					
8	Armario Tau hena	3	3					

9	Meja escritorio	1	1					
10	Meja han	1	1					
11	Meja TV (kiik)	1						
12	Kadeira escritorio	6	6					
13	Kadeira han	4	4					
14	Sofa	1 Set	1					
15	Springbed +sumasu 4+sprei 3	3 Set	1					
16	Jeleira	1	1					
17	Water Dispenser	1	1					
18	TV + Parabola	1 Set	1					
19	AC	4	4					
20	Kompor	0	0					
21	Kompor Gas	0	0					
22	Rack sepatu	0	0					
23	Rack Piring	0	0					
24	Water Pump Sanyo	1	1					

1.3 : Lista Projectos

Projetu hotu ne'ebe akumula iha lista ne'e bazeia ba dadus projetu ne'ebe sei lao hela no mos projeto ne'ebe abandona ona tinan barak, projeto hirak ne'e fahe tuir lista 1.3.1 Projeto Por Fundus Finansiamentos, 1.3.2 Projeto Por Sectors no 1.3.3 Projeto Por Ministerios.

1.3.1 : Lista Projectos Municipio Baucau Por Fundus Finansiamentos

NO	POSTO ADMINISTRATIVO	TOTAL FI+Fundu Covid-19+LM-BS+LM-CD+LM-TP+PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	14	$ 2,230,497.80	45.39%
2	Baucau Villa	20	$ 10,638,283.98	52.62%
3	Laga	11	$ 2,698,206.10	48.50%
4	Multi Posto	6	$ 110,461,376.54	73.18%
5	Quelicai	16	$ 9,587,999.47	65.67%
6	Vemasse	7	$ 1,824,722.56	42.66%
7	Venilale	11	$ 6,830,895.16	36.95%
	Grand Total	85	$ 144,271,981.61	68.17%

NO	POSTO ADMINISTRATIVO	FI		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	2	$ 561,399.61	89.89%
2	Baucau Villa	5	$ 8,312,880.92	59.65%
3	Laga	2	$ 719,359.34	81.57%
4	Multi Posto	4	$ 109,889,602.64	73.51%
5	Quelicai	4	$ 7,600,628.19	76.18%
6	Vemasse	1	$ 690,194.30	90.00%
7	Venilale	6	$ 6,194,968.60	38.45%
	Grand Total	24	$ 133,969,033.60	71.38%

NO	POSTO ADMINISTRATIVO	Fundu Covid-19		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia		$ -	0.00%
2	Baucau Villa	1	$ 469,360.62	70.14%
3	Laga		$ -	0.00%
4	Multi Posto		$ -	0.00%
5	Quelicai		$ -	0.00%
6	Vemasse		$ -	0.00%
7	Venilale		$ -	0.00%
	Grand Total	1	$ 469,360.62	70.14%

Dadus kada projeto: Anexu A

NO	POSTO ADMINISTRATIVO	LM-BS		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	1	$ 255,148.17	18.07%
2	Baucau Villa	2	$ 207,288.36	65.36%
3	Laga	2	$ 595,138.56	38.87%
4	Multi Posto		$ -	0.00%
5	Quelicai		$ -	0.00%
6	Vemasse	1	$ 50,000.00	60.97%
7	Venilale		$ -	0.00%
	Grand Total	6	$ 1,107,575.09	40.03%

NO	POSTO ADMINISTRATIVO	LM-CD		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	1	$ 316,447.42	89.84%
2	Baucau Villa	3	$ 487,013.64	12.65%
3	Laga	2	$ 968,003.94	44.59%
4	Multi Posto	2	$ 571,773.90	8.45%
5	Quelicai	4	$ 1,205,716.58	41.97%
6	Vemasse	4	$ 1,030,442.93	10.44%
7	Venilale	1	$ 282,288.02	43.36%
	Grand Total	17	$ 4,861,686.43	32.13%

NO	POSTO ADMINISTRATIVO	LM-TP		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	8	$ 845,834.12	0.00%
2	Baucau Villa	7	$ 786,409.33	0.00%
3	Laga	3	$ 288,126.88	0.00%
4	Multi Posto		$ -	0.00%
5	Quelicai	8	$ 781,654.70	0.00%
6	Vemasse		$ -	0.00%
7	Venilale	3	$ 298,750.16	0.00%
	Grand Total	29	$ 3,000,775.19	0.00%

NO	POSTO ADMINISTRATIVO	PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	2	$ 251,668.48	70.50%
2	Baucau Villa	2	$ 375,331.11	29.93%
3	Laga	2	$ 127,577.38	46.17%
4	Multi Posto		$ -	0.00%
5	Quelicai		$ -	0.00%
6	Vemasse	1	$ 54,085.33	35.55%
7	Venilale	1	$ 54,888.38	35.55%
	Grand Total	8	$ 863,550.68	44.86%

1.3.2 : Lista Projectos Municipio Baucau Por Sectors

NO	POR SECTOR	TOTAL MUNICIPIO BAUCAU		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA	1	$ 316,447.42	89.84%
2	EDIFICIOS PUBLICOS	13	$ 1,999,417.79	29.65%
3	EDUKASAUN	31	$ 3,743,421.04	16.69%
4	ELETRIFIKASAUN NASIONAL	10	$ 3,110,591.49	84.79%
5	ESTRADAS	17	$ 22,189,429.73	50.50%
6	IMPRESTIMO	4	$ 109,889,602.64	73.51%
7	MANUTENSAUN NO REHABILITASAUN	8	$ 2,553,710.88	74.11%
8	SAUDE	1	$ 469,360.62	70.14%
	Grand Total	85	$ 144,271,981.61	68.17%

NO	POR SECTOR	Baguia		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA	1	$ 316,447.42	89.84%
2	EDIFICIOS PUBLICOS	2	$ 251,668.48	70.50%
3	EDUKASAUN	8	$ 845,834.12	0.00%
4	ELETRIFIKASAUN NASIONAL	1	$ 485,365.98	89.88%
5	ESTRADAS		$ -	0.00%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN	2	$ 331,181.80	34.58%
8	SAUDE		$ -	0.00%
	Grand Total	14	$ 2,230,497.80	45.39%

NO	POR SECTOR	Baucau Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	4	$ 464,962.08	34.44%
3	EDUKASAUN	8	$ 1,463,612.86	38.65%
4	ELETRIFIKASAUN NASIONAL	2	$ 584,858.54	82.59%
5	ESTRADAS	5	$ 7,655,489.88	53.03%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE	1	$ 469,360.62	70.14%
	Grand Total	20	$ 10,638,283.98	52.62%

NO	POR SECTOR	Laga		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	2	$ 574,764.00	19.63%
3	EDUKASAUN	4	$ 353,569.20	16.66%
4	ELETRIFIKASAUN NASIONAL		$ -	0.00%
5	ESTRADAS	2	$ 656,863.79	58.74%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN	3	$ 1,113,009.11	67.48%
8	SAUDE		$ -	0.00%
	Grand Total	11	$ 2,698,206.10	48.50%

NO	POR SECTOR	Multi Posto		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS		$ -	0.00%
3	EDUKASAUN		$ -	0.00%
4	ELETRIFIKASAUN NASIONAL		$ -	0.00%
5	ESTRADAS	2	$ 571,773.90	8.45%
6	IMPRESTIMO	4	$ 109,889,602.64	73.51%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE		$ -	0.00%
	Grand Total	6	$ 110,461,376.54	73.18%

NO	POR SECTOR	Quelicai		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	2	$ 549,049.52	13.32%
3	EDUKASAUN	8	$ 781,654.70	0.00%
4	ELETRIFIKASAUN NASIONAL	2	$ 729,303.13	95.71%
5	ESTRADAS	4	$ 7,527,992.12	73.40%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE		$ -	0.00%
	Grand Total	16	$ 9,587,999.47	65.67%

NO	POR SECTOR	Vemasse		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	2	$ 104,085.33	47.76%
3	EDUKASAUN		$ -	0.00%
4	ELETRIFIKASAUN NASIONAL	2	$ 840,963.28	86.66%
5	ESTRADAS	3	$ 879,673.95	0.00%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE		$ -	0.00%
	Grand Total	7	$ 1,824,722.56	42.66%

NO	POR SECTOR	Venilale		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	1	$ 54,888.38	35.55%
3	EDUKASAUN	3	$ 298,750.16	0.00%
4	ELETRIFIKASAUN NASIONAL	3	$ 470,100.56	61.99%
5	ESTRADAS	1	$ 4,897,636.09	24.21%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN	3	$ 1,109,519.97	87.70%
8	SAUDE		$ -	0.00%
	Grand Total	11	$ 6,830,895.16	36.16%

1.3.3 : Lista Projectos Municipio Baucau Por Ministerios

NO	POR MINISTERIO	GRAND TOTAL		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	7	$ 798,108.36	41.16%
2	MINISTERIO AGRIKULTURA E PESCAS	1	$ 316,447.42	89.84%
3	MINISTERIO DAS OBRAS PUBLICAS	40	$ 137,763,172.77	70.07%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	31	$ 3,743,421.04	16.69%
5	MINISTERIO SAUDE	2	$ 748,725.31	53.73%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 50,000.00	60.97%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	2	$ 782,313.77	14.42%
8	SAMES	1	$ 69,792.94	42.92%
	Grand Total	85	$ 144,271,981.61	68.17%

NO	POR MINISTERIO	Baguia		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	2	$ 251,668.48	70.50%
2	MINISTERIO AGRIKULTURA E PESCAS	1	$ 316,447.42	89.84%
3	MINISTERIO DAS OBRAS PUBLICAS	3	$ 816,547.78	67.45%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	$ 845,834.12	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	14	$ 2,230,497.80	45.39%

NO	POR MINISTERIO	Baucau Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	2	$ 375,331.11	29.93%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	8	$ 8,260,186.45	55.21%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	$ 1,463,612.86	38.65%
5	MINISTERIO SAUDE	1	$ 469,360.62	70.14%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES	1	$ 69,792.94	42.92%
	Grand Total	20	$ 10,638,283.98	52.62%

NO	POR MINISTERIO	Laga		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	$ 62,135.06	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	5	$ 1,769,872.90	64.23%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	4	$ 353,569.20	16.66%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	$ 512,628.94	22.01%
8	SAMES		$ -	0.00%
	Grand Total	11	$ 2,698,206.10	48.50%

NO	POR MINISTERIO	Multi Posto		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		$ -	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	6	$ 110,461,376.54	73.18%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		$ -	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	6	$ 110,461,376.54	73.18%

NO	POR MINISTERIO	Quelicai		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		$ -	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	6	$ 8,257,295.25	75.37%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	$ 781,654.70	0.00%
5	MINISTERIO SAUDE	1	$ 279,364.69	26.17%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	$ 269,684.83	0.00%
8	SAMES		$ -	0.00%
	Grand Total	16	$ 9,587,999.47	65.67%

NO	POR MINISTERIO	Vemasse		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	$ 54,085.33	35.55%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	5	$ 1,720,637.23	42.36%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		$ -	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 50,000.00	60.97%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	7	$ 1,824,722.56	42.66%

NO	POR MINISTERIO	Venilale		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	$ 54,888.38	35.55%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	7	$ 6,477,256.62	37.83%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	$ 298,750.16	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	11	$ 6,830,895.16	36.16%

1.4. Dadus Populasaun Munisipiu Baucau

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade Poduktivu (idade 15-64)		idade la Produltivu (idade 0-14+65 ba leten	
		Male	Female	Male	Female
Baguia	13,569	4,111	3,962	2,769	2,727
Baucau	48,990	14,524	14,547	10,211	9,709
Laga	16,291	4,549	4,591	3,567	3,585
Quelicai	6,127	1,774	1,413	1,536	1,405
Vemasse	2,783	711	698	707	667
Venilale	5,136	1,223	1,197	1,369	1,347

Fontes : Projeksaun Populasaun bazea ba Census Populasaun no Umakain 2015,

Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan nia laran, husi lista #anexu B hatudu progresu aktual fulan ida ne'e ho nia prensentagen servisu, montante aktual bazeia ba orsamento ne'ebe hetan husi progresu fulan ida ne'e, ikus liu prentangen aktual fulan ida ne'e hatudu progresu fisiku komulativu husi prosentu antrior no fulan ida ne'e nian, lista kompletu ba detallu bele hare iha #anexu B, detallu ba back-up #anexu C, no Instrusaun Servisu #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáclo Servisu Iha Terenu

1. Transporte no Engenheiro la Suficiente
2. Ho Volume Servisu ne'ebe barak Planu Inspeksaun kada fulan dala Tolu(3) ba visita Projetu sente todan ou la kobre **(karik iha villa laran bele halo Monitorizasaun kada fulan bele dala tolu(3) maibe ho distancia ne'ebe do'ok no estrada ne'ebe grave hanesan Laga, Quelicai, Baguia no Venilale sebele halo monitorizasaun kada fulan dala ida (1) deit**).
3. Mina la suficente
4. Pakote hodi asesu ba **Dropbox** ami husi Baucau sei uza ida idak nia pakote ou pulsa pribado
5. Ami Engenherio Municipio sente todan tamba planu inspeksaun kada fulan dala tolu (3) ho distancia balun ne'ebe do'ok no estrada grave ami dala ruma la iha tempu atu sukat kada item por item tamba ami maneija tempu hodi ba fali projetu seluk no dala ruma mos ami fila kalan bo'ot to'o des oras (10) hanesan ne'e ami la konsege **update** informasaun kada projetu ba **Dropbox**.

- **Obstaclo Parte Eletricidade**
  1. Laptop laiha atu halo relatorio waihira iha Municipiu
  2. Transporte (Kareta / motor) la Suficiente atu koresponde ba plano ne'ebe Aprovado
  3. Combustibel / Mina (Municipiu Baucau, Viqueque, Lautem, Pertamina Eto laiha)
  4. Kontractor laiha site ou kontaktu / telfone la tama no contractor la ba iha site/terenu
  5. Menus Enginheiro ME
  6. Natureza hanesan Udan Boot, Estrada kotu dalan la asesu ba kareta

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Sujere ba Superior sebele aumenta transporte no Enginheiro
2. Sujere ba Superior karik bele planu Inspeksaun kada fulan dala tolu (3) ba visita projetu sente todan ou la kobre **(ho distancia ne'ebe do'ok no estrada ne'ebe grave hanesan Posto Administrativo Laga, Quelicai no Baguia sebele halo monitorizasaun kada fulan dala ida 1 deit).**
3. Sujere ba Superior karik bele planu Inspeksaun kada fulan dala ida 2 ou tuir planu Inspesaun ba projetu sira ne'ebe iha **Posto Administrativo Baucau villa, Vemase no Venilale.**
4. Projecto nebe'e mak enginheiro la iha terenu ami la presija halo monitorizasaun no sukat nia volume
5. Presija aumenta mina
6. Husu ba Logistik sebele resolve tiha linha Internet iha Residence ADN Baucau.

- **Recomedacasaun Parte Eletricidade**

1. Rekomenda ba parte Logistik atu prepara Laptop kada Enginheiro (ba Eng. Ne'ebe seidauk hetan).
2. Rekomenda ba Logistik atu Aumenta tranporte ka kareta ba Enginheiro Electricidade.
3. Rekomeda ba parte Logistik atu hare problema konbustibel / Mina iha parte leste mak hanesan Municipio Baucau, Lautem no Viqueque problema iha neba pertamina Eto laiha nemak dificulta Ami nia plano monitorizasaun karik mina hotu ami tenki fila mai atesta iha municipio Manatuto.
4. Rekomenda ba Superior sira atu koordena ho Dono do projeito (EDTL,EP) oinsa atu kria linha koordenasaun ne'ebe diak.
5. Rekomenda ba HR atu Amenta Eng. Electricidade (Recruta tan Eng. ME)
6. Rekomenda ba parte Logistik atu prepara / Facilita simcard Office nian ba Eng. Electerica.

Note: Asinatura Husi Eng. Municipio Baucau

Força de Trabalho ADN,I.P Municipio Baucau						
No	**Deskrisaun**	**Identidade**				
		Naran Kompletu	**Nu. ID Card**	**Pozisaun**	**Fotografia**	**Asinatura**
1	Enjineiru	Agustinho Aranda	153	Enjineiru EPAS		
		Jacob da Costa Camoes	165	Enjineiru ITI		
		Jerry Gil M. Pereira	255	Enjineiru EPAS		

		Leonito Pereira	241	Enjineiru ITI		
		Adonis Julio Fernandes	152	Enjineiru ME		
2	Enjineira	Olivia Soares	112	Enjineira VEBD		
3	Motorista	Anaceto de S. Belo	048	Motorista		

#ANEXU A

MUNICIPIO BAUCAU (LISTA GERAL)

					LOKALIZASAUN PROJETU									
NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNICIPIO	NARAN COMP.	NARAN KONT.	MONT. KONT. ($)	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. ($)	BAL. ($)	STATUS PROJECTO	OBS
1	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	$ 22,000.00	0.00%	0.00%	$ -	$ 22,000.00	ON-GOING	
2	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	$ 562,858.54	95.35%	85.82%	$ 483,039.75	$ 79,818.79	ON-GOING	
3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Domin Timor Diak, Lda	SSS/078/MOPTC-2017	$ 3,599,951.87	93.55%	73.52%	$ 2,646,594.70	$ 953,357.17	ON-GOING	Progresso Fisiko iha Tereno ba FulanJulho Aumenta 3.81%
4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Gihon Unip, Lda	SSS/066/MOPTC-2017	$ 3,450,866.98	92.50%	36.62%	$ 1,263,582.64	$ 2,187,284.34	ON-GOING	Progresso Fisiko iha Tereno ba FulanJulho Aumenta 52.89%
5	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	$ 19,838.03	100.00%	90.00%	$ 17,854.23	$ 1,983.80	ON-GOING	Falta Retensaun
6	Rural Roads Routine Maintenance Baucau - Uatabo Chainage 0+000 - 4+800 and Boile - Uatabo Chainage 0+000 - 5+200 in Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Baucau Villa	Baucau	Talamori	MPWTC-W-190090	$ 63,815.15	80.00%	68.56%	$ 43,751.20	$ 20,063.95	ON-GOING	
7	Road Maintenance Section: Baucau Urbans, Baucau Town, Baucau Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Baucau Villa	Baucau	Jomarjo Unipessoal Lda	MPW-W-190158	$ 137,495.42	85.28%	76.75%	$ 105,530.79	$ 31,964.63	ON-GOING	
8	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Baucau Villa	Baucau	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	$ 469,360.62	85.72%	70.14%	$ 329,188.84	$ 140,171.78	ON-GOING	
9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Baucau Villa	Baucau	Mexa	MPW-W-210047	$ 403,360.46	67.37%	0.00%	$ -	$ 403,360.46	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 65.41%
10	Construção de Nova Escola Polo de Baucau, de Referência da Escola Portuguesa de Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Baucau Villa	Baucau	Sanira Construction Unip Lda	RDTL-326	$ 677,203.53	92.82%	83.53%	$ 565,698.21	$ 111,505.32	ABANDONA	
11	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Rozi Unipessoal, Lda	04/KDM/-BAUCAU/IX/2021	$ 59,323.84	0.00%	0.00%	$ -	$ 59,323.84	ON-GOING	
12	Konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Gardel Unipessoal.Lda	07/KDM/-BAUCAU/IX/2021	$ 316,007.27	39.50%	35.55%	$ 112,329.98	$ 203,677.29	ON-GOING	
13	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Talamori	RDTL-SAMES-RFQ-021-071	$ 69,792.94	69.33%	42.92%	$ 29,956.90	$ 39,836.04	ON-GOING	
14	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF MAUCALE	-	$ 83,515.23	27.79%	0.00%	$ -	$ 83,515.23	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 6.60%
15	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF ZONA GOLGOTA	-	$ 82,531.68	36.04%	0.00%	$ -	$ 82,531.68	ON-GOING	
16	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	-	$ 144,241.57	0.00%	0.00%	$ -	$ 144,241.57	ON-GOING	
17	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	-	$ 164,157.57	27.41%	0.00%	$ -	$ 164,157.57	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 27.41%
18	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESG FILIAL KILIK WAIGA'E	-	$ 76,528.56	17.08%	0.00%	$ -	$ 76,528.56	ON-GOING	
19	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	-	$ 117,273.54	0.00%	0.00%	$ -	$ 117,273.54	ON-GOING	
20	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	-	$ 118,161.18	0.00%	0.00%	$ -	$ 118,161.18	ON-GOING	
21	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Lalaisi, Unip. Lda	RT/023/MOP-2019	$ 377,873.70	97.47%	64.91%	$ 245,269.41	$ 132,604.29	ON-GOING	
22	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 1+600 - 3+300 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Rozi Unipessoal, Lda	RT/024/MOP-2019	$ 341,485.64	100.00%	100.00%	$ 341,485.63	$ 0.01	FHO	Projecto Finaliza ona
23	Rural Roads Periodic Maintenance Samaguia - Namanei Chainage 0+000 - 7+000 Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Delatina	MPTCW-W-190091	$ 393,649.77	84.80%	41.73%	$ 164,273.69	$ 229,376.08	ON-GOING	
24	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Laga	Baucau	Sumber Urip Unip. Lda	04/KDAM-BCU/IX/2019	$ 65,442.32	100.00%	90.00%	$ 58,898.09	$ 6,544.23	PHO	Falta Retensaun
25	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laga	Baucau	Uatoos Unip. Lda	MOP-W-200002	$ 201,488.79	40.00%	33.29%	$ 67,076.91	$ 134,411.88	ON-GOING	
26	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 :Laga to Baguia	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laga	Baucau	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	$ 455,375.00	70.00%	70.00%	$ 318,762.50	$ 136,612.50	ON-GOING	
27	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Laga	Baucau	Costa Estelia Unipessoal,Lda	05/KDM/-BAUCAU/IX/2021	$ 62,135.06	20.29%	0.00%	$ -	$ 62,135.06	ON-GOING	

28	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Laga	Baucau	Juga Te Figa Unipessoal Lda	40/MACLN/X/2021	$ 512,628.94	35.79%	22.01%	$ 112,848.70	$ 399,780.24	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 5.98%
29	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF LALA-BU'U	-	$ 109,706.08	0.00%	0.00%	$ -	$ 109,706.08	ON-GOING	
30	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	-	$ 87,554.29	21.19%	0.00%	$ -	$ 87,554.29	ON-GOING	
31	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	-	$ 90,866.51	0.00%	0.00%	$ -	$ 90,866.51	ON-GOING	
32	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baguia	Baucau	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	$ 485,365.98	100.09%	89.88%	$ 436,225.01	$ 49,140.97	ON-GOING	
33	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Baguia	Baucau	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	$ 76,033.63	100.00%	90.00%	$ 68,430.27	$ 7,603.36	PHO	Falta Retensaun
34	Konstrusaun Posto Administrativo Baguia	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Delatina Unip. Lda	02/KDAM-BCU/VIII/2019	$ 197,153.25	100.00%	90.00%	$ 177,437.92	$ 19,715.33	PHO	Falta Retensaun
35	Baguia - Larisula Chainage 0+000 - 12+900 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Baguia	Baucau	Lamegua Star Unip Lda	MPW-W-190088	$ 255,148.17	20.07%	18.07%	$ 46,093.40	$ 209,054.77	ON-GOING	
36	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Mexa	06/KDM/-BAUCAU/IX/2021	$ 54,515.23	12.06%	0.00%	$ -	$ 54,515.23	ON-GOING	
37	Konstrusaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	MINISTERIO AGRIKULTURA E PESCAS	LM-CD	AGRICULTURA	Baguia	Baucau	Makasae Construction LDA	RDTL-2021-14628	$ 316,447.42	99.83%	89.84%	$ 284,307.87	$ 32,139.55	ON-GOING	
38	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF GULARI	-	$ 89,797.83	0.00%	0.00%	$ -	$ 89,797.83	ON-GOING	
39	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF OSSU-UFULARI	-	$ 105,390.82	0.00%	0.00%	$ -	$ 105,390.82	ON-GOING	
40	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF UACALA	-	$ 81,847.60	0.00%	0.00%	$ -	$ 81,847.60	ON-GOING	
41	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE FINI BAGUIA	-	$ 91,267.16	0.00%	0.00%	$ -	$ 91,267.16	ON-GOING	
42	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari - Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE LARI-SULA	-	$ 97,046.05	10.64%	0.00%	$ -	$ 97,046.05	ON-GOING	
43	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC OSSU-HUNA	-	$ 84,264.57	25.80%	0.00%	$ -	$ 84,264.57	ON-GOING	
44	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC BUAUA LAVATERI	-	$ 120,700.62	0.00%	0.00%	$ -	$ 120,700.62	ON-GOING	
45	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE ESGF DE BAGUIA	-	$ 175,519.47	4.17%	0.00%	$ -	$ 175,519.47	ON-GOING	
46	Aumenta C. O no Kliesntes	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	$ 24,365.04	100.00%	90.00%	$ 21,928.54	$ 2,436.50	PHO	Falta Retensaun
47	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	$ 163,447.50	100.00%	90.00%	$ 147,102.75	$ 16,344.75	PHO	Falta Retensaun
48	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Venilale	Baucau	Ruvic unip, lda	SSS/118/MOPTC-2016	$ 4,897,636.09	27.52%	24.21%	$ 1,185,891.06	$ 3,711,745.03	PENDENTE	
49	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Caidailale Unip.Lda	RT/069/MOPTC-2016	$ 343,674.56	96.10%	86.49%	$ 297,228.67	$ 46,445.89	ON-GOING	
50	Rehabilitasaun Estrada Bercoli-Bahamori 3 Sta. 2+750-4+000-Municipal of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Maubere Spirit	RT/071/MOPTC-2016	$ 282,114.39	100.00%	99.31%	$ 280,155.69	$ 1,958.70	FHO	
51	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Wetodo Unip. Lda	SSS/296/MOPTC-2016	$ 483,731.02	92.96%	92.96%	$ 449,670.20	$ 34,060.82	ON-GOING	
52	Instalacao Electricidade Linha Medium Voltagem & Transformer Ba Comunidade (Energia Eletricidade ba Sistema Bomba Be'e Mos) ba Comunidade Fatulia Watuhaco & Waihaia (Venilale)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Bozer Construcao,unip.lda	MOP-W-190173	$ 282,288.02	48.18%	43.36%	$ 122,394.52	$ 159,893.50	ON-GOING	
53	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Venilale	Baucau	Caidara Lata Unipessoal,Lda	02/KDM/-BAUCAU/IX/2021	$ 54,888.38	39.50%	35.55%	$ 19,512.87	$ 35,375.51	ON-GOING	
54	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBC UAI-BUA	-	$ 88,801.74	0.00%	0.00%	$ -	$ 88,801.74	ON-GOING	
55	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBF CULINA-OSSU-UAILALE	-	$ 120,371.07	0.00%	0.00%	$ -	$ 120,371.07	ON-GOING	

56	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	-	$ 89,577.35	40.47%	0.00%	$ -	$ 89,577.35	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 9.71%
57	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Quelicai	Baucau	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	$ 471,847.32	98.83%	98.83%	$ 466,310.41	$ 5,536.91	ON-GOING	
58	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Quelicai	Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	$ 257,455.81	100.00%	90.00%	$ 231,710.23	$ 25,745.58	PHO	Falta Retensaun
59	Rehabilitation Of Roads Uiaca - Queleqai - Lacluta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Quelicai	Baucau	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	$ 3,451,113.20	94.61%	75.53%	$ 2,606,757.82	$ 844,355.38	ON-GOING	
60	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Quelicai	Baucau	Lalaisi, Unip. Lda	MPWTC-W-190089	$ 157,601.26	58.92%	53.03%	$ 83,569.34	$ 74,031.92	ON-GOING	
61	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Quelicai	Baucau	Niceles Unipessoal Lda	MPW-CS-2000026	$ 499,065.80	70.00%	70.00%	$ 349,346.06	$ 149,719.74	ON-GOING	
62	Rehabilitation of Roads, Road Section: Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Quelicai	Baucau	Wingstone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	$ 3,420,211.86	92.14%	72.67%	$ 2,485,573.04	$ 934,638.82	ON-GOING	
63	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	$ 279,364.69	29.08%	26.17%	$ 73,115.51	$ 206,249.18	ON-GOING	
64	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Samadare Unip. Lda	40/MACLN/XI/2021	$ 269,684.83	2.90%	0.00%	$ -	$ 269,684.83	ON-GOING	
65	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UADA-BORU	-	$ 61,695.67	0.00%	0.00%	$ -	$ 61,695.67	ON-GOING	
66	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAI-ACA/MULIA	-	$ 101,309.07	26.69%	0.00%	$ -	$ 101,309.07	ON-GOING	
67	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF ABO-LIR LALETEK	-	$ 75,117.25	0.00%	0.00%	$ -	$ 75,117.25	ON-GOING	
68	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBC LETEMUMO	-	$ 159,065.75	9.87%	0.00%	$ -	$ 159,065.75	ON-GOING	
69	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	-	$ 125,450.86	0.00%	0.00%	$ -	$ 125,450.86	ON-GOING	
70	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF CATOLICA DARENAFA	-	$ 47,094.07	0.00%	0.00%	$ -	$ 47,094.07	ON-GOING	
71	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF MAURO DARALA/BORUMODO	-	$ 106,571.86	21.49%	0.00%	$ -	$ 106,571.86	ON-GOING	
72	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAIDORA/OSSOLIA	-	$ 105,350.17	0.00%	0.00%	$ -	$ 105,350.17	ON-GOING	
73	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Vemasse	Baucau	We-Rua Unip, Lda	RDTL-11003725	$ 690,194.30	100.00%	90.00%	$ 621,173.06	$ 69,021.24	PHO	Falta Retensaun
74	Instalacao Electricidade Linha Distribuicao ba uma (Energia Eletricidade ba Sistema Bomba Be'e) ba Comunidade Loiubu (Watulari)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Vemasse	Baucau	El Nicholay unip.Lda	MOP-W-190181	$ 150,768.98	79.32%	71.39%	$ 107,628.62	$ 43,140.36	ON-GOING	
75	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Rozi const. unip. Lda	MPW-W-210048	$ 379,137.63	93.08%	0.00%	$ -	$ 379,137.63	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 23.49%
76	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Rozi const. unip. Lda	MPW-W-210051	$ 258,534.75	93.75%	0.00%	$ -	$ 258,534.75	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 0.35%
77	R4D Rural Road Spot Improvement Vemase-Osoala Chainage 0+000-21+600	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Chacailala Unipessoal Lda	MPW-W-210052	$ 242,001.57	17.99%	0.00%	$ -	$ 242,001.57	ON-GOING	
78	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Vemasse	Baucau	Esa-Un	56/DNAL-MTAC/III/2017	$ 50,000.00	67.74%	60.97%	$ 30,483.00	$ 19,517.00	PENDENTE	
79	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Vemasse	Baucau	Wrangler Unipessoal,Lda	01/KDM/-BAUCAU/IX/2021	$ 54,085.33	65.19%	35.55%	$ 19,227.89	$ 34,857.44	ON-GOING	
80	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto	Baucau	Shangai Construction Group Co.,Ltd	ICB/021/MPWTC-2015	$ 59,287,453.57	84.82%	85.78%	$ 50,859,620.95	$ 8,427,832.62	ON-GOING	
81	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto	Baucau	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/078/MPWTC-2015	$ 29,315,346.10	87.26%	78.40%	$ 22,983,875.13	$ 6,331,470.97	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 0.14%
82	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto	Baucau	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	$ 16,024,500.97	31.80%	28.50%	$ 4,566,556.06	$ 14,508,434.30	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 0.14%

83	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto	Baucau	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)	RFP/003/MOP/2018	$ 5,262,302.00	46.81%	45.07%	$ 2,371,905.90	$ 2,890,396.10	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 1.74%
84	R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multi Posto	Baucau	Juga Te Figa Unipessoal Lda	MPW-W-210054	$ 272,285.28	24.23%	0.00%	$ -	$ 272,285.28	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Julho Aumenta 21.20%
85	R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multi Posto	Baucau	DB-Ingracia Unipessoal Lda	MPW-W-210049	$ 299,488.62	92.37%	16.13%	$ 48,310.58	$ 251,178.04	ON-GOING	
	TOTAL								**$ 144,271,981.61**			**$ 98,347,684.54**	**$ 48,974,786.46**		

Prepara Husi:

1. Eng. Agostinho Aranda
Eng. ba Porjecto Edificio Publico Beé no Saneamento Municipio Baucau,ADN,I.P

2. Eng. Jacob da Costa Camoes
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Baucau, ADN, I.P

3. Eng. Adonis Julio Fernandes
Eng. ba Projeito ME, ADN, I.P

Certifika Husi:

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN,I.P

#ANEXU B

PROGRESSU FISIKU KADA FULAN MUNICIPIO BAUCAU

					LOKALIZASAUN PROJETU						Jul-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
1	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	$ 22,000.00	Jan. 1, 2016	0.00%		0.00%
2	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	$ 562,858.54	July 6, 2016	95.35%		95.35%
3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Domin Timor Diak, Lda	SSS/078/MOPTC-2017	$ 3,599,951.87	Sept. 12, 2017	89.74%	3.81%	93.55%
4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Gihon Unip, Lda	SSS/066/MOPTC-2017	$ 3,450,866.98	Sept. 12, 2017	39.61%	52.89%	92.50%
5	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	$ 19,838.03	Aug. 1, 2016	100.00%		100.00%
6	Rural Roads Routine Maintenance Baucau - Uatabo Chainage 0+000 - 4+800 and Boile - Uatabo Chainage 0+000 - 5+200 in Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Baucau Villa	Baucau	Talamori	MPWTC-W-190090	$ 63,815.15	Jan. 10, 2012	80.00%		80.00%
7	Road Maintenance Section: Baucau Urbans, Baucau Town, Baucau Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Baucau Villa	Baucau	Jomarjo Unipessoal Lda	MPW-W-190158	$ 137,495.42	Nov. 30, 2019	85.28%		85.28%
8	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Baucau Villa	Baucau	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	$ 469,360.62	Dec. 10, 2020	85.72%		85.72%
9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Baucau Villa	Baucau	Mexa Unip.lda	MPW-W-210047	$ 403,360.46	June 10, 2021	1.95%	65.41%	67.37%
10	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Baucau Villa	Baucau	Sanira Construction Unip Lda	RDTL-326	$ 677,203.53	Nov. 12, 2012	92.82%		92.82%
11	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Rozi Unipessoal, Lda	04/KDM/-BAUCAU/IX/2021	$ 59,323.84	8-Jul-21	0.00%		0.00%
12	konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Gardel Unipessoal.Lda	07/KDM/-BAUCAU/IX/2021	$ 316,007.27	8-Jul-21	39.50%		39.50%
13	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Talamori	RDTL-SAMES-RFQ-021-071	$ 69,792.94	8-Jul-21	69.33%		69.33%
14	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF MAUCALE	-	$ 83,515.23	Oct. 15, 2021	21.19%	6.60%	27.79%
15	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF ZONA GOLGOTA	-	$ 82,531.68	Oct. 15, 2021	36.04%		36.04%
16	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	-	$ 144,241.57	Oct. 15, 2021	0.00%		0.00%
17	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	-	$ 164,157.57	Oct. 15, 2021	0.00%	27.41%	27.41%
18	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	-	$ 76,528.56	Oct. 15, 2021	17.08%		17.08%
19	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	-	$ 117,273.54	Oct. 15, 2021	0.00%		0.00%
20	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	-	$ 118,161.18	Oct. 15, 2024	0.00%		0.00%
21	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Lalaisi, Unip. Lda	RT/023/MOP-2019	$ 377,873.70	Jan. 15, 2020	97.47%		97.47%
22	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 1+600 - 3+300 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Rozi Unipessoal, Lda	RT/024/MOP-2019	$ 341,485.64	Jan. 1, 2020	100.00%		100.00%
23	Rural Roads Periodic Maintenance Samaguia - Namanei Chainage 0+000 - 7+000 Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Delatina	MPTCW-W-190091	$ 393,649.77	Aug. 23, 2019	84.80%		84.8%
24	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Laga	Baucau	Sumber Urip Unip. Lda	04/KDAM-BCU/IX/2019	$ 65,442.32	Sept. 24, 2019	100.00%		100.00%
25	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laga	Baucau	Uatoos Unip. Lda	MOP-W-200002	$ 201,488.79	May 5, 2014	40.00%		40.00%

					LOKALIZASAUN PROJETU						Jul-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
26	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 :Laga to Baguia	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laga	Baucau	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	$ 455,375.00	March 25, 2020	70.00%		70.00%
27	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Laga	Baucau	Costa Estelia Unipessoal,Lda	05/KDM/-BAUCAU/IX/2021	$ 62,044.03	8-Jul-21	20.29%		20.29%
28	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Laga	Baucau	Juga Te Figa Unipessoal Lda	40/MACLN/X/2021	$ 512,628.94	Jan. 1, 2022	29.81%	5.98%	35.79%
29	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF LALA-BU'U	-	$ 109,706.08	Oct. 15, 2021	0.00%		0.00%
30	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	-	$ 87,554.29	Oct. 15, 2021	21.19%		21.19%
31	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	-	$ 90,866.51	Oct. 15, 2021	0.00%		0.00%
32	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baguia	Baucau	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	$ 485,365.98	July 6, 2016	100.09%		100.09%
33	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Baguia	Baucau	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	$ 76,033.63	Nov. 15, 2016	100.00%		100.00%
34	Konstrusaun Posto Administrativo Baguia	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Delatina Unip. Lda	02/KDAM-BCU/VIII/2019	$ 197,153.25	Aug. 1, 2019	100.00%		100.00%
35	Baguia - Larisula Chainage 0+000 - 12+900 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Baguia	Baucau	Lamegua Star Unip Lda	MPW-W-190088	$ 255,148.17	Aug. 23, 2019	20.07%		20.07%
36	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Mexa Unip.lda	06/KDM/-BAUCAU/IX/2021	$ 54,515.23	8-Jul-21	12.06%		12.06%
37	Konstrusaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	MINISTERIO AGRIKULTURA E PESCAS	LM-CD	AGRICULTURA	Baguia	Baucau	Makasae Construction LDA	RDTL-2021-14628	$ 316,447.42	Sept. 16, 2021	99.83%		99.83%
38	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF GULARI	-	$ 89,797.83	Oct. 15, 2021	0.00%		0.00%
39	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF OSSU-UFULARI	-	$ 105,390.82	Oct. 15, 2021	0.00%		0.00%
40	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF UACALA	-	$ 81,847.60	Oct. 15, 2021	0.00%		0.00%
41	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE FINI BAGUIA	-	$ 91,267.16	Oct. 15, 2021	0.00%		0.00%
42	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE LARI-SULA	-	$ 97,046.05	Oct. 15, 2021	10.64%		10.64%
43	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC OSSU-HUNA	-	$ 84,264.57	Oct. 15, 2021	25.80%		25.80%
44	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC BUAUA LAVATERI	-	$ 120,700.62	Oct. 15, 2021	0.00%		0.00%
45	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE ESGF DE BAGUIA	-	$ 175,519.47	Oct. 15, 2021	4.17%		4.17%
46	Aumenta C. O no Kliesntes	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	$ 24,365.04	Jan. 1, 2017	100.00%		100.00%
47	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	$ 163,447.50	July 6, 2016	100.00%		100.00%

					LOKALIZASAUN PROJETU						Jul-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA - PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
48	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Venilale	Baucau	Ruvic unip, lda	SSS/118/MOPTC-2016	$ 4,897,636.09	July 29, 2016	27.52%		27.52%
49	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Caidailale Unip.Lda	RT/069/MOPTC-2016	$ 343,674.56	Aug. 18, 2016	96.10%		96.10%
50	Rehabilitasaun Estrada Bercoli-Bahamori 3 Sta. 2+750-4+000-Municipal of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Maubere Spirit	RT/071/MOPTC-2016	$ 282,114.39	Aug. 18, 2016	100.00%		100.00%
51	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Wetodo Unip. Lda	SSS/296/MOPTC-2016	$ 483,731.02	Nov. 22, 2016	92.96%		92.96%
52	Instalacao Electricidade Linha Medium Voltagem & Transformer Ba Comunidade (Energia Eletricidade ba Sistema Bomba Be'e Mos) ba Comunidade Fatulia Watuhaco & Waihaia (Venilale)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Bozer Construcao,unip.lda	MOP-W-190173	$ 282,288.02	Oct. 30, 2019	48.18%		48.18%
53	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Venilale	Baucau	Caidara Lata Unipessoal,Lda	02/KDM/-BAUCAU/IX/2021	$ 54,888.38	8-Jul-21	39.50%		39.50%
54	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBC UAI-BUA	-	$ 88,801.74	Oct. 15, 2021	0.00%		0.00%
55	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBF CULINA-OSSU-UAILALE	-	$ 120,371.07	Oct. 15, 2021	0.00%		0.00%
56	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	-	$ 89,577.35	Oct. 15, 2021	30.76%	9.71%	40.47%
57	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Quelicai	Baucau	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	$ 471,847.32	July 6, 2016	98.83%		98.83%
58	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Quelicai	Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	$ 257,455.81	Sept. 1, 2016	100.00%		100.00%
59	Rehabilitation Of Roads Uiaca - Queleqai - Lacluta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Quelicai	Baucau	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	$ 3,451,113.20	Oct. 28, 2016	94.61%		94.61%
60	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Quelicai	Baucau	Lalaisi, Unip. Lda	MPWTC-W-190089	$ 157,601.26	Aug. 23, 2019	58.92%		58.92%
61	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Quelicai	Baucau	Niceles Unipessoal Lda	MPW-CS-2000026	$ 499,065.80	March 25, 2020	70.00%		70.00%
62	Rehabilitation of Roads, Road Section: Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Quelicai	Baucau	Wingstone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	$ 3,420,211.86	Oct. 28, 2016	92.14%		92.14%
63	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	$ 279,364.69	Aug. 23, 2021	29.08%		29.08%
64	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Samadare Unip. Lda	40/MACLN/XI/2021	$ 269,684.83	Jan. 1, 2022	2.90%		2.90%
65	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UADA-BORU	-	$ 61,695.67	Oct. 15, 2021	0.00%		0.00%
66	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAI- ACA/MULIA	-	$ 101,309.07	Oct. 15, 2021	26.69%		26.69%
67	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF ABO-LIR LALETEK	-	$ 75,117.25	Oct. 15, 2021	0.00%		0.00%
68	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBC LETEMUMO	-	$ 159,065.75	Oct. 15, 2021	9.87%		9.87%
69	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	-	$ 125,450.86	Oct. 15, 2021	0.00%		0.00%
70	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF CATOLICA DARENAFA	-	$ 47,094.07	Oct. 15, 2021	0.00%		0.00%
71	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF MAURO DARALA/BORUMODO	-	$ 106,571.86	Oct. 15, 2021	21.49%		21.49%
72	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAIDORA/OSSOLIA	-	$ 105,350.17	Oct. 15, 2021	0.00%		0.00%
73	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Vemasse	Baucau	We-Rua Unip, Lda	RDTL-11003725	$ 690,194.30	Oct. 22, 2010	100.00%		100.00%
74	Instalacao Electricidade Linha Distribuicao ba uma (Energia Eletricidade ba Sistema Bomba Be'e) ba Comunidade Loiubu (Watulari)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Vemasse	Baucau	El Nicholay unip.Lda	MOP-W-190181	$ 150,768.98	May 11, 2019	79.32%		79.32%
75	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Rozi const. unip. Lda	MPW-W-210048	$ 379,137.63	June 10, 2021	69.59%	23.49%	93.08%
76	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Rozi const. unip. Lda	MPW-W-210051	$ 258,534.75	June 10, 2021	93.40%	0.35%	93.75%
77	R4D Rural Road Spot Improvement Vemase-Osoala Chainage 0+000-21+600	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Chacailala Unipessoal Lda	MPW-W-210052	$ 242,001.57	June 10, 2021	17.99%		17.99%
78	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Vemasse	Baucau	Esa-Un	56/DNAL-MTAC/III/2017	$ 50,000.00	Aug. 18, 2015	67.74%		67.74%
79	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Vemasse	Baucau	Wrangler Unipessoal,Lda	01/KDM/-BAUCAU/IX/2021	$ 54,085.33	8-Jul-21	65.19%		65.19%
80	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	Multi Posto	Baucau	Shangai Construction Group Co.,Ltd	ICB/021/MPWTC-2015	$ 59,287,454.00	Aug. 18, 2016	84.82%		84.82%

					LOKALIZASAUN PROJETU						Jul-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
81	Road nrtwork Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	Multi Posto	Baucau	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/078/MPWTC-2015	$ 29,315,346.10	Nov. 12, 2016	87.12%	0.14%	87.26%
82	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto	Baucau	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	$ 16,024,500.97	March 21, 2019	31.66%	0.14%	31.80%
83	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	Multi Posto	Baucau	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)	RFP/003/MOP/2018	$ 5,262,302.00	Apr. 03, 2019	45.07%	1.74%	46.81%
84	R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multi Posto	Baucau	Juga Te Figa Unipessoal Lda	MPW-W-210054	$ 272,285.28	June 10, 2021	3.03%	21.20%	24.23%
85	R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Baharnori Chainage 0+000-4+000 Bururna-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multi Posto	Baucau	DB-Ingracia Unipessoal Lda	MPW-W-210049	$ 299,488.62	June 10, 2021	92.37%		92.37%

Inspeksaun Husi :

1. Eng. Agustinho Aranda
Eng. ba Porjecto Edifício Publico Beé no Saneamento Municipio Baucau,ADN,I.P

2. Eng. Jacob da Costa Camoes
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Baucau, ADN, I.P

3. Eng. Antonis Julio Fernandes
Eng. ba Projeito ME, ADN, I.P

Verifika Husi :

Eng. Remigio da C. S. dos Santos
Eng. Senior ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Eng/Arch.Francisco Xavier de D. Jeronimo
Eng. Senior ba Porjecto Edificio Publico Beé no Saneamento, ADN,I.P

Eng. Deolindo de Fatima Marques
ChefeSeksaun ME& ITC, ADN, I.P

Certifika Husi :

Eng. Emerenciana da Costa M.Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN,I.P

#ANEXU C1 (MP-5)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality**
No. kontratu : **MPW-W-210054**

Data Inspesaun : 04 – 08 – 2022

Fatin Inspesaun :

Koordinadas :

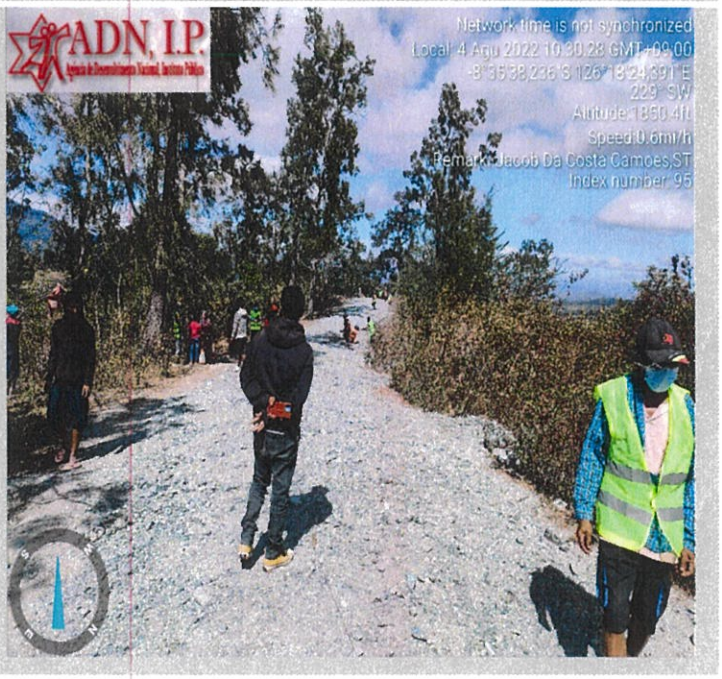
Start Point : Long : -8.628332, Latetude : 126.658177

End Point : Long : -8.66641, Latetude : 126.744860

Naran Inspector : 1. Jacob Da costa Camoes

2. .....

3. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Item servisu : Manutensaun hamos du'ut	

#ANEXU C1 (MP-5)

Back-up Data

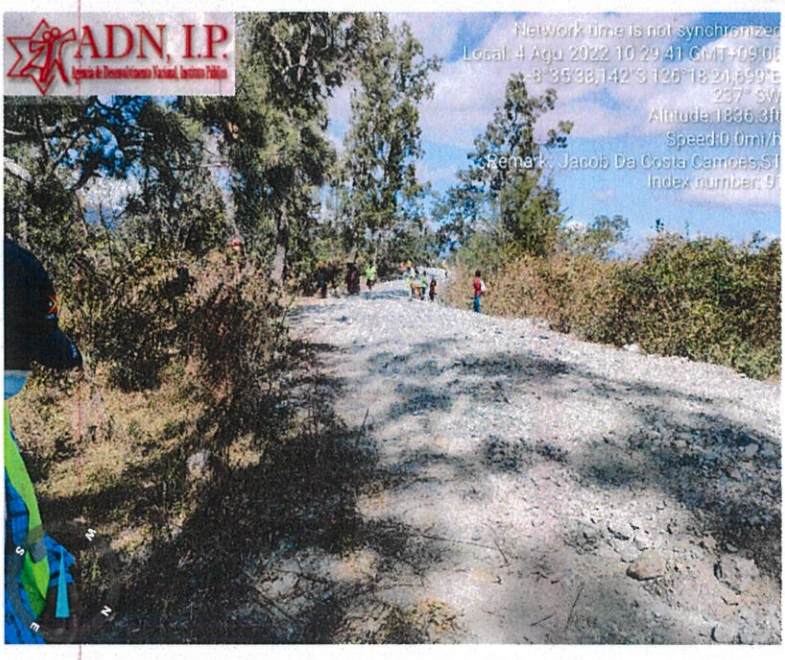
Naran Projeto : **R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality**
No. kontratu : **MPW-W-210054**

Sketch & Foto Desenho

Item Servisu:

Manutensaun hamos duut

Observasaun iha tereno no Foto Aktual



#ANEXU C2 (MP-5)

Summary

Road name	1-Road Baguia to Larisual	Chainage start & end	0+00	12+900
	2-Road Samalari-Sorugua		0+00	2+800
	3-Road Teriluedae - Saelari - Binagua		0+00	3+500
	4-Road Dailari to Boleha		0+00	8+500
Municipality	Baucau	Length		27.8 Km
Postu	Baguia and Laga	Sukos	Larisula Saelari, Samalari	

Item	Description	Price		Progress Previous		Progress Julho		Progress Up to date	
				AMOUNT	%	AMOUNT	%	AMOUNT	%
R-01	General works	$	8,400.00	$ 1,700.00	0.62%	2,591.67	0.95%	4,291.67	1.58%
R-03	Earth work	$	16,529.40	$ -	0.00%	590.00	0.22%	590.00	0.22%
R-05	Sub-base, base and pavement	$	13,327.50	$ -	0.00%	1,400.00	0.51%	1,400.00	0.51%
R-07	Bituminous pavement	$	39,830.00	$ -	0.00%	-	0.00%	-	0.00%
R-08	Structures	$	78,166.53	$ -	0.00%	3.36	0.00%	3.36	0.00%
R-10	Dayworks	$	2,450.00	$ -	0.00%	602.00	0.22%	602.00	0.22%
R-11	Routine maintenance	$	41,946.40	$ 1,659.00	0.61%	22,511.29	8.27%	24,170.29	8.88%
R-12	Cleaning	$	400.00	$ -	0.00%	700.00	0.26%	700.00	0.26%
R-15	Provisional sum	$	800.00	$ -	0.00%	200.00	0.07%	200.00	0.07%
A	**Construction cost**	**$**	**201,849.83**	**$ 3,359.00**	**1.23%**	**$ 28,598.32**	**10.50%**	**$ 31,957.32**	**11.74%**
B	Contractor Fee (A x 10%)	$	20,184.98	$ 335.90	0.12%	$ 2,859.83	1.05%	$ 3,195.73	1.17%
C	General items	$	44,911.54	$ 4,388.50	1.61%	$ 25,145.50	9.23%	$ 29,534.00	10.85%
D	Construction tax (A+B+C x 2%)	$	5,338.93	$ 161.67	0.06%	$ 1,132.07	0.42%	$ 1,293.74	0.48%
E	**Total**	**$**	**272,285.28**	**$ 8,245.07**	**3.03%**	**$ 57,735.72**	**21.20%**	**$ 65,980.79**	**24.23%**

Inspesaun Husi :

Eng. Jacob Da costa Camoes
Eng. ba Projeito Infrastutura Tranporte e Irigasaun ADN,I.P

Verifika Husi :

Eng. Remigio D.C.dos Santos
Eng. Senior ba Projeito Infrastutura Tranporte e Irigasaun ADN,I.P

Certifika Husi :

Eng. Emerenciana da Costa M.Freitas
Cordenadora Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (MP-5)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality

Kompanha : Juga Te Figa Unipessoal Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	4/8/2022	Baucau/Multi Postu	Jacob da Costa Camoes	Eng. ADN Municipiu Baucau	1	Husu ba kontraktor iha terenu tenki iha Engineiru ho Site Supervisor	*Ami ba iha Terenu Engineiru laiha*	
					2	Husu kontraktor servisu hotu tenki tuir planu		
					3	Husu ba kontraktor wainhira servisu remata tenki sura kedas nia volume hodi halo relatorio atu nune'e submete ba ADN ho MOP		
					4	Husu kontraktor tenki taka papan Informasaun Projectu nian iha terenu		
					5	Husu kontraktor tenki aselera servisu		

#ANEXU C1 (BV-9)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800**
No. kontratu : **MPW-W-210047**

Data Inspesaun : **12 / 05/ 2022**

Fatin Inspesaun : Baucau Vila (Boile – Uatabo)

Koordinadas :

Start Point : Long : -8.460625, Latetude : 126.455995

End Point : Long : -8.440356, Latetude : 126.463871

Naran Inspector : **1. Jacob da Costa Camoes**

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Penetration Macadam	

#ANEXU C1 (BV-9)

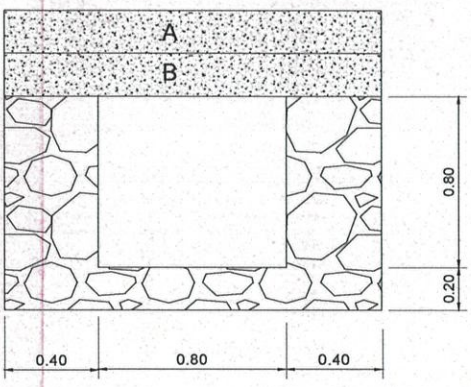
Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800**
No. kontratu : **MPW-W-210047**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu stone Masonry

Box culver



Stone masonry

Luas = 0.96 m3

V = 0.96 x 5 x 2 = 9.60 m3

Volume Structure Concrete M20

A = 0.20 x 0.20 x 1.60 x 4 = 0.256 m3

B = 0.20 x 1.60 x 5 x 2 = 3.20 m3



Penetratan Mcadan

MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXU C2 (BV-9)

Road name	Baucau to Uatabo	Chainage start	0+00
Municipality	Baucau	Chainage end	4+800
Postu	Baucau Vila	Length	4.800Km
Sukos	Trilolo – Bahu -Buruma- Caibada		

SUMMARY

Item	Description	CONTRACT PRICE	Progress Previus		Progress Phisic Jullu		Up to date	
			Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)
R-01	General works	$ 3,110.00	$ 750.00	0.19%	$ 1,420.00	0.35%	$ 2,170.00	0.54%
R-03	Earth work	$ 10,685.18	$ 476.52	0.12%	$ 3,334.71	0.83%	$ 3,811.23	0.94%
R-05	Sub-base, base and pavement	$ 4,927.66	$ -	0.00%	$ 1,385.19	0.34%	$ 1,385.19	0.34%
R-07	Bituminous pavement	$ 238,238.00	$ -	0.00%	$ 199,231.95	49.39%	$ 199,231.95	49.39%
R-08	Structures	$ 75,344.34	$ 2,624.49	0.65%	$ 22,971.40	5.70%	$ 25,595.88	6.35%
R-10	Dayworks	$ 500.00	$ -	0.00%	$ 25.00	0.01%	$ 25.00	0.01%
R-11	Routine maintenance	$ 5,922.40	$ -	0.00%	$ 4,704.00	1.17%	$ 4,704.00	1.17%
R-12	Cleaning	$ 200.00	$ -	0.00%	$ 200.00	0.05%	$ 200.00	0.05%
R-15	Provisional sum	$ 200.00	$ -	0.00%	$ 200.00	0.05%	$ 200.00	0.05%
A	Construction cost	$ 339,127.58	$ 3,851.01	0.95%	$ 233,472.24	57.88%	$ 237,323	58.84%
B	Contractor Fee (A x 10%)	$ 33,912.76	$ 385.10	0.10%	$ 23,347.22	5.79%	$ 23,732.32	6%
C	General items	$ 22,411.09	$ 3,481.40	0.86%	$ 1,863.40	0.46%	$ 5,344.80	1.33%
D	Construction tax (A+B+C x 2%)	$ 7,909.03	$ 154.35	0.04%	$ 5,173.66	1.28%	$ 5,328.01	1.32%
E	Total	$ 403,360.46	$ 7,871.86	1.95%	$ 263,856.52	65.41%	$ 271,728	67.37%

Inspeksaun Husi :

Eng. Jacob Da Costa Camoes

Eng. Ba Projeito Insfrasturctura e Irigasaun, M. Baucau

ADN, I.P

Verifika Husi :

Eng. Remigio Da .C. S Dos Santos

Eng. Senior ba Projeito Insfrasturctura e

Irigasaun, ADN, I.P

Cerifika Husi :

Eng. Emerenciana da Costa M.Freitas

Coordenadora Da Unidade de Controlo e Validação De Qualidade

ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

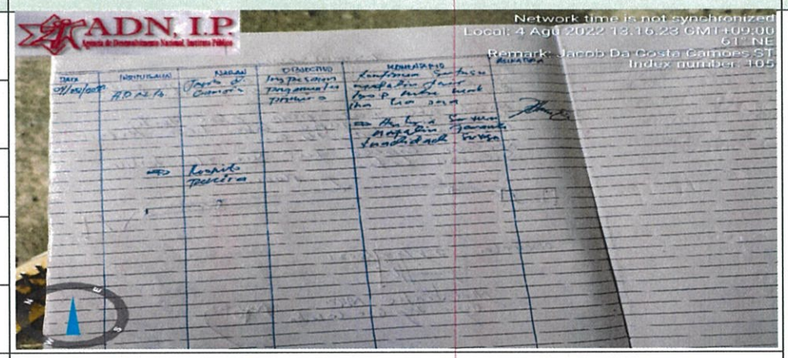
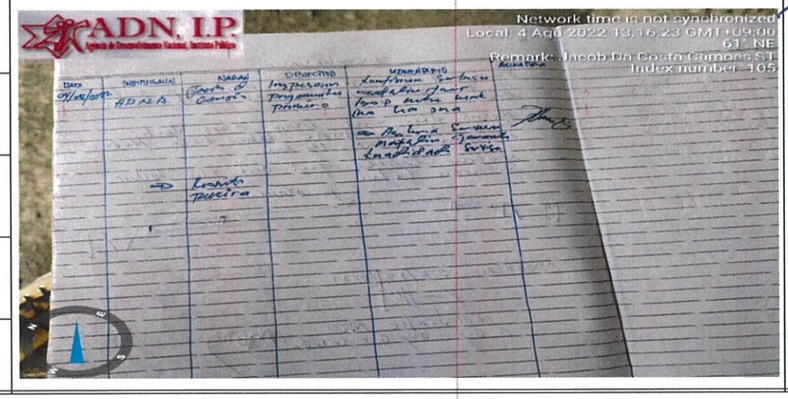
ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (BV-9)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800

Kompanha : Mexa

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	INSTRUSAUN TERENU IHA LIVRU VIZITA	Asinatura
I	04/5/08022	Baucau	Jacob Da costa Camoes	ENG. ADN I.P M. BAUCAU	1	Kompanha : NE halo servisu lao tarde los neduni ami husu kompanha tenki Aselera servisu ne atu nune halo hotutuir tempu de kontrato		
					2	Servisu tenki aselera tamba tarde liu		
					3	Aument trabalhador hodi halo servisu ho lalais		
					4	Material plumb concrete ho Macadam (penmark) tenki stok ona mai terenu hodi kontinua servisu		
					5	Tenki hatama relatorio labele liu data, 15-10-2021		
II					1	Husu ba kontraktor tenki hola sapatu boots entrega ba trabalhador hodi uza halo servisu		
					2	Tenki prepara palnu ho diak antes executa servisu		
					3	Husu ba Engineiru nafatin organiza trabalhador hodi aselera servisu		
					4	Tenki prepara relatorio kada loron no entrega ba ADN ho MOP wainhira to'o fulan remata		
					5			

#ANEXU C1 (BV-3)

Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025**
No. kontratu : **SSS/078/MOPTC-2017**

Data Inspesaun : 02 Agus 2022


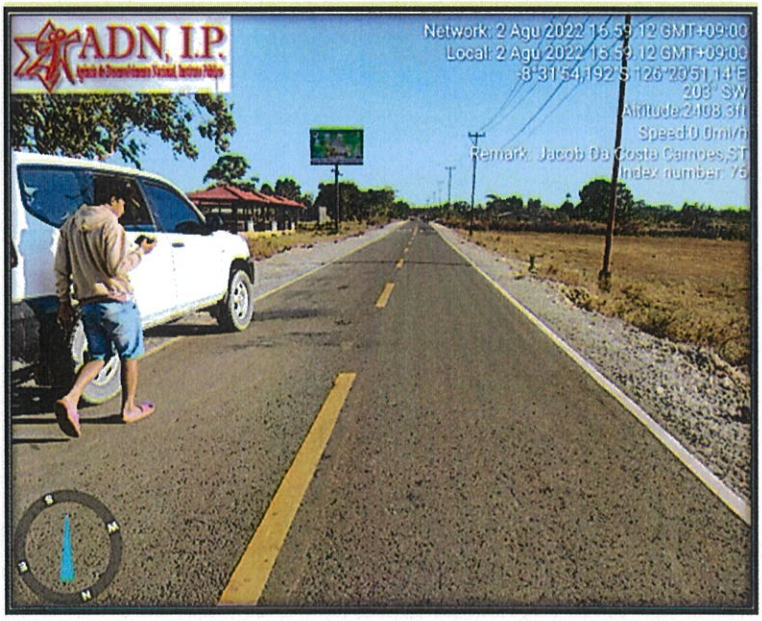
Fatin Inspesaun : Baucau, Triloka

Koordinadas :

Start Point : Long : -8.4899755, Latetude : 126.36965833

End Point : Long : -8.53136333, Latetude : 126.34772833

Naran Inspector : 1. Jacob da Costa Camoes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu AC-BC husi STA. 0+000 – 6 +025  Volume AC-BC = 6.025 x 5 x 0.06 = 18075 m3	

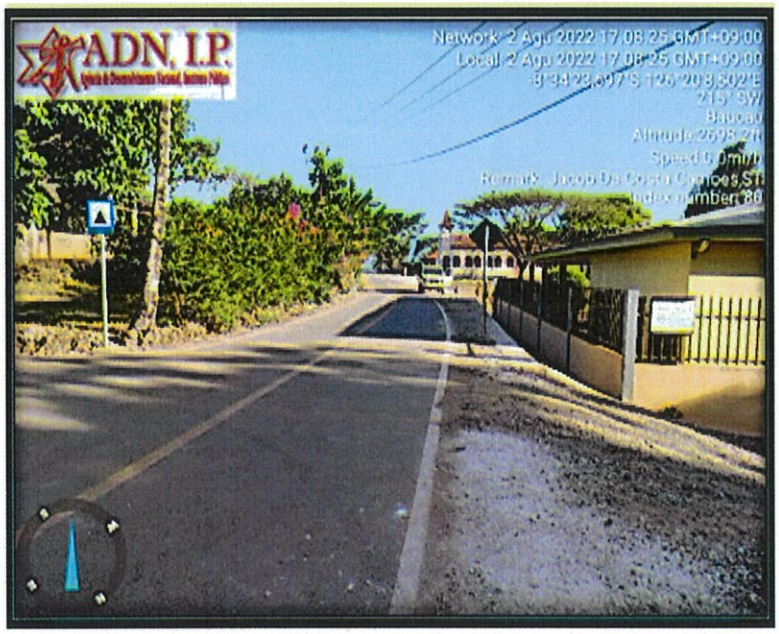
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

#ANEXU C1 (BV-3)

Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025**
No. kontratu : **SSS/078/MOPTC-2017**

Sketch Item servisu Surface Course/ Asphal



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (BV-3)

PROJECT DATA

Project Name	: Rehabilitation of Roads Jct. A01 Triloca - Jct. A06 Fatumaca - Loilubu - Jct. A06 Venilale road
Road Section	: Sta. 0+000 - 6+025 (Package I)
Contractor	: Domin Timor Diak Construction, Lda
Contract Number	: SSS/078/MOPTC-2017
Contract Date	: September, 12th 2017
Contruction Period	: 365 Days
Completion date	: May, 30th 2021
Defect Liability Period	: 365 Days
Contract Amount	: $ 3,599,951.87

ITEM NO	ITEM DESCRIPTION	AMOUNT (US$)		WEIGHT (%)	Progress Previus Fulan 1 - 7		Progress Phisic Julho		Progress Up to date	
		Original	Variation Order		Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)
100	GENERAL REQUIEMENT	$ 25,480.62	$ 25,480.62	0.71%	$ 18,635.86	0.52%	$ -	0.00%	$ 18,635.86	0.52%
200	EARTH WORKS	*$ 361,076.76*	*$ 346,362.23*	10.03%	$ 358,114.24	9.95%	$ -	0.00%	$ 358,114.24	9.95%
300	SUBBASE AND BASE COURSE	$ 1,240,459.52	$ 1,118,026.41	34.46%	$ 1,118,026.42	31.06%	$ -	0.00%	$ 1,118,026.42	31.06%
400	SURFACE COURSE	$ 1,383,899.14	$ 1,383,899.14	38.44%	$ 1,383,899.14	38.44%	$ 133,221.83	3.70%	$ 1,517,120.97	42.14%
500	BRIDGE CONSTRUCTION	$ 327,666.05	$ 23,474.41	9.10%	$ 23,474.41	0.65%	$ -	0.00%	$ 23,474.41	0.65%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 59,953.05	$ 492,645.06	1.67%	$ 314,684.16	8.74%	$ -	0.00%	$ 314,684.16	8.74%
700	MISCELLANEOUS STRUCTURES	$ 201,416.73	$ 210,063.99	5.59%	$ 12,353.23	0.34%	$ 3,903.68	0.11%	$ 16,256.91	0.45%
	GRANT TOTAL	**$ 3,599,951.87**	**$ 3,599,951.87**	**100.00%**	**$ 3,229,187.47**	**89.70%**	**$ 137,125.51**	**3.81%**	**$ 3,366,312.98**	**93.51%**

Inspeksaun Husi :

Eng. Jacob Da costa Camoes
Eng. Ba Projeito Insfrasturctura e Irigasaun , ADN, I.P

Verifika

Eng. Remigio Da.C. dos Santos
Eng. Senior ba Projeito
Insfrasturctura e Irigasaun ,

Certifika Husi :

Eng. Emerenciana Da costa Maia Freitas
Coord, da Unidade de Controlo e Validacao de Qualidade
ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

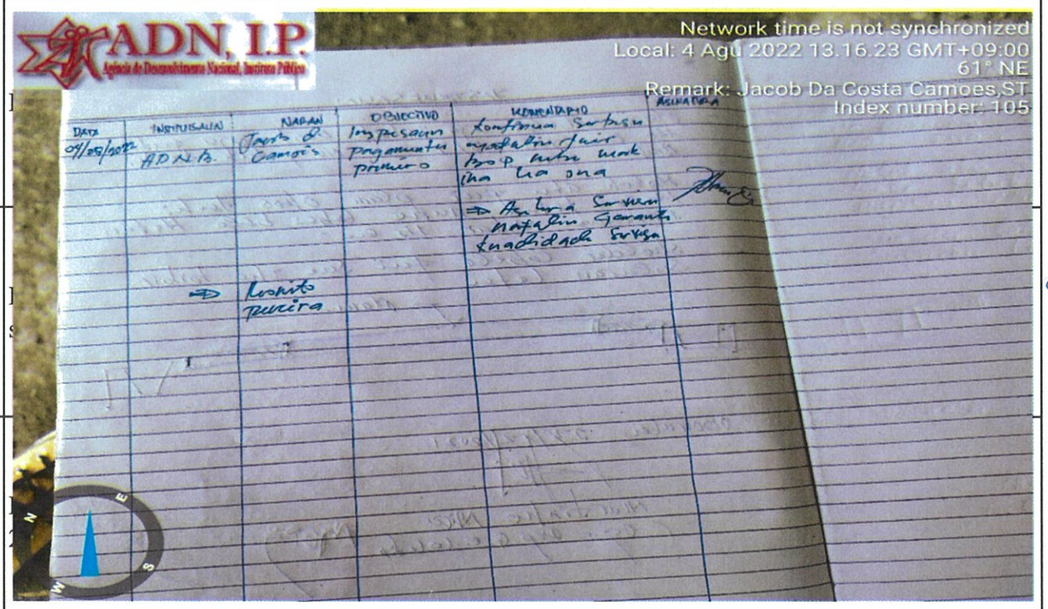
ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXU D (BV-3)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025

Kompanha : Domin Timor Diak. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	2/8/2022	Baucau Villa	Jacob da Costa Camoes	Eng. Baucau	1 2 3		

#ANEXU CI (BV-4)
Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075**
No. kontratu : **SSS/066/MOPTC-2017**

Data Inspesaun : 04 Jully 2022

Fatin Inspesaun : Baucau Vila, Triloka - Fatumaka

Koordinadas :


Start Point : Long : -8.53136333 Latetude : 126.34772833

End Point : Long : -8.57320340 Latetude : 126.335748333

Naran Inspector : 1. Jacob da Costa Camoes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

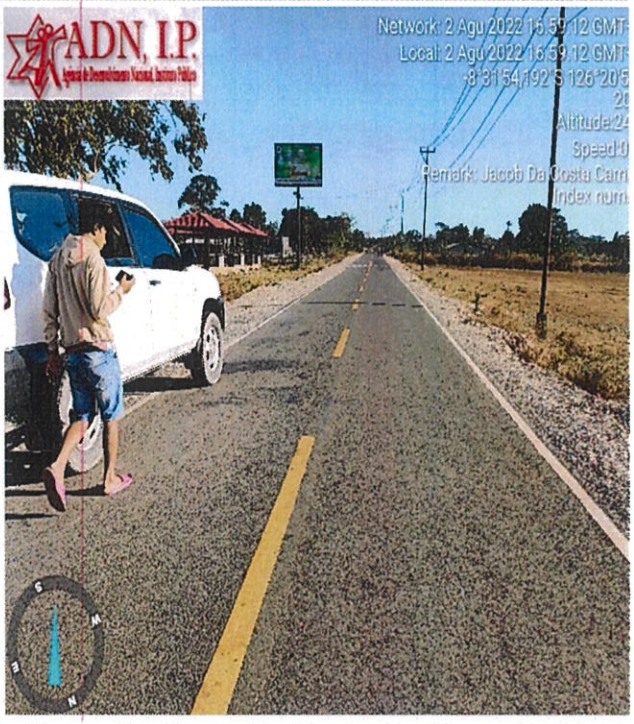
Sketch Item servisu Subbase, Base course and Asphal



Subbase course = 31.423 x 7 x 0.25 = 55 m3

Base Course = 3004.50 x 5 x0.20 = 3004.50 m3

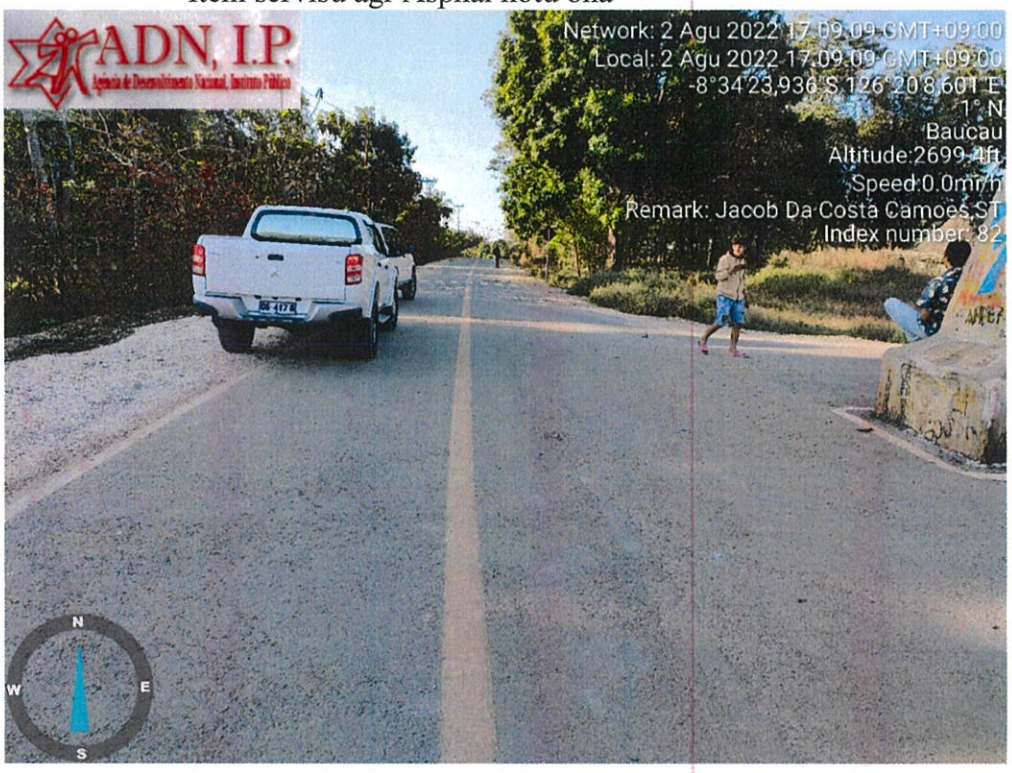
Prime coat = 6050 x 5 = 30250 m2



#ANEXU CI (BV-4)
Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075**
No. kontratu : **SSS/066/MOPTC-2017**

Item servisu agr Asphal hotu ona



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PROJECT DATA

#ANEXU C2 (BV-4)

Project Name: Rehabilitation of Roads Jct. A01 Triloca – Jct. A06 Fatumaca – Loilubu – Jct. A06 Venilale road

Road Section: Sta. 6+025 – 12+075 (Package II)

Contractor: Gihon Unipessoal, Lda

Contract Number: SSS/078/MOPTC-2017

SUMMARY

ITEM NO.	ITEM DESCRIPTION	ORIGINAL CONTRACT		Progres Phisic Previous 2022		Progres Phisic Julho 2022		Progres Phisic Up to date	
		Amount (USD)	Weight %	Amount (USD)	Weight %	Amount (USD)	Weight %	Amount (USD)	Weight %
100	GENERAL REQUIEMENT	$ 13,464.00	0.39%	$ 5,610.00	0.16%	$ -	0.00%	$ 5,610.00	0.16%
200	EARTH WORKS	$ 229,255.44	6.64%	$ 185,924.31	5.39%	$ 229,255.44	6.64%	$ 415,179.76	12.03%
300	SUBBASE AND BASE COURSE	$ 1,245,606.67	36.10%	$ 966,740.20	28.01%	$ 1,036,748.00	30.04%	$ 2,003,488.20	58.06%
400	SURFACE COURSE	$ 1,389,641.45	40.27%	$ 68,063.82	1.97%	$ -	0.00%	$ 68,063.82	1.97%
500	BRIDGE CONSTRUCTION	$ 131,299.24	3.80%	$ 22,425.80	0.65%	$ 117,680.09	3.41%	$ 140,105.89	4.06%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 240,183.43	6.96%	$ 116,789.85	3.38%	$ 240,183.43	6.96%	$ 356,973.28	10.34%
700	MISCELLANEOUS STRUCTURES	$ 201,416.73	5.84%	-	0.00%	201,416.73	5.84%	$ 201,416.73	5.84%
	GRANT TOTAL	$ 3,450,866.97	100.00%	$ 1,365,553.98	39.57%	$ 1,825,283.70	52.89%	$ 3,190,837.68	92.46%

Inspeksaun Husi :

Eng. Jacob Da Costa Camoes

Eng. Ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Verifika Husi :

Eng. Remogio Da.C.dos Santos

Eng. Senior ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Certifika Husi :

Eng. Emerenciana Da Costa Maia Freitas

Coordenadora Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

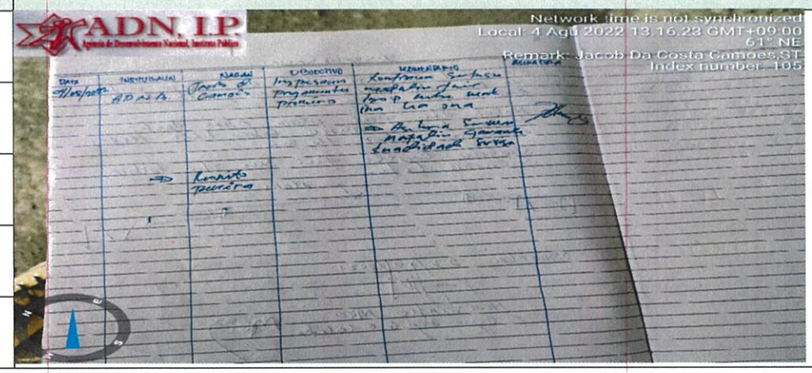
ADN, I.P. Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (BV-4)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075

Kompanha : Gihon Unip, Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	1/7/2021	Baucau Villa	Jacob da C. Camoes		1	Pagamentu neebe rekomenda ona iha tinan 2022 to agora seidauk selu.		
					2	Projeitu refere kompanha la iha ona lokasih tamba servisu ona		
					3			
					4			
					5			

ANEXU C1 (VEM-3)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality**
No. kontratu : **MPW-W-210048**

Data Inspesaun : 04 / 05/ 2022

Fatin Inspesaun :Vemasse, Osoala

Koordinadas :

Start Point : Long : -8.5945000 Latetude : 126.3072116

End Point : Long : -8.5874266 Latetude : 126.3119733

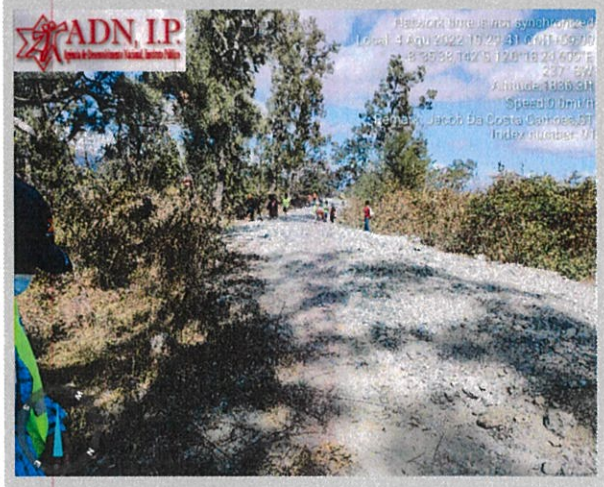
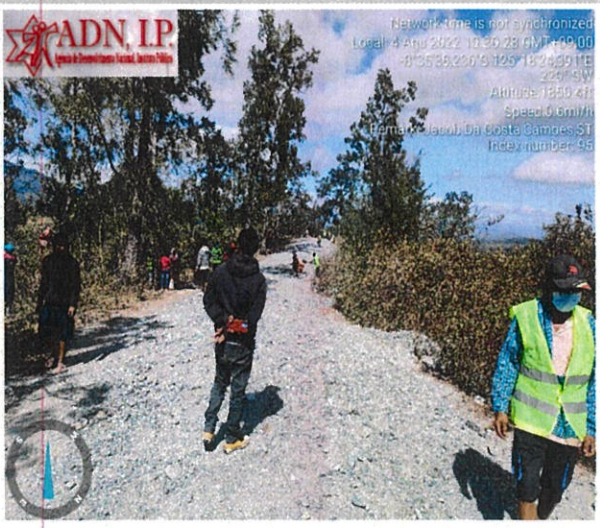
Naran Inspector : 1. Jacob Da costa Camoes

Sketch & Foto Desenho	*Observasaun iha tereno no Foto Aktual*
Item servisu **Papan Nama Projeit**	

ANEXU C1 (VEM-3)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality**
No. kontratu : **MPW-W-210048**

Item servisu Item Servisu **Gravel** *Long = 20 m3* *Volume = 0.16 x 3.5 x 20 = 11,2 m3*	Observasaun iha tereno no Foto Aktual 
Item servisu Item Servisu **Gravel** *Long = 20 m3* *Volume = 0.16 x 3.5 x 20 = 11,2 m3*	

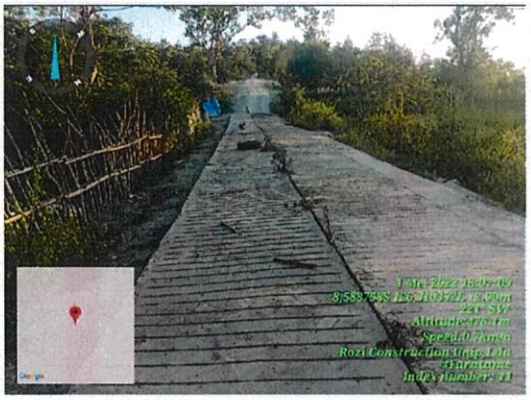
ANEXU C1 (VEM-3)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality**
No. kontratu : **MPW-W-210048**

Long = 194.25 m3

Volume = 194.25 x 0,15 x 1,75=50.990 m3





Traffic signboard

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (VEM-3)

Road name	Loilubu-Osso Ala
Municipality	Baucau
Postu	Vemasse
Sukos	Osso Ala

Chainage start	0+00
Chainage end	2+500
Length	2.500Km

SUMMARY

Item	Description	Summary original	Progress Phisic Junho		Progress Phisic Julho		Up to date	
			Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)
R-01	General works	$ 5,820.00	$ 5,238.00	1.38%	$ -	0.00%	$ 5,238.00	1.38%
R-03	Earth work	$ 34,480.96	$ 34,480.96	9.09%	$ -	0.00%	$ 34,480.96	9.09%
R-05	Sub-base, base and pavement	$ 19,017.38	$ 19,017.38	5.02%	$ -	0.00%	$ 19,017.38	5.02%
R-07	Bituminous pavement		$ -	0.00%			$ -	0.00%
R-08	Structures	$ 238,007.06	$ 170,089.53	44.86%	$ 79,371.08	20.93%	$ 249,460.60	65.80%
R-10	Dayworks	$ 750.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-11	Routine maintenance	$ 4,036.00	$ 274.00	0.07%	$ -	0.00%	$ 274.00	0.07%
R-12	Cleaning	$ 400.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-15	Provisional sum	$ 400.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	Construction cost	$ 302,911.40	$ 229,099.86	60.43%	$ 79,371.08	20.93%	$ 308,470.94	81.36%
B	Contractor Fee (A x 10%)	$ 30,291.14	$ 22,909.99	6.04%	$ 7,937.11	2.09%	$ 30,847.09	8.14%
C	General items	$ 38,501.02	$ 6,665.00	1.76%	$ -	0.00%	$ 6,665.00	1.76%
D	Construction tax (A+B+C x 2%)	$ 7,434.07	$ 5,173.50	1.36%	$ 1,746.16	0.46%	$ 6,919.66	1.83%
E	Total	$ 379,137.63	$ 263,848.34	69.59%	$ 89,054.35	23.49%	$ 352,902.69	93.08%

Inspesaun Hosi ;

Eng. Jacob Da costa Camoes

Eng.ba Projeito Infrastutura Tranporte e Irigasaun Municipio Baucau ADN,I.P

Verifika Husi .

Eng. Remigio Da C.S Dos Santos

Eng. Senior ba Projeito Infrastutura Tranporte e Irigasaun ADN,I.P

Certifika Husi .

Eng. Emerenciana da Costa M.Freitas

Cordenadora Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

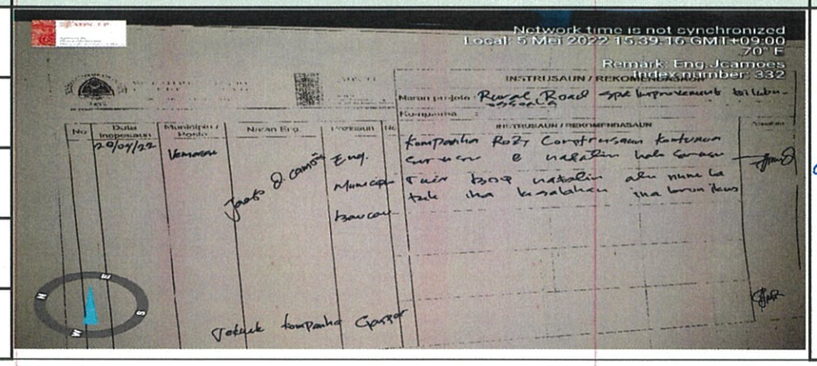
MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN
ANEXU D (VEM-3)

Naran projeto : R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality

Kompanha : Rozi const. unip. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
II	28/05/2022	Baucau Vemasse	Jacob da costa Camoes	Engineiru ADN Municipiu Baucau	1	Husu ba kontraktor aselera servisu		
					2	Kompanhia halo servisu diak e tuir Dezenho no BOQ		
					3	Prepara palnu ne'ebe diak atu submete mai 'ADN		
					4			
					5			

#ANEXU C1 (VEM-4)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality**
No. kontratu : **MPW-W-210051**

Data Inspesaun : 04/08/2022

Fatin Inspesaun : Vemasse, Ossoala

Koordinadas :

Start Point : Long : -8.5945000 Latetude : 126.3072116

End Point : Long : -8.5874266 Latetude : 126.3119733

Naran Inspector : 1. Jacob Da costa Camoes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
	

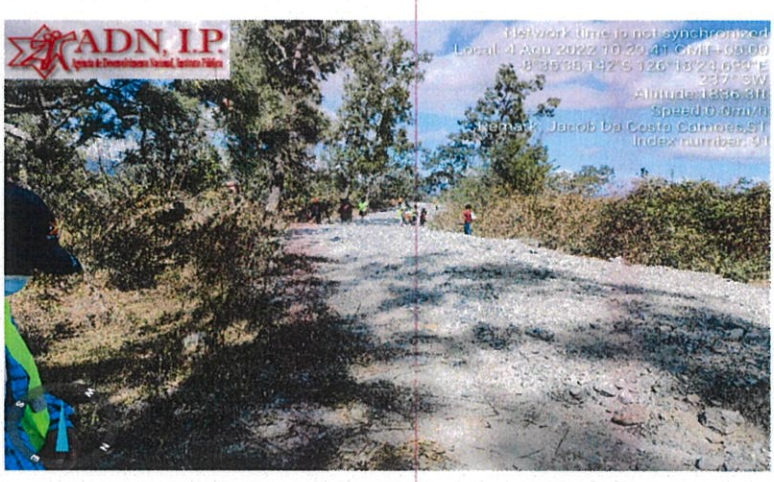
#ANEXU C1 (VEM-4)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality**
No. kontratu : **MPW-W-210051**

Item servisu Pengencooran Plum Concreate

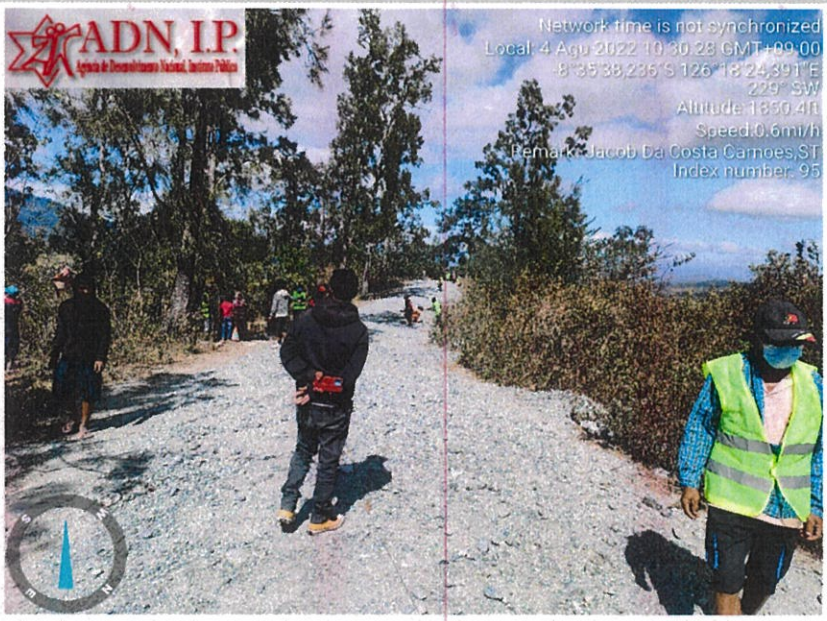
Long = 540 meter
Volume = 540 x 1,75 x 0.15 = 141, 75 m3



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Item servisu Pengencooran Plum Concreate

Long = 540 meter
Volume = 540 x 1,75 x 0.15 = 141, 75 m3



	Observasaun iha tereno no Foto Aktual

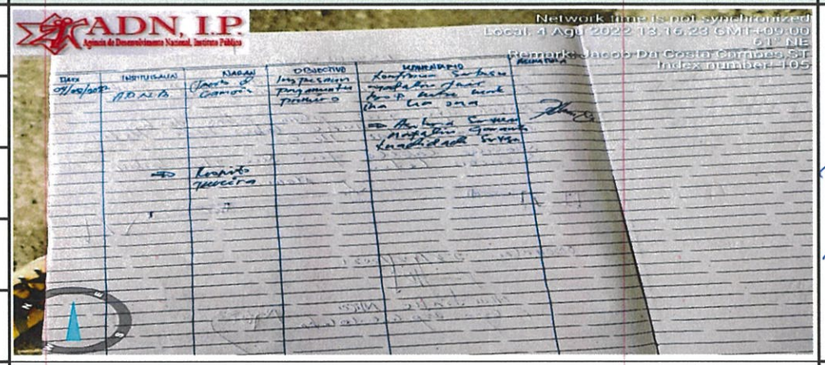
MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN
#ANEXU D (VEM-4)

Naran projeto : R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality

Kompanha : Rozi const. unip. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	28/05/2022	Baucau Vemasse	Jacob Da costa Camoes	Engineiru ADN Municipiu Baucau	1	Kontinua servisu tuir nafatin dezenho BOQ		
					2	Item servisu ba saluran, stone masonry hotu ona ho total masonry 469.696 m3		
					3			
					4			
					5			
					5			

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (VEM - 4)

Road name	Loilubu-Osso Ala
Municipality	Baucau
Postu	Vemasse
Sukos	Osso Ala

Chainage start	2+500
Chainage end	4+500
Length	2.000Km

SUMMARY

Item	Description	Amount (U$)	Progress Phisic Previous		Progress Phisic Jully		Up to date	
			Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)
R-01	General works	$ 5,620.00	$ 5,563.80	2.15%	$ -	0.00%	$ 5,563.80	2.15%
R-03	Earth work	$ 34,856.84	$ 34,508.27	13.35%	$ 100.00	0.04%	$ 34,608.27	13.39%
R-05	Sub-base, base and pavement	$ 21,592.74	$ 21,376.81	8.27%	$ 205.30	0.08%	$ 21,582.11	8.35%
R-08	Structures	$ 133,469.47	$ 132,134.78	51.11%	$ 500.00	0.19%	$ 132,634.78	51.30%
R-10	Dayworks	$ 750.00		0.00%	$ -	0.00%	$ -	0.00%
R-11	Routine maintenance	$ 2,930.00		0.00%	$ -	0.00%	$ -	0.00%
R-12	Cleaning	$ 400.00		0.00%	$ -	0.00%	$ -	0.00%
R-15	Provisional sum	$ 400.00		0.00%	$ -	0.00%	$ -	0.00%
				0.00%				
A	Construction cost	$ 200,019.05	$ 193,583.66	74.88%	$ 805.30	0.31%	$ 194,388.96	75.19%
B	Contractor Fee (A x 10%)	$ 20,001.90	$ 19,358.37	7.49%	$ 80.53	0.03%	$ 19,438.90	7.52%
C	General items	$ 33,444.49	$ 23,782.38	9.20%	$ -	0.00%	$ 23,782.38	9.20%
D	Construction tax (A+B+C x 2%)	$ 5,069.31	$ 4,734.49	1.83%	$ 17.72	0.01%	$ 4,752.20	1.84%
E	Total	$ 258,534.75	$ 241,458.89	93.40%	$ 903.54	0.35%	$ 242,362.44	93.74%

Inspesaun Husi :

(Eng. Jacob da Costa Camões)
Eng. ba Projeito Infraestrutura
Tranporte e Irigasaun Baucau, ADN.I.P

Verifika Husi :

(Eng. Remigio Da C.S. Dos Santos)
Eng. Senior ba Projeito Infraestrutura
Tranporte e Irigasaun ADN,I.P

Certifika Husi :

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora Unidade de Controlo e
Validasaun de Qualidade, ADN,I.P

#ANEXU C1 (BV-16)
Back-up Data

Naran Projeto : **NOVA CONSTRUCAO EBF-357 MAUCALE**
No. kontratu:

Data Inspesaun : Monday, 19 July 2022

Fatin Inspesaun : Baucau,Baucau Villa

Koordinadas :

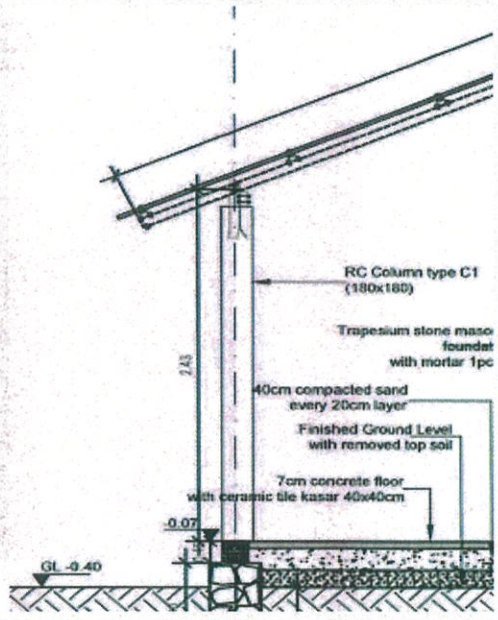
Start Point : Long:**E 15504387** ....., Latetude : **N 7119296** .....

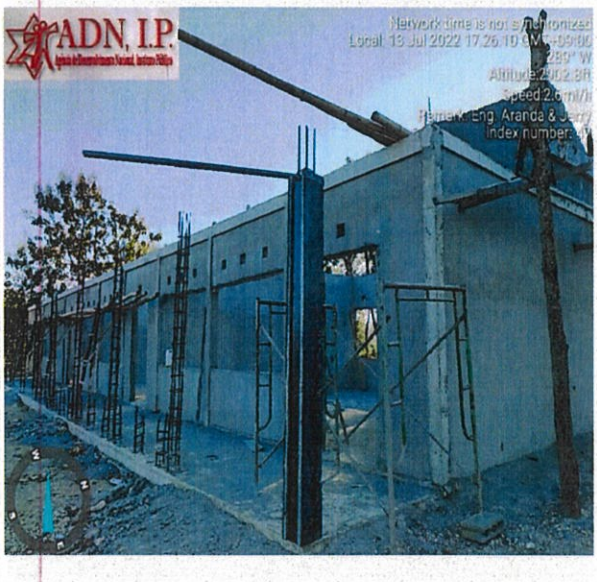
End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Eng. AGUSTINHO ARANDA

2. Eng. JERRY GIL M. PEREIRA

Sketch & Foto Desenho	Observ. iha tereno no Foto Aktual
Sketch Item servisu Sides of columns above ground level (kolom diatas permukaan tanah) typu RC Column C1 (180x 180)	Reinforced Concrete Grade 25Mpa (mutu beton 25Mpa)





#ANEXU C1 (BV-16)
Back-up Data

Naran Projeto : **NOVA CONSTRUCAO EBF-357 MAUCALE**
No. kontratu:

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Item servisu reboka/plasteran	Tebal/mahar plaster/reboka 1,5cm
Tuir observasaun visual ITEM servisu plasteran lao dadaun Atinji ona 40%	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Data Inspesaun : Thursday, February 10, 2022

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (BV-17)

NARAN PROJETU : NOVA CONSTRUCAO EBF-357 MAUCALE
FATIN PROJETU : GARIUAI-BAUCAU-BAUCAU
PROJETU NAIN : MEJD

MAIN SUMMARY			PROGRESS July 2022					
			Previous		This Bill		Up do date	
NO	DESCRIPTION	AMOUNT (USD)	Amount $	Weigh %	Amount $	Weigh %	Amount $	Weigh %
I	PRELIMINARIES	3,144.97	$ 1,609.99	1.4%	$ -	0.00%	$ 1,609.99	1.36%
II	CLASSROOM BUILDING Ca	64,183.71	$ 21,160.97	17.9%	$ 6,260.61	6.59%	$ 27,421.58	24.50%
III	PROVISIONAL SUM FOR SITEWORKS	6,846.56	$ -	0.0%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**74,175.23**	**22,770.96**	**19.3%**	**6,260.61**	**6.59%**	**29,031.56**	**25.868%**
B	CONTINGENCY	3,000.00	$ -	0.0%	$ -	0.00%	$ -	0.00%
D	OVERHEAD	6,340.00	$ 2,271.00	1.92%	$ -	0.00%	$ 2,271.00	1.92%
E	**TOTAL COST (A + B)**	**83,515.23**	**17,699.42**	**21.19%**	**5,509.76**	**6.60%**	**23,209.18**	**27.79%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Eng.Jerry Gil M. Pereira
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Francisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL


ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (VEN -9)
INSTRUSAUN / REKOMENDASAUN

Naran projeto :NOVA CONSTRUCAO PRE ESKOLAR-1347 AMIZADE VENILALE

Kompanha : Grupo Komunitario

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Tuesday, July 19, 2022	Venilale , Uailaha	Eng.Agustinho Aranda	Eng.Adn Baucau	1	Husu ba Eng. Grupo mantein nafatin iha tereno hodi bele garantia kualidade obra		
					2	Servisu kontinua lao nafatin tir BOQ no Dezenu ne'ebe iha kontratu		
			Eng. Jerry Gil M. Pereira		3	konaba eltrisidade depois ekipa husi ADN, I.P Electricidade sei halo inspesaun		
					4	Halo As Built - drawing karik iha mudansa		
					5	Aselera Servisu		

#ANEXU C1 (VEN-9)

Back-up Data

Naran Projeto : **NOVA CONSTRUCAO PRE ESKOLAR-1347 AMIZADE VENILALE**
No. kontratu :

Data Inspesaun : Wednesday, July 13, 2022

Fatin Inspesaun : **Baucau, Venilale, Uailaha**

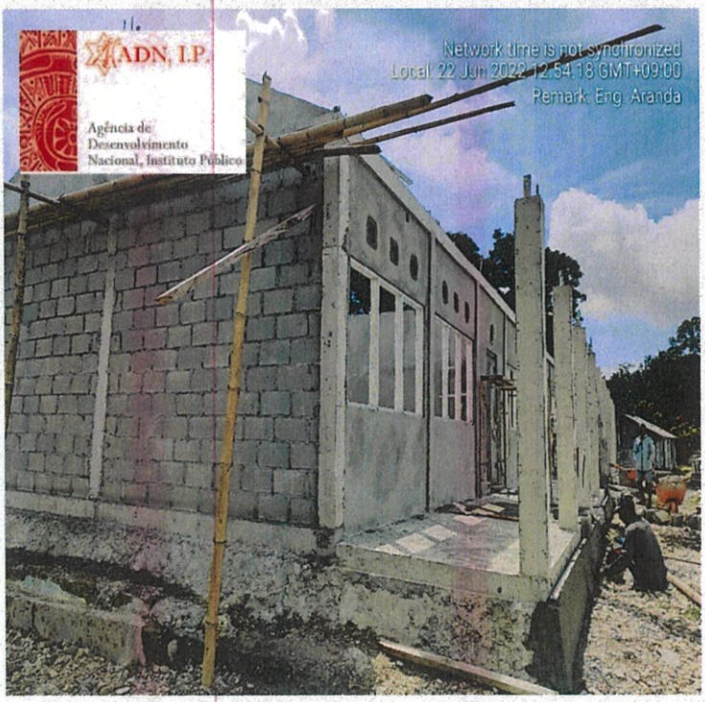
Koordinadas :

Start Point : Long: ....., Latetude : .....

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

2. Jerry Gil M. Pereira

Foto iha terenu	*Observa/Recommend. iha tereno*
	1. Ba kolom no sloof nebe kropos tenki hadia 2. Eng.grupo tenki prepara relatori progress

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

NARAN PROJETU : **NOVA CONSTRUCAO PRE ESKOLAR-1347 AMIZADE VENILALE**
FATIN PROJETU : **UATOACO-VENILALE-BAUCAU**
PROJETU NAIN : **MEJD**

#ANEXU C2 (VEN-9)

MAIN SUMMARY

NO	DESCRIPTION	AMOUNT (USD)	PROGRES ACTUAL JULY					
			PREVIOUS		THIS BILL		UP TO DATE	
I	PRELIMINARIES	3,254.31	$ 1,538.58	1.72%	$ -	0.00%	$ 1,538.58	1.72%
II	CLASSROOM BUILDING C2	64,688.96	$ 23,406.76	26.13%	$ 8,701.36	9.71%	$ 32,108.12	35.84%
III	PROVISIONAL SUM FOR SITEWORKS	12,298.48	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**80,241.75**	$ 24,945.34	27.85%	$ 8,701.36	9.71%	$ 33,646.70	37.56%
B	CONTINGENCY	3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
IV	OVER HEAD	6,340.00	$ 2,605.00	2.91%	$ -	0.00%	$ 2,605.00	2.91%
C	**TOTAL COST (A + B + C)**	**89,577.35**	$ 27,550.34	30.76%	$ 8,701.36	9.71%	$ 36,251.70	40.47%

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Eng.Jerry Gil M. Pereira
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Françisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (BV-17)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NOVA CONSTRUCAO EBF-357 MAUCALE

Kompanhia : Grupo Komunitario

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
1	Monday, July 19, 2021	Baucau Villa	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Mantein Linha kordenasaun entre grupo no Dono de projeto Tanba iha kolom Baluh baluh kropos tenki hadia		
					2	Mantein Linha kordenasaun entre grupo no Dono de projeto hodi mantein kualidade no finaliza tuir tempo ne'ebe determina		
					3	Eng. Grupo presija halo Time Schedule plano atual taka iha Quadro informasaun		
			Eng. Jerry Gil M. Pereira		4	Eng. Grupo presija Tenki tau atensaun ba ITEM kolom tenki dimensi hanesan hotu tuir BOQ no dezenho ne'ebe iha		
					5	Servisu tenki nafatin lao tuir matadalan tekniku ne'ebe anexu iha kontratu		

#ANEXU C1 (LA- 7)
Back-up Data

Naran Projeto : **NEW CONSTRUCTION OF CAMPAS AND LEVELING, PAVEMENT WORKS IN GARDEN HEROIS LAGA**

No. kontratu : **40/MACLN/X/2021**

Data Inspesaun : Thursday, July 07, 2022

Fatin Inspesaun : Baucau , Laga

Koordinadas :

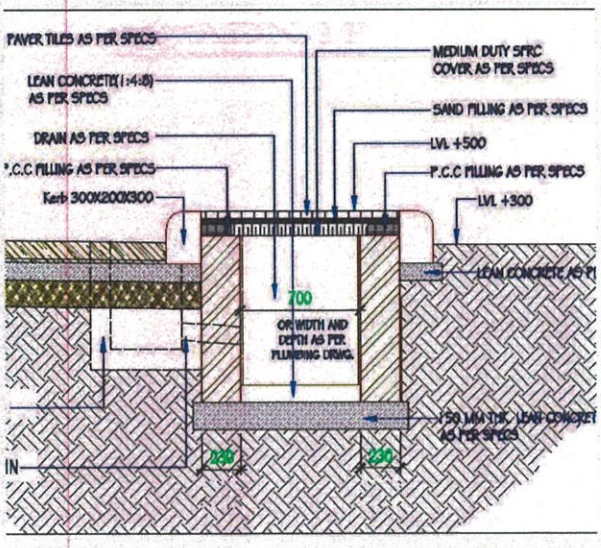
Start Point : Long: **-8.448589**....., Latetude : **126.476555**.....

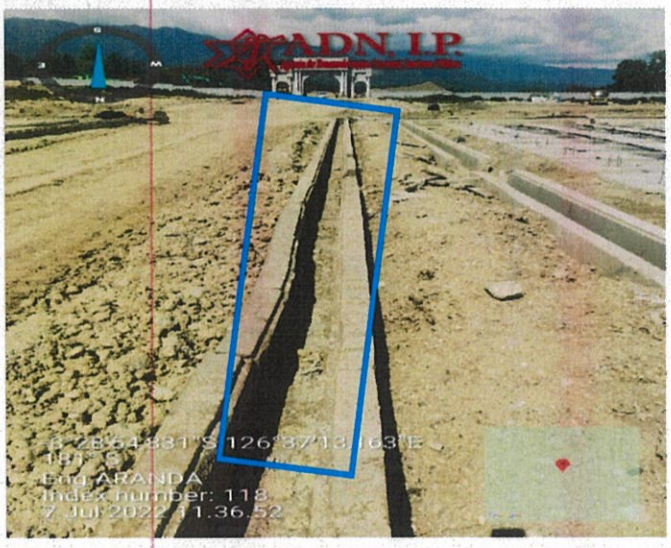
End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

2. Jerry Gil M. Pereira

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item Servisu **DRAINAGE AND SLOPE PROTECTION WORKS**	• Drainase nebe sira hada kuaze qualidade la diak tan ne Ekipa AND, I,P husu site eng,tenki sobu no hada tuir composisi nebe iha boq laran



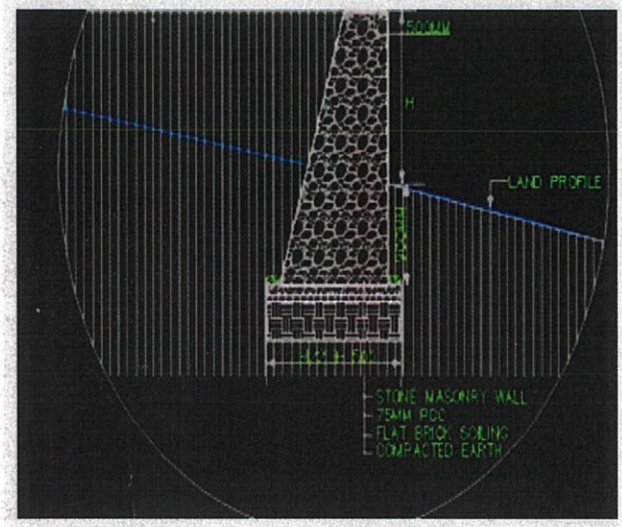


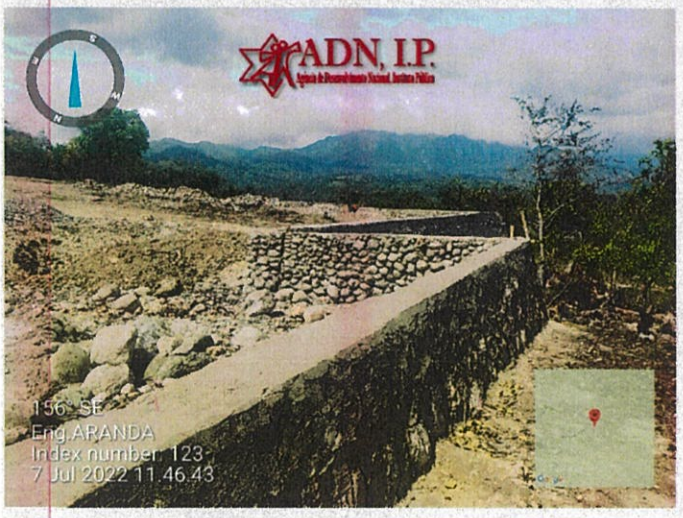
#ANEXU C1 (LA- 7)
Back-up Data

Naran Projeto : **NEW CONSTRUCTION OF CAMPAS AND LEVELING, PAVEMENT WORKS IN GARDEN HEROIS LAGA**

No. kontratu : **40/MACLN/X/2021**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item Servisu **Wall protection**	Wall protection Stone Masonry





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU C2 (LA-7)

PROJECT OWNER : MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÂO NACIONAL
PROJECT NAME : NEW CONSTRUCTION OF CAMPA AND LEVELING, PAVEMENT WORKS IN GARDEN HEROIS LAGA
LOCATION : LAGA, BAUCAU, TIMOR-LESTE

SUMMARY OF COST ESTIMATION

No.	ITEM DESCRIPTION	TOTAL BIAYA (US $)	PREVIOUS		THIS BILLING		UP TO DATE	
			AMOUNT (US $)	WEIGHT %	AMOUNT (US $)	WEIGHT %	AMOUNT (US $)	WEIGHT %
100	GENERAL REQUIREMENTS	$ 5,100.00	$ 4,080.00	0.80%	$ -	0.00%	$ 4,080.00	0.80%
200	EARTH WORKS	$ 79,332.72	$ 12,763.39	2.49%	$ 0.00	0.00%	$ 12,763.39	2.49%
500	CAMPAS WORKS	$ 173,515.50	$ 112,575.00	21.96%	$ -	0.00%	$ 112,575.00	21.96%
600	DRAINAGE AND SLOPE PROTECTION WORKS	$ 25,411.62	$ -	0.00%	$ 5,026.90	0.98%	$ 5,026.90	0.98%
700	MISCELLANEUS STRUCTURE	$ 76,196.70	$ -	0.00%	$ -	0.00%	$ -	0.00%
800	NEW WELL DRILL AND INSTALLATION WATER PUMP AUBMERSIBLE AND INTELLIGENCY RECTRACTABLE GATE	$ 55,895.13	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**TOTAL CONSTRUCTION COST**	**$ 415,451.67**	**$ 129,418.39**	**25.25%**	**$ 5,026.90**	**0.98%**	**$ 134,445.29**	**26.23%**
B	CONTRACTOR FEE (10 X A)	$ 41,545.17	$ 12,941.84	2.52%	$ 502.69	0.10%	$ 13,444.53	2.62%
C	OVER HEAD	$ 4,850.00	$ 1,616.67	0.32%	$ -	0.00%	$ 1,616.67	0.32%
D	TAX (2% X (A+B+C)	$ 9,236.94	$ 2,879.54	0.56%	$ 110.59	0.02%	$ 2,990.13	0.58%
E	CONTIGENCY 10%	$ 41,545.17	$ 5,982.01	1.17%	$ 25,000.00	4.88%	$ 30,982.01	6.04%
F	**GRAND TOTAL (A+B+C+D+E)**	**$ 512,628.94**	**$ 152,838.44**	**29.81%**	**$ 30,640.18**	**5.98%**	**$ 183,478.62**	**35.79%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro ADN, I. P. Municipio de Baucau

Eng.Jerry Gil M. Pereira
Engineiro ADN, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ...../ 2022

Eng/Arch.Françisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico
Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN , I. P.

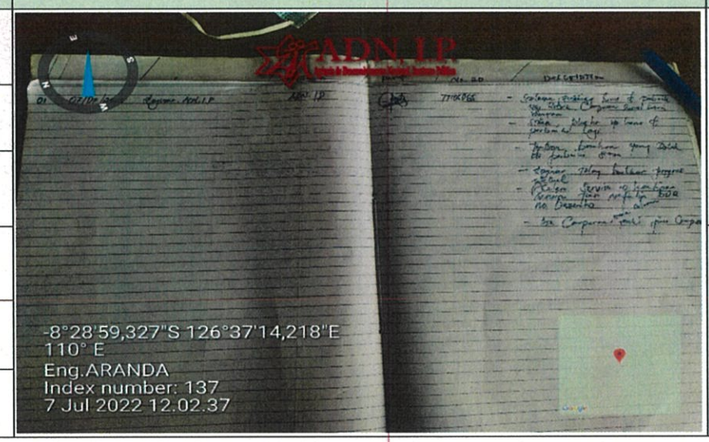
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (LA-7)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NEW CONSTRUCTION OF CAMPAS AND LEVELING, PAVEMENT WORKS IN GARDEN HEROIS LAGA

Kompanhia : Jugatefiga Unipessoal Lda

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Thursday, July 07, 2022	Baucau ,Laga	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Saluran Finishing harus di Perbaiki yang retak ,Canpuran harus sesuai		
					2	Plester Stair harsu di perbaiki lagi		
					3	Tembok Penahan yang retak harus di perbaiki semua		
			Eng.Jerry Gil M. Pereira		4	Engineer harus buatkan Progress Plan sama Aktual		
					5	**ASELERA SERVISU no kontunia nafatin Boq no Dezenho nebe iha**		

#ANEXU CI (QUE-3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343**

Data Inspesaun : 28 – 07 - 2022

Fatin Inspesaun : Darabata Bere, Lelalai, Walikoko, Daramutu, Waibobo & Boronaha

Koordinadas :

Start Point : Long : 8.64415542S, Latetude : 126.49730992E

End Point : Long : 8.62737446S, Latetude : 126.48035273E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 m Pinta mos ona	

#ANEXU CI (QUE-3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Treckschoor mamar & Pondasi rahun/nakfera	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 m halis ou kleuk	

#ANEXU CI (QUE-3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343**

Warning sign monu



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….	
Ai besik iha linha Media tensaun	



#ANEXU C1 (VEM – 1)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District**

No. kontratu : **RDTL-11003725**

Data Inspesaun : **26 - 07 - 2022**

Fatin Inspesaun : Vemasse – Cairaebela - Waicoa

Koordinadas :

Start Point : Long : 8.52708673S, Latetude : 126.18276804E

End Point : Long : 8.48282723S, Latetude : 126.27878275E

Naran Inspector : **Adonis Julio Fernandes**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Start point project	

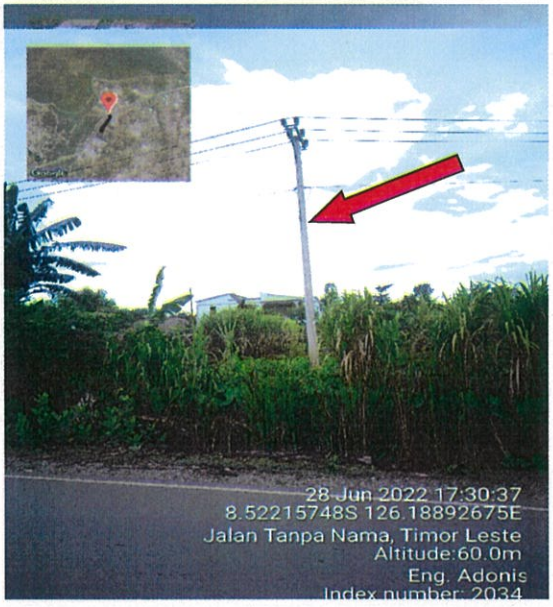
#ANEXU C1 (VEM – 1)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District**

No. kontratu : **RDTL-11003725**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Fiu Baixadas kois / kotu	

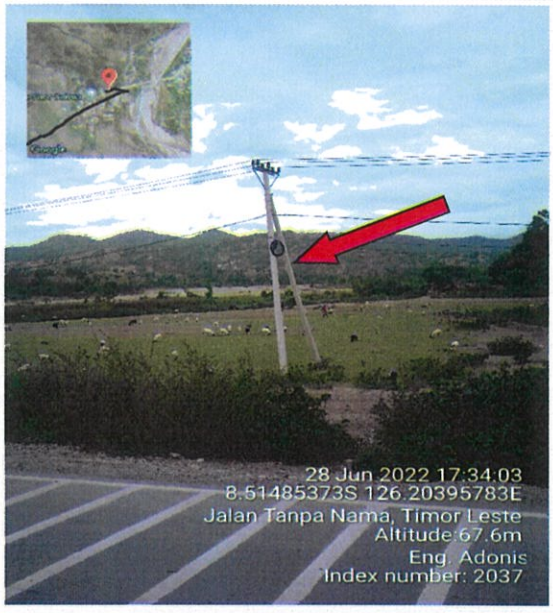
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste halis & treckschoor kotu	

#ANEXU C1 (VEM – 1)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District**

No. kontratu : **RDTL-11003725**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Assecores Druckschoor seidauk installa	

#ANEXU C1 (VEN – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344**

Data Inspesaun : 26 – 07 - 2022

Fatin Inspesaun : Uaihacu, Tugu - Venilale

Koordinadas :

Start Point : Long : 8.64382205S, Latetude : 126.37762811E

End Point : Long : 8.65001927S, Latetude : 126.37896519E

Naran Inspector : **Adonis Julio Fernandes**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Lauja pipa galvanized ba ending TR	

#ANEXU C1 (VEN – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Treckschoor mamar & Poste halis	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 pinta mos ona	

#ANEXU C1 (VEN – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Ai besik iha linha	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Climber protection no warning sign seidauk installa	

#ANEXU C1 (BA – 1)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

Data Inspesaun : 28 – 07 - 2022

Fatin Inspesaun : Buava & Defawasi

Koordinadas :

Start Point : Long : 8.5780543S, Latetude : 126.6795899E

End Point : Long : 8.6063765S, Latetude : 126.68644416E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Treckschoor mamar	

#ANEXU C1 (BA – 1)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 12 m halis ou kleuk	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 m pondasi rahun/ lauja besi	

#ANEXU C1 (BA – 1)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Poste 12 m pinta mos ona no treckschoor mamar	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

#ANEXU C1 (BV – 2)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN: 00000340**

Data Inspesaun : 27 – 07 - 2022

Fatin Inspesaun : Uani Uma, Keraboe, bodo kho, kaibada makasae, Lutumutu

Koordinadas :

Start Point : Long : 8.45470674S, Latetude : 126.44196355S

End Point : Long : 8.44889296S, Latetude : 126.43876642E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12m treckschoor mamar	

#ANEXU C1 (BV – 2)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN: 00000340**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Acessores bac abo baixadas seidauk installa	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Start point	

#ANEXU C1 (BV – 2)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN: 00000340**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Coneksaun arde kotu	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 12m halis / kleuk	

#ANEXU C1 (BV-18)

Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA TECNICA VOCACIONAL BAUCAU**

No. kontratu :

Data Inspesaun : Wednesday, 06 July 2022

Fatin Inspesaun : Baucau,Baucau Villa

Koordinadas :

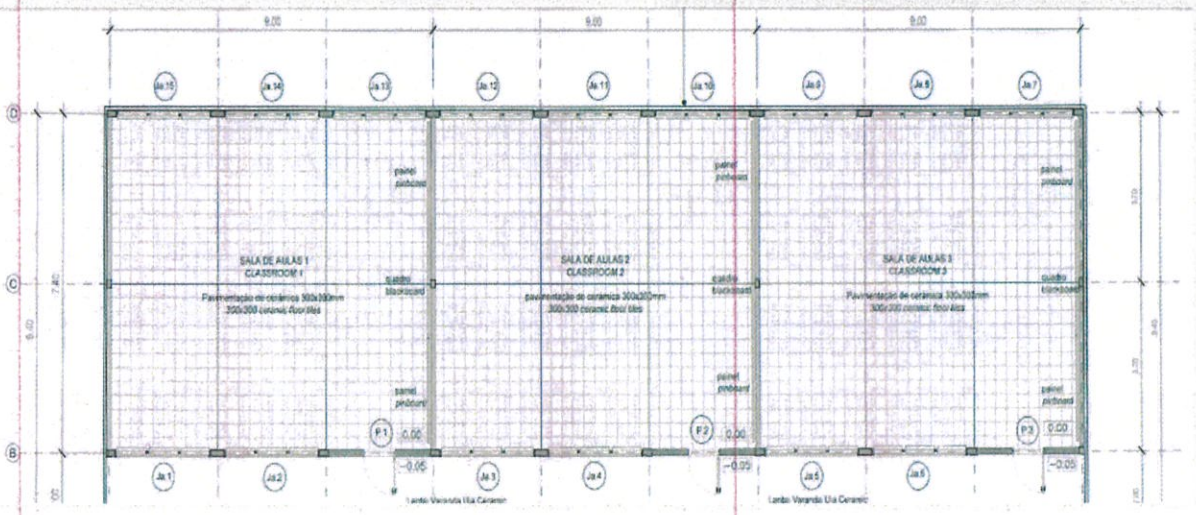
Start Point : Long:**E 15504387** ....., Latetude : **N 7119296** .....

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Eng. AGUSTINHO ARANDA

2. Eng. JERRY GIL M. PEREIRA

Sketch & Foto Desenho	Observ. iha tereno no Foto Aktual
Sketch Item servisu 50mm thick ground slab, horizontal, laid in bays between isolation joints as per drawings (50mm tebal pengecoran lantai yang dicor secara berpetak diantara konstruksi joint sesuai gambar)	CONCRETE (Pekerjaan Beton) 



#ANEXU C1 (BV-18)
Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA TECNICA VOCACIONAL BAUCAU**

No. kontratu :

Data Inspesaun : Monday, 19 July 2022

Fatin Inspesaun : Baucau,Baucau Villa

Koordinadas :

Start Point : Long:**E 15504387** ....., Latetude : **N 7119296** .....

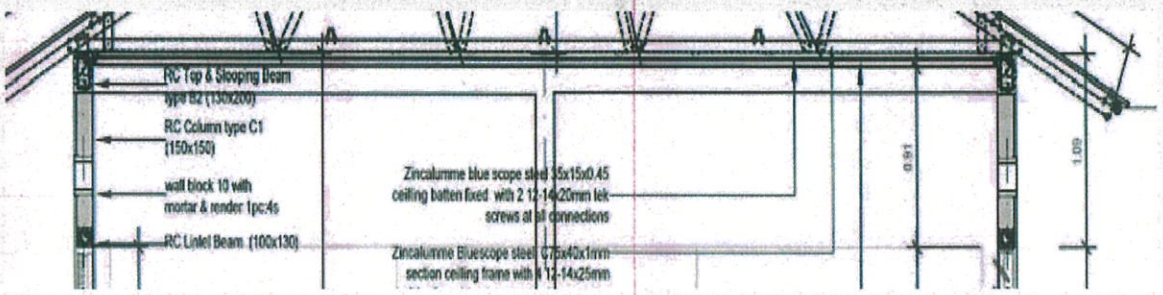
End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Eng. AGUSTINHO ARANDA

2. Eng. JERRY GIL M. PEREIRA

Sketch & Foto Desenho	Observ. iha tereno no Foto Aktual
Sketch Item servisu 12mm diameter bars in Lintel BEAMS (besi ulir untuk balok latai dia 12mm) and 8mm diameter bars as ligatures in ground beams (begel diameter 8mm untuk sloof) ***type RC Lintle Beam (100x130)***	Reinforcement (besi beton) Plain round mild steel bar reinforcement (besi beton polos)





MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PROJECT NAME : **NOVA CONSTRUÇÃO ESCOLA TECNICA VOCACIONAL BAUCAU**
NO CODE EMIS : 1117

#ANEXU C2 (BV-18)

LOCATION : **SUCO BUIBAU, POSTO ADMINISTRATIVO BAUCAU, MUNICIPIO BAUCAU.**

Summary			PROGRESS Juny 2022					
			Previous		Up to Date		This Bill	
No	ITEM SERVISU	VERIFIED BY A D N	Amount $	Weigh %	Amount $	Weigh %	Amount $	Weigh %
1	Preleminaries Work	$ 3,075.00	$ -	0.00%	$ 1,537.50	1.30%	$ 1,537.50	1.30%
2	Class Room Building C	$ 54,919.08	$ -	0.00%	$ 14,010.77	11.86%	$ 14,010.77	11.86%
3	Techer Office	$ 78,538.28	$ -	0.00%	$ 14,163.77	11.99%	$ 14,163.77	11.99%
5	Professiona Sum For Site Works	$ 18,285.21	$ -	0.00%	$ -	0.00%	$ -	0.00%
I	**Total Constructio Cost**	**$ 154,817.57**	**$ -**	**0.00%**	**$ 29,712.04**	**25.15%**	**$ 29,712.04**	**25.15%**
II	**Overhead**	**$ 6,340.00**	**$ -**	**0.00%**	$ 2,681.00	2.27%	$ 2,681.00	2.27%
III	**Contigency**	**$ 3,000.00**	$ -	0.00%	$ -	0.00%	$ -	0.00%
IV	**Grand Total**	**$ 164,157.57**	**$ -**	**0.00%**	**$ 32,393.04**	**27.41%**	**$ 32,393.04**	**27.41%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Eng.Jerry Gil M. Pereira
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Francisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação
de Qualidade ADN , I. P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

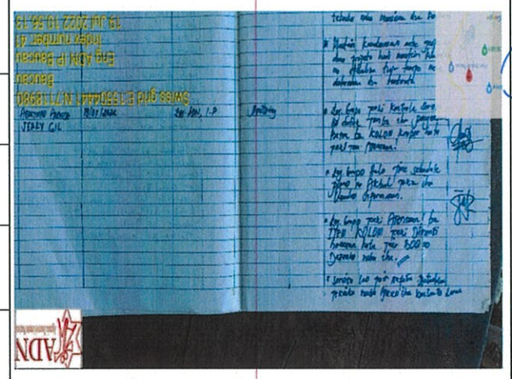
ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (BV-18)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NOVA CONSTRUÇÃO ESCOLA TECNICA VOCACIONAL BAUCAU

Kompanhia : Grupo Komunitario

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Monday, July 19, 2021	Baucau Villa	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Mantein Linha kordenasaun entre grupo no Dono de projeto Tanba iha kolom Baluh baluh kropos tenki hadia		
					2	Mantein Linha kordenasaun entre grupo no Dono de projeto hodi mantein kualidade no finaliza tuir tempo ne'ebe determina		
					3	Eng. Grupo presija halo Time Schedule plano atual taka iha Quadro informasaun		
			Eng. Jerry Gil M. Pereira		4	Eng. Grupo presija Tenki tau atensaun ba ITEM kolom tenki dimensi hanesan hotu tuir BOQ no dezenho ne'ebe iha		
					5	Servisu tenki nafatin lao tuir matadalan tekniku ne'ebe anexu iha kontratu		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

Naran Eng.	AGUSTINHO ARANDA
Municipio / Posto	MUNICIPIO BAUCAU NO POSTOS

INSPECTION PLAN 2022

JULY

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
BAUCAU VILLA	1	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Co. Cactus Unip. Lda	PLAN																																	FHO
							ACTUAL																																	
	2	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Central Hill Unipessoal Lda	PLAN																																OG GOING
							ACTUAL																																
	3	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Sanira Construction Unip Lda	PLAN																																	ABANDONA
							ACTUAL																																
	4	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Rozi Unipessoal, Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																
	5	konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Gardel Unipessoal.Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																
	6	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Talamori	PLAN																																	ON GOING
							ACTUAL																																
	7	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAUCALE	PLAN																																	ON GOING
							ACTUAL																																
	8	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ZONA GOLGOTA	PLAN																																	ON GOING
							ACTUAL																																
	9	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	PLAN																																	ON GOING
							ACTUAL																																
	10	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPEC/ESTV BAUCAU	PLAN																																	ON GOING
							ACTUAL																																
	11	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	Plan																																	ON GOING
							ACTUAL																																
	12	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	PLAN																																	ON GOING
							ACTUAL																																
	13	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESG NO. 01 BAUCAU	PLAN																																	ON GOING
							ACTUAL																																
	1	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Sumber Urip Unip. Lda	PLAN																																	PHO
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Costa Estelia Unipessoal,Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Laga	3	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																	ON GOING
							ACTUAL																																	
	4	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF LALA-BU'U	PLAN																																	ON GOING
							ACTUAL																																	
	5	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																	ON GOING
							ACTUAL																																	
	6	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	PLAN																																	ON GOING
							ACTUAL																																	
	7	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	PLAN																																	ON GOING
							ACTUAL																																	
Baguia	1	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Mexa Unip.lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							Actual																																	
	2	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF GULARI	PLAN																																	ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																	
	3	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF OSSU-UFULARI	PLAN																																	ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																	
	4	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UACALA	PLAN																																	ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																	
	5	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE FINI BAGUIA	PLAN																																	ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																	
	6	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE LARI-SULA	PLAN																																	ON GOING
							ACTUAL																																	
	7	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC OSSU-HUNA	Plan																																	ON GOING
							Actual																																	
	8	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC BUAUA LAVATERI	PLAN																																	ON GOING
							ACTUAL																																	
	9	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGF DE BAGUIA	PLAN																																	ON GOING
							ACTUAL																																	
Venilia	1	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Wetodo Unip. Lda	PLAN																																	ON GOING
							ACTUAL																																	
	2	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Caidara Lata Unipessoal,Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																	
	3	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC UAI-BUA	PLAN																																	ON GOING
							ACTUAL																																	

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Ie	4	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CULINA-OSSU-UAILALE	PLAN																																ON GOING
							ACTUAL																																
	5	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	PLAN																																ON GOING
							ACTUAL																																
Quelicai	1	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Jova Construction Unip. Lda	PLAN																																ON GOING
							ACTUAL																																
	2	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Samadare Unip. Lda	PLAN																																ON GOING
							ACTUAL																																
	3	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UADA-BORU	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	4	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAI-ACA/MULIA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	5	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ABO-LIR LALETEK	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	6	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC LETEMUMO	PLAN																																ON GOING
							ACTUAL																																
	7	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	8	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CATOLICA DARENAFA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	9	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAURO DARALA/BORUMODO	PLAN																																ON GOING
							ACTUAL																																
	10	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAIDORA/OSSOLIA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
Vemasse	1	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Esa-Un	PLAN																																ABANONA
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Wrangler Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																

Note:

Periode inspesaun iha tereinu | **Implementasaun Plano Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Agustinho Aranda)
Eng. Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi :

(Eng.Januario maia Guterres)
Adjunto Director Executivo ADN , I. P.

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

Naran Eng.	JERRY GIL M. PEREIRA
Municipio / Posto	MUNICIPIO BAUCAU NO POSTOS

INSPECTION PLAN 2022

JULY

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
BAUCAU VILLA	1	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Co. Cactus Unip. Lda	PLAN																																	FHO
							ACTUAL																																	
	2	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Central Hill Unipessoal Lda	PLAN																																OG GOING
							ACTUAL																																
	3	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Sanira Construction Unip Lda	PLAN																																	ABANDONA
							ACTUAL																																
	4	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Rozi Unipessoal, Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																
	5	konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Gardel Unipessoal.Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																
	6	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Talamori	PLAN																																	ON GOING
							ACTUAL																																
	7	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAUCALE	PLAN																																	ON GOING
							ACTUAL																																
	8	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ZONA GOLGOTA	PLAN																																	ON GOING
							ACTUAL																																
	9	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	PLAN																																	ON GOING
							ACTUAL																																
	10	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPEC/ESTV BAUCAU	PLAN																																	ON GOING
							ACTUAL																																
	11	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	Plan																																	ON GOING
							ACTUAL																																
	12	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	PLAN																																	ON GOING
							ACTUAL																																
	13	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESG NO. 01 BAUCAU	PLAN																																	ON GOING
							ACTUAL																																
	1	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Sumber Urip Unip. Lda	PLAN																																	PHO
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Costa Estelia Unipessoal,Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Laga	3	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																ON GOING
							ACTUAL																																
	4	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF LALA-BU'U	PLAN																																ON GOING
							ACTUAL																																
	5	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																ON GOING
							ACTUAL																																
	6	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	PLAN																																ON GOING
							ACTUAL																																
	7	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	PLAN																																ON GOING
							ACTUAL																																
Baguia	1	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Mexa Unip.lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							Actual																																
	2	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF GULARI	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	3	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF OSSU-UFULARI	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	4	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UACALA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	5	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE FINI BAGUIA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	6	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE LARI-SULA	PLAN																																ON GOING
							ACTUAL																																
	7	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC OSSU-HUNA	Plan																																ON GOING
							Actual																																
	8	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC BUAUA LAVATERI	PLAN																																ON GOING
							ACTUAL																																
	9	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGF DE BAGUIA	PLAN																																ON GOING
							ACTUAL																																
Venilia	1	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Wetodo Unip. Lda	PLAN																																ON GOING
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Caidara Lata Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																
	3	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC UAI-BUA	PLAN																																ON GOING
							ACTUAL																																

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Ile	4	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CULINA-OSSU-UAILALE	PLAN																																ON GOING
							ACTUAL																																
	5	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	PLAN																																ON GOING
							ACTUAL																																
Quelicai	1	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Jova Construction Unip. Lda	PLAN																																ON GOING
							ACTUAL																																
	2	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Samadare Unip. Lda	PLAN																																ON GOING
							ACTUAL																																
	3	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UADA-BORU	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	4	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAI-ACA/MULIA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	5	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ABO-LIR LALETEK	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	6	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC LETEMUMO	PLAN																																ON GOING
							ACTUAL																																
	7	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	8	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CATOLICA DARENAFA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
	9	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAURO DARALA/BORUMODO	PLAN																																ON GOING
							ACTUAL																																
	10	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAIDORA/OSSOLIA	PLAN																																ON GOING HELA MAIBE CEIDAUK BA HALO MONITORIZASAUN IHA FATIN PROJECTO REFERE KESTAUN UDAN
							ACTUAL																																
Vemasse	1	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Esa-Un	PLAN																																ABANONA
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Wrangler Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																

Note:

Periode inspesaun iha tereinu | **Implementasaun Plano Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Jerry Gil M. Pereira)
Eng. Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi :

(Eng.Januario Maia Guterres)
Adjunto Director Executivo ADN , I. P.

ANEXU C1 MP-16

Back-up Data

Naran Projeto : **Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120**
No. kontratu : **ICB/046/MOPTC-2017**

Data Inspesaun : **19/ 07/ 2022**

Fatin Inspesaun : Baucau -Venilale

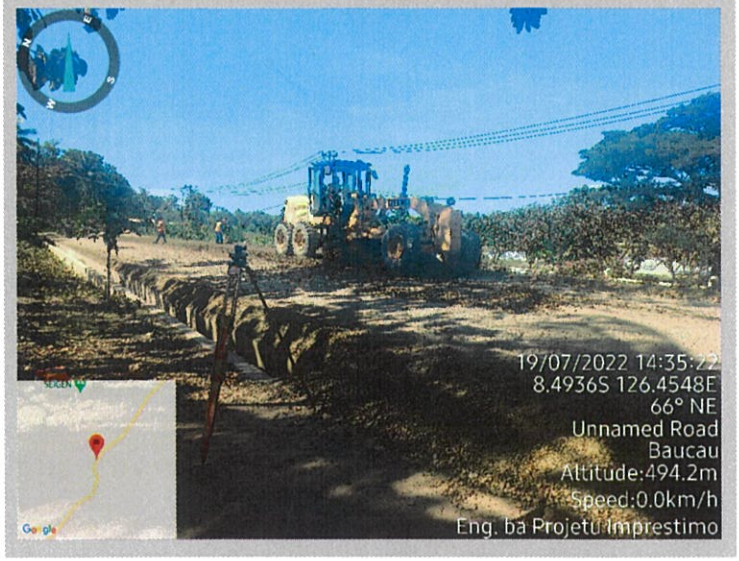
Koordinadas :

Start Point : Long : (-8.48'34,833" S), Latetude : (-8'64'38,31 S)

End Point : Long : (126'45'78,15" E), Latetude : (126'37'60,73 E)

Naran Inspector : **1. Eng. Vidal Guterres**

2. Eng. Augusta da Costa Ferreira

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sub-Base	

ANEXU C1 MP-16

Back-up Data

Naran Projeto : **Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120**
No. kontratu : **ICB/046/MOPTC-2017**

Foto Desemho Item Servisu	Observasaun iha Terenu & Foto Actual
Sub-Base	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (MP- 2)

Project Name :

Road Network Upgrading Sector Project (RNUSP) ADB Loan Nos.3643-TIM and 3644- TIM (COL) Upgrading and Maintenance of Baucau-Viqueque Highway Project Lot 1: Baucau - Venilale Sta.3+740 to Sta.27+120(with exceptions) ICB/046/MOPTC/2017

Contractor : China Railway International Group Co.,Ltd in Joint Venture With China Overseas Engineering(Group)Co.,Ltd.

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
100	GENERAL REQUIREMENTS	$ 1,242,409.12	$ 1,106,140.40	6.90%	$ -	0.00%	$ 1,106,140.40	6.90%	$ 136,268.72
200	EARHWORKS	$ 1,528,842.11	$ 1,266,097.42	7.90%	$ -	0.00%	$ 1,266,097.42	7.90%	$ 262,744.69
300	SUBBASE AND BASE COURSES	$ 1,741,306.42	$ 276,267.61	1.72%	$ 22,480.00	0.14%	$ 298,747.61	1.86%	$ 1,442,558.81
400	SURFACE COURSE	$ 2,540,739.06	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 2,540,739.06
500	BRIDGE CONSTRUCTION	$ 213,100.10	$ 47,790.72	0.30%	$ -	0.00%	$ 47,790.72	0.30%	$ 165,309.38
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 3,969,077.53	$ 2,098,483.60	13.10%	$ -	0.00%	$ 2,098,483.60	13.10%	$ 1,870,593.93
700	MISCELLANEOUS STRUCTURES	$ 689,163.84	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 689,163.84
800	BIO ENGINEERING	$ 226,555.95	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 226,555.95
DW	DAYWORKS	$ 190,159.64	$ 22,363.30	0.14%	$ -	0.00%	$ 22,363.30	0.14%	$ 167,796.34
	PROVISIONAL SUM AND CONTINGENCY	$ 3,509,200.00	$ 256,808.16	1.60%	$ -	0.00%	$ 256,808.16	1.60%	$ 3,252,391.84
	TOTAL =	**$ 15,850,553.77**	**$ 5,073,951.21**	**31.66%**	**$ 22,480.08**	**0.14%**	**$ 5,096,431.21**	**31.80%**	**$ 10,754,122.55**
	Sub Total for Non - Competitive Component (C]								
	PERFORMANCE BASED MAINTENANCE WORKS	$ 173,947.20	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 173,947.20
	CONTRACT AMOUNT	**$ 16,024,500.97**	$ -	31.66%	**$ 22,480.08**	0.14%	$ -	31.80%	**$ 16,024,500.97**
	GRAND TOTAL	**$ 16,024,500.97**	**$ 5,073,951.21**	**31.66%**	**$ 22,480.08**	**0.14%**	**$ 5,096,431.21**	**31.80%**	**$ 10,928,069.75**

Inspection By :

(Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projeito (Imprestimu), ADN, I.P.

(Eng. Vidal Guterres)
Eng. PMU ba Projeito (Imprestimu), ADN, I.P.

Verifika Husi :

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba projeito Infraestrutura, Transporte e Irrigasaun, ADN, I.P.

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

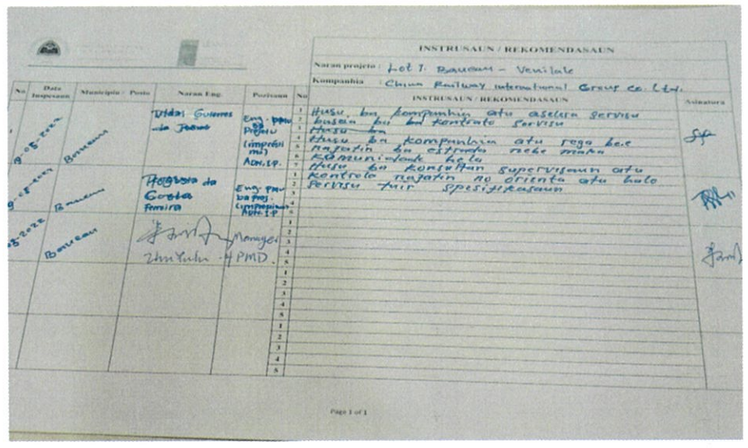
Agência de Desenvolvimento Nacional, Instituto Público

ANEXU D (MP-16)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120

Kompanhia : China Railway Int. Group co, jv with China oversees

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	19/07/2022	Baucau	Augusta da Costa Ferreira	Eng. PMU ba Projetu (Imprestimo), ADN, I.P.	1	husu ba Kontraktor iha fatin komunidade nebe barak tenki rega nafatin.		
					2	husu ba Konsultan Supervisaun wainhira kontraktor halao servisu presija tau matan nafatin no orienta halo tuir speksifikasaun nebe iha contracto.		
II			Vidal Guterres		3	Husu ba Kontraktor atu aselera servisu baseia ba tempo nebe maka mensiona iha kontrato.		

#Anexu C1 (MP-2)

Back-up Data

Naran Projeto : **Road Network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road**

No. kontratu : **ICB/078/MPWTC-2015**

Data Inspesaun : 19/ 07/ 2022

Fatin Inspesaun : Baucau-Lautem

Koordinadas :

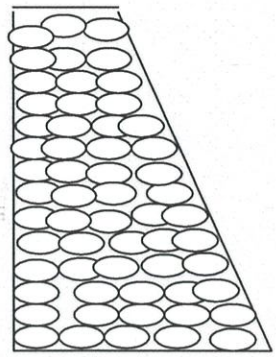
Start Point : Long : 126'27"3,361 E, Latetude: -8.27'39, 004S

End Point : Long : 126'53"58,999 E, Latetude: -8.27'39, 004S

Naran Inspector : 1. Eng. Vidal Guterres

2. Eng. Augusta da Costa Ferreira

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Item servisu Retaining Wall	



Volume= 500 M3

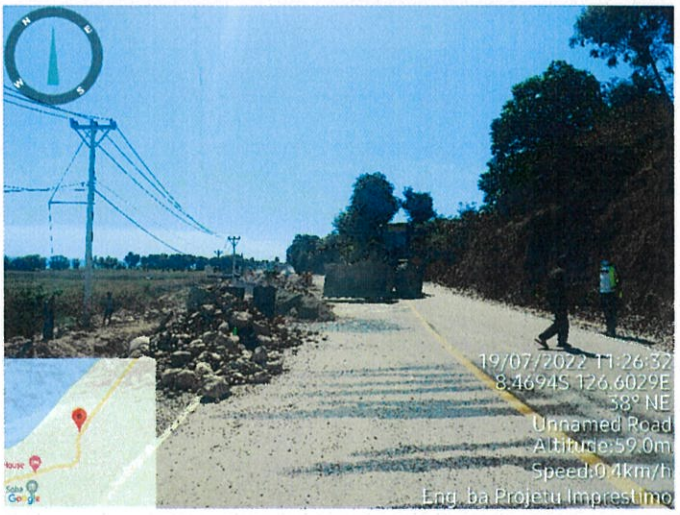


#Anexu C1 (MP-2)

Back-up Data

Naran Projeto : **Road Network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road**

No. kontratu : **ICB/078/MPWTC-2015**

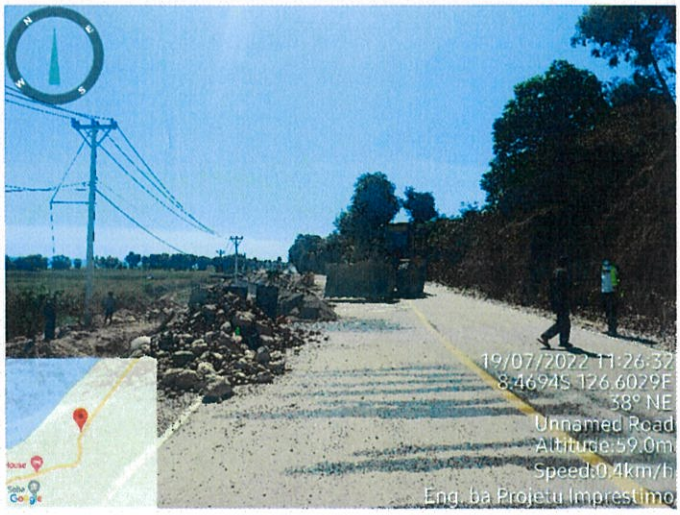
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Item servisu Excavation **Volume= 300 M3**	

#Anexu C1 (MP-2)

Back-up Data

Naran Projeto : **Road Network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road**

No. kontratu : **ICB/078/MPWTC-2015**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Volume= 200 M3	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (MP- 2)

Project Name : Road Network Upgrading Sector Project (RNUSP) ADB Loan Nos.3341/3342(SF)-TIM Upgrading and Maintenance of Baucau-Lautem Section Sta.123+105 to Sta.182+040(with exceptions) ICB/078/MPWTC/2015

Contractor : CBMI Const.Co.,Ltd./Chongqing Road Engineering(Group)Co.,Ltd.

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
100	GENERAL REQUIREMENTS	$ 2,063,252.00	$ 2,063,252.00	7.04%	$ -	0.00%	$ 2,063,252.00	7.04%	$ 0.00
200	EARHWORKS	$ 5,155,850.16	$ 5,022,403.73	17.13%	$ -	0.00%	$ 5,022,403.73	17.13%	$ 133,446.44
300	SUBBASE AND BASE COURSES	$ 6,522,335.98	$ 6,178,053.84	21.07%	$ 14,102.00	0.05%	$ 6,192,155.84	21.12%	$ 330,180.14
400	SURFACE COURSE	$ 4,955,077.48	$ 4,830,795.05	16.48%		0.00%	$ 4,830,795.05	16.48%	$ 124,282.43
500	BRIDGE CONSTRUCTION	$ 1,071,229.18	$ 1,008,191.25	3.44%	$ -	0.00%	$ 1,008,191.25	3.44%	$ 63,037.93
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 6,455,958.11	$ 5,607,066.42	19.13%	$ 26,830.00	0.09%	$ 5,633,896.42	19.22%	$ 822,061.69
700	MISCELLANEOUS STRUCTURES	$ 1,193,530.20	$ 367,643.25	1.25%	$ -	0.00%	$ 367,643.25	1.25%	$ 825,886.95
800	BIO ENGINEERING	$ 142,981.40	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 142,981.40
DW	DAYWORKS	$ 305,612.88	$ 137,311.52	0.47%	$ -	0.00%	$ 137,311.52	0.47%	$ 168,301.36
	PROVISIONAL SUM AND CONTINGENCY	$ 1,062,211.51	$ 324,535.66	1.11%	$ -	0.00%	$ 324,535.66	1.11%	$ 737,675.85
	TOTAL =	**$ 28,928,038.90**	**$ 25,539,252.71**	**87.12%**	**$ 40,932.00**	**0.14%**	**$ 25,580,184.71**	**87.26%**	**$ 3,347,854.18**
	PERFORMANCE BASED MAINTENANCE WORKS	$ 387,307.20	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 387,307.20
	CONTRACT AMOUNT	**$ 29,315,346.10**	**$ -**	87.12%	**$ 40,932.00**	0.14%	**$ -**	87.26%	**$ 29,315,346.10**
	GRAND TOTAL	**$ 29,315,346.10**	**$ 25,539,252.71**	**87.12%**	**$ 40,932.00**	**0.14%**	**$ 25,580,184.71**	**87.26%**	**$ 3,735,161.38**

Prepara Husi :

1. (Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projecto (Imprestimo)
ADN, I.P.

2. (Eng. Vidal Guterres)
Eng. PMU ba Projecto (Imprestimo)
ADN, I.P.

Verifika Husi :

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba projeito Infraestrutura, Transporte e Irrigasaun, ADN, I.P.

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

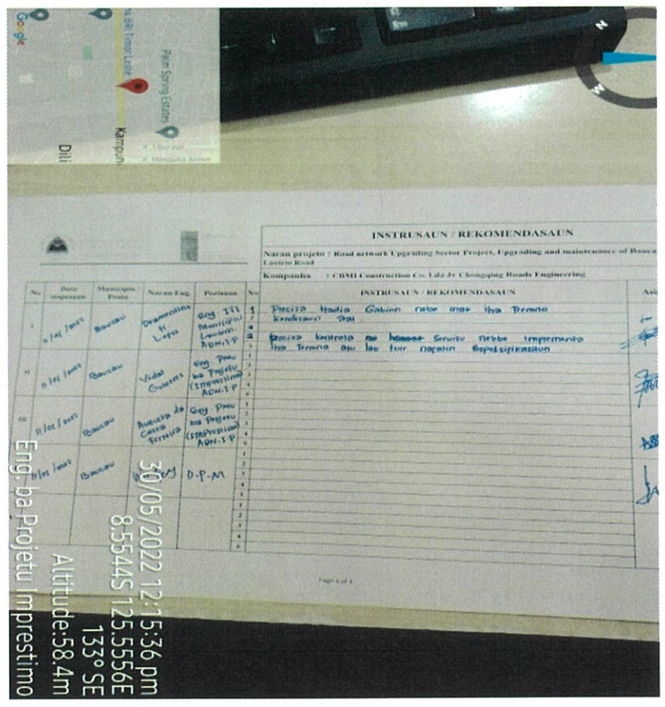
ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXU D (MP-2)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Road network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road

Kompanha : CBMI Construction Co. Lda Jv Chongqing Roads Engineering

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	19/07/2022	Baucau-Lautem	Augusta da Costa Ferreira	Eng. Ba Projetu ITI Munisipiu Lautem, ADN, I.P.	1	Presiza kontrola servisu ne'ebe implementa iha Terreno atu lao tuir nafatin espesifikasaun.		
II.			Vidal Guterres					

PROJECT :Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau – Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (sta 3+740 to Sta 27+120), Lot 2 : Venilale - Viqueque Section (Sta 27+120 to Sta . 62+010)

Consultant : Intercontinental Consultants And Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis.(Icp) Inc. .(Philippines) (As Sub-Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor -Leste) (As Sub-Consultant)

IPC No. : 33 (March 2022)

SUMMARY BACK UP DATA

ITEM NO.	DESCRIPTION	CONTRACT – ORIGINAL CONTRACT UNIT	RATE (US$)	Home / Field	QTY.	AMOUNT (US$)	ADN PROGRESS – PREVIOUS BILLING Amount	Progress %	THIS BILLING Amount	Progress %	TOTAL TO DATE Amount	PROGRESS PAYMENT TO DATE
A	REMUNERATION											
	Key Experts (International)											
	TOTAL					$ 2,679,000.00	$ 1,247,285.00	23.70%	$ 44,000.00	0.84%	$ 1,291,285.00	24.54%
	Non-Key Experts (National) - Lot-1											
	Sub-Total					$ 615,600.00	$ 475,822.00	9.04%	$ 32,400.00	0.62%	$ 508,222.00	9.66%
	TOTAL					$ 1,072,100.00	$ 874,647.00	16.62%	$ 46,500.00	0.88%	$ 921,147.00	17.50%
	Administrative Support Staff - Lot-1											
	Sub-Total					$ 87,000.00	$ 87,000.00	1.65%	$ -	0.00%	$ 87,000.00	1.65%
	Sub-Total					$ 102,000.00	$ 72,240.00	1.37%	$ 2,400.00	0.05%	$ 74,640.00	1.42%
TOTAL						$ 189,000.00	$ 159,240.00	3.03%	$ 2,400.00	0.05%	$ 161,640.00	3.07%
	(A). TOTAL COSTS REMUNERETION					$ 3,940,100.00	$ 2,281,172.00	43.35%	$ 92,900.00	1.77%	2,374,072.00	45.11%
B	REIMBURSABLES EXPENCES											
Sub Total Cost International (1)						$ 145,720.00	$ 90,733.90	1.72%	-$ 1,305.05	-0.02%	$ 89,428.85	1.70%
National												
Sub Total Cost National (2)						$ -						
Total Cost Reimbursable Expenses 1+2						$ 145,720.00	$ 90,733.90	1.72%	-$ 1,305.05	-0.02%	$ 89,428.85	1.70%
Sub Total Cost Provisional Sums (3)							$ -	0.00%				
Provisional Sums (PS)							$ -	0.00%				
Contigency (4)		LS	$ 500,000.00		1.00	$ 500,000.00	$ -	0.00%				
(B). TOTAL COSTS Expenses + Provisional Sums						$ 645,720.00	$ 90,733.90	1.72%	-$ 1,305.05	-0.02%	$ 89,428.85	1.70%
Total Costs (A + B)						$ 4,585,820.00	$ 2,371,905.90	45.07%	$ 91,594.95	1.74%	$ 2,463,500.85	46.81%
incoming tax on Corporation / Witholding Tax (10%)						$ 408,582.00						
Income Tax on Non-Resident Experts (10%)						$ 267,900.00						
Total Estimate for Indirect Local Tax (B)						$ 676,482.00					-	
Grand Total / Contract Amount (A+B+C)						$ 5,262,302.00						

Checked by

Eng. Teresa Gomes
(Eng. Projecto Infrastructura, Transportes e Irigasaun, ADN, I.P.)

Eng. Tito Edgar F.N. de Jesus
(Eng. Projecto Infrastructura, Transportes e Irigasaun, ADN, I.P.)

Verified by

Eng. Remigio C.S Dos Santos
(Enginheiro Senior ba Projecto Infrastructura,Transportes e Irigasaun, ADN, I.P.)

Certified by

Eng.Emerenciana da Costa Maia Freitas
(Coordenadora Unidade de Controlo e Validação de Qualidade , ADN, I.P.)

MINISTERIO DO PLANO E ORDENAMENTO TIB-ORAIANO LOMOR-SA'E NASIONAL

ADN, I.P. Agência de Desenvolvimento Nacional Timor-Leste

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJEITO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	JUIHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BAGUIA VILLA	3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	FI	ESTRADAS	Domin Timor Diak, Lda	555/078/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
	4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	FI	ESTRADAS	Gihon Unip, Lda	555/066/MOPTC-2017	TERIO DAS OBRAS PU	Plan																																On going
								Actual																																
	6	Rural Roads Routine Maintenance Baucau - Uatabo Chainage 0+000 - 4+800 and Boile - Uatabo Chainage 0+000 - 5+200 in Municipality Baucau / 162	LM-CD	ESTRADAS	Talamori	MPWTC-W-190090	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Falta Retensaun
								Actual																																
	7	Road Maintenance Section. Baucau Urbano, Baucau Town, Baucau Municipality (162)	LM-BS	ESTRADAS	Jomarjo Unipessoal Lda	MPW-W-190158	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Progress fisik 88.25% Empreza laiha kontinuasaun
								Actual																																
	9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800	LM-CD	ESTRADAS	Mexa	MPW-W-210047	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
LAGA	1	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Lalaisi, Unip. Lda	RT/023/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
	2	R4D Rural Road Rehabilitation Qaeeai - Binagua Chainage 1+600 - 3+300 Baucau Municipality	FI	ESTRADAS	F.res Unipessoal, Lda	RT/024/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																
	3	Rural Roads Periodic Maintenance Samaguia - Namanei Chainage 0+000 - 7+000 Municipality Baucau / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Delatina	MPTCW-W-190091	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
	5	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	LM-BS	ESTRADAS	Uatoos Unip. Lda	MOP-W-200002	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
	6	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 ,Laga to Baguia	LM-CD	ESTRADAS	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																
BAGUIA	2	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	FI	MANUTENSAUN NO REHABILITASAUN	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Progress Fisiic 100%. Falta Retensaun
								Actual																																
	4	Baguia - Larisula Chainage 0+000 - 12+900 / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Lamegua Star Unip Lda	MPW-W-190088	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
	6	Konstruasaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	LM-CD	AGRICULTURA	Makasae Construction LDA	RDTL-2021-14628	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	Progress Fisiic 99.53% Empreza hasi kontinuasaun
								Actual																																
VENILALE	3	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	FI	ESTRADAS	Ruvic unip, lda	555/118/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Paradu
								Actual																																
	4	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Caidailale Unip.Lda	RT/069/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																
	5	Rural Road Rehabilitation of Venilale - Uaioli Chainage Sta 0 + 000 - 3 + 000, Baucaun Municipality	FI	ESTRADAS	Putra Baucau, Unp,Lda	RT/014/MOP - 2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																
	6	Rural Road Rehabilitation of Venilale - Uaioli Chainage Sta 6 + 000 -8 + 550, Baucaun Municipality	FI	ESTRADAS	Macaloco, Unp, Lda	RT/...../MOP - 2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																
	7	Rural Road Rehabilitation of Venilale - Uaioli Chainage Sta 6 + 000 -8 + 550, Baucaun Municipality	FI	ESTRADAS	Morende Const. Unp,Lda	RT/016/ MOP - 2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																

MINISTÉRIO DO PLANO E ORDENAMENTO VII GOVERNO CONSTITUCIONAL

ADN, I.P. Agência de Desenvolvimento Nacional Timor-Leste

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJEITO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	JUIHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
QUELICAI	3	Rehabilitation Of Roads Uiaca - Queleqai - Lacluta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	FI	ESTRADAS	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	4	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	LM-CD	ESTRADAS	Lalaisi, Unip. Lda	MPWTC-W-190089	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	5	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	LM-CD	ESTRADAS	Niceles Unipessoal Lda	MPW-CS-2000026	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
	6	Rehabilitation of Roads, Road Section. Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	FI	ESTRADAS	Wingstone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	7	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 0 + 000 - 3 + 000 Baucau Municipality	FI	ESTRADAS	Flores Unipessoal, Lda	RT/099/MOP-2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	8	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 6 + 000 - 9 + 000 Baucau Municipality	FI	ESTRADAS	DVP Const. Unp .Lda	RT/011/MOP-2020	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	9	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 6 + 000 - 9 + 000 Baucau Municipality	FI	ESTRADAS	Lia - Lura Unp, Lda	RT/...../MOP-2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	10	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 3 + 000 - 6 + 000 Baucau Municipality	FI	ESTRADAS	Helcia Unp. Lda	RT/010/MOP-2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
VEMASSE	3	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality	LM-CD	ESTRADAS	Rozi const. unip. Lda	MPW-W-210048	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	4	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality	LM-CD	ESTRADAS	Rozi const. unip. Lda	MPW-W-210051	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	5	R4D Rural Road Spot Improvement Vemase-Osoala Chainage 0+000-21+600	LM-CD	ESTRADAS	Chacailala Unipessoal Lda	MPW-W-210052	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	8	Nasional Road no.1 Upgrading project Manatuto Baucau (paketckage A01 - 02/STA 56+400-114+102(56.82km)	FI	ESTRADAS IMPRESTIMO	Shangai Construction Group Co.,Ltd	ICB/021/MPWTC-2015	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
MULTI POSTO	1	RNUSPJ Road Link No. A01 - 03 , Upgrading and Maintenance of Baucau - Lautem Section , Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	FI	ESTRADA-IMPRESTIMO	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/078/MPWTC-2015	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																	
	2	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1, Baucau - Venilale , Sta. 03 + 740 to Sta. 27 + 120	FI	IMPRESTIMO	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																	
	3	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 , Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 , Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	FI	ESTRADA-IMPRESTIMO	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)	RFP/003/MOP/2018	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																	
	4	R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality	LM-CD	ESTRADAS	Juga Te Figa Unipessoal Lda	MPW-W-210054	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	5	R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800	LM-CD	ESTRADAS	DB-Ingracia Unipessoal Lda	MPW-W-210049	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	

TOTAL PROJETO ON - GOING = 36 PROJECTO

Note.

Periode inspesaun iha tereinu

Implementasaun Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi ,

(Eng. Jacob da Costa Camoes)
Eng. Ba Projecto Infrastuturu e Irigasaun Municipio Baucau ADN, I.P

Sertifika Husi ,

(Eng.Emerenciana da Costa M. Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi ,

(Eng. Januario Maia Guteres)
Ajunto Director Executivo - ADN I. P

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJEITO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	JUIHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BAGUIA VILLA	3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	FI	ESTRADAS	Domin Timor Diak, Lda	555/078/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	FI	ESTRADAS	Gihon Unip, Lda	555/066/MOPTC-2017	TERIO DAS OBRAS PU	Plan																																	On going
								Actual																																	
	6	Rural Roads Routine Maintenance Baucau – Uatabo Chainage 0+000 – 4+800 and Boile – Uatabo Chainage 0+000 – 5+200 in Municipality Baucau / 162	LM-CD	ESTRADAS	Talamori	MPWTC-W-190090	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Falta Retensaun
								Actual																																	
	7	Road Maintenance Section, Baucau Urbans, Baucau Town, Baucau Municipality (162)	LM-BS	ESTRADAS	Jomarjo Unipessoal Lda	MPW-W-190158	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Progress fisik 65.78% Empreza hein kontinua ona
								Actual																																	
	9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 – 4+800	LM-CD	ESTRADAS	Mexa	MPW-W-210047	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
LAGA	1	R4D Rural Road Rehabilitation Terihuedae – Saelari – Binagua Chainage 0+000 – 1+600 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Lalaisi, Unip. Lda	RT/023/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	2	R4D Rural Road Rehabilitation Queeai – Binagua Chainage 1+600 – 3+300 Baucau Municipality	FI	ESTRADAS	F.res Unipessoal, Lda	RT/024/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
	3	Rural Roads Periodic Maintenance Samaguia – Namanei Chainage 0+000 – 7+000 Municipality Baucau / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Delatina	MPTCW-W-190091	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	5	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	LM-BS	ESTRADAS	Uatoos Unip. Lda	MOP-W-200002	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	6	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 ,Laga to Baguia	LM-CD	ESTRADAS	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
BAGUIA	2	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	FI	MANUTENSAUN NO REHABILITASAUN	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Progress Fisisc 100%. Falta Retensaun
								Actual																																	
	4	Baguia – Larisula Chainage 0+000 – 12+900 / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Lamegua Star Unip Lda	MPW-W-190088	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																	
	6	Konstrusaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	LM-CD	AGRICULTURA	Makasae Construction LDA	RDTL-2021-14628	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	Progress Fisisc 68.56% Empreza hein kontinua ona
								Actual																																	
VENILALE	3	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	FI	ESTRADAS	Ruvic unip, lda	SSS/118/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Paradu
								Actual																																	
	4	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Caidailale Unip.Lda	RT/069/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
	5	Rural Road Rehabilitation of Venilale - Uaioli Chainage Sta 0 + 000 - 3 + 000, Baucaun Municipality	FI	ESTRADAS	Putra Baucau, Unp,Lda	RT/014/MOP - 2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
	6	Rural Road Rehabilitation of Venilale - Uaioli Chainage Sta 6 + 000 -8 + 550, Baucaun Municipality	FI	ESTRADAS	Macaloco, Unp, Lda	RT/...../MOP - 2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	
	7	Rural Road Rehabilitation of Venilale - Uaioli Chainage Sta 6 + 000 -8 + 550, Baucaun Municipality	FI	ESTRADAS	Morende Const. Unp,Lda	RT/016/ MOP - 2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
								Actual																																	

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJEITO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	JUIHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
QUELICAI	3	Rehabilitation Of Roads Uiaca - Quelequai - Lachuta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	FI	ESTRADAS	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	4	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	LM-CD	ESTRADAS	Lalaini, Unip. Lda	MPWTC-W-190089	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	LM-CD	ESTRADAS	Niceles Unipessoal Lda	MPW-CS-2000026	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																																
	6	Rehabilitation of Roads, Road Section, Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	FI	ESTRADAS	Wingatone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	7	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 0 + 000 - 3 + 000 Baucau Municipality	FI	ESTRADAS	Flores Unipessoal, Lda	RTJ099/MOP-2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	8	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 6 + 000 - 9 + 000 Baucau Municipality	FI	ESTRADAS	DVP Const. Unp .Lda	RTJ011/MOP-2020	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	9	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 6 + 000 - 9 + 000 Baucau Municipality	FI	ESTRADAS	Lia - Lura Unp, Lda	RTJ...../MOP-2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	10	R4D Rural Road Rehabilitation Of afaca - Uaitame Chainage 3 + 000 - 6 + 000 Baucau Municipality	FI	ESTRADAS	Helcia Unp. Lda	RTJ010/MOP-2021	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
VEMASSE	3	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality	LM-CD	ESTRADAS	Rezi const. unip. Lda	MPW-W-210048	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	4	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality	LM-CD	ESTRADAS	Rezi const. unip. Lda	MPW-W-210051	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	R4D Rural Road Spot Improvement Vemase-Osoala Chainage 0+000-21+600	LM-CD	ESTRADAS	Chacailala Unipessoal Lda	MPW-W-210052	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	8	Nasional Road no.1 Upgrading project Manatuto Baucau (paketckage A01 - 02/STA 56+400-114+102(56.82km)	FI	ESTRADAS IMPRESTIMO	Shangai Construction Group Co.,Ltd	ICB/021/MPWTC-2015	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																																
MULTI POSTO	1	RNUSFJ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	FI	ESTRADA-IMPRESTIMO	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/078/MPWTC-2015	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																
	2	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120	FI	IMPRESTIMO	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																
	3	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	FI	ESTRADA-IMPRESTIMO	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)	RFP/003/MOP/2018	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																
	4	R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+500 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality	LM-CD	ESTRADAS	Juga Te Figa Unipessoal Lda	MPW-W-210054	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+600 Boile-Uatabo Chainage 0+000-2+500	LM-CD	ESTRADAS	DB-Ingracia Unipessoal Lda	MPW-W-210049	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																

TOTAL PROJETO ON - GOING = 51 PROJECTO

Note.

Periode inspesaun iha tereinu

Implementassaun Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi ,

(Eng. Jacob da Costa Camoes)
Eng. Ba Projecto Infrastutura e Irigasaun Municipio Baucau ADN, LP

Sertifika Husi ,

(Eng.Emerenciana da Costa M. Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi ,

(Eng. Januario Maia Guteres)
Ajunto Director Executivo - ADN I. P

MINISTÉRIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng.	**Adonis Julio Fernandes**
Municipio	**MUNICIPIO BAUCAU NO POSTOS**

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	JULHO 1	2	3	4	5	6	10	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BAUCAU VILLA (BV)	1	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	2	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	3	Rehabilitasaun ba ESG Filial Kilik Waiga'e iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG FILIAL KILIK WAIGA'E	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	4	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Plan																																	Servisu Electricidade Seidauk
	5	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	6	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																	Projeitu refere Kontratu seidauk iha
	7	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																	
	8	Rehabilitation of MPWTC Office in the Municipality Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																	Projeitu abandona
	9	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	LM	MINISTERIO SAUDE	Plan																																
							Actual																																	
	10	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	Talamori	RDTL-SAMES-RFQ-021-071	LM-BS	SAMES	Plan																																
							Actual																																	
	11	Construsaun Escola Polo Baucau	Sanira Construction Unip Lda	RDTL-326	FI	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Projeitu Abandona
LAGA (LA)	1	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF LALA-BU'U	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	2	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	3	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF. FITUN SAGADATE-LAGA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
GUIA (BA)	1	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	2	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	3	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UACALA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	4	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE FINI BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk
	5	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE LARI-SULA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																	Servisu Electricidade Seidauk

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	JULHO 1	2	3	4	5	6	10	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BA(	6	Rehabilitasaun ba EBC Ossu - Huna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC OSSU-HUNA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	7	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	GRUPU KOMUNITARIU MEJD PKRIE EBC BUAUA LAVATERI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	8	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGF DE BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	9	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	Lakonsege hare tamba tempu
VENILALE (VEN)	1	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC UAI-BUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	2	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CULINA-OSSU-UAILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	3	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	4	Aumenta C. O no Kliesntes	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	5	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	6	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	Wetodo Unip. Lda	SSS/296/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	Projeitu refere FHO ona
QUELICAI (QUE)	1	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UADA-BORU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	2	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAI-ACA/MULIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	3	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF ABO-LIR LALETEK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	4	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC LETEMUMO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	5	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	6	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CATOLICA DARENAFA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	7	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF MAURO DARALA/BORUMODO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	8	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAIDORA/OSSOLIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	Servisu Electricidade Seidauk
	9	New Construction of Health Post and Douctor House Building Municipality Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	LM-CD	MINISTERIO SAUDE	Plan																																	
							Actual																																	

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	JULHO																													OBS
								1	2	3	4	5	6	10	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
	10	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																Projeitu Refere FHO ona
	11	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
VEMASSE (VEM)	1	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	We-Rua Unip, Lda	MOP-W-190173	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	2	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	Esa-Un	56/DNAL-MTAC/III/2017	LM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																																
							Actual																																Projeitu Abandona
TOTAL PROJETO ON-GOING																																					

Note:

Periode inspesaun iha tereinu — **Implementasaun Plano Periode inspesaun iha tereinu** — **Relatoriu avaliasuan mensal iha Dili** — **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Adonis Julio Fernandes)
Eng. Electricidade, ADN,I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres_)
Adjunto Director Executivo, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VI CONVERSO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng.	**Adonis Julio Fernandes**
Municipio	**MUNICIPIO BAUCAU NO POSTOS**

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	JULHO 1	2	3	4	5	6	10	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BAUCAU VILLA (BV)	1	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan															■															
							Actual																																
	2	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan															■															
							Actual																																
	3	Rehabilitasaun ba ESG Filial Kilik Waiga'e iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG FILIAL KILIK WAIGA'E	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan											■																			
							Actual																																
	4	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan											■																			
							Plan																																
	5	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan											■																			
							Actual																																
	6	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	7	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan											■																			
							Actual																																
	8	Rehabilitation of MPWTC Office in the Municipality Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan											■																			
							Actual																																
	9	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	LM	MINISTERIO SAUDE	Plan											■																			
							Actual																																
	10	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	Talamori	RDTL-SAMES-RFQ-021-071	LM-BS	SAMES	Plan																																
							Actual																																
	11	Construsaun Escola Polo Baucau	Sanira Construction Unip Lda	RDTL-326	FI	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan											■																			
							Actual																																
LAGA (LA)	1	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF LALA-BU'U	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan															■															
							Actual																																
	2	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan															■															
							Actual																																
	3	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF. FITUN SAGADATE-LAGA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan															■															
							Actual																																
GUIA (BA)	1	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan												■																		
							Actual																																
	2	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan												■																		
							Actual																																
	3	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UACALA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan												■																		
							Actual																																
	4	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE FINI BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan												■																		
							Actual																																
	5	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE LARI-SULA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan												■																		
							Actual																																

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	JULHO 1	2	3	4	5	6	10	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BA	6	Rehabilitasaun ba EBC Ossu - Huna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC OSSU-HUNA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	7	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	GRUPU KOMUNITARIU MEJD PKRIE EBC BUAUA LAVATERI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	8	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGF DE BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	9	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
VENILALE (VEN)	1	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC UAI-BUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	2	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CULINA-OSSU-UAILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	3	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	4	Aumenta C. O no Kliesntes	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	5	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	6	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	Wetodo Unip. Lda	SSS/296/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
QUELICAI (QUE)	1	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UADA-BORU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	2	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAI-ACA/MULIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	3	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF ABO-LIR LALETEK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	4	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC LETEMUMO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	5	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	6	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CATOLICA DARENAFA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	7	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF MAURO DARALA/BORUMODO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	8	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAIDORA/OSSOLIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																	
	9	New Construction of Health Post and Douctor House Building Municipality Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	LM-CD	MINISTERIO SAUDE	Plan																																	
							Actual																																	

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	JULHO																													OBS
								1	2	3	4	5	6	10	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
	10	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	11	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Walililko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
VEMASSE (VEM)	1	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	We-Rua Unip, Lda	MOP-W-190173	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	2	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	Esa-Un	56/DNAL-MTAC/III/2017	LM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																																
							Actual																																
TOTAL PROJETO ON-GOING																																					

Note:

Periode inspesaun iha tereinu **Implementasaun Plano Periode inspesaun iha tereinu** **Relatoriu avaliasuan mensal iha Dili** **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Adonis Julio Fernandes)
Eng. Electricidade, ADN,I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Teresa Gomes

Municipio MUNICIPIO DILI NO POSTOS

2022

Julho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan	Halo relatorio Pagamento
							Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan	FHO
							Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan	Halo relatorio Pagamento Konsultan
							Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento Kontractor
							Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan	PHO
							Actual	
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan	PHO
							Actual	
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan	Halo Relatorio Pagamento konsultan
							Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Julho																																					
								Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su								
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31								
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																																						
							Actual																																							
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																																						
							Actual																																							
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																																						
							Actual																																							
	21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																																						
							Actual																																							
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																																						
							Actual																																							
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																																						
							Actual																																							
	24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan																																						
							Actual																																							
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																																						
							Actual																																							
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																																						
							Actual																																							
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																																						
							Actual																																							
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																																						
							Actual																																							
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																																						
							Actual																																							
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																																						
							Actual																																							
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																																						
							Actual																																							
	32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																						
							Actual																																							
	33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																						
							Actual																																							
	34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																						
							Actual																																							
		TOTAL PROJETO ON-GOING																																											

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Teresa Gomes)
Eng. PMU ba Projetu (Impréstimo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controle e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Investimentos Públicos

PLANU INSPESAUN

Naran Eng. Teresa Gomes

Municipio MUNICIPIO DILI NO POSTOS

2022

Julho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	FHO
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co .Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO Ltda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phils, (Iep) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Julho																																				
								Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31						
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																																					
							Actual																																						
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Desgn Indonesia	MPW-Cs -2000032	LM	MOP	Plan																																					
							Actual																																						
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																																					
							Actual																																						
	21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																																					
							Actual																																						
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																																					
							Actual																																						
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																																					
							Actual																																						
	24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Intercoenental Unip Lda	MPW- CS 2000028	LM		Plan																																					
							Actual																																						
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																																					
							Actual																																						
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																																					
							Actual																																						
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																																					
							Actual																																						
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																																					
							Actual																																						
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																																					
							Actual																																						
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																																					
							Actual																																						
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																																					
							Actual																																						
	32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																					
							Actual																																						
	33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																					
							Actual																																						
	34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																					
							Actual																																						
		TOTAL PROJETO ON-GOING																																										

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Teresa Gomes)
Eng. PMU ba Projetu (Impréstimo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Tito Edgar F. N. de Jesus

Municipio

2022

Julho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	FHO
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo relatorio Pagamento Konsultan
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento Kontractor
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Julho																																						
								Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su									
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31									
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																																							
							Actual																																								
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																																							
							Actual																																								
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																																							
							Actual																																								
	21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																																							
							Actual																																								
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																																							
							Actual																																								
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																																							
							Actual																																								
	24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan																																							
							Actual																																								
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																																							
							Actual																																								
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																																							
							Actual																																								
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																																							
							Actual																																								
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																																							
							Actual																																								
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																																							
							Actual																																								
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																																							
							Actual																																								
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																																							
							Actual																																								
	32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																							
							Actual																																								
	33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																							
							Actual																																								
	34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																							
							Actual																																								
		TOTAL PROJETO ON-GOING																																												

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Tito Edgar F. N. de Jesus)
Eng. PMU ba Projetu (Imprestimo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Tito Edgar F.N. de Jesus

Municipio MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		2022 Julho	Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual		FHO
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Josint venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Josint venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual		PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongqung International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual		PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Assocration with Desing Science, INC , and Kai Wutu Kmanck Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanut and Technocrats Pvt Ltd. (India) in Association With Infra Consultants in the Pilis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual		

| Municipio / Posto | No. | Naran Projeto | Naran Companha | No Contrato | Kategoria | Dono do Projeto | | Julho | | |

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		2022 Julho	Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan		Halo relatorio Pagamento
							Actual		
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan		FHO
							Actual		
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan		Halo relatorio Pagamento Konsultan
							Actual		
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan		
							Actual		
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento Kontractor
							Actual		
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan		PHO
							Actual		
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan		PHO
							Actual		
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan		
							Actual		
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan		Halo Relatorio Pagamento konsultan
							Actual		
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan		
							Actual		
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan		
							Actual		

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Julho																																			
								Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su							
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31							
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																																					
							Actual																																							
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																																					
							Actual																																							
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																																					
							Actual																																							
	21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																																					
							Actual																																							
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																																					
							Actual																																							
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																																					
							Actual																																							
	24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan																																					
							Actual																																							
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																																					
							Actual																																							
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																																					
							Actual																																							
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																																					
							Actual																																							
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																																					
							Actual																																							
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																																					
							Actual																																							
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																																					
							Actual																																							
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																																					
							Actual																																							
	32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																					
							Actual																																							
	33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																					
							Actual																																							
	34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																					
							Actual																																							
		TOTAL PROJETO ON-GOING																																										

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Vidal Guterres)
Eng. PMU ba Projetu (Imprés:timo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Campanha	No Contrato	Kategoria	Dono do Projeto		2022 Julho	Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shunghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual		FHO
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Soleremа - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual		PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual		PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Soleremа Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Soleremа Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt Ltd. (India) in Association With Infra Consultants in the Phils, (Icp) Inc (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual		
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual		

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Julho																																					
								Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su								
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31								
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																																						
							Actual																																							
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																																						
							Actual																																							
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 . Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																																						
							Actual																																							
	21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																																						
							Actual																																							
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																																						
							Actual																																							
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																																						
							Actual																																							
	24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan																																						
							Actual																																							
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																																						
							Actual																																							
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																																						
							Actual																																							
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																																						
							Actual																																							
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																																						
							Actual																																							
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																																						
							Actual																																							
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																																						
							Actual																																							
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																																						
							Actual																																							
	32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																						
							Actual																																							
	33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																						
							Actual																																							
	34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																						
							Actual																																							
		TOTAL PROJETO ON-GOING																																											

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Vidal Guterres)
Eng. PMU ba Projetu (Imprestimo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Augusta da Costa Ferreira

Municipio MUNICIPIO DILI NO POSTOS

2022 — **Julho**

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	FHO
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo relatorio Pagamento Konsultan
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento Kontractor
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento konsultan
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Julho																																			
								Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su							
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31							
	18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan																																					
							Actual																																							
	19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan																																					
							Actual																																							
	20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan																																					
							Actual																																							
	21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan																																					
							Actual																																							
	22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan																																					
							Actual																																							
	23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan																																					
							Actual																																							
	24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Intereonental Unip Lda	MPW- CS 2000028	LM		Plan																																					
							Actual																																							
	25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan																																					
							Actual																																							
	26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan																																					
							Actual																																							
	27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan																																					
							Actual																																							
	28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan																																					
							Actual																																							
	29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan																																					
							Actual																																							
	30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan																																					
							Actual																																							
	31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan																																					
							Actual																																							
	32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan																																					
							Actual																																							
	33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan																																					
							Actual																																							
	34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan																																					
							Actual																																							
		TOTAL PROJETO ON-GOING																																										

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projetu (Impréstimo), ADN, I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Augusta da Costa Ferreira

Municipio MUNICIPIO DILI NO POSTOS

2022

Julho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	FHO
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const Co.,Ltd. / Chongqing Road Engineering (Group)Co .Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const Co .Ltd. / Chongqing Road Engineering (Group)Co .Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co .Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (JCB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing Internatuonal Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO Ltda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co .Ltd in Joint Venture with Dongsung Eng. Co .Ltd., and in Association with Desng Science, INC ., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co .Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phils, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezernvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

| Municipio / Posto | No. | Naran Projeto | Naran Companha | No Contrato | Kategoria | Dono do Projeto | | Julho | | |

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

Naran Eng.	JERRY GIL M. PEREIRA
Municipio / Posto	MUNICIPIO BAUCAU NO POSTOS

INSPECTION PLAN 2022

JULY

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
BAUCAU VILLA	1	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Co. Cactus Unip. Lda	PLAN																																	FHO
							ACTUAL																																	
	2	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Central Hill Unipessoal Lda	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	3	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Sanira Construction Unip Lda	PLAN																																ABANDONA
							ACTUAL																															
	4	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Rozi Unipessoal, Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																															
	5	konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Gardel Unipessoal.Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																															
	6	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Talamori	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	7	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAUCALE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	8	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ZONA GOLGOTA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	9	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	10	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPEC/ESTV BAUCAU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	11	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	Plan																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	12	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	13	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Trilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESG NO. 01 BAUCAU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	1	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Sumber Urip Unip. Lda	PLAN																																PHO
							ACTUAL																															
	2	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Costa Estelia Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																															

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Laga	3	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	4	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF LALA-BU'U	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	5	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	6	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	7	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	PLAN																																	tirr planu tamba volume servisu barak
							ACTUAL																																	
Baguia	1	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Mexa Unip.lda	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							Actual																																	
	2	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF GULARI	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	3	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF OSSU-UFULARI	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	4	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UACALA	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	5	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE FINI BAGUIA	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	6	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE LARI-SULA	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	7	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC OSSU-HUNA	Plan																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							Actual																																	
	8	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC BUAUA LAVATERI	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	9	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGF DE BAGUIA	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
Venilia	1	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Wetodo Unip. Lda	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	2	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Caidara Lata Unipessoal,Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																	
	3	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC UAI-BUA	PLAN																																	monitorizasaun Actual la tuirr planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Ie	4	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CULINA-OSSU-UAILALE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	5	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
Quelicai	1	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Jova Construction Unip. Lda	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	2	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Samadare Unip. Lda	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	3	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UADA-BORU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	4	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAI-ACA/MULIA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	5	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ABO-LIR LALETEK	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	6	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC LETEMUMO	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	7	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	8	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CATOLICA DARENAFA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	9	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAURO DARALA/BORUMODO	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	10	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAIDORA/OSSOLIA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
Vemasse	1	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Esa-Un	PLAN																																ABANONA
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Wrangler Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																

Note:

Periode inspesaun iha tereinu | **Implementasaun Plano Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Jerry Gil M. Pereira)
Eng. Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi :

(Eng.Januario maia Guterres)
Adjunto Director Executivo ADN , I. P.

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

Naran Eng.	AGUSTINHO ARANDA
Municipio / Posto	MUNICIPIO BAUCAU NO POSTOS

INSPECTION PLAN 2022

JULY

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
BAUCAU VILLA	1	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Co. Cactus Unip. Lda	PLAN																																	FHO
							ACTUAL																																	
	2	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Central Hill Unipessoal Lda	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	3	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Sanira Construction Unip Lda	PLAN																																ABANDONA
							ACTUAL																															
	4	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Rozi Unipessoal, Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																															
	5	konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Gardel Unipessoal.Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																															
	6	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Talamori	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	7	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAUCALE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	8	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ZONA GOLGOTA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	9	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	10	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPEC/ESTV BAUCAU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	11	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	Plan																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	12	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CAIBADA MACASSAE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	13	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Trilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESG NO. 01 BAUCAU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																															
	1	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Sumber Urip Unip. Lda	PLAN																																PHO
							ACTUAL																															
	2	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Costa Estelia Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																															

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Laga	3	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	4	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF LALA-BU'U	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	5	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Juga Te Figa Unipessoal Lda	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	6	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	7	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	PLAN																																	tuir planu tamba volume servisu barak
							ACTUAL																																
Baguia	1	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Mexa Unip.lda	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							Actual																																
	2	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF GULARI	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	3	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF OSSU-UFULARI	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	4	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UACALA	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	5	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE FINI BAGUIA	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	6	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE LARI-SULA	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	7	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC OSSU-HUNA	Plan																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							Actual																																
	8	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC BUAUA LAVATERI	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	9	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGF DE BAGUIA	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
Venila	1	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Wetodo Unip. Lda	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																
	2	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Caidara Lata Unipessoal,Lda	PLAN																																	PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																
	3	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC UAI-BUA	PLAN																																	monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																

Posto	NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	[illegible]	NARAN COMPANHA	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBSERVASAUN
Quelicai	4	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CULINA-OSSU-UAILALE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	5	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	1	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Jova Construction Unip. Lda	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	2	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Samadare Unip. Lda	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	3	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UADA-BORU	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	4	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAI-ACA/MULIA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	5	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF ABO-LIR LALETEK	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	6	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBC LETEMUMO	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	7	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	8	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CATOLICA DARENAFA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	9	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF MAURO DARALA/BORUMODO	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
	10	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF UAIDORA/OSSOLIA	PLAN																																monitorizasaun Actual la tuir planu tamba volume servisu barak no conbustivel la sufisiente
							ACTUAL																																	
Vemasse	1	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Esa-Un	PLAN																																ABANONA
							ACTUAL																																	
	2	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Wrangler Unipessoal,Lda	PLAN																																PROJECTO REFERE ENTREGA TIHA ONA BA MUNICIPIO
							ACTUAL																																	

Note:

Periode inspesaun iha tereinu

Implementasaun Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Agustinho Aranda)
Eng. Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi :

(Eng.Januario maia Guterres)
Adjunto Director Executivo ADN , I. P.
