REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público

A.D.N, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

RELATÓRIU MENSÁL IMPLEMENTASAUN PROJETUS MUNISÍPIU LIQUICA

JULHO 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTASAUN PROJETO INFRAESTRUTURA IHA MUNICIPIO LIQUICA JULHO 2022

Prepara Husi :

(Eng. Juninho Antonio A. Da Cruz)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Liquica ADN, I.P

(Eng. Marcus Ximenes de Araujo)
Eng. ba Projeto Infraestrutura,Transporte e Irigasaun, Municipio Liquica ADN, I.P

(Eng. Antonia de Fatima Morais)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Liquica ADN, I.P

(Eng. Luduvina Maria H. Guterres)
Eng. ba Projeto Infraestrutura,Transporte e Irigasaun, Municipio Liquica ADN, I.P

(Eng. Camilio de Jesus)
Eng. ba Projeto ME Municipio Liquica ADN, I.P

Verifika Husi :

(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edificio Publiku no Beé Saneamentu, ADN, I.P

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba Projeto Infraestrutura e Irigasaun, ADN, I.P

(Deolindo de Fátima Marques)
Chefe Seksaun ba Projeto M. E & ITC, ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :

(Mariano Renato Monteiro da Cruz, S. T, M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO 1

I. INTRODUSAUN. 3

1.1 Enkuadramentu Legal 3

1.2 Perfil Municipio Liquica 3

1.3 Lista Projecto 7

II. PROGRESU FISIKU 18

2.1 Progresso Fisiku Kada Fulan 18

III OBSTÁKLU IHA TERENU 18

3.1 Obstáclo Servisu Iha Terenu 18

VI. REKOMENDASAUN IHA TERENU 19

4.1 Rekomendasaun Servisu iha Terenu 19

INDICE TABELA

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica 5

Tabela 1. 2: Lista Asset ADN,I.P Municipio Liquica 5

Tabela 1.3. 1 Projecto Municipio Liquica Por Fundus Financimento 7

Tabela 1.3. 2 Projecto Muncipio Liquica Por Sectores 9

Tabela 1.3. 3 Projecto Municipio Liquica Por Ministerios 14

Tabela 4. 1 Dadus Populasaun Munisipiu Liquica 18

I. INTRODUSAUN.


1.1 Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análize kustu-benefísiu ne'ebe razoável no viavél.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimentu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba Projeto sira iha programa Kapital Desenvolvimentu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Liquica

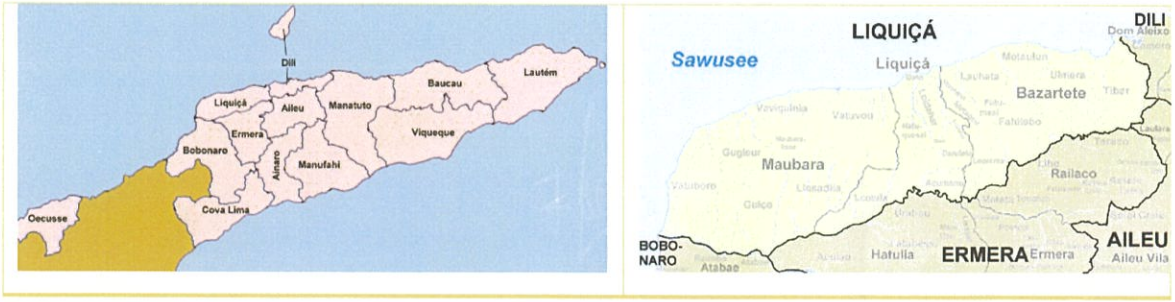

Mapa hatudu pozisaun Administrasaun Munisipal Liquica iha luan area 543 km² ho populasaun nain – 63.403 tuir Sensus 2010. Administrasaun Munisipal Liquica iha Postu Administrativu tolu (3) , Sukus 23 no aldeias 134, mak hanesan hatudu iha Tabela 1

Tabela 1: Postos Administrativos, Sucos no Aldeias.

Bazartete		Liquica		Maubara	
sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**
Fahilelo	3	Açumano	4	Gugleur	11
Fatumasi	4	Darulete	4	Guiço	5
Lauhata	5	Dato	10	Lissadila	7
Leorema	10	Hatuquesi	8	Maubaralissa	5
Maumeta	4	Leotala	5	Vatuboro	5
Metagou	3	Loidahar	4	Vatuvou	10
Motaulun	3	Luculai	4	Vaviquinia	7
Tibar	4	-	-	-	-
Ulmera	9	-	-	-	-
Total	**45**	-	**39**	-	**50**

Data husi: Livro 3 B OJE 2021, pag 58

Tabela 1. 1 : Força de Trabalho ADN, I.P Municipio Liquica

Forca de Trabalho ADN,I.P Municipio Liquica								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro		2				2	
2	Administrasaun no Financas		0				0	
3	Motorista		1				1	
4	Seguransa		0				0	
Total			**3**				**3**	

Tabela 1. 2 : Lista Asset ADN,I.P Municipio Liquica

ASSET ADN,IP MUNICIPIO LIQUICA								
No	**Deskrisaun**	**Total Aset Kada Tinan**					**Total**	**OBS**
		2021	**2022**	**2023**	**2024**	**2025**		
1	Edificio		1					
2	Kareta		1					
3	Desktop HP / Monitor		1					
4	Laptop HP		1					
5	Printer Cannon		1					
6	UPS		1					
7	Armario File		1					
8	Armario Tau hena		3					
9	Meja escritorio		1					
10	Meja han		1					
11	Meja TV (kiik)		1					
12	Kadeira escritorio		6					
13	Kadeira han		4					

14	Sofa		1 Set					
15	Springbed +sumasu 4+sprei 3		3 Set					
16	Jeleira		1					
17	Water Dispenser		1					Aát
18	TV + Parabola		1 Set					
19	AC		4					
20	Kipas Angin		1					
21	Kompor		1					
22	Kompor Gas		1					
23	Rack sepatu		3					
24	Rack Piring		1					
25	Lampu		11					
26	Water Pump Sanyo		0					

1.3 Lista Projecto

Projeto hotu ne'ebe akumula iha lista neé bazeia ba dadus Projeto nebe sei lao hela no mos Projeto nebe abandona ona iha tinan barak nia laran, Projeto hirak ne'e fahe tuir lista tabela 1.3.1 Projeto Por Fundus Finansiamento, Tabela 1.3.2 Projeto Por Sector no tabela 1.3.3 Projeto Por Ministerio, no lista detallu kada Projeto bele hare iha #Aneksu A.

Tabela 1.3. 1 Projeto Municipio Liquica Por Fundus Financiamento



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

NO	POSTO ADMINISTRATIVO	TOTAL FI + LM (CD + BS + TP + FUNDO COVID etc..) + EMERGENCY + PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	28	$ 8,783,221.83	$ 2,291,293.83	26.09%
2	LIQUICA VILA	26	$ 5,849,524.82	$ 1,904,064.56	32.55%
3	MAUBARA	19	$12,054,713.43	$ 8,440,206.88	70.02%
	Grand Total	**73**	**$26,687,460.08**	**$12,635,565.27**	**47.35%**

NO	POSTO ADMINISTRATIVO	FI			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	$ 5,508,958.72	$ 546,664.59	9.92%
2	LIQUICA VILA	5	$ 3,337,190.73	$ 1,574,997.92	47.20%
3	MAUBARA	5	$10,171,195.89	$ 8,144,321.76	80.07%
	Grand Total	**14**	**$19,017,345.34**	**$10,265,984.27**	**53.98%**

Dados Detallu Kada Projeto #Anexu A

NO	POSTO ADMINISTRATIVO	LM -CD			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	7	$ 834,783.75	$ 201,118.76	24.09%
2	LIQUICA VILA	11	$1,528,099.12	$ 158,980.66	10.40%
3	MAUBARA	7	$ 951,175.37	$ 85,262.85	8.96%
	Grand Total	**25**	**$3,314,058.24**	**$ 445,362.27**	**13.44%**

NO	POSTO ADMINISTRATIVO	LM –BS			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	6	$ 897,734.42	$674,396.77	75.12%
2	LIQUICA VILA	3	$ 332,370.82	$170,085.98	51.17%
3	MAUBARA	2	$ 344,450.27	$ 72,706.50	21.11%
	Grand Total	**11**	**$1,574,555.51**	**$917,189.25**	**58.25%**

NO	POSTO ADMINISTRATIVO	LM -TP			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	$ 289,002.61		
2	LIQUICA VILA	6	$ 474,930.65		
3	MAUBARA	3	$ 359,595.59		
	Grand Total	**13**	**$1,123,528.85**		

Dados Detallu Kada Projeto #Anexu A

NO	POSTO ADMINISTRATIVO	FUNDO - COVID			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	4	$ 433,364.88	$ 287,933.63	66.44%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	**4**	**$433,364.88**	**$287,933.63**	**66.44%**

NO	POSTO ADMINISTRATIVO	EMERGENCY			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	1	$ 502,473.28	$ 441,060.32	87.78%
2	LIQUICA VILA				
3	MAUBARA				
	Grand Total	**1**	**$ 502,473.28**	**$ 441,060.32**	**87.78%**

NO	POSTO ADMINISTRATIVO	PDIM			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN (%)
1	BAZARTETE	2	$ 316,904.17	$ 140,119.76	44.22%
2	LIQUICA VILA	1	$ 176,933.50		
3	MAUBARA	2	$ 228,296.31	$ 137,915.77	60.41%
	Grand Total	**5**	**$ 722,133.98**	**$ 278,035.53**	**38.50%**

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 2 Projeto Municipio Liquica Por Sectores

NO	SECTOR	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA	2	$ 91,877.21	$ 80,662.08	87.79%
2	AGUA E SANEAMENTO	3	$ 293,629.77	$ 167,315.56	56.98%
3	EDIFICIOS PUBLICOS	2	$ 210,635.04	$ -	0.00%
4	EDUKASAUN	18	$ 1,956,926.91	$ 302,946.05	15.48%
5	ELETRIFIKASAUN NASIONAL	7	$ 7,088,688.86	$ 1,356,756.80	19.14%
6	ESTRADA- IMPRESTIMO	1	$ 7,693,101.00	$ 5,921,336.53	76.97%
7	ESTRADAS	25	$ 5,166,524.75	$ 2,184,514.45	42.28%
8	FLOOD CONTROL	1	$ 502,473.28	$ 441,060.32	87.78%
9	MANUTENSAUN NO REHABILITASAUN	7	$ 1,522,380.50	$ 1,081,134.13	71.02%
10	PORTOS	1	$ 1,394,750.00	$ 657,275.92	47.12%
11	SAUDE	4	$ 433,364.88	$ 287,933.63	66.44%
12	SEGURANCA NO DEFESA	1	$ 58,107.88	$ 50,129.80	86.27%
13	TURISMO	1	$ 275,000.00	$ 104,500.00	38.00%
	Grand Total	**73**	**$26,687,460.08**	**$12,635,565.27**	**47.35%**

Dados Detallu Kada Projeto #Anexu A

NO	SECTOR	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA	2	$ 91,877.21	$ 80,662.08	87.79%
2	AGUA E SANEAMENTO	2	$ 122,664.12	$ 94,609.06	77.13%
3	EDIFICIOS PUBLICOS	1	$ 154,189.34	$ -	0.00%
4	EDUKASAUN	7	$ 783,470.96	$ 165,030.28	21.06%
5	ELETRIFIKASAUN NASIONAL	2	$5,296,850.84	$ 449,325.76	8.48%
6	ESTRADA- IMPRESTIMO				
7	ESTRADAS	7	$ 774,770.99	$ 165,825.10	21.40%
8	FLOOD CONTROL	1	$ 502,473.28	$ 441,060.32	87.78%
9	MANUTENSAUN NO REHABILITASAUN	1	$ 565,452.33	$ 556,717.80	98.46%
10	PORTOS				
11	SAUDE	4	$ 433,364.88	$ 287,933.63	66.44%
12	SEGURANCA NO DEFESA	1	$ 58,107.88	$ 50,129.80	86.27%
13	TURISMO				
	Grand Total	**28**	**$8,783,221.83**	**$2,291,293.83**	**26.09%**

Dados Detallu Kada Projeto #Anexu A

NO	SECTOR	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA				
2	AGUA E SANEAMENTO				
3	EDIFICIOS PUBLICOS				
4	EDUKASAUN	7	$ 642,009.75		
5	ELETRIFIKASAUN NASIONAL	3	$1,490,077.80	$ 689,824.97	46.29%
6	ESTRADA- IMPRESTIMO				
7	ESTRADAS	9	$1,365,759.10	$ 32,547.34	2.38%
8	FLOOD CONTROL				
9	MANUTENSAUN NO REHABILITASAUN	6	$ 956,928.17	$ 524,416.33	54.80%
10	PORTOS	1	$1,394,750.00	$ 657,275.92	47.12%
11	SAUDE				
12	SEGURANCA NO DEFESA				
13	TURISMO				
	Grand Total	**26**	**$5,849,524.82**	**$1,904,064.56**	**32.55%**

Dados Detallu Kada Projeto #Anexu A

NO	SECTOR	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	AGRICULTURA				
2	AGUA E SANEAMENTO	1	$ 170,965.65	$ 72,706.50	42.53%
3	EDIFICIOS PUBLICOS	1	$ 56,445.70		
4	EDUKASAUN	4	$ 531,446.20	$ 137,915.77	25.95%
5	ELETRIFIKASAUN NASIONAL	2	$ 301,760.22	$ 217,606.07	72.11%
6	ESTRADA- IMPRESTIMO	1	$ 7,693,101.00	$5,921,336.53	76.97%
7	ESTRADAS	9	$ 3,025,994.66	$1,986,142.01	65.64%
8	FLOOD CONTROL				
9	MANUTENSAUN NO REHABILITASAUN				
10	PORTOS				
11	SAUDE				
12	SEGURANCA NO DEFESA				
13	TURISMO	1	$ 275,000.00	$ 104,500.00	38.00%
	Grand Total	**19**	**$12,054,713.43**	**$8,440,206.88**	**70.02%**

Dados Detallu Kada Projeto #Anexu A

Tabela 1.3. 3 Projeto Municipio Liquica Por Ministerios



MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL



ADN, I.P.

Agência de
Desenvolvimento
Nacional, Instituto Público

NO	DONO DO PROJETO	GRAND TOTAL			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	3	$ 387,568.54		
2	MINISTERIO AGRIKULTURA E PESCAS	3	$ 139,176.53	$ 118,527.60	85.16%
3	MINISTERIO DAS OBRAS PUBLICAS	41	$21,943,080.54	$11,031,749.58	50.27%
4	MINISTERIO DO INTERIOR	1	$ 58,107.88	$ 50,129.80	86.27%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	18	$ 1,956,926.91	$ 302,946.05	15.48%
6	MINISTERIO PLANU E ORDENAMENTU	1	$ 99,484.80	$ 82,502.69	82.93%
7	MINISTERIO SAUDE	4	$ 433,364.88	$ 287,933.63	66.44%
8	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$ 1,394,750.00	$ 657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 275,000.00	$ 104,500.00	38.00%
	Grand Total	**73**	**$26,687,460.08**	**$12,635,565.27**	**47.35%**

Dados Detallu Kada Projeto #Anexu A

NO	DONO DO PROJETO	BAZARTETE			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	1	$ 154,189.34		
2	MINISTERIO AGRIKULTURA E PESCAS	2	$ 91,877.21	$ 80,662.08	87.79%
3	MINISTERIO DAS OBRAS PUBLICAS	12	$7,162,726.76	$1,625,035.35	22.69%
4	MINISTERIO DO INTERIOR	1	$ 58,107.88	$ 50,129.80	86.27%
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	$ 783,470.96	$ 165,030.28	21.06%
6	MINISTERIO PLANU E ORDENAMENTU	1	$ 99,484.80	$ 82,502.69	82.93%
7	MINISTERIO SAUDE	4	$ 433,364.88	$ 287,933.63	66.44%
8	MINISTERIO TRANPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
	Grand Total	**28**	**$8,783,221.83**	**$2,291,293.83**	**26.09%**

Dados Detallu Kada Projeto #Anexu A

NO	DONO DO PROJETO	LIQUICA VILA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	1	$ 176,933.50		
2	MINISTERIO AGRIKULTURA E PESCAS	1	$ 47,299.32	$ 37,865.52	80.06%
3	MINISTERIO DAS OBRAS PUBLICAS	16	$3,588,532.25	$1,208,923.12	33.69%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	7	$ 642,009.75		
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$1,394,750.00	$ 657,275.92	47.12%
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA				
	Grand Total	**26**	**$5,849,524.82**	**$1,904,064.56**	**32.55%**

Dados Detallu Kada Projeto #Anexu A

NO	DONO DO PROJETO	MAUBARA			
		TOTAL PROJETO	MONTANTE KONTRATU ($)	MONTANTE EZEKUSAUN ($)	PERCENTAGEM EZEKUSAUN ($)
1	ESTATAL	1	$ 56,445.70		
2	MINISTERIO AGRIKULTURA E PESCAS				
3	MINISTERIO DAS OBRAS PUBLICAS	13	$11,191,821.53	$8,197,791.11	73.25%
4	MINISTERIO DO INTERIOR				
5	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	4	$ 531,446.20	$ 137,915.77	25.95%
6	MINISTERIO PLANU E ORDENAMENTU				
7	MINISTERIO SAUDE				
8	MINISTERIO TRANPORTES E KOMUNIKASAUN				
9	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 275,000.00	$ 104,500.00	38.00%
	Grand Total	**19**	**$12,054,713.43**	**$8,440,206.88**	**70.02%**

Dados Detallu Kada Projeto #Anexu A

Tabela 4. 1 : Dadus Populasaun Munisipiu Liquica

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Bazartete	31,983	9,158	9,039	7,089	6,697
Liquiça	25,334	6,978	7,348	5,672	5,337
Maubara	25,234	7,088	6,802	5,766	5,578

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan refere hetan husi Progressu servisu nebe kompanha sira atinji iha fulan neé nia laran, husi lista nebe iha #Anexu B hatudu progressu aktual fulan ida neé ho nia persentagen servisu, montante aktual bazeia ba orsamento nebe hetan husi progressu fulan ida neé, ikus liu persentagen aktual fulan ida neé hatudu progressu fisiku komulativa husi porsento anterior no fulan ida neé nian, lista kompletu ba detailho bele hare iha #Anexu B, detallu ba Backup Fotografia #Anexu C1, Detallu ba Backup BoQ #Anexu C2 no Instrusaun servisu bele hare #Anexu D

III. OBSTÁKLU IHA TERENU

3.1 Obstáclo Servisu Iha Terenu

Durante iha Fulan ida nia laran, problema nebe ami enjineiru municipio hasoru mak hanesan :

1. Projeto lao tarde
2. Companhia balun servisu la tuir spesifikasaun
3. Companhia balun servisu la iha Site Engineer
4. Difikulidade ba Ekipa ADN M.Liquica hasoru susar ba Be'e mos

VI. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu iha Terenu

1. Rekomenda ba Kompanhia sira servisu tuir spesifikasaun nebe iha ona
2. Rekomenda ba Kompanhia sira tenke iha Site Engineer iha terenu

Rekomenda ba ADN.I.P. Nacional liu-liu ba Superior sira hodi hare ba Edificio ADN.I.P.

Note : Assinatura Husi Enjineiru Municipio Liquica

Força de Trabalho ADN,I.P Municipio Liquica					
No	**Deskrisaun**	**Identidade**			
		Naran Kompletu e Asinatura	**Nu. ID Card**	**Pozisaun**	**Fotografia**
1	Enjineiru	Juninho António A. Da Cruz	216	Enjineiru EPAS	
		Marcus Ximenes de Araujo	172	Enjineiru ITI	
		Luduvina Maria H. Guterres	251	Enjineira ITI	

		Antonia de Fatima Morais	241	Enjineira EPAS	
		Camilio de Jesus	061	Enjineiru METIC	
2	Enjineira	Nencia F.O. do Rêgo	173	Enjineira VEBD	
3	Motorista	Rui Antonio Gaio	029	Motorista	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica - JULHO 2022

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
1	New Installation MV,LV Line and House Connection for Bazartete Vila to Leorema -Bazartete Sub District-Liquica District	Mina Petro Leste Unip, Lda	RDTL-11004589	$ 499,250.84		100.00%	90.00%	$ 449,325.76	$ 49,925.08	ABANDONA	
2	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica	Banir Lema	MPW-W-190097	$ 565,452.33	Aug. 14, 2019	100.00%	98.46%	$ 556,717.80	$ 8,734.53	FHO	Progresio Fisiko 100% e hela pagamento retensaun 10%
3	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	$ 162,714.83	Aug. 16, 2019	95.68%	86.11%	$ 140,119.76	$ 22,595.07	PHO	Progresu fizikamente remata ona no hein retensaun
4	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	Lep Laco Dato	MPW-W-190111	$ 73,270.51	Sept. 5, 2019	100.00%	97.90%	$ 71,729.53	$ 8,712.25	FHO	Progresu fizikamente 100 % e sei falta pagamento ba retensaun
5	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	$ 23,950.17	Dec. 5, 2019	77.60%	69.84%	$ 16,726.74	$ 7,223.43	ON-GOING	Provezoriamente servisu paradu hela
6	Konstrusaun Foun EBF Hotugara Bazartete, Liquica	Milcha Unip Lda	(RFQ:19/029-Q-R)	$ 67,492.69	Nov. 10, 2019	41.01%	36.91%	$ 24,910.52	$ 42,582.17	ON-GOING	
7	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	$ 23,179.32	Oct. 22, 2019	79.24%	52.23%	$ 12,106.37	$ 11,072.90	ON-GOING	Provezoriamente servisu paradu hela
8	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	$ 58,107.88	Nov. 29, 2019	86.27%	86.27%	$ 50,129.80	$ 10,484.57	FHO	
9	Konstrusaun Armagen Foun Matadouro	Naesalobu	MAP-P02019:19532	$ 67,927.04	Dec. 5, 2019	82.29%	94.12%	$ 63,935.34	$ 17,617.77	FHO	Progresu fizikamente remata ona
10	New Construction of Laboratory for Covid 19 in Liquica Ministry of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	$ 66,557.90	Oct. 23, 2020	73.90%	66.51%	$ 44,268.56	$ 22,289.34	ON-GOING	ongoing
11	New construction of isolation for covid 19 in liquica, Timor Leste	SENIZU UNIPESSOAL LDA	MS-DNA-NCB-20-163	$ 243,368.08	Oct. 22, 2020	96.86%	87.18%	$ 212,156.22	$ 31,211.86	PHO	Projetu refere hela retensaun (10%) e Fisiku iha Tereno atinji deit 96.86%
12	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	$ 99,484.80	Sept. 9, 2019	92.14%	82.93%	$ 82,502.69	$ 16,982.11	ON-GOING	Falta retensaun
13	Emergency Project For Tibar River	Sali Magu Unipessoal Lda	RT/067/MOP-2021	$ 502,473.28	Sept. 20, 2021	99.75%	87.78%	$ 441,060.32	$ 61,412.96	ON-GOING	ON-GOING
14	Konstrusaun Edificio Posto Administrativo Bazartete & Moru Haleu	Aquarius Construction Unip,Lda	02/SMA-AML/PDIM VIII/2021	$ 154,189.34	Aug. 31, 2021	0.00%	0.00%	$ -	$ -	ON-GOING	Adn,IP la hare
15	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	$ 149,732.87	Oct. 01, 2021	36.39%	0.00%	$ -	$ -	ON-GOING	
16	R4D Rural Road Spot Improvement Fahilebo -Fatumasi Chainage 0+000-2+300 , Liquica Municipality	Hatumeta Oan, Unip.Lda	MOP - CD-RFQ - 21017	$ 88,852.44	Oct. 01, 2021	15.75%	0.00%	$ -	$ -	ON-GOING	
17	R4D Rural Road Spot Improvement Libaloa - Fahilebo Chainage 0+000-7+000, liquica Municipality	Hatuleo Unip Lda	MPW-W-210144	$ 88,425.80	Oct. 01, 2021	53.86%	35.54%	$ 31,422.82	$ -	ON-GOING	
18	Rural Road Spot Improvement Maumeta-Metagou-Bazartete Chainage 0+000 - 10+000, Liquica Municipality	CRAELEKI BERCOLI UNIPESSOAL LDA	MPW-W-210145	$ 62,024.04	Oct. 01, 2021	30.43%	24.93%	$ 15,463.72	$ 46,560.32	ON-GOING	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica - JULHO 2022

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
19	R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality	TM Caileba Unip,Lda	MPW-W-210158	$ 158,465.33	Oct. 01, 2021	33.67%	0.00%	$ -	$ -	ON-GOING	
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	Biamali Unipessoal Lda	RDTL-MS	$ 65,271.32		74.84%	48.27%	$ 31,508.85	$ 33,762.47	ON-GOING	
22	Konstrusaun Foun ESTV Leorema - Liquica	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	$ 264,260.83	1/11/2021	20.76%	0.00%	$ -		ON-GOING	
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MEJD PKRIE EPE BAURA	-	$ 9,072.12	15/10/2021	10.86%	0.00%	$ -		ON-GOING	
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MEJD PKRIE EPE ERMETA	-	$ 86,365.84	15/10/2021	10.99%	0.00%	$ -		ON-GOING	
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MEJD PKRIE EPE CASSAIT	-	$ 78,250.89	15/10/2021	14.34%	0.00%	$ -		ON-GOING	
26	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MEJD PKRIE ESG-PARALELO BOGORO	-	$ 115,313.76	15/10/2021	9.39%	0.00%	$ -		ON-GOING	
27	Melhoramento no Suplly Energia Elektricidade husi Sub Stasaun Liquisa ba Portu Tibar (Engineering Procurement Construction - Design, Suplly, Installtion, Testing and Commissioning Extension Transformer Bay Of the Existing 150/20kV LIquica Substation to Suplly Power to Tibar Bay Port)	China Shandong International Economic And Technical Cooperation Group. LTD	RFP/054/MOP-2021	$ 4,797,600.00	Dec. 16, 2021	0.00%	0.00%	$ -	$ -	ON-GOING	
28	Supervision Consultant for Construction of Intersection in the Existing Dili - Liquica Road to Connect Access Road from Tibar Bay Port (National Road - A03) Sta. 0+000 - Sta. 0+620	Lelo Engineering Unipessoal Lda	RFP/072/MOP-2021	$ 154,000.00	Dec. 14, 2021	95.77%	30.66%	$ 47,209.03	$ 106,790.97	ON-GOING	
29	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	$ 153,851.88	Dec. 5, 2019	95.49%	85.94%	$ 132,220.46	$ 21,631.42	FHO	Servisu iha Tereno remata tiha ona, sei hein kompanha Amenda kontratu nebe mate tiha ona
30	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	$ 1,394,750.00	May 17, 2017	100%	47.12%	$ 657,275.92	$ 737,474.08	ON-GOING	
31	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	Nheu	MPW-W-RFQ-190093	$ 55,012.05	Aug. 22, 2019	100%	99.91%	$ 54,964.83	$ 5,543.70	FHO	Projetu refere hela retensaun (10%) e Fisiku iha Tereno atinji deit 99.91%
32	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica	Goubara Unip Lda	MPW-W-190096	$ 71,468.49	Aug. 19, 2019	92.32%	100.00%	$ 71,468.49	$ 7,146.85	FHO	
33	New Installation MV, LV LIne and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	$ 593,093.80	Jan. 6, 2017	92.77%	67.45%	$ 400,036.22	$ 193,057.58	ON-GOING	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica - JULHO 2022

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
34	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	$ 276,484.00	July 6, 2016	80.84%	83.49%	$ 230,841.25	$ 45,642.75	ON-GOING	
35	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	$ 452,362.93	Dec. 20, 2019	80.84%	50.38%	$ 227,897.03	$ 224,465.90	ON-GOING	
36	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip,Lda	RDTL 0000	$ 47,299.32	Aug. 18,2021	88.95%	80.06%	$ 37,865.52	$ 9,433.80	PHO	
37	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	$ 176,933.50	Aug. 31, 2021	0.00%	0.00%	$ -	$ -	ON-GOING	Adn,IP la hare
38	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	$ 131,219.62	Oct. 01, 2021	37.36%	0.00%	$ -	$ -	ON-GOING	
39	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	$ 123,631.72	Oct. 01, 2021	36.16%	0.00%	$ -	$ -	ON-GOING	
40	R4D Rural Road Spot Improvement Metagou - Aibenu Chainage 0+000-7+600, Liquica Municipality	Metalika Unipessoal, Lda	MOP - CD - NCB -R - 21038	$ 238,739.71	Oct. 01, 2021	26.40%	0.00%	$ -	$ -	ON-GOING	
41	R4D Rural Road Spot Improvement Dato - Loidahar Chainage 0+000-12+300, Liquica Municipality	Luqueli Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	$ 188,589.13	Oct. 01, 2021	37.33%	0.00%	$ -	$ -	ON-GOING	
42	R4D Rural Road Spot Improvement Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality	Caiulu, Unip Lda	MOP - CD - NCB -R - 21035	$ 162,215.27	Oct. 01, 2021	36.86%	0.00%	$ -	$ -	ON-GOING	
43	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leurema Chainage 0+000-5+000, Liquica Municipality	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	$ 165,363.43	Oct. 01, 2021	24.09%	0.00%	$ -	$ -	ON-GOING	
44	R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chainage 2+500-5+400	Claridade Unip,Lda	MPW-W-210163	$ 167,071.89	Oct. 01, 2021	21.26%	0.00%	$ -	$ -	ON-GOING	
45	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000	Craeleki Bercoli, Unip Lda	MPW-W-210143	$ 76,423.05	Oct. 01, 2021	20.98%	0.00%	$ -	$ -	ON-GOING	
46	Projeitu Konstrusaun foun ESG publico 01 Liquica	Roman Furak Unip,Lda	NCB 16/MEJD/DNA/2021	$ 167,079.099	Nov. 1, 2021	28.85%	0.00%	$ -	$ -	ON-GOING	
47	For Roads Maintenance Section : Tibar - Liquica - Maubara, Carimbala - Loes (A03)	Chantel Chander Unipessoal Lda	MPW-W-210202	$ 112,505.280	13/12/2021	32.14%	28.93%	$ 32,547.34	$ 79,957.94	ON-GOING	
48	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MEJD PKRIE EBC MAUBOQUE	-	$ 112,530.010	15/10/2021	13.84%	0.00%	$ -	$ -	ON-GOING	
49	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MEJD PKRIE EBC 1,2,3 LIQUICA	-	$ 99,456.040	15/10/2021	13.09%	0.00%	$ -	$ -	ON-GOING	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica - JULHO 2022

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
50	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MEJD PKRIE EPE LOIDAHAR	-	$ 79,735.630	15/10/2021	10.19%	0.00%	$ -	$ -	ON-GOING	
51	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclolema	MEJD PKRIE Ebf 1,2 LACLOLEMA	-	$ 89,650.660	15/10/2021	12.10%	0.00%	$ -	$ -	ON-GOING	
54	Consultant Services to Supervise EPC Contractor for the Up-Gradation of Liquica 150/20kV Substation to Supply Power to Tibar Bay Port	PT. Artefak Arkindo (Indonesia) JV with Jazicasnu Unipessoal Lda	RFP/054/MOP-2021	$ 620,500.000	Dec. 16, 2021	10.00%	9.50%	$ 58,947.50	$ 561,552.50	ON-GOING	
55	Addt. Poste liga Maubara	Fu Unip,Lda	RDTL - 0000	$ 13,000.00	Jan. 1, 2016	0.00%	0.00%	$ -	$ 13,000.00	ON-GOING	
56	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000364	$ 288,760.22	July 6, 2016	83.73%	75.36%	$ 217,606.07	$ 71,154.15	ON-GOING	
57	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	Montana Diak, Unipessoal, Lda	SSS/126/MOPTC-2017	$ 1,901,334.67	Sept. 7, 2017	99.98%	99.98%	$ 1,900,879.16	$ 455.51	FHO	
58	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	$ 275,000.00	Dec. 27, 2016	0.00%	0.00%	$ 104,500.00	$ 170,500.00	ON-GOING	Adn,IP la hare
59	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	$ 171,850.61	Aug. 16, 2019	89.18%	80. 25%	$ 137,915.77	$ 33,934.84	ON-GOING	
60	Rehabilitasaun Sistema be'e mos iha aldeia Pandevou ho Mau-Uno,Sucu Guico /162	Oceania Const Unip.Lda	NCB-MOP-190051	$ 170,965.65	Jan. 3, 2019	54.99%	42.53%	$ 72,706.50	$ 98,259.15	ON-GOING	Provizoriamente paradu hela
61	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOPTC/2016	$ 7,693,101.00	May 3, 2017	76.97%	76.97%	$ 5,921,336.53	$ 1,771,764.47	ON-GOING	Ekipa AND.I.P Nacional nebe toma konta ba Imprestimo maka Hare
62	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000 - 1+600 Vaviquinia - Maubaralisa Chainage 0+000 - 12+500	Luliana Unip,Lda	MPW-W-190098	$ 50,702.59	Aug. 28, 2019	95.90%	86.31%	$ 43,761.73	$ 6,940.86	FHO	
63	Konstrusaun Moru Haleu no Posto Siguransa ba Edificio Posto Administrativo Maubara	Rafio Unip. Lda	01/AML/SMA-PDIM/VIII/2021	$ 56,445.70	July 21, 2021	0.00%	0.00%	$ -	$ -	ON-GOING	Adn,IP la hare
64	R4D Rural Road Spot Improvement Nunulete - Darulema Chainage 0+000-2+000, Liquica Municipality	Rito - Pu, Unipessoal,Lda	MOP -CD-RFQ - 21013	$ 67,382.23	Oct. 01, 2021	2.07%	0.00%	$ -	$ -	ON-GOING	
65	R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600	Malibo, Unipessoal LDA	MOP - CD- NCB-R- 21033	$ 152,622.90	Oct. 01, 2021	28.98%	0.00%	$ -	$ -	ON-GOING	
66	R4D Rural Road Spot Improvement Barkau (Vaviquenia)-Maubaralisa Chainage 0+000-4+200	Nheu, Unipessoal LDA	MOP - CD- NCB-R- 21027	$ 173,484.62	Oct. 01, 2021	45.61%	0.00%	$ -	$ -	ON-GOING	
67	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+000-4+800	Murak, Unipessoal Lda	MPW-W-210157	$ 153,049.65	Oct. 01, 2021	35.21%	27.12%	$ 41,501.12	$ 111,548.53	ON-GOING	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

#ANEXO A

Lista Geral Projetu On-going Municipio Liquica - JULHO 2022

NU	NARAN PROJETU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROGRESO FISIKU (%)	PROGRESO PAGAMENTO (%)	PAGAMENTO ($)	BALANSU ($)	STATUS PROJECT	OBSERVASAUN
68	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa, Chainage 8+400-12+500)	Meta Loe Crae Bau Unip,Lda	MPW-W-210160	$ 198,698.25	Oct. 01, 2021	11.66%	0.00%	$ -	$ -	ON-GOING	
69	R4D Rural Road Spot Improvement Samarapo -Gisu Chainage 0+000-2+000	Nazico Unip Lda	-	$ 114,789.50	Oct. 01, 2021	11.39%	0.00%	$ -	$ -	ON-GOING	
70	R4D Rural Road Spot Improvement Barkau (Vaviquina) - Maubaralisa Chainage 4+200-8+400	Luliana Unip,Lda	MPW-W-210161	$ 213,930.25	Oct. 01, 2021	16.53%	0.00%	$ -	$ -	ON-GOING	
71	Konstrusaun ka Reabilitasaun ba EBF Gariana	MEJD PKRIE EBF GARIANA	-	$ 117,902.04	Oct. 15, 2021	1.98%	0.00%	$ -	$ -	ON-GOING	
72	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MEJD PKRIE EBF TAPO	-	$ 100,033.33	Oct. 15, 2021	0.00%	0.00%	$ -	$ -	ON-GOING	
73	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MEJD PKRIE ESG-PARALELO MAUBARA/BATUVOU	-	$ 141,660.22	Oct. 15, 2021	10.78%	0.00%	$ -	$ -	ON-GOING	

PREPARA HUSI,

(Eng. Marcus Ximenes de Araujo)
Eng. ba Projetu Infrastutura
Transporte e Irigasaun, ADN,I.P

(Eng. Camilio de Jesus)
Eng. Mekanikal e Electrikal ADN,I.P

(Eng. Juninho A. Abrantes da Cruz)
Eng. ba Edificio Publico Agua e
Sanramento, ADN,I.P

(Eng. Luduvina Maria Helena Guterres)
Eng. ba Projetu Infrastutura Transporte e
Irigasaun, ADN,I.P

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa M.Freitas)
Coordenadora da Unidade de Controlo e
Validasaun de Qualidade, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO B

PROGRESSU FISIKU FULAN JULHO MUNICIPIO LIQUICA

					LOKALIZASAUN PROJETO						Jul-22		
NU	NARAN PROJETU	DONO PROJETO	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNICIPIO	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	OBSERVASAUN	Previous Progress (%)	This Month Progress (%)	Comulative Progress (%)
1	New Installation MV,LV Line and House Connection for Bazartete Vila to Leorema - Bazartete Sub District-Liquica District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	BAZARTETE	LIQUICA	Mina Petro Leste Unip, Lda	RDTL-11004589	$ 499,250.84	Oct. 1, 2020				
2	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Banir Lema	MPW-W-190097	$ 565,452.33	Aug. 14, 2019	FHO	98.46%	0.00%	98.46%
3	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	BAZARTETE	LIQUICA	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	$ 162,714.83	Aug. 16, 2019	Progresu fizikamente remata ona no hein retensaun	95.68%	0.00%	95.68%
4	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Lep Laco Dato	MPW-W-190111	$ 73,270.51	Sept. 5, 2019	FHO	97.90%	0.00%	97.90%
5	Konstrusaun Moralha Foun Matadoro Tibar	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	$ 23,950.17	Dec. 5, 2019	Provezoriamente servisu paradu hela	77.60%	0.00%	77.60%
6	Konstrusaun Foun EBF Hotugara Bazartete, Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	EDUKASAUN	BAZARTETE	LIQUICA	Milcha Unip Lda	(RFQ:19/029-Q-R)	$ 67,492.69	Nov. 10, 2019	Parado	41.01%	0.00%	41.01%
7	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Culoco Unipessoal Lda	Contract No.MOP-W-190184	$ 23,179.32	Oct. 22, 2019	Provezoriamente servisu paradu hela	79.24%	0.00%	79.24%
8	New Water Supply of Bairos PNTL Liquica	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	BAZARTETE	LIQUICA	Holuli Unipessoal, Lda	SSS/054/MI-2019	$ 58,107.88	Nov. 29, 2019	FHO	86.27%	0.00%	86.27%
9	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	BAZARTETE	LIQUICA	Naesalobu	MAP-P02019:19532	$ 67,927.04	Dec. 5, 2019	FHO	94.12%	0.00%	94.12%
10	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	MINISTERIO SAUDE	FUNDO COVID	SAUDE	BAZARTETE	LIQUICA	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	$ 66,557.90	Oct. 23, 2020	Servisu Refere seidauk 100%	73.90%	0.00%	73.90%
11	New construction of isolation for covid 19 in liquica, Timor Leste	MINISTERIO SAUDE	FUNDO COVID	SAUDE	BAZARTETE	LIQUICA	Senizu	MS-DNA-NCB-20-163	$ 243,368.08	Oct. 22, 2020	PHO	96.86%	0.00%	96.86%
12	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	MINISTERIO PLANU E ORDENAMENTU	LM -CD	AGUA E SANEAMENTO	BAZARTETE	LIQUICA	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	$ 99,484.80	Sept. 9, 2019	PHO	92.14%	0.00%	92.14%
13	Emergency Project For Tibar River	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	FLOOD CONTROL	BAZARTETE	LIQUICA	Sali Magu Unipessoal Lda	RT/067/MOP-2021	$ 502,473.28	Sept. 20, 2021	PHO	99.75%	0.00%	99.75%
14	Konstrusaun Edificio Posto Administrativo Bazartete & Moru Haleu	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	BAZARTETE	LIQUICA	Aquarius Construction Unip,Lda	02/SMA-AML/PDIM VIII/2021	$ 154,189.34	Aug. 31, 2021	ADN, I.P La Hare			
15	R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-NCB-R -21030	$ 149,732.87	Oct. 01, 2021	On Going	25.07%	11.32%	36.39%
16	R4D Rural Road Spot Improvemrnt Fahilebo -Fatumasi Chainage 0+000-2+300 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatumeta Oan, Unip.Lda	MOP - CD-RFQ - 21017	$ 88,852.44	Oct. 01, 2021	On Going	15.75%	0.00%	15.75%
17	R4D Rural Road Spot Improvemrnt Libaloa - Fahilebo Chainage 0+000-7+000, liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Hatuleo Unip Lda	MPW-W-210144	$ 88,425.80	Oct. 01, 2021	On Going	41.18%	12.68%	53.86%
18	Routine Maintenance Maumeta- Metagou - Bazartete Chainage 0+000+10+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	Craseleki Bercoli Unip,Lda	MPW-W-210145	$ 62,024.04	Oct. 01, 2021	On Going	12.71%	17.72%	30.43%
19	R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	BAZARTETE	LIQUICA	TM Caileba Unip,Lda	MPW-W-210158	$ 158,465.33	Oct. 01, 2021	On Going	26.48%	7.20%	33.67%
20	New Construction of Fence Around for Isolation COVID-19 in Liquica Maumeta, Ministerio da Saude Timor Leste	MINISTERIO DA SAUDE	Fundo Covid	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	Biamali Unipessoal Lda	RDTL-MS-C19-DNA-DC-21-233	$ 65,271.32	11/01/2022	On Going	74.84%	0.00%	74.84%
21	Supply and installation connection for isolation and laboratorium Building Maumeta Liquica	MINISTERIO DA SAUDE	Fundo Covid	EDIFICIOS PUBLICOS	BAZARTETE	LIQUICA	ZYC UNIPESSOAL LDA	RDTL-MS-C19-DNA-DC-21-228	$ 58,167.58	11/01/2022	On Going	18.20%	2.53%	20.74%
22	Konstrusaun Foun ESTV Leorema - Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM -BS	EDUKASAUN	BAZARTETE	LIQUICA	U-Rema Unip. Lda.	NCB:15/MEJD/DNA/2021	$ 264,260.83	1/11/2021	On Going	18.21%	2.55%	20.76%
23	Konstrusaun ka Reabilitasaun ba EPE Baura	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 9,072.12	15/10/2021	On Going	10.86%	0.00%	10.86%
24	Konstrusaun ka Reabilitasaun ba EPE Ermeta	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 86,365.84	15/10/2021	On Going	10.06%	0.92%	10.99%
25	Konstrusaun ka Reabilitasaun ba EPE Cassait	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 78,250.89	15/10/2021	On Going	11.89%	2.45%	14.34%
26	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Bogoro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	BAZARTETE	LIQUICA	Grupu Komunitariu	-	$ 115,313.76	15/10/2021	On Going	7.47%	1.92%	9.39%
27	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	$ 153,851.88	Dec. 5, 2019	FHO	95.49%	0.00%	95.49%
28	Development of Tibar Bay Port - PPP Project - on BDFOT Basis	MINISTERIO TRANPORTES E KOMUNIKASAUN	FI	PORTOS	LIQUICA VILA	LIQUICA	EGT ENGENHARIA IN JV with FASE - Estudos e Projectos, S.A.	REP/007/MOPTC-2017	$ 1,394,750.00	May 17, 2017				
29	R4D Rural Road Periodic Maintenance Aibenu - Asumanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Nheu	MPW-W-RFQ-190093	$ 55,012.05	Aug. 22, 2019	FHO	99.91%	0.00%	99.91%
30	Rural Roads Periodic Gunaba - Lukulai Chainage 0+000 & Metagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Goubara Unip Lda	MPW-W-190096	$ 71,468.49	Aug. 19, 2019	FHO	100.00%	0.00%	100.00%
31	New Installation MV, LV LIne and House Connection From Loetela 1 to Loetela 2 - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	LIQUICA VILA	LIQUICA	Maferdi, Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000399	$ 593,093.80	Jan. 6, 2017				
32	New Installation of MV, LV Line and House Connection fromLiquica Vila to Loidahar, Maudemo, Hekar Loidahar, Hatuleho, Koni Leopa, Aipelo, Maumeta, and Leopa - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	LIQUICA VILA	LIQUICA	Busa.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000371	$ 276,484.00	July 6, 2016				
33	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	15 Raelti Unip. Lda	RT/034/MOP-2019	$ 452,362.93	Dec. 20, 2019	On Going	80.84%	0.00%	80.84%
34	Manutensaun Kanais Irrigasaun Faulara - Liquica	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Banir Lema Unip,Lda	RDTL 0000	$ 47,299.32	Aug. 18,2021	PHO	88.95%	0.00%	88.95%
35	Rehabilitasaun Residencia Administrador Municipio, Jardim, Picina no Moru	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	01/SMA-AML/PDIM VIII/2021	$ 176,933.50	Aug. 31, 2021	ADN, I.P La Hare			
36	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Goubara, Unip Lda	MOP - CD - NCB-R - 21025	$ 131,219.62	Oct. 01, 2021	On Going	24.28%	13.08%	37.36%
37	R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	PRUDENCIA CONSTRUCTION, Unip LDA	MOP - CD - NCB-R - 21036	$ 123,631.72	Oct. 01, 2021	On Going	19.39%	16.78%	36.16%
38	R4D Rural Road Spot Improvemrnt Metaqou - Aibenu Chainage 0+000-7+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Metalika Unipessoal, Lda	MOP - CD - NCB -R - 21038	$ 238,739.71	Oct. 01, 2021	On Going	26.40%	0.00%	26.40%
39	R4D Rural Road Spot Improvemrnt Dato - Liodahar Chainage 0+000-12+300, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Luqueli Oan Unipessoal Lda	MOP-CD-NCB-R - 21039	$ 188,589.13	Oct. 01, 2021	On Going	22.00%	15.33%	37.33%
40	R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Caiulu, Unip Lda	MOP - CD - NCB -R - 21035	$ 162,215.27	Oct. 01, 2021	On Going	25.25%	11.61%	36.86%
41	R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Vicaroman, Unip Lda	MOP - CD NCB - R - 21034	$ 165,363.43	Oct. 01, 2021	On Going	18.49%	5.60%	24.09%
42	R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chainage 2+500-5+400	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Claridade Unip,Lda	MPW-W-210163	$ 167,071.89	Oct. 01, 2021	On Going	16.14%	5.12%	21.26%

43	R4D Rural Road Spot Improvement Gunaba - Lukulai Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	LIQUICA VILA	LIQUICA	Craeleki Bercoli, Unip Lda	MPW-W-210143	$ 76,423.05	Oct. 01, 2021	On Going	20.98%	0.00%	20.98%
44	Projeitu Konstrusaun foun ESG publico 01 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM -CD	EDUKASAUN	LIQUICA VILA	LIQUICA	Roman Furak Unip,Lda	NCB 16/MEJD/DNA/2021	$ 167,079.099	Nov. 1, 2021	On Going	28.03%	0.82%	28.85%
45	Roads Maintenance Section ; Tibar - Liquica - Maubara - Carimbala - Loes (A03)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	LIQUICA VILA	LIQUICA	Chantel Chander Unipessoal Lda	MPW-W-210202	$ 112,505.280	44543	On Going	6.47%	25.68%	32.14%
46	Konstrusaun ka Reabilitasaun ba EBF Mauboque	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 112,530.010	44484	On Going	12.28%	1.57%	13.84%
47	Konstrusaun ka Reabilitasaun ba EBC 1,2,3 Liquica	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 99,456.040	44484	On Going	12.35%	0.74%	13.09%
48	Konstrusaun ka Reabilitasaun ba EPE Loidahar	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 79,735.630	44484	On Going	9.70%	0.49%	10.19%
49	Konstrusaun ka Reabilitasaun ba EBF 1,2 Laclolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 89,650.660	44484	On Going	9.97%	2.13%	12.10%
50	Konstrusaun ka Reabilitasaun ba EBF 1,2 Tolema	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 88,407.020	44484	On Going	0.00%	12.64%	12.64%
51	Konstrusaun ka Reabilitasaun ba EBF 1,2 Luculai	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	LIQUICA VILA	LIQUICA	Grupu Komunitariu	-	$ 5,151.290	44484	On Going	0.00%	0.00%	0.00%
52	Addt. Poste liga Maubara	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	MAUBARA	LIQUICA	Fu Unip,Lda	RDTL - 0000	$ 13,000.00	Jan. 1, 2016				
53	New Installation MV, LV Line and House Connection from Kulau to Maubara - Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	MAUBARA	LIQUICA	Britas Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN - 00000364	$ 288,760.22	July 6, 2016				
54	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	MAUBARA	LIQUICA	Montana Diak Unipessoal, Lda	SSS/126/MOPTC-2017	$ 1,901,334.67	Sept. 7, 2017	FHO	99.98%	0.00%	99.98%
55	Consulting services for study master plan and detailed design for ecotourism of Lagoa Maubara	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	TURISMO	MAUBARA	LIQUICA	Bernabad Arquitectura SLP	RFP/147/MTAC/2016	$ 275,000.00	Dec. 27, 2016	ADN, I.P La Hare			
56	Novo Konstrusaun Edificio ESTV Lisadila	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	MAUBARA	LIQUICA	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	$ 171,850.61	Aug. 16, 2019	Servisu Refere seidauk 100%	89.18%	0.00%	89.18%
57	Rehabilitasaun Sistema be'e mos iha aldeia Pandevou ho Mau-Uno,Sucu Guico /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	MAUBARA	LIQUICA	Oceania Const Unip.Lda	NCB-MOP-190051	$ 170,965.65	Jan. 3, 2019	Provizoriamente paradu hela	54.99%	0.00%	54.99%
58	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	MAUBARA	LIQUICA	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOPTC/2016	$ 7,693,101.00	May 3, 2017	Ekipa AND.I.P Nacional nebe toma konta ba Imprestimo maka Hare			
59	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000 - 1+600 Vaviquinia - Maubaralisa Chainage 0+000 - 12+500	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-190098	$ 50,702.59	Aug. 28, 2019	PHO	95.90%	0.00%	95.90%
60	Konstrusaun Moru Haleu no Posto Siguransa ba Edificio Posto Administrativo Maubara	ESTATAL	PDIM	MANUTENSAUN NO REHABILITASAUN	MAUBARA	LIQUICA	Rafio Unip. Lda	01/AML/SMA-PDIM/VIII/2021	$ 56,445.70	July 21, 2021	ADN, I.P La Hare			
61	R4D Rural Road Spot Improvement Nunulete - Darulema Chainage 0+000-2+000, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Rito - Pu, Unipessoal,Lda	MOP -CD-RFQ - 21013	$ 67,382.23	Oct. 01, 2021	On Going	2.07%	0.00%	2.07%
62	R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Malibo, Unipessoal LDA	MOP - CD- NCB-R- 21033	$ 152,622.90	Oct. 01, 2021	On Going	10.49%	18.49%	28.98%
63	R4D Rural Road Spot Improvement Barkau (VaVIQUENIA) - Maubaralisa Chainage 0+000-4+200, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Nhau, Unipessoal LDA	MOP - CD- NCB-R- 21027	$ 173,484.62	Oct. 01, 2021	On Going	41.64%	3.97%	45.61%
64	R4D Rural Road Spot Improvement Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Murak, Unipessoal Lda	MOP - CD- NCB-R- 21032	$ 153,049.65	Oct. 01, 2021	On Going	30.13%	5.08%	35.21%
65	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa, Chainage 8+400-12+500)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Meta Loe Crae Bau Unip,Lda	MPW-W-210160	$ 198,698.25	Oct. 01, 2021	On Going	11.66%	0.00%	11.66%
66	R4D Rural Road Spot Improvement Samarapo -Gisu Chainage 0+000-2+000	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Nazico Unip Lda	MPW-W-210152	$ 114,789.50	Oct. 01, 2022	On Going	11.39%	0.00%	11.39%
67	R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubaralisa Chainage 4+200-8+400)	MINISTERIO DAS OBRAS PUBLICAS	LM -CD	ESTRADAS	MAUBARA	LIQUICA	Luliana Unip,Lda	MPW-W-210161	$ 213,930.25	Oct. 01, 2021	On Going	14.88%	1.65%	16.53%
68	Konstrusaun ka Reabilitasaun ba EBF Gariana	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 117,902.04	Oct. 15, 2021	On Going	1.98%	0.00%	1.98%
69	Konstrusaun ka Reabilitasaun ba EBF Tapo Manuhulu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 100,033.33	Oct. 15, 2021	On Going	0.00%	0.00%	0.00%
70	Konstrusaun ka Reabilitasaun ba ESG-Paralelo Maubara/Batuvou	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MAUBARA	LIQUICA	Grupu Komunitariu	-	$ 141,660.22	Oct. 15, 2021	On Going	8.72%	2.06%	10.78%

INSPEKSAUN HUSI,

(Eng. Marcos Ximenes de Araujo)
Engineru ba Projetu Infrastrutura Transporte
e Irigasaun ADN,I.P

(Eng. Ludovina Maria Helena Guterres)
Engineru ba Projetu Infrastrutura Transporte
e Irigasaun ADN,I.P

(Eng. Juninho António Abrantes da Cruz)
Engineru ba Edificio Publiku Agua e
Sanamento ADN,I.P

(Eng. Camilo de Jesus)
Engineru ba Projetu Mekanikal
e Elektrikal ADN,I.P

VERIFIKA HUSI,

(Eng. Remigio da C.S.dos Santos)
Engineru Senior ba Projetu Infrastutura Transporte e
Irigasaun ADN,I.P

(Arq. Francisco Xavier D D. Jeronimo)
Engineru Senior ba Projetu Edificio Publiko
no Be'e Sanleamento ADN,I.P

(Eng. Deolindo de Fatima Marques)
Chefe Seksaun Mekanikal
e Elektrikal & ITC ADN,I.P

SERTIFIKA HUSI,

(Eng. Emerenciana da Costa
M.Freitas)
Coordenadora da Unidade de
Controlo e Validasaun
de Qualidade, ADN,I.P

ANEXO C1 (BZT16)

Naran Projeto :R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000
Contractor : Hatumeta Oan Unip.Lda
No. kontratu :MOP - CD-NCB-R -21030

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Libaloa -Bucumera

Koordinat :


Start Point :	Long :	125.3931986	Latetude	: - 8.63674152
End Point :	Long :	125.3833257	Latetude	: - 8.63314678

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Plum Concrete*

Sta, 0+600-0+750




T	w	*Distacia*	*Volume*
0.12	4.00	150.00	72.00
Total			72.00 m³

Companhia halo hela Servisu Plum Concrete iha Sta, Sta, 0+600-0+750




Sketch Item servisu : *Plum Concrete*

Sta, 1+800-1+860



T	w	*Distacia*	*Volume*
0.12	4.00	60.00	28.80
Total			28.80 m³

Companhia halo hela Servisu Plum Concrete iha Sta, Sta, 0+600-0+750

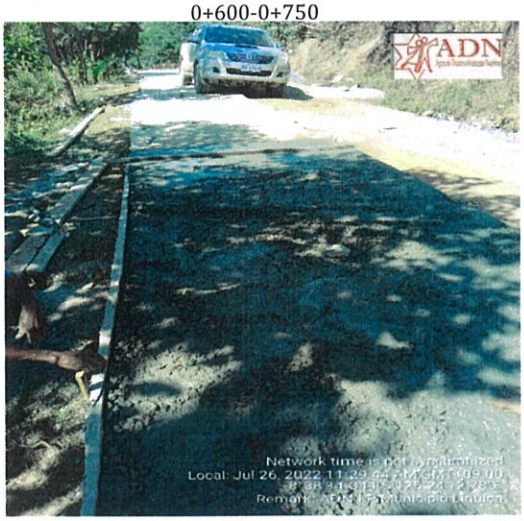

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.



Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (BZT16)

INSTRUSAUN / REKOMENDASAUN **KADA PROJETO**

Naran projeto : R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000

Naran Kompanha : Hatumeta Oan Unipessoal.Lda

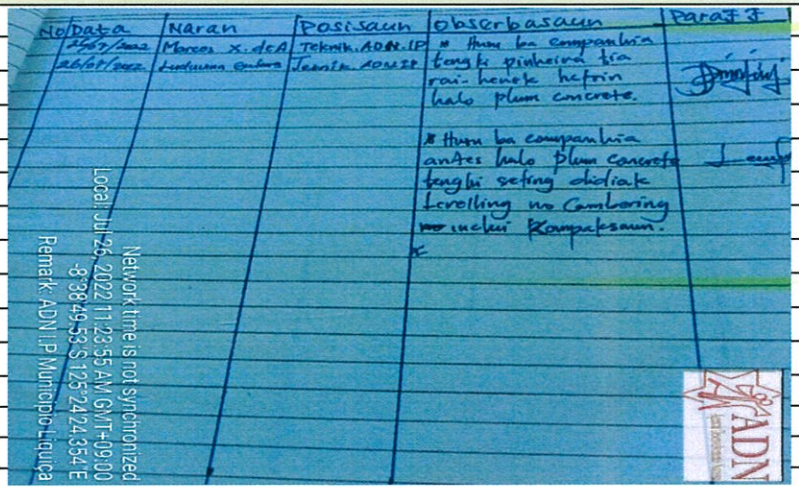No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Julho/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
II	26/Julho/2022	Liquica	Luduvina Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

ANEXO C2 (BZT16)

Naran Projeto :R4D Rural Road Spot Improvemrnt Fahilebo - Bucumera Chainage 0+000-3+000

Contractor : Hatumeta Oan Unip.Lda

No. kontratu :MOP - CD-NCB-R -21030

SUMMARY													
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,000.00					$ 1,400.00	0.93%	$ -	0.00%	$ 1,400.00	0.93%
R-02	Drainage	$ 97.72										
R-03	Earth work	$ 4,936.60					$ 1,009.34	0.67%	$ -	0.00%	$ 1,009.34	0.67%
R-05	Sub-base, base and pavement	$ 793.80										
R-08	Structures	$ 97,039.43					$ 15,777.52	10.54%	$ 13,019.33	8.70%	$ 28,796.85	19.23%
R-11	Routine maintenance	$ 7,192.50					$ 5,544.00	3.70%	$ -	0.00%	$ 5,544.00	3.70%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 1,380.00					$ 690.00	0.46%		0.00%	$ 690.00	0.46%
G-02	Project team	$ 12,150.00					$ 5,700.00	3.81%	$ 2,300.00	1.54%	$ 8,000.00	5.34%
G-03	Safety and protection	$ 4,103.00					$ 4,103.00	2.74%	$ -	0.00%	$ 4,103.00	2.74%
G-05	Meetings	$ 100.00					$ 100.00	0.07%	$ -	0.00%	$ 100.00	0.07%
G-06	Ceremonial costs	$ 200.00					$ 100.00	0.07%	$ -	0.00%	$ 100.00	0.07%
G-07	Mineral fees	$ 5,091.88										
A	**Construction cost**	**$ 112,310.04**					**$ 23,730.86**	**15.85%**	**$ 13,019.33**	**8.70%**	**$ 36,750.19**	**24.54%**
B	**Contractor Fee (A x 10%)**	**$ 11,231.00**					**$ 2,373.09**	**1.58%**	**$ 1,301.93**	**0.87%**	**$ 3,675.02**	**2.45%**
C	**General items**	**$ 23,024.88**					**$ 10,693.00**	**7.14%**	**$ 2,300.00**	**1.54%**	**$ 12,993.00**	**8.68%**
D	**Construction tax (A+B+C x 2%)**	**$ 2,931.32**					**$ 735.94**	**0.49%**	**$ 332.43**	**0.22%**	**$ 1,068.36**	**0.71%**
E	**Total**	**$ 149,732.87**					**$ 37,532.89**	**25.07%**	**$ 16,953.69**	**11.32%**	**$ 54,486.57**	**36.39%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (BZT20)

Naran Projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Contractor : TM.Cailebo Unip.Lda

No. kontratu : MPW-W-210158

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Fahilebo -Bucumera

Koordinat :

Start Point : Long : 125.3958511 Latetude : - 8.634983018


End Point : Long : 125.3828331 Latetude : - 8.640302834

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Plum Concrete*

Sta, 3+200-3+300




T	w	*Distacia*	*Volume*
0.12	2.00	100.00	24.00
Total			24.00 m³




Sketch Item servisu : *Plum Concrete*

Sta,3+900-4+000



T	w	*Distacia*	*Volume*
0.12	2.00	100.00	24.00
Total			24.00 m³

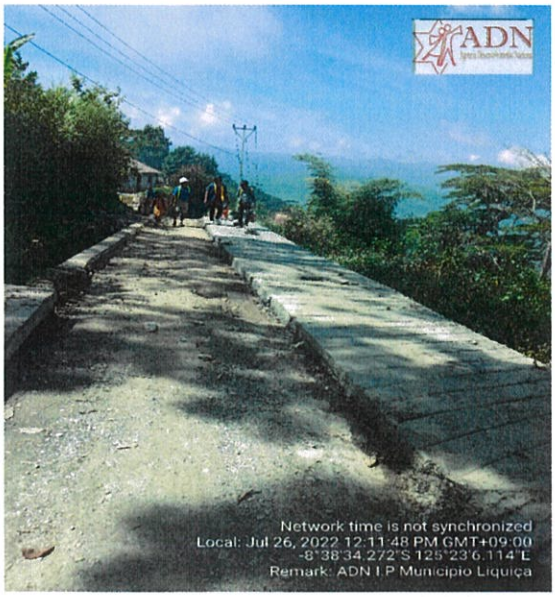

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público


ANEXO D (BZT20)

INSTRUSAUN / REKOMENDASAUN **KADA PROJETO**

Naran projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Naran Kompanha : TM Caileba Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Julho/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	M	
					2	Co	
					3		
					4		
					5		
II	26/Julho/2022	Liquica	Luduvina Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

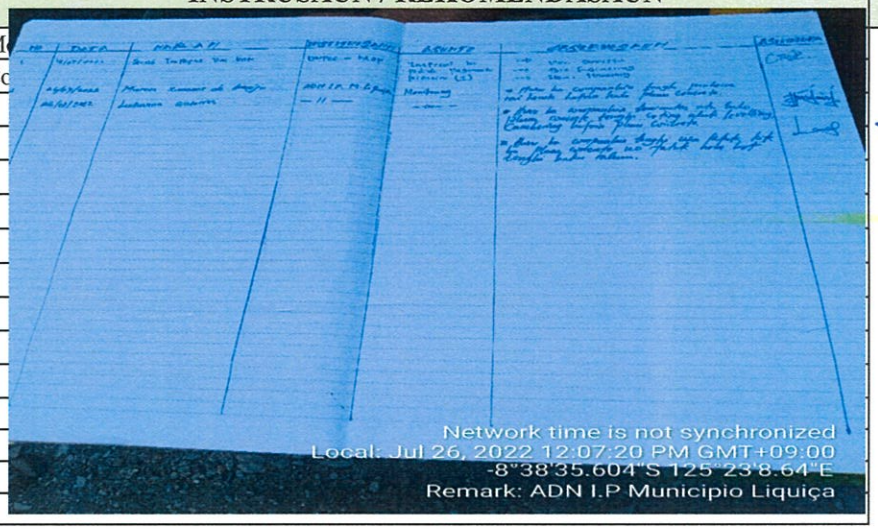

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (BZT20)

Naran Projeto : R4D Rural Road Spot Improvement Fahilebo - Bucumera Chainage 3+000+6+500) Liquica Municipality

Contractor : TM.Cailebo Unip.Lda

No. kontratu :MPW-W-210158

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,500.00					$ 1,900.00	1.20%	$ -	0.00%	$ 1,900.00	1.20%
R-02	Drainage	$ 164.55										
R-03	Earth work	$ 6,714.14					$ 1,436.50	0.91%	$ -	0.00%	$ 1,436.50	0.91%
R-05	Sub-base, base and pavement	$ 2,216.25										
R-08	Structures	$ 102,616.19					$ 19,304.41	12.18%	$ 8,173.44	5.16%	$ 27,477.85	17.34%
R-11	Routine maintenance	$ 6,427.50					$ 5,631.50	3.55%	$ -	0.00%	$ 5,631.50	3.55%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 1,440.00					$ 600.00	0.38%	$ 240.00	0.15%	$ 840.00	0.53%
G-02	Project team	$ 11,700.00					$ 5,500.00	3.47%	$ 1,950.00	1.23%	$ 7,450.00	4.70%
G-03	Safety and protection	$ 3,735.00					$ 3,735.00	2.36%	$ -	0.00%	$ 3,735.00	2.36%
G-05	Meetings	$ 100.00					$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-06	Ceremonial costs	$ 200.00					$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-07	Mineral fees	$ 4,974.69										
A	**Construction cost**	**$ 120,888.63**					**$ 28,272.41**	**17.84%**	**$ 8,173.44**	**5.16%**	**$ 36,445.85**	**23.00%**
B	**Contractor Fee (A x 10%)**	**$ 12,088.86**					**$ 2,827.24**	**1.78%**	**$ 817.34**	**0.52%**	**$ 3,644.59**	**2.30%**
C	**General items**	**$ 22,149.69**					**$ 10,035.00**	**6.33%**	**$ 2,190.00**	**1.38%**	**$ 12,225.00**	**7.71%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,102.54**					**$ 822.69**	**0.52%**	**$ 223.62**	**0.14%**	**$ 1,046.31**	**0.66%**
E	**Total**	**$ 158,465.33**					**$ 41,957.34**	**26.48%**	**$ 11,404.40**	**7.20%**	**$ 53,361.74**	**33.67%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (BZT18)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality
Contractor : Hatuleo Unip.Lda
No. kontratu : MPW-W-210144

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Libaloa-Fahilebo

Koordinat :


Start Point : Long : 125.43836103 Latetude : - 8.64943384
End Point : Long : 125.4135714 Latetude : - 8.63017393788538

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
1 Eng. Luduvina Guterres

Sketch & Foto Desenho


Sketch Item servisu : Line Drain

STA, 3+350-3+450

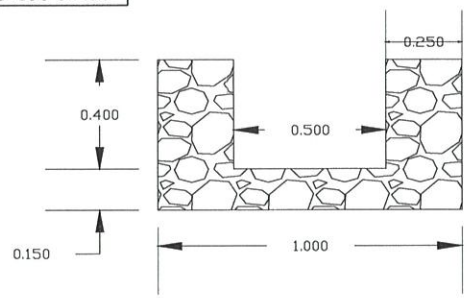


T	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m³

Observasaun iha tereno no Foto Aktual

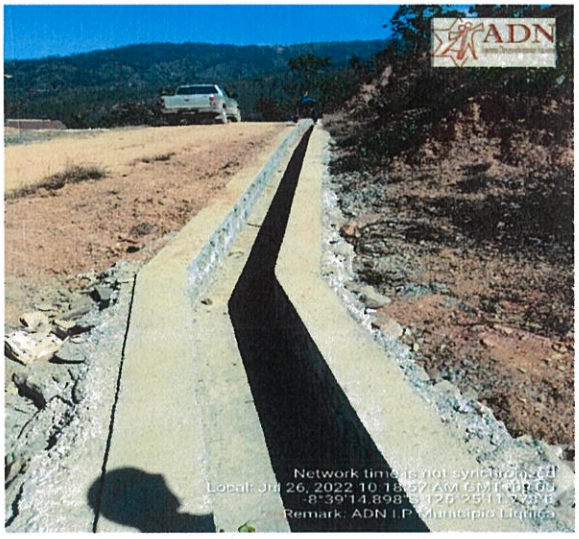

Sketch Item servisu : *Excavation*

STA, 4+450-4+550

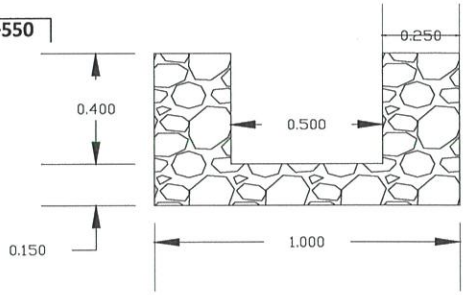

T	w	*Distacia*	*Volume*
0.55	0.25	100.00	13.75
	1.00		
Total			13.75 m³

Fotografia foti iha terreno wainhira trabalhador sira halo hela Drainagem



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.



Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (BZT18)

INSTRUSAUN / REKOMENDASAUN **KADA PROJETO**

Naran projeto : R4D Rural Road Spot Improvemrnt Libaloa - Fahilebo Chainage 0+000-7+000, liquica Municipality

Naran Kompanha : Hatuleo Unip,Lda

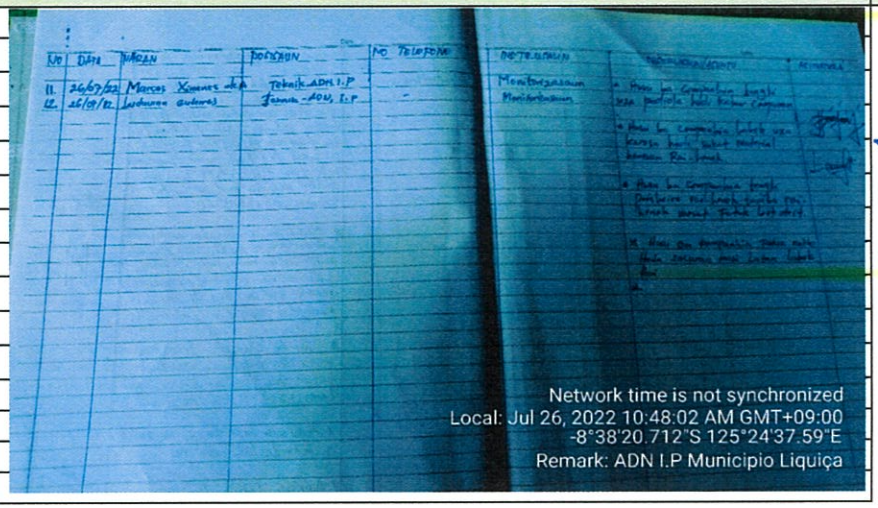No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Julho/2022	Liquica	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
II	26/Julho/2022	Liquica	Luduvina Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

 # ANEXO C2 (BZT18)

Naran Projeto : R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality
Companhia : Hatuleo Unip.Lda
No. kontratu :MPW-W-210144

SUMMARY

Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP					RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	%	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,250.00		$ 650.00	0.74%	$ 650.00	0.74%	$ 650.00	0.74%	$ -	0.00%	$ 650.00	0.74%
R-02	Drainage	$ 121.86						$ -				$ -	0.00%
R-03	Earth work	$ 3,188.68		$ 751.72	0.85%	$ 751.72	0.85%	$ 751.72	0.85%	$ 574.43	0.65%	$ 1,326.15	1.50%
R-05	Sub-base, base and pavement	$ 6,285.96		$ 1,468.93	1.66%	$ 1,468.93	1.66%	$ 1,468.93	1.66%	$ -	0.00%	$ 1,468.93	1.66%
R-08	Structures	$ 26,959.42		$ 10,618.77	12.01%	$ 10,618.77	12.01%	$ 12,973.92	14.67%	$ 9,420.60	10.65%	$ 22,394.52	25.33%
R-11	Routine maintenance	$ 12,699.00		$ 6,223.00	7.04%	$ 6,223.00	7.04%	$ 4,858.00	5.49%	$ -	0.00%	$ 4,858.00	5.49%
R-15	Provisional sum	$ 250.00						$ -				$ -	0.00%
	General items												
G-01	Security	$ 1,200.00		$ 400.00	0.45%	$ 400.00	0.45%	$ 400.00	0.45%			$ 400.00	0.45%
G-02	Project team	$ 14,700.00		$ 6,600.00	7.46%	$ 6,600.00	7.46%	$ 6,600.00	7.46%			$ 6,600.00	7.46%
G-03	Safety and protection	$ 5,886.00		$ 5,726.00	6.48%	$ 5,726.00	6.48%	$ 5,726.00	6.48%	$ -	0.00%	$ 5,726.00	6.48%
G-05	Meetings	$ 100.00		$ 100.00	0.11%	$ 100.00	0.11%	$ 100.00	0.11%	$ -	0.00%	$ 100.00	0.11%
G-06	Ceremonial costs	$ 175.00		$ 100.00	0.11%	$ 100.00	0.11%	$ 100.00	0.11%	$ -	0.00%	$ 100.00	0.11%
G-07	Mineral fees	$ 8,800.55						$ -				$ -	0.00%
								$ -				$ -	0.00%
A	**Construction cost**	**$ 50,754.92**		**$ 19,712.42**	**22.29%**	**$ 19,712.42**	**22.29%**	**$ 20,702.57**	**23.41%**	**$ 9,995.03**	**11.30%**	**$ 30,697.60**	**34.72%**
B	**Contractor Fee (A x 10%)**	**$ 5,075.49**		**$ 1,971.24**	**2.23%**	**$ 1,971.24**	**2.23%**	**$ 2,070.26**	**2.34%**	**$ 999.50**	**1.13%**	**$ 3,069.76**	**3.47%**
C	**General items**	**$ 30,861.55**		**$ 12,926.00**	**14.62%**	**$ 12,926.00**	**14.62%**	**$ 12,926.00**	**14.62%**	**$ -**	**0.00%**	**$ 12,926.00**	**14.62%**
D	**Construction tax (A+B+C x 2%)**	**$ 1,733.84**		**$ 692.19**	**0.78%**	**$ 692.19**	**0.78%**	**$ 713.98**	**0.81%**	**$ 219.89**	**0.25%**	**$ 933.87**	**1.06%**
E	**Total**	**$ 88,425.80**		**$ 35,301.85**	***39.92%***	**$ 35,301.85**	***39.92%***	**$ 36,412.80**	**41.18%**	**$ 11,214.42**	***12.68%***	**$ 47,627.23**	***53.86%***

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (LV17)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality

Contractor : Vicaroman Unip.Lda

No. kontratu : MOP - CD NCB - R - 21034

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3416468 Latetude : - 8.65444508

End Point : Long : 125.3469018 Latetude : - 8.680286396


Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Stone Masonry*

Sta, 4+200- 4+250

Sta,4+150-4+180




t	Area	*Distacia*	*Volume*
1.00	0.38	50.00	18.75
	0.35		17.50
Total			36.25 m³




Sketch Item servisu : *Stone Masonry*

Sta, 4+300 - 4+345

Sta,4+150-4+180



t	Area	*Distacia*	*Volume*
1.00	0.38	45.00	16.88
	0.35		15.75
Total			32.63 m³

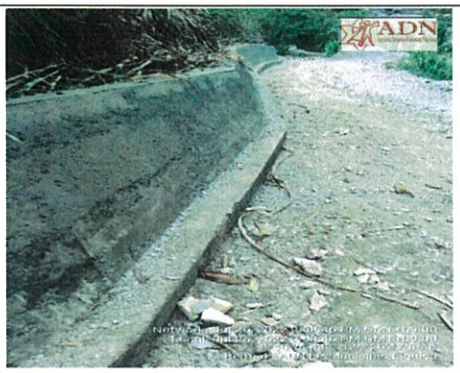

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL
ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 0+000 - 5+000, Liquica Municipality
Contractor : Vicaroman Unip.Lda
No. kontratu : MOP - CD NCB - R - 21034

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :

Start Point : Long : 125.3416 Latetude : - 8.65444508


End Point : Long : 125.3469 Latetude : - 8.680286396

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres


Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Stone Masonry*

Sta.4+190-4+270



Area	*Distacia*	*Volume*
0.35	80.00	28.00
Total		28.00 m³

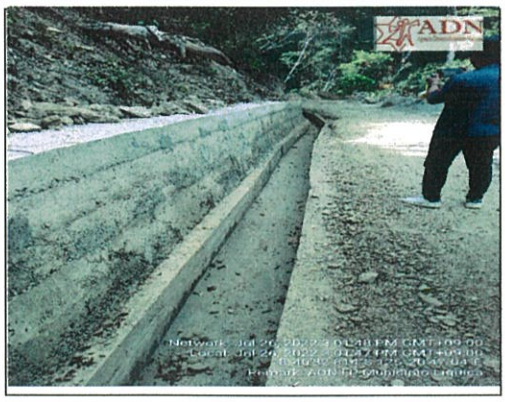

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV17)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)

Kompanha : Vicaroman Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/07/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Monitorizasaun ba Terreno laiha ema servisu	
					2	Kompanhia La lori Buku Tamu	
					3		
					4		
					5		
II	26/07/2022	Lquica/Liquica Villa	Luduvina Maria H. Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV17)

Name of Roads : R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)
Contract No : MPW-W-210155
Contractor : Vicaroman Unip.Lda

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,750.00					$ 600.00	0.36%	$ -	0.00%	$ 600.00	0.36%
R-02	Drainage	$ 37.00										
R-03	Earth work	$ 13,233.46					$ 260.40	0.16%	$ -	0.00%	$ 260.40	0.16%
R-05	Sub-base, base and pavement	$ 8,729.99										
R-08	Structures	$ 82,879.01					$ 14,469.75	8.75%	$ 3,711.75	2.24%	$ 18,181.50	10.99%
R-11	Routine maintenance	$ 8,882.00					$ 450.00	0.27%	$ 1,900.00	1.15%	$ 2,350.00	1.42%
R-15	Provisional sum	$ 250.00										
	General Items											
G-01	Security	$ 1,380.00					$ 575.00	0.35%	$ 230.00	0.14%	$ 805.00	0.49%
G-02	Project team	$ 17,520.00					$ 5,340.00	3.23%	$ 2,670.00	1.61%	$ 8,010.00	4.84%
G-03	Safety and protection	$ 6,501.00					$ 6,501.00	3.93%	$ -	0.00%	$ 6,501.00	3.93%
G-05	Meetings	$ 100.00					$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-06	Ceremonial costs	$ 200.00					$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-07	Mineral fees	$ 8,290.40										
A	**Construction cost**	**$ 115,761.46**					**$ 15,780.15**	**9.54%**	**$ 5,611.75**	**3.39%**	**$ 21,391.90**	**12.94%**
B	**Contractor Fee (A x 10%)**	**$ 11,576.15**					**$ 1,578.02**	**0.95%**	**$ 561.18**	**0.34%**	**$ 2,139.19**	**1.29%**
C	**General items**	**$ 33,991.40**					**$ 12,616.00**	**7.63%**	**$ 2,900.00**	**1.75%**	**$ 15,516.00**	**9.38%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,226.58**					**$ 599.48**	**0.36%**	**$ 181.46**	**0.11%**	**$ 780.94**	**0.47%**
E	**Total**	**$ 165,363.43**					**$ 30,573.65**	**18.49%**	**$ 9,254.38**	**5.60%**	**$ 39,828.03**	**24.09%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Eng. Luduvina M.H.Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P

Verifika Husi :

Eng.Remegio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :


Start Point :	Long :	125.3469018	Latetude	: - 8.680286396
End Point :	Long :	125.3739113	Latetude	: - 8.684259297

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Luduvina M.H.Guterres

Sketch & Foto Desenho


Sketch Item servisu : *Stone Masonry*

Sta, 1+500-1+570




Area	*Distacia*	*Volume*
0.35	70.00	24.50
Total		24.50 m³

Observasaun iha tereno no Foto Aktual

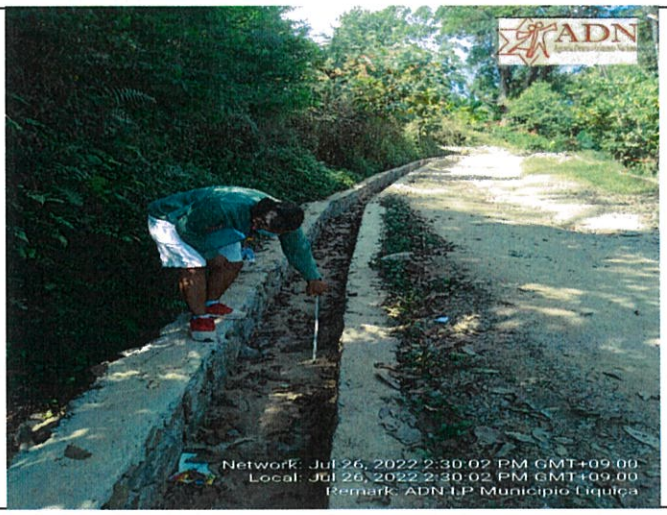


Sketch Item servisu : *Stone Masonry*

Sta, 1+600- 1+700



Area	*Distacia*	*Volume*
0.35	100.00	35.00
Total		35.00 m³

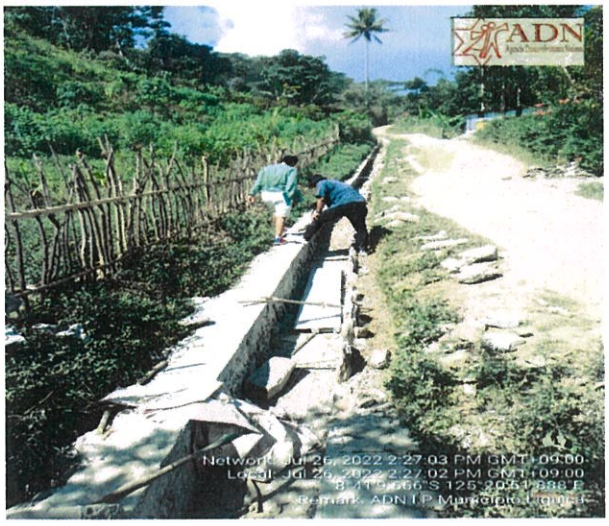

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality

Contractor : Caiulu Unip.Lda

No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :


Start Point :	Long :	125.3469018	Latetude	: - 8.680286396
End Point :	Long :	125.3739113	Latetude	: - 8.684259297

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : *Gabion*


Sta, 1+565 - 1+565

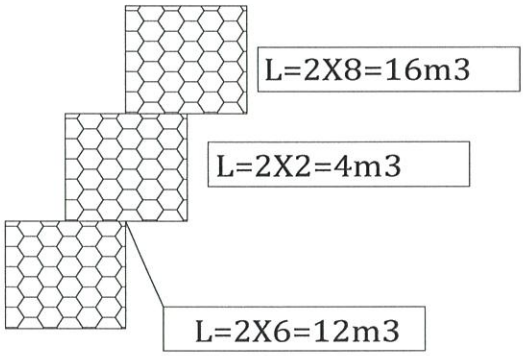




Sketch Item servisu :Gabion

Sta, 1+565 - 1+565

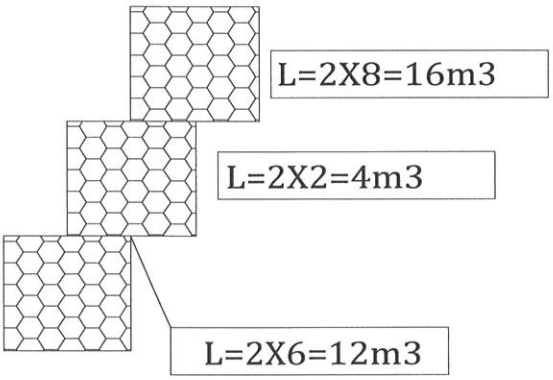

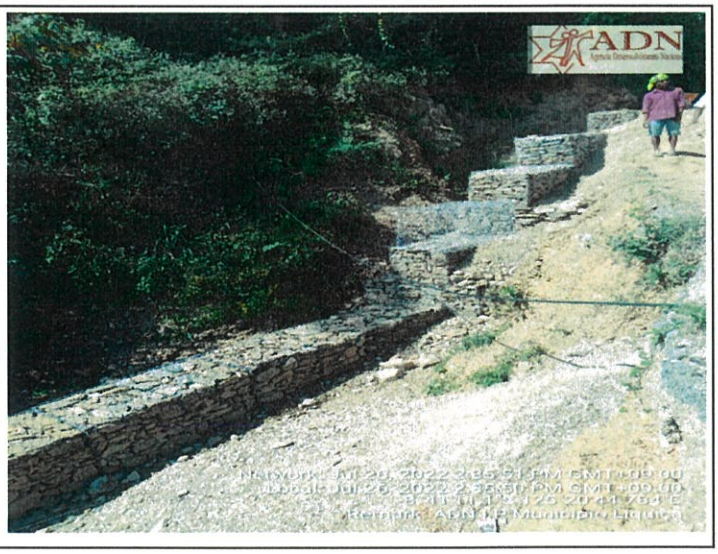

ANEXO C1 (LV16)

Naran Projeto : R4D Rural Road Spot Improvemrnt Aibenu - Asumanu - Leurema Chainage 5+000 - 10 +000, Liquica Municipality
Contractor : Caiulu Unip.Lda
No. kontratu : MOP - CD - NCB -R - 21035

Data Inspeksaun : 20/Junho/2022

Fatin Inspeksaun : Suco Asu-Manu

Koordinat :


Start Point :	Long :	125.3469018	Latetude	: - 8.680286396
End Point :	Long :	125.3739113	Latetude	: - 8.684259297

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : *Excavation*

Sta, 2+210 - 2+290




T	*W*	*Distacia*	*Volume*
0.12	4	90.00	43.20
Total			43.20 m³

Observasaun iha tereno no Foto Aktual




Sketch Item servisu : *Excavation*

Sta, 3+800 - 3+920



T	*W*	*Distacia*	*Volume*
0.12	4	120.00	57.60
Total			57.60 m³

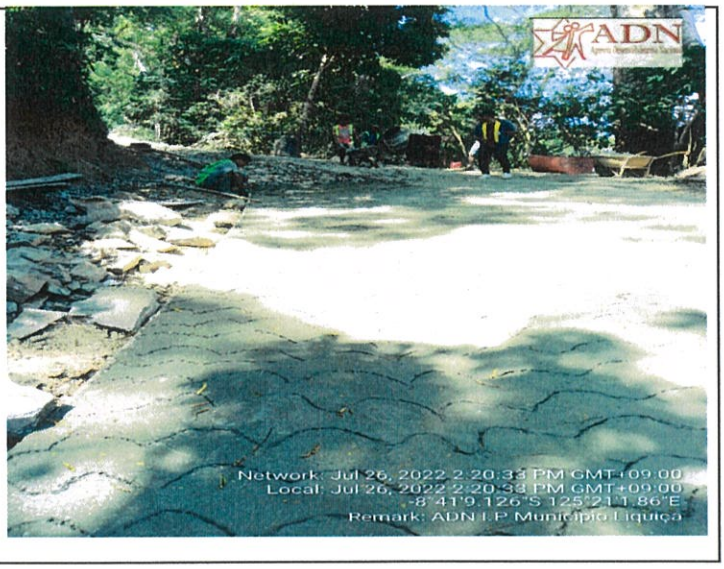

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV16)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)

Kompanha : Caiulu Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Junho/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1		
					2	Companhia la Prepara Buku tamu iha Tereno	
					3		
					4		
II	26/Julho/2022	Lquica/Liquica Villa	Luduvina M.H.Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV16)

Name of Roads : R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)
Contract No : MPW-W-210154
Contractor : Caiulu Unipessoal.Lda

SUMMARY											
Itime	**DESCRIPTION**	**CONTRACT ORIGINAL**	**RESULTADO INSPEKSAUN MOP**			**RESULTADO INSPEKSAUN ADN.IP**					
			PREVIOUS BILLING	**THIS BILLING**	**TO DATE**	**PREVIOUS BILDING**	**%**	**THIS BILLING**	**%**	**TO DATE**	**%**
R-01	General works	$ 1,700.00				$ 850.00	0.52%	$ -	0.00%	$ 850.00	0.52%
R-02	Drainage	$ 174.10									
R-03	Earth work	$ 11,371.21				$ 1,385.14	0.85%	$ -	0.00%	$ 1,385.14	0.85%
R-05	Sub-base, base and pavement	$ 8,458.48									
R-08	Structures	$ 82,977.14				$ 22,649.48	13.96%	$ 13,516.40	8.33%	$ 36,165.87	22.29%
R-11	Routine maintenance	$ 11,409.50				$ 560.00	0.35%	$ -	0.00%	$ 560.00	0.35%
R-15	Provisional sum	$ 250.00									
	General items										
G-01	Security	$ 1,800.00				$ 750.00	0.46%	$ 300.00	0.18%	$ 1,050.00	0.65%
G-02	Project team	$ 15,900.00				$ 6,600.00	4.07%	$ 3,300.00	2.03%	$ 9,900.00	6.10%
G-03	Safety and protection	$ 4,618.00				$ 4,618.00	2.85%	$ -	0.00%	$ 4,618.00	2.85%
G-05	Meetings	$ 100.00				$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-06	Ceremonial costs	$ 200.00				$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-07	Mineral fees	$ 8,442.11									
A	**Construction cost**	**$ 116,340.43**				**$ 25,444.61**	**15.69%**	**$ 13,516.40**	**8.33%**	**$ 38,961.01**	**24.02%**
B	**Contractor Fee (A x 10%)**	**$ 11,634.04**				**$ 2,544.46**	**1.57%**	**$ 1,351.64**	**0.83%**	**$ 3,896.10**	**2.40%**
C	**General items**	**$ 31,060.11**				**$ 12,168.00**	**7.50%**	**$ 3,600.00**	**2.22%**	**$ 15,768.00**	**9.72%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,180.69**				**$ 803.14**	**0.50%**	**$ 369.36**	**0.23%**	**$ 1,172.50**	**0.72%**
E	**Total**	**$ 162,215.27**				**$ 40,960.22**	**25.25%**	**$ 18,837.40**	**11.61%**	**$ 59,797.61**	**36.86%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria H.Guterres
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes, e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

#ANEXO C2 (LV18)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400
Contractor : Claridade Unip.Lda
No. kontratu : MPW-W-210163

Data Inspeksaun : 13/Julho/2022

Fatin Inspeksaun : Suco Berlakulidu - Laberlaka

Koordinat :


Start Point : Long : 125.29520251 Latetude : - 8.63329600
End Point : Long : 125.30192345 Latetude : - 8.641753681

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : **Plam Concrete**

STA,3+100-3+160




t	L	*Distacia*	*Volume*
0.12	2.00	60.00	14.40
Total			14.40 m³




Sketch Item servisu : ***Plam Concrete***


STA, 3+700-3+770




t	w	*Distacia*	*Volume*
0.12	2.00	70.00	16.80
Total			16.80 m³

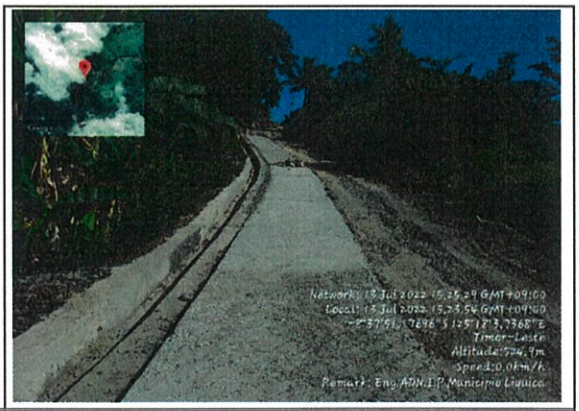

STA, 2+800-2+876



t	w	*Distacia*	*Volume*
0.40	0.25	76.00	15.20
0.15	1.00		11.40
Total			26.60 m³

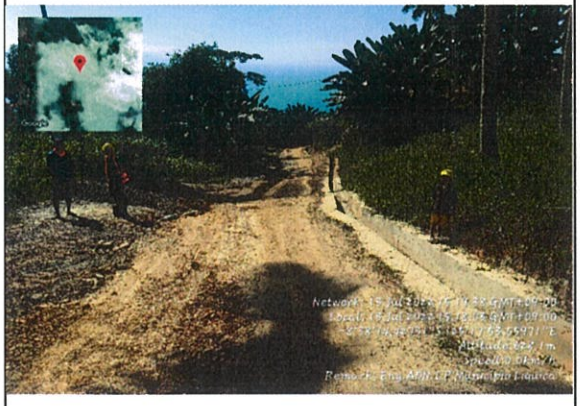

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (LV18)

INSTRUSAUN / REKOMENDASAUN KADA PROJETO

Naran projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400

Naran Kompanha : Claridade Unipessoal.Lda

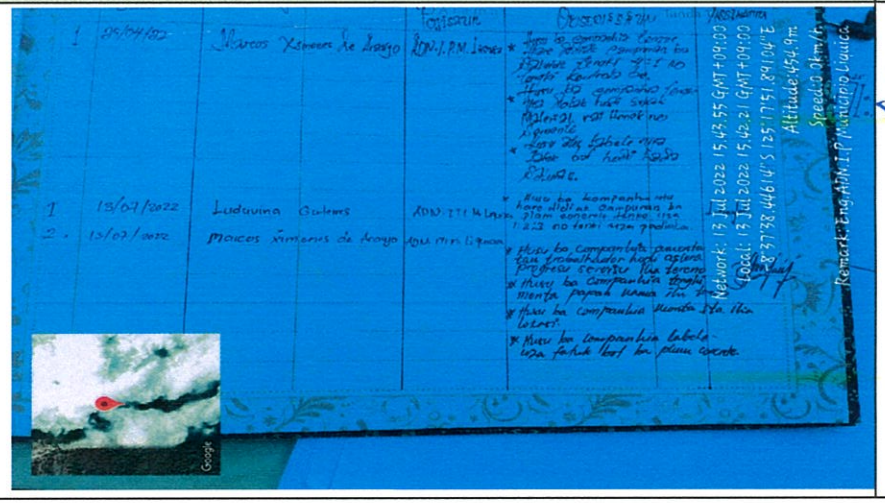No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	13/Julho/2022	Liquiça	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquiça	1 2 3 4 5		
II	13/Julho/2022	Liquiça	Luduvina M.H.Guterres	Teknik ADN.I.P M.Liquiça	1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO C2 (LV18)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu - Laberlaka Chaingane Chainage 2+500-5+400
Contractor : Claridade Unip.Lda
No. kontratu : MPW-W-210163

SUMMARY											
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP			RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,700.00				$ 1,600.00	0.96%	$ -	0.00%	$ 1,600.00	0.96%
R-02	Drainage	$ 319.00									
R-03	Earth work	$ 6,484.77				$ 1,827.40	1.09%	$ -	0.00%	$ 1,827.40	1.09%
R-05	Sub-base, base and pavement	$ 2,196.00									
R-08	Structures	$ 109,034.33				$ 9,718.09	5.82%	$ 5,176.55	3.10%	$ 14,894.64	8.92%
R-10	Dayworks	$ 140.00									
R-11	Routine maintenance	$ 5,440.50				$ 4,637.50	2.78%	$ -	0.00%	$ 4,637.50	2.78%
R-15	Provisional sum	$ 1,000.00									
GENERAL ITEM											
G-01	Security	$ 2,760.00				$ 920.00	0.55%	$ 460.00	0.28%	$ 1,380.00	0.83%
G-02	Project team	$ 12,180.00				$ 5,760.00	3.45%	$ 2,230.00	1.33%	$ 7,990.00	4.78%
G-03	Safety and protection	$ 2,513.00									
G-05	Meetings	$ 100.00				$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-06	Ceremonial costs	$ 200.00				$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-07	Mineral fees	$ 5,996.91									
A	**Construction cost**	**$ 127,314.60**				**$ 17,782.99**	**10.64%**	**$ 5,176.55**	**3.10%**	**$ 22,959.54**	**13.74%**
B	Contractor Fee (A x 10%)	$ 12,731.46				$ 1,778.30	1.06%	$ 517.65	0.31%	$ 2,295.95	1.37%
C	General items	$ 23,749.91				$ 6,880.00	4.12%	$ 2,690.00	1.61%	$ 9,570.00	5.73%
D	Construction tax (A+B+C x 2%)	$ 3,275.92				$ 528.83	0.32%	$ 167.68	0.10%	$ 696.51	0.42%
E	**Total**	**$ 167,071.89**				**$ 26,970.11**	**16.14%**	**$ 8,551.89**	**5.12%**	**$ 35,522.00**	**21.26%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineira ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura, Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade, ADN I.P.

ANEXO C1 (LV12)
Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)
Contractor : Goubara Unip.Lda
No. kontratu : MPW-W-210162

Data Inspeksaun : 13/Julho/2022

Fatin Inspeksaun : Suco Berlakuliado-Laberlaka

Koordinat :


Start Point : Long : 125.29724167 Latetude : - 8.60635641
End Point : Long : 125.2952025 Latetude : - 8.62329599714

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Luduvina M.H.Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry (Line Drain)

1+800- 1+900




t	L	*Distacia*	*Volume*
0.12	4.00	100.00	48.00
Total			48.00 m³

Fotografia terreno hatudo katak companhia halo hela Saluran




Sketch Item servisu : *Stone Masonry (Line Drain)*

2+300 - 2+400




t	L	*Distacia*	*Volume*
0.12	4.00	100.00	48.00
Total			48.00 m³

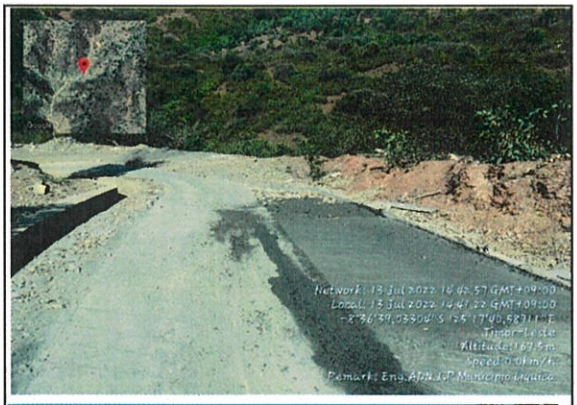


Sketch Item servisu : Line Drain

STA, 1+700-1+800

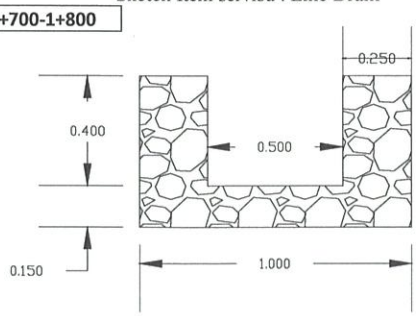

T	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m³

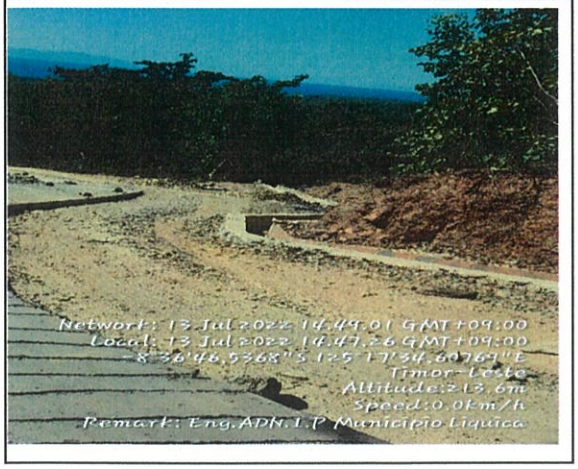

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV12)

INSTRUSAUN / REKOMENDASAUN

Naran projeto :R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-2+500, Liquica Municipality

Kompanha : Goubara Unip.Lda

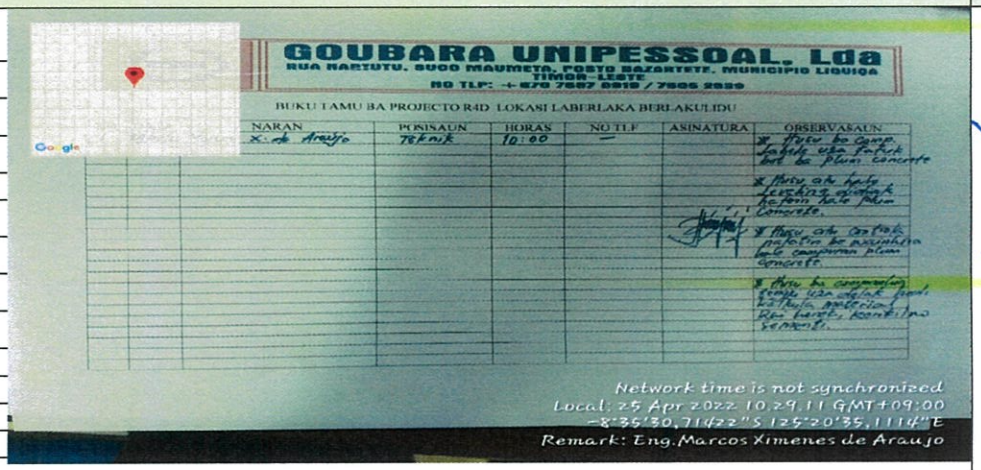No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	13/Julho/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II	13/Julho/2022	Lquica/Liquica Villa	Luduvina M.H.Guterres	Teknik ADN.I.P M.Liquica	1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV12)

Naran Projeto : R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)

Contractor : Goubara Unip.Lda

No. kontratu :MPW-W-210162

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,300.00					$ 1,200.00	0.91%	$ -	0.00%	$ 1,200.00	0.91%
R-02	Drainage	$ 171.01										
R-03	Earth work	$ 4,699.77					$ 1,110.25	0.85%	$ 225.50	0.17%	$ 1,335.75	1.02%
R-05	Sub-base, base and pavement	$ 2,653.56										
R-08	Structures	$ 81,840.38					$ 20,244.66	15.43%	$ 15,068.86	11.48%	$ 35,313.52	26.91%
R-10	Dayworks	$ 105.00										
R-11	Routine maintenance	$ 5,957.00					$ 343.00	0.26%	$ -	0.00%	$ 343.00	0.26%
R-15	Provisional sum	$ 775.00										
	General items											
G-01	Security	$ 690.00					$ 345.00	0.26%	$ -	0.00%	$ 345.00	0.26%
G-02	Project team	$ 11,700.00					$ 5,500.00	4.19%	$ -	0.00%	$ 5,500.00	4.19%
G-03	Safety and protection	$ 2,949.00										
G-05	Meetings	$ 100.00					$ 100.00	0.08%	$ -	0.00%	$ 100.00	0.08%
G-06	Ceremonial costs	$ 200.00					$ 100.00	0.08%	$ -	0.00%	$ 100.00	0.08%
G-07	Mineral fees	$ 4,655.79										
A	**Construction cost**	**$ 98,501.72**					**$ 22,897.91**	**17.45%**	**$ 15,294.36**	**11.66%**	**$ 38,192.27**	**29.11%**
B	**Contractor Fee (A x 10%)**	**$ 9,850.17**					**$ 2,289.79**	**1.75%**	**$ 1,529.44**	**1.17%**	**$ 3,819.23**	**2.91%**
C	**General items**	**$ 20,294.79**					**$ 6,045.00**	**4.61%**	**$ -**	**0.00%**	**$ 6,045.00**	**4.61%**
D	**Construction tax (A+B+C x 2%)**	**$ 2,572.93**					**$ 624.65**	**0.48%**	**$ 336.48**	**0.26%**	**$ 961.13**	**0.73%**
E	**Total**	**$ 131,219.62**					**$ 31,857.36**	***24.28%***	**$ 17,160.27**	***13.08%***	**$ 49,017.63**	***37.36%***

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (LV15)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)

No. kontratu : MPW-W-210150

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Loidahar

Koordinat :

Start Point : Long : 125°19'36.41779 Latetude : - 8°36'46.93352


End Point : Long : 125°19'36.41779 Latetude : - 8°36'46.93352

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina Maria H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : *Plum Concrete*

Sta, 7+550-7+650



t	L	*Distacia*	*Volume*
0.12	4.00	100.00	48.00
Total			48.00 m³


Observasaun iha tereno no Foto Aktual

Companhia halo Plum Concrete iha Suco Loidahar no Sta, 7+550-7+650



Sketch Item servisu : *Plum Concrete*

Sta,7+400-7+500




t	L	*Distacia*	*Volume*
0.12	4.00	100.00	48.00
Total			48.00 m³

Companhia halo Plum Concrete iha Suco Loidahar no Sta, 4+680 - 4+780




Sketch Item servisu : *Plum Concrete*

Sta,6+400-6+500



t	L	*Distacia*	*Volume*
0.12	4.00	100.00	48.00
Total			48.00 m³

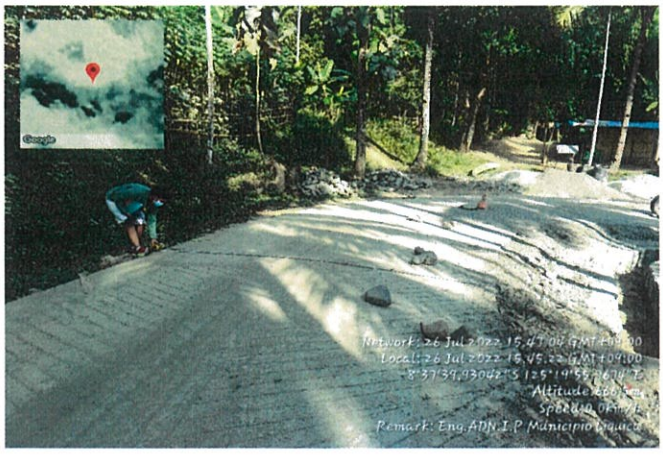

ANEXO C1 (LV15)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)

No. kontratu : MPW-W-210150

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Loidahar

Koordinat :


Start Point : Long : 125°19'36.41779 Latetude : - 8°36'46.93352
End Point : Long : 125°19'36.41779 Latetude : - 8°36'46.93352

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng. Luduvina M.H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : *Stone Masonry*

Sta,7+300-7+400



Area	*Distacia*	*Volume*
0.35	100.00	35.00
Total		35.00 m³


Observasaun iha tereno no Foto Aktual

Companhia halo Line Draen iha Suco Loidahar no Sta, 4+300 - 4+400



Sketch Item servisu : *Stone Masonry*

Sta, 8+300-8+400




Area	*Distacia*	*Volume*
0.35	100.00	35.00
Total		35.00 m³


Companhia halo Line Draen iha Suco Loidahar no Sta, 4+300 - 4+400



Sta, 6+200-6+300



Area	*Distacia*	*Volume*
0.35	100.00	35.00
Total		35.00 m³

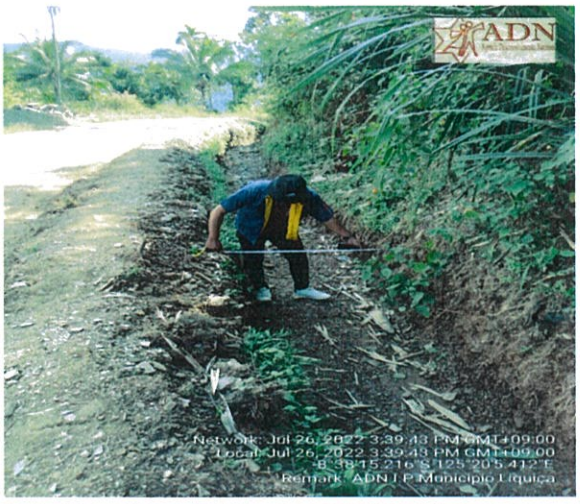

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV15)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)

Kompanha : Luqueli Oan Unip.Lda

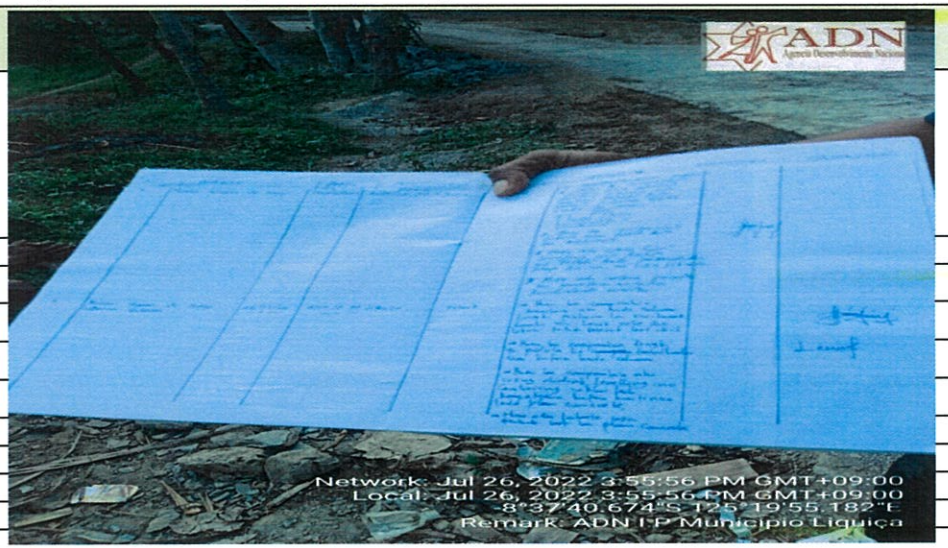No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No		Asinatura
I	26/Julho/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II	26/Julho/2022	Lquica/Liquica Villa	Luduvina M.H.Guterres	Teknik ADN.I.P M.Liquica	1 2 3 4 5		
III					1 2 3 4 5		

ANEXO C2 (LV15)

Name of Roads : R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)
Contract No : MPW-W-210150
Contractor : Luqueli Oan Unipessoal.Lda

SUMMARY

NO	DESCRIPTION	CONTRAC ORIGINAL	RESULTADO INSPEKSAUN MOP			RESULTADO INSPEKSAUN ADN.					
			PREVIOUS BILLING	THIS BILLING	TO DATE	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,300.00				$ 700.00	0.37%	$ -	0.00%	$ 700.00	0.37%
R-02	Drainage	$ 1,905.47									
R-03	Earth work	$ 19,160.19				$ 2,227.39	1.18%	$ 477.95	0.25%	$ 2,705.34	1.43%
R-05	Sub-base, base and pavement	$ 5,007.60									
R-08	Structures	$ 97,539.20				$ 22,848.67	12.12%	$ 25,290.96	13.41%	$ 48,139.63	25.53%
R-11	Routine maintenance	$ 18,278.00				$ 1,720.00	0.91%	$ -	0.00%	$ 1,720.00	0.91%
R-15	Provisional sum	$ 250.00									
	Sub Total	**$ 143,440.46**				**$ 27,496.06**	**14.58%**	**$ 25,768.91**	**13.66%**	**$ 53,264.97**	**28.24%**
	General items										
G-01	Security	$ 1,680.00				$ 1,120.00	0.59%	$ -	0.00%	$ 1,120.00	0.59%
G-02	Project team	$ 9,960.00				$ 3,010.00	1.60%	$ -	0.00%	$ 3,010.00	1.60%
G-03	Safety and protection	$ 6,094.50				$ 6,066.50		$ -	0.00%	$ 6,066.50	3.22%
G-05	Meetings	$ 100.00				$ 100.00		$ -	0.00%	$ 100.00	0.05%
G-06	Ceremonial costs	$ 175.00				$ 137.50	0.07%	$ -	0.00%	$ 137.50	0.07%
G-07	Mineral fees	$ 9,097.30									
	Sub Total	**$ 27,106.80**				**$ 10,434.00**	**2.26%**	**$ -**	**0.00%**	**$ 10,434.00**	**5.53%**
A	**CONSTRUCTION COST**	**$ 143,440.46**				**$ 27,496.06**	**14.58%**	**$ 25,768.91**	**13.66%**	**$ 53,264.97**	**28.24%**
B	**PROFIT 10% x A**	**$ 14,344.05**				**$ 2,749.61**	**1.46%**	**$ 2,576.89**	**1.37%**	**$ 5,326.50**	**2.82%**
C	**OVERHEAD**	**$ 27,106.80**				**$ 10,434.00**	**5.53%**	**$ -**	**0.00%**	**$ 10,434.00**	**5.53%**
D	**TAX 2% (A+B+C)**	**$ 3,697.83**				**$ 813.59**	**0.43%**	**$ 566.92**	**0.30%**	**$ 1,380.51**	**0.73%**
E	**GRAND TOTAL (A+B+C)**	***$ 188,589.13***				***$ 41,493.26***	**22.00%**	***$ 28,912.72***	**15.33%**	***$ 70,405.98***	**37.33%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Eng. Luduvina Maria Helena Guterres
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (MBR12)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemrnt Barkau (VaVIQUENIA) - Maubaralisa Chainage 0+000-4+200, Liquica Municipality
Contractor : Nheu Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21027

Data Inspeksaun : 18/Julho/2022

Fatin Inspeksaun : Suco Vaviquenia-Maubaralisa

Koordinat :


Start Point : Long : 125.21124422 Latetude : -8.61803763
End Point : Long : 125.2281181 Latetude : -8.632661686

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng.Luduvina Maria.H.Guterres


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry

STA, 3+920 - 4+020




t	w	Distacia	Volume
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3

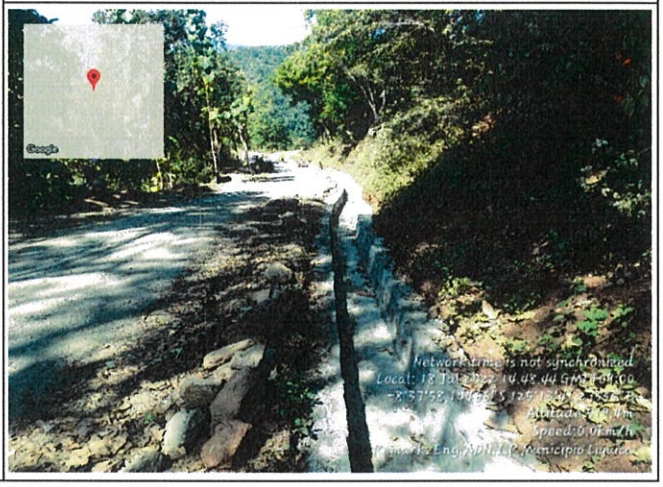


Sketch Item servisu : Stone Masonry

STA, 3+920 - 4+020




t	w	Distacia	Volume
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3

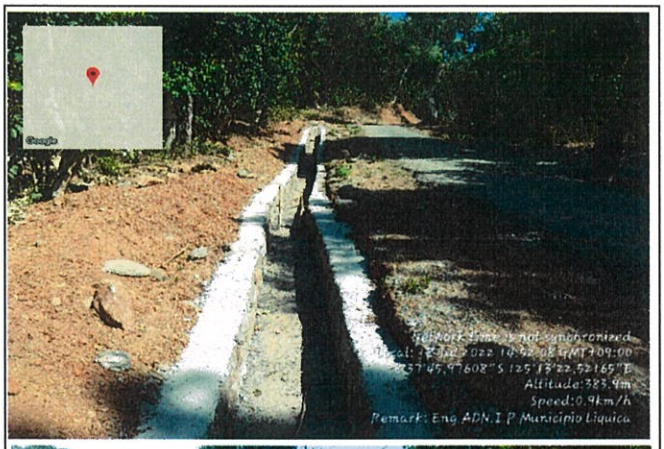


Sketch Item servisu : Stone Masonry

STA, 3+920 - 4+020



t	w	Distacia	Volume
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3

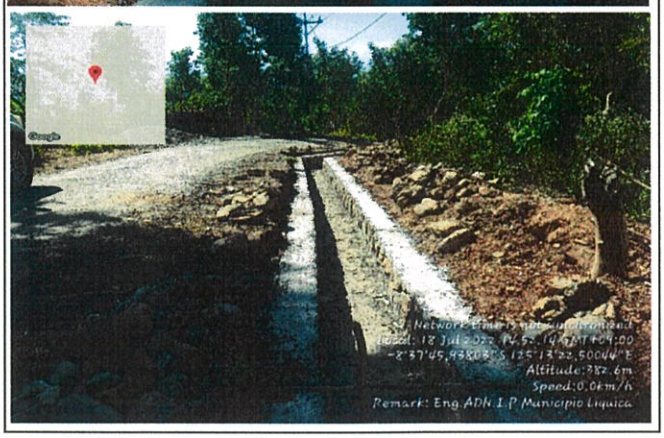

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (MBR12)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvemrnt Barkau (VaVIQUENIA) - Maubaralisa Chainage 0+000-4+200, Liquica Municipality

Kompanha : Nheu Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	18/Julho/2022	Lquica/Maubara	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Halo monitorizasaun iha tereno	
					2	La Priense buku tamu tamba teknik kompanhia haluhan la lori	
					3		
					4		
II	18/Julho/2022	Lquica/Maubara	Luduvina Maria.H.Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO C2 (MBR12)

Naran Projeto : R4D Rural Road Spot Improvemrnt Barkau (VaVIQUENIA) - Maubaralisa Chainage 0+000-4+200, Liquica Municipality
Naran Companhia : Nheu Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21027

SUMMARY											
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP			RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 3,458.00				$ 1,050.00	0.61%	$ -	0.00%	$ 1,050.00	0.61%
R-02	Drainage	$ 281.40									
R-03	Earth work	$ 12,812.63				$ 9,850.62	5.68%	$ -	0.00%	$ 9,850.62	5.68%
R-05	Sub-base, base and pavement	$ 546.98									
R-08	Structures	$ 103,036.65				$ 38,729.61	22.32%	$ 2,489.20	1.43%	$ 41,218.81	23.76%
R-10	Dayworks	$ 210.00									
R-11	Routine maintenance	$ 6,112.00				$ 1,722.00	0.99%	$ 862.00	0.50%	$ 2,584.00	1.49%
R-15	Provisional sum	$ 500.00									
	General items										
G-01	Security	$ 3,600.00				$ 1,500.00	0.86%	$ 600.00	0.35%	$ 2,100.00	1.21%
G-02	Project team	$ 11,580.00				$ 4,940.00	2.85%	$ 2,470.00	1.42%	$ 7,410.00	4.27%
G-03	Safety and protection	$ 7,441.55				$ 7,441.55	4.29%	$ -	0.00%	$ 7,441.55	4.29%
G-05	Meetings	$ 100.00				$ 100.00	0.06%	$ -	0.00%	$ 100.00	0.06%
G-06	Ceremonial costs	$ 350.00				$ 350.00	0.20%			$ 350.00	0.20%
G-07	Mineral fees	$ 7,357.99									
A	**Construction cost**	**$ 126,957.66**				**$ 51,352.23**	**29.60%**	**$ 3,351.20**	**1.93%**	**$ 54,703.43**	**31.53%**
B	**Contractor Fee (A x 10%)**	**$ 12,695.77**				**$ 5,135.22**	**2.96%**	**$ 335.12**	**0.19%**	**$ 5,470.34**	**3.15%**
C	**General items**	**$ 30,429.54**				**$ 14,331.55**	**8.26%**	**$ 3,070.00**	**1.77%**	**$ 17,401.55**	**10.03%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,401.66**				**$ 1,416.38**	**0.82%**	**$ 135.13**	**0.08%**	**$ 1,551.51**	**0.89%**
E	**Total**	**$ 173,484.62**				**$ 72,235.38**	**41.64%**	**$ 6,891.45**	**3.97%**	**$ 79,126.83**	**45.61%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Verifika Husi :

Eng.Remigio da C. S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura, Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade, ADN I.P.

 # ANEXO C1 (MBR16)
Back-up Data

Naran Projeto R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubaralisa Chainage 4+200-8+400)
Contractor : Luliana Unip,Lda
No. kontratu MPW-W-210160




Data Inspeksau 18/Julho/2022

Fatin Inspeksau Suco Vaviquenia - Maubaralisa

Koordinat :

Start Point :	Long :	125.22811811	Latetude : -8.6326617
End Point :	Long :	125.21757267	Latetude : -8.649459943

Naran Inspekto 1 Eng. Marcos Ximenes de Araujo
2 Eng.Luduvina Maria Helena Guterres

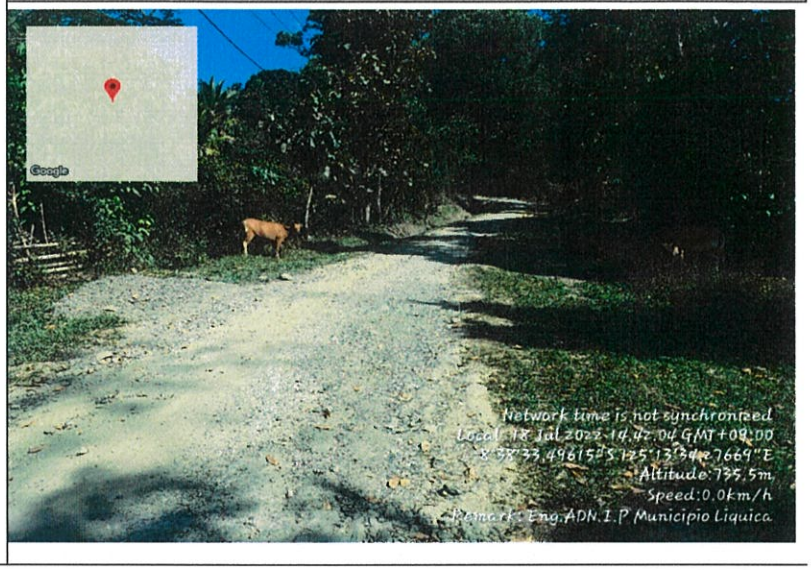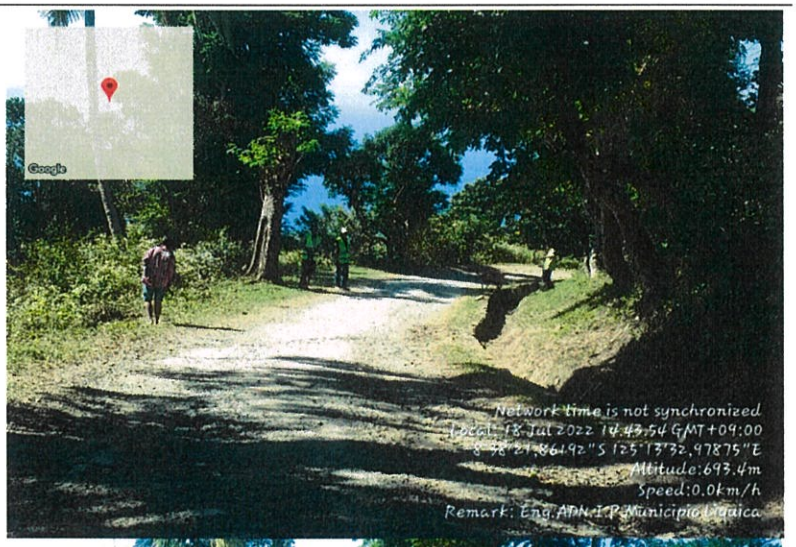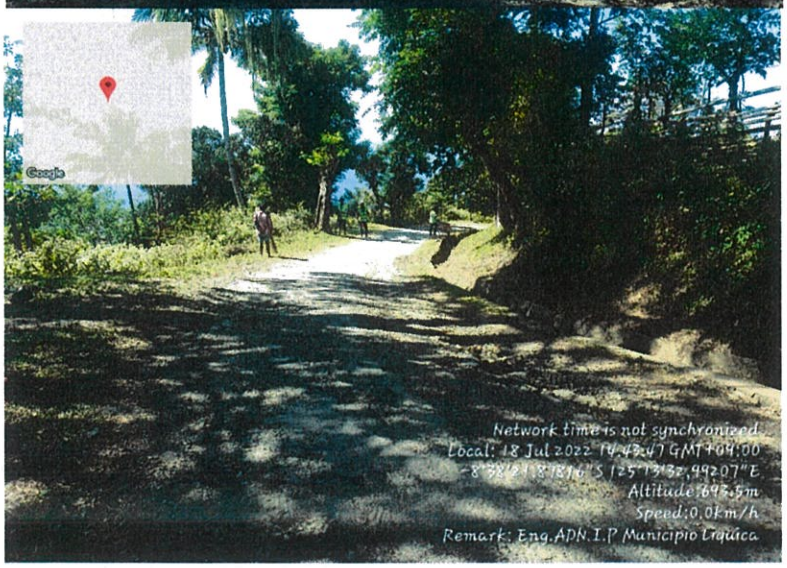Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : CMG leader - dry season **STA, 1+250 - 2+000** Companhia Kontinua servisu iha Item Routine maintenance - CMG leader - dry season	
Sketch Item servisu : CMG leader - dry season **STA, 2+000 - 3+000** Companhia Kontinua servisu iha Item Routine maintenance - CMG leader - dry season	
Sketch Item servisu : CMG leader - dry season **STA, 3 + 000 - 3+500** Companhia Kontinua servisu iha Item Routine maintenance - CMG leader - dry season	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL


ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (MBR16)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubaralisa Chainage 4+200-8+400)

Kompanha : Luliana Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	18/Julho/2022	Lquica/Maubara	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Monitorizasaun Projeitu	
					2	Bukua Tamu laiha atu priense	
					3		
					4		
II	18/Julho/2022	Lquica/Maubara	Luduvina M. Helena Guterres		1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (MBR16)

Name of Roads : R4D Rural Road Spot Improvement Barkau (Vaviquina - Maubaralisa Chainage 4+200-8+400)
Contract No : MPW-W-210160
Contractor : Luliana,Unip Lda

SUMMARY

Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 3,458.00					$ 1,550.00	0.72%	$ -	0.00%	$ 1,550.00	0.72%
R-02	Drainage	$ 393.96										
R-03	Earth work	$ 9,533.98					$ 1,570.16	0.73%	$ -	0.00%	$ 1,570.16	0.73%
R-05	Sub-base, base and pavement	$ 2,334.15										
R-08	Structures	$ 139,095.11					$ 11,810.23	5.52%	$ -	0.00%	$ 11,810.23	5.52%
R-10	Dayworks	$ 210.00										
R-11	Routine maintenance	$ 6,112.00					$ 5,028.00	2.35%	$ 172.00	0.08%	$ 5,200.00	2.43%
R-15	Provisional sum	$ 500.00										
	GENERAL ITEM											
G-01	Security	$ 3,600.00					$ 1,500.00	0.70%	$ 600.00	0.28%	$ 2,100.00	0.98%
G-02	Project team	$ 11,580.00					$ 4,380.00	2.05%		0.00%	$ 4,380.00	2.05%
G-03	Safety and protection	$ 7,441.55					$ 3,204.50	1.50%	$ 2,470.00	1.15%	$ 5,674.50	2.65%
G-05	Meetings	$ 100.00							$ 100.00	0.05%	$ 100.00	0.05%
G-06	Ceremonial costs	$ 350.00					$ 175.00	0.08%	$ 100.00	0.05%	$ 275.00	0.13%
G-07	Mineral fees	$ 8,863.06										
A	**Construction cost**	**$ 161,637.20**					**$ 19,958.38**	**9.33%**	**$ 172.00**	**0.08%**	**$ 20,130.38**	**9.41%**
B	**Contractor Fee (A x 10%)**	**$ 16,163.72**					**$ 1,995.84**	**0.93%**	**$ 17.20**	**0.01%**	**$ 2,013.04**	**0.94%**
C	**General items**	**$ 31,934.61**					**$ 9,259.50**	**4.33%**	**$ 3,270.00**	**1.53%**	**$ 12,529.50**	**5.86%**
D	**Construction tax (A+B+C x 2%)**	**$ 4,194.71**					**$ 624.27**	**0.29%**	**$ 69.18**	**0.03%**	**$ 693.46**	**0.32%**
E	**TOTAL**	**$ 213,930.25**					**$ 31,838.00**	**14.88%**	**$ 3,528.38**	**1.65%**	**$ 35,366.38**	**16.53%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (MBR13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality
Contractor : Murak Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21032

Data Inspeksaun : 18/Julho/2022

Fatin Inspeksaun : Suco Maubaralisa

Koordinat :


Start Point : Long : 125.22682227 Latetude : -8.644211521
End Point : Long : 125.2382274 Latetude : -8.672448189

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng.Luduvina Maria Helena Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry

STA, 1+050-1+100




t	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3




Sketch Item servisu : Stone Masonry

STA, 1+050-1+100




t	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3

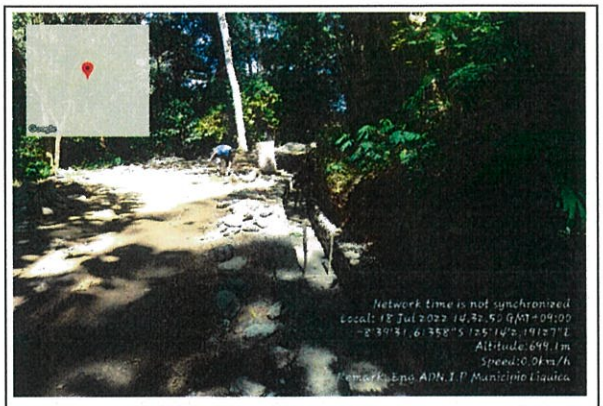


Sketch Item servisu : Stone Masonry

STA, 1+050-1+100



t	w	*Distacia*	*Volume*
0.40	0.25	100.00	20.00
0.15	1.00		15
Total			35.00 m3

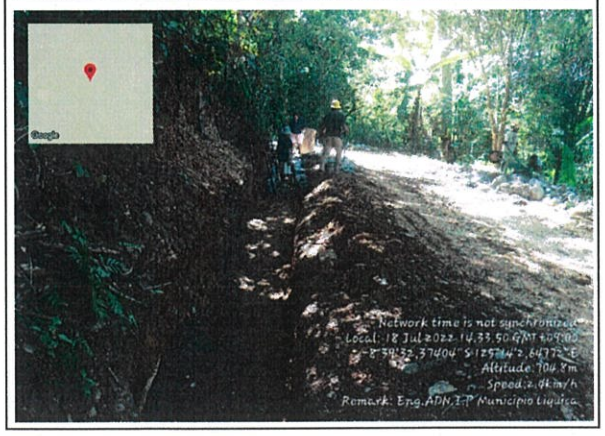

ANEXO C1 (MBR13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality
Contractor : Murak Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21032

Data Inspeksaun : 18/Julho/2022

Fatin Inspeksaun : Suco Maubaralisa

Koordinat :


Start Point : Long : 125.22682227 Latetude : -8.644211521
End Point : Long : 125.2382274 Latetude : -8.672448189

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng.Luduvina Maria Helena Guterres

Sketch & Foto Desenho


Sketch Item servisu : Stone Masonry

STA, 2+760-2+770




t	w	*Distacia*	*Volume*
1.00	2.00	15.00	30.00
Total			30.00 m3

Observasaun iha tereno no Foto Aktual

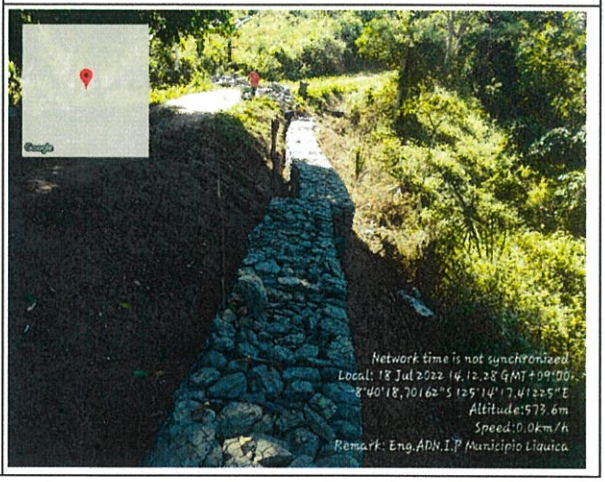

Sketch Item servisu : Gabion

STA, 2+760-2+770




t	w	*Distacia*	*Volume*
1.00	0.55	25.80	14.19
Total			14.19 m3



Sketch Item servisu : Gabion

STA, 2+760-2+770



t	w	*Distacia*	*Volume*
1.00	0.55	25.80	14.19
Total			14.19 m3



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (MBR13)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality

Kompanha : Murak Unip,Lda

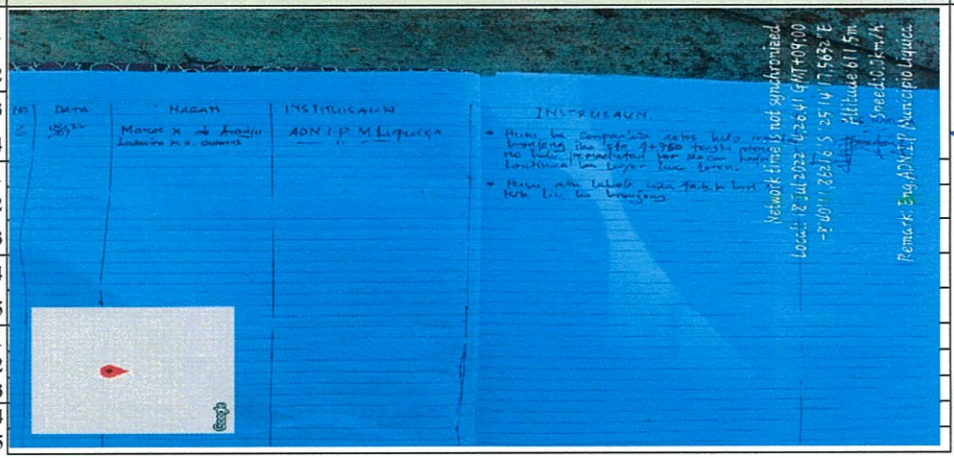No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	18/Julho/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II	18/Julho/2022	Lquica/Liquica Villa	Luduvina Maria.H.Guterres	Teknik ADN.I.P M.Liquica	1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO C2 (MBR13)

Naran Projeto : R4D Rural Road Spot Improvemrnt Malaisera - Lissadila Chainage 0+000-4+800, Liquica Municipality

Contractor : Murak Unip.Lda

No. kontratu : MOP - CD- NCB-R- 21032

Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	%	TO DATE	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 3,030.00		$ 850.00	0.56%		$ 850.00	0.56%	$ -	0.00%	$ 850.00	0.56%
R-02	Drainage	$ 25.95										
R-03	Earth work	$ 9,149.46		$ 2,962.94	1.94%		$ 2,962.94	1.94%	$ -	0.00%	$ 2,962.94	1.94%
R-05	Sub-base, base and pavement	$ 5,890.13										
R-08	Structures	$ 71,162.98		$ 15,577.63	10.18%		$ 15,577.63	10.18%	$ 1,480.20	0.97%	$ 17,057.83	11.15%
R-10	Dayworks	$ 105.00										
R-11	Routine maintenance	$ 10,808.86		$ 6,131.88	4.01%		$ 6,131.88	4.01%	$ -	0.00%	$ 6,131.88	4.01%
R-15	Provisional sum	$ 250.00										
	GENERAL ITEM											
G-01	Security	$ 3,000.00		$ 1,250.00	0.82%		$ 1,250.00	0.82%	$ 500.00	0.33%	$ 1,750.00	1.14%
G-02	Project team	$ 23,400.00		$ 12,000.00	7.84%		$ 12,000.00	7.84%	$ 5,500.00	3.59%	$ 17,500.00	11.43%
G-03	Safety and protection	$ 6,131.00		$ 3,633.50	2.37%		$ 3,633.50	2.37%	$ -	0.00%	$ 3,633.50	2.37%
G-05	Meetings	$ 100.00		$ 100.00	0.07%		$ 100.00	0.07%	$ -	0.00%	$ 100.00	0.07%
G-06	Ceremonial costs	$ 300.00		$ 150.00	0.10%		$ 150.00	0.10%	$ -	0.00%	$ 150.00	0.10%
G-07	Mineral fees	$ 6,653.08										
A	**Construction cost**	**$ 100,422.37**		**$ 25,522.45**	**16.68%**		**$ 25,522.45**	**16.68%**	**$ 1,480.20**	**0.97%**	**$ 27,002.65**	**17.64%**
B	**Contractor Fee (A x 10%)**	**$ 10,042.24**		**$ 2,552.24**	**1.67%**		**$ 2,552.24**	**1.67%**	**$ 148.02**	**0.10%**	**$ 2,700.26**	**1.76%**
C	**General items**	**$ 39,584.08**		**$ 17,133.50**	**11.19%**		**$ 17,133.50**	**11.19%**	**$ 6,000.00**	**3.92%**	**$ 23,133.50**	**15.12%**
D	**Construction tax (A+B+C x 2%)**	**$ 3,000.97**		**$ 904.16**	**0.59%**		**$ 904.16**	**0.59%**	**$ 152.56**	**0.10%**	**$ 1,056.73**	**0.69%**
E	**Total**	**$ 153,049.66**		**$ 46,112.36**	**30.13%**		**$ 46,112.36**	**30.13%**	**$ 7,780.78**	**5.08%**	**$ 53,893.14**	**35.21%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria H.Guterres
Engineiro ba Projecto Infraestructura, Transporte e irigaaun Municipio Liquica, ADN I.P.

Verifika Husi :

Eng.Remigio da C.S. dos Santos
Enginheiro Senior ba Projeito Insfrastructura, Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade, ADN I.P.

ANEXO C1 (LV13)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality
Naran Companhia : Prudencia Unip.Lda
No. kontratu : MOP - CD - NCB-R - 21036

Data Inspeksaun : 26/Julho/2022

Fatin Inspeksaun : Suco Taltabi - Kutulau

Koordinat :


Start Point : Long : 125.3714575 Latetude : - 8.64451919
End Point : Long : 125.3801075 Latetude : - 8.6527164

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
1 Eng. Luduvina Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual


Sketch Item servisu : *Plum Concrete*

Sta, 2+100-2+300




t	L	*Distacia*	*Volume*
0.12	4.00	100.00	48.00
Total			48.00 m³

Companhia halo Plum Concrete iha no Sta, 1+200 - 1+300

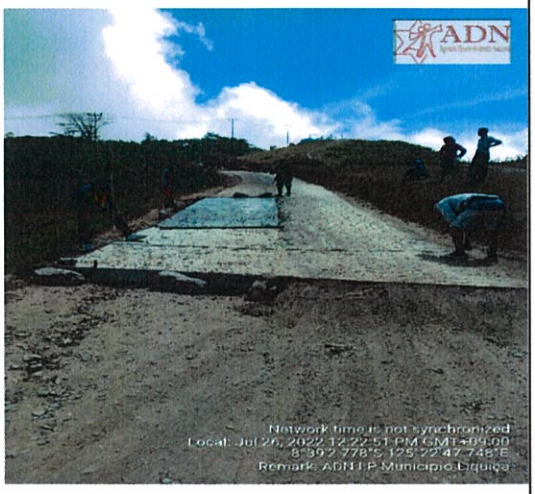


Sketch Item servisu : *Plum Concrete*


Sta, 1+400 - 1+500



t	L	*Distacia*	*Volume*
0.12	3.75	100.00	45.00
Total			45.00 m³

Companhia halo Plum Concrete iha no Sta, 1+200 - 1+300

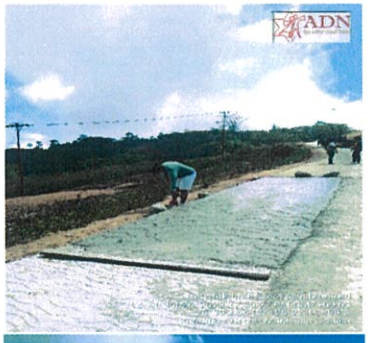

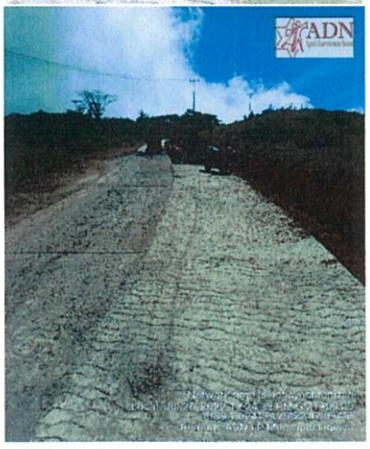

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (LV13)

INSTRUSAUN / REKOMENDASAUN

Naran projeto :R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality

Kompanha : Prudencia Unip.Lda

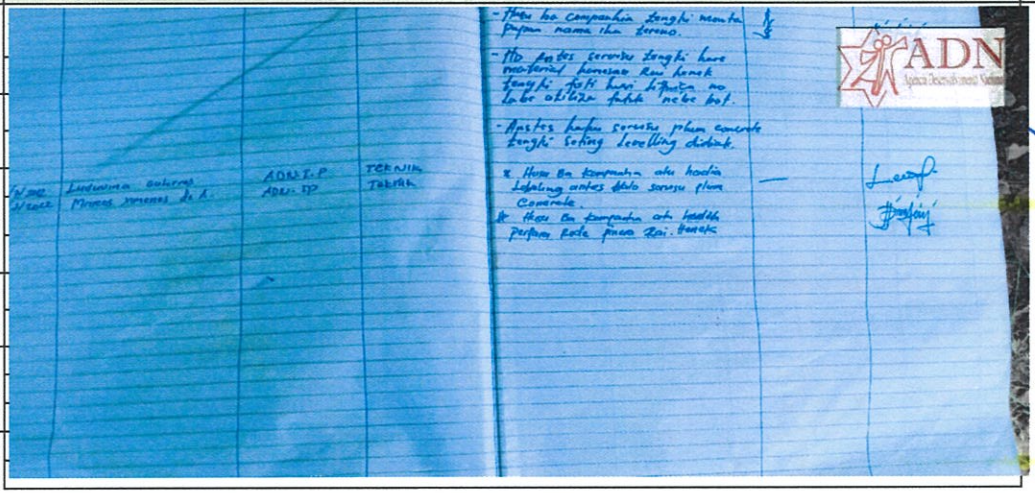No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/Julho/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1 2 3 4		
II	26/Julho/2022	Lquica/Liquica Villa	Luduvina Guterres	Teknik ADN.I.P M.Liquica	1 2 3 4 5		
III					1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (LV13)

Name of Roads :R4D Rural Road Spot Improvemrnt Taltabi - Kutulau Chainage 0+000-1+700, Liquica Municipality
Contract No : MOP - CD - NCB-R - 21036
Contractor : Prudencia Construction Unipessoal.Lda

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP				RESULTADO INSPEKSAUN ADN.IP					
			PREVIOUS BILLING	THIS BILLING	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 1,550.00					$ 600.00	0.49%	$ -	0.00%	$ 600.00	0.49%
R-03	Earth work	$ 6,216.90					$ 140.00	0.11%	$ -	0.00%	$ 140.00	0.11%
R-05	Sub-base, base and pavement	$ 2,205.60										
R-08	Structures	$ 69,266.99					$ 9,336.44	7.55%	$ 15,211.80	12.30%	$ 24,548.24	19.86%
R-11	Routine maintenance	$ 3,842.00					$ 560.00	0.45%	$ -	0.00%	$ 560.00	0.45%
R-15	Provisional sum	$ 250.00										
	General items											
G-01	Security	$ 15.00					$ 6.25	0.01%	$ 2.50	0.00%	$ 8.75	0.01%
G-02	Project team	$ 21,600.00					$ 8,800.00	7.12%	$ 3,600.00	2.91%	$ 12,400.00	10.03%
G-03	Safety and protection	$ 2,816.00					$ 2,816.00	2.28%	$ -	0.00%	$ 2,816.00	2.28%
G-05	Meetings	$ 100.00					$ 100.00	0.08%	$ -	0.00%	$ 100.00	0.08%
G-06	Ceremonial costs	$ 150.00					$ 75.00	0.06%	$ -	0.00%	$ 75.00	0.06%
G-07	Mineral fees	$ 4,861.93										
A	Construction cost	$ 83,331.49					$ 10,636.44	8.60%	$ 15,211.80	12.30%	$ 25,848.24	20.91%
B	Contractor Fee (A x 10%)	$ 8,333.15					$ 1,063.64	0.86%	$ 1,521.18	1.23%	$ 2,584.82	2.09%
C	General items	$ 29,542.93					$ 11,797.25	9.54%	$ 3,602.50	2.91%	$ 15,399.75	12.46%
D	Construction tax (A+B+C x 2%)	$ 2,424.15					$ 469.95	0.38%	$ 406.71	0.33%	$ 876.66	0.71%
E	Total	$ 123,631.72					$ 23,967.28	19.39%	$ 20,742.19	16.78%	$ 44,709.47	36.16%

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria Helena Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

ANEXO C1 (MBR11)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600, Liquica Municipality
Contractor : Malibo Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21033

Data Inspeksaun : 18/Julho/2022

Fatin Inspeksaun : Suco Lisadila

Koordinat :


Start Point : Long : 125.23822736 Latetude : -8.672448189
End Point : Long : 125.2291648 Latetude : -8.693159140

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng.Luduvina Maria H.Guterres

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu : Stone Masonry

STA, 4+300 - 4+353




t	w	Distacia	Volume
0.40	0.25	53.00	10.60
0.15	1.00		7.95
Total			18.55 m3




Sketch Item servisu : Stone Masonry

STA, 4+400 - 4+444




t	w	Distacia	Volume
0.40	0.25	44.00	8.80
0.15	1.00		6.6
Total			15.40 m3

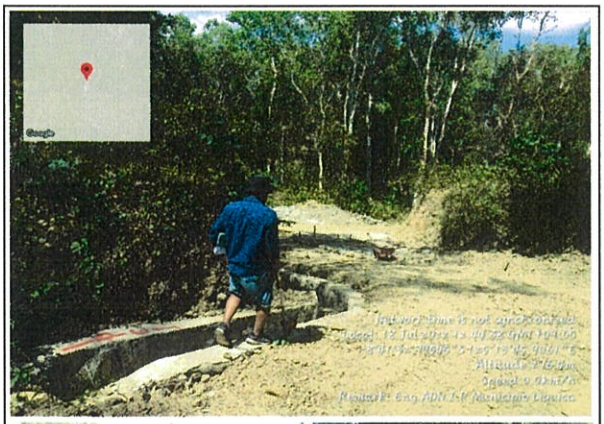

Sketch Item servisu : Stone Masonry

STA, 4+600 - 4+674



t	w	Distacia	Volume
0.40	0.25	74.00	14.80
0.15	1.00		11.1
Total			25.90 m3



ANEXO C1 (MBR11)

Back-up Data

Naran Projeto : R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600, Liquica Municipality
Contractor : Malibo Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21033

Data Inspeksaun : 18/Julho/2022

Fatin Inspeksaun : Suco Lisadila

Koordinat :


Start Point : Long : 125.23822736 Latetude : -8.672448189
End Point : Long : 125.2291648 Latetude : -8.693159140

Naran Inspektor : 1 Eng. Marcos Ximenes de Araujo
2 Eng.Luduvina Maria H.Guterres

Sketch & Foto Desenho

Sketch Item servisu : Excavation and disposal

STA, 4+300 - 4+353




t	w	*Distacia*	*Volume*
0.55	1.00	53.00	29.15
Total			29.15 m3

Observasaun iha tereno no Foto Aktual




Sketch Item servisu : Excavation and disposal

STA, 4+400 - 4+444




t	w	*Distacia*	*Volume*
0.55	1.00	44.00	24.20
Total			24.20 m3

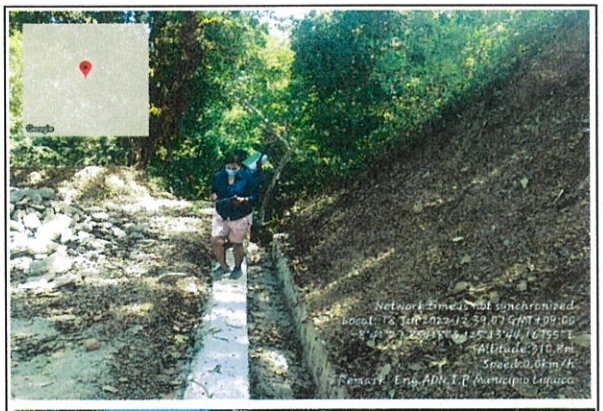


Sketch Item servisu : Excavation and disposal

STA, 4+600 - 4+674



t	w	*Distacia*	*Volume*
0.55	1.00	73.00	40.15
Total			40.15 m3

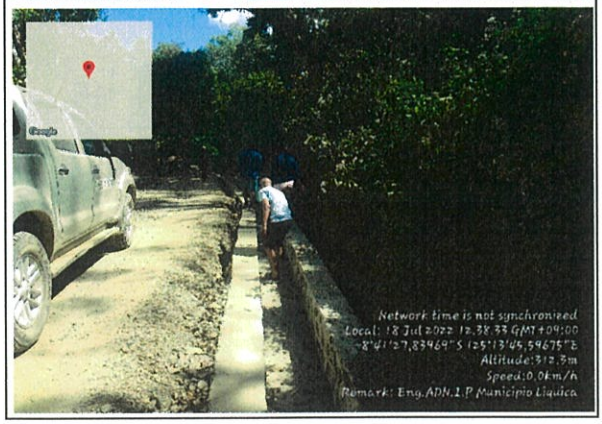

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO D (MBR11)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600, Liquica Municipality

Kompanha : Malibo Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	18/Julho/2022	Lquica/Liquica Villa	Marcos Ximenes de Araujo	Teknik ADN.I.P M.Liquica	1	Inspeksaun Pagamentu	
					2	Kompanhia la prepara buku tamu atu priense	
					3		
					4		
II	18/Julho/2022	Lquica/Liquica Villa	Luduvina Maria H.Guterres	Teknik ADN.I.P M.Liquica	1		
					2		
					3		
					4		
III					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXO C2 (MBR11)

Naran Projeto : R4D Rural Road Spot Improvement Malaisera -Lissadila Chainage 4+800-9+600, Liquica Municipality
Contractor : Malibo Unip.Lda
No. kontratu : MOP - CD- NCB-R- 21033

SUMMARY												
Itime	DESCRIPTION	CONTRACT ORIGINAL	RESULTADO INSPEKSAUN MOP					RESULTADO INSPEKSAUN ADN.IP				
			PREVIOUS BILLING	THIS BILLING	%	TO DATE	%	PREVIOUS BILDING	%	THIS BILLING	%	TO DATE	%
R-01	General works	$ 2,600.00						$ 250.00	0.16%	$ 350.00	0.23%	$ 600.00	0.39%
R-02	Drainage	$ 26.20								$ -	0.00%	$ -	0.00%
R-03	Earth work	$ 8,447.92						$ 1,285.35	0.84%	$ 3,326.08	2.18%	$ 4,611.43	3.02%
R-05	Sub-base, base and pavement	$ 2,583.44								$ 1,231.58	0.81%	$ 1,231.58	0.81%
R-08	Structures	$ 87,375.26						$ 7,602.00	4.98%	$ 11,935.14	7.82%	$ 19,537.14	12.80%
R-10	Dayworks	$ 105.00								$ -	0.00%	$ -	0.00%
R-11	Routine maintenance	$ 9,862.80						$ 385.00	0.25%	$ 3,196.00	2.09%	$ 3,581.00	2.35%
R-15	Provisional sum	$ 250.00								$ -	0.00%	$ -	0.00%
	General item												
G-01	Security	$ 2,100.00						$ 875.00	0.57%	$ -	0.00%	$ 875.00	0.57%
G-02	Project team	$ 12,162.00						$ 4,203.00	2.75%	$ 1,401.00	0.92%	$ 5,604.00	3.67%
G-03	Safety and protection	$ 4,249.00								$ 4,049.00	2.65%	$ 4,049.00	2.65%
G-05	Meetings	$ 100.00								$ 100.00	0.07%	$ 100.00	0.07%
G-06	Ceremonial costs	$ 300.00						$ 150.00	0.10%	$ 75.00	0.05%	$ 225.00	0.15%
G-07	Mineral fees	$ 6,883.92								$ -	0.00%	$ -	0.00%
A	**Construction cost**	**$ 111,250.62**						**$ 9,522.35**	**6.24%**	**$ 20,038.80**	**13.13%**	**$ 29,561.15**	**19.37%**
B	**Contractor Fee (A x 10%)**	**$ 11,125.06**						**$ 952.24**	**0.62%**	**$ 2,003.88**	**1.31%**	**$ 2,956.11**	**1.94%**
C	**General items**	**$ 25,794.92**						**$ 5,228.00**	**3.43%**	**$ 5,625.00**	**3.69%**	**$ 10,853.00**	**7.11%**
D	**Construction tax (A+B+C x 2%)**	**$ 2,963.41**						**$ 314.05**	**0.21%**	**$ 553.35**	**0.36%**	**$ 867.41**	**0.57%**
E	**Total**	**$ 152,622.90**						**$ 16,016.64**	**10.49%**	**$ 28,221.03**	**18.49%**	**$ 44,237.67**	**28.98%**

Inspeksaun Husi :

Eng. Marcos Ximenes de Araujo
Engineiro ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Inspeksaun Husi :

Eng. Luduvina Maria.H.Guterres
Engineira ba Projecto Infraestructura,Transporte e irigaaun Municipio Liquica,ADN I.P.

Verifika Husi :

Eng.Remigio da C.S.dos Santos
Enginheiro Senior ba Projeito Insfrastructura,Transportes e Irigasaun, ADN I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação da Qualidade,ADN I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Marcos Ximenes de Araujo

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

JULHO

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	PHO
							Actual	
	2	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	3	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	4	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	5	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	6	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	7	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	8	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan	PHO
							Actual	
	9	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	10	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	11	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	12	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	13	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip.Lda	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	
							Actual	
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip,Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan	
							Actual	
	3	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	
							Actual	
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan	Ekipa ADN.I.P nebe maka toma konta Projeito IMPRESTIMO
							Actual	
	5	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000-1+600 Vaviquinia-Maubaralisa Chainage 0+000-12+500	Luliana Unip.Lda	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	PHO
							Actual	
	6	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 0+000-4+200)	Nhcu.Unip.Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	7	R4D Rural Road Spot Improvement Nunuleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip.Lda	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	8	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 4+800-9+600)	Malibo Unip.Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	9	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+000-4+800)	Murak.Unip.Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	10	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 8+400-12+500)	Meta Loe Crae Bau.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	11	R4D Rural Road Spot Improvement Samarapo-Gisu Chainage 0+000-2+000)	Nazico.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	12	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 4+200-8+400)	Luliana Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	2	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	
							Actual	
	3	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan	
							Actual	
	4	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip Lda	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan	
							Actual	
	5	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	
							Actual	
	6	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan	
							Actual	
	7	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan	
							Actual	
	8	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan	
							Actual	
	9	New construction of isolation for covid 19 in chi liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan	
							Actual	
	10	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan	
							Actual	
	11	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	PHO
							Actual	
	12	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan.Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	13	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan.Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	14	R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	15	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	16	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
	17	Construction of Intersection in the Existing Dili-Liquica Road to Connect Acces Road From Tibar Bay Port (Nacional Road-A03)	Aitula.Unip.Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan	On Going
							Actual	
TOTAL PROJETO ON-GOING								

Note:

Plano Periode inspesaun iha tereinu | Relatoriu avaliasuan mensal iha Dili | Inspesaun Pagamentu Anual iha tereinu | Implementasaun Plano Periode Inspesaun iha tereinu | Iha Edifisio Municipio Liquica

Prepara Husi :

(Eng.Luduvina Maria Helena Guterres)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun Municipio

Sertifika Husi :

(Eng.Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.I.P

Aprova Husi :

(Eng.Januario Maia Guteres)
Adjunto Director Executivo ADN.I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERSO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Marcos Ximenes de Araujo

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

JULHO

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		PHO
							Actual																																		
	2	R4D Rural Road Rehabilitation Bebadiri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	3	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	4	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Cailu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	5	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	6	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	7	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	8	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																		PHO
							Actual																																		
	9	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	10	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	11	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	12	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	13	Projeitu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip.Lda	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip,Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		
							Actual																																		
	3	Konstrusaun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		
							Actual																																		Ekipa ADN.I.P nebe maka toma konta Projeito IMPRESTIMO
	5	R4D Rural Road Maintenance Berlakulidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000-1+600 Vaviquinia-Maubaralisa Chainage 0+000-12+500	Luliana Unip.Lda	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		PHO
							Actual																																		
	6	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 0+000-4+200)	Nheu.Unip.Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	7	R4D Rural Road Spot Improvement Nunuleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip.Lda	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	8	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 4+800-9+600)	Malibo Unip.Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	9	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+000-4+800)	Murak.Unip.Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	10	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 8+400-12+500)	Meta Loe Crae Bau.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	11	R4D Rural Road Spot Improvement Samarapo-Gisu Chainage 0+000-2+000)	Nazico.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	12	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 4+200-8+400)	Luliana Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	2	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
	3	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																		
							Actual																																		
	4	Konstrusaun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip Lda	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
	5	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		
							Actual																																		
	6	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																																		
							Actual																																		
	7	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Naesalobu	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																		
							Actual																																		
	8	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																																		
							Actual																																		
	9	New construction of isolation for covid 19 in chi liquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																																		
							Actual																																		
	10	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																		
							Actual																																		
	11	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		PHO
							Actual																																		
	12	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan.Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	13	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan.Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	14	R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	15	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	16	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	17	Construction of Intersection in the Existing Dili-Liquica Road to Connect Acces Road From Tibar Bay Port (Nacional Road-A03)	Aitula.Unip.Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
TOTAL PROJETO ON-GOING																																							

Note:

Plano Periode inspesaun iha tereinu — Relatoriu avaliasuan mensal iha Dili — Inspesaun Pagamentu Anual iha tereinu — Implementasaun Plano Periode Inspesaun iha tereinu — Iha Edifício Municipio Liquica

Prepara Husi :

(Eng.Marcos Ximenes de Araujo)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun Municipio

Sertifika Husi :

(Eng.Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.I.P

Aprova Husi :

(Eng.Januario Maia Guteres)
Adjunto Director Executivo ADN.I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Marcos Ximenes de Araujo

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	JULHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		PHO
							Actual																																		
	2	R4D Rural Road Rehabilitation Bebadri - Lebokalako Chainage 0+000 - 5+000 Liquica Municipality	15 Raelti Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	3	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Luqueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	4	R4D Rural Road Spot Improvement Aibenu-Asumanu Chainage 5+000-10+000)	Caitu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	5	R4D Rural Road Spot Improvement Aibenu-Asumanu-Leorema Chainage 0+000-5+000)	Vicaroman Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	6	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metaliku Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	7	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudencia Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	8	Manutensaun Kanais Irrigasaun Faulara - Liquica	Banir Lema Unip.Lda		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																		PHO
							Actual																																		
	9	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 0+000-2+500)	Goubara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	10	R4D Rural Road Spot Improvement Berlakuidu-Laberlaka Chainage 2+500-5+400)	Claridade Unip .Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	11	R4D Rural Road Spot Improvement Gunaba- Lukulai Chainage 0+000-2+000)	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	12	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	13	Projeitu Konstruasun Foun ESG Publico 01-Liquica	Roman Furak Unip.Lda	NCB:16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip,Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		
							Actual																																		
	3	Konstruasun ESTV Lisadila Maubara-Liquisa (CA + CB)	Aleni Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Lda Jr Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		Ekipa ADN I.P nebe maka toma konta Projeito IMPRESTIMO
							Actual																																		
	5	R4D Rural Road Maintenance Berlakuidu - Laberlaka Chainage 0+000 - 5+400 Nunuleta - Darulema Chainage 0+000-1+600 Vaviquinua-Maubaralisa Chainage 0+000-12+500	Lulisna Unip.Lda	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		PHO
							Actual																																		
	6	R4D Rural Road Spot Improvement Barkau (Vaviquenua - Maubaralisa Chainage 0+000-4+200)	Nheu.Unip.Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	7	R4D Rural Road Spot Improvement Nunuleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip.Lda	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	8	R4D Rural Road Spot Improvement Malaisera-Lisuadila Chainage 4+800-9+600)	Malibo Unip.Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	9	R4D Rural Road Spot Improvement Malaisera-Lisuadila Chainage 0+000-4+800)	Muzak Unip.Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	10	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 8+400-12+500)	Meta Loc Crae Bau Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	11	R4D Rural Road Spot Improvement Samarapo-Gisu Chainage 0+000-2+000)	Nazico.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	12	R4D Rural Road Spot Improvement Barkau (Vaviquenia - Maubaralisa Chainage 4+200-8+400)	Lulisna Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	2	Konstruasun ESTV Maumeta - Liquisa (CA + CB)	Vida Diak Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
	3	Konstruasun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019:19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																		
							Actual																																		
	4	Konstruasun Foun EBF Hotugara Bazartete, Liquica (162)	Milcha Unip Lda	(RFQ:19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																		
							Actual																																		
	5	Hamos Tangki Estasaun Tratamento Agua Residuais Etar Tibar / 162	Culoco Unipessoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		
							Actual																																		
	6	New Water Supply of Bairos PNTL Liquica	Holuli Unipessoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																																		
							Actual																																		
	7	Konstruasun Armagen Foun Matadouro (Bom Servisu)	Naesalobu	MAP-P02019:19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																		
							Actual																																		
	8	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Queson SQ Unipessoal Lda	MS-DNA-RBK-20-178	LM	MINISTERIO SAUDE	Plan																																		
							Actual																																		
	9	New construction of isolation for covid 19 in chi lsquica, Timor Leste	Senizu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																																		
							Actual																																		
	10	Kanalizasaun Be Mos ho Sistema Gravitasaun Iha Aipelo-Lquisa	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																		
							Actual																																		
	11	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		PHO
							Actual																																		
	12	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan.Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	13	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan.Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	14	R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	15	Routine Maintenance Maumeta-Metagou-Bazartete Chainage 0+000-10+000	Craeleki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	16	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM Casleba.Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
	17	Construction of Intersection in the Existing Dili-Liquica Road to Connect Acces Road From Tibar Bay Port (Nacional Road-A03)	Aitula.Unip.Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		On Going
							Actual																																		
		TOTAL PROJETO ON-GOING																																						

Note:
[redacted] Plano Periode inspesaun iha tereinu | Relatoriu avaliasaun mensal iha Dili | [redacted] Inspesaun Pagamentu Anual iha tereinu | [redacted] Implementasaun Plano Periode Inspesaun iha tereinu | [redacted] Iha Edificio Municipio Liquica

Prepara Husi :

(Eng.Marcos Ximenes de Araujo)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun Municipio

Sertifika Husi :

(Eng.Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN.I.P

Aprova Husi :

(Eng.Januario Maia Guteres)
Adjunto Director Executivo ADN.I.P

#ANEXU C1 – (BZT3)

Back-up Data

Naran Projeto : **Konstrusaun ESTV Maumeta - Liquisa (CA + CB)**
Kompania : **Vida Diak Unip. Lda.**
No. kontratu : **CID/600/PDIM/AM-LIQ/VIII/2019/02**

Data Inspesaun : 01 Julho 2022

Fatin Inspesaun : Maumeta, Liquica

Koordinadas :

Start Point : Long : S 8°35'26.471'', Latetude : .....

End Point : Long : E 125° 20'58.069'', Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....


4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu Konstrusaun Foun ESTV Maumeta – Liquica (CA + CB) neebe lokaliza iha suku Maumeta, postu Bazartete, Munisipiu Liquisa, obra nee kaer husi kompania Vida Diak Unip. Lda. No projeitu nain ba obra refere maka PDIM no MEJD.	

#ANEXU C1 – (BZT3)

Back-up Data

Naran Projeto : **Konstrusaun ESTV Maumeta - Liquisa (CA + CB)**
Kompania : **Vida Diak Unip. Lda.**
No. kontratu : **CID/600/PDIM/AM-LIQ/VIII/2019/02**

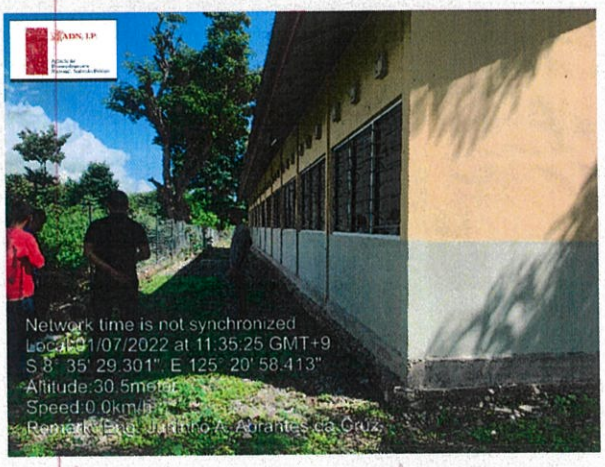Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa kordena ho ekipa tekniku husi projeitu nain (PDIM Munisipal) no ekipa husi kompania neebe kaer projeitu refere halao inspesaun ba periodu retensaun 10% neebe finaliza tiha ona.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Iha inspesaun refere ekipa tekniku sira hatoo ona ba kompania hadia ka hare fila fali item ruma neebe mak hetan estragus mak hanesan, lampu balu la lakan presija troka no mos ba estragus redi haleu nian neebe impaktu husi udan boot. Kompania hatan ona atu finaliza lalais item hirak nee molok rekomenda.	

#ANEXU D - (BZT3)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN ESTV MAUMETA - LIQUISA (CA + CB)

Kompanha : VIDA DIAK UNIP. LDA

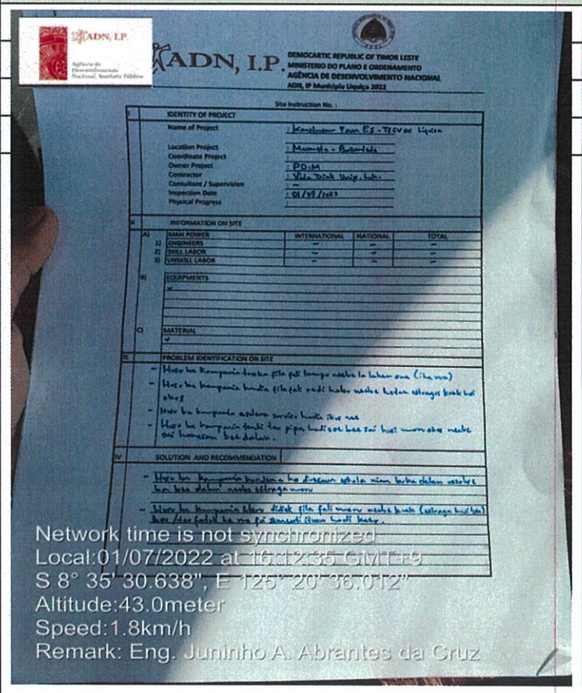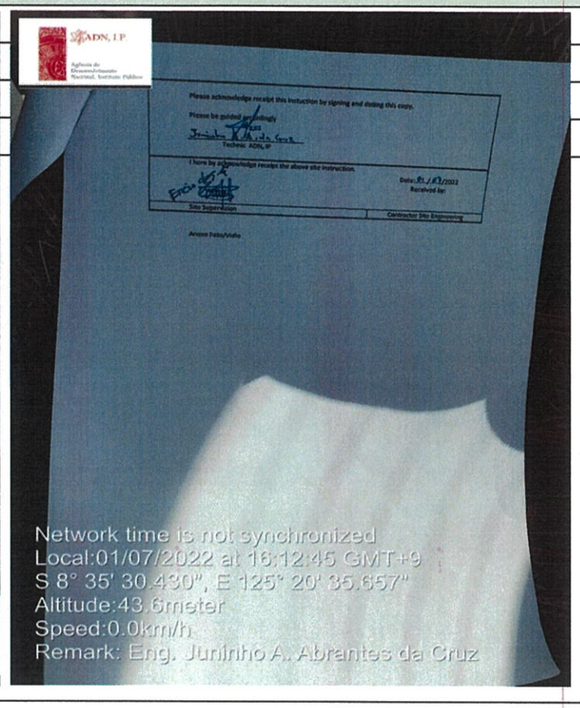No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	1/07/2022	Maumeta, Bazartete, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5	 	

#ANEXU C1 – (BZT22)

Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

Data Inspesaun : 01 Julho 2022

Fatin Inspesaun : Maumeta – Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 33. 307''**, Latetude : .....


End Point : Long : **E 125º 20' 30. 962''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....


3. .....

4. .....

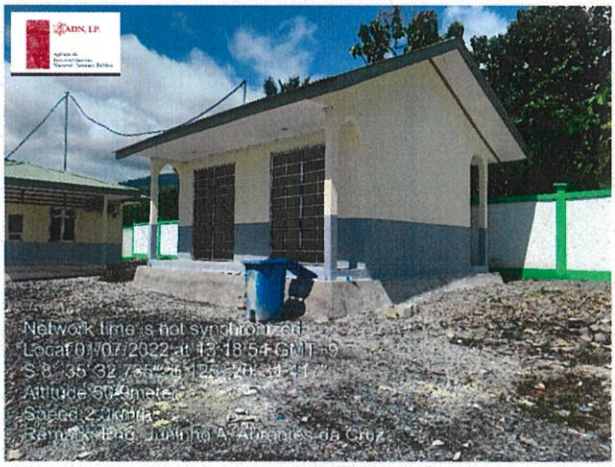Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu Foun Supply and Installation Connection for Isolation and Laboratorium Building iha Liquisa, obra husi Ministeriu Saude husi fundu Covid no kaer husi kompania Zyc Unip. Lda.	

#ANEXU C1 – (BZT22)
Back-up Data

Naran Projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Kompania : Zyc Unip. Lda.
No. kontratu : RDTL-MS-C19-DNA-DC-21-228

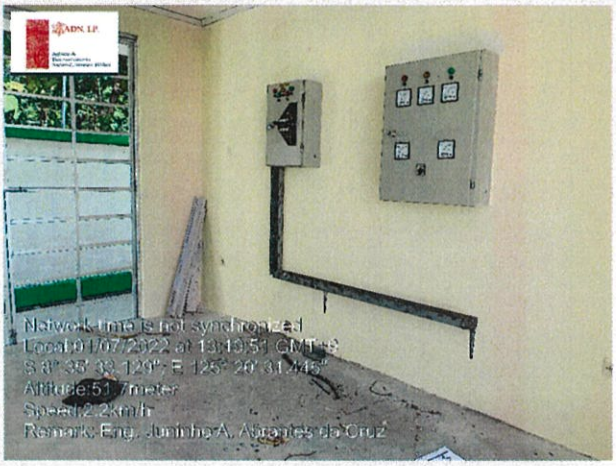Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku hatoo ona ba kompania atu kordena ho ekipa tekniku Eletrisidade husi projeitu nain (MDS) no mos tekniku Eletrisidade husi ADN, IP molok halao servisu instalasaun ruma ba item eletrisidade nian iha terenu.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku mos hatoo nafatin ba kompania atu hare fila fali servisu item *lisplank* nian neebe ladun rapi/kleuk hela, maibe iha terenu trabaliador sira la servisu iha terenu no tekniku kompania mos la iha terenu.	

#ANEXU D - (BZT22)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica

Kompanha : Zyc Unipessoal Lda

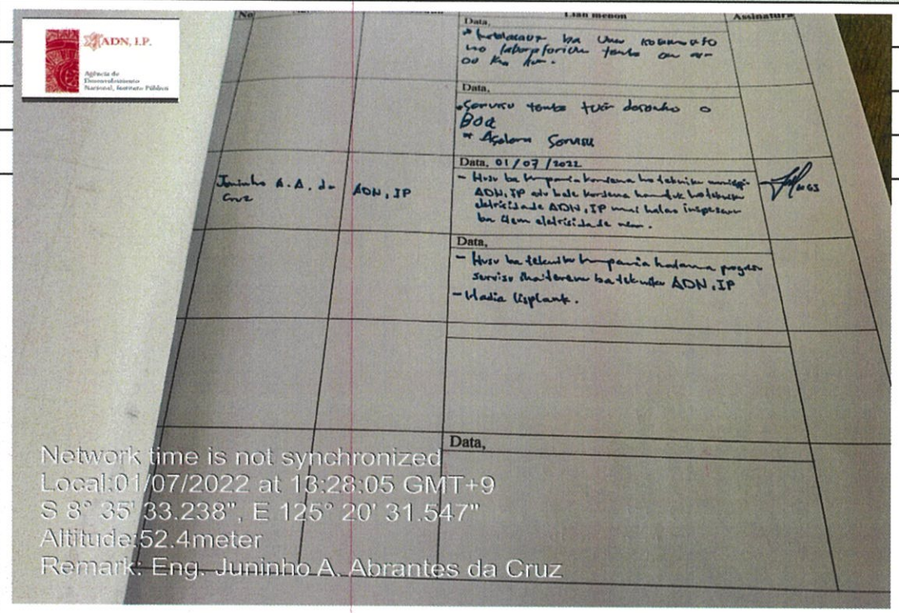No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	1/07/2022	Maumeta, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Project Name : Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica
Location : Liquica Municipality - Timor Leste
Project Owner : Ministry of Health

#ANEXU C2 - (BZT22)				VERIFIED BY A D N , I P											
NO	DESCRIPTION	Amount (USD)		PREVIOUS	% BILLED	THIS BILLING	% BILLED	TO DATE	% BILLED	PROGRESU IHA TERENU					TOTAL %
										FULAN KOTUK	%	FULAN NEE	%		
I	PREPARATION WORKS	$	4,200.00							$ 2,100.00	3.61%	$ -	0.00%		3.61%
II	NEW INSTALLATION LOW VOLTAGE (LV) LINE	$	1,044.00							$ -	0.00%	$ -	0.00%		0.00%
III	MAIN CONNECTION TO ISOLATION INCLUDE PROVIDE GENSET	$	22,726.44							$ -	0.00%	$ -	0.00%		0.00%
IV	CONSTRUCTION HOUSE FOR GENSET	$	15,040.67							$ 7,337.44	12.61%	$ 1,313.85	2.26%		14.87%
V	FINAL CLEARING	$	1,000.00							$ -	0.00%	$ -	0.00%		0.00%
A	GRAND TOTAL	$	44,011.11							$ 9,437.44	16.22%	$ 1,313.85	2.26%		18.48%
B	Fee Contractor(10% x A)	$	4,401.11							$ 943.74	1.62%	$ 131.39	0.23%		1.85%
C	Overhead	$	4,300.00							$ -	0.00%	$ -	0.00%		0.00%
D	TAX 2% x (A + B + C)	$	1,054.24							$ 207.62	0.36%	$ 28.90	0.05%		0.41%
E	CONTIGENCY (10% x A)	$	4,401.11							$ -	0.00%	$ -	0.00%		0.00%
F	TOTAL PROJECT COST (A + B + C + D + E)	$	58,167.58							$ 10,588.80	18.20%	$ 1,474.14	2.53%		20.74%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (BZT23)

Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

Data Inspesaun : 26 Julho 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 40' 43. 435''**, Latetude : .....


End Point : Long : **E 125º 22' 18. 833''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antonia de Fatima Morais Soares


3. .....

4. .....

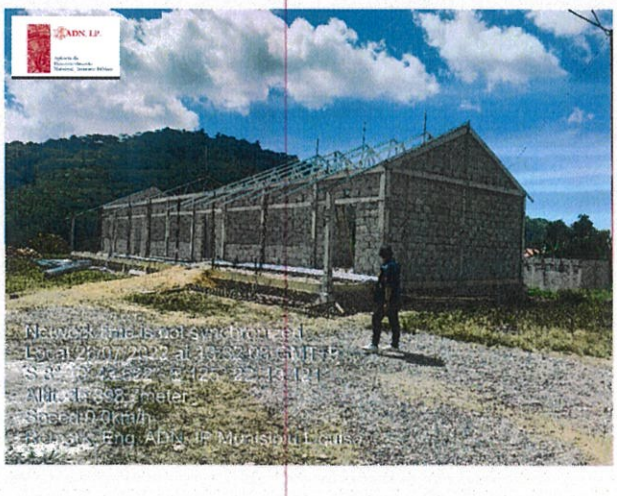Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu Konstrusaun Foun ESTV Leorema lokaliza iha suku Leorema, Bazartete, Munisipiu Liquisa projeitu nee kaer husi kompania U-Rema Unip. Lda.	

#ANEXU C1 – (BZT23)
Back-up Data

Naran Projeto : Projeitu Konstrusaun Foun ESTV Leorema - Liquica
Kompania : U-Rema Unip. Lda.
No. kontratu : NCB:15/MEJD/DNA/2021

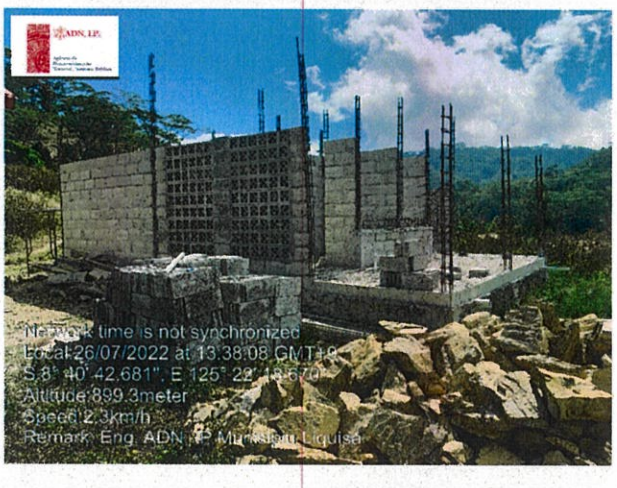Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa hato'o ona ba tekniku atu taka no rai kopia dezeniu iha terenu no entrega relatorio progresu servisu mensal no softcopy BOQ projeitu ba ekipa tekniku Munisipiu ADN, IP.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa foo instrusaun ona ba kompania atu taka *plat Truss (20cm)* ba iha sambungan kuda-kuda nian. No wainhira tama ba servisu plesteran rekomenda ona atu uza *promo*.	

#ANEXU D - (BZT23)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN ESTV LEOREMA

Kompania : U-REMA UNIP. LDA.

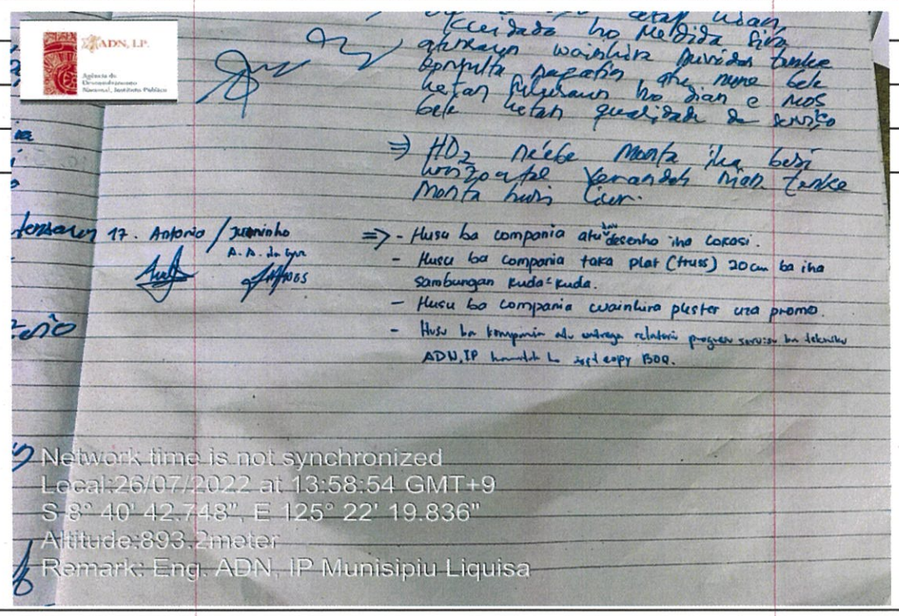No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/07/2022	Leorema, Liquisa	Juninho António Abrantes da Cruz/ Antonia de Fatima Morais Soares	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA TÉCNICA VOCACIONAL LEOREMA
FATIN PROJEITO : LEOREMA, BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

ANEKSU C2 - (BZT 23)			VERIFIED BY A D N , I P													
NO	ITEM SERVISU	AMOUNT US$	PROGRESU IHA TERENU						PREVIOUS BILLING	%	THIS BILLING		%	TOTAL TO DATE	%	
			FULAN KOTUK	%	FULAN NEE	%	TOTAL PROGRESS	%								
i	PRELIMINARIES WORKS	$ 3,035.00	$ 1,517.50	0.57%	$ -	0.00%	$ 1,517.50	0.57%								
ii	CLASSROOM BUILDING C 2 UNIT	$ 113,269.89	$ 31,715.57	12.00%	$ 278.00	0.11%	$ 31,993.57	12.11%								
iii	TEACHER OFFICE	$ 77,944.01	$ 9,353.28	3.54%	$ 5,312.71	2.01%	$ 14,665.99	5.55%								
iv	TOILET BUILDING Tb	$ 30,577.69	$ 305.78	0.12%	$ 416.08	0.16%	$ 721.87	0.27%								
v	PROVISIONAL SUM FOR SITEWORKS	$ 6,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%								
A	CONSTRUCTION COST	$ 230,826.59	$ 42,892.13	16.23%	$ 6,006.79	2.27%	$ 48,898.92	18.50%								
B	CONTRACTOR FEE (10% x A)	$ 23,082.66	$ 4,289.21	1.62%	$ 600.68	0.23%	$ 4,889.89	1.85%								
C	OVERHEAD	$ 5,170.00	$ -	0.00%	$ -	0.00%	$ -	0.00%								
D	TAX (2% x (A+B+C))	$ 5,181.58	$ 943.63	0.36%	$ 132.15	0.05%	$ 1,075.78	0.41%								
E	CONTIGENCY		$ -	0.00%	$ -	0.00%	$ -	0.00%								
F	TOTAL COST (A + B + C + D + E)	$ 264,260.83	$ 48,124.97	18.21%	$ 6,739.62	2.55%	$ 54,864.59	20.76%								

Inspeksaun Husi :

Eng. Juninho Antonio Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (BZT24)
Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Data Inspesaun : 26 Julho 2022

Fatin Inspesaun : Leorema - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 39' 21. 442''**, Latetude : .....

End Point : Long : **E 125º 22' 51. 232''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antonia de Fatima Morais Soares

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu foun husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Baura lokaliza iha suku Leorema, postu Bazartete, Munisipiu Liquisa projeitu nee kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (BZT24)
Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Baura Bazartete
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku Munisipiu ADN, I.P. hato'o ona enjineiru grupu atu ativa iha terenu hodi aselera servisu tuir plano neebe iha ona.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku sira hato'o ona ba grupu hodi kontinua servisu wainhira trabaliador no material sira iha ona terenu.	

#ANEXU D - (BZT24)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EPE BAURA

GRUPU KOMUNITARIU

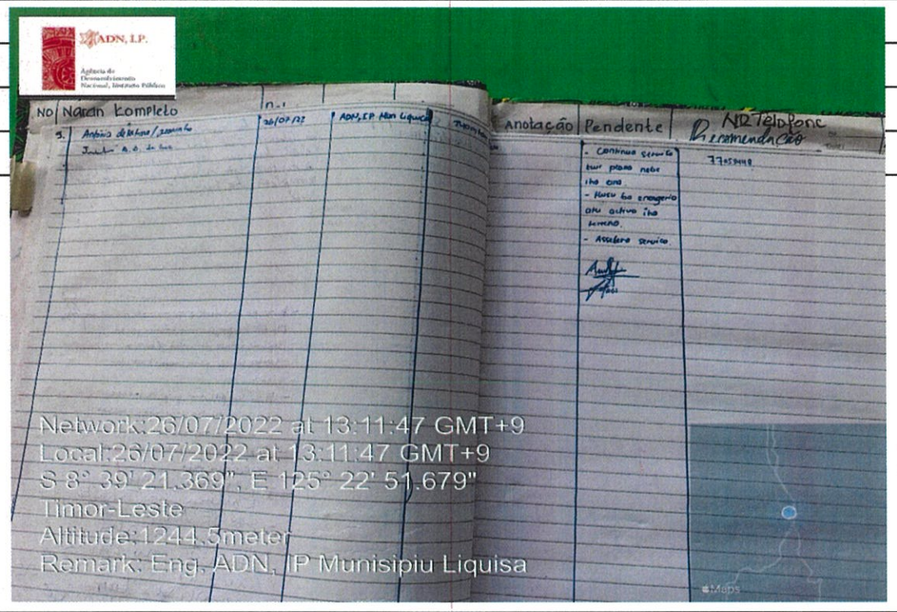No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/07/2022	Leorema, Bazartete	Juninho António Abrantes da Cruz/Antonia de Fatima Morais Soares	Tekniku ADN, IP Liquisa	1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : REHABILITAÇÃO ESCOLA PRE-ESCOLAR BAURA
FATIN PROJEITO : LEOREMA , BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (BZT24)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 1,970.00	$ 985.00	10.86%	$ -	0.00%					$ 985.00	10.86%
II	CLASSROOM BUILDING RF	RF/21	(i)	US$	$ 4,102.12	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 6,072.12	$ 985.00	10.86%	$ -	0.00%					$ 985.00	10.86%
B	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	GRAND TOTAL			US$	$ 9,072.12	$ 985.00	10.86%	$ -	0.00%					$ 985.00	10.86%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (BZT25)

Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

Data Inspesaun : 26 Julho 2022

Fatin Inspesaun : Fahilebo - Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 38' 12. 154''**, Latetude : .....


End Point : Long : **E 125º 24' 35. 457''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antonia de Fatima Morais Soares



3. .....

4. .....

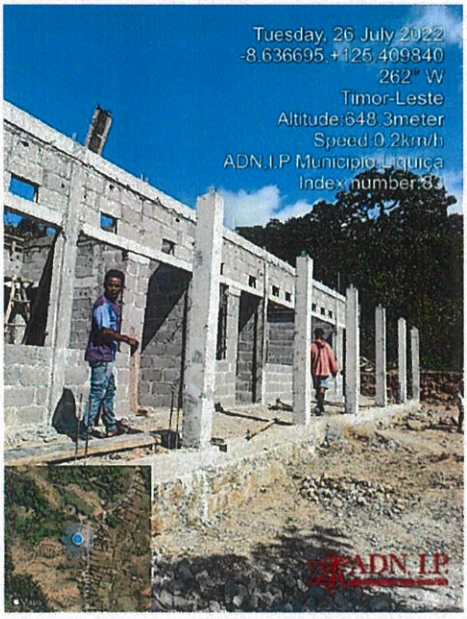Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu foun husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Ermeta Fahilebo iha suku Fahilebo, postu Bazartete, Liquisa projeitu nee kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (BZT25)
Back-up Data

Naran Projeto : Konstrusaun Foun EPE Ermeta Fahilebo
Kompania :
No. kontratu :

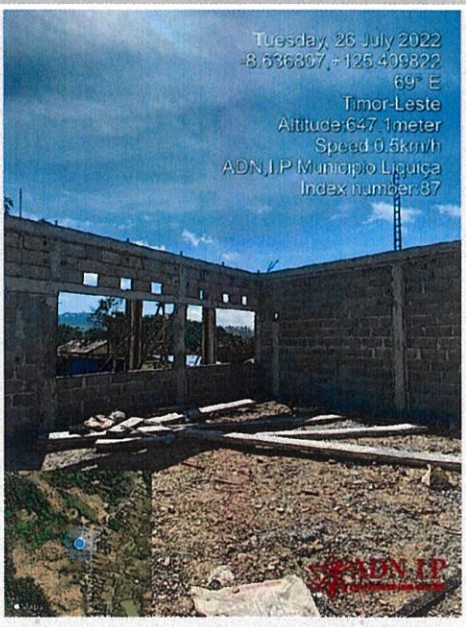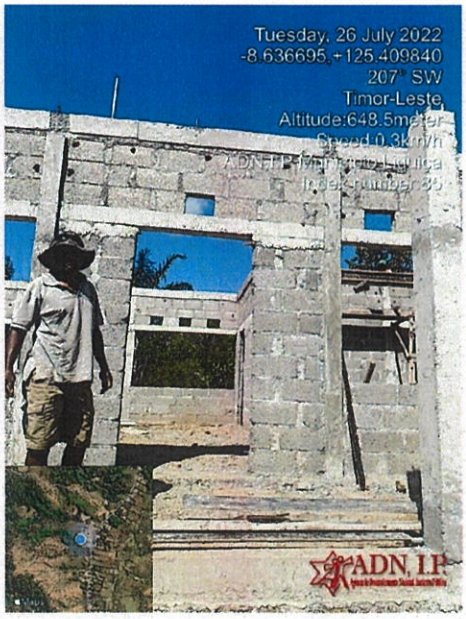Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Wainhira ekipa tekniku ADN ,I.P halao inspesaun iha terenu hatoo ona ba grupu konaba servisu neebe menus ka iha aumenta tenki kordena hamutuk ho ekipa tekniku projeitu nain no ADN, I.P atu nunee nafatin lao tuir no la ses husi dezeniu.	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku hato'o ona ba grupu atu troka fali plat *HD* iha uma oin (*terras*) tanba la hanesan ho design neebe iha tan nee tekniku grupu tenki prepara *HD* foun tuir nia design neebe mensiona, no husu atu halo dokumentasaun wainhira remata.	

#ANEXU D - (BZT25)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EPE ERMETA FAHILEBO

GRUPU KOMUNITARIU

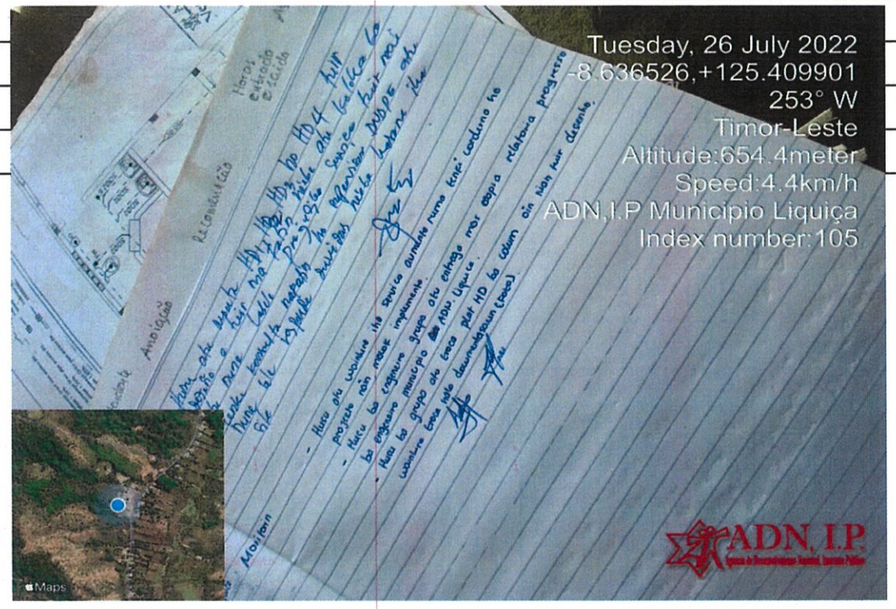No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/07/2022	Fahilebo, Liquisa	Juninho António Abrantes da Cruz/Antonia de Fatima Morais Soares	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA PRE-ESCOLAR ERMETA FAHILEBO
FATIN PROJEITO : FAHILEBO, BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (BZT25)							VERIFIED BY A D N , I P							
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	BILLED %	THIS BILLING	BILLED %	TOTAL TO DATE	BILLED %
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.78%	$ -	0.00%					$ 1,537.50	1.78%
II	CLASSROOM BUILDING C2	C2/47	(i)	US$	$ 59,793.47	$ 7,152.94	8.28%	$ 797.63	0.92%					$ 7,950.57	9.21%
III	PROVISIONAL SUM FOR SITE WORKS	SW/23	(i)	US$	$ 14,157.37	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 77,025.84	$ 8,690.44	10.06%	$ 797.63	0.92%					$ 9,488.07	10.99%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 86,365.84	$ 8,690.44	10.06%	$ 797.63	0.92%					$ 9,488.07	10.99%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (BZT26)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Cassait
Kompania :
No. kontratu :

Data Inspesaun : 08 Julho 2022

Fatin Inspesaun : Lauhata - Bazartete, Liquisa

Koordinadas :

Start Point : Long : **S 8º 34' 19. 391''**, Latetude : .....


End Point : Long : **E 125º 27' 52. 593''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

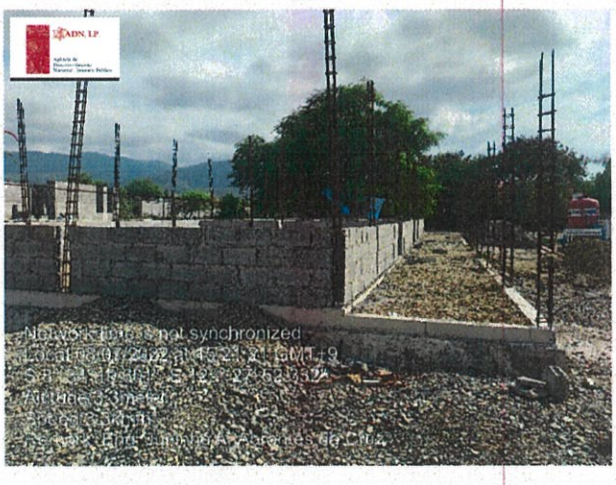Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Likisa halao inspesaun ba projeitu foun husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Cassait iha suku Lauhata, Bazartete, Liquisa projeitu nee kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (BZT26)
Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EPE Cassait
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Wainhira ekipa tekniku ADN, IP halao inspesaun iha terenu servisu projeitu refere paradu hela, hatoo husi autoridade sira katak trabaliador no tekniku grupu sira servisu loron balu deit.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku grupu presija halo justifikasaun konaba item neebe grupu atu sosa ka stock mai iha terenu tanba tuir informasaun katak grupu hola sala ona item fiu nian balu neebe la hanesan ho design ka mensiona iha BoQ.	

#ANEXU D - (BZT26)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EPE CASSAIT

GRUPU KOMUNITARIU

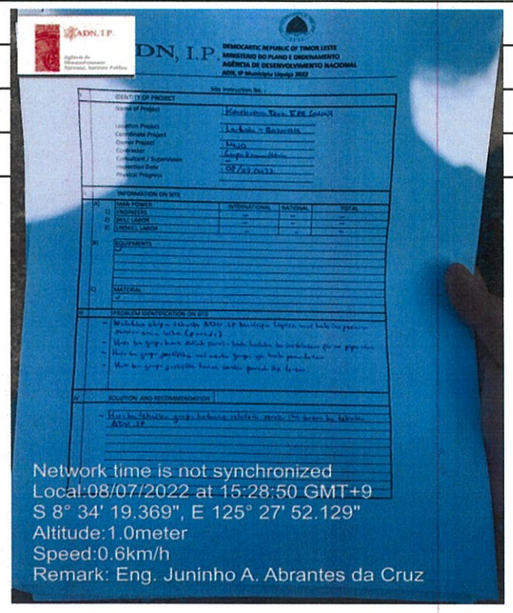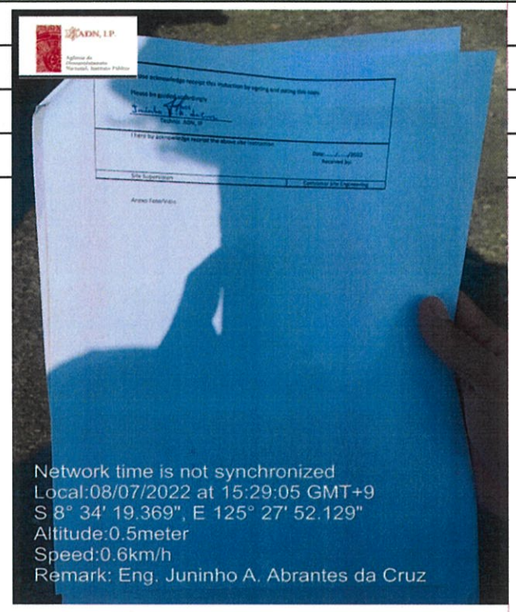No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/07/2022	Lauhata, Liquica	Juninho António Abrantes da Cruz	Tekniku ADN, IP Likisa	1 2 3 4 5	 	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA PRE-ESCOLAR CASSAIT
FATIN PROJEITO : ULMERA , BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (BZT26)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.96%	$ -	0.00%					$ 1,537.50	1.96%
II	PROVISIONAL SUM FOR DEMOLITION	DM/3		US$	$ 686.50	$ -	0.00%	$ -	0.00%					$ -	0.00%
III	CLASSROOM BUILDING C2	C2/47	(i)	US$	$ 57,955.41	$ 7,766.70	9.93%	$ 1,916.17	2.45%					$ 9,682.87	12.37%
IV	PROVISIONAL SUM FOR SITE WORKS	SW/19	(i)	US$	$ 7,193.98	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 68,910.89	$ 9,304.20	11.89%	$ 1,916.17	2.45%					$ 11,220.37	14.34%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 78,250.89	$ 9,304.20	11.89%	$ 1,916.17	2.45%					$ 11,220.37	14.34%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (BZT27)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE ESG Classe Paralelo Bogoro
Kompania :
No. kontratu :

Data Inspesaun : 08 Julho 2022

Fatin Inspesaun : Bogoro – Bazartete, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 36. 980''**, Latetude : .....

End Point : Long : **E 125º 23' 58. 119''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....


4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu Foun MEJD PKRIE ba Konstrusaun ka Reabilitasaun ESG Classe Paralelo Bogoro, lokaliza iha suku Bogoro, Bazartete, Munisipiu Liquisa, neebe kaer husi servisu Grupu Komunitariu	

#ANEXU C1 – (BZT27)
Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE ESG Classe Paralelo Bogoro
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu konstrusaun klase *Ca* (figura iha sorin) nia progresu iha terenu atinji ona servisu stock batako, no grupu mos hetan ona instrusaun atu kontinua instala batako wainhira servisu stock material nee finaliza.	

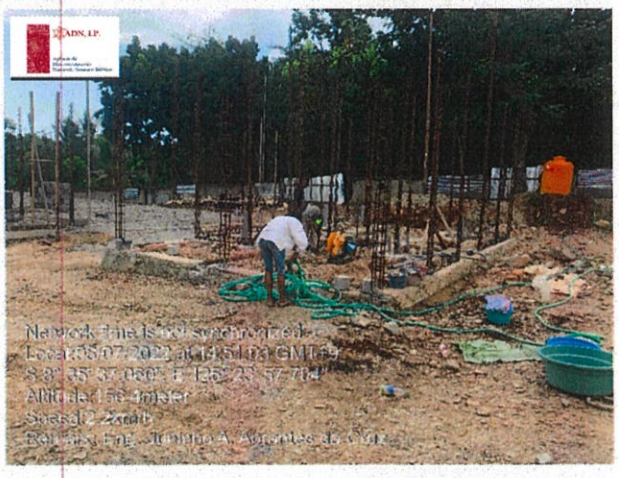Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba iha servisu konstrusaun *toilet building Tb* nian grupu finaliza ona servisu betaun ba iha kolom pendek nian tuir kompozisaun husi Obras Nasional no grupu mos hadia ona begel tuir tekniku ADN, IP nia instrusaun.	

#ANEXU D - (BZT27)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE ESG CLASSE PARALELO BOGORO

GRUPU KOMUNITARIU

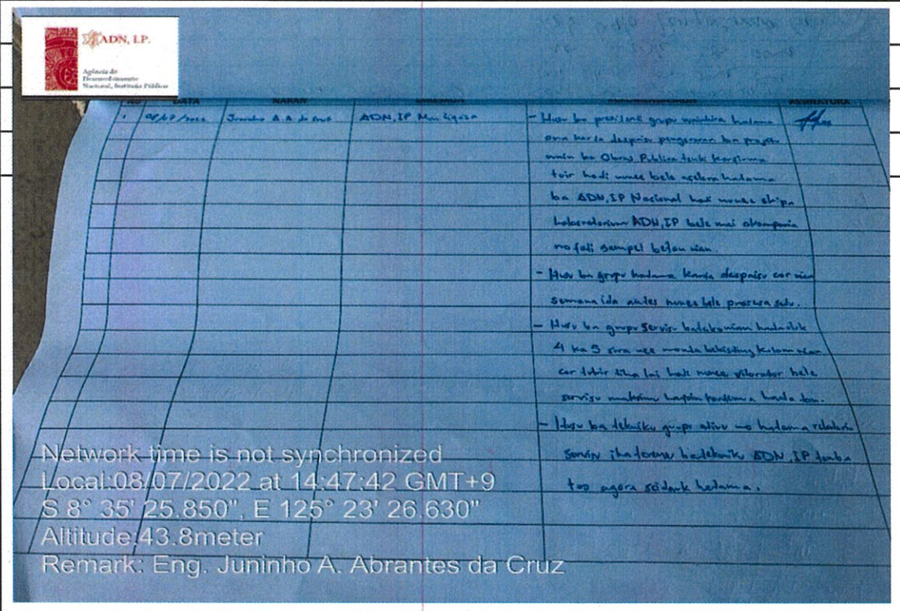No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/07/2022	Bogoro, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA SECUNDARIA GERAL PARALELO BOGORO
FATIN PROJEITO : MOTAULUN, BAZARTETE
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

# ANEXU C2 - (BZT27)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.33%	$ -	0.00%					$ 1,537.50	1.33%
II	CLASSROOM BUILDING CA	CA/39	(i)	US$	$ 65,492.93	$ 5,699.89	4.94%	$ 2,022.77	1.75%					$ 7,722.66	6.70%
III	TOILET BUILDING Tb	TB/39	(i)	US$	$ 24,504.47	$ 1,380.77	1.20%	$ 191.56	0.17%					$ 1,572.33	1.36%
IV	PROVISIONAL SUM FOR SITE WORKS	SW/28	(i)	US$	$ 12,901.36	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 105,973.76	$ 8,618.16	7.47%	$ 2,214.33	1.92%					$ 10,832.48	9.39%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 115,313.76	$ 8,618.16	7.47%	$ 2,214.33	1.92%					$ 10,832.48	9.39%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Data Inspesaun : 18 Julho 2022

Fatin Inspesaun : Dato, Liquica Vila

Koordinadas :

Start Point : Long : 8.35'21.273"S, Latetude : .....


End Point : Long : 125.20'1.933"E, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

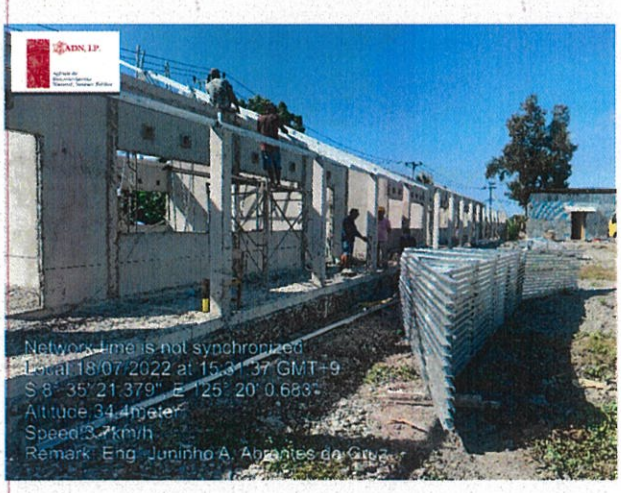
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu husi Ministeriu Edukasaun Juventude no Desportu nian ba Konstrusaun Foun ESG Publico 01-Liquica lokaliza iha suku Dato, Liquisa Vila, Munisipiu Liquisa, neebe kaer husi kompania Roman Furak Unip. Lda.	

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu iha klase *C* (figura iha sorin) nia progresu iha terenu atinji ona item servisu ba *roof trusses* (kuda-kuda) nian. Kompania hetan ona instrusaun husi tekniku ADN, IP atu servisu item ida nee lao tuir nia design no BoQ neebe mensiona.	

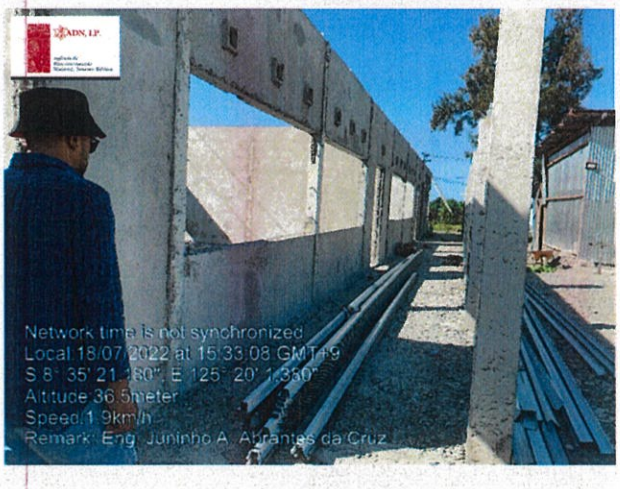Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Iha klase *Cb* (figura iha sorin) trabaliador kompania sei kontinua monta kuda-kuda wainhira finaliza monta ba klase *C* ninian, no dadaun nee trabaliador balu servisu hela ba plesteran nian.	

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

Data Inspesaun : 21 Julho 2022

Fatin Inspesaun : Dato, Liquica Vila

Koordinadas :

Start Point : Long : 8.35'21.273"S, Latetude : .....

End Point : Long : 125.20'1.933"E, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....


4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu husi Ministeriu Edukasaun Juventude no Desportu nian ba Konstrusaun Foun ESG Publico 01-Liquica lokaliza iha suku Dato, Liquisa Vila, Munisipiu Liquisa, neebe kaer husi kompania Roman Furak Unip. Lda.	

#ANEXU C1 – (LV20)

Back-up Data

Naran Projeto : **Projeitu Konstrusaun Foun ESG Publico 01-Liquica**
Kompania : **Roman Furak Unip. Lda.**
No. kontratu : **NCB:16/MEJD/DNA/2021**

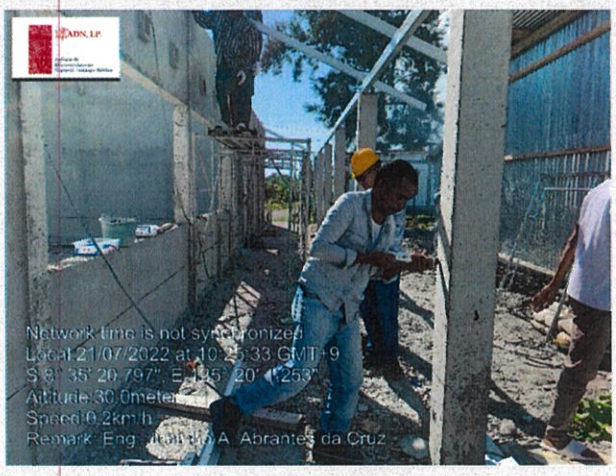Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa kordena hamutuk ho ekipa tekniku husi Laboratorium ADN, IP mai halao *hammer test* ba projeitu refere iha terenu tanba kompania nia rezultadu teste betaun iha Laboratorium la passa.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku Laboratorium ADN, IP foti dadus *hammer test* ba iha item servisu betaun nian hanesan, *column* no *top beam*. Teste nee foti dadus haleu eskola neebe fui tiha ona no foti ba klase *C* no *Cb* hotu.	

#ANEXU D - (LV20)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran Projeitu: Projeitu Konstrusaun Foun ESG Publico 01-Liquica

Kompanha : ROMAN FURAK Unip. Lda.

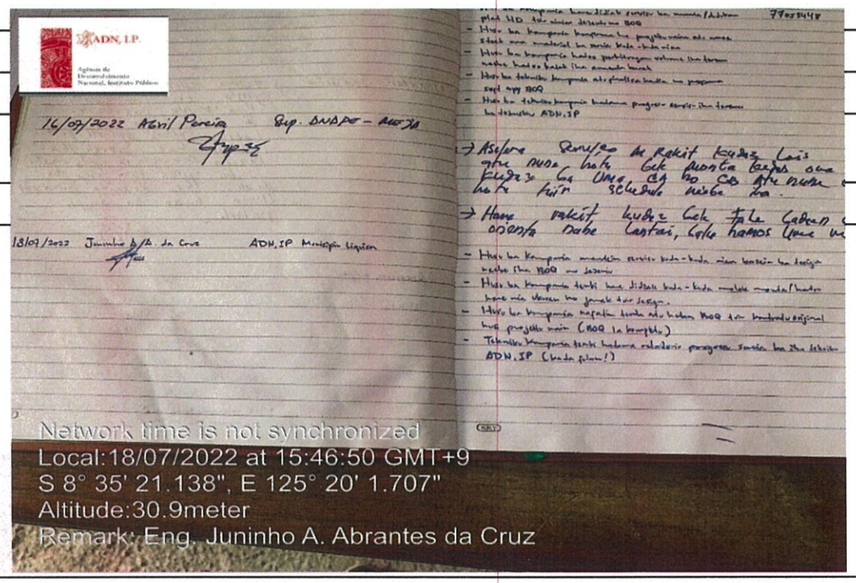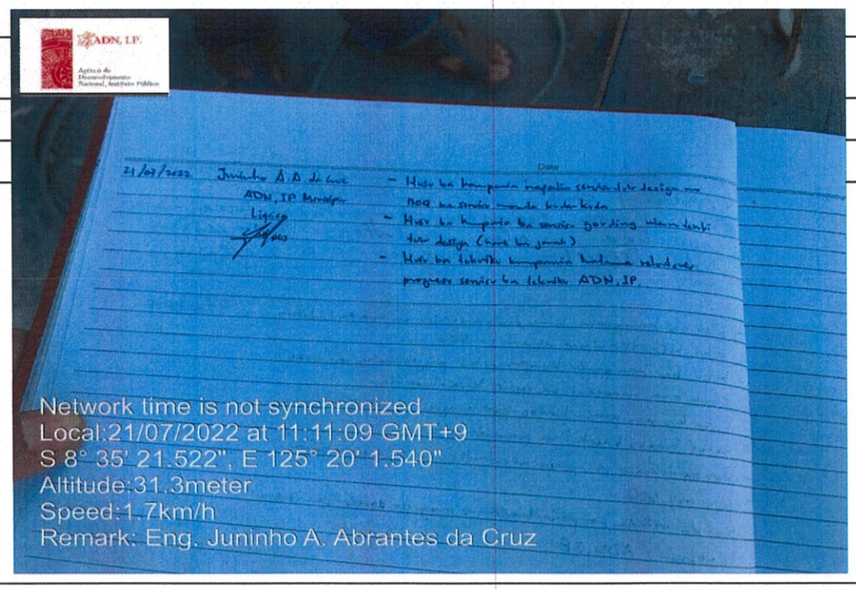No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	18/07/2022	Dato, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5 6		
II	21/07/2022	Dato, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA SECUNDÁRIA GERAL LIQUIÇA
FATIN PROJEITO : CAIMEO VILA, SUCO DATO
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

ANEKSU C2 - (LV20)			VERIFIED BY A D N , I P											
NO	WORK DESCRIPTION	AMOUNT USD	PROGRESU IHA TERENU						PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
			FULAN KOTUK	%	FULAN NEE	%	TOTAL PROGRESU	%						
I	PRELIMINARIES	$ 2,870.00	$ 1,435.00	0.86%	$ -	0.00%	$ 1,435.00	0.86%						
II	CLASSROOM BUILDING C	$ 53,423.84	$ 11,753.24	7.03%	$ 1,011.82	0.61%	$ 12,765.06	7.64%						
III	CLASSROOM BUILDING Cb	$ 75,136.99	$ 28,552.06	17.09%	$ 213.90	0.13%	$ 28,765.95	17.22%						
IV	PROVISIONAL SUM FOR SITEWORKS	$ 13,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%						
A	CONSTRUCTION COST	$ 144,430.83	$ 41,740.30	24.98%	$ 1,225.72	0.73%	$ 42,966.02	25.72%						
B	CONTRACTOR FEE (10% x A)	$ 14,443.08	$ 4,174.03	2.50%	$ 122.57	0.07%	$ 4,296.60	2.57%						
C	OVERHEAD	$ 4,930.00	$ -	0.00%	$ -	0.00%	$ -	0.00%						
D	TAX (2% x (A+B+C))	$ 3,276.08	$ 918.29	0.55%	$ 26.97	0.02%	$ 945.25	0.57%						
E	CONTIGENCY	$ -	$ -	0.00%	$ -	0.00%	$ -	0.00%						
F	TOTAL COST (A + B + C + D + E)	$ 167,079.99	$ 46,832.62	28.03%	$ 1,375.25	0.82%	$ 48,207.87	28.85%						

Inspeksaun Husi :

Eng, Juninho António Abrantes da Cruz
Engineru ba Edifisiu Publiku Agua Saneamentu, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineer ba Projeitu
Edificio Publiku Agua Saneamento
ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ
ADN, I.P.

#ANEXU C1 – (LV22)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Data Inspesaun : 08 Julho 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 49. 086''**, Latetude : .....

End Point : Long : **E 125º 18' 51. 269''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu husi MEJD PKRIE ba Konstrusaun ka Reabilitasaun EBF 1, 2 Mauboque lokaliza iha suku Dato, Liquisa Vila Munisipiu Liquisa neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (LV22)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun EBF 1,2 Mauboque
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu konstrusaun klase *Cdl* (figura iha sorin) iha terenu lao ona too iha servisu monta bekisting ba iha item *lintel beam* no mos iha item *column* nian balu neebe seidauk halo pengecoran.	

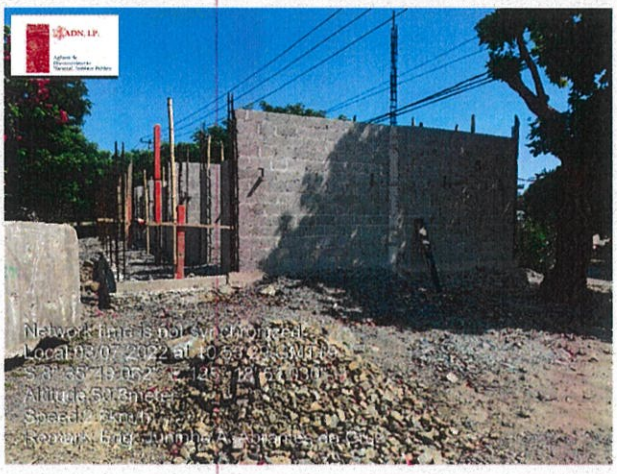Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Iha fali konstrusaun klase *C* (figura iha sorin) trabaliador grupu sira foin atu hahuu monta tulangan no kesi begel ba iha item *lintel beam* nian no mos ba item *column* nian monta hotu ona bekisting no hein atu cor.	

#ANEXU D - (LV22)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EBF MAUBOQUE

GRUPU KOMUNITARIU

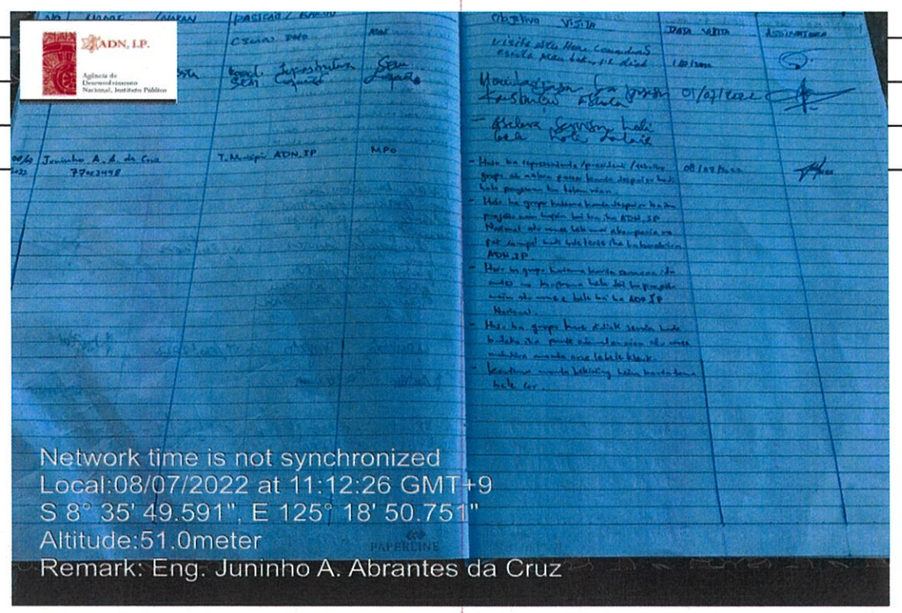No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/07/2022	Dato, Liquisa Vila	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA BÁSICA FILIAL MAUBOQUE
FATIN PROJEITO : DATO, LIQUICA
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (LV 22)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.37%	$ -	0.00%					$ 1,537.50	1.37%
II	PROVISIONAL SUM FOR DEMOLITION	DM/3		US$	$ 590.80	$ -	0.00%	$ -	0.00%					$ -	0.00%
III	CLASSROOM BUILDING C	C/39	(i)	US$	$ 48,285.30	$ 6,717.93	5.97%	$ 646.65	0.57%					$ 7,364.58	6.54%
IV	CLASSROOM BUILDING Cdl	C/36	(i)	US$	$ 43,049.04	$ 5,558.68	4.94%	$ 1,115.74	0.99%					$ 6,674.42	5.93%
V	PROVISIONAL SUM FOR SITE WORKS	SW/27	(i)	US$	$ 8,189.87	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 103,190.01	$ 13,814.11	12.28%	$ 1,762.39	1.57%					$ 15,576.50	13.84%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 112,530.01	$ 13,814.11	12.28%	$ 1,762.39	1.57%					$ 15,576.50	13.84%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edifício Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edifício Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (LV23)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBC 1,2,3 Liquica
Kompania :
No. kontratu :

Data Inspesaun : 12 Julho 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 32. 592''**, Latetude : .....

End Point : Long : **E 125º 19' 53. 005''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu Foun MEJD PKRIE ba Konstrusaun ka Reabilitasaun EBC 1, 2, 3 Liquica lokaliza iha suku Dato, Liquisa Vila munisipiu Liquisa, neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (LV23)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBC 1,2,3 Liquica
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tuir autoridade sira iha terenu no trabaliador grupu balu neebe servisu mesak iha neba katak servisu lao tarde ituan no semana hirak nee trabaliador sira instala deit bekisting ba item betaun *column* nian.	

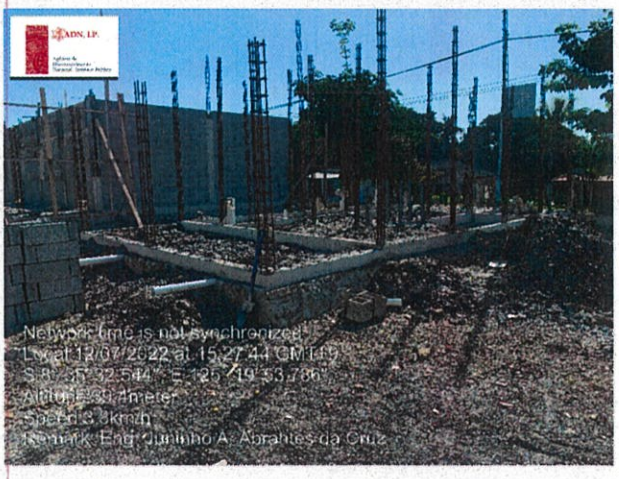Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu *Tb* (figura iha sorin) mos nia progresu seidauk lao desde ekipa tekniku sira ba halo inspesaun, tekniku ADN, IP foo ona instrusaun atu wainhira halo pemadatan tenki hasai fatuk boot sira.	

#ANEXU D - (LV23)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EBC 1,2,3 LIQUICA

GRUPU KOMUNITARIU

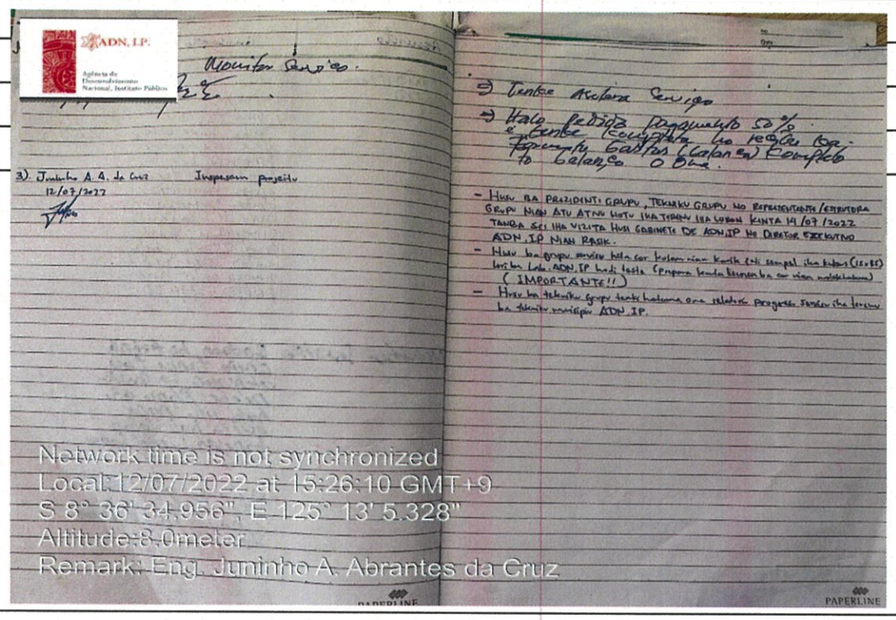No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12/07/2022	Dato, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA BASICA CENTRAL LIQUICA
FATIN PROJEITO : DATO, LIQUICA
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (LV23)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.55%	$ -	0.00%					$ 1,537.50	1.55%
II	CLASSROOM BUILDING C	C/39	(i)	US$	$ 45,885.30	$ 7,646.21	7.69%	$ 740.11	0.74%					$ 8,386.31	8.43%
III	TOILET BUILDING Tb	C/39	(i)	US$	$ 23,742.51	$ 3,096.78	3.11%	$ -	0.00%					$ 3,096.78	3.11%
IV	PROVISIONAL SUM FOR SITE WORKS	SW/27	(i)	US$	$ 17,413.23	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 90,116.04	$ 12,280.48	12.35%	$ 740.11	0.74%					$ 13,020.59	13.09%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 99,456.04	$ 12,280.48	12.35%	$ 740.11	0.74%					$ 13,020.59	13.09%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edifício Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Francisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edifício Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (LV24)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EPE Loidahar
Kompania :
No. kontratu :

Data Inspesaun : 26 Julho 2022

Fatin Inspesaun : Loidahar - Liquica Vila, Liquica

Koordinadas :

Start Point : Long : **S 8º 35' 32. 592''**, Latetude : .....


End Point : Long : **E 125º 19' 53. 005''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antonia de Fatima Morais Soares

3. .....

4. .....

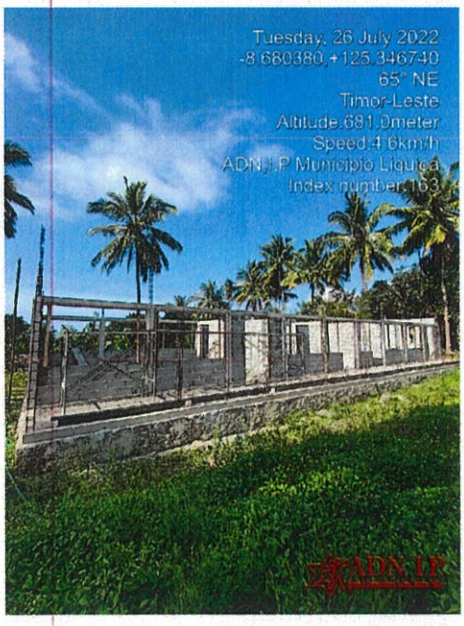Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu Foun MEJD PKRIE ba Konstrusaun ka Reabilitasaun EPE Loidahar lokaliza iha suku Loidahar, Liquisa Vila munisipiu Liquisa, neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (LV24)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EPE Loidahar
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, I.P Munisipiu Liquisa hato'o ona ba grupu konaba servisu betaun tenki foti sampel, ho maneira halo *kubus* 15x15 (6 buah) rua ba 7 dias, rua ba 14 dias no rua ba 28 dias. Grupu sei lori sampel mai hatama iha Laboratorium ADN, I.P hodi halo teste no hetan rezultadu.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku ADN, I.P. mos husu ona grupo atu hatama relatoriu progresu servisu iha terenu tuir progresu neebe grupu atinji ona.	

#ANEXU D - (LV24)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EPE LOIDAHAR

GRUPU KOMUNITARIU

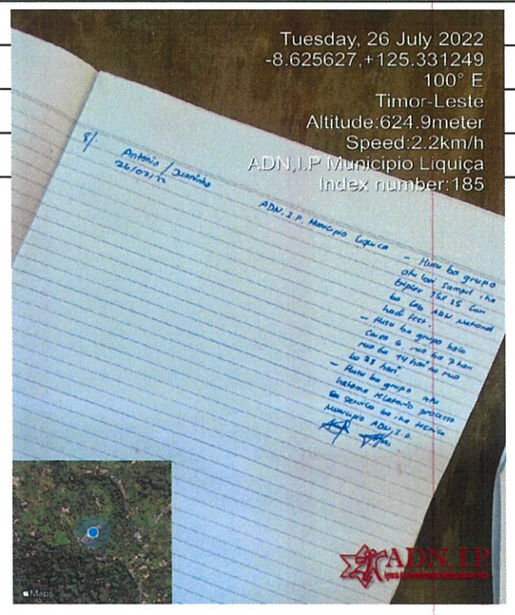No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/07/2022	Loidahar, Liquisa Vila	Juninho António Abrantes da Cruz/ Antonia de Fatima Morais Soares	Tekniku ADN, IP Liquisa	1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA PRE-ESCOLAR LOIDAHAR
FATIN PROJEITO : LOIDAHAR, LIQUICA
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

#ANEKSU C2 - (LV24)						PROGRESU IHA TERENU						VERIFIED BY A D N , I P					
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	FULAN KOTUK	%	FULAN NEE	%	TOTAL	%	PREVIOUS BILLING	BILLED %	THIS BILLING	BILLED %	TOTAL BILLED	BILLED %
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.93%	$ -	0.00%	$ 1,537.50	1.93%						
II	CLASSROOM BUILDING C2	C2/47	(i)	US$	$ 59,253.63	$ 6,196.53	7.77%	$ 389.72	0.49%	$ 6,586.24	8.26%						
III	PROVISIONAL SUM FOR SITE WORKS	SW/19	(i)	US$	$ 8,067.00		0.00%	$ -	0.00%	$ -	0.00%						
A	CONSTRUCTION COST			US$	$ 70,395.63	$ 7,734.03	9.70%	$ 389.72	0.49%	$ 8,123.74	10.19%						
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%	$ -	0.00%						
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%						
D	GRAND TOTAL			US$	$ 79,735.63	$ 7,734.03	9.70%	$ 389.72	0.49%	$ 8,123.74	10.19%						

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edifício Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edifício Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (LV25)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Laclolema
Kompania :
No. kontratu :

Data Inspesaun : 11 Julho 2022

Fatin Inspesaun : Dato – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : **S 8º 37' 11. 666''**, Latetude : .....

End Point : Long : **E 125º 18' 55. 306''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu MEJD PKRIE ba Konstrusaun ka Reabilitasaun EBF 1, 2 Laclolema lokaliza iha suku Dato, Liquisa Vila munisipiu Liquisa, neebe kaer husi servisu grupu komunitariu.	

#ANEXU C1 – (LV25)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Laclolema
Kompania :
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu konstrusaun klase *Cb* (figura iha sorin) ba projeitu refere grupu halao ona too iha servisu hada batako tuir design (390 x 190 mm) ho ninia *perbandingan pasangan* 1:4. Grupu mos finaliza ona servisu cor ba iha *ground beam* nian.	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Tekniku ADN, IP foo ona instrusaun ba iha ekipa grupu nian atu hare didiak no tau atensaun ba servisu hada batako nian tanba iha parte balu ladun diak (la rapi/kleuk). No foo ona instrusaun ba Presidente Grupu konaba prezensa tekniku grupu neebe la ativa iha terenu atu hasoru tekniku ADN, IP sira.	

#ANEXU D - (LV25)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EBF 1,2 LACLOLEMA

GRUPU KOMUNITARIU

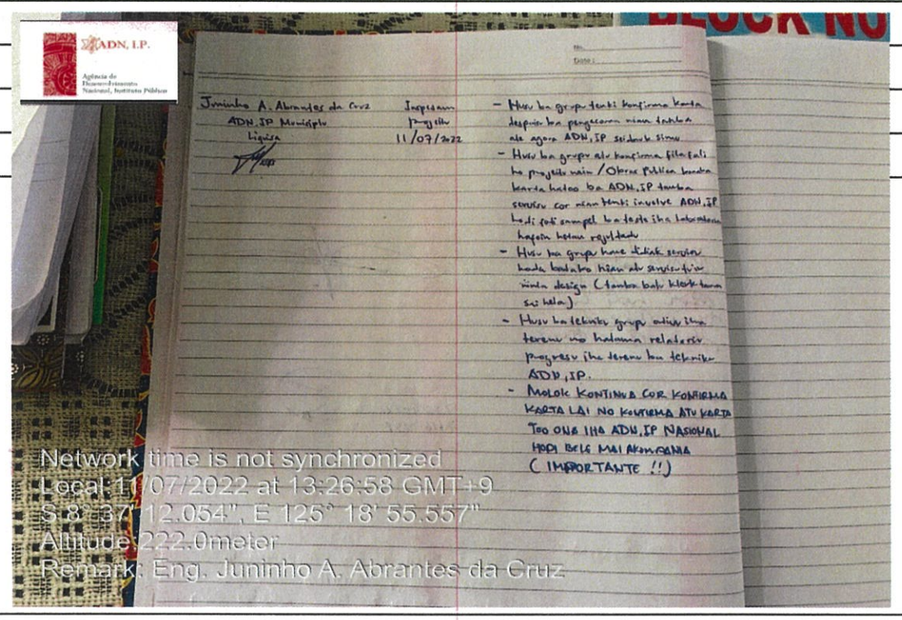No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	11/07/2022	Dato, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA BASICA FILIAL LACLOLEMA
FATIN PROJEITO : DATO, LIQUICA
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

# ANEXU C2 - (LV25)							VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD		PROGRESU IHA TERENU				PREVIOUS BILLING	%	THIS BILLING	%	TOTAL TO DATE	%
							FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$	3,075.00	$ 1,537.50	1.71%	$ -	0.00%					$ 1,537.50	1.71%
II	PROVISIONAL SUM FOR DEMOLITION	DM/3		US$	$	687.20	$ -	0.00%	$ -	0.00%					$ -	0.00%
III	CLASSROOM BUILDING Cb	C/39	(i)	US$	$	67,508.34	$ 7,402.02	8.26%	$ 1,906.13	2.13%					$ 9,308.14	10.38%
IV	PROVISIONAL SUM FOR SITE WORKS	SW/27	(i)	US$	$	9,040.12	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$	80,310.66	$ 8,939.52	9.97%	$ 1,906.13	2.13%					$ 10,845.64	12.10%
B	OVERHEAD			US$	$	6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$	3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$	89,650.66	$ 8,939.52	9.97%	$ 1,906.13	2.13%					$ 10,845.64	12.10%

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edificio Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku, Be'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (LV26)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Tolema
Kompania :
No. kontratu :

Data Inspesaun : 11 Julho 2022

Fatin Inspesaun : Leotela – Liquica Vila, Liquica

Koordinadas :

Start Point : Long : **S 8º 40' 25. 106''**, Latetude : .....

End Point : Long : **E 125º 18' 39. 875''**, Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual


Ekipa tekniku ADN, IP Munisipiu Liquisa halao inspesaun ba projeitu MEJD PKRIE ba Konstrusaun ka Reabilitasaun EBF 1, 2 Tolema lokaliza iha suku Leotela, Liquisa Vila munisipiu Liquisa, neebe kaer husi servisu grupu komunitariu.



#ANEXU C1 – (LV26)

Back-up Data

Naran Projeto : Konstrusaun Foun MEJD PKRIE EBF 1,2 Tolema
Kompania :
No. kontratu :

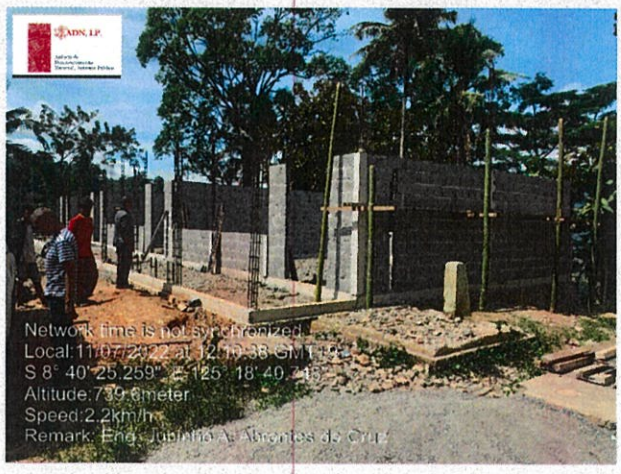Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa foin halao inspesaun iha area refere ba projeitu ida nee tanba ho kestaun dalan neebe perigu iha tempu udan nia laran. Hatoo husi Presidente Grupu nian katak servisu lao diak maibe stock material mai terenu mak tarde ituan tanba asesu dalan dalaruma ladiak.	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu hada pondasi ba iha konstrusaun klase *Ca* nian maka iha aumenta ituan ba volume tanba tuir kondisaun iha terenu la hanesan ho kondisaun iha dezeniu, tan nee tekniku ADN, IP sei konsulta ho tekniku grupu konaba asuntu nee.	

#ANEXU D - (LV26)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : KONSTRUSAUN FOUN MEJD PKRIE EBF 1,2 TOLEMA

GRUPU KOMUNITARIU

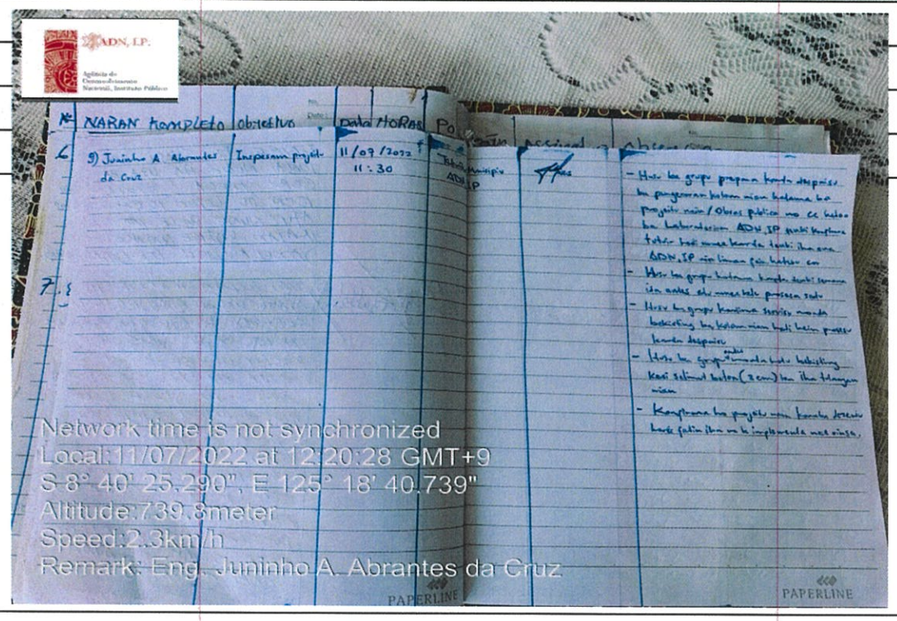No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	11/07/2022	Leotela, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA BASICA FILIAL TOLEMA
FATIN PROJEITO : LEOTELA, LIQUICA VILA
DONO DO PROJEITO : MINISTERÍO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

ANEKSU C2 - (LV26)						PROGRESU IHA TERENU						VERIFIED BY A D N , I P					
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	FULAN KOTUK		FULAN NEE		TOTAL PROGRESU		PREVIOUS BILLING		THIS BILLING		TOTAL BILLED	
						AMOUNT (U$)	%	AMOUNT (U$)	%	AMOUNT (U$)	%	AMOUNT (U$)	%	AMOUNT (U$)	%	AMOUNT (U$)	%
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ -	0.00%	$ 1,537.50	1.74%	$ 1,537.50	1.74%						
II	CLASSROOM BUILDING CA	CA/39	(i)	US$	$ 69,218.33	$ -	0.00%	$ 9,634.72	10.90%	$ 9,634.72	10.90%						
III	PROVISIONAL SUM FOR SITE WORKS	SW/10	(i)	US$	$ 6,773.69	$ -	0.00%	$ -	0.00%	$ -	0.00%						
A	**CONSTRUCTION COST**			**US$**	**$ 79,067.02**	**$ -**	**0.00%**	**$ 11,172.22**	**12.64%**	**$ 11,172.22**	**12.64%**						
B	**OVERHEAD**			**US$**	**$ 6,340.00**	**$ -**	**0.00%**	**$ -**	**0.00%**	**$ -**	**0.00%**						
C	**CONTIGENCY**			**US$**	**$ 3,000.00**	**$ -**	**0.00%**	**$ -**	**0.00%**	**$ -**	**0.00%**						
D	**GRAND TOTAL**			**US$**	**$ 88,407.02**	**$ -**	**0.00%**	**$ 11,172.22**	**12.64%**	**$ 11,172.22**	**12.64%**						

Inspeksaun Husi :

Eng. Juninho António Abrantes da Cruz
Engineru ba Edifício Publiku Agua Saneamento, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edifício Publiku, Re'e e Saneamentu, ADN, I.P.

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P.

#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Data Inspesaun : 12 Julho 2022

Fatin Inspesaun : Maubara - Liquica

Koordinadas :

Start Point : Long : S 8º 36' 33. 682", Latetude : .....

End Point : Long : E 125º 13' 5. 010", Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. .....



3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa nian halao inspesaun ba projeitu MEJD PKRIE – Konstrusaun Foun ESG Classe Paralelo Maubara iha suku Maubara, postu Maubara, munisipiu Liquisa. Neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (MBR19)
Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

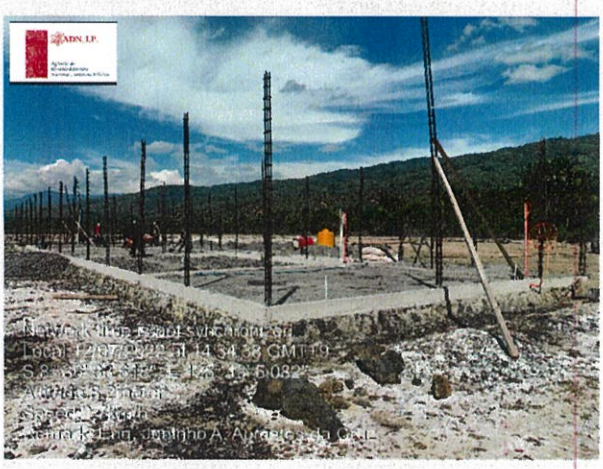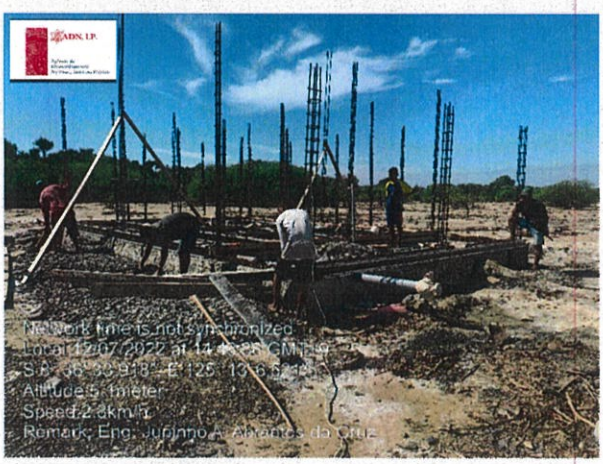Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa grupu finaliza tiha ona servisu cor ba iha *ground beam* ba klase *Ca* (figura iha sorin) no hatoo husi grupu katak ekipa husi Obras Nasional foti ona sampel, maibe ekipa Laboratorium ADN, IP mak la konsege partisipa tanba karta despaisu la iha.	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ba servisu *Tb* (figura iha sorin) trabaliador grupu sira monta hela bekisiting ba iha tulangan *ground beam* ninian no tekniku ADN, IP foo ona instrusaun atu mantein uja selimut beton (3 cm).	

#ANEXU C1 – (MBR19)

Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

Data Inspesaun : 25 Julho 2022

Fatin Inspesaun : Maubara - Liquica

Koordinadas :

Start Point : Long : S 8º 36' 33. 682", Latetude : .....


End Point : Long : E 125º 13' 5. 010", Latetude : .....

Naran Inspector : 1. Juninho António Abrantes da Cruz

2. Antonia de Fatima Morais Soares



3. .....

4. .....

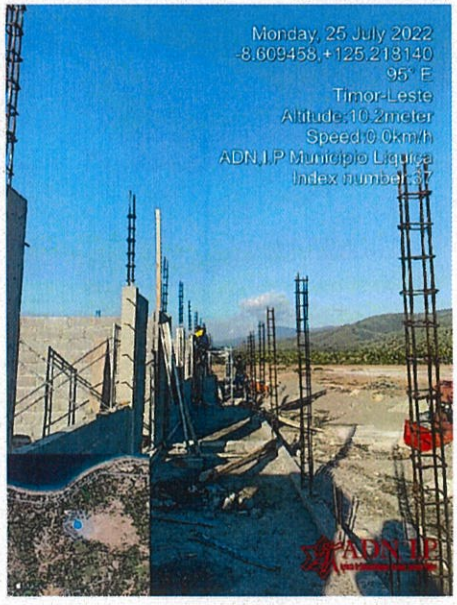Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku ADN, IP Munisipiu Liquisa nian halao inspesaun ba projeitu MEJD PKRIE – Konstrusaun Foun ESG Classe Paralelo Maubara iha suku Maubara, postu Maubara, munisipiu Liquisa. Neebe kaer husi servisu Grupu Komunitariu.	

#ANEXU C1 – (MBR19)
Back-up Data

Naran Projeto : **Konstrusaun Foun ESG Classe Paralelo Maubara**
Kompania :
No. kontratu :

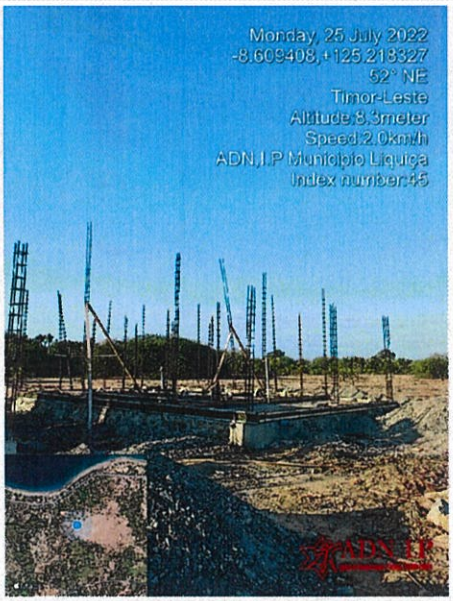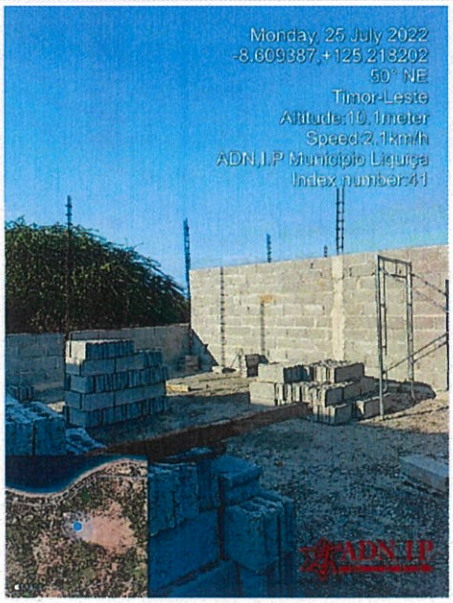Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Wainhira ekipa tekniku ADN, I.P halao inspesaun iha terenu hato'o ona ba grupo molok atu halo pemadatan ou atu uja kerikil ba servisu cor nian tenki fase uluk lai tanba udan no loron hoban kleur. No mos antes atu cor rega uluk lai rai refere.	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Ekipa tekniku hato'o mos ba grupu wainhira servisu cor ruma karik wainhira ekipa Laboratorium ADN, I.P la konsenge marka prezensa grupu bele foti deit sampel beton iha *kubus* 15 x 15 (6 buah) hodi ba halo teste iha Laboratoriun ADN, I.P.	

#ANEXU D - (MBR 19)



MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Konstrusaun Foun ESG Classe Paralelo Maubara

Grupu Komunitariu

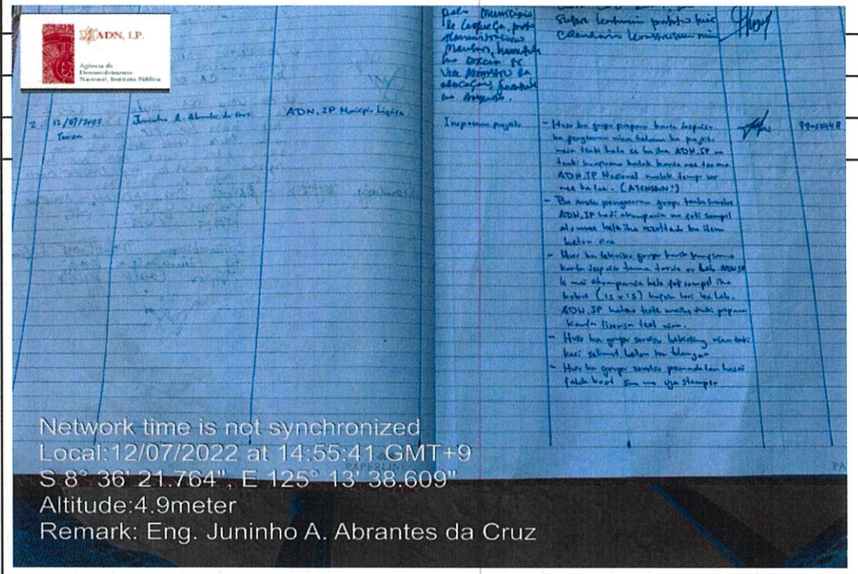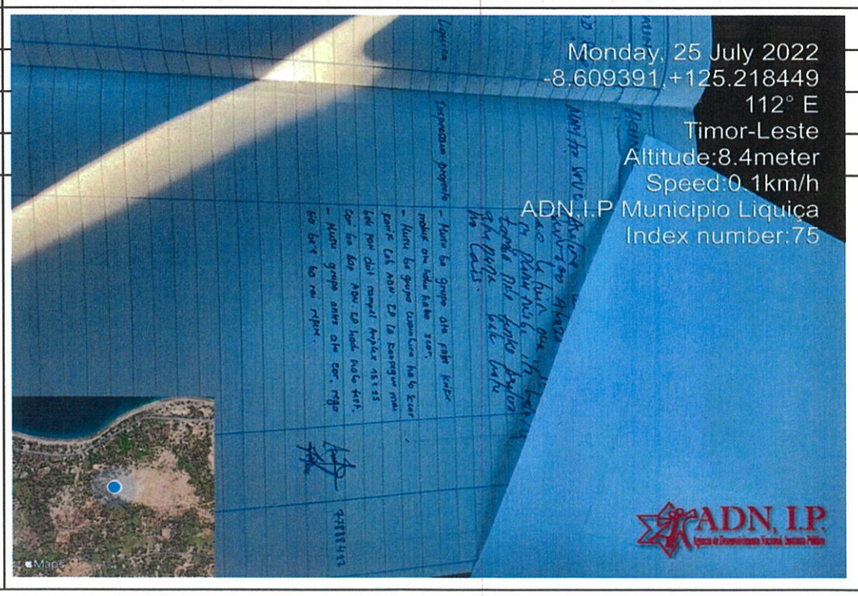No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	12/07/2022	Maubara, Liquisa	Juninho António Abrantes da Cruz	Tekniku ADN, IP Liquisa	1 2 3 4 5		
II	25/07/202	Maubara, Liquisa	Juninho António Abrantes da Cruz/ Antonia de Fatima Morais Soares	Tekniku ADN, IP Liquica	1 2 3 4 5		

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

TÍTULO DO PROJEITO : NOVA CONSTRUÇÃO ESCOLA SECUNDARIA GERAL PARALELO MAUBARA
FATIN PROJEITO : VAVIQUINA, MAUBARA
DONO DO PROJEITO : MINISTÉRIO DA EDUCAÇÃO JUVENTUDE E DESPORTO

MAIN SUMMARY

ANEXU C2 - (MBR 19)						VERIFIED BY A D N , I P									
NO	WORK DESCRIPTION	PAGE NO			AMOUNT USD	PROGRESU IHA TERENU				PREVIOUS BILLING	BILLED %	THIS BILLING	BILLED %	TOTAL TO DATE	BILLED %
						FULAN KOTUK	%	FULAN NEE	%						
I	PRELIMINARIES	PP/3		US$	$ 3,075.00	$ 1,537.50	1.09%	$ -	0.00%					$ 1,537.50	1.09%
III	CLASSROOM BUILDING CA	CA/39	(i)	US$	$ 67,673.42	$ 6,959.36	4.91%	$ 2,921.55	2.06%					$ 9,880.91	6.98%
IV	TOILET BUILDING Tb	TB/39	(i)	US$	$ 31,055.68	$ 3,857.68	2.72%	$ -	0.00%					$ 3,857.68	2.72%
V	PROVISIONAL SUM FOR SITE WORKS	SW/28	(i)	US$	$ 30,516.12	$ -	0.00%	$ -	0.00%					$ -	0.00%
A	CONSTRUCTION COST			US$	$ 132,320.22	$ 12,354.53	8.72%	$ 2,921.55	2.06%					$ 15,276.08	10.78%
B	OVERHEAD			US$	$ 6,340.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
C	CONTIGENCY			US$	$ 3,000.00	$ -	0.00%	$ -	0.00%					$ -	0.00%
D	GRAND TOTAL			US$	$ 141,660.22	$ 12,354.53	8.72%	$ 2,921.55	2.06%					$ 15,276.08	10.78%

Inspeksaun Husi :

Eng. Juninho Antônio Abrantes da Cruz
Engineru ba Edifisiu Publiku Agua Saneamentu, ADN, I.P

Verifika Husi :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Engineriu ba Projeitu Edificio Publiku Agua Saneamentu, ADN, I.P

Sertifika Husi :

Eng. Emerenciana da Costa Maia Freitas
Koordenadora UCVQ, ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Juninho António Abrantes da Cruz

Municipio MUNICIPIO LIQUICA NO POSTOS

2022

Municipio / Posto	No.	Naran Projeto	Naran Kompanha	No. Contrato	Kategoria	Dono do Projeto	Action	JULHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
Liquica Vila (LV)	1	Road and Bridge Maintenance Section : Tibar - Liquica - Maubara (A03) & Carimbala - Loes (A03) Municipality Liquica /162	Naroman Mosu Dadaun Unip. Lda	MPW-W190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	2	R4D Rural Road Periodic Maintenance Aibenu - Anamanu Chainage 0+000 - 4+300 Rutine Maintenance Dato - Liquica - Loidahar Chainage 0+000 - 12+300 Municipality Liquica	Nheu	MPW-W-RFQ-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	3	Rural Roads Periodic Guraba - Lukulai Chainage 0+000 & Metagou - Aibenu Chainage 0+000 - 7+600 Rutine Maintenance Taltabi - Kutulau Chainage 0+000 - 1+700 Municipality Liquica (162)	Goubaru Unip Lda	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	4	R4D Rural Road Rehabilitation Bebadiri - Lebokakalo Chainage 0+000 - 5+000 Liquica Municipality	15 Raethi Unip. Lda	RT/034/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	5	R4D Rural Road Spot Improvement Dato-Loidahar Chainage 0+000-12+300)	Lisgueli Oan Unip.Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	6	R4D Rural Road Spot Improvement Aibenu-Anamanu Chainage 5+000-10+000)	Cailu Unip.Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	7	R4D Rural Road Spot Improvement Aibenu-Anamanu-Leorema Chainage 0+000-5+000)	Vicaoreau Unip.Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	8	R4D Rural Road Spot Improvement Metagou-Aibenu Chainage 0+000-7+600)	Metalika Unipensoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	9	R4D Rural Road Spot Improvement Taltabi - Kutulau Chainage 0+000-1+700)	Prudência Construction Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	10	Manutenusun Kanais Irrigasaun Fasilara - Liquica	Basir Lema Unip.Lda		LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	
							Actual																																	
	11	R4D Rural Road Spot Improvement Berlaksuidu-Laberlaka Chainage 0+000-2+500)	Goubaru Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	12	R4D Rural Road Spot Improvement Berlaksuidu-Laberlaka Chainage 2+500-5+400)	Clarisdade Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	13	R4D Rural Road Spot Improvement Guraba - Lukulai Chainage 0+000-2+000)	Cruelcki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	14	Road Maintenance Section Tibar - Liquica - Maubara - Carimbala - Loes (A03)	Chantel Chander Unip.Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	15				LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	16	Projetu Konstrusaun Foun ESG Publico 01-Liquica	Roman Furak Unip.Lda	NCB/16/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																On-going
							Actual																																
	17	For Roads Maintenance Section Tibar-Liquica-Maubara-Carimabala-Loes (A03)	Chanel Chander Unip.Lda	MPW-W210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	18	MEJD PKRIE EBF Mauboque	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going
	19	MEJD PKRIE EBC 1,2,3 Liquica	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going
	20	MEJD PKRIE EPE Loidahar	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going
	21	MEJD PKRIE EBF 1,2 Lacilolema	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going
	22	MEJD PKRIE EBF 1,2 Tolensa	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going
	23	MEJD PKRIE EBF 1,2 Lacolai	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going
Maubara (MBR)	1	Addt. Poste liga Maubara	Fu Unip,Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	2	Road and Drainage Rehabilitation Project Emergency Road at Tibalau and Karimbala Liquica Municipality Liquica	Montana Diak, Unipensoal, Lda	SSS/126/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	3	Konstrusaun ESTV Lissadila Maubara-Liquisa (CA + CB)	Alenu Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																Pagamentu Seidauk 100%	
	4	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/077/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	5	R4D Rural Road Maintenance Berlaksuidu - Laberlaka Chainage 0+000 - 5+400 Numuleta - Darulema Chainage 0+000-1+600 Vaviquinia-Maubaralau Chainage 0+000-12+500	Lulisea Unip.Lda	MPW-W-190098	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	6	R4D Rural Road Spot Improvement Barlau (Vaviquinia - Maubaralau Chainage 0+000-4+200)	Nheu Unip.Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	7	R4D Rural Road Spot Improvement Numuleta - Darulema Chainage 0+000-2+000) Liquica Municipality	Rito-Pu Unip.Lda	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	8	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 4+800-9+600)	Malibo Unip.Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	9	R4D Rural Road Spot Improvement Malaisera-Lissadila Chainage 0+000-4+800)	Murak Unip.Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	10	R4D Rural Road Spot Improvement Barlau (Vaviquinia - Maubaralau Chainage 8+400-12+500)	Meta Loe Cruz Bau Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	11	R4D Rural Road Spot Improvement Samarapo-Oisu Chainage 0+000-2+000)	Nuzico Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	12	R4D Rural Road Spot Improvement Barlau (Vaviquinia - Maubaralau Chainage 4+200-8+400)	Lulisea Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	13	MEJD PKRIE EBF Gariuna	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
	14	MEJD PKRIE EBF 1,2 Tapo Manubulu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
	15	MEJD PKRIE ESG-Paralelo Maubara	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
Baurtete (BZT)	1	Rural Road Rehabilitation Metagou Baurtete 0+000 - 3+000 & Periodic Maintenance Maumeta - Metagou Sta. 0+000 - 7+000 Municipality Liquica (162)	Basir Lema	MPW-W-190097	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	2	Konstrusaun ESTV Maumeta - Liquisa (CA + CB)	Vida Disk Unip. Lda	CID/600/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																PHO	
	3	R4D Rural Road Periodic Maintenance Libaloa - Fahilebo Chainage 0+000 - 7+000 & Fahilebo - Fatumasi Chainage 0+000 - 2+300 Routine Maintenance Fahilebo Bucumera Chainage 0+000 - 6+500 Municipality Liquica	Lep Laco Dato	MPW-W-190111	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	4	Konstrusaun Moralha Foun Matadoro Tibar	Manoko Unip. Lda	RDTL-MAP-PO2019/19726	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	
							Actual																																Paradu	
	5	Konstrusaun Foun EBF Hotugaru Baurtete, Liquica (162)	Milcha Unip Lda	(RFQ/190229-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																Paradu	
	6	Hamos Tangki Estasaun Tratamento Agua Residuais Iha Tibar / 162	Culoco Unipensoal Lda	Contract No.MOP-W-190184	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																Pagamentu Seidauk 100%	
	7	New Water Supply of Bairos PNTL Liquica	Holuli Unipensoal, Lda	SSS/054/MI-2019	FI	MINISTERIO DO INTERIOR	Plan																																	
							Actual																																FHO	
	8	Konstrusaun Armagen Foun Matadouro (Bem Servisu)	Nanualobu Unip. Lda.	MAP-F02019/19532	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	
							Actual																																FHO	
	9	New Construction of Laboratory for Covid 19 in Liquica Ministery of Health, Timor Leste	Queson SQ Unipensoal Lda	MS-DNA-RBIC-20-178	LM	MINISTERIO SAUDE	Plan																																	
							Actual																																Pagamentu Seidauk 100%	
	10	New construction of isolation for covid 19 in chi liquica, Timor Leste	Sminu	MS-DNA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																																	
							Actual																																PHO	
	11	Kanalizasaun Be Mos ho Sistema Orawitasaun Iha Aipelo-Liquisa	Tinocya	022LM/RDTL/MPIE/AND/DA-RFQ/IX/2019/IEIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																	
							Actual																																PHO	
	12	Emergency Project For Tibar River	Sali-Magu Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	13	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 0+000-3+000)	Hatumeta Oan Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	14	R4D Rural Road Spot Improvement Fahilebo-Fatumasi Chainage 0+000-2+300) Liquica Municipality	Hatumeta Oan Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	15	R4D Rural Road Spot Improvement Libaloa- Fahilebo Chainage 0+000-7+000) Liquica Municipality	Hatubo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	16	Routine Maintenance Maumeta-Metagou-Baurtete Chainage 0+000-10+000	Cruelcki Bercoli Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	17	R4D Rural Road Spot Improvement Fahilebo-Bucumera Chainage 3+000-6+500) Liquica Municipality	TM.Caileba Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	
	18	New Construction of Fence Around for Isolation Covid-19 in Liquica Maumeta	Biamali Unip. Lda.	RDTL-MS-C19-DNA-DC-21-233	LM	MINISTERIO SAUDE	Plan																																	
							Actual																																On-going	
	19	Supply and Installation Connection for Isolation and Laboratorium Building Maumeta Liquica	Zyc Unip. Lda.	RDTL-MS-C19-DNA-DC-21-228	LM	MINISTERIO SAUDE	Plan																																	
							Actual																																On-going	
	20	Projetu Konstrusaun Foun ESTV Leorema - Liquica	U-Rama Unip. Lda.	NCB/15/MEJD/DNA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
	21	MEJD PKRIE EPE Baura	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
	22	MEJD PKRIE EPE Ermeta	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
	23	MEJD PKRIE EPE Cassait	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
	24	MEJD PKRIE ESG-Paralelo Bogoro	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																	
							Actual																																On-going	
		TOTAL PROJETO ON-GOING																																					

Note:

Plano Periode Inspesaun iha terenu — Relatoriu avaliasaun mensal iha Dili — Inspesaun Pagamentu Anual iha terenu — Implementasaun Plano Periode inspesaun iha terenu

Prepara Husi :

(Eng Juninho António Abrantes da Cruz)
Eng. ba Edifício Publico Agua e Saneamento Municipio Liquica
ADN, I.P

Sertifika Husi :

(Eng Emerenciano da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN I.P

Aprova Husi :

(Eng Januario Maia Gabriel)
Adjunto Director Executivo ADN.I.P

MINISTERIO DO PLANO E ORDENAMENTO TERRITORIAL

ADN, I.P.

Naran Eng. **Juninho António Abrantes da Cruz**

PLANU INSPESAUN

2022

JULHO

Municipio / Poste	No.	Naran Projeto	Naran Kompañia	No. Contrato	Kategoria	Dono do Projeto	Artim	1	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
MUNICIPIO LIQUICA NO POSTOS																																						
Liquica Vila (LV)	1	Road and Bridge Maintenance Section Tibar - Liquica - Maubara (A03) & Cutrubula - Lore (A03) Municipality Liquica /162	Nuraman Mese Dadaun Unip. Lda	MPW-W/190250	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	2	R4D Rural Road Periodic Maintenance Aileu - Aruanura Chainage 0+000 - 4+390 Rotine Maintenanse Dato - Liquica - Loidohor Chainage 0+000 - 12+300 Municipality Liquica	Nhm	MPW-W-82Q-190093	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	3	Rural Roads Periodic Gravins - Lahohi Chainage 0+000 & Metagou - Aileau Chainage 0+000 - 7+600 Rotine Maintenanse Tahobi - Hatubo Chainage 0+000 - 1+700 Municipality Liquica (162)	Gruhara Unip Lda	MPW-W-190096	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	4	R4D Rural Road Rehabilitation Bobodai - Lahohohi Chainage 0+000 - 5+000 Liquica Municipality	15 Rushi Unip. Lda	RFQ/49/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	5	R4D Rural Road Spot Improvement Date-Loidohor Chainage 0+000-12+300)	Loquili Con Unip Lda	MPW-W-210150	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	6	R4D Rural Road Spot Improvement Aileau-Aruanura Chainage 5+000-10+000)	Caila Unip Lda	MPW-W-210154	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	7	R4D Rural Road Spot Improvement Aileau-Aruanura-Lavenue Chainage 0+000-5+000)	Viaurunu Unip.Lda	MPW-W-210153	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	8	R4D Rural Road Spot Improvement Metagou-Aileau Chainage 0+000-7+600)	Metallka Unipessoal, Lda	MPW-W-210151	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	9	R4D Rural Road Spot Improvement Tahobi - Hatubo Chainage 0+000-1+700)	Fruhenia Construction Unip Lda	MPW-W-210155	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	10	Maintenanse Kanso Irrigasaun Faularu - Liquica	Barar Laura Unip Lda		LM	MINISTERIO AGRICULTURA E PESCAS	Plan																															
							Atual																															
	11	R4D Rural Road Spot Improvement Bwikhoito-Lahohito Chainage 0+000-2+500)	Gruhara Unip Lda	MPW-W-210162	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	12	R4D Rural Road Spot Improvement Bwikhoito-Lahohito Chainage 2+500-5+600)	Cheimbi Unip Lda			MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	13	R4D Rural Road Spot Improvement Gunuba- Lukuloi Chainage 0+000-2+000)	Cmaloki Dumii Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	14	Road Maintenance Section Tibar - Liquica - Maubara - Cutrubula - Lore (A03)	Chanul Chander Unip Lda	MPW-W-210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	15				LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Atual																															
	16	Projeitu Konstruksaun Foun EISO Publiku 01-Liquica	Roman Fumi Unip Lda	NCB 16/MEJD/ENA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	17	For Roads Maintenance Section Tibar Liquica-Maubara-Cutrubula-Lore (A03)	Chanul Chander Unip Lda	MPW-W/210202	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	18	MEJD PKRE ESF Mauboque	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	19	MEJD PKRE EBC 1,2,3 Liquica	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	20	MEJD PKRE EPE Loidohor	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	21	MEJD PKRE ESF 1,2 Lactoleso	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	22	MEJD PKRE ESF 1,2 Tolreu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	23	MEJD PKRE ESF 1,2 Loculu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
Maubara (MBR)	1	ASA Poste Kps Maubara	Fa Unip.Lda		FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	2	Road and Drainage Rehabilitation Project Emergency Road at Tibubu and Kurimbula Liquica Municipality Liquica	Mesteva Diak, Unipessoal, Lda	SSS/126/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	3	Konstruksaun ESTV Limbilu Maubara-Liquica (CA + CB)	Alesi Unip. Lda	CED/008/PDIM/AM-LIQ/VIII/2019/03	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															Pagamentu finalmik 100%
							Atual																															
	4	RNRIP / Road Link No. A01 - 03 - Upgrading and Maintenance of Maubara - Kurimbula Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.0)and Atabae - Motu Ain Road (Km 55.3 to Km 114.2)	CBM Construction Co. Ltd Jv Chongqing Roads Engineering	ICB/07/MPWTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	5	R4D Rural Road Maintenance Bwikhoito - Lahohito Chainage 0+000 - 5+400 Hawaina - Darabasa Chainage 0+000-3+600 Verisqueia-Maubaralau Chainage 0+000-12+500	Lafiana Unip.Lda	MPW-W-190099	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	6	R4D Rural Road Spot Improvement Burlau (Verisqueia - Maubaralau Chainage 0+000-4+200)	Nhua Unip Lda	MPW-W-210164	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	7	R4D Rural Road Spot Improvement Nunduta - Darabasa Chainage 0+000-2+000) Liquica Municipality	Rhu-Fu Unip.Lda	MPW-W-210146	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	8	R4D Rural Road Spot Improvement Maluleo-Limalda Chainage 4+800-5+600)	Maliho Unip.Lda	MPW-W-210156	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	9	R4D Rural Road Spot Improvement Maluleo-Limalda Chainage 0+000-4+800)	Munik Unip.Lda	MPW-W-210157	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	10	R4D Rural Road Spot Improvement Burlau (Verisqueia - Maubaralau Chainage 8+400-12+500)	Mota Lee Cruz Boa Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	11	R4D Rural Road Spot Improvement Somarapo-Ilimo Chainage 0+000-2+000)	Nonico Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	12	R4D Rural Road Spot Improvement Burlau (Verisqueia - Maubaralau Chainage 4+200-8+400)	Lufiana Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	13	MEJD PKRE ESF Gariuu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	14	MEJD PKRE ESF 1,2 Tapo Maubaralu	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	15	MEJD PKRE ESO Paraiso Maubara	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
Bazartete (BZT)	1	Rural Road Rehabilitation Metagou Bazartete 0+000 - 3+000 & Periodic Maintenance Maoneta - Metagou Sta. 0+000 - 7+000 Municipality Liquica (162)	Bunir Lanu	MPW-W-190097	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	2	Konstruksaun ESTV Maoneta - Liquica (CA + CB)	Vida Diak Unip. Lda	CED/009/PDIM/AM-LIQ/VIII/2019/02	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															FIIO
							Atual																															
	3	R4D Rural Road Periodic Maintenance Liburlau - Faluleo Chainage 0+000 - 7+000 & Faluleo - Futunusi Chainage 0+000 - 2+300 Rotine Maintenanse Faluleo Bazartete Chainage 0+000 - 6+500 Municipality Liquica	Lay Laco Dato	MPW-W-190111	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	4	Konstruksaun Moniha Foun Matadoro Tibar	Maneko Unip. Lda	RFIL-MAP-PO2019.19726	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																															Parado
							Atual																															
	5	Konstruksaun Foun EBF Bobagou Bazartete, Liquica (162)	Mihiba Unip Lda	(RFQ 19/029-Q-R)	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															Parado
							Atual																															
	6	Kanoo Tanghi Entasan Tratamentu Agua Reziduais Eco Tibar / 162	Cubcus Unipessoal Lda	Contract No.MOP-W-190054	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Pagamentu finalmik 100%
							Atual																															
	7	New Water Supply of Bairro FHTL Liquica	Hohiki Unipessoal, Lda	SSS/054/8-2019	FI	MINISTERIO DO INTERIOR	Plan																															FIIO
							Atual																															
	8	Konstruksaun Atenqeru Foun Matadouro (Bem Servisu)	Nemaitebu Unip. Lda	MAP-PO2019.19532	LM	MINISTERIO AGRICULTURA E PESCAS	Plan																															FIIO
							Atual																															
	9	New Construction of Laboratory for Covid 19 in Liquica Ministray of Health, Timor Leste	Quanco SQ Unipessoal Lda	MS-ENA-RISE-20-178	LM	MINISTERIO SAUDE	Plan																															Pagamentu finalmik 100%
							Atual																															
	10	New construction of isolation for covid 19 in eha Equica, Timor Leste	Tmsins	MS-ENA-NCB-20-163	LM	MINISTERIO SAUDE	Plan																															FIIO
							Atual																															
	11	Konslimasaun Ba Mos ho Sistema Gravitasaun Ba Aipelo Liquica	Tinaqya	RFIL-MOP/LMPB/ANSEDA-RFQ/DO2019/SEPFICO-DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																															PIIO
							Atual																															
	12	Emergency Project For Tibar River	Safi-Mapa Unip.Lda	RT/067/MOP-2021	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	13	R4D Rural Road Spot Improvement Faluleo-Bazarete Chainage 6+000-3+000)	Hanaeta Oan Unip.Lda	MPW-W-210159	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	14	R4D Rural Road Spot Improvement Faluleo-Futunusi Chainage 0+000-2+300) Liquica Municipality	Hatoeta Oan Unip.Lda	MPW-W-210142	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	15	R4D Rural Road Spot Improvement Liburlau- Faluleo Chainage 0+000-7+000) Liquica Municipality	Hatuleo Unip.Lda	MPW-W-210144	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	16	Erosion Maintenance Maoneta-Metagou Bazartete Chainage 0+020-10+000	Cmaloki Dumii Unip.Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	17	R4D Road Road Spot Improvement Faluleo-Bazarete Chainage 3+000-6+500) Liquica Municipality	TM Culeho Unip Lda		LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Atual																															
	18	New Construction of Fence Around for Isolation Covid-19 in Liquica Maoneta	Rumdi Unip. Lda.	RFIL-MS-C19-ENA-DC-21-233	LM	MINISTERIO SAUDE	Plan																															On-going
							Atual																															
	19	Supply and Installation Connection for Isolation and Laboratorium Building Maoneta Liquica	Zyc Unip. Lda.	RFIL-MS-C19-ENA-DC-21-228	LM	MINISTERIO SAUDE	Plan																															On-going
							Atual																															
	20	Projeitu Konstruksaun Foun ESTV Lacoma - Liquica	U-Rama Unip. Lda	NCB 15/MEJD/ENA/2021	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	21	MEJD PKRE EPE Buara	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	22	MEJD PKRE EPE Emeta	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	23	MEJD PKRE EPE Cmasi	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
	24	MEJD PKRE ESO-Paraiso Bugoro	Grupu Komunitariu		LM - TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															On-going
							Atual																															
		TOTAL PROJETO ON-GOING																																					

Note:

Plano Periode inspesaun iha tuirlou | Relatoriu avaliasaun mensal iha ISG | Inspesaun Pagamentu Anual iha tuirlou | Implementasaun Plano Periode inspesaun iha tuirlou

Prepara Husi :

(Eng Juninho António Abrantes da Cruz)
Eng. ba Edifício Publico Agua e Saneamento Municipio Liquica
ADN, I.P

Sertifika Husi :

(Eng Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN I.P

Aprova Husi :

(Eng Jamsuri Jaya Gutterres)
Adjunto Diretor Executivo ADN I.P
