REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público

A.D.N. I.P.
Agência de Desenvolvimento Nacional, Instituto Público

RELATÓRIU MENSÁL IMPLEMENTASAUN PROJETUS MUNISÍPIU BAUCAU

JUNHO 2022



SUMÁRIO

RELATÓRIO

IMPLEMENTASAUN PROJETU INFRAESTRUTURA IHA MUNICIPIO BAUCAU

JUNHO 2022

Prepara Husi :

(Eng. Agustinho Aranda)
Eng. ba Porjecto Edificio Publico Beé no Saneamento Municipio Baucau,ADN,I.P

(Eng. Jacob da Costa Camoês)
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Baucau, ADN, I.P

(Eng. Adonis Julio Fernades)
Eng. ba Projeito ME, ADN, I.P

Verifika Husi :

(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edificio Publiku no Beé Saneamentu, ADN, I.P

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba Projetu Infraestrutura e Irigasaun, ADN, I.P

(Eng. Deolindo de F. Marques)
Chefe Seksaun ba Projetu M.E & ITC, ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :

(Mariano Renato Monteiro da Cruz, S. T, M. Eng)
Director Executivo, ADN, I.P

INDICE

SUMÁRIO 1

INDICE 2

I. INTRODUSAUN 3

1.1 Enkuadramentu Legal 3

1.2 Perfil Municipio Baucau 3

1.3. Lista Projectos 8

II. PROGRESU FISIKU 28

2.1 Progresso Fisiku Kada Fulan 28

III. OBSTÁCLO IHA TERENU 29

3.1 Obstáclo Servisu Iha Terenu 29

IV. REKOMENDASAUN IHA TERENU 30

4.1 Rekomendasaun Servisu Iha Terenu 30

INDICE TABELA

Tabela 1 : Postos Administrativos,Sucos no Aldeias 4

Tabela 1.1 : Forca de Trabalho ADN, I.P Municipio Baucau 6

Tabela 1.2 : Lista Asset ADN,I.P Municipio Baucau 6

Tabela 1.3.1 : Projecto Municipio Baucau Por Fundus Finansiamentos 8

Tabela 1.3.2 : Projecto Municipio Baucau Por Sectores 12

Tabela 1.3.3 : Projecto Municipio Baucau Por Ministerio 20

Tabela 1.4 : Dadus Populasaun Munisipiu Baucau 28

I. INTRODUSAUN.

1.1.Enkuadramentu Legal.

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análize kustu-benefísiu ne'ebe razoável no viavél.

Depois de Dekretu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimentu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projetu sira iha programa Kapital Desenvolvimentu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2. Perfil Municipio Baucau



Mapa 3 hatudu pozisaun jeográfika Autoridade Munisipal Baucau ne'ebé ho luan área hamutuk 1,494 km² ho populasaun 111,694 tuir Sensus 2010. Autoridade Munisipal Baucau iha Posto Administrativo neen (6) ho 59 Sukus no 282 Aldeias hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos,Sucos no Aldeias.

Baguia		Baucau		Laga		Quelicai	
Sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**
Afaloicai	4	Bahu	5	Atelari	10	Abafala	3
Alaua craic	5	Bucoli	6	Libagua	5	Abo	4
Alaua leten	5	Buibau	6	Nunira	5	Afaca	3
Defa-uassi	4	Buruma	4	Saelari	9	Baguia	3
Haeconi	6	Caibada(Uaima)	7	Sagadati	11	Bualale	2
Larisula	7	Gariuai	8	Samalari	7	Guruca	5
Lavateri	5	Samalari	4	Soba	6	lacoliu	3
Osso huna	3	Seiçal	5	Tequi naumata	5	Laisoro Lai de baixo	4
Samalari	4	Trilolo	6	-	-	Laisorolai De cima	3
Uacala	4	Triloca	4	-	-	lelalai	4
-	-	Ualili	10	-	-	Letemumo	5
-	-	-	-	-	-	Macalaco	3
-	-	-	-	-	-	Maluro	4
-	-	-	-	-	-	Namanei	4
-	-	-	-	-	-	Uaitame	4
Total	**48**		**65**		**58**		**54**

Vemasse		Venilale	
sukus	**Aldeia**	**Suku**	**Aldeia**
Caicua	2	Bado-Ho'o	5
Loilubo	3	Baha Mori	6
Ossouala	5	Fatulia	4
Ostico	3	Uailaha	4
Uaigae	2	Uai-Oli	4
Uatulari	3	Uatu Hoco	4
Vemasse	4	Uma AnaUlo	4
-	-	Uma Ana Ico	4
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-
	22		**35**

Tabela 1.1: Forca de Trabalho ADN, I.P Municipio Baucau

Forca de Trabalho ADN,I.P **Municipio Baucau**								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	**3**	**2**				**3**	
2	Administrasaun no Financas	**0**	**0**				**0**	
3	Motorista	**1**	**1**				**1**	
4	Seguransa	**0**	**0**				**0**	
Total		**4**					**4**	

Tabela 1.2 : Lista Asset ADN,I.P Municipio Baucau.

ASET ADN,IP MUNICIPIO BAUCAU								
No	**Deskrisaun**	**Total Aset Kada Tinan**					**Total**	**OBS**
		2021	**2022**	**2023**	**2024**	**2025**		
1	Edificio	1	1				**1**	
2	Kareta	1	1					
3	Desktop HP / Monitor	0	0					
4	Laptop HP	2	2					
5	Printer Cannon	1	1					
6	UPS	0	0					
7	Armario File	1	1					
8	Armario Tau hena	3	3					

9	Meja escritorio	1	1					
10	Meja han	1	1					
11	Meja TV (kiik)	1						
12	Kadeira escritorio	6	6					
13	Kadeira han	4	4					
14	Sofa	1 Set	1					
15	Springbed +sumasu 4+sprei 3	3 Set	1					
16	Jeleira	1	1					
17	Water Dispenser	1	1					
18	TV + Parabola	1 Set	1					
19	AC	4	4					
20	Kompor	0	0					
21	Kompor Gas	0	0					
22	Rack sepatu	0	0					
23	Rack Piring	0	0					
24	Water Pump Sanyo	1	1					

1.3 : Lista Projectos

Projetu hotu ne'ebe akumula iha lista ne'e bazeia ba dadus projetu ne'ebe sei lao hela no mos projeto ne'ebe abandona ona tinan barak, projeto hirak ne'e fahe tuir lista 1.3.1 Projeto Por Fundus Finansiamentos, 1.3.2 Projeto Por Sectors no 1.3.3 Projeto Por Ministerios.

1.3.1 : Lista Projectos Municipio Baucau Por Fundus Finansiamentos

NO	POSTO ADMINISTRATIVO	TOTAL FI+Fundu Covid-19+LM-BS+LM-CD+LM-TP+PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	14	$ 2,230,497.80	45.39%
2	Baucau Villa	20	$ 10,638,283.98	52.62%
3	Laga	11	$ 2,698,206.10	48.50%
4	Multi Posto	6	$ 110,461,376.54	73.18%
5	Quelicai	16	$ 9,587,999.47	64.79%
6	Vemasse	7	$ 1,824,722.56	42.66%
7	Venilale	11	$ 6,830,895.16	36.16%
	Grand Total	85	$ 144,271,981.61	68.07%

NO	POSTO ADMINISTRATIVO	FI		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	2	$ 561,399.61	89.89%
2	Baucau Villa	5	$ 8,312,880.92	59.65%
3	Laga	2	$ 719,359.34	81.57%
4	Multi Posto	4	$ 109,889,602.64	73.51%
5	Quelicai	4	$ 7,600,628.19	75.08%
6	Vemasse	1	$ 690,194.30	90.00%
7	Venilale	6	$ 6,194,968.60	37.58%
	Grand Total	24	$ 133,969,033.60	71.28%

NO	POSTO ADMINISTRATIVO	Fundu Covid-19		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia		$ -	0.00%
2	Baucau Villa	1	$ 469,360.62	70.14%
3	Laga		$ -	0.00%
4	Multi Posto		$ -	0.00%
5	Quelicai		$ -	0.00%
6	Vemasse		$ -	0.00%
7	Venilale		$ -	0.00%
	Grand Total	1	$ 469,360.62	70.14%

Dadus kada projeto: Anexu A

NO	POSTO ADMINISTRATIVO	LM-BS		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	1	$ 255,148.17	18.07%
2	Baucau Villa	2	$ 207,288.36	65.36%
3	Laga	2	$ 595,138.56	38.87%
4	Multi Posto		$ -	0.00%
5	Quelicai		$ -	0.00%
6	Vemasse	1	$ 50,000.00	60.97%
7	Venilale		$ -	0.00%
	Grand Total	6	$ 1,107,575.09	40.03%

NO	POSTO ADMINISTRATIVO	LM-CD		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	1	$ 316,447.42	89.84%
2	Baucau Villa	3	$ 487,013.64	12.65%
3	Laga	2	$ 968,003.94	44.59%
4	Multi Posto	2	$ 571,773.90	8.45%
5	Quelicai	4	$ 1,205,716.58	41.97%
6	Vemasse	4	$ 1,030,442.93	10.44%
7	Venilale	1	$ 282,288.02	43.36%
	Grand Total	17	$ 4,861,686.43	32.13%

NO	POSTO ADMINISTRATIVO	LM-TP		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	8	$ 845,834.12	0.00%
2	Baucau Villa	7	$ 786,409.33	0.00%
3	Laga	3	$ 288,126.88	0.00%
4	Multi Posto		$ -	0.00%
5	Quelicai	8	$ 781,654.70	0.00%
6	Vemasse		$ -	0.00%
7	Venilale	3	$ 298,750.16	0.00%
	Grand Total	29	$ 3,000,775.19	0.00%

NO	POSTO ADMINISTRATIVO	PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	Baguia	2	$ 251,668.48	70.50%
2	Baucau Villa	2	$ 375,331.11	29.93%
3	Laga	2	$ 127,577.38	46.17%
4	Multi Posto		$ -	0.00%
5	Quelicai		$ -	0.00%
6	Vemasse	1	$ 54,085.33	35.55%
7	Venilale	1	$ 54,888.38	35.55%
	Grand Total	8	$ 863,550.68	44.86%

1.3.2 : Lista Projectos Municipio Baucau Por Sectors

NO	POR SECTOR	TOTAL MUNICIPIO BAUCAU		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA	1	$ 316,447.42	89.84%
2	EDIFICIOS PUBLICOS	13	$ 1,999,417.79	29.65%
3	EDUKASAUN	31	$ 3,743,421.04	16.69%
4	ELETRIFIKASAUN NASIONAL	10	$ 3,110,591.49	82.09%
5	ESTRADAS	17	$ 22,189,429.73	50.50%
6	IMPRESTIMO	4	$ 109,889,602.64	73.51%
7	MANUTENSAUN NO REHABILITASAUN	8	$ 2,553,710.88	72.00%
8	SAUDE	1	$ 469,360.62	70.14%
	Grand Total	85	$ 144,271,981.61	68.07%

NO	POR SECTOR	Baguia		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA	1	$ 316,447.42	89.84%
2	EDIFICIOS PUBLICOS	2	$ 251,668.48	70.50%
3	EDUKASAUN	8	$ 845,834.12	0.00%
4	ELETRIFIKASAUN NASIONAL	1	$ 485,365.98	89.88%
5	ESTRADAS		$ -	0.00%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN	2	$ 331,181.80	34.58%
8	SAUDE		$ -	0.00%
	Grand Total	14	$ 2,230,497.80	45.39%

NO	POR SECTOR	Baucau Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	4	$ 464,962.08	34.44%
3	EDUKASAUN	8	$ 1,463,612.86	38.65%
4	ELETRIFIKASAUN NASIONAL	2	$ 584,858.54	82.59%
5	ESTRADAS	5	$ 7,655,489.88	53.03%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE	1	$ 469,360.62	70.14%
	Grand Total	20	$ 10,638,283.98	52.62%

NO	POR SECTOR	Laga		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	2	$ 574,764.00	19.63%
3	EDUKASAUN	4	$ 353,569.20	16.66%
4	ELETRIFIKASAUN NASIONAL		$ -	0.00%
5	ESTRADAS	2	$ 656,863.79	58.74%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN	3	$ 1,113,009.11	67.48%
8	SAUDE		$ -	0.00%
	Grand Total	11	$ 2,698,206.10	48.50%

NO	POR SECTOR	Multi Posto		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS		$ -	0.00%
3	EDUKASAUN		$ -	0.00%
4	ELETRIFIKASAUN NASIONAL		$ -	0.00%
5	ESTRADAS	2	$ 571,773.90	8.45%
6	IMPRESTIMO	4	$ 109,889,602.64	73.51%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE		$ -	0.00%
	Grand Total	6	$ 110,461,376.54	73.18%

NO	POR SECTOR	Quelicai		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	2	$ 549,049.52	13.32%
3	EDUKASAUN	8	$ 781,654.70	0.00%
4	ELETRIFIKASAUN NASIONAL	2	$ 729,303.13	84.18%
5	ESTRADAS	4	$ 7,527,992.12	73.40%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE		$ -	0.00%
	Grand Total	16	$ 9,587,999.47	64.79%

NO	POR SECTOR	Vemasse		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	2	$ 104,085.33	47.76%
3	EDUKASAUN		$ -	0.00%
4	ELETRIFIKASAUN NASIONAL	2	$ 840,963.28	86.66%
5	ESTRADAS	3	$ 879,673.95	0.00%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN		$ -	0.00%
8	SAUDE		$ -	0.00%
	Grand Total	7	$ 1,824,722.56	42.66%

NO	POR SECTOR	Venilale		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	AGRICULTURA		$ -	0.00%
2	EDIFICIOS PUBLICOS	1	$ 54,888.38	35.55%
3	EDUKASAUN	3	$ 298,750.16	0.00%
4	ELETRIFIKASAUN NASIONAL	3	$ 470,100.56	61.99%
5	ESTRADAS	1	$ 4,897,636.09	24.21%
6	IMPRESTIMO		$ -	0.00%
7	MANUTENSAUN NO REHABILITASAUN	3	$ 1,109,519.97	87.70%
8	SAUDE		$ -	0.00%
	Grand Total	11	$ 6,830,895.16	36.16%

1.3.3 : Lista Projectos Municipio Baucau Por Ministerios

NO	POR MINISTERIO	GRAND TOTAL		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	7	$ 798,108.36	41.16%
2	MINISTERIO AGRIKULTURA E PESCAS	1	$ 316,447.42	89.84%
3	MINISTERIO DAS OBRAS PUBLICAS	40	$ 137,763,172.77	69.97%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	31	$ 3,743,421.04	16.69%
5	MINISTERIO SAUDE	2	$ 748,725.31	53.73%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 50,000.00	60.97%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	2	$ 782,313.77	14.42%
8	SAMES	1	$ 69,792.94	42.92%
	Grand Total	85	$ 144,271,981.61	68.07%

NO	POR MINISTERIO	Baguia		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	2	$ 251,668.48	70.50%
2	MINISTERIO AGRIKULTURA E PESCAS	1	$ 316,447.42	89.84%
3	MINISTERIO DAS OBRAS PUBLICAS	3	$ 816,547.78	67.45%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	$ 845,834.12	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	14	$ 2,230,497.80	45.39%

NO	POR MINISTERIO	Baucau Villa		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	2	$ 375,331.11	29.93%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	8	$ 8,260,186.45	55.21%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	$ 1,463,612.86	38.65%
5	MINISTERIO SAUDE	1	$ 469,360.62	70.14%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES	1	$ 69,792.94	42.92%
	Grand Total	20	$ 10,638,283.98	52.62%

NO	POR MINISTERIO	Laga		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	$ 62,135.06	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	5	$ 1,769,872.90	64.23%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	4	$ 353,569.20	16.66%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	$ 512,628.94	22.01%
8	SAMES		$ -	0.00%
	Grand Total	11	$ 2,698,206.10	48.50%

NO	POR MINISTERIO	Multi Posto		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		$ -	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	6	$ 110,461,376.54	73.18%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		$ -	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	6	$ 110,461,376.54	73.18%

NO	POR MINISTERIO	Quelicai		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL		$ -	0.00%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	6	$ 8,257,295.25	74.35%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	8	$ 781,654.70	0.00%
5	MINISTERIO SAUDE	1	$ 279,364.69	26.17%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	1	$ 269,684.83	0.00%
8	SAMES		$ -	0.00%
	Grand Total	16	$ 9,587,999.47	64.79%

NO	POR MINISTERIO	Vemasse		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	$ 54,085.33	35.55%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	5	$ 1,720,637.23	42.36%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU		$ -	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 50,000.00	60.97%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	7	$ 1,824,722.56	42.66%

NO	POR MINISTERIO	Venilale		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PRESENTAZEN EXECUSAUN (%)
1	ESTATAL	1	$ 54,888.38	35.55%
2	MINISTERIO AGRIKULTURA E PESCAS		$ -	0.00%
3	MINISTERIO DAS OBRAS PUBLICAS	7	$ 6,477,256.62	37.83%
4	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	$ 298,750.16	0.00%
5	MINISTERIO SAUDE		$ -	0.00%
6	MINISTERIO TURISMO KOMERCIO E INDUSTRIA		$ -	0.00%
7	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL		$ -	0.00%
8	SAMES		$ -	0.00%
	Grand Total	11	$ 6,830,895.16	36.16%

1.4. Dadus Populasaun Munisipiu Baucau

Posto Administrativo, Suco no Sexu	2022				
	Total	Idade Poduktivu (idade 15-64)		idade la Produltivu (idade 0-14+65 ba leten	
		Male	Female	Male	Female
Baguia	13,569	4,111	3,962	2,769	2,727
Baucau	48,990	14,524	14,547	10,211	9,709
Laga	16,291	4,549	4,591	3,567	3,585
Quelicai	6,127	1,774	1,413	1,536	1,405
Vemasse	2,783	711	698	707	667
Venilale	5,136	1,223	1,197	1,369	1,347

Fontes : Projeksaun Populasaun bazea ba Census Populasaun no Umakain 2015,

Direccao Geral de Estatistika, MoF

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progressu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan nia laran, husi lista #anexu B hatudu progresu aktual fulan ida ne'e ho nia prensentagen servisu, montante aktual bazeia ba orsamento ne'ebe hetan husi progresu fulan ida ne'e, ikus liu prentangen aktual fulan ida ne'e hatudu progresu fisiku komulativu husi prosentu antrior no fulan ida ne'e nian, lista kompletu ba detallu bele hare iha #anexu B, detallu ba back-up #anexu C, no Instrusaun Servisu #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáclo Servisu Iha Terenu

1. Transporte no Engenheiro la Suficiente
2. Ho Volume Servisu ne'ebe barak Planu Inspeksaun kada fulan dala Tolu(3) ba visita Projetu sente todan ou la kobre **(karik iha villa laran bele halo Monitorizasaun kada fulan bele dala tolu(3) maibe ho distancia ne'ebe do'ok no estrada ne'ebe grave hanesan Laga, Quelicai, Baguia no Venilale sebele halo monitorizasaun kada fulan dala ida (1) deit**).
3. Mina la suficente
4. Pakote hodi asesu ba **Dropbox** ami husi Baucau sei uza ida idak nia pakote ou pulsa pribado
5. Ami Engenherio Municipio sente todan tamba planu inspeksaun kada fulan dala tolu (3) ho distancia balun ne'ebe do'ok no estrada grave ami dala ruma la iha tempu atu sukat kada item por item tamba ami maneija tempu hodi ba fali projetu seluk no dala ruma mos ami fila kalan bo'ot to'o des oras (10) hanesan ne'e ami la konsege **update** informasaun kada projetu ba **Dropbox**.

- **Obstaclo Parte Eletricidade**
  1. Laptop laiha atu halo relatorio waihira iha Municipiu
  2. Transporte (Kareta / motor) la Suficiente atu koresponde ba plano ne'ebe Aprovado
  3. Combustibel / Mina (Municipiu Baucau, Viqueque, Lautem, Pertamina Eto laiha)
  4. Kontractor laiha site ou kontaktu / telfone la tama no contractor la ba iha site/terenu
  5. Menus Enginheiro ME
  6. Natureza hanesan Udan Boot, Estrada kotu dalan la asesu ba kareta

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Sujere ba Superior sebele aumenta transporte no Enginheiro
2. Sujere ba Superior karik bele planu Inspeksaun kada fulan dala tolu (3) ba visita projetu sente todan ou la kobre **(ho distancia ne'ebe do'ok no estrada ne'ebe grave hanesan Posto Administrativo Laga, Quelicai no Baguia sebele halo monitorizasaun kada fulan dala ida 1 deit).**
3. Sujere ba Superior karik bele planu Inspeksaun kada fulan dala ida 2 ou tuir planu Inspesaun ba projetu sira ne'ebe iha **Posto Administrativo Baucau villa, Vemase no Venilale.**
4. Projecto nebe'e mak enginheiro la iha terenu ami la presija halo monitorizasaun no sukat nia volume
5. Presija aumenta mina
6. Husu ba Logistik sebele resolve tiha linha Internet iha Residence ADN Baucau.

- **Recomedacasaun Parte Eletricidade**

1. Rekomenda ba parte Logistik atu prepara Laptop kada Enginheiro (ba Eng. Ne'ebe seidauk hetan).
2. Rekomenda ba Logistik atu Aumenta tranporte ka kareta ba Enginheiro Electricidade.
3. Rekomeda ba parte Logistik atu hare problema konbustibel / Mina iha parte leste mak hanesan Municipio Baucau, Lautem no Viqueque problema iha neba pertamina Eto laiha nemak dificulta Ami nia plano monitorizasaun karik mina hotu ami tenki fila mai atesta iha municipio Manatuto.
4. Rekomenda ba Superior sira atu koordena ho Dono do projeito (EDTL,EP) oinsa atu kria linha koordenasaun ne'ebe diak.
5. Rekomenda ba HR atu Amenta Eng. Electricidade (Recruta tan Eng. ME)
6. Rekomenda ba parte Logistik atu prepara / Facilita simcard Office nian ba Eng. Electerica.

Note: Asinatura Husi Eng. Municipio Baucau

Força de Trabalho ADN,I.P Municipio Baucau						
No	**Deskrisaun**	**Identidade**				
		Naran Kompletu	**Nu. ID Card**	**Pozisaun**	**Fotografia**	**Asinatura**
1	Enjineiru	Agustinho Aranda	153	Enjineiru EPAS		
		Jacob da Costa Camoes	165	Enjineiru ITI		
		Adonis Julio Fernandes	152	Enjineiru ME		

	Enjineira	Olivia Soares	112	Enjineira VEBD		
2	Motorista	Anaceto de S. Belo	048	Motorista		

#ANEXU A

MUNICIPIO BAUCAU (LISTA GERAL)

					LOKALIZASAUN PROJETU										
NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	Posto Administrativo	MUNICIPIO	NARAN COMP.	NARAN KONT.	MONT. KONT. ($)	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. ($)	BAL. ($)	STATUS PROJECTO	OBS
1	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	$ 22,000.00	0.00%	0.00%	$ -	$ 22,000.00	ON-GOING	
2	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	$ 562,858.54	95.35%	95.35%	$ 483,039.75	$ 79,818.79	ON-GOING	
3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Domin Timor Diak, Lda	SSS/078/MOPTC-2017	$ 3,599,951.87	89.74%	89.74%	$ 2,646,594.70	$ 953,357.17	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 0,04%
4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Gihon Unip, Lda	SSS/066/MOPTC-2017	$ 3,450,866.98	39.61%	39.61%	$ 1,263,582.64	$ 2,187,284.34	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 0,04%
5	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	$ 19,838.03	100.00%	100.00%	$ 17,854.23	$ 1,983.80	ON-GOING	Falta Retensaun
8	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Baucau Villa	Baucau	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	$ 469,360.62	85.72%	85.72%	$ 329,188.84	$ 140,171.78	ON-GOING	
10	Construção de Nova Escola Polo de Baucau, de Referência da Escola Portuguesa de Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Baucau Villa	Baucau	Sanira Construction Unip Lda	RDTL-326	$ 677,203.53	92.82%	92.82%	$ 565,698.21	$ 111,505.32	ABANDONA	
11	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Rozi Unipessoal, Lda	04/KDM/-BAUCAU/IX/2021	$ 59,323.84	0.00%	0.00%	$ -	$ 59,323.84	ON-GOING	
12	Konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Gardel Unipessoal.Lda	07/KDM/-BAUCAU/IX/2021	$ 316,007.27	39.50%	39.50%	$ 112,329.98	$ 203,677.29	ON-GOING	
13	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Talamori	RDTL-SAMES-RFQ-021-071	$ 69,792.94	69.33%	69.33%	$ 29,956.90	$ 39,836.04	ON-GOING	
14	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF MAUCALE	-	$ 83,515.23	21.19%	21.19%	$ -	$ 83,515.23	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 21,19%
15	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF ZONA GOLGOTA	-	$ 82,531.68	36.04%	36.04%	$ -	$ 82,531.68	ON-GOING	
16	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	-	$ 144,241.57	0.00%	0.00%	$ -	$ 144,241.57	ON-GOING	
17	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	-	$ 164,157.57	0.00%	0.00%	$ -	$ 164,157.57	ON-GOING	
18	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESG FILIAL KILIK WAIGA'E	-	$ 76,528.56	17.08%	17.08%	$ -	$ 76,528.56	ON-GOING	
19	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	-	$ 117,273.54	0.00%	0.00%	$ -	$ 117,273.54	ON-GOING	
20	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	-	$ 118,161.18	0.00%	0.00%	$ -	$ 118,161.18	ON-GOING	
21	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Lalaisi, Unip. Lda	RT/023/MOP-2019	$ 377,873.70	97.47%	97.47%	$ 245,269.41	$ 132,604.29	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 31.12%
22	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 1+600 - 3+300 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Rozi Unipessoal, Lda	RT/024/MOP-2019	$ 341,485.64	100.00%	100.00%	$ 341,485.63	$ 0.01	FHO	Projecto Finaliza ona
23	Rural Roads Periodic Maintenance Samaguia - Namanei Chainage 0+000 - 7+000 Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Delatina	MPTCW-W-190091	$ 393,649.77	84.80%	84.80%	$ 164,273.69	$ 229,376.08	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 15.53%
24	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Laga	Baucau	Sumber Urip Unip. Lda	04/KDAM-BCU/IX/2019	$ 65,442.32	100.00%	100.00%	$ 58,898.09	$ 6,544.23	PHO	Falta Retensaun
25	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laga	Baucau	Uatoos Unip. Lda	MOP-W-200002	$ 201,488.79	40.00%	40.00%	$ 67,076.91	$ 134,411.88	ON-GOING	
26	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 :Laga to Baguia	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laga	Baucau	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	$ 455,375.00	70.00%	70.00%	$ 318,762.50	$ 136,612.50	ON-GOING	
27	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Laga	Baucau	Costa Estelia Unipessoal,Lda	05/KDM/-BAUCAU/IX/2021	$ 62,135.06	20.29%	20.29%	$ -	$ 62,135.06	ON-GOING	
28	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Laga	Baucau	Juga Te Figa Unipessoal Lda	40/MACLN/X/2021	$ 512,628.94	29.81%	29.81%	$ 112,848.70	$ 399,780.24	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 15.55%
29	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF LALA-BU'U	-	$ 109,706.08	0.00%	0.00%	$ -	$ 109,706.08	ON-GOING	
30	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	-	$ 87,554.29	21.19%	21.19%	$ -	$ 87,554.29	ON-GOING	

31	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	-	$ 90,866.51	0.00%	0.00%	$ -	$ 90,866.51	ON-GOING	
34	Konstrusaun Posto Administrativo Baguia	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Delatina Unip. Lda	02/KDAM-BCU/VIII/2019	$ 197,153.25	100.00%	100.00%	$ 177,437.92	$ 19,715.33	PHO	Falta Retensaun
36	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Mexa	06/KDM/-BAUCAU/IX/2021	$ 54,515.23	12.06%	12.06%	$ -	$ 54,515.23	ON-GOING	
38	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF GULARI	-	$ 89,797.83	0.00%	0.00%	$ -	$ 89,797.83	ON-GOING	
39	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF OSSU-UFULARI	-	$ 105,390.82	0.00%	0.00%	$ -	$ 105,390.82	ON-GOING	
40	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF UACALA	-	$ 81,847.60	0.00%	0.00%	$ -	$ 81,847.60	ON-GOING	
41	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE FINI BAGUIA	-	$ 91,267.16	0.00%	0.00%	$ -	$ 91,267.16	ON-GOING	
42	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari - Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE LARI-SULA	-	$ 97,046.05	10.64%	10.64%	$ -	$ 97,046.05	ON-GOING	
43	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC OSSU-HUNA	-	$ 84,264.57	25.80%	25.80%	$ -	$ 84,264.57	ON-GOING	
44	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC BUAUA LAVATERI	-	$ 120,700.62	0.00%	0.00%	$ -	$ 120,700.62	ON-GOING	
45	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE ESGF DE BAGUIA	-	$ 175,519.47	4.17%	4.17%	$ -	$ 175,519.47	ON-GOING	
51	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Wetodo Unip. Lda	SSS/296/MOPTC-2016	$ 483,731.02	92.96%	92.96%	$ 395,709.78	$ 88,021.24	ON-GOING	
53	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Venilale	Baucau	Caidara Lata Unipessoal,Lda	02/KDM/-BAUCAU/IX/2021	$ 54,888.38	39.50%	39.50%	$ 19,512.87	$ 35,375.51	ON-GOING	
54	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBC UAI-BUA	-	$ 88,801.74	0.00%	0.00%	$ -	$ 88,801.74	ON-GOING	
55	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBF CULINA-OSSU-UAILALE	-	$ 120,371.07	0.00%	0.00%	$ -	$ 120,371.07	ON-GOING	
56	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	-	$ 89,577.35	30.76%	30.76%	$ -	$ 89,577.35	ON-GOING	
63	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	$ 279,364.69	29.08%	29.08%	$ 73,115.51	$ 206,249.18	ON-GOING	
64	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Samadare Unip. Lda	40/MACLN/XI/2021	$ 269,684.83	2.90%	2.90%	$ -	$ 269,684.83	ON-GOING	
65	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UADA-BORU	-	$ 61,695.67	0.00%	0.00%	$ -	$ 61,695.67	ON-GOING	
66	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAI-ACA/MULIA	-	$ 101,309.07	26.69%	26.69%	$ -	$ 101,309.07	ON-GOING	
67	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF ABO-LIR LALETEK	-	$ 75,117.25	0.00%	0.00%	$ -	$ 75,117.25	ON-GOING	
68	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBC LETEMUMO	-	$ 159,065.75	9.87%	9.87%	$ -	$ 159,065.75	ON-GOING	
69	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	-	$ 125,450.86	0.00%	0.00%	$ -	$ 125,450.86	ON-GOING	
70	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF CATOLICA DARENAFA	-	$ 47,094.07	0.00%	0.00%	$ -	$ 47,094.07	ON-GOING	
71	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF MAURO DARALA/BORUMODO	-	$ 106,571.86	21.49%	21.49%	$ -	$ 106,571.86	ON-GOING	
72	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAIDORA/OSSOLIA	-	$ 105,350.17	0.00%	0.00%	$ -	$ 105,350.17	ON-GOING	

78	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Vemasse	Baucau	Esa-Un	56/DNAL-MTAC/III/2017	$ 50,000.00	67.74%	67.74%	$ 30,483.00	$ 19,517.00	PENDENTE	
79	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Vemasse	Baucau	Wrangler Unipessoal,Lda	01/KDM/-BAUCAU/IX/2021	$ 54,085.33	65.19%	65.19%	$ 19,227.89	$ 34,857.44	ON-GOING	Progresso Fisiko iha Tereno ba Fulan Maio Aumenta 14.98%
	TOTAL								**$ 144,271,981.61**			**$ 98,209,610.04**	**$ 49,112,860.96**		

Prepara Husi:

1. Eng. Agustinho Aranda **Eng. ba**
Porjecto Edifício Publico Beé no Saneamento
Municipio Baucau,ADN,I.P

2. Eng. Jacob da Costa Camoes
Eng. ba Projeito Insfrasturctura e Irigasaun
Municipiu Baucau, ADN, I.P

3. Eng. Adonis Julio Ferndandes
Eng. ba Projeito ME, ADN, I.P

Certifika Husi:

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Da Unidade de Controlo e Validação
De Qualidade ADN,I.P

#ANEXU B

PROGRESSU FISIKU KADA FULAN MUNICIPIO BAUCAU

					LOKALIZASAUN PROJETU						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
1	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	$ 22,000.00	Jan. 1, 2016	0.00%		0.00%
2	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baucau Villa	Baucau	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	$ 562,858.54	July 6, 2016	95.35%		95.35%
3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Domin Timor Diak, Lda	SSS/078/MOPTC-2017	$ 3,599,951.87	Sept. 12, 2017	89.70%	0.04%	89.74%
4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Baucau Villa	Baucau	Gihon Unip, Lda	SSS/066/MOPTC-2017	$ 3,450,866.98	Sept. 12, 2017	39.57%	0.04%	39.61%
5	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	$ 19,838.03	Aug. 1, 2016	100.00%		100.00%
6	Rural Roads Routine Maintenance Baucau - Uatabo Chainage 0+000 - 4+800 and Boile - Uatabo Chainage 0+000 - 5+200 in Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Baucau Villa	Baucau	Talamori	MPWTC-W-190090	$ 63,815.15	Jan. 10, 2012	80.00%		80.00%
7	Road Maintenance Section: Baucau Urbans, Baucau Town, Baucau Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Baucau Villa	Baucau	Jomarjo Unipessoal Lda	MPW-W-190158	$ 137,495.42	Nov. 30, 2019	85.28%		85.28%
8	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Baucau Villa	Baucau	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	$ 469,360.62	Dec. 10, 2020	85.72%		85.72%
9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Baucau Villa	Baucau	Mexa Unip.lda	MPW-W-210047	$ 403,360.46	June 10, 2021	1.95%		1.95%
10	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Baucau Villa	Baucau	Sanira Construction Unip Lda	RDTL-326	$ 677,203.53	Nov. 12, 2012	92.82%		92.82%
11	Konstrusaun Sede Suku, Suku Samalari Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Rozi Unipessoal, Lda	04/KDM/-BAUCAU/IX/2021	$ 59,323.84	8-Jul-21	0.00%		0.00%
12	konstrusaun Moru Haleu Mercadu Tualiku Baucau Villa Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Gardel Unipessoal.Lda	07/KDM/-BAUCAU/IX/2021	$ 316,007.27	8-Jul-21	39.50%		39.50%
13	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Baucau Villa	Baucau	Talamori	RDTL-SAMES-RFQ-021-071	$ 69,792.94	8-Jul-21	69.33%		69.33%
14	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF MAUCALE	-	$ 83,515.23	Oct. 15, 2021	0.00%	21.19%	21.19%
15	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF ZONA GOLGOTA	-	$ 82,531.68	Oct. 15, 2021	36.04%		36.04%
16	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	-	$ 144,241.57	Oct. 15, 2021	0.00%		0.00%
17	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	-	$ 164,157.57	Oct. 15, 2021	0.00%		0.00%
18	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	-	$ 76,528.56	Oct. 15, 2021	17.08%		17.08%
19	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	-	$ 117,273.54	Oct. 15, 2021	0.00%		0.00%
20	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baucau Villa	Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	-	$ 118,161.18	Oct. 15, 2024	0.00%		0.00%
21	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Lalaisi, Unip. Lda	RT/023/MOP-2019	$ 377,873.70	Jan. 15, 2020	97.47%		97.47%
22	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 1+600 - 3+300 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Rozi Unipessoal, Lda	RT/024/MOP-2019	$ 341,485.64	Jan. 1, 2020	99.56%		100.00%
23	Rural Roads Periodic Maintenance Samaguia - Namanei Chainage 0+000 - 7+000 Municipality Baucau / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Laga	Baucau	Delatina	MPTCW-W-190091	$ 393,649.77	Aug. 23, 2019	69.28%	15.53%	84.80%
24	Konstrusaun EBF Publiku Selegua	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Laga	Baucau	Sumber Urip Unip. Lda	04/KDAM-BCU/IX/2019	$ 65,442.32	Sept. 24, 2019	100.00%		100.00%
25	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Laga	Baucau	Uatoos Unip. Lda	MOP-W-200002	$ 201,488.79	May 5, 2014	40.00%		40.00%

					LOKALIZASAUN PROJETU						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
26	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 :Laga to Baguia	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Laga	Baucau	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	$ 455,375.00	March 25, 2020	70.00%		70.00%
27	Konstrusaun Sede Suku, Suku Atelari Laga Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Laga	Baucau	Costa Estelia Unipessoal,Lda	05/KDM/-BAUCAU/IX/2021	$ 62,044.03	8-Jul-21	20.29%		20.29%
28	New Construction of Camp and Leveling, pavement works no jardim de herois de laga Baucau	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Laga	Baucau	Juga Te Figa Unipessoal Lda	40/MACLN/X/2021	$ 512,628.94	Jan. 1, 2022	29.81%		29.81%
29	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF LALA-BU'U	-	$ 109,706.08	Oct. 15, 2021	0.00%		0.00%
30	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	-	$ 87,554.29	Oct. 15, 2021	0.00%		21.19%
31	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Laga	Baucau	MEJD PKRIE EBF. FITUN SAGADATE-LAGA	-	$ 90,866.51	Oct. 15, 2021	0.00%		0.00%
32	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Baguia	Baucau	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	$ 485,365.98	July 6, 2016	100.09%		100.09%
33	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Baguia	Baucau	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	$ 76,033.63	Nov. 15, 2016	100.00%		100.00%
34	Konstrusaun Posto Administrativo Baguia	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Delatina Unip. Lda	02/KDAM-BCU/VIII/2019	$ 197,153.25	Aug. 1, 2019	100.00%		100.00%
35	Baguia - Larisula Chainage 0+000 - 12+900 / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Baguia	Baucau	Lamegua Star Unip Lda	MPW-W-190088	$ 255,148.17	Aug. 23, 2019	20.07%		20.07%
36	Konstrusaun Sede Suku, Suku Samalari Baguia Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Baguia	Baucau	Mexa Unip.lda	06/KDM/-BAUCAU/IX/2021	$ 54,515.23	8-Jul-21	12.06%		12.06%
37	Konstrusaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	MINISTERIO AGRIKULTURA E PESCAS	LM-CD	AGRICULTURA	Baguia	Baucau	Makasae Construction LDA	RDTL-2021-14628	$ 316,447.42	Sept. 16, 2021	99.83%		99.83%
38	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF GULARI	-	$ 89,797.83	Oct. 15, 2021	0.00%		0.00%
39	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF OSSU-UFULARI	-	$ 105,390.82	Oct. 15, 2021	0.00%		0.00%
40	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBF UACALA	-	$ 81,847.60	Oct. 15, 2021	0.00%		0.00%
41	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE FINI BAGUIA	-	$ 91,267.16	Oct. 15, 2021	0.00%		0.00%
42	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EPE LARI-SULA	-	$ 97,046.05	Oct. 15, 2021	0.00%	10.64%	10.64%
43	Rehabilitasaun ba EBC Ossu - HUna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC OSSU-HUNA	-	$ 84,264.57	Oct. 15, 2021	0.00%	25.80%	25.80%
44	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE EBC BUAUA LAVATERI	-	$ 120,700.62	Oct. 15, 2021	0.00%		0.00%
45	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Baguia	Baucau	MEJD PKRIE ESGF DE BAGUIA	-	$ 175,519.47	Oct. 15, 2021	0.00%	4.17%	4.17%
46	Aumenta C. O no Kliesntes	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	$ 24,365.04	Jan. 1, 2017	100.00%		100.00%
47	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	$ 163,447.50	July 6, 2016	100.00%		100.00%

					LOKALIZASAUN PROJETU						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
48	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Venilale	Baucau	Ruvic unip, lda	SSS/118/MOPTC-2016	$ 4,897,636.09	July 29, 2016	27.52%		27.52%
49	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Caidailale Unip.Lda	RT/069/MOPTC-2016	$ 343,674.56	Aug. 18, 2016	96.10%		96.10%
50	Rehabilitasaun Estrada Bercoli-Bahamori 3 Sta. 2+750-4+000-Municipal of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Maubere Spirit	RT/071/MOPTC-2016	$ 282,114.39	Aug. 18, 2016	100.00%		100.00%
51	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Venilale	Baucau	Wetodo Unip. Lda	SSS/296/MOPTC-2016	$ 483,731.02	Nov. 22, 2016	92.96%		92.96%
52	Instalacao Electricidade Linha Medium Voltagem & Transformer Ba Comunidade (Energia Eletricidade ba Sistema Bomba Be'e Mos) ba Comunidade Fatulia Watuhaco & Waihaia (Venilale)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Venilale	Baucau	Bozer Construcao,unip.lda	MOP-W-190173	$ 282,288.02	Oct. 30, 2019	48.18%		48.18%
53	Konstrusaun Sede Suku, Suku Uailaha Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Venilale	Baucau	Caidara Lata Unipessoal,Lda	02/KDM/-BAUCAU/IX/2021	$ 54,888.38	8-Jul-21	39.50%		39.50%
54	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBC UAI-BUA	-	$ 88,801.74	Oct. 15, 2021	0.00%		0.00%
55	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EBF CULINA-OSSU-UAILALE	-	$ 120,371.07	Oct. 15, 2021	0.00%		0.00%
56	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Venilale	Baucau	MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	-	$ 89,577.35	Oct. 15, 2021	0.00%	30.76%	30.76%
57	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Quelicai	Baucau	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	$ 471,847.32	July 6, 2016	90.70%	8.13%	98.83%
58	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Quelicai	Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	$ 257,455.81	Sept. 1, 2016	100.00%		100.00%
59	Rehabilitation Of Roads Uiaca - Queleqai - Lacluta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Quelicai	Baucau	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	$ 3,451,113.20	Oct. 28, 2016	94.61%		94.61%
60	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Quelicai	Baucau	Lalaisi, Unip. Lda	MPWTC-W-190089	$ 157,601.26	Aug. 23, 2019	58.92%		58.92%
61	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Quelicai	Baucau	Niceles Unipessoal Lda	MPW-CS-2000026	$ 499,065.80	March 25, 2020	70.00%		70.00%
62	Rehabilitation of Roads, Road Section: Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Quelicai	Baucau	Wingstone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	$ 3,420,211.86	Oct. 28, 2016	92.14%		92.14%
63	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	$ 279,364.69	Aug. 23, 2021	29.08%		29.08%
64	New construction of Tom,pavement and Gabion no jardim de Herois de Quelicai	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	EDIFICIOS PUBLICOS	Quelicai	Baucau	Samadare Unip. Lda	40/MACLN/XI/2021	$ 269,684.83	Jan. 1, 2022	2.90%		2.90%
65	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UADA-BORU	-	$ 61,695.67	Oct. 15, 2021	0.00%		0.00%
66	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAI- ACA/MULIA	-	$ 101,309.07	Oct. 15, 2021	26.69%		26.69%
67	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF ABO-LIR LALETEK	-	$ 75,117.25	Oct. 15, 2021	0.00%		0.00%
68	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBC LETEMUMO	-	$ 159,065.75	Oct. 15, 2021	0.00%	9.87%	9.87%
69	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	-	$ 125,450.86	Oct. 15, 2021	0.00%		0.00%
70	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF CATOLICA DARENAFA	-	$ 47,094.07	Oct. 15, 2021	0.00%		0.00%
71	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF MAURO DARALA/BORUMODO	-	$ 106,571.86	Oct. 15, 2021	0.00%	21.49%	21.49%
72	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Quelicai	Baucau	MEJD PKRIE EBF UAIDORA/OSSOLIA	-	$ 105,350.17	Oct. 15, 2021	0.00%		0.00%
73	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Vemasse	Baucau	We-Rua Unip, Lda	RDTL-11003725	$ 690,194.30	Oct. 22, 2010	100.00%		100.00%
74	Instalacao Electricidade Linha Distribuicao ba uma (Energia Eletricidade ba Sistema Bomba Be'e) ba Comunidade Loiubu (Watulari)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Vemasse	Baucau	El Nicholay unip.Lda	MOP-W-190181	$ 150,768.98	May 11, 2019	79.32%		79.32%
75	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Rozi const. unip. Lda	MPW-W-210048	$ 379,137.63	June 10, 2021	69.59%		69.59%
76	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Rozi const. unip. Lda	MPW-W-210051	$ 258,534.75	June 10, 2021	93.40%		93.40%
77	R4D Rural Road Spot Improvement Vemase-Osoala Chainage 0+000-21+600	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Vemasse	Baucau	Chacailala Unipessoal Lda	MPW-W-210052	$ 242,001.57	June 10, 2021	17.99%		17.99%
78	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Vemasse	Baucau	Esa-Un	56/DNAL-MTAC/III/2017	$ 50,000.00	Aug. 18, 2015	67.74%		67.74%
79	Konstrusaun Sede Suku, Suku Uaigae Vemasse Municipio Baucau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Vemasse	Baucau	Wrangler Unipessoal,Lda	01/KDM/-BAUCAU/IX/2021	$ 54,085.33	8-Jul-21	65.19%		65.19%
80	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	Multi Posto	Baucau	Shangai Construction Group Co.,Ltd	ICB/021/MPWTC-2015	$ 59,287,454.00	Aug. 18, 2016	84.82%		84.82%

					LOKALIZASAUN PROJETU						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	This Month Progress	Komulativu Progress
81	Road nrtwork Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	Multi Posto	Baucau	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/078/MPWTC-2015	$ 29,315,346.10	Nov. 12, 2016	81.68%	5.44%	87.12%
82	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto	Baucau	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	$ 16,024,500.97	March 21, 2019	31.66%		31.66%
83	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA- IMPRESTIMO	Multi Posto	Baucau	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)	RFP/003/MOP/2018	$ 5,262,302.00	Apr. 03, 2019	40.97%		45.07%
84	R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multi Posto	Baucau	Juga Te Figa Unipessoal Lda	MPW-W-210054	$ 272,285.28	June 10, 2021	3.03%		3.03%
85	R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Multi Posto	Baucau	DB-Ingracia Unipessoal Lda	MPW-W-210049	$ 299,488.62	June 10, 2021	77.38%	14.98%	92.37%

Inspeksaun Husi :

1. Eng. Agustinho Aranda
Eng. ba Porjecto Edificio Publico Beé no Saneamento Municipio Baucau,ADN,I.P

2. Eng. Jacob da Costa Camoes
Eng. ba Projeito Insfrasturctura e Irigasaun Municipiu Baucau, ADN, I.P

3. Eng. Adonis Julio Fernandes
Eng. ba Projeito ME, ADN, I.P

Verifika Husi :

Eng. Remigio da C. S. dos Santos
Eng. Senior ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Eng/Arch.Francisco Xavier de D. Jeronimo
Eng. Senior ba Porjecto Edificio Publico Beé no Saneamento ADN,I.P

Eng. Deolindo de Fatima Marques
ChefeSeksaun ME& ITC, ADN, I.P

Certifika Husi :

Eng. Emerenciana da Costa M.Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C1 (LA- 8)
Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA BASICA FILIAL LIBAGUA**
No. kontratu :

Data Inspesaun : Thrusday, Juny 09, 2022

Fatin Inspesaun : Baucau , Laga,libaguia

Koordinadas :

Start Point : Long: ....., Latetude : .....

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

Foto iha terenu	*Observa/Recommend. iha tereno*
Class Room Building C	
	1. Eng.grupo tenki mantein iha terenu hodi bele kontrola servisu hodi garante kualidade projecto 2. Molok atu halo pengecoran ba lantai tenki Stamper/halo pemdatan lai hafoin bele cor 3. Pres.grupo tenki halo linha kordenasaun ho projecto nain(Owner)relasiona ho servisu iha terenu

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (LA-8)

NARAN PROJECTO : NOVA CONSTRUÇÃO ESCOLA BASICA FILIAL LIBAGUA
FATIN PROJECTO : LIBAGUA , LAGA, BAUCAU
PROJECTO NAIN : MEJD

MAIN SUMMARY			Progress Juny 2022					
			PREVIOUS		THIS BILL		UP TO DATE	
NO	DESCRIPTION	AMOUNT	TOTAL $	WEIGH %	TOTAL $	WEIGH %	TOTAL $	WEIGH %
I	PRELIMINARIES	$ 3,262.12	$ -	0.00%	$ 2,118.56	2.54%	$ 2,118.56	2.54%
II	CLASSROOM BUILDING Ca	$ 64,413.36	$ -	0.00%	$ 13,651.44	16.35%	$ 13,651.44	16.35%
III	PROVISIONAL SUM FOR SITEWORKS	$ 6,648.56	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**$ 74,324.04**	**$ -**	**$ -**	**$ 15,770.00**	**18.88%**	**$ 15,770.00**	**18.88%**
B	CONTINGENCY	$ 3,000.00	$ -	$ -	$ -	0.00%	$ -	0.00%
D	OVERHEAD	$ 6,340.00	$ -	$ -	$ 1,925.00	2.30%	$ 1,925.00	2.30%
E	**TOTAL COST (A + B)**	**$ 83,515.23**	**$ -**	**0.00%**	**$ 17,695.00**	**21.19%**	**$ 17,695.00**	**21.19%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ...../ 2022

Eng/Arch.Francisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico
Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e
Validação de Qualidade ADN , I. P.

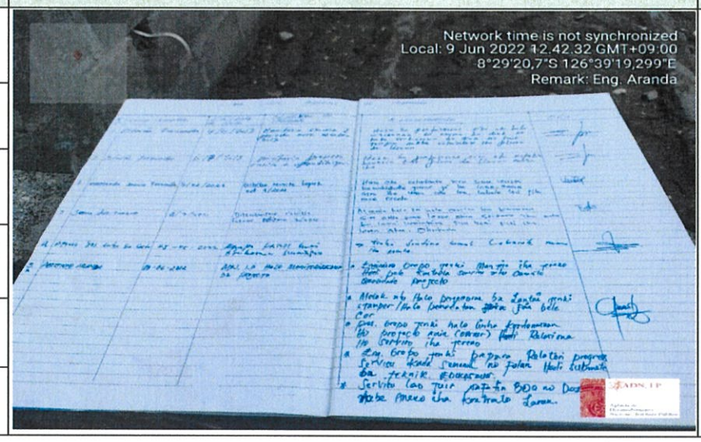
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (LA-8)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : Construsaun/Rehabilitasaun da Escola EBF libagua

Kompanhia : GRUPO Komunitaruio Libagua

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Thursday, June 09, 2022	Baucau , Lagal	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Eng.grupo tenki mantein iha terenu hodi bele kontrola servisu hodi garante kualidade projecto		
					2	Molok atu halo pengecoran ba lantai tenki Stamper/halo pemdatan lai hafoin bele cor		
					3	Pres.grupo tenki halo linha kordenasaun ho projecto nain(Owner)relasiona ho servisu iha terenu		
					4	Prepara relatori progres servisu kada semanal Fulanhodi submete ba teknik educasaun		
					5	Servisu lao tuir nafatin BOQ no Dezenho nebe anexo iha kontrato laran		
					6	Kontinua nafatin servisu		

#ANEXU C1 (BA- 8)
Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA SECUNDARIO GERAL PUBLICO FILIAL BAGUIA**

No. kontratu :

Data Inspesaun : Thrusday, Juny 23, 2022

Fatin Inspesaun : Baucau , Baguia,Alawa kraik

Koordinadas :

Start Point : Long: **-8.628371** , Latetude : **126.654175**

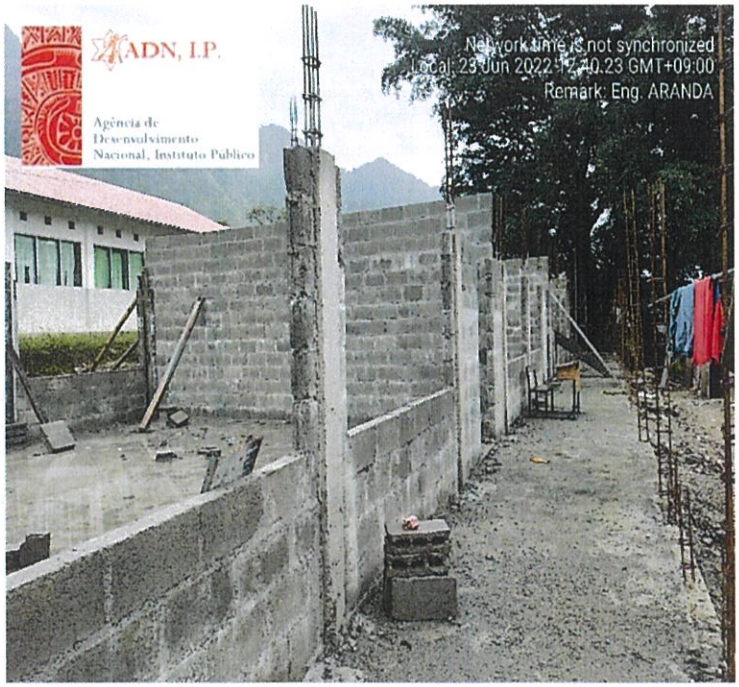
End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

2. .....

3. .....

Foto iha terenu	*Observa/Recommend. iha tereno*
Building B tampak samping	



1. Jarak senkang tenki tuir dezenho
2. Eng.Grupo tnki mantein iha terene hodi bele halo jestaun ba servisu tamba servisu lao tarde liu
3. Servisu lapo tuir nafatin boq no dezneho nebe iha
4. Halo relatori progress
5. Boq no Dezenho tenki rai Iha terenu

#ANEXU C1 (BA- 8)
Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA SECUNDARIO GERAL PUBLICO FILIAL BAGUIA**

No. kontratu :

Foto iha terenu	*Observa/Recommend. iha tereno*
Area toilet	
	1. Ba Instalasaun nebe instala ona taka tiha hodi nune foer labele tama 2. Instalasaun tenki seting halo didiak nivelado
	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (BA-9)

PROJECT NAME : NOVA CONSTRUÇÃO ESCOLA SECUNDARIO GERAL PUBLICO FILIAL BAGUIA
NO CODE EMIS : 442
LOCATION : SUCO ALAUA CRAIC, POSTO ADMINISTRATIVO BAGUIA, MUNICIPIO BAUCAU .

Summary			Progress Juny 2022					
			PREVIOUS		THIS BILL		UP TO DATE	
No	ITEM SERVISU	VERIFIED BY A D N	TOTAL	WEIGH %	TOTAL	WEIGH %	TOTAL	WEIGH %
1	Preleminaries Work	$ 3,075.00	$ -	$ -	$ 1,975.00	1.13%	$ 1,975.00	1.13%
2	Class Room CB	$ 92,419.73	$ -	$ -	$ 24,159.58	2.39%	$ 24,159.58	2.39%
3	Class Room Building Cdl	$ 56,317.28	$ -	$ -	$ 9,583.19	0.27%	$ 9,583.19	0.27%
4	Provisional Sum For Demolition	$ 675.00	$ -	$ -	$ 675.00	0.38%	$ 675.00	0.38%
5	Provisional Sum For Site Works	$ 12,798.37	$ -	$ -	$ -	0.00%	$ -	0.00%
	Total Constructio Cost	**$ 165,285.38**	**$ -**	**$ -**	**$ 36,392.77**	**4.16%**	**$ 36,392.77**	**4.16%**
	Overhead	**$ 6,340.00**	**$ -**	**$ -**	$ 2,668.33	0.01%	$ 2,668.33	0.01%
	Contigency	**$ 3,000.00**	**$ -**	**$ -**	$ -	0.00%	$ -	0.00%
	Grand Total	**$ 175,519.47**	**$ -**	**$ -**	**$ 39,061.11**	**4.17%**	**$ 39,061.11**	**4.17%**

Prepara husi :
Date; ...../ ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Francisco Xavier de D. Jeronimo
Senior Engineiro ba Projecto Edificio Publico Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

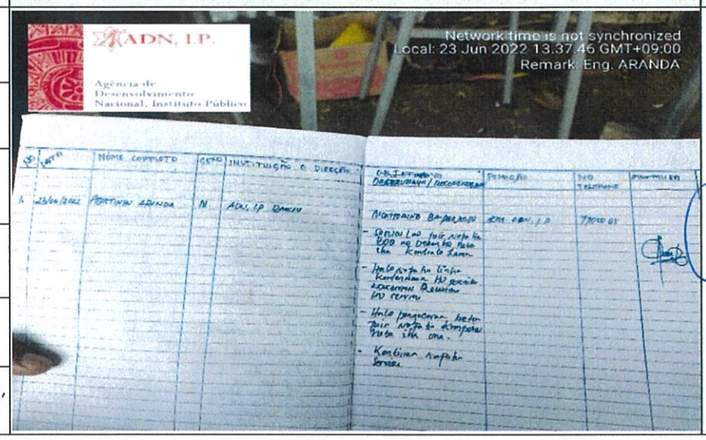
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (LA-8)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NOVA CONSTRUÇÃO ESCOLA SECUNDARIO GERAL PUBLICO FILIAL BAGUIA

Kompanhia : GRUPO Komunitaruio

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Thursday, June 23, 2022	Baucau , Lagal	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Jarak senkang tenki tuir dezenho		
					2	Eng.Grupo tnki mantein iha terene hodi bele halo jestaun ba servisu tamba servisu lao tarde liu		
					3	Servisu lapo tuir nafatin boq no dezneho nebe iha		
					4	Halo relatori progress		
					5	Boq no Dezenho tenki rai Iha terenu		
					6	Ba Instalasaun nebe instala ona taka tiha hodi nune foer labele tama, Instalasaun tenki seting halo didiak nivelado		

#ANEXU C1 (BA- 9)
Back-up Data

Naran Projeto : **NOVA CONSTRUCAO PRE ESKOLAR-1342 LARISULA**
No. kontratu :

Data Inspesaun : Thrusday, Juny 23, 2022

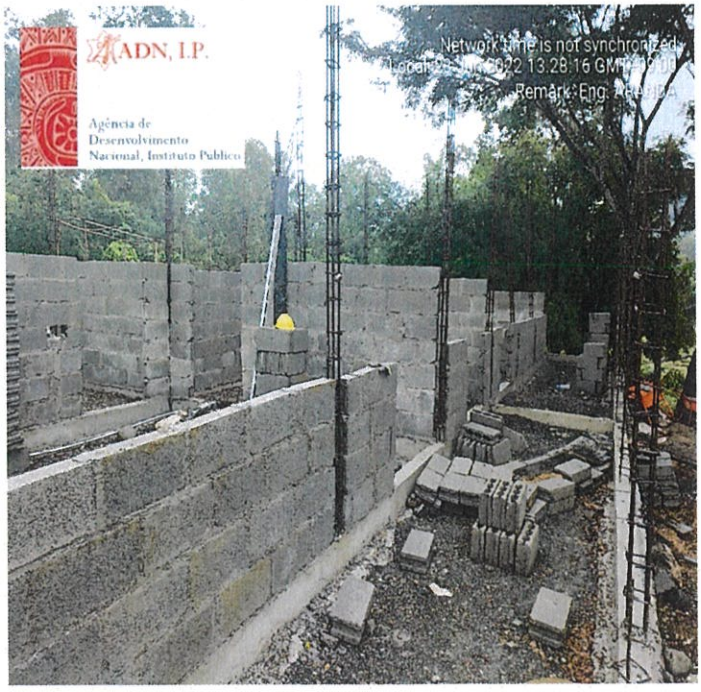
Fatin Inspesaun : Baucau , Baguia ,Larisula

Koordinadas :

Start Point : Long: Latetude :

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

Foto iha terenu	*Observa/Recommend. iha tereno*
Class Room Building C , Toilet Building	
	1. Husu ba eng.atu halo pengecoran ba beton sira ne tenki didiak bekisting no uja vibrator para lebele beton labele kropos. 2. Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (BA-9)

NARAN PROJETU : **NOVA CONSTRUCAO PRE ESKOLAR-1342 LARISULA**
FATIN PROJETU : **LARISULA-BAGUIA-BAUCAU**
PROJETU NAIN : **MEJD**

MAIN SUMMARY			Progress Juny 2022					
			PREVIOUS		THIS BILL		UP TO DATE	
NO	DESCRIPTION	AMOUNT (USD)	TOTAL	WEIGH %	TOTAL	WEIGH %	TOTAL	WEIGH %
I	PRELIMINARIES	3,379.27	$ -	0.00%	$ 1,946.28	1.22%	$ 1,946.28	1.22%
II	CLASSROOM BUILDING C2	69,330.85	$ -	0.00%	$ 12,839.46	8.07%	$ 12,839.46	8.07%
III	PROVISIONAL SUM FOR SITEWORKS	14,995.93	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**87,706.05**	**-**	**-**	**14,785.74**	**9.30%**	**14,785.74**	**9.30%**
B	CONTINGENCY	3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
C	OVER HEAD	6,340.00	$ -	0.00%	$ 2,131.00	1.34%	$ 2,131.00	1.34%
D	**TOTAL COST (A + B + C)**	**97,046.05**	**-**	**0.00%**	**16,916.74**	**10.64%**	**16,916.74**	**10.64%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Françisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no
Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação
de Qualidade ADN , I. P.

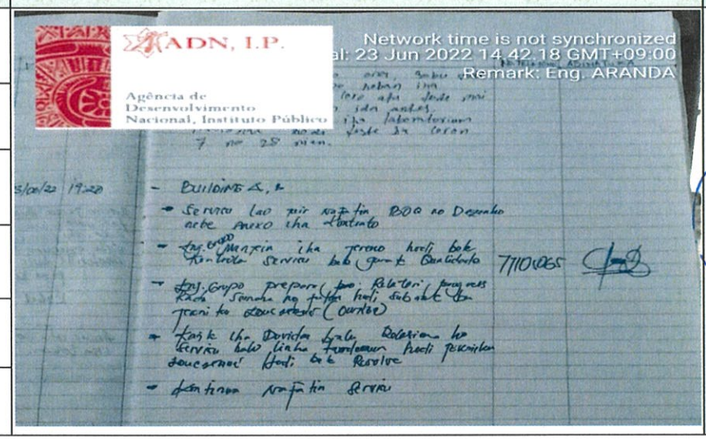
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (BA-9)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NOVA CONSTRUCAO PRE ESKOLAR-1342 LARISULA

Kompanhia : GRUPO Komunitario

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Thursday, June 23, 2022	Baucau , Baguia, Larisula	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Husu ba eng.atu halo pengecoran ba beton sira ne tenki didiak bekisting no uja vibrator para lebele beton labele kropos.		
					2	Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton		
					3	antes halo pengecoran tenki konfirma ho owner para sira bele mai foti **slumb Test**		
					4	Sampel beton karik foti tiha tenki hoba 24 jam foin bele hasai no lori ba lab.hodi bel halo test		
					5	Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton		
					6	Toilet building antes atu ateru no halo pengecoran ba sloof sebele instala ona pipa		

#ANEXU C1 (BA-7)
Back-up Data

Naran Projeto: REHABILITAÇÃO ESCOLA BASICA CENTRAL OSSO HUNA
No. kontratu :

Data Inspesaun : Thursday, Juny 23, 2022

Fatin Inspesaun : Baucau,Baucau Villa

Koordinadas :

Start Point : Long: ....., Latetude : .....

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. AGUSTINHO ARANDA

Foto iha terenu	*Observa/Recommend. iha tereno*

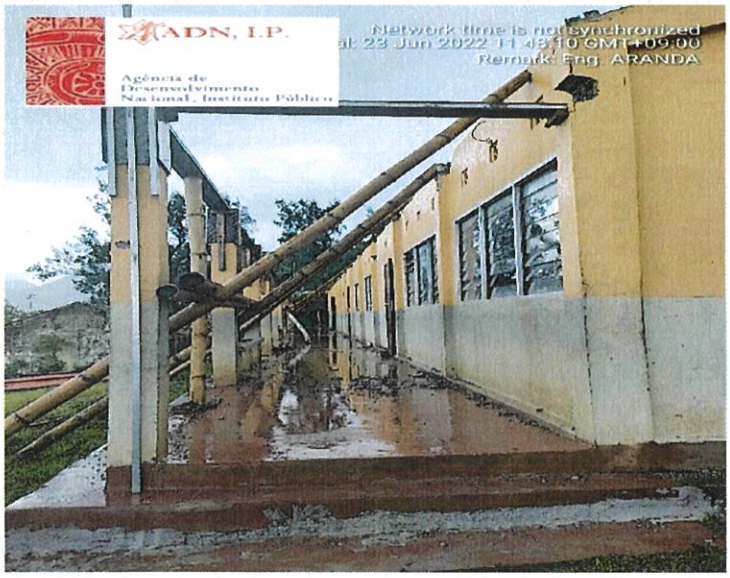
UMA RF1 (STEEL ROOF STRUCTURE)



1. Servisu tenki lao tuir BOQ no DEZENHO nebe iha
2. Eng.Grupo tenki mantein iha terenu ho atu kontrola servisu hodi bele garante qualidade projecto
3. Eng.Grupo tenki prepar relatori prpgres servisu kada seman no fulan
4. Monta steel roof tenki foti kemiringan halo lolos

#ANEXU C1 (BA-7)
Back-up Data

Naran Projeto: REHABILITAÇÃO ESCOLA BASICA CENTRAL OSSO HUNA
No. kontratu :

Foto iha terenu	*Observa/Recommend. iha tereno*
Uma RF2 (Formwork (bekisting) sloof	
	1. Seting didiak bekisting antes atu halo pengecoran beton 2. Atu halo pengecoran karik pastikan udan tenki para hodi labele impaktu ba mutu beton 3. Campuran Beton tenki tuir komposisi nebe iha ona 4. Ba instalasaun electrical tenki instala ho didiak
	1. Servisu durante semana 2 parado tamba impaktu husi udan

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PROJECT NAME : **REHABILITAÇÃO ESCOLA BASICA CENTRAL OSSO HUNA NO CODE EMIS : 343**

LOCATION : **SUCO OSSO HUNA, POSTO ADMINISTRATIVO, BAGUIA MUNICIPIO BAUCAU.**

#ANEXU C2 (BA-7)

Summary			PROGRES JUNY 2022					
No	ITEM SERVISU	VERIFIED BY A D N	PREVIOUS		THIS BILL		UP TO DATE	
			AMOUNT$	WEIGH %	AMOUNT$	WEIGH %	AMOUNT$	WEIGH %
1	Preleminaries Work	$ 3,075.00	$ -	0.00%	$ 2,015.00	2.39%	$ 2,015.00	2.39%
2	Refurbished Room Building RF1	$ 36,310.43	$ -	0.00%	$ 11,682.76	13.86%	$ 11,682.76	13.86%
3	Refurbished Room Building RF2	$ 30,599.03	$ -	0.00%	$ 4,647.00	5.51%	$ 4,647.00	5.51%
3	Provicional for external Electrical instalation	$ 4,493.91	$ -	0.00%	$ -	0.00%	$ -	0.00%
4	Provicional for Demolition	$ 446.20	$ -	0.00%	$ -	0.00%	$ -	0.00%
I	**Total Constructio Cost**	**$ 74,924.57**	**$ -**	**0.0%**	**$ 18,344.76**	**21.8%**	**$ 18,344.76**	**21.8%**
II	**Overhead**	**$ 6,340.00**	**$ -**	**0.0%**	**$ 3,394.50**	**4.03%**	**$ 3,394.50**	**4.03%**
II	**Contigency**	**$ 3,000.00**	**$ -**	**0.0%**	**$ -**	**0.00%**	**$ -**	**0.00%**
IV	**Grand Total**	**$ 84,264.57**	**$ -**	**0.0%**	**$ 21,739.26**	**25.80%**	**$ 21,739.26**	**25.80%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Françisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no
Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação
de Qualidade ADN , I. P.

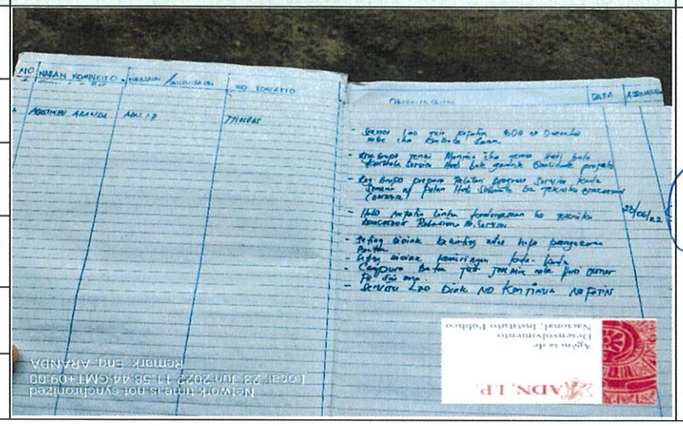
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (BA-7)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : REHABILITAÇÃO ESCOLA BASICA CENTRAL OSSO HUNA

Kompanhia : GRUPO Komunitaruio OSSO HUNA

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	**Thursday, June 23, 2022**	Baucau , Baguia	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Eng.grupo tenki mantein iha terenu hodi bele kontrola servisu hodi garante kualidade projecto		
					2	Molok atu halo pengecoran ba lantai tenki Stamper/halo pemdatan lai hafoin bele cor		
					3	Pres.grupo tenki halo linha kordenasaun ho projecto nain(Owner)relasiona ho servisu iha terenu		
					4	Prepara relatori progres servisu kada semanal Fulanhodi submete ba teknik educasaun		
					5	Servisu lao tuir nafatin BOQ no Dezenho nebe anexo iha kontrato laran		
					6	Kontinua nafatin servisu		

#ANEXU C1 (QUE- 12)
Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA BASICA CENTRAL LETEMUMU**
No. kontratu :

Data Inspesaun : Thrusday, Juny 30, 2022

Fatin Inspesaun : Baucau , Quelicai,Letemumu

Koordinadas :

Start Point : Long: **-8.602496666** Latetude : **126.55798166**

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

Foto iha terenu	*Observa/Recommend. iha tereno*
Class Room Building C	
	1. Rai nebe ateru iha lantai lantai tenki stamper / halo pemadtan ho diak 2. Jarak antara senkang tenki tuir dezenho 3. Eng.Grupo tenki mantein iha terenu
	Observa/Recommend. iha tereno

#ANEXU C1 (QUE- 12)
Back-up Data

Naran Projeto : **NOVA CONSTRUÇÃO ESCOLA BASICA CENTRAL LETEMUMU**
No. kontratu :

Class Room Building CDL



1. Sampel beton nebe foti tiha tenki hoba 24 jam foin bele hasai no lori ba lab.hodi bel halo test
2. Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton



1. Toilet building antes atu ateru no halo pengecoran ba sloof sebele instala ona pipa

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (QUE-12)

PROJECT NAME : **NOVA CONSTRUÇÃO ESCOLA BASICA CENTRAL LETEMUMU LOCATION**
: **SUCO LETEMUMU, POSTO ADMINISTRATIVO QUELICAI,**

Summary			Progress Juny 2022					
No	ITEM SERVISU	VERIFIED BY A D N	UP TO DATE		UP TO DATE		UP TO DATE	
			TOTAL	WEIGH %	TOTAL	WEIGH %	TOTAL	WEIGH %
1	Preleminaries Work	$ 3,075.00	$ -	0.00%	$ 1,775.00	1.12%	$ 1,775.00	1.12%
2	Class Room Building C (2 Unit 2x54,257.08)	$ 104,951.45	$ -	0.00%	$ 8,475.19	5.33%	$ 8,475.19	5.33%
3	Toilet Building	$ 26,129.19	$ -	0.00%	$ 3,211.87	2.02%	$ 3,211.87	2.02%
5	Provisional Sum For Site Works	$ 15,570.11						
I	**Total Constructio Cost**	**$ 149,725.75**	**$ -**	**0.00%**	**$ 13,462.06**	**8.46%**	**$ 13,462.06**	**8.46%**
II	**Overhead**	**$ 6,340.00**	**$ -**	**0.00%**	**$ 2,238.00**	**1.41%**	**$ 2,238.00**	**1.41%**
III	**Contigency**	**$ 3,000.00**	**$ -**	**0.00%**	**$ -**	**0.00%**	**$ -**	**0.00%**
IV	**Grand Total**	**$ 159,065.75**	**$ -**	**0.00%**	**$ 15,700.06**	**9.87%**	**$ 15,700.06**	**9.87%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Francisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no
Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação
de Qualidade ADN , I. P.

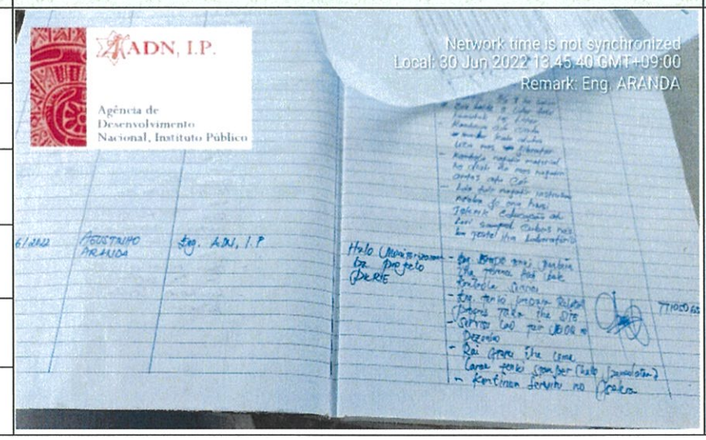
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (QUE-12)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NOVA CONSTRUÇÃO ESCOLA BASICA CENTRAL LETEMUMU

Kompanhia : GRUPO Komunitaruio Letemumu

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Thursday, June 30, 2022	Baucau , Quelicai, Letemumu	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Rai nebe ateru iha lantai lantai tenki stamper / halo pemadtan ho diak		
					2	Jarak antara senkang tenki tuir dezenho		
					3	Eng.Grupo tenki mantein iha terenu		
					4	Sampel beton nebe foti tiha tenki hoba 24 jam foin bele hasai no lori ba lab.hodi bel halo test		
					5	Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton		
					6	Toilet building antes atu ateru no halo pengecoran ba sloof sebele instala ona pipa		

#ANEXU C1 (QUE- 13)
Back-up Data

Naran Projeto : **NOVA CONSTRUCAO EBF-1114 DARLA'A**
No. kontratu :

Data Inspesaun : Thrusday, Juny 30, 2022

Fatin Inspesaun : Baucau , Quelicai,Laisorlai

Koordinadas :

Start Point : Long: Latetude :

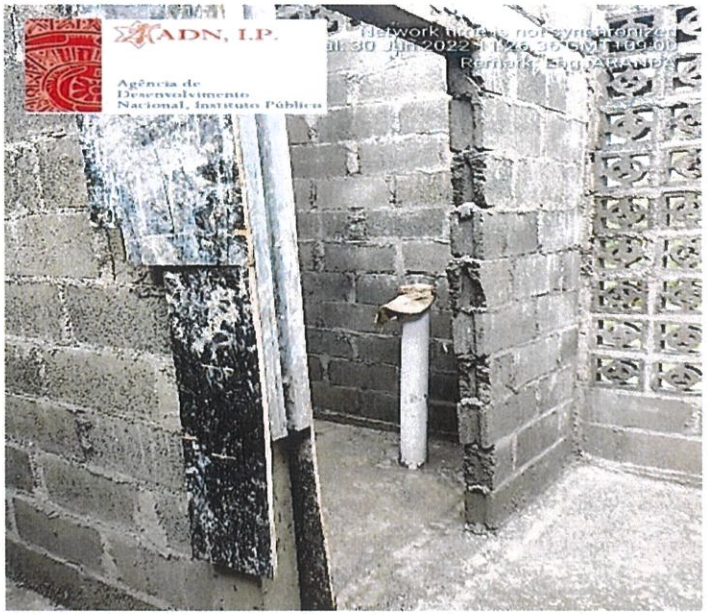
End Point : Long: ....., Latetude : .....

Naran Inspector : 1. Agustinho Aranda

Foto iha terenu	*Observa/Recommend. iha tereno*
Class Room Building C , Toilet Building	
	1. Husu ba eng.atu halo pengecoran ba beton sira ne tenki didiak bekisting no uja vibrator para lebele beton labele kropos. 2. Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton

#ANEXU C1 (QUE- 13)
Back-up Data

Naran Projeto : **NOVA CONSTRUCAO EBF-1114 DARLA'A**
No. kontratu :

Foto iha terenu	*Observa/Recommend. iha tereno*
Class Room Building CDL	
	1. Eng.kompanhia halo relatori progress taka iha site 2. BOQ no Dezenho rai iha SITE
	1. Toilet building karik udan para sebele kontinua halo servisu plester hodi bele aselera

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (QUE-13)

NARAN PROJETU : NOVA CONSTRUCAO EBF-1114 DARLA'A
FATIN PROJETU : LAISORULAI-QUELICAI-BAUCAU
PROJETU NAIN : MEJD

MAIN SUMMARY			Progress Juny 2022					
			UP TO DATE		UP TO DATE		UP TO DATE	
NO	DESCRIPTION	AMOUNT (USD)	TOTAL	WEIGH %	TOTAL	WEIGH %	TOTAL	WEIGH %
I	PRELIMINARIES	3,348.03	$ -	0.00%	$ 1,584.21	1.00%	$ 1,584.21	1.00%
II	CLASSROOM BUILDING C	55,772.91	$ -	0.00%	$ 19,470.68	12.24%	$ 19,470.68	12.24%
III	TOILET BUILDING Tb	27,864.48	$ -	0.00%	$ 10,412.03	6.55%	$ 10,412.03	6.55%
IV	PROVISIONAL SUM FOR SITEWORKS	10,246.45	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**97,231.86**	**-**	**0.00%**	**31,466.92**	**19.78%**	**31,466.92**	**19.78%**
B	CONTINGENCY	3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
D	OVERHEAD	6,340.00	$ -	0.00%	$ 2,718.00	1.71%	$ 2,718.00	1.71%
E	**TOTAL COST (A + B)**	**106,571.86**	**$ -**	**0.00%**	**$ 34,184.92**	**21.49%**	**$ 34,184.92**	**21.49%**

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Françisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no
Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação
de Qualidade ADN , I. P.

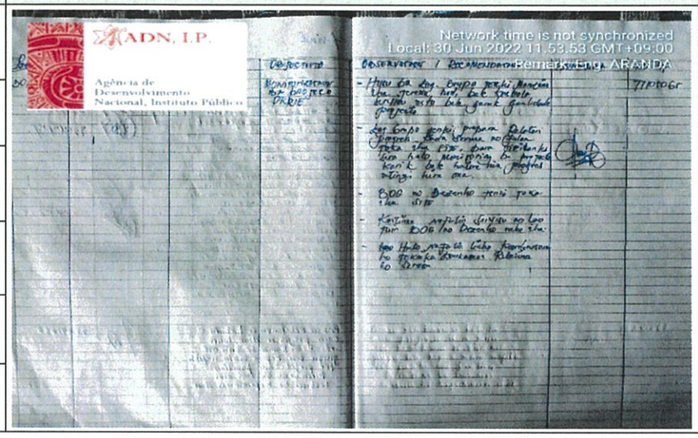
MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

#ANEXU D (QUE-13)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : : NOVA CONSTRUCAO EBF-1114 DARLA'A

Kompanhia : GRUPO Komunitario

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
1	Thursday, June 30, 2022	Baucau , Quelicai, Letemumu	Eng.Agustinho Aranda	Eng.ADN Municipio Baucau	1	Husu ba eng.atu halo pengecoran ba beton sira ne tenki didiak bekisting no uja vibrator para lebele beton labele kropos.		
					2	Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton		
					3	Eng.Grupo tenki mantein iha terenu		
					4	Sampel beton nebe foti tiha tenki hoba 24 jam foin bele hasai no lori ba lab.hodi bel halo test		
					5	Atu halo pengecoran ba beton pastikan udan labele tau atu nune labele impaktu ba mutu beton		
					6	Toilet building antes atu ateru no halo pengecoran ba sloof sebele instala ona pipa		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN
Agência de Desenvolvimento Nacional

PLANU INSPESAUN (EDIFICIU)

2022

Naran Eng.	AGUSTINHO ARANDA							JUNHO																										OBS
Municipio	BAUCAU																																	
MUNICIPIOS/POSTO	NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	NARAN COMP.	ACTION	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
Baucau Villa	5	Rehabilitation of MPWTC Office in the Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Co. Cactus Unip. Lda	Plan																															FHO
							Actual																															
	8	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	MINISTERIO SAUDE	Fundu Covid-19	SAUDE	Central Hill Unipessoal Lda	Plan																															ON GOING
							Actual																															
	10	Construsaun Escola Polo Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	FI	EDUKASAUN	Sanira Construction Unip Lda	Plan																															ABANDONA
							Actual																															
	13	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	SAMES	LM-BS	EDIFICIOS PUBLICOS	Talamori	Plan																															ON GOING
							Actual																															
	14	Rehabilitasaun ba EBF Maucale iha Aldeia Maucale Suco Gariuai Posto Administrativo Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE EBF MAUCALE	Plan																																OG GOING
							Actual																															
	15	Rehabilitasaun ba EBF Zona Golgota iha Aldeia Ro - Ulo Suco Bahu Posto Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE EBF ZONA GOLGOTA	Plan																																OG GOING
							Actual																															
	16	Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	Plan																																OG GOING
							Actual																															
	17	Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE EPEC/ESTV BAUCAU	Plan																																OG GOING
							Actual																															
	18	Rehabilitasaun ba ESG Filial Kilik Waiga'e iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE ESG FILIAL KILIK WAIGA'E	Plan																																OG GOING
							Actual																															
	19	Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE EBF CAIBADA MACASSAE	Plan																																OG GOING
							Actual																															
	20	Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDIFICIOS PUBLICOS	GRUPU KOMUNITARIU MEJD PKRIE ESG NO. 01 BAUCAU	Plan																																OG GOING
							Actual																															
Laga	8	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF LALA-BU'U	Plan																																OG GOING
							Actual																															
	9	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	Plan																																OG GOING
							Actual																															
	10	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF. FITUN SAGADATE-LAGA	Plan																																OG GOING
							Actual																															
	7	Rehabilitasaun ba EBF Gulari iha Aldeia Daraloi de Baixo Suco Samalari Postu Administrativu Baguia Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF GULARI	Plan																																OG GOING
							Actual																															

Naran Eng.	AGUSTINHO ARANDA							JUNHO																										OBS
Municipio	BAUCAU																																	
MUNICIPIOS/POSTO	NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	NARAN COMP.	ACTION	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
Baguia	8	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	Plan																															OG GOING
							Actual																															
	9	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF UACALA	Plan																															OG GOING
							Actual																															
	10	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EPE FINI BAGUIA	Plan																															OG GOING
							Actual																															
	11	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EPE LARI-SULA	Plan																															OG GOING
							Actual																															
	12	Rehabilitasaun ba EBC Ossu - Huna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBC OSSU-HUNA	Plan																															OG GOING
							Actual																															
	13	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBC BUAUA LAVATERI	Plan																															OG GOING
							Actual																															
	14	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE ESGF DE BAGUIA	Plan																															OG GOING
							Actual																															
Venilale	9	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBC UAI-BUA	Plan																															OG GOING
							Actual																															
	10	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF CULINA-OSSU-UAILALE	Plan																															OG GOING
							Actual																															
	11	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	Plan																															OG GOING
							Actual																															
Quelicai	7	New Construction of Health Post and Douctor House Building Municipality Baucau	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Jova Construction Unip. Lda	Plan																															OG GOING
							Actual																															
	8	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF UADA-BORU	Plan																															OG GOING
							Actual																															
	9	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF UAI-ACA/MULIA	Plan																															OG GOING
							Actual																															
	10	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF ABO-LIR LALETEK	Plan																															OG GOING
							Actual																															
	11	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBC LETEMUMO	Plan																															OG GOING
							Actual																															
	12	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	Plan																															OG GOING
							Actual																															
	13	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu	MINISTERIO EDUKASAUN	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF	Plan																															OG GOING

Naran Eng.	AGUSTINHO ARANDA							JUNHO																										OBS
Municipio	BAUCAU																																	
MUNICIPIOS/POSTO	NU.	NARAN PROJ.	DONO PROJ.	KAT. PROJ.	SECTOR	NARAN COMP.	ACTION	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
	13	Jiif - Laco/Lor - Rua Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	MEJD PKRIE EBF CATOLICA DARENAFA	Actual																														OG GOING
	14	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF MAURO DARALA/BORUMODO	Plan																														OG GOING
							Actual																														
	15	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	GRUPU KOMUNITARIU MEJD PKRIE EBF UAIDORA/OSSOLIA	Plan																														OG GOING
							Actual																														
Vemasse	6	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	EDIFICIOS PUBLICOS	Esa-Un	Plan																														ABANDONA
							Actual																														
TOTAL PROJETO ON-GOING																																				

Note:

Periode inspesaun iha tereinu

Implementasaun Plano Periode inspesaun i Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Relatoriu avaliasuan mensal iha Dili

Prepara Husi :

(Agustinho Aranda)
Engineiro ADN, I. P. Municipio de Baucau

Sertifika Husi :

(Eng.Emerenciana da Costa Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi :

(Eng.Januario Maia Guteres)
Adjunto Director Executivo - ADN, I. P

#ANEXU C1 (VEN-9)

Back-up Data

Naran Projeto : **NOVA CONSTRUCAO PRE ESKOLAR-1347 AMIZADE VENILALE**
No. kontratu :

Data Inspesaun : Wednesday, Juny 22, 2022

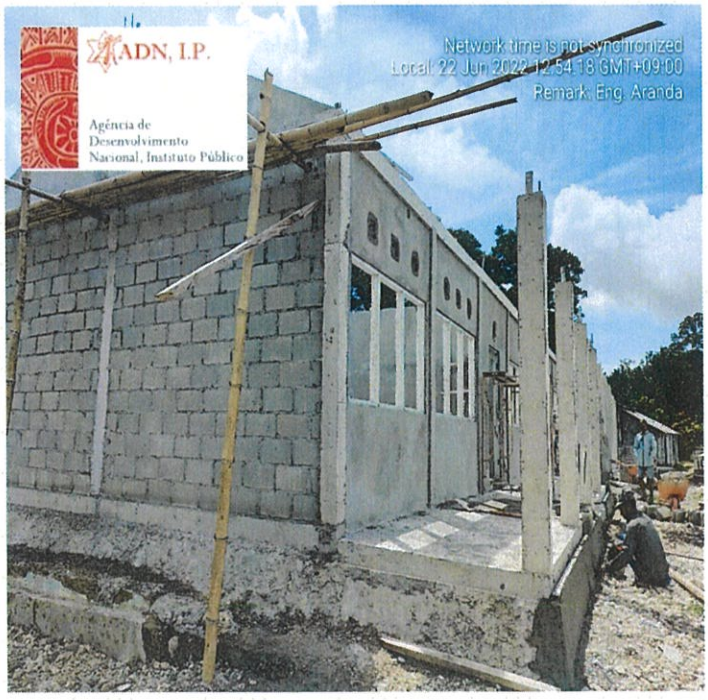
Fatin Inspesaun : **Baucau, Venilale, Uailaha**

Koordinadas :

Start Point : Long: ....., Latetude : .....

End Point : Long: ....., Latetude : .....

Naran Inspector : 1. AGUSTINHO ARANDA

Foto iha terenu	*Observa/Recommend. iha tereno*
	1. Ba kolom no sloof nebe kropos tenki hadia 2. Eng.grupo tenki prepara relatori progress 3. Ba kuda kuda sebele monta ho didiak hodi bele hetan ni kemiringan 4. Servisu seluk hanesan septitak halo dadauk dauk 5. Eng.Grupo tenki halo jestaun servisu atu nune labele kleur

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

NARAN PROJETU : **NOVA CONSTRUCAO PRE ESKOLAR-1347 AMIZADE VENILALE**
FATIN PROJETU : **UATOACO-VENILALE-BAUCAU**
PROJETU NAIN : **MEJD**

#ANEXU C2 (VEN-9)

MAIN SUMMARY

NO	DESCRIPTION	AMOUNT (USD)	PROGRES ACTUAL JUNY					
			PREVIOUS		THIS BILL		UP TO DATE	
I	PRELIMINARIES	3,254.31	$ -	0.00%	$ 1,538.58	1.72%	$ 1,538.58	1.72%
II	CLASSROOM BUILDING C2	64,688.96	$ -	2.63%	$ 23,406.76	26.13%	$ 23,406.76	26.13%
III	PROVISIONAL SUM FOR SITEWORKS	12,298.48	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**80,241.75**	$ -	2.63%	$ 24,945.34	27.85%	$ 24,945.34	27.85%
B	CONTINGENCY	3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
IV	OVER HEAD	6,340.00	$ -	0.00%	$ 2,605.00	2.91%	$ 2,605.00	2.91%
C	**TOTAL COST (A + B + C)**	**89,577.35**	$ -	2.63%	$ 27,550.34	30.76%	$ 27,550.34	30.76%

Prepara husi :
Date; ..... / ..... / 2022

Eng.Agustinho Aranda
Engineiro AND, I. P. Municipio de Baucau

Verifika husi :
Date; ..... / ..... / 2022

Eng/Arch.Françisco Xavier de D. Jeronimo
Senior Engineiro ba Porjecto Edificio Publico Beé no Saneamento ADN, I. P.

Serttifika husi :
Date; ..... / ..... / 2022

Eng.Emerenciana da Costa Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

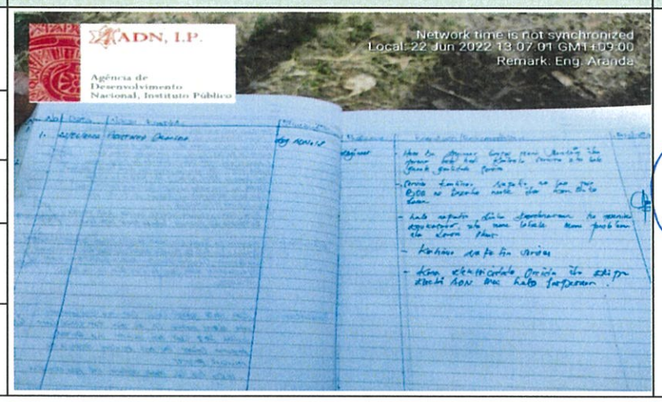
ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (VEN -9)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : NOVA CONSTRUCAO PRE ESKOLAR-1347 AMIZADE VENILALE

Kompanhia : Grupo Komunitario

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	Wednesday, June 22, 2022	Venilale , Uailaha	Eng.Agustinho Aranda	Eng.Adn Baucau	1	Ba kolom no sloof nebe kropos tenki hadia		
					2	Eng.grupo tenki prepara relatori progress		
					3	BOQ ho Dezneho tenki tau iha terenu		
					4	halo linha koordensaun ho owner		
					5	Aselera Servisu		

#Anexu C1 (MP-2)

Back-up Data

Naran Projeto : **Road Network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road**

No. kontratu : **ICB/078/MPWTC-2015**

Data Inspesaun : 06/ 06/ 2022

Fatin Inspesaun : Baucau-Lautem

Koordinadas :

Start Point : Long : 126'27"3,361 E, Latetude: -8.27'39, 004S


End Point : Long : 126'53"58,999 E, Latetude: -8.27'39, 004S

Naran Inspector : 1. Eng. Vidal Guterres

2. Eng. Deamantino H. Lopes

3. Eng. Jacob da Costa Camões

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu Reinforced Concrete Pipe Culvert, 1520mm dia., Class II	



Volume=11 l.m

#Anexu C1 (MP-2)

Back-up Data

Naran Projeto : **Road Network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road**

No. kontratu : **ICB/078/MPWTC-2015**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Item servisu Metal Guardrail (Metal Beam) including Concrete Posts **Volume= 4,286.25 l.m**	

#Anexu C1 (MP-2)


Back-up Data

Naran Projeto : **Road Network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road**

No. kontratu : **ICB/078/MPWTC-2015**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu Retainning Wall





Volume= 5,892.72 m3

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (MP- 2)

Project Name : Road Network Upgrading Sector Project (RNUSP) ADB Loan Nos.3341/3342(SF)-TIM Upgrading and Maintenance of Baucau-Lautem Section Sta.123+105 to Sta.182+040(with exceptions) ICB/078/MPWTC/2015

Contractor : CBMI Const.Co.,Ltd./Chongqing Road Engineering(Group)Co.,Ltd.

IPC no. : IPC. No. 20(February 01, 2022 - March 5, 2022)

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
100	GENERAL REQUIREMENTS	$ 2,063,252.00	$ 2,063,252.00	7.04%	$ -	0.00%	$ 2,063,252.00	7.04%	$ 0.00
200	EARHWORKS	$ 5,155,850.16	$ 4,845,114.66	16.53%	$ 177,289.06	0.60%	$ 5,022,403.73	17.13%	$ 133,446.44
300	SUBBASE AND BASE COURSES	$ 6,522,335.98	$ 5,880,839.17	20.06%	$ 297,214.67	1.01%	$ 6,178,053.84	21.07%	$ 344,282.14
400	SURFACE COURSE	$ 4,955,077.48	$ 4,534,151.66	15.47%	$ 296,643.39	1.01%	$ 4,830,795.05	16.48%	$ 124,282.43
500	BRIDGE CONSTRUCTION	$ 1,071,229.18	$ 996,191.25	3.40%	$ 12,000.00	0.04%	$ 1,008,191.25	3.44%	$ 63,037.93
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 6,455,958.11	$ 5,163,474.94	17.61%	$ 443,591.48	1.51%	$ 5,607,066.42	19.13%	$ 848,891.69
700	MISCELLANEOUS STRUCTURES	$ 1,193,530.20	$ -	0.00%	$ 367,643.25	1.25%	$ 367,643.25	1.25%	$ 825,886.95
800	BIO ENGINEERING	$ 142,981.40	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 142,981.40
DW	DAYWORKS	$ 305,612.88	$ 136,635.08	0.47%	$ 676.44	0.00%	$ 137,311.52	0.47%	$ 168,301.36
	PROVISIONAL SUM AND CONTINGENCY	$ 1,062,211.51	$ 324,535.66	1.11%	$ -	0.00%	$ 324,535.66	1.11%	$ 737,675.85
	TOTAL =	**$ 28,928,038.90**	**$ 23,944,194.42**	**81.68%**	**$ 1,595,058.29**	**5.44%**	**$ 25,539,252.71**	**87.12%**	**$ 3,388,786.18**
	PERFORMANCE BASED MAINTENANCE WORKS	$ 387,307.20	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 387,307.20
	CONTRACT AMOUNT	**$ 29,315,346.10**	**$ 23,944,194.42**	81.68%	**$ 1,595,058.29**	5.44%	$ -	87.12%	**$ 29,315,346.10**
	GRAND TOTAL	**$ 29,315,346.10**	**$ 23,944,194.42**	**81.68%**	**$ 1,595,058.29**	**5.44%**	**$ 25,539,252.71**	**87.12%**	**$ 3,776,093.38**

Inspesaun Husi :

1. (Eng. Deamantino H. Lopes)
Eng. ba projetu Infraestrutura Transporte e Irrigasaun Munisipiu Lautem, ADN, I.P

2. (Eng. Geovanio M. X. C. Aleixo)
Eng. ba projetu Infraestrutura Transporte e Irrigação Munisipiu Lautem, ADN, I.P

3. (Eng. Jacob da Costa Camões)
Eng. ba Projetu Infraestrutura Tansporte e Irrigasaun Munisipiu Baucau, ADN, I.P.

4. (Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projecto (Imprestimo) ADN, I.P.

5. (Eng. Vidal Guterres)
Eng. PMU ba Projecto (Imprestimo) ADN. I.P.

Verifika Husi :

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba projeito Infraestrutura, Transporte e Irrigasaun, ADN, I.P.

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

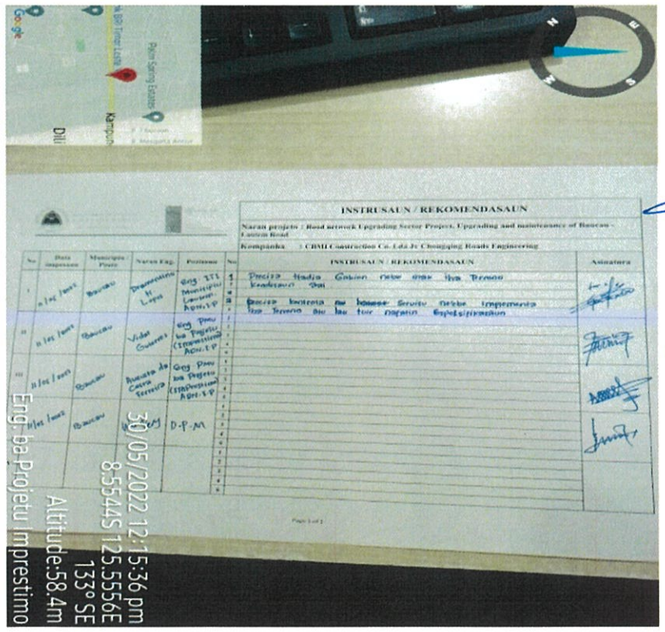
Agência de Desenvolvimento Nacional, Instituto Público

ANEXU D (MP-2)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Road network Upgrading Sector Project, Upgrading and maintenance of Baucau - Lautem Road

Kompanha : CBMI Construction Co. Lda Jv Chongqing Roads Engineering

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	6/6/2022	Baucau-Lautem	Deamantino H. Lopes	Eng. Ba Projetu ITI Munisipiu Lautem, ADN, I.P.	1	Presiza kontrola servisu ne'ebe implementa iha Terreno atu lao tuir nafatin espesifikasaun.		
II			Geovanio M. X. C Aleixo	Eng. Ba Projetu ITI Munisipiu Lautem, ADN, I.P.				
III			Jacob da Costa Camões	Eng. Ba Projetu ITI Munisipiu Baucau, ADN, I.P.				
IV			Vidal Guterres	Eng. PMU ba Projetu (Imprestimo), ADN, I.P.				
V			Augusta da Costa Ferreira					

#ANEXU C1 (BV – 2)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN: 00000340**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Acessores bac abo baixadas seidauk installa	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Start point	

#ANEXU C1 (BV – 2)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN: 00000340**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Cabo Baixadas tabele no tesi ai nebe besik iha linha	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Lampu Manutensaun seidauk installa	

#ANEXU CI (BV-4)

Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075**
No. kontratu : **SSS/066/MOPTC-2017**

Data Inspesaun : 01 Junho 2022


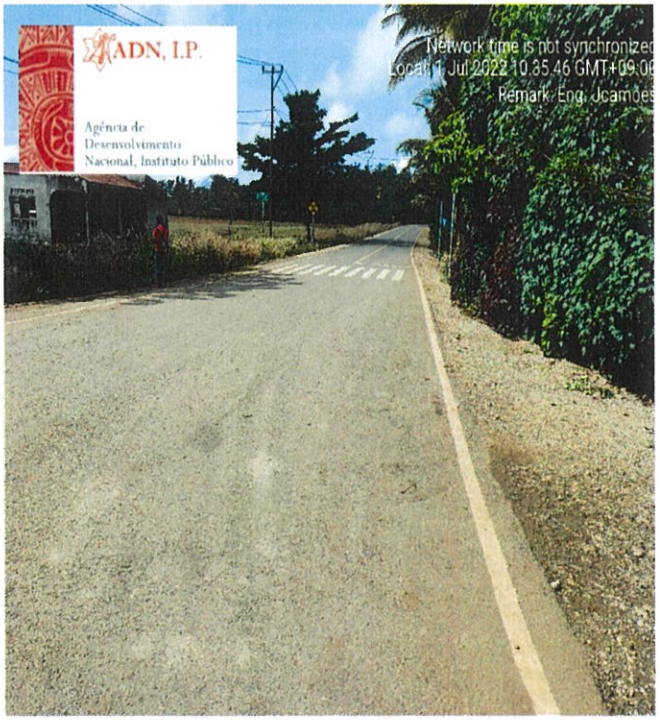
Fatin Inspesaun : Baucau Vila, Triloka - Fatumaka

Koordinadas :

Start Point : Long : -8.53136333 Latetude : 126.34772833

End Point : Long : -8.57320340 Latetude : 126.335748333

Naran Inspector : 1. Jacob da Costa Camoes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu Subbase, Base course and Asphal  Subbase course = 31.423 x 7 x 0.25 = 55 m3 Base Course = 3004.50 x 5 x0.20 = 3004.50 m3 Prime coat = 6050 x 5 = 30250 m2	

#ANEXU CI (BV-4)

Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075**

No. kontratu : **SSS/066/MOPTC-2017**

Item servisu agr Asphal hotu ona



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (BV-3)

PROJECT DATA

Project Name	: Rehabilitation of Roads Jct. A01 Triloca - Jct. A06 Fatumaca - Loilubu - Jct. A06 Venilale road
Road Section	: Sta. 0+000 - 6+025 (Package I)
Contractor	: Domin Timor Diak Construction, Lda
Contract Number	: SSS/078/MOPTC-2017
Contract Date	: September, 12th 2017
Contruction Period	: 365 Days
Completion date	: May, 30th 2021
Defect Liability Period	: 365 Days
Contract Amount	: $ 3,599,951.87

ITEM NO	ITEM DESCRIPTION	AMOUNT (US$)		WEIGHT (%)	Progress Previus Payment		Progress Previus Fulan 1-7		Progress Phisic Junho		Progress Up to date	
		Original	Variation Order		Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)
100	GENERAL REQUIEMENT	$ 25,480.62	$ 25,480.62	0.71%	15,155.42	0.42%	$ 18,635.86	0.52%	$ -	0.00%	$ 18,635.86	0.52%
200	EARTH WORKS	*$ 361,076.76*	*$ 346,362.23*	10.03%	177,253.49	4.92%	$ 358,114.24	9.95%	$ -	0.00%	$ 358,114.24	9.95%
300	SUBBASE AND BASE COURSE	$ 1,240,459.52	$ 1,118,026.41	34.46%	1,082,192.33	30.06%	$ 1,118,026.42	31.06%	$ -	0.00%	$ 1,118,026.42	31.06%
400	SURFACE COURSE	$ 1,383,899.14	$ 1,383,899.14	38.44%	34,031.92	0.95%	$ 1,383,899.14	38.44%	$ 1,378.16	0.04%	$ 1,385,277.30	38.48%
500	BRIDGE CONSTRUCTION	$ 327,666.05	$ 23,474.41	9.10%	9,106.15	0.25%	$ 23,474.41	0.65%	$ -	0.00%	$ 23,474.41	0.65%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 59,953.05	$ 492,645.06	1.67%	59,630.06	1.66%	$ 314,684.16	8.74%	$ -	0.00%	$ 314,684.16	8.74%
700	MISCELLANEOUS STRUCTURES	$ 201,416.73	$ 210,063.99	5.59%	-	0.00%	$ 12,353.23	0.34%	$ -	0.00%	$ 12,353.23	0.34%
	GRANT TOTAL	**$ 3,599,951.87**	**$ 3,599,951.87**	**100.00%**	**$ 1,377,369.36**	**38.26%**	**$ 3,229,187.47**	**89.70%**	**$ 1,378.16**	**0.04%**	**$ 3,230,565.63**	**89.74%**

Inspeksaun Husi :

Eng. Jacob Da costa Camoes
Eng. Ba Projeito Insfrasturctura e Irigasaun , ADN, I.P

Verifika Husi :

Eng. Remigio Da.C. dos Santos
Eng. Senior ba Projeito Insfrasturctura e Irigasaun , ADN, I.P

Certified By:

(Eng. Emerenciana da Costa M.Freitas.)
Coordenadora da Unidade de Controlo e Validação de Qualidade, ADN,IP.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

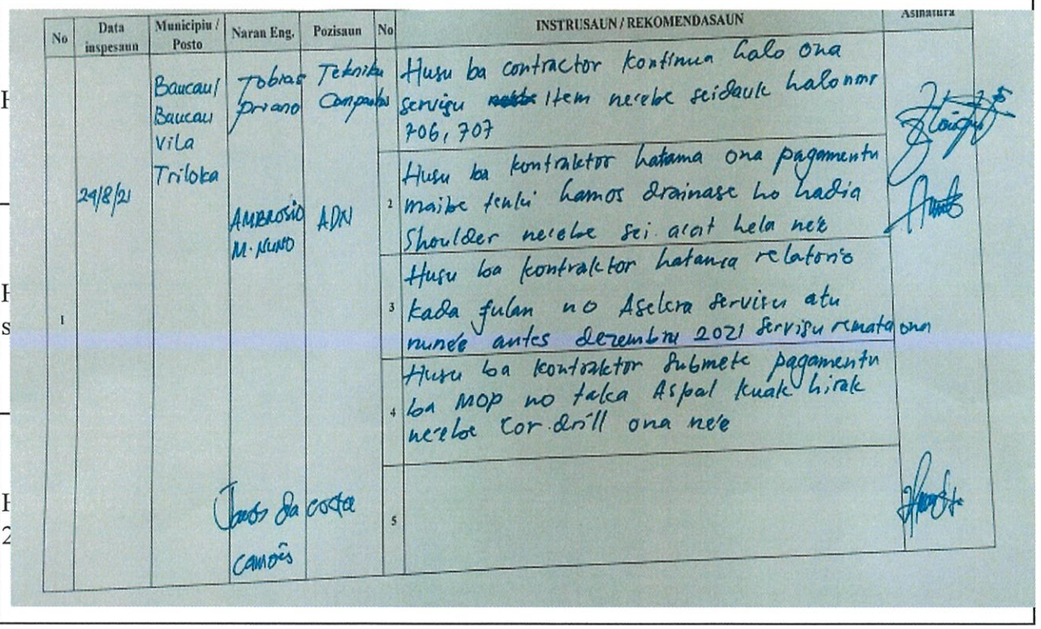
Agência de Desenvolvimento Nacional, Instituto Público

ANEXU D (BV-3)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025

Kompanha : Domin Timor Diak. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	1/7/2022	Baucau Villa	Jacob da Costa Camoes	Eng. Baucau	1	H	
					2	H s	
					3	H 2	



#ANEXU C1 (BV-3)

Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025**
No. kontratu : **SSS/078/MOPTC-2017**

Data Inspesaun :

Fatin Inspesaun : Baucau, Triloka

Koordinadas :

Start Point : Long : -8.4899755, Latetude : 126.36965833

End Point : Long : -8.53136333, Latetude : 126.34772833


Naran Inspector : 1. Ambrosio Martins Nuno

2. Jacob da Costa Camoes

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu AC-BC husi STA. 0+000 – 6 +025	



Volume AC-BC = 6.025 x 5 x 0.06 = 18075 m3

#ANEXU C1 (BV-3)

Back-up Data

Naran Projeto : **Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025**
No. kontratu : **SSS/078/MOPTC-2017**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu Cor drill Surface Course Parte Laboratorium ADN IP hamutuk ho Municipiu Halo servisu Cor drill ba Aspal Paket 1	
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

PROJECT DATA

#ANEXU C2 (BV-4)

Project Name: Rehabilitation of Roads Jct. A01 Triloca - Jct. A06 Fatumaca - Loilubu - Jct. A06 Venilale road

Road Section: Sta. 6+025 - 12+075 (Package II)

Contractor: Gihon Unipessoal, Lda

Contract Number: SSS/078/MOPTC-2017

SUMMARY

ITEM NO.	ITEM DESCRIPTION	ORIGINAL CONTRACT		Progress Paymet		Progres Phisic Previous 2022		Progres Phisic Junho 2022		Progres Phisic Up to date	
		Amount (USD)	Weight %	Amount (USD)	Weight %	Amount (USD)	Weight %	Amount (USD)	Weight %	Amount (USD)	Weight %
100	GENERAL REQUIEMENT	$ 13,464.00	0.39%	$ 5,610.00	0.16%	$ 7,124.70	0.21%	$ -	0.00%	$ 7,124.70	0.21%
200	EARTH WORKS	$ 229,255.44	6.64%	$ 185,924.31	5.39%	$ 185,924.32	5.39%	$ -	0.00%	$ 185,924.32	5.39%
300	SUBBASE AND BASE COURSE	$ 1,245,606.67	36.10%	$ 966,740.20	28.01%	$ 1,071,716.05	31.06%	$ -	0.00%	$ 1,071,716.05	31.06%
400	SURFACE COURSE	$ 1,389,641.45	40.27%	$ 68,063.82	1.97%	$ 1,332.22	0.04%	$ 1,378.16	0.04%	$ 2,710.38	0.08%
500	BRIDGE CONSTRUCTION	$ 131,299.24	3.80%	$ 22,425.80	0.65%	$ 22,425.80	0.65%	$ -	0.00%	$ 22,425.80	0.65%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 240,183.43	6.96%	$ 116,789.85	3.38%	$ 116,789.85	3.38%	$ -	0.00%	$ 116,789.85	3.38%
700	MISCELLANEOUS STRUCTURES	$ 201,416.73	5.84%	$ -	0.00%	-	0.00%	-	0.00%	$ -	0.00%
	GRANT TOTAL	$ 3,450,866.97	100.00%	$ 1,365,553.99	39.57%	$ 1,405,312.94	40.72%	$ 1,378.16	0.04%	$ 1,406,691.09	40.76%

Inspeksaun Husi :

Eng. Jacob Da Costa Camoes
Eng. Ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Verifika Husi :

Eng. Remogio Da.C.dos Santos
Eng. Senior ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Certifika Husi :

Eng. Emerenciana Da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

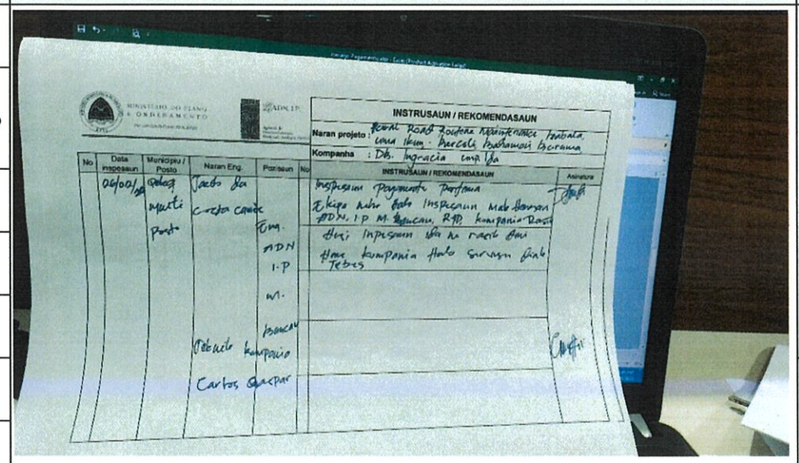
ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (MP-6)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800

Kompanha : DB-Ingracia Unipessoal Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	22/07/2022	Baucau/Venilale	Jacob da costa Camoes	Eng.ADN.I.P. M.Baucau	1	Trabalhador la kolabora diak ho Eng. Kompania hodi difikulta ba servisu iha terenu lao tarde		
					2	Husu kompania atu koalia didiak ho Autoridade lokal hodi fo solusaun ne'ebe diak no halo kolaborasaun atu nune'e servisu bele lao ho diak		
					3			
					4			
					5			
II				Eng.ADN.I.P. M.Baucau	1			
					2			
					3			
					4			
					5			

#ANEXU C1 (MP - 6)

Back-up Data

Naran Projeto : **R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800**
No. kontratu : **MPW-W-210049**

Data Inspesaun : 22 – 07 - 2022

Fatin Inspesaun : Uma Ana ikun

Koordinadas :

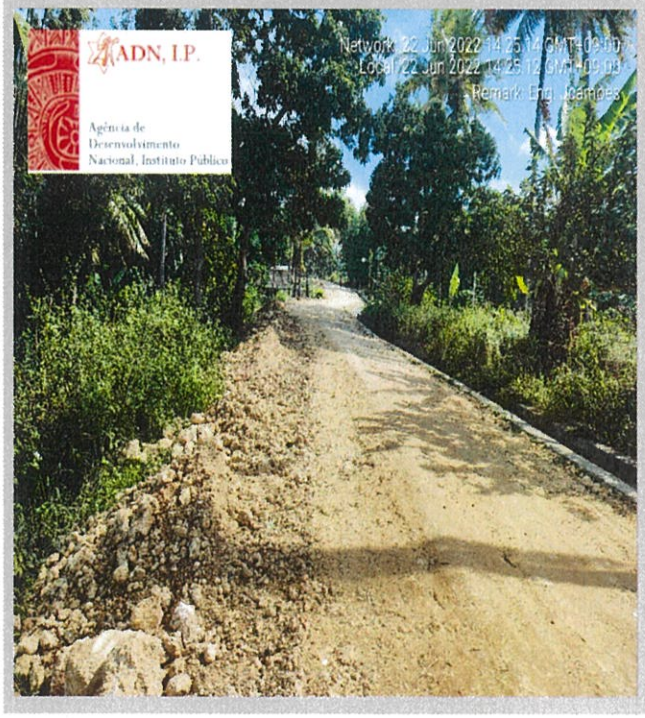
Start Point : Long : -8.45925833, Latetude : 126.4780250

End Point : Long : -8.444718332, Latetude : 126.4770166

Naran Inspector : 1. Jacob Da costa Camoes

2. .....

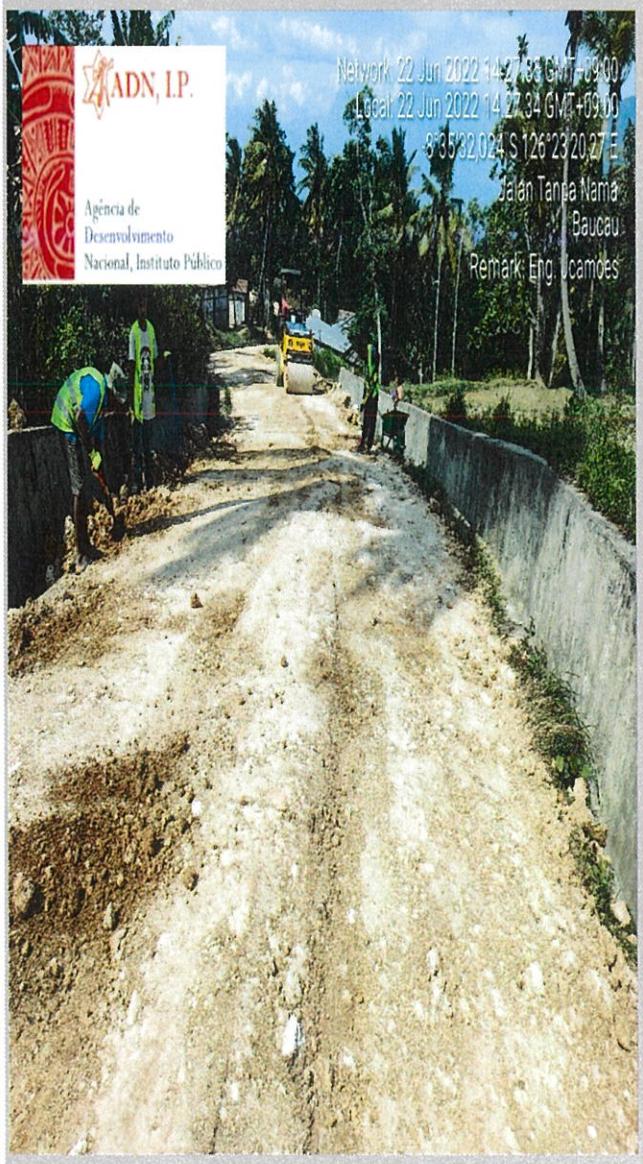
4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual **Kompanhia Halo Gravel**
Item servisu : Plumb concrete Gravel : 0,16 x 3,5 x 1500 = 840 m3	Foto Aktual iha terreno 

#ANEXU C1 (MP - 6)

Back-up Data

Naran Projeto : **R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800**
No. kontratu : **MPW-W-210049**

Item servisu : Plumb concrete Gravel : 0,16 x 3,5 x 1500 = 840 m3	Foto Aktual Iha Terreno 

#ANEXU C1 (MP - 6)

Back-up Data

Naran Projeto : **R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800**
No. kontratu : **MPW-W-210049**

Item servisu : Plumb concrete

Gravel : 0,16 x 3,5 x 1500 = 840 m3



	Obserbasaun Foto Aktual Iha terreno

MINISTÉRIO DO PLANO
E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Road name			Chainage start& End	
	2-Caicoli to Liabala			6+500
	3-Uma Ana Iko			4+500
	4-Bercoli to Bahamori			4+000
	5-Buruma to Uaimateme			2+800
	6-Boile to Uatabo			5+200
Municipality	Baucau		Length	23Km
Postu	Baucau Vila, Venilale and Vemase			

#ANEXU C2 (MP - 6)

Summary

Item	Description	PRICE	Progress Previous		Progress Juny		Progress Up to date	
			AMOUNT	%	AMOUNT	%	AMOUNT	%
I	Caicoli to liabala Sta : 0+000-6+500	$ 79,215.42	$ 68,248.09	1.18%	$ 23,889.20	7.98%	$ 92,137.29	1.18%
II	Uma ana iku chainage, Sta : 0+000-4+500	$ 93,102.37	$ 88,073.59	10.57%	$ 10,848.42	3.62%	$ 98,922.00	10.57%
III	Bercoli - Bahamori chainage,Sta : 0+000-4+000	$ 17,976.89	$ 18,436.43	0.79%	$ 5,252.50	1.75%	$ 23,688.93	0.79%
IV	Buruma to Uaimateme, Sta 0+000-2+800	$ 19,054.50	$ 3,092.00	0.52%	$ -	0.00%	$ 3,092.00	0.52%
V	Boile to Uatabo, Sta 0 + 000 - 2+800	$ 21,475.45	$ 13,727.70	0.85%	$ -	0.00%	$ 13,727.70	0.85%
A	**Construction cost**	**$ 230,824.63**	$ 191,577.81	63.98%	$ 39,990.12	13.35%	$ 231,567.92	77.33%
B	Contractor Fee (A x 10%)	$ 23,082.46	$ 19,157.78	6.40%	$ 3,999.01	1.34%	$ 23,156.79	7.73%
C	General items	$ 39,670.00	$ 16,429.86	5.49%	$ -	0.00%	$ 16,429.86	5.49%
D	Construction tax (A+B+C x 2%)	$ 5,871.54	$ 4,543.31	1.52%	$ 879.78	0.29%	$ 5,423.09	1.81%
E	**Total**	**$ 299,448.62**	$ 231,708.76	77.38%	$ 44,868.91	14.98%	$ 276,577.66	92.36%

Inspesaun Husi .

Eng. Jacob Da costa Camoes
Eng.ba Projeito Infrastutura Tranporte e Irigasaun ADN,I.P

Verifika Husi .

Eng. Remigio da C.S. dos Santos
Eng. Senior ba Projeito Infrastutura Tranporte e Irigasaun ADN,I.P

Certifika Husi .

Eng. Emerenciana da Costa M.Freitas
Cordenadora Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

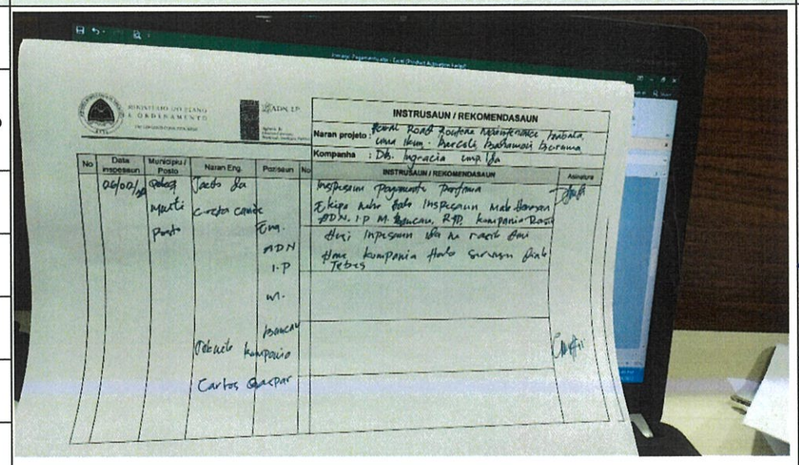
MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (MP-6)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800

Kompanha : DB-Ingracia Unipessoal Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN		Asinatura
I	22/07/2022	Baucau/Venilale	Jacob da costa Camoes	Eng.ADN.I.P. M.Baucau	1	Trabalhador la kolabora diak ho Eng. Kompania hodi difikulta ba servisu iha terenu lao tarde		
					2	Husu kompania atu koalia didiak ho Autoridade lokal hodi fo solusaun ne'ebe diak no halo kolaborasaun atu nune'e servisu bele lao ho diak		
					3			
					4			
					5			
II				Eng.ADN.I.P. M.Baucau	1			
					2			
					3			
					4			
					5			

#ANEXU C1 (BV-9)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800**
No. kontratu : **MPW-W-210047**

Data Inspesaun : **12 / 05/ 2022**

Fatin Inspesaun : Baucau Vila (Boile – Uatabo)

Koordinadas :

Start Point : Long : -8.460625, Latetude : 126.455995

End Point : Long : -8.440356, Latetude : 126.463871

Naran Inspector : **1. Jacob da Costa Camoes**

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Penetration Macadam	

#ANEXU C1 (BV-9)

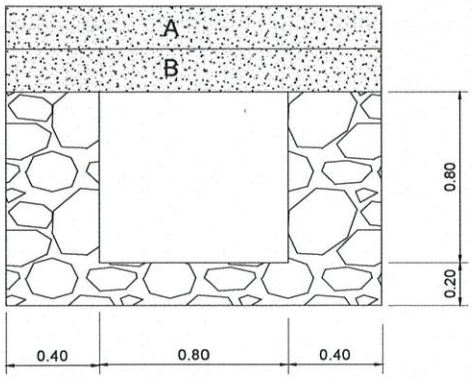
Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800**
No. kontratu : **MPW-W-210047**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu stone Masonry

Box culver



Stone masonry

Luas = 0.96 m3

V = 0.96 x 5 x 2 = 9.60 m3

Volume Structure Concrete M20

A = 0.20 x 0.20 x 1.60 x 4 = 0.256 m3

B = 0.20 x 1.60 x 5 x 2 = 3.20 m3



Penetratan Mcadan

#ANEXU C2 (BV-9)

Road name	Baucau to Uatabo	Chainage start	0+00
Municipality	Baucau	Chainage end	4+800
Postu	Baucau Vila	Length	4.800Km
Sukos	Trilolo - Bahu -Buruma- Caibada		

SUMMARY

Item	Description	PRICE	Progress Previus		Progress Phisic Jullu		Up to date	
			Amount (US$)	Weight (%)	Amount (US$)	Weight (%)	Amount (US$)	Weight (%)
R-01	General works	$ 3,110.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-03	Earth work	$ 10,685.18	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-05	Sub-base, base and pavement	$ 4,927.66	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-07	Bituminous pavement	$ 238,238.00	$ 549,960.00	136.34%	$ 549,960.00	136.34%	$ 1,099,920.00	272.69%
R-08	Structures	$ 75,344.34	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-10	Dayworks	$ 500.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-11	Routine maintenance	$ 5,922.40	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-12	Cleaning	$ 200.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
R-15	Provisional sum	$ 200.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	Construction cost	$ 339,127.58	$ 549,960.00	136.34%	$ 549,960.00	136.34%	$ 1,099,920	272.69%
B	Contractor Fee (A x 10%)	$ 33,912.76	$ 54,996.00	13.63%	$ 54,996.00	13.63%	$ 109,992.00	27%
C	General items	$ 22,411.09	$ 3,481.40	0.86%	$ 1,863.40	0.46%	$ 5,344.80	1.33%
D	Construction tax (A+B+C x 2%)	$ 7,909.03	$ 12,168.75	3.02%	$ 12,136.39	3.01%	$ 24,305.14	6.03%
E	Total	$ 403,360.46	$ 620,606.15	17.51%	$ 618,955.79	17.11%	$ 1,239,562	34.62%

Inspeksaun Husi :

Eng. Jacob Da Costa Camoes
Eng. Ba Projeito Insfrasturctura e Irigasaun, M. Baucau
ADN, I.P

Verifika Husi :

Eng. Remigio Da .C. S Dos Santos
Eng. Senior ba Projeito Insfrasturctura e Irigasaun, ADN, I.P

Cerifika Husi :

Eng. Emerenciana da Costa M.Freitas
Coordenadora Da Unidade de Controlo e Validação De Qualidade
ADN,I.P

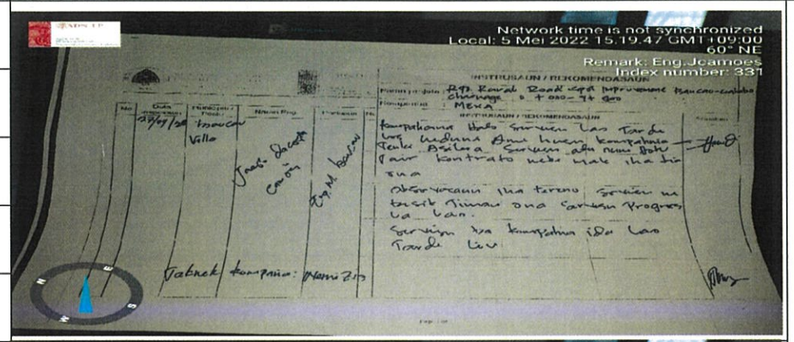
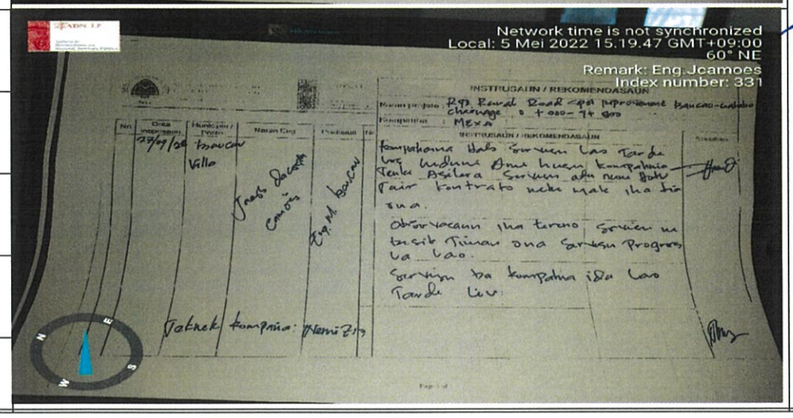
MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (BV-9)
INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800

Kompanha : Mexa

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	INSTRUSAUN TERENU IHA LIVRU VIZITA	Asinatura
I	12/5/2022	Baucau	Jacob Da costa Camoes	ENG. ADN I.P M. BAUCAU	1	Kompanha : NE halo servisu lao tarde los neduni ami husu kompanha tenki Aselera servisu ne atu nune halo hotutuir tempu de kontrato		
					2	Servisu tenki aselera tamba tarde liu		
					3	Aument trabalhador hodi halo servisu ho lalais		
					4	Material plumb concrete ho Macadam (penmark) tenki stok ona mai terenu hodi kontinua servisu		
					5	Tenki hatama relatorio labele liu data. 15-10-2021		
II					1	Husu ba kontraktor tenki hola sapatu boots entrega ba trabalhador hodi uza halo servisu		
					2	Tenki prepara palnu ho diak antes executa servisu		
					3	Husu ba Engineiru nafatin organiza trabalhador hodi aselera servisu		
					4	Tenki prepara relatorio kada loron no entrega ba ADN ho MOP wainhira to'o fulan remata		
					5			

#ANEXU C1 (BA – 1)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

Data Inspesaun : 28 – 06 - 2022

Fatin Inspesaun : Buava & Defawasi

Koordinadas :

Start Point : Long : 8.5780543S, Latetude : 126.6795899E

End Point : Long : 8.6063765S, Latetude : 126.68644416E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Treckschoor mamar	

#ANEXU C1 (BA – 1)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 12 m halis ou kleuk	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 12 m pondasi rahun/ lauja besi	

#ANEXU C1 (BA – 1)

Back-up Data

瞰aran Projeto : **New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality**

儞 No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Poste 12 m pinta mos ona no treckschoor mamar	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

#ANEXU C1 (BV – 2)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN: 00000340**

Data Inspesaun : 28 – 06 - 2022

Fatin Inspesaun : Uani Uma, Keraboe, bodo kho, kaibada makasae, Lutumutu

Koordinadas :

Start Point : Long : 8.45470674S, Latetude : 126.44196355S

End Point : Long : 8.44889296S, Latetude : 126.43876642E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 m halis / kleuk	

#ANEXU C1 (VEN – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344**

Data Inspesaun : 29 – 06 - 2022

Fatin Inspesaun : Uaihacu, Tugu - Venilale

Koordinadas :

Start Point : Long : 8.64382205S, Latetude : 126.37762811E

End Point : Long : 8.65001927S, Latetude : 126.37896519E

Naran Inspector : **Adonis Julio Fernandes**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Uja pipa galvanized ba ending JTR	

#ANEXU C1 (VEN – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Treckschoor mamar	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 12 pinta mos ona	

#ANEXU C1 (VEN – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Ai besik iha linha	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 9 m kleuk/halis & Pinta mos ona	

#ANEXU C1 (VEM – 1)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District**

No. kontratu : **RDTL-11003725**

Data Inspesaun : 28 - 06 - 2022

Fatin Inspesaun : Vemasse – Cairaebela - Waicoa

Koordinadas :

Start Point : Long : 8.52708673S, Latetude : 126.18276804E

End Point : Long : 8.48282723S, Latetude : 126.27878275E

Naran Inspector : Adonis Julio Fernandes

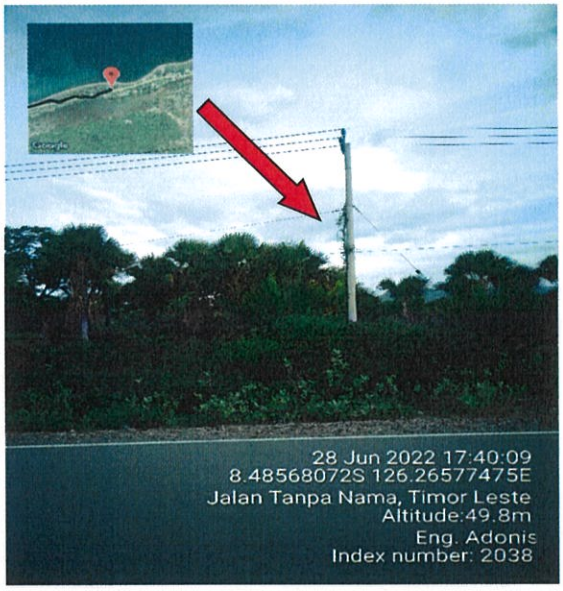
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Start point project	

#ANEXU C1 (VEM – 1)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District**

No. kontratu : **RDTL-11003725**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Fiu Baixadas kois / kotu	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste halis & treckschoor kotu	

#ANEXU C1 (VEM – 1)

Back-up Data

Naran Projeto : **New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District**

No. kontratu : **RDTL-11003725**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Assecores Druckschoor seidauk installa	

#ANEXU C1 (QUE – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338**

Data Inspesaun : 22 – 06 - 2022

Fatin Inspesaun : Nara Aba, Liuraga & Batikasa

Koordinadas :

Start Point : Long : 8.64373894S, Latetude : 126.54199481E

End Point : Long : 8.66038572S, Latetude : 126.52554116E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Poste halis no suspention kotu	

#ANEXU C1 (QUE – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste halis/kleuk	

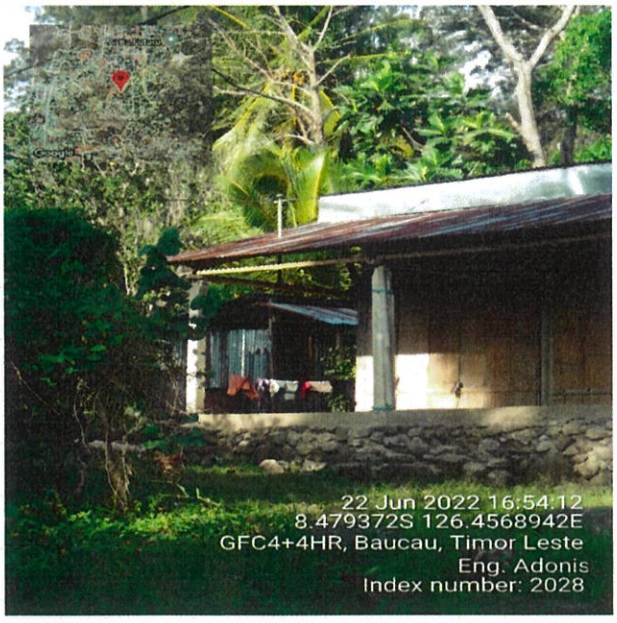
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……	

#ANEXU C1 (QUE – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338**



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..	
Home Conection	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (QUE - 2)

Inspection Date : 22 - 06 - 2022
Location : Nara Aba, Liuraga, Batikasa Laisorulai - Quelicai - Baucau Municipality
Company : Lolulai Unipessoal. Lda
Project Name : New Installation of MV, LV & Home Conection

SUMMARY

ORIGINAL CONTRACT				ADN,IP VERIFICATION/INSPECTION					
NO	DESCRIPTION			PREVIOUS BILLING		THIS BILLING		UP TO DATE	
		AMOUNT ($)	PERCENTAGE(%)	AMOUNT ($)	PERCENTAGE(%)	AMOUNT ($)	PERCENTAGE(%)	AMOUNT ($)	PERCENTAGE(%)
I	PREPARATION WORK	$ 24,576.90	5.21%	$ 24,576.90	5.21%	$ -	0.00%	$ 24,576.90	5.21%
II	INSTALLATOIN MV IINE	$ 221,604.84	46.97%	$ 223,656.68	47.40%	$ 1,721.22	0.36%	$ 225,377.90	47.77%
III	INSTALLATION OF TRANSFORMER	$ 58,436.82	12.38%	$ 58,436.82	12.38%	$ -	0.00%	$ 58,436.82	12.38%
IV	EXTENTION LV LINE	$ 110,228.76	23.36%	$ 107,988.26	22.89%	$ 530.53	0.11%	$ 108,518.79	23.00%
V	HOME CONECTION	$ 57,000.00	12.08%	$ 13,300.00	2.82%	$ 36,100.00	7.65%	$ 49,400.00	10.47%
	GRAND TOTAL	$ 471,847.32	100.00%	$ 427,958.66	90.70%	$ 38,351.75	8.13%	$ 466,310.41	98.83%
	AMOUNT CONTRACT	$ 471,847.32							

Inpeksaun Husi :

Eng. Adonis Julio Fernandes
Eng. ba Projecto ME, ADN, I.P

Verifika Husi :

Eng. Deolindo de Fatima Marques
Chefe Seksaun ME & ITC , ADN, I.P

Sertifika Husi :

Eng. Emerenciana Da Costa Maia Freitas
Coordenadora UCVQ, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (QUE-3) INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau

Kompanha : Mau - Tasi

No	Data Inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/06/2022	Baucau/Quelicai	Adonis Julio Fernandes	Tekniku ME	1	Hadia no intika fali treckschoor nebe mak mamar no kotu	
					2	Pinta fali poste 12 m no poste trafo nebe tinta mos ona	
					3	Hadia no halos fali poste 12m nebe halis no kleuk	
					4	Hadia no installa warning sign no climber protection trafo nian	
					5	Tesi Ai nebe besik iha linha	
					6	Cor Fali Pondasi nebe mak rahun (Poste 12 m no poste Trafo)	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU D (QUE - 2) **INSTRUSAUN / REKOMENDASAUN**

Naran projeto : New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality

Kompanhia : Lolulai Unip. Lda

No	Data Inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/06/2022	Baucau/Quelicai	Adonis Julio Fernandes	Tekniku ME	1	Hadia no istika fali trecschoor nebe mak mamar no kotu	
					2	Hadia no halos fali poste nebe halis ou kleuk (Poste 9 m)	
					3	Hadia no istika fali fiu baixadas nebe mak monu / tabele	
					4		
					5		

#ANEXU CI (QUE-3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343**

Data Inspesaun : 22 – 06 - 2022

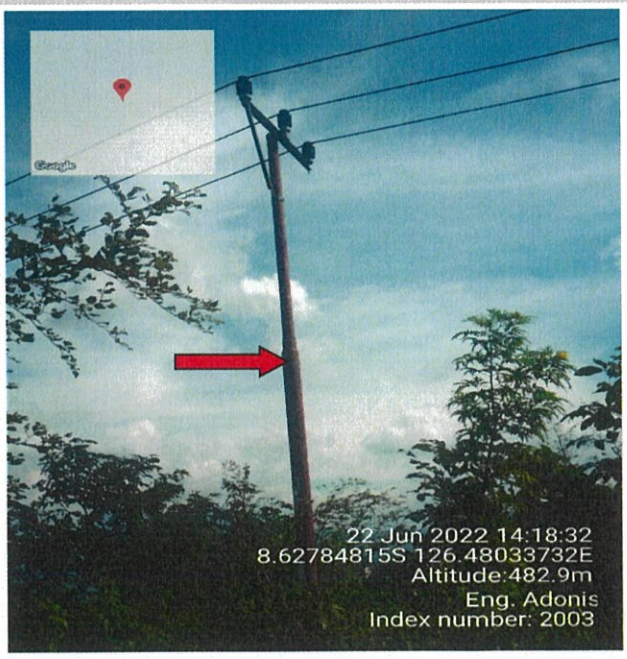
Fatin Inspesaun : Darabata Bere, Lelalai, Walikoko, Daramutu, Waibobo & Boronaha

Koordinadas :

Start Point : Long : 8.64415542S, Latetude : 126.49730992E

End Point : Long : 8.62737446S, Latetude : 126.48035273E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Poste 12 m Pinta mos ona	

#ANEXU CI (QUE-3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Treckschoor mamar & Pondasi rahun/nakfera	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 m halis ou kleuk	

#ANEXU CI (QUE-3)

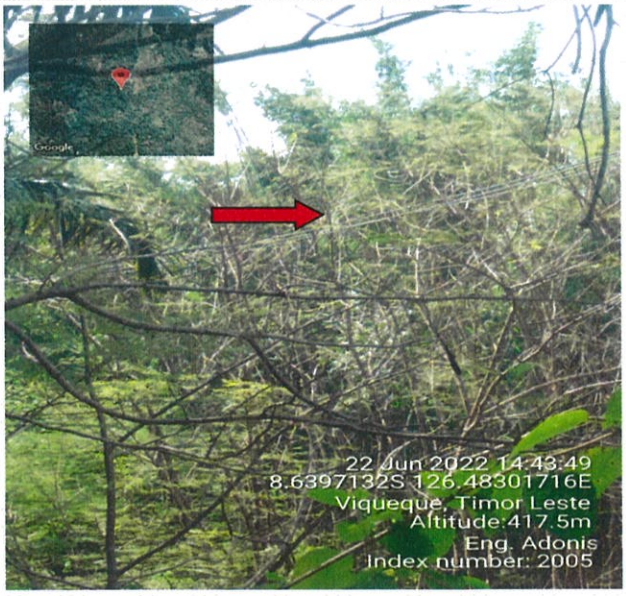
Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau**
No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343**

Warning sign monu



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….	
Ai besik iha linha Media tensaun	



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (QUE - 3)

Date Inspection : 22 - 06 - 2022
Location : Dara Batabere, Lelealai, Wailalico, Waibobo - Quelicai - Baucau Municipality
Company : Mautasi Unipessoal. Lda
Project Name : New Installation of MV, LV & Home Conection

SUMMARY

ORIGINAL CONTRACT				ADN,IP VERIFICATION					
NO	DESCRIPTION			PREVIOUS BILLING		THIS BILLING		UP TO DATE	
		AMOUNT ($)	PERCENTAGE(%)	AMOUNT ($)	PERCENTAGE(%)	AMOUNT ($)	PERCENTAGE(%)	AMOUNT ($)	PERCENTAGE(%)
I	PREPARATION WORK	$ 14,600.89	5.67%	$ 14,600.89	5.67%	$ -	0.00%	$ 14,600.89	5.67%
II	INSTALLATOIN MV IINE	$ 206,317.58	80.14%	$ 209,883.59	81.52%	$ 1,625.40	0.63%	$ 211,508.99	82.15%
III	INSTALLATION OF TRANSFORMER	$ 19,478.94	7.57%	$ 19,420.92	7.54%	$ 58.02	0.02%	$ 19,478.94	7.57%
IV	EXTENTION LV LINE	$ 7,558.40	2.94%	$ 25,922.87	10.07%	$ 17.69	0.01%	$ 25,940.56	10.08%
V	HOME CONECTION	$ 9,500.00	3.69%	$ -	0.00%	$ 5,700.00	2.21%	$ 5,700.00	2.21%
	TOTAL	$ 257,455.81	100.00%	$ 269,828.27	104.81%	$ 7,401.11	2.87%	$ 277,229.38	107.68%
	GRAND TOTAL CONTRACT	$ 257,455.81							

Inpeksaun Husi :

Eng. Adonis Julio Fernandes
Eng. ba Projecto ME, ADN, I.P

Verifika Husi :

Eng. Deolindo de Fatima Marques
Chefe Seksaun ME & ITC , ADN, I.P

Sertifika Husi :

Eng. Emerenciana Da Costa Maia Freitas
Coordenadora UCVQ, ADN,I.P

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL
ZEES

ADN, I.P.
Agência de Desenvolvimento Nacional - Instituto Público

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJEITO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	JUNHO 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	OBS
BAGUIA VILLA	3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	FI	ESTRADAS	Domin Timor Diak, Lda	SSS/078/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	FI	ESTRADAS	Gihon Unip, Lda	SSS/066/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	6	Rural Roads Routine Maintenance Baucau - Uatabo Chainage 0+000 - 4+800 and Boile - Uatabo Chainage 0+000 - 5+200 in Municipality Baucau / 162	LM-CD	ESTRADAS	Talamori	MPWTC-W-190090	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Falta Retensaun
								Actual																																
	7	Road Maintenance Section: Baucau Urbans, Baucau Town, Baucau Municipality (162)	LM-BS	ESTRADAS	Jomarjo Unipessoal Lda	MPW-W-190158	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Progress fizik 85.28% Empreza lakoi kontinua ona
								Actual																																
	9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800	LM-CD	ESTRADAS	Mexa	MPW-W-210047	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
LAGA	1	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Lalaisi, Unip. Lda	RT/023/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	2	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 1+600 - 3+300 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Rozi Unipessoal, Lda	RT/024/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Retensaun selu hotu ona
								Actual																																
	3	Rural Roads Periodic Maintenance Samaguia - Namanei Chainage 0+000 - 7+000 Municipality Baucau / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Delatina	MPTCW-W-190091	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	LM-BS	ESTRADAS	Uatoos Unip, Lda	MOP-W-200002	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	6	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 :Laga to Baguia	LM-CD	ESTRADAS	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																																
BAGUIA	2	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	FI	MANUTENSAUN NO REHABILITASAUN	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Progress Fhisic 100%. Falta Retensaun
								Actual																																
	4	Baguia - Larisula Chainage 0+000 - 12+900 / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Lamegua Star Unip Lda	MPW-W-190088	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	6	Konstrusaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	LM-CD	AGRICULTURA	Makasae Construction LDA	RDTL-2021-14628	MINISTERIO AGRIKULTURA E PESCAS	Plan																																On going
								Actual																																
VENILALE	3	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	FI	ESTRADAS	Ruvic unip, lda	SSS/118/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Paradu
								Actual																																
	4	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Caidailale Unip.Lda	RT/069/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Paradu
								Actual																																
QUELICAI	3	Rehabilitation Of Roads Uiaca - Queleqai - Lacluta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	FI	ESTRADAS	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	4	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	LM-CD	ESTRADAS	Lalaisi, Unip. Lda	MPWTC-W-190089	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	LM-CD	ESTRADAS	Niceles Unipessoal Lda	MPW-CS-2000026	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																																
	6	Rehabilitation of Roads, Road Section: Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	FI	ESTRADAS	Wingstone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																

| | | |

MINISTERIO DO PLANU E FORTIFIKASAUN NO ORSAMENTO CONSTITUCIONAL

ADN, I.P.

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJEITO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	Juni 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
BAGUIA VILLA	3	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.0+000-6+025	FI	ESTRADAS	Domin Timor Diak, Lda	SSS/078/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	4	Rehabilitasaun Estrada Jct Triloka -jct Fatumaca-jct Venilale Ch.6+025-12+075	FI	ESTRADAS	Gihon Unip, Lda	SSS/066/MOPTC-2017	TERIO DAS OBRAS PU	Plan																															On going
								Actual																															
	6	Rural Roads Routine Maintenance Baucau - Uatabo Chainage 0+000 - 4+800 and Boile - Uatabo Chainage 0+000 - 5+200 in Municipality Baucau / 162	LM-CD	ESTRADAS	Talamori	MPWTC-W-190090	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Falta Retensaun
								Actual																															
	7	Road Maintenance Section, Baucau Urbans, Baucau Town, Baucau Municipality (162)	LM-BS	ESTRADAS	Jomarjo Unipessoal Lda	MPW-W-190158	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Progress fizik 100% ona
								Actual																															
	9	R4D Rural Road Spot Improvement Baucau-Uatabo Chainage 0+000 - 4+800	LM-CD	ESTRADAS	Mexa	MPW-W-210047	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
LAGA	1	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 0+000 - 1+600 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Lalaisi, Unip. Lda	RT/023/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	2	R4D Rural Road Rehabilitation Teriluedae - Saelari - Binagua Chainage 1+600 - 3+300 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Rozi Unipessoal, Lda	RT/024/MOP-2019	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Progress Fhisic 100%
								Actual																															
	3	Rural Roads Periodic Maintenance Samaguia - Naunanei Chainage 0+000 - 7+000 Municipality Baucau / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Delatina	MPTCW-W-190091	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	5	Roads Maintenance Section Laga Baguia Municipality Baucau (162)	LM-BS	ESTRADAS	Uatoos Unip. Lda	MOP-W-200002	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	6	For Preparation of Detailed Engineering Design For Rehabilitation of Municipio Roads Packager 4 :Laga to Baguia	LM-CD	ESTRADAS	Detile Consultant Lda, in Association with PDP Utek (M) SDN. BHD	MPW-CS-2000027	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																															
BAGUIA	2	Manutensaun Estrada Baquia-Larisula Sta. 0+000-12+900-Municipal of Baucau	FI	MANUTENSAUN NO REHABILITASAUN	Mr Construction Unip Lda	RFQ/129/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Progress Fhisic 100%. Hela Retensaun
								Actual																															
	4	Baguia - Larisula Chainage 0+000 - 12+900 / 162	LM-BS	MANUTENSAUN NO REHABILITASAUN	Lamegua Star Unip Lda	MPW-W-190088	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	6	Konstrusaun Intek no Kanais Irrigasaun Larisula iha Baguia Municipio Baucau	LM-CD	AGRICULTURA	Makasae Construction LDA	RDTL-2021-14628	MINISTERIO AGRIKULTURA E PESCAS	Plan																																Progress Fhisic 99.83%.
								Actual																															
VENILALE	3	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 0+000-10+300, Baucau Municipality	FI	ESTRADAS	Ruvic unip, lda	SSS/118/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Paradu
								Actual																															
	4	Rehabilitation Bercoli - Bahamori 1 Chainage Sta. 0+000-1+500 Baucau Municipality	FI	MANUTENSAUN NO REHABILITASAUN	Caidailale Unip.Lda	RT/069/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																															
QUELICAI	3	Rehabilitation Of Roads Uiaca - Queleqai - Lacluta Sta. 5+400 to 10+800 (5.40 Km) Municipality of Baucau	FI	ESTRADAS	Develop Timor, Lda	RDTL-SSS/123/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	4	Rural Roads Rutine maintenance Laisorulai - Nae - Chainage 0+000 - 1500 and Quelicai Chainage 0+000 - 10 + 000 in Baucau Municipality	LM-CD	ESTRADAS	Lalaisi, Unip. Lda	MPWTC-W-190089	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															
	5	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 3 Uacala - Quelicai to Ossu	LM-CD	ESTRADAS	Niceles Unipessoal Lda	MPW-CS-2000026	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																															
	6	Rehabilitation of Roads, Road Section: Uaiaca - Quelicai - Lacudala Sta. 0+000 - Sta. 5+400 (Package 1) Municipality Baucau	FI	ESTRADAS	Wingstone Const. Lda JV PT. Putra Mas Pratama	RDTL-SSS/298/MOPTC-2016	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																															

MINISTERIO DO PLANO E ORDENAMENTO VII GOVERNO CONSTITUCIONAL

ADN, I.P. Agência de Desenvolvimento Nacional - Instituto Público

PLANU INSPESAUN

2022

Naran Eng.		Jacob Da Costa Camoes
Municipio		Baucau

POSTO	NU.	NARAN PROJETO	KAT. PROJECTO	SECTOR	NARAN COMP.	NARAN KONT.	DONO PROJECTO	Action	Juni 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
VEMASSE	3	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 0+000-2+500 Baucau Municipality	LM-CD	ESTRADAS	Rozi const. unip. Lda	MPW-W-210048	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	4	R4D Rural Road Spot Improvement Loilubu-Osoala Chainage 2+500-4+500 Baucau Municipality	LM-CD	ESTRADAS	Rozi const. unip. Lda	MPW-W-210051	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	R4D Rural Road Spot Improvement Vemase-Osoala Chainage 0+000-21+600	LM-CD	ESTRADAS	Chacailala Unipessoal Lda	MPW-W-210052	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	8	Nasional Road no.1 Upgrading project Manatuto Baucau (paketckage A01 - 02/STA 56+400-114+102(56.82km)	FI	ESTRADAS IMPRESTIMO	Shangai Construction Group Co.,Ltd	ICB/021/MPWTC-2015	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
								Actual																																
MULTI POSTO	1	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	FI	ESTRADA-IMPRESTIMO	CBMI Construction Co. Lda Jv Chongqing Roads Engineering	ICB/078/MPWTC-2015	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																
	2	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120	FI	IMPRESTIMO	China Railway Int. Group co. jv with China oversees	ICB/046/MOPTC-2017	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																
	3	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	FI	ESTRADA-IMPRESTIMO	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)	RFP/003/MOP/2018	MINISTERIO DAS OBRAS PUBLICAS	Plan																																		Nasional mak halo Monitoring ba projeitu imprestimu
								Actual																																
	4	R4D Rural Road Spot Improvement Baguia Larisula Chainage 0+000-12+900, Rural Roads Routine Maintenance Samalari-Sorugua Chainage 0+000-2+800 Teriluedae-Saelari-Binagua Chainage 0+000-3+600 Baucau Municipality	LM-CD	ESTRADAS	Juga Te Figa Unipessoal Lda	MPW-W-210054	MINISTERIO DAS OBRAS PUBLICAS	Plan																																On going
								Actual																																
	5	R4D Rural Road Routine Maintenance Caicoli-Liabala Chainage 0+000-6+500 Uma Ana Iku Chainage 0+000-4+500 Bercoli-Bahamori Chainage 0+000-4+000 Buruma-Uaimateme Chainage 0+000-2+800 Boile-Uatabo Chainage 0+000-2+800	LM-CD	ESTRADAS	DB-Ingracia Unipessoal Lda	MPW-W-210049	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	On going
								Actual																																
TOTAL PROJETO ON - GOING = 29																																						

Note.

Periode inspesaun iha tereinu

Implementasaun Plano Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi ,

(Eng. Jacob da Costa Camoes)

Eng. Ba Projecto Inafrastitura e Irigasaun Municipio Baucau ADN, I.P

Sertifika Husi ,

(Eng.Emerenciana da Costa M. Freitas)

Coordenadora da Unidade de Controlo e Validação de Qualidade ADN , I. P.

Aprova Husi

(Eng. Januario Maia Gueres)

Ajunto Director Executivo - ADN I. P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Tito Edgar F.N. de Jesus

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Pagamento
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun ba Pagamento

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Tito Edgar F.N. de Jesus)
Eng. PMU ba Projetu (Impréstimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Tito Edgar F.N. de Jesus

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

OBSERVASAUN

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		We 1	Th 2	Fr 3	Sa 4	Su 5	Mo 6	Tu 7	We 8	Th 9	Fr 10	Sa 11	Su 12	Mo 13	Tu 14	We 15	Th 16	Fr 17	Sa 18	Su 19	Mo 20	Tu 21	We 22	Th 23	Fr 24	Sa 25	Su 26	Mo 27	Tu 28	We 29	Th 30	OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															

| | | |

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Teresa Gomes

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		We 1	Th 2	Fr 3	Sa 4	Su 5	Mo 6	Tu 7	We 8	Th 9	Fr 10	Sa 11	Su 12	Mo 13	Tu 14	We 15	Th 16	Fr 17	Sa 18	Su 19	Mo 20	Tu 21	We 22	Th 23	Fr 24	Sa 25	Su 26	Mo 27	Tu 28	We 29	Th 30	OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Pagamento
							Actual																															
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phils, (Iep) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun ba Pagamento
							Actual																															

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual		
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
								PHO
TOTAL PROJETO ON-GOING								

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Teresa Gomes)
Eng. PMU ba Projetu (Impréstimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Teresa Gomes

Municipio: MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companhi	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Soleremа - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Soleremа Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Soleremа Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phls. (Iep) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

| | | |

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Augusta da Costa Ferreira

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Observasaun
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Pagamento
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Philis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun ba Pagamento

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projetu (Impréstimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Augusta da Costa Ferreira

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd (Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phils, (Iep) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

| | | |

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Pagamento
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Iep) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun ba Pagamento

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	
TOTAL PROJETO ON-GOING							

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

PHO

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Vidal Guterres)
Eng. PMU ba Projetu (Imprestimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co .,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Wutu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co .,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

| | | |

MINISTÉRIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Adonis Julio Fernandes

Municipio MUNICIPIO BAUCAU NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
BAUCAU VILLA (BV)		Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Servisu electricidade seidauk
		Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Servisu electricidade seidauk
		Rehabilitasaun ba ESG Filial Kilik Waiga'e iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG FILIAL KILIK WAIGA'E	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Servisu electricidade seidauk
		Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Servisu electricidade seidauk
		Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Servisu electricidade seidauk
	1	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	2	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	3	Rehabilitation of MPWTC Office in the Municipality Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															Projeitu refere PHO ona
	4	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	LM	MINISTERIO SAUDE	Plan																															
							Actual																															
	5	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	Talamori	RDTL-SAMES-RFQ-021-071	LM-BS	SAMES	Plan																															
							Actual																															
	6	Construsaun Escola Polo Baucau	Sanira Construction Unip Lda	RDTL-326	FI	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu Abandona
LAGA (LA)	1	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF LALA-BU'U	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	2	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	3	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF. FITUN SAGADATE-LAGA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
BAGUIA (BA)	1	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	2	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	3	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UACALA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	4	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE FINI BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	5	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE LARI-SULA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha
	6	Rehabilitasaun ba EBC Ossu - Huna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC OSSU-HUNA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																															
							Actual																															Projeitu refere kontratu seidauk iha

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho																											OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
VENILALE (VEN)	7	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	GRUPU KOMUNITARIU MEJD PKRIE EBC BUAUA LAVATERI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Projeitu refere kontratu seidauk iha
	8	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGF DE BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Projeitu refere kontratu seidauk iha
	9	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	1	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC UAI-BUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Projeitu refere kontratu seidauk iha
	2	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CULINA-OSSU-UAILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Projeitu refere kontratu seidauk iha
	3	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Projeitu refere kontratu seidauk iha
	4	Aumenta C. O no Kliesntes	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														Lakonsege hare tamba tempu
	5	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	6	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	Wetodo Unip. Lda	SSS/296/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
QUELICAI (QUE)	1	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UADA-BORU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	2	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAI-ACA/MULIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	3	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF ABO-LIR LALETEK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	4	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC LETEMUMO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	5	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	6	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CATOLICA DARENAFA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	7	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF MAURO DARALA/BORUMODO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	8	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAIDORA/OSSOLIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														Lakonsege hare tamba tempu
	9	New Construction of Health Post and Douctor House Building Municipality Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	LM-CD	MINISTERIO SAUDE	Plan																														
							Actual																														Lakonsege hare tamba tempu
	10	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho																												OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
	11	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
VEMASSE (VEM)	1	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	We-Rua Unip, Lda	MOP-W-190173	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	Esa-Un	56/DNAL-MTAC/III/2017	LM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																															
							Actual																															Projeitu Abandona
TOTAL PROJETO ON-GOING																																				

Note:

Periode inspesaun iha tereinu **Implementasaun Plano Periode inspesaun iha tereinu** **Relatoriu avaliasuan mensal iha Dili** **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Adonis Julio Fernandes)
Eng. Electricidade, ADN,I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VII. GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng.	Adonis Julio Fernandes
Municipio	MUNICIPIO BAUCAU NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
BAUCAU VILLA (BV)		Rehabilitasaun ba ESG 02 Vila Nova Baucau iha Aldeia Samalatu Liba Suco Buibau Postu Administrativu Baucau Villa Municipiu Baucau	MEJD PKRIE ESGP NU. 02 VILA NOVA BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
		Rehabilitasaun ba EPEC/ESTV Baucau iha Aldeia Samalaculiba Suco Buibau Postu Administarivu Baucau Villa Municipiu Baucau	MEJD PKRIE EPEC/ESTV BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
		Rehabilitasaun ba ESG Filial Kilik Waiga'e iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG FILIAL KILIK WAIGA'E	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
		Rehabilitasaun ba EBF Caibada Macassae iha Aldeia Caiobilale Suco Caibada Postu Administrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE EBF CAIBADA MACASSAE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
		Rehabilitasaun ba ESG 01 Baucau iha Aldeia Lutumutu Suco Tirilolo Postu Admimistrativu Baucau Villa Munisipiu Baucau	MEJD PKRIE ESG NO. 01 BAUCAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	1	Instalasaun Media tensaun husi Dokubere to'o Ponte Seical	Alandio Tahame	RDTL/MOP-SEE/CGI-PEN : 0000162	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	2	New Installation Mv, Lv Line & House Connection From Caibada Makasae to Lutumumu, Kaibada Waimua, Knua Waimataoli, Kaiwa'a and Haucati - Baucau Municipality	Lover Unip.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000340	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	3	Rehabilitation of MPWTC Office in the Municipality Baucau	Co. Cactus Unip. Lda	546/DGCS-MOPTC/VI/2016	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	4	Rehabilitasaun Eis hospital Trilolo Baucau ba Fatin Karantina,ICU,Laboratorium no Izolamento Ministerio	Central Hill Unipessoal Lda	RDTL-MS-DNA-NCB-20-252	LM	MINISTERIO SAUDE	Plan																																
							Actual																																
	5	Konstrusaun Foun ba Moru Protesaun ba Armazen SAMES Regional Baucau iha Municipio Baucau	Talamori	RDTL-SAMES-RFQ-021-071	LM-BS	SAMES	Plan																																
							Actual																																
	6	Construsaun Escola Polo Baucau	Sanira Construction Unip Lda	RDTL-326	FI	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
LAGA (LA)	1	Rehabilitasaun ba EBF. Lala - Bu'u iha Aldeia Sire - Bu'u Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF LALA-BU'U	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	2	Rehabilitasaun ba EBF 1 no 2 ciclo Libagua iha Aldeia Libagua Suco Libagua Posto Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF 1 NO 2 CICLO LIBAGUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	3	Rehabilitasaun ba EBF Fitun Sagadate - Laga iha Aldeia Samagata Suco Sagadate Postu Administrativu Laga Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF. FITUN SAGADATE-LAGA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
BAGUIA (BA)	1	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	2	Rehabilitasaun ba EBC Ossu - Ufulari iha Aldeia Ossu - Ufulari Suco Samalari Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF OSSU-UFULARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	3	Rehabilitasaun ba EBF Uacala iha Aldeia Uacala Suco Uacala Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UACALA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	4	Rehabilitasaun ba EPE Fini Baguia ih Aldeia Neolidae Suco Alaua Craic Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE FINI BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	5	Rehabilitasaun ba EPE Lari - Sula iha Aldeia Lauhare Suco Lari -Sula Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE LARI-SULA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	6	Rehabilitasaun ba EBC Ossu - Huna iha Aldeia Uaicade Suco Ossu - Huna Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC OSSU-HUNA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho																											OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
	7	Rehabilitasaun ba EBC Buaua Lavateri iha Aldeia Fanalolo Suco Lavateri Postu Administrativu Baguia Munisipiu	GRUPU KOMUNITARIU MEJD PKRIE EBC BUAUA LAVATERI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	8	Rehabilitasaun ba ESG de Baguia iha Aldeia Neolidae Suco Alua Kraik Postu Administrativu Baguia Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGF DE BAGUIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	9	New Installation MV, LV Line and House Connection from Buava to Defawasi - Baucau Municipality	Power Engineering Construction Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000377	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
VENILALE (VEN)	1	Rehabilitasaun ba EBC Uai - Bua iha Aldeia Uato - Hassa Suco Uato - Haco Postu Administrativu Venilale Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC UAI-BUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	2	Rehabilitasaun ba EBF Culina - Ossu - Uailale, Ossu - Uaque iha Aldeia Osso - Uaque Suco Fatulia Postu Administrativu Venilale Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CULINA-OSSU-UAILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	3	Rehabilitasaun ba EPE Publico Amizade Venilale iha Aldeia Uato Hasa Suco Uato - Haco Postu Administrativu Venilale Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EPE PÚBLICO AMIZADE VENILALE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	4	Aumenta C. O no Kliesntes	Pae-Le Unip,Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000445	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	5	New Installation MV, LV Line and House Connection from Uaihacu to Tugu SP3 - Baucau Municipality	Hawa-Ali Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000344	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	6	Construction of Water Supply with Pump System (Multy Suco) Watuhaco – Venilale In Baucau Municipality	Wetodo Unip. Lda	SSS/296/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
QUELICAI (QUE)	1	Rehabilitasaun ba EBF. Uada - Boru iha Aldeia Uada - Buro Suco Guruca Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UADA-BORU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	2	Rehabilitasaun ba EBF. Uai-Aca/Mulia iha Aldeia Uai-Aca/Mulia Suco Tame Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAI-ACA/MULIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	3	Rehabilitasaun ba EBF Abo - Lir Laletek iha Aldeia Abor Lir Suco Abo Postu Administrativu Quelicai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF ABO-LIR LALETEK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	4	Rehabilitasaun ba EBC Letemumo iha Aldeia Lebenei Suco Letemumo Postu Administrativu Quilecai Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBC LETEMUMO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	5	Rehabilitasaun ba ESGPF Dom Carlos Filipe Ximenes Belo Afaca iha Aldeia Veco - Buti Suco Afaca Postu Administrativu Quelica Municipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE ESGPF DOM CARLOS FILIPE XIMENES BELO AFAÇA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	6	Rehabilitasaun ba EBF Catolica Darenafa iha Aldeia Siri - Laco/Loi - Rae Suco Namanei Postu Administrativu Quelecai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF CATOLICA DARENAFA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	7	Rehabilitasaun ba EBF Mauro Darala/Borumodo iha Aldeia Namanei Suco Maluro Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF MAURO DARALA/BORUMODO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	8	Rehabilitasaun ba EBF Uaidora Ossolia iha Aldeia Ossolia Suco Letemumu Postu Administrativu Quelicai Munisipiu Baucau	GRUPU KOMUNITARIU MEJD PKRIE EBF UAIDORA/OSSOLIA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																														
	9	New Construction of Health Post and Douctor House Building Municipality Baucau	Jova Construction Unip. Lda	RDTL-MS-DNA-NCB-21-069	LM-CD	MINISTERIO SAUDE	Plan																														
							Actual																														
	10	New Installation MV, LV Line and House Connection from Laisorulai Nara Aba to Liuraga and Batikasa - Baucau Munipality	Lolulai Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000338	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22
	11	New Installation, MV, LV Line and House Connection from Darabata Bere, Lelalai, Waliliko, Daramutu to Waibobo and Boronaha, Laisorulai - Baucau	Mau - Tasi	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000343	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																						
							Actual																						
VEMASSE (VEM)	1	New Installation of MV, LV Line and House Connection from Vemasse to Cairabela and Waigoa - Baucau District	We-Rua Unip, Lda	MOP-W-190173	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																						
							Actual																						
	2	Rehabilitasaun of Cairabela Mini Tradisional Food in Vemasse	Esa-Un	56/DNAL-MTAC/III/2017	LM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																						
							Actual																						
TOTAL PROJETO ON-GOING																													

Note:

Periode inspesaun iha tereinu — **Implementasaun Plano Periode inspesaun iha tereinu** — **Relatoriu avaliasuan mensal iha Dili** — **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Adonis Julio Fernandes)
Eng. Electricidade, ADN,I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN,I.P
