REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE

MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público

A.D.N, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

RELATÓRIU MENSÁL IMPLEMENTASAUN PROJETUS MUNISÍPIU DÍLI

ABRIL 2022



SUMARIO

RELATÓRIO

IMPLEMENTASAUN PROJETU INFRAESTRUTURA IHA MUNICIPIO DILI

ABRIL 2022

Prepara Husi :

(Eng. Manuel Estrela)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Dili ADN,IP

(Eng. Pedro de Lurdes Alves)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Dili ADN,IP

(Eng. Rosalia de Fatima)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Dili ADN,IP

(Eng. Julmira S.Sampaio,
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Dili ADN,IP

(Eng. Egidio Goncalves)
Eng. ba Edificio Publiku no Beé Saneamentu, Municipio Dili ADN,IP

(Eng. Eduardo do Santos)
Eng. ba Projetu Infraestrutura e Irigasaun, Municipio Dili ADN, I.P

(Eng. João O. do Rego)
Eng. ba Projetu Infraestrutura e Irigasaun, Municipio Dili ADN, I.P

(Camilio de Jesus)
Eng. M & E, Municipio Dili ADN, I.P

(Ezequiel R. de Oliveira)
Eng. ITC, Municipio Dili ADN, I.P

Verifika Husi :

(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edificio Publiku no Beé Saneamentu, ADN, I.P

(Eng. Remigio da C.S.dos Santos)
Eng. Senior ba Projetu Infraestrutura e Irigasaun, ADN, I.P

(Deolindo de F Marques)
Chefe Sek. Projetu M.E & ITC, ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :

(Mariano Renato Monteiro da Cruz, S. T, M. Eng)
Director Executivo, ADN, I.P

Contents

I. INTRODUSAUN 2

Tabel 1.2.1 : Postos Administrativos,Sucos no Aldeias. 2

Tabel 2.2.2 : Força de Trabalho ADN, I.P Municipio Dili 4

Tabel 3.2.3: Lista Asset ADN,I.P Municipio Dili. 4

1.3. Lista Projectos 5

Tabel 1.3.1: Projecto Municipio Dili Por Fundus Finansiamento 5

Tabel 1.3.2: Projecto Municipio Dili Por Sector 9

Tabel 1.3.3: Projecto Municipio Dili Por Ministerio 19

Tabela 1.3.4 : Population Projection Municipiu, Postu Administrativo, Suco tuir Sexu no Grupu idade 2015-2022 34

II. PROGRESU FISIKU 35

2.1 Progresso Fisiku Kada Fulan 35

III. OBSTÁCLO IHA TERENU 35

3.1 Obstáclo Servisu Iha Terenu 35

IV. REKOMENDASAUN IHA TERENU 36

4.1 Rekomendasaun Servisu Iha Terenu 36

I. INTRODUSAUN

1.1 Enkuadramentu Legal


Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análize kustu-benefísiu ne'ebe razoável no viavél.

Depois de Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimentu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projetu sira iha programa Kapital Desenvolvimentu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liuhusi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Dili



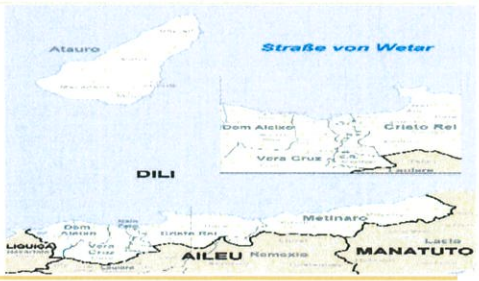

Dadus husi Livru 3B OJE 2021, Pajina 46

Mapa hatudu pozisaun jeográfika Autoridade Munisipal Dili iha luan hamutuk 372 km² ho populasaun 234,026 tuir Sensus 2010. Autoridade Munisipal Dili iha Posto Administrativo 6 ho Sukus 31 no aldeias 241 hanesan hatudu iha Tabela 1.

Tabel 1.2.1 : Postos Administrativos,Sucos no Aldeias.

Cristo Rei		**Dom Aleixo**		**Vera Cruz**	
Sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**T.Aldeias**
Balibar		Bairro Pite		Caicoli	
Becora		Comoro		Colmera	
Bidau Santana		Fatuhada		Dare	
Camea		Kampung Alor		Lahane Ocidental	
Culu Hun				Mascarenhas	
Hera				Motael	
Metiaut				Vila Verde	
Total					
Nain Feto		**Atauro**		**Metinaro**	
Sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**T.Aldeias**
Acadiru Hun		Beloi		Duyung	
Bemori		Biqueli		Sabuli	
Bidau Lecidere		Macadade			
Gricenfor		Maquili			
Lahane Oriental		Vila Maumeta			
Santa Cruz	-	-	-		
Total					

Tabel 2.2.2 : Força de Trabalho ADN, I.P Municipio Dili

Forca de Trabalho ADN,I.P Municipio **Dili**								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	7					7	
2	Administrasaun no Financas	0					0	
3	Motorista	0					0	
4	Seguransa	0					0	
Total		7					7	

Tabel 3.2.3: Lista Asset ADN,I.P Municipio Dili.

ASET ADN,IP MUNICIPIO DILI								
No	**Deskrisaun**	**Total Aset Kada Tinan**					**Total**	**OBS**
		2021	**2022**	**2023**	**2024**	**2025**		
1	Edificio	0						
2	Armazem	0						
3	Kareta	0						
4	Motor	0						
5	Destop	6						
6	Laptop	1						
7	Printer	0						
8	Maquina Foto copya	0						
9	UPS	0						
10	Projector	0						
11	Saund System	0						
12	Server	0						
13	Handy Cam	0						
14	TV							
15	Equipamento Laboratorium	0						
16	Mesa	0						
17	Mesa Parti san	0						
18	Kadeira Roda	7						
19	Kadeira Biasa	0						
20	Armario File Besi	0						
21	Armario File Aluminium	0						
22	Armario File Ai	0						
23	Gaveta	7						
24	Sofa	0						
25	AC	0						
26	Lampu	0						

1.3. Lista Projectos

Projetu hotu neébe akumula iha lista neé bazeia ba dadus projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamento, tabela 1.3.2 Projetu por Sector no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabel 1.3.1: Projecto Municipio Dili Por Fundus Finansiamento

NO	POSTO ADMINISTRATIVO	TOTAL Emergency		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro			
2	Cristo Rei	3	$ 546,174.64	75.39%
3	Dom aleixo	5	$ 534,349.31	55.31%
4	Metinaro			
5	Nain Feto	1	$ 122,960.04	90.00%
6	Nasional			
7	Oe-cusse			
8	Regional			
9	vera cruz			
	Grand Total	9	$ 1,203,483.99	67.96%

NO	POSTO ADMINISTRATIVO	TOTAL FI		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro	1	$ 297,409.09	17.65%
2	Cristo Rei	13	$ 7,117,352.76	80.87%
3	Dom aleixo	22	$ 36,799,568.69	51.18%
4	Metinaro	2	$ 275,661.02	69.39%
5	Nain Feto	7	$ 8,577,328.59	69.73%
6	Nasional	22	$ 225,069,986.25	71.22%
7	Oe-cusse	4	$ 2,353,321.65	78.72%
8	Regional	1	$ 8,178,886.44	81.13%
9	vera cruz	12	$ 23,886,226.38	16.48%
	Grand Total	84	$ 312,555,740.87	65.12%

NO	POSTO ADMINISTRATIVO	TOTAL LM-BS		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro	1	$ 56,359.98	0.00%
2	Cristo Rei	8	$ 1,209,322.49	58.33%
3	Dom aleixo	15	$ 1,236,213.23	73.57%
4	Metinaro	3	$ 1,479,660.47	37.95%
5	Nain Feto	11	$ 830,444.42	43.25%
6	Nasional	4	$ 532,040.89	45.88%
7	Oe-cusse			
8	Regional	1	$ 373,666.00	70.00%
9	vera cruz	7	$ 594,043.63	50.72%
	Grand Total	50	$ 6,311,751.11	52.96%

NO	POSTO ADMINISTRATIVO	TOTAL LM-CD		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro			
2	Cristo Rei	11	$ 1,399,222.27	44.05%
3	Dom aleixo	16	$ 3,645,799.75	48.46%
4	Metinaro	4	$ 2,207,240.84	35.70%
5	Nain Feto	9	$ 1,763,876.82	50.87%
6	Nasional	2	$ 47,452,247.00	63.41%
7	Oe-cusse			
8	Regional	1	$ 53,025,601.00	70.88%
9	vera cruz	23	$ 7,863,843.55	31.91%
	Grand Total	66	$ 117,357,831.23	63.27%

NO	POSTO ADMINISTRATIVO	TOTAL LM-Covid 19		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro	2	$ 373,000.50	60.20%
2	Cristo Rei			
3	Dom aleixo			
4	Metinaro			
5	Nain Feto	1	$ 739,937.34	0.00%
6	Nasional			
7	Oe-cusse			
8	Regional			
9	vera cruz	2	$ 715,961.43	77.27%
	Grand Total	5	$ 1,828,899.27	42.53%

NO	POSTO ADMINISTRATIVO	TOTAL LM-TP		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro	1	$ 99,817.07	0.00%
2	Cristo Rei	5	$ 2,495,103.48	71.70%
3	Dom aleixo	9	$ 5,614,799.63	19.25%
4	Metinaro	3	$ 701,784.97	48.42%
5	Nain Feto	4	$ 303,948.57	14.71%
6	Nasional			
7	Oe-cusse			
8	Regional			
9	vera cruz	2	$ 2,033,100.61	34.44%
	Grand Total	24	$ 11,248,554.33	35.16%

NO	POSTO ADMINISTRATIVO	TOTAL PDIM		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro			
2	Cristo Rei	3	$ 745,628.55	85.33%
3	Dom aleixo	2	$ 109,095.91	88.19%
4	Metinaro			
5	Nain Feto			
6	Nasional			
7	Oe-cusse			
8	Regional			
9	vera cruz	1	$ 143,579.83	83.72%
	Grand Total	6	$ 998,304.29	85.41%

NO	POSTO ADMINISTRATIVO	TOTAL MUNICIPIO DILI,NASIONAL,RAEOA		
		TOTAL PROJECTO	MONTANTE KONTRATO ($)	PERSENTAGEM EXECUSAUN (%)
1	Atauro	5	$ 826,586.64	33.52%
2	Cristo Rei	43	$ 13,512,804.19	73.37%
3	Dom aleixo	69	$ 47,939,826.52	47.94%
4	Metinaro	12	$ 4,664,347.30	40.32%
5	Nain Feto	33	$ 12,338,495.78	59.92%
6	Nasional	28	$ 273,054,274.14	69.82%
7	Oe-cusse	4	$ 2,353,321.65	78.72%
8	Regional	3	$ 61,578,153.44	72.24%
9	vera cruz	47	$ 35,236,755.43	23.05%
	Grand Total	244	$ 451,504,565.09	63.69%

Dadus detallu kada projetu: #Anexu A

Tabel 1.3.2: Projecto Municipio Dili Por Sector

NO	SECTOR PROJECTO	Atauro		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO			
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS	3	$ 429,360.48	52.30%
6	EDUKASAUN	1	$ 99,817.07	0.00%
7	ELETRIFIKASAUN NASIONAL			
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO			
10	ESTRADAS			
11	FLOOD CONTROL			
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU			
15	MANUTENSAUN NO REHABILITASAUN	1	$ 297,409.09	17.65%
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS			
19	SAUDE			
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO			
24	Grand Total	5	$ 826,586.64	33.52%

NO	SECTOR PROJECTO	CRISTO REI		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO	5	$ 318,322.19	44.20%
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS	4	$ 2,588,866.25	80.49%
6	EDUKASAUN	8	$ 1,346,434.73	39.28%
7	ELETRIFIKASAUN NASIONAL	9	$ 2,921,692.53	78.41%
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO			
10	ESTRADAS	7	$ 4,087,396.37	80.39%
11	FLOOD CONTROL	2	$ 530,978.82	76.40%
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU			
15	MANUTENSAUN NO REHABILITASAUN	4	$ 869,444.03	70.69%
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS			
19	SAUDE	3	$ 675,251.63	67.68%
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO	1	$ 174,417.64	61.54%
24	Grand Total	43	$ 13,512,804.19	73.37%

NO	SECTOR PROJECTO	DOM ALEIXO		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO	7	$ 1,272,323.44	69.77%
4	DESENVOLVIMENTO URBANO E RURAL	1	$ 781,121.90	28.50%
5	EDIFICIOS PUBLICOS	14	$ 6,489,312.21	30.55%
6	EDUKASAUN	6	$ 661,099.82	0.00%
7	ELETRIFIKASAUN NASIONAL	6	$ 2,830,884.39	40.44%
8	EQUIPAMENTO INFROMATICO	1	$ 56,935.00	85.00%
9	ESTRADA- IMPRESTIMO			#DIV/0!
10	ESTRADAS	16	$ 32,563,247.07	51.81%
11	FLOOD CONTROL	1	$ 263,699.22	92.53%
12	ICT	1	$ 1,152,955.98	80.96%
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU	1	$ 42,859.34	71.50%
15	MANUTENSAUN NO REHABILITASAUN	8	$ 448,597.38	77.53%
16	PONTES	2	$ 238,814.51	0.00%
17	PORTOS	1	$ 386,456.87	0.00%
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS	2	$ 486,700.00	21.08%
19	SAUDE	2	$ 264,819.39	63.07%
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO			
24	Grand Total	69	$ 47,939,826.52	47.94%

NO	SECTOR PROJECTO	METINARO		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA	1	$ 273,270.70	70.00%
3	AGUA E SANEAMENTO	1	$ 87,856.59	43.07%
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS	2	$ 1,391,803.88	37.63%
6	EDUKASAUN	2	$ 241,530.97	0.00%
7	ELETRIFIKASAUN NASIONAL	1	$ 2,390.32	0.00%
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO			
10	ESTRADAS	2	$ 1,360,343.71	29.08%
11	FLOOD CONTROL			
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU			
15	MANUTENSAUN NO REHABILITASAUN			
16	PONTES			
17	PORTOS	1	$ 460,254.00	73.83%
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS			
19	SAUDE			
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL	1	$ 449,600.23	77.90%
23	TURISMO	1	$ 397,296.90	10.64%
24	Grand Total	12	$ 4,664,347.30	40.32%

NO	SECTOR PROJECTO	NAIN FETO		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO	1	$ 139,971.80	0.00%
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS	7	$ 2,375,802.46	79.94%
6	EDUKASAUN	3	$ 251,716.02	0.00%
7	ELETRIFIKASAUN NASIONAL	3	$ 843,062.08	75.03%
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO			
10	ESTRADAS	5	$ 6,315,379.08	64.44%
11	FLOOD CONTROL	1	$ 129,168.62	30.21%
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU	5	$ 1,036,371.13	50.55%
15	MANUTENSAUN NO REHABILITASAUN	5	$ 309,471.33	49.95%
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS			
19	SAUDE	2	$ 890,648.26	4.02%
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO	1	$ 46,905.00	81.41%
24	Grand Total	33	$ 12,338,495.78	59.92%

NO	SECTOR PROJECTO	VERA CRUZ		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO	2	$ 209,926.33	63.54%
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS	27	$ 19,629,714.08	32.57%
6	EDUKASAUN	3	$ 1,891,351.90	0.00%
7	ELETRIFIKASAUN NASIONAL	2	$ 505,188.97	62.89%
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO			
10	ESTRADAS	1	$ 7,049.68	90.00%
11	FLOOD CONTROL			
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU	1	$ 285,700.00	66.50%
15	MANUTENSAUN NO REHABILITASAUN	4	$ 569,901.35	81.88%
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS	4	$ 1,083,198.35	36.34%
19	SAUDE	1	$ 282,726.57	15.78%
20	SEGURANCA NO DEFESA	2	$ 10,771,998.20	1.62%
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO			
24	Grand Total	47	$ 35,236,755.43	23.05%

NO	SECTOR PROJECTO	NASIONAL		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS	1	$ 1,100,000.00	54.55%
2	AGRICULTURA	1	$ 69,978.38	92.28%
3	AGUA E SANEAMENTO	6	$ 7,557,238.90	53.51%
4	DESENVOLVIMENTO URBANO E RURAL	2	$ 23,850,768.60	72.91%
5	EDIFICIOS PUBLICOS			
6	EDUKASAUN			
7	ELETRIFIKASAUN NASIONAL	1	$ 46,872,339.00	63.33%
8	EQUIPAMENTO INFROMATICO	2	$ 3,363,254.74	91.99%
9	ESTRADA- IMPRESTIMO	1	$ 12,964,487.49	83.52%
10	ESTRADAS	4	$ 706,837.51	58.29%
11	FLOOD CONTROL			
12	ICT			
13	IMPRESTIMO	6	$ 170,621,744.75	70.59%
14	JUVENTUDE NO DESPORTU	1	$ 1,938,481.77	47.75%
15	MANUTENSAUN NO REHABILITASAUN			
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS	2	$ 902,708.00	75.54%
19	SAUDE			
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS	1	$ 3,106,435.00	79.40%
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO			
24	Grand Total	28	$ 273,054,274.14	69.82%

NO	SECTOR PROJECTO	REGIONAL		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO			
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS			
6	EDUKASAUN			
7	ELETRIFIKASAUN NASIONAL	1	$ 53,025,601.00	70.88%
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO	1	$ 8,178,886.44	81.13%
10	ESTRADAS	1	$ 373,666.00	70.00%
11	FLOOD CONTROL			
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU			
15	MANUTENSAUN NO REHABILITASAUN			
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS			
19	SAUDE			
20	SEGURANCA NO DEFESA			
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO			
24	Grand Total	3	$ 61,578,153.44	72.24%

NO	SECTOR PROJECTO	OECUSSE		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS			
2	AGRICULTURA			
3	AGUA E SANEAMENTO			
4	DESENVOLVIMENTO URBANO E RURAL			
5	EDIFICIOS PUBLICOS			
6	EDUKASAUN			
7	ELETRIFIKASAUN NASIONAL	3	$ 693,149.25	51.71%
8	EQUIPAMENTO INFROMATICO			
9	ESTRADA- IMPRESTIMO			
10	ESTRADAS			
11	FLOOD CONTROL			
12	ICT			
13	IMPRESTIMO			
14	JUVENTUDE NO DESPORTU			
15	MANUTENSAUN NO REHABILITASAUN			
16	PONTES			
17	PORTOS			
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS			
19	SAUDE			
20	SEGURANCA NO DEFESA	1	$ 1,660,172.40	90.00%
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS			
22	SOLIDARIEDADE E SOCIAL			
23	TURISMO			
24	Grand Total	4	$ 2,353,321.65	78.72%

NO	SECTOR PROJECTO	TOTAL MUNICIPIO DILI,REGIONAL,NASIONAL,RAEOA		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	AEROPORTOS	1	$ 1,100,000.00	54.55%
2	AGRICULTURA	2	$ 343,249.08	74.54%
3	AGUA E SANEAMENTO	22	$ 9,585,639.25	54.70%
4	DESENVOLVIMENTO URBANO E RURAL	3	$ 24,631,890.50	71.50%
5	EDIFICIOS PUBLICOS	57	$ 32,904,859.36	39.84%
6	EDUKASAUN	23	$ 4,491,950.51	11.78%
7	ELETRIFIKASAUN NASIONAL	26	$ 107,694,307.54	66.87%
8	EQUIPAMENTO INFROMATICO	3	$ 3,420,189.74	91.87%
9	ESTRADA- IMPRESTIMO	2	$ 21,143,373.93	82.60%
10	ESTRADAS	36	$ 45,413,919.42	55.72%
11	FLOOD CONTROL	4	$ 923,846.66	74.55%
12	ICT	1	$ 1,152,955.98	80.96%
13	IMPRESTIMO	6	$ 170,621,744.75	70.59%
14	JUVENTUDE NO DESPORTU	8	$ 3,303,412.24	50.55%
15	MANUTENSAUN NO REHABILITASAUN	22	$ 2,494,823.18	65.58%
16	PONTES	2	$ 238,814.51	0.00%
17	PORTOS	2	$ 846,710.87	40.13%
18	PREPARASAUN DESENHOS NO SUPERVISAUN -NOVOS PROJECTOS	8	$ 2,472,606.35	47.65%
19	SAUDE	8	$ 2,113,445.85	33.33%
20	SEGURANCA NO DEFESA	3	$ 12,432,170.60	13.42%
21	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS	1	$ 3,106,435.00	79.40%
22	SOLIDARIEDADE E SOCIAL	1	$ 449,600.23	77.90%
23	TURISMO	3	$ 618,619.54	30.36%
24	Grand Total	244	$ 451,504,565.09	63.69%

Dadus detallu kada projetu: #Anexu A

Tabel 1.3.3: Projecto Municipio Dili Por Ministerio

NO	DONO DO PROJECTO	Atauro		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO			
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS			
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	1	$ 56,359.98	0.00%
9	MINISTERIO DA DEFESA			
10	MINISTERIO DA JUSTICA			
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	1	$ 297,409.09	17.65%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	1	$ 99,817.07	0.00%
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE	2	$ 373,000.50	60.20%

22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN			
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU			
32	SEFOPE			
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	5	$ 826,586.64	33.52%

NO	DONO DO PROJECTO	Cristo Rei		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO	1	$ 2,068,587.24	86.48%
6	HOSPITAL NACIONAL GUIDO VALADARES	1	$ 63,076.61	82.11%
7	MINISTERIO AGRIKULTURA E PESCAS			
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	1	$ 58,919.16	17.52%
9	MINISTERIO DA DEFESA			
10	MINISTERIO DA JUSTICA			
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	25	$ 8,254,457.42	78.06%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	9	$ 1,756,734.64	43.89%
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus	1	$ 119,578.85	37.76%
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE	3	$ 815,417.40	64.99%
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN			
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 174,417.64	61.54%

25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU			
32	SEFOPE			
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	1	$ 201,615.23	82.51%
	Grand Total	43	$ 13,512,804.19	73.37%

NO	DONO DO PROJECTO	Dom Aleixo		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO	3	$ 4,953,699.81	21.82%
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS	1	$ 19,249.03	95.84%
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	2	$ 109,095.91	88.19%
9	MINISTERIO DA DEFESA	4	$ 302,542.80	80.14%
10	MINISTERIO DA JUSTICA	1	$ 57,463.94	73.28%
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			

12	MINISTERIO DAS OBRAS PUBLICAS	37	$ 39,047,736.88	52.28%
13	MINISTERIO DEFESA	1	$ 38,450.39	90.04%
14	MINISTERIO DO INTERIOR	1	$ 89,984.12	84.52%
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	6	$ 661,099.82	0.00%
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU	6	$ 1,007,079.87	39.85%
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE	3	$ 316,264.30	62.03%
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$ 464,002.78	59.55%
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	2	$ 486,700.00	21.08%
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC	1	$ 386,456.87	0.00%
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU			
32	SEFOPE			
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	69	$ 47,939,826.52	47.94%

NO	DONO DO PROJECTO	Metinaro		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO			
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS	1	$ 273,270.70	70.00%
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL			
9	MINISTERIO DA DEFESA	2	$ 1,391,803.88	37.63%
10	MINISTERIO DA JUSTICA			
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	3	$ 501,660.45	73.07%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	2	$ 241,530.97	0.00%
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE			
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	1	$ 449,600.23	77.90%
23	MINISTERIO TRANPORTES E KOMUNIKASAUN			

24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	2	$ 1,346,227.07	8.10%
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU			
32	SEFOPE	1	$ 460,254.00	73.83%
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	12	$ 4,664,347.30	40.32%

NO	DONO DO PROJECTO	Nain Feto		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC	1	$ 256,843.00	69.08%
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA	1	$ 97,498.81	85.89%
5	GABINETE DO PRIMEIRO MINISTRO	1	$ 52,232.55	85.62%
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS			
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	1	$ 46,905.00	81.41%
9	MINISTERIO DA DEFESA			
10	MINISTERIO DA JUSTICA			
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	2	$ 158,889.74	13.60%

12	MINISTERIO DAS OBRAS PUBLICAS	12	$ 9,264,959.90	67.09%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	3	$ 251,716.02	0.00%
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA	1	$ 7,583.06	87.03%
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE	2	$ 890,648.26	4.02%
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$ 26,426.13	85.73%
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	1	$ 95,425.00	88.63%
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL	1	$ 30,037.14	90.00%
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	3	$ 505,899.40	5.38%
32	SEFOPE			
33	SEJD	2	$ 530,471.73	93.62%
34	TRADE INVEST			
35	TRIBUNAL RECUSSO	1	$ 122,960.04	90.00%
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	33	$ 12,338,495.78	59.92%

NO	DONO DO PROJECTO	Vera Cruz		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega	2	$ 134,670.96	63.30%
3	CFP	1	$ 35,500.00	95.00%
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO	2	$ 2,033,100.61	34.44%
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS			
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	2	$ 222,397.21	59.59%
9	MINISTERIO DA DEFESA			
10	MINISTERIO DA JUSTICA	4	$ 536,146.59	9.35%
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	13	$ 1,715,903.70	61.08%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR	2	$ 10,771,998.20	1.62%
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE	3	$ 998,688.00	59.86%
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN			
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
25	MINISTRO PARA OS ASSUNTOS DOS	1	$ 88,510.00	30.00%

	COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA	1	$ 556,612.74	89.73%
29	RADIO TELEVISAUN TIMOR LESTE	1	$ 37,605.25	90.00%
30	SECRETARIADO ESTADO KOMUNIKASAUN	2	$ 412,212.00	18.44%
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	1	$ 285,700.00	66.50%
32	SEFOPE			
33	SEJD			
34	TRADE INVEST	1	$ 37,582.90	50.29%
35	TRIBUNAL RECUSSO	2	$ 11,557,966.35	24.82%
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	9	$ 5,812,160.92	27.28%
	Grand Total	47	$ 35,236,755.43	23.05%

NO	DONO DO PROJECTO	Nasional		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO	2	$ 3,363,254.74	91.99%
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS	1	$ 69,978.38	92.28%
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL			
9	MINISTERIO DA DEFESA			
10	MINISTERIO DA JUSTICA			
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	19	$ 239,556,829.65	69.32%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			

15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS	2	$ 4,206,435.00	72.90%
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	2	$ 23,850,768.60	72.91%
21	MINISTERIO SAUDE			
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN	1	$ 68,526.00	68.03%
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	1	$ 1,938,481.77	47.75%
32	SEFOPE			
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	28	$ 273,054,274.14	69.82%

NO	DONO DO PROJECTO	OECUSSE		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO			
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS			
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL			
9	MINISTERIO DA DEFESA	1	$ 1,660,172.40	90.00%
10	MINISTERIO DA JUSTICA			
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	3	$ 693,149.25	51.71%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE			
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN			

24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU			
32	SEFOPE			
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	4	$ 2,353,321.65	78.72%

NO	DONO DO PROJECTO	Regional		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC			
2	Centro Nacional Chega			
3	CFP			
4	CONSELHO DA EMPRENSA			
5	GABINETE DO PRIMEIRO MINISTRO			
6	HOSPITAL NACIONAL GUIDO VALADARES			
7	MINISTERIO AGRIKULTURA E PESCAS			
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL			
9	MINISTERIO DA DEFESA			
10	MINISTERIO DA JUSTICA			

11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS			
12	MINISTERIO DAS OBRAS PUBLICAS	3	$ 61,578,153.44	72.24%
13	MINISTERIO DEFESA			
14	MINISTERIO DO INTERIOR			
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU			
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA			
17	MINISTERIO FINANCAS			
18	MInisterio Koordenador Asuntu Ekonómikus			
19	MINISTERIO PLANU E ORDENAMENTU			
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS			
21	MINISTERIO SAUDE			
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN			
23	MINISTERIO TRANPORTES E KOMUNIKASAUN			
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA			
25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL			
26	MTC			
27	PARLAMENTU NASIONAL			
28	PROCURADORIA GERAL DA REPUBLIKA			
29	RADIO TELEVISAUN TIMOR LESTE			
30	SECRETARIADO ESTADO KOMUNIKASAUN			
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU			
32	SEFOPE			
33	SEJD			
34	TRADE INVEST			
35	TRIBUNAL RECUSSO			
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E			
	Grand Total	3	$ 61,578,153.44	72.24%

NO	DONO DO PROJECTO	TOTAL MUNICIPIO DILI,NASIONAL,REGIONAL, RAEOA		
		TOTAL PROJECTO	MONTANTE KONTRATU ($)	PERSENTAGEM EXECUSAUN (%)
1	CAC	1	$ 256,843.00	69.08%
2	Centro Nacional Chega	2	$ 134,670.96	63.30%
3	CFP	1	$ 35,500.00	95.00%
4	CONSELHO DA EMPRENSA	1	$ 97,498.81	85.89%
5	GABINETE DO PRIMEIRO MINISTRO	9	$ 12,470,874.95	53.79%
6	HOSPITAL NACIONAL GUIDO VALADARES	1	$ 63,076.61	82.11%
7	MINISTERIO AGRIKULTURA E PESCAS	3	$ 362,498.11	75.67%
8	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	7	$ 493,677.26	56.16%
9	MINISTERIO DA DEFESA	7	$ 3,354,519.08	67.38%
10	MINISTERIO DA JUSTICA	5	$ 593,610.53	15.54%
11	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	2	$ 158,889.74	13.60%
12	MINISTERIO DAS OBRAS PUBLICAS	116	$ 360,910,259.78	68.00%
13	MINISTERIO DEFESA	1	$ 38,450.39	90.04%
14	MINISTERIO DO INTERIOR	3	$ 10,861,982.32	2.30%
15	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	21	$ 3,010,898.52	25.61%
16	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA	1	$ 7,583.06	87.03%
17	MINISTERIO FINANCAS	2	$ 4,206,435.00	72.90%
18	MInisterio Koordenador Asuntu Ekonómikus	1	$ 119,578.85	37.76%
19	MINISTERIO PLANU E ORDENAMENTU	6	$ 1,007,079.87	39.85%
20	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	2	$ 23,850,768.60	72.91%
21	MINISTERIO SAUDE	13	$ 3,394,018.46	46.68%
22	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	1	$ 449,600.23	77.90%
23	MINISTERIO TRANPORTES E KOMUNIKASAUN	3	$ 558,954.91	61.83%
24	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	4	$ 756,542.64	38.93%

25	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	3	$ 1,434,737.07	9.45%
26	MTC	1	$ 386,456.87	0.00%
27	PARLAMENTU NASIONAL	1	$ 30,037.14	90.00%
28	PROCURADORIA GERAL DA REPUBLIKA	1	$ 556,612.74	89.73%
29	RADIO TELEVISAUN TIMOR LESTE	1	$ 37,605.25	90.00%
30	SECRETARIADO ESTADO KOMUNIKASAUN	2	$ 412,212.00	18.44%
31	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	5	$ 2,730,081.17	41.86%
32	SEFOPE	1	$ 460,254.00	73.83%
33	SEJD	2	$ 530,471.73	93.62%
34	TRADE INVEST	1	$ 37,582.90	50.29%
35	TRIBUNAL RECUSSO	3	$ 11,680,926.39	25.50%
36	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	10	$ 6,013,776.15	29.13%
	Grand Total	244	$ 451,504,565.09	63.69%

Dadus detallu kada projetu: #Anexu A

Tabela 1.3.4 : Population Projection Municipiu, Postu Administrativo, Suco tuir Sexu no Grupu idade 2015-2022.

Administrativo Posto, Suco no Sexu	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Atauro	**3,494**	**3,562**	**2,786**	**2,675**	**3,494**
Cristo Rei	**26,813**	**24,505**	**15,769**	**15,087**	**26,813**
Dom Aleixo	**58,165**	**52,276**	**30,971**	**29,264**	**58,165**
Metinaro	**2,189**	**2,004**	**1,657**	**1,615**	**2,189**
Nain Feto	**15,028**	**13,668**	**7,522**	**7,094**	**15,028**
Vera Cruz	**16,486**	**15,193**	**8,540**	**8,060**	**16,486**

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan ne'e hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu katak progresu actual fulan ida ne'e siknifika porsentagen servisu ne'ebe atinje deit iha fulan ne'e nia laran, montante actual fulan ida ne'e bazeia ba orsamentu ne'ebe hetan husi progresu fulan ida ne'e nia rasik no ikus porsentagen actual fulan ida ne'e hatudu progresu fisiku komulativu ne'ebe akumula husi porsento anterior no fulan ida ne'e nian, kompletu ba detallu bele haree iha #Anexu B, detallu ba Back-Up #Anexu C no Fotografia bele hare #Anexu D.

III. OBSTÁCLO IHA TERENU

3.1 Obstáclo Servisu Iha Terenu

- **Obstaclo l ba ITI no EPAS**

1. Buka solusaun lalais ba projetu sira ne'ebé abandona ho projetu na'in se la'e enginheiru munisipiu ninia relatoriu laiha rejultadu no projetu sira sei kontinua abandona
2. Aumenta transporte nune'e bele fasilita hala'o inspesaun
3. Hasa'e kapasidade internet
4. Diminui tiha parte instrusaun serbisu tamba enjinheru munisipiu halo *"trible"* hodi aumenta volume serbsu maibe fungsaun ida de'it.

- **Responsavel Konsultan**

1. Ba servisu konsultan design ami imfrenta problema wainhira atu halo planu inspeksaun tamba ezekusaun ba servisu hirak ne'e bazeia husi relatorio nebe Ministerio/Dono do projeto submete mai ADN. Ne'e duni susar baa ami atu prienxe planu servisu.

2. Ami imfrenta problema wainhira atu input data konsultan design ba Sistema drop box tamba folder nebe prepara ona responde liu ba servisu kontraktor nian.

3. Menos transporte hodi afeita ba planu inspeksaun iha terrenu

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

- Recomendação parte **Konsultan**

1. Husu ba ekipa base de dadus atu kria folder iha Sistema drop box nebe bele relata imformasaun kona ba servisu konsultan design nian
2. Husu atu iha Sistema manjamen logistika nebe diak hodi la bele fo impaktu wainhira atu halo inspeksaun iha terrenu tuir planu servisu nebe engineiru sira prepara ona.

- Recomendação parte Eletricidade

1. Husu ba parte ITC, ADN – I.P bele kria Folder Sistem ba Seksaun M & E, ADN – I.P.
2. Husu atu aumenta tan rekursu iha Seksaun M & E, ADN – I.P.

Note: Asinatura husi Eng Municipio Dili

Força de Trabalho ADN,I.P Municipio Dili						
No	**Deskrisaun**	**Identidade**				
		Naran Kompletu	**Nu. ID Card**	**Pozisaun**	**Fotografia**	**Asinatura**
1	Enjineiru	Pedro de Lurdes Alves		Enjineiru EPAS		
		Julmira Soares Sampaio		Enjineiru EPAS		

		Egidio Goncalves		Enjineiru EPAS		
		Joao Q do Rego		Enjineiru ITI		
		Rosalia de Fatima		Enjineiru EPAS		
		Manuel Estrela		Enjineiru EPAS		
	Enjineiru	Eduardo do Santos		Enjineiru ITI		
		Camilio de Jesus		Enjineiru METIC		

		Ezequiel R. de Oliveira		Enjineiru METIC		
		Johanes Hornay		Enjineiru VEBD		
3	Motorista			Motorista	Nao identifikado	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Atauro	Dili	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	$ 297,409.09	Dec. 20, 2019	19.61%		19.61%
2	New Construction of Laboratory for Covid-19	MINISTERIO SAUDE	LM-Covid 19	EDIFICIOS PUBLICOS	Atauro	Dili	Fitun Galilea Unipessoal Lda	No: /NCB/M.S/DNA/RBK-20-160	$ 69,859.04	Sept. 30, 2020	96.09%		96.09%
3	New Construction of Isolation for Covid-19 i	MINISTERIO SAUDE	LM-Covid 19	EDIFICIOS PUBLICOS	Atauro	Dili	Lygelina Alexix Unip. Lda	No: /NCB/M.S/DNA/DC-20-161	$ 303,141.46	Oct. 9, 2020	75.12%	9.04%	84.16%
4	konstrusaun residensia oficial posto administ	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-BS	EDIFICIOS PUBLICOS	Atauro	Dili	Realidade Salmes Unip,Lda		$ 56,359.98		0.00%		0.00%
5	Konstrusaun ka Reabilitasaun ba EBC Biqueli	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Atauro	Dili	MEJD PKRIE EBC BIQUELI	KONTRATU COMUNITARIA	$ 99,817.07		0.00%		0.00%
6	Rehabilitasaun intake no kanu transmisaun iha La Koto & Mutu Dare	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Cristo Rei	Dili	Amigo Unip. Lda	SSS/021/MOP-2020	$ 51,111.18	June 12, 2020	60.66%		60.66%
7	New Installation Street Light at Cristo Rei - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Silkar International Unip. Lda	RDTL/MOP-SEE/CGI-PEN:0000246	$ 45,715.42	Oct. 2, 2013	100.00%		100.00%
8	New Installation of MV, LV Line and House Connection from FeederII Becora to Taibesi, Bemori and Balide - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Ceuilaju.Lda	DTL/MOPTC-VOMPTC/CGI-PEN:00004	$ 724,286.69	Sept. 1, 2016	86.66%		86.66%
9	New Installation of MV, LV Line and House Connection from Balide to Delta 3, Fomento, Manleuana, Bualaran, Aldeia Moris Dame, Eskola Fatumeta, Cacaulido, Ailok Laran, Bua Laran and Lisbutak - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Derren Construction Unip.Lda.	TL/MOPTC-VMOPTC/CGI-PEN : 0000	$ 1,292,209.31	Sept. 1, 2016	86.00%		86.00%
10	New Installation of MV, LV Line and House Connection from Biterlaun Fatu Ahi to Lenuk Hun Cristo Rei - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Jmindo	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 262,372.99	Sept. 1, 2016	96.27%		96.27%
11	New Installation of MV, LV Line and House Connection from Hera Ailok Laran to Sokaer Laran - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Vinario Unip.,Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 323,645.08	Sept. 10, 2016	96.27%		96.27%
12	New Construction of ICCU at Hospital Nacional Guido Valadares, Dili Municipality	MINISTERIO SAUDE	FI	SAUDE	Cristo Rei	Dili	SIKUNDI, Unipessoal, Lda	SSS/281/MOH-2016	$ 243,636.40	Sept. 14, 2017	32.19%		32.19%
13	Consulting Services for Detail Engineering Design (DED) for Pediatric and ICCU Building in Guido Valadares National Hospital	MINISTERIO SAUDE	FI	SAUDE	Cristo Rei	Dili	Philcoei International, Inc. In JV with Luis and Associates, Co	SSS/035/MOPTC-2017	$ 230,000.00	May 5, 2014	95.00%		95.00%
14	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Cristo Rei	Dili	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	$ 862,117.01	Aug. 25, 2017	99.62%		99.62%
15	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Cristo Rei	Dili	Aspalink Unip Lda	SSS/131/MOPTC-2017	$ 1,942,664.52	Sept. 7, 2017	89.36%		89.36%
16	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Cristo Rei	Dili	Star King Unip. Lda	SSS/012/MOP-2020	$ 396,875.59	June 4, 2020	100.00%		100.00%
17	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Cristo Rei	Dili	Nimia Unip Lda	RT/154/MOPTC-2016	$ 84,143.33	April 21, 2017	90.00%		90.00%
18	Rehabilitasaun Tanke Reservatoriu iha Asgor no Bidau Masaur/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Cristo Rei	Dili	Selhar	RFQ-MOP-190047	$ 94,675.28	Oct. 22, 2019	51.65%		51.65%
19	Konstrusaun Moru Hadulas Bomba Bidau /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Cristo Rei	Dili	SARCADEFAT Unip.Lda	MOP-W-190164	$ 93,376.42	Oct. 22, 2019	100.00%		100.00%
20	Konstrusaun Moru Hadulas Bomba fomentu /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Cristo Rei	Dili	H FOUN Unip.Lda	MOP-W-190189	$ 39,586.42	May 11, 2019	100.00%	0.00%	100.00%
21	Lot 1 Urgent Installation of Street Lights in Mota Ulun-Bedois-Benamauk,Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Sirlacoli Unip. Lda	MPW-W-200032	$ 39,780.30	Dec. 19, 2019	75.91%		75.91%
22	Installation of Street Lights Prizaun Becora-Culuhun California (Lot 2)/162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Oulale unip.Lda	MPW-W-190261	$ 46,948.00	Oct. 19, 2019	93.48%		93.48%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
23	Konstrusaun Igreza Sagrada Corasaun de Jesus Becora	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	Cristo Rei	Dili	Carya Timor Leste Lda	Transferencia Publica	$ 2,068,587.24	Sept. 15, 2015	100.00%		100.00%
24	Rehabilitasaun & Extensaun Laboratorio Nacional Bidau - Dili	HOSPITAL NACIONAL GUIDO VALADARES	LM-BS	MANUTENSAUN NO REHABILITASAUN	Cristo Rei	Dili	Talamori	RDTL-MS-LNS-RFQ-17-064	$ 63,076.61	Dec. 6, 2017	91.23%		91.23%
25	Escola Secundaria Tekniko Vocasional 28 de Novembru iha Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	MANUTENSAUN NO REHABILITASAUN	Cristo Rei	Dili	Dirbajudi	RDTL RCB/01-R/ME-DNA/REHAB	$ 410,299.91	Oct. 27, 2016	65.56%		65.56%
26	Rehabilitasaun Konstrusaun ESTV 28 Novembro - Dili (Rf)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Cristo Rei	Dili	Biqueli Pala Unip. Lda	08KDM/AM-DIL/XI/2019	$ 329,247.37	Nov. 6, 2019	98.60%		98.60%
27	Rehabilitasaun ESTV Comercio E Economia	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN	Cristo Rei	Dili	Fitun Roman Polmar Unip. Lda	06/KDM/AM-DIL/X/2019	$ 241,963.54	Oct. 8, 2019	93.82%		93.82%
28	RM Pecas Sofremento pagamento Bee Mos	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Cristo Rei	Dili	Flocinob Motis Unip Lda	MOP/W-190185	$ 39,572.89	Dec. 31, 2019	100.00%	0.00%	100.00%
29	Rehabilitation of Medicine Laboratorium in Lahane	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	SAUDE	Cristo Rei	Dili	Nevan Construction Unip Lda	012/UNTL/EXT/C/2016	$ 201,615.23	Sept. 28, 2015	91.68%		91.68%
30	Lot 1 Urgent Installation of Street Lights in Cristo Rei,Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	Hanaria Electrial Unip.Lda	MOP-W-190136	$ 96,161.99	Aug. 15, 2019	72.97%		72.97%
31	Urgent Installation of Street Lights in Cristo Rei, Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Cristo Rei	Dili	9 Brothers Unip Lda	MOP-W-190134	$ 90,572.75	Aug. 15, 2020	60.75%		60.75%
32	Consultancy to develop A feasibility study and master plan Guido Valadares National Hospital (Bem Serviso)	MINISTERIO SAUDE	LM-BS	EDIFICIOS PUBLICOS	Cristo Rei	Dili	Mafra Consultante Unipessoal Lda	FBS-DNA-MOP-19018-B	$ 341,781.00	March 25, 2020	40.00%		40.00%
33	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Cristo Rei	Dili	Titisa Louro Unip.Lda	MPW-W-210067	$ 173,960.80	June 15, 2021	90.82%		90.82%
34	New Construction Of Gabions Tower No. 6 Section Dili-Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	FLOOD CONTROL	Cristo Rei		Jova Construction	NCB/034/MOP-2020	$ 232,158.43	5-Jul-21	100.00%		100.00%
35	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY.	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	FLOOD CONTROL	Cristo Rei	Dili	KEFI OEL Unip.Lda		$ 298,820.39		75.09%		75.09%
36	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Cristo Rei	Dili	Carya Timor Leste Lda	SSS/009/MOP-2020	$ 477,527.99	June 4, 2020	100.00%		100.00%
37	For Clean Up Of Metiaut - Cristo Rei, Areia Branca - Dolok Oan Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS	Cristo Rei	Dili	Tinolina Unipessoal, Lda	MPW-W-SS-210023	$ 50,020.86	28-May-21	100.00%		100.00%
38	New Construction of Gabion Tower No 6 Section Hera -Manatuto, Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS	Cristo Rei	Dili	Vilagem Construction Unip.Lda	NCB/032/MOP/2020	$ 184,229.60		100.00%		100.00%
39	Rehabilitation Construction Of Crocodile Cas	MInisterio Koordenador Asuntu Ekonómikus	LM-BS	EDIFICIOS PUBLICOS	Cristo Rei	Dili	Santana Diak Unipessoal Lda	603DNRHAL/DGA/SEA-MCAE/IX/2021	$ 119,578.85		70.64%	7.12%	77.76%
40	Rehabilitasaun no Konstrusaun Jardim Kristo	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	TURISMO	Cristo Rei	Dili	Mendith UnipLda	01/PDIM/A.M./DILI/X/2017	$ 174,417.64		75.00%		75.00%
41	Konstrusaun sede suko Ailok	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-CD	EDIFICIOS PUBLICOS	Cristo Rei	Dili	Liberta	05/KAM/AM-DIL/IX/2021	$ 58,919.16		42.62%	12.15%	54.77%
42	Projetu Konstrusaun Foun no Rehabilitasaun ba EBC Sergio Viera de Melo Becora, Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	Cristo Rei	Dili	Delatina	NCB:06/MEJD/DNA/2021	$ 149,587.82		0.00%		0.00%
43	Projetu Konstrusaun Foun ba ESTV Hera	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	Cristo Rei	Dili	Timorindo Unip. Lda	NCB:05/MEJD/DNA/2021	$ 199,119.76		0.00%		0.00%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
44	Konstrusaun ka Reabilitasaun ESTV 28 de Novembro Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Cristo Rei	Dili	MEJD PKRIE ESTV 28 DE NOVEMBRO BECORA	KONTRATU COMUNITARIA	$ 143,567.64		4.16%		4.16%
45	Konstrusaun ka Reabilitasaun ba ESG 12 de Novembro Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Cristo Rei	Dili	MEJD PKRIE ESG 12 DE NOVEMBRO-BECORA	KONTRATU COMUNITARIA	$ 132,376.67		3.53%		3.53%
46	Konstrusaun ka Reabilitasaun ba ESG FINANTIL	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Cristo Rei	Dili	MEJD PKRIE ESG FINANTIL	KONTRATU COMUNITARIA	$ 71,201.61		3.70%		3.70%
47	Konstrusaun ka Reabilitasaun ba EPE Ai-Loktuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Cristo Rei	Dili	MEJD PKRIE EPE AI-LOKTUTO	KONTRATU COMUNITARIA	$ 79,370.32		20.10%		20.10%
48	Emergency Project for Mota Bidau Toko Baru Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	Emergency	MANUTENSAUN NO REHABILITASAUN	Cristo Rei	Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	311,924.18		100.00%		100.00%
49	Instalasaun baixada electricidade, instalasaun kanu transmisaun & lutu hadulas estasaun bomba Tuana Laran	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	Dom aleixo	Dili	Montez Frere Unip. Lda	SSS/022/MOP-2020	$ 68,988.75	June 12, 2020	85.84%		85.84%
50	Melhoramento kanu transmisaun no distribuisaun iha Maloa	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	Dom aleixo	Dili	Haksolok Java Motor Unip Lda	SSS/020/MOP-2010	$ 190,507.61	June 12, 2020	81.85%	0.00%	81.85%
51	New Installation of MV, LV line and House Connection from Timor Block to Vila Verde, Ponte Comoro and Fomento - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Dom aleixo	Dili	Cartilo.Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 733,130.60	Sept. 1, 2016	46.22%		46.22%
52	Rehabilitasaun Linha Media Tensaun & Baixa Tensaun / Feeder 1 central elctric comoro Rotunda	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Dom aleixo	Dili	Embi elcrtic.Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 643,682.73	Sept. 1, 2016	27.91%		27.91%
53	New Installation MV, LV Line and House Connection from Bairo Pite to Aldeia ba Dame - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Dom aleixo	Dili	Joia Leste Unip. Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 275,458.38	Sept. 1, 2016	90.00%		90.00%
54	New Installation of MV, LV Line and House Connection from Fatuhada to Behoris, Arbiru Beach, Comoro Market, and Bebonuk - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Dom aleixo	Dili	Ladamutu Unip. Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 917,122.66	Sept. 1, 2016	50.48%		50.48%
55	New Installation MV, LV Line and House Connection From Rotunda Nicolau Lobato to Terminal Tasi Tolu-Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Dom aleixo	Dili	Sonalevi Unip. Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 174,335.12	Sept. 1, 2016	94.87%		94.87%
56	Maintenance, Repair & New Electrical Installation at Ministerio Do Plano E Ordenamento	MINISTERIO PLANU E ORDENAMENTU	LM-CD	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Titam Star Supplayer unip.lda	RFQ/040/ANATL,EP-2019	$ 25,089.09	Oct. 26, 2020	92.28%		92.28%
57	Consulting services for DED of the new Ministry of Commerce Industry and Enviroment Training Center	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Dom aleixo	Dili	Vítor Hugo Coordenação e Gestão de Projetos, S.A., através de emprendimento conjunto com a Quadromor Timor - Sistemas de Engenharia, S.A	RFP/030/MCIE-2013	$ 216,700.00	May 16, 2014	0.00%		0.00%
58	Detail Engineering design (DED) of The New Ministry of Commerce, Industry and Environment	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Dom aleixo	Dili	Philkoei International Inc. in JV with Arch Haus Asia Consultant, Inc	RFP/029/MCIE-2013	$ 270,000.00	May 28, 2014	40.00%		40.00%
59	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	$ 4,223,035.47	June 8, 2015	83.21%		83.21%
60	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	$ 3,752,597.99	Nov. 14, 2014	55.09%		55.09%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
61	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	$ 2,377,535.18	June 23, 2015	63.35%		63.35%
62	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	G and S Unipessoal Lda	SSS/040/MOPTC-2015	$ 4,290,731.32	Nov. 14, 2014	68.35%		68.35%
63	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	$ 3,501,758.11	June 26, 2015	45.68%		45.68%
64	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	$ 3,854,769.23	June 22, 2015	44.52%		44.52%
65	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	$ 2,471,296.53	Nov. 14, 2014	27.77%		27.77%
66	Road and Drainage Rehabilitation Project Aimutin to Manleuana	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Aspalink Unip Lda	SSS/308/MOPTC-2016	$ 2,238,074.57	July 11, 2016	98.61%		98.61%
67	New Construction of Median Line "Leader to Elemloi JNC"	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	$ 684,334.48	Sept. 7, 2017	100.00%		100.00%
68	Comoro Power Plant CCTV	MINISTERIO DAS OBRAS PUBLICAS	FI	ICT	Dom aleixo	Dili	SM Bark Technolgy Ltd	SSS/344/MOPTC-2016	$ 1,152,955.98	Dec. 9, 2016	92.00%		92.00%
69	Maloa River	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	$ 1,409,964.88	Sept. 12, 2017	50.00%		50.00%
70	Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dom aleixo	Dili	Mejori, Lda	SSS/127/MOPTC-2017	$ 2,571,467.20	Dec. 9, 2017	48.50%		48.50%
71	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	FLOOD CONTROL	Dom aleixo	Dili	DMF ACESO	MPW-W180036	$ 263,699.22	Jan. 10, 2019	92.53%		92.53%
72	Konstrusaun Beé mos ba Residencia Sr. Jeneral F-FDTL no Sr. Lu Olo iha Manleuana	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Dom aleixo	Dili	Caileba	MPWTC-502/5G/MOPTC/V/2017	$ 171,554.48	Aug. 5, 2017	56.89%		56.89%
73	Melhoramento Sistema Beé mos iha Area Delta 1,2,3 no 4	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Dom aleixo	Dili	Carisma	MPWTC-NCB-170020	$ 370,082.97	Sept. 12, 2017	100.00%		100.00%
74	Rehabilitasaun no Installasaun Metro Contador Sistema Be'e mos iha Perumnas Bairo Pite (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Dom aleixo	Dili	Sos Alssonix	MPWTC-NCB-170024	$ 178,740.80	Feb. 1, 2018	93.72%		93.72%
75	Urgent Repair of Roof Leaks at the New Building Ministry of Finance RDTL	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Carya Timor Leste	RDTL-SSS/MOPTC-2017	$ 273,512.05	Sept. 15, 2017	88.17%		88.17%
76	Perfurasaun Sistema Be'e Mos Iha Area Comoro DMA 37 /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Dom aleixo	Dili	Domin Timor Diak Lda	RFQ-MOP-190044	$ 95,321.33	Dec. 31, 2019	100.00%	0.00%	100.00%
77	Novo construsaun do campo polisportivo do Ministerio das Obras publicas (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	JUVENTUDE NO DESPORTU	Dom aleixo	Dili	ATUNEGOS UNIP.LDA	RFQ MOP/-W-190249	$ 42,859.34	Dec. 15, 2019	79.45%		79.45%
78	Construction of Terminal in Tasi Tolu	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-CD	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Mar vermelha unip.lda	RDTL-2014-C-101-MTC	$ 464,002.78	Oct. 20, 2014	66.17%		66.17%
79	Maintenance and Repair at F-FDTL, Head Qaurtel, Fatuhada	MINISTERIO DA DEFESA	LM-BS	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Victoria Const. Unip. Lda	2015-000065	$ 79,869.00	Sept. 14, 2015	90.57%		90.57%
80	Separasaun ba Aula Tolu iha Ministerio da	MINISTERIO DA DEFESA	LM-BS	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Algis	la mensiona nomor iha contratu	$ 6,200.17	Aug. 9, 2019	100.00%		100.00%
81	Manutensaun Edificio Ministerio da Defesa	MINISTERIO DA DEFESA	LM-BS	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Algis	RDTL 11 /MNEC /2019	$ 9,082.00	May 6, 2019	96.06%		96.06%
82	Manutensaun Residencia C.E.M.G. das F-FDTL	MINISTERIO DA DEFESA	LM-BS	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Panca Sekawan	No la mensiona contratu	$ 207,391.63	Feb. 22, 2019	87.83%		87.83%
83	New Construction of Sao Jose Aimutin Church in Comoro	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Grupo Timindo	Transferencia Publica	$ 3,000,000.00	May 25, 2015	72.33%		72.33%
84	New Construction of An'Nur Orphanage Building	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Asda A3i Unip. Lda.	Transferencia Publica	$ 269,156.17	Sept. 26, 2016	80.83%		80.83%
85	Konstrusaun Escola de Musica iha fatumeta	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Talisahe	Transferencia Publica	$ 1,684,543.64	Feb. 15, 2017	55.30%		55.30%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
86	Konstrusaun Sede Suku Bebonuk	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	PDIM	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Gazelle Unip. Lda	02/KDM/AM-DIL/VIII/2019	$ 54,548.53	Aug. 19, 2019	98.45%		98.45%
87	Konstrusaun Sede Suku Madohi	MINISTÉRIO DA	PDIM	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Domcos Hornay Unip. Lda	05/KDM/AM-DIL/VIII/2019	$ 54,547.38	Sept. 18, 2019	97.52%		97.52%
88	Rehabilitasaun and Maintanance of Vice Minister office in Mandarin	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Milcha Unip Lda	364/DNA-DGAF-MOP/XII/2019	$ 9,466.24	April 5, 2020	81.76%		81.76%
89	Manutensaun Edificio iha Gabinete Ministro nian	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Otsop Paris Unip Lda	RDTL-MAP176/GM/VIII/2019	$ 19,249.03	Aug. 26, 2010	95.84%		95.84%
90	Urgent Instalation of Street Lights in Tasi Tolu, Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Dom aleixo	Dili	Alefa Unip Lda	MOP-W-190133	$ 87,154.90	Aug. 15, 2019	72.00%		72.00%
91	Konstrusaun Lutu Hadulas WTP Central iha Bairo-Pite Dom Aleixo Municipio Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Dom aleixo	Dili	Iki Bia-Nunu Unip Lda	NCB/MOP/W-200015	$ 197,127.50	Oct. 7, 2019	74.81%		74.81%
92	Rehabilitation Recident & Carport of Vice PM (Bem Serviso)	MINISTERIO PLANU E ORDENAMENTU	LM-BS	EDIFICIOS PUBLICOS	Dom aleixo	Dili	D. Likibo Unip. Lda	05/RDTL/MPO/ADN/DA-Afq/X/2020	$ 49,078.24	Nov. 17, 2020	100.00%		100.00%
93	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Dom aleixo	Dili	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	$ 314,106.58	April 20, 2021	100.00%		100.00%
94	Revitalization of Community Aitarak Laran	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Dom aleixo	Dili	TPF Timor Unipessoal Lda	MPW-S-190272	$ 399,974.64	March 25, 2020	20.00%		20.00%
95	Servisu Manutensaun Edificio Agencia de Desenvolvimento Nasional	MINISTERIO PLANU E ORDENAMENTU	LM-BS	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	Giovanio	002.LM/RDTL/MPO/ADN,I.P/III/2021	$ 60,000.00	March 18, 2021	49.21%		49.21%
96	Instalasaun Agua Potavel iha Edificio Ministerio da Defesa no QG das F-FTL	MINISTERIO DEFESA	LM-CD	MANUTENSAUN NO REHABILITASAUN	Dom aleixo	Dili	CAPTAIN HOOK		$ 38,450.39	24-Apr-21	94.78%		94.78%
97	River Normalization , Roads Embankment and Road Clean Up of Comoro Mota Ulun-Casnafar, Air Terjun Sarlala Emergency Project, Resulted from the Calamity of rain-Induced Disaster on the 4th April 2021	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS	Dom aleixo	Dili	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS-210006	$ 148,256.87	28-May-21	100.00%		100.00%
98	Enhancement of Project - Management Information System (PMIS)	MINISTERIO PLANU E ORDENAMENTU	LM-BS	EQUIPAMENTO INFROMATICO	Dom aleixo	Dili	KINOS Unip,Lda	011/RDTL/MPO/ADN,I.P/V/202	$ 56,935.00	May 24, 2021	85.00%		85.00%
99	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS	Dom aleixo	Dili	Bintang Fajar, Lda	MPW-W-SS 210028	$ 88,970.39		100.00%		100.00%
100	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS	Dom aleixo	Dili	Monte Veado Unip Lda	MPW-W-SS 210008	$ 58,307.54		100.00%		100.00%
101	Rehabilitasaun Edificio Dormitoriu INS Comoro-Dili Timor Leste	MINISTERIO SAUDE	LM-CD	SAUDE	Dom aleixo	Dili	Grandis		$ 155,299.96	Aug. 4, 2021	82.55%	0.00%	82.55%
102	New Construction Lanscaping and Gazebo at Vice Prime Minister Official Recident	MINISTERIO PLANU E ORDENAMENTU	LM-BS	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Rubic Unip. Lda		$ 34,855.64		96.67%		96.67%
103	Extention of Sames Ware-House Building at Kampo Alor	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Unidade Unip Lda		$ 51,444.91		63.00%		63.00%
104	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Dom aleixo	Dili	Lizi Construction, Unipessoal Lda		$ 578,040.73		29.11%	16.67%	45.78%
105	Consulting services of spatial planing of Timor Leste	MINISTERIO PLANU E ORDENAMENTU	FI	DESENVOLVIMENTO URBANO E RURAL	Dom aleixo	Dili	Intersisment S.A in Joint Venture with Queternaire Portugal Consultoria para o Desenvolvimento. SA	SSS/041/MPO-2021	$ 781,121.90	May 13, 2021	30.00%		30.00%
106	New construction archive werehouse at bebora	MINISTERIO SAUDE	LM-BS	SAUDE	Dom aleixo	Dili	Hilobadi Unip,Lda	RDTL-MS-C19-DNA-NCB-21-011	$ 109,519.43	Aug. 31, 2021	43.34%		43.34%
107	Construsaun de Balcao de atendimento publica para a Direcsaun Geral dos servicos de registos e do Notariado do Ministerio da Justica	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	Dom aleixo	Dili	Fatuk Mota Construction Unipessoal. Lda	MJ-046/Junho 2021	$ 57,463.94	July 7, 2021	81.42%		81.42%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
108	Manutensaun de salao Nobre	MINISTERIO DO INTERIOR	LM-BS	EDIFICIOS PUBLICOS	Dom aleixo	Dili	DCO Unip.Lda	RDTL/19/MNEC/2021	$ 89,984.12	May 17, 2021	93.92%		93.92%
109	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	MTC	LM-CD	PORTOS	Dom aleixo	Dili	Holgapa Unip.Lda	RDTL - 2021 - MTC - CD - 031	$ 386,456.87		44.11%		44.11%
110	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	MINISTERIO DAS OBRAS PUBLICAS	Emergency	PONTES	Dom aleixo	Dili	Chegue Rau	NCB/040/MOP-2020	$ 24,919.25		100.00%		100.00%
111	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	MINISTERIO DAS OBRAS PUBLICAS	Emergency	PONTES	Dom aleixo	Dili	Holgapa Unip.Lda	RT/069/MOP-2021	$ 213,895.26		47.16%		47.16%
112	Konstrusaun ka Reabilitasaun ba ESG 10 de Dezembro Comoro - Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	DOM ALEIXO	Dili	MEJD PKRIE ESG 10 DE DEZEMBRO COMORO-DILI	KONTRATU COMUNITARIA	$ 108,265.95		0.00%		0.00%
113	Konstrusaun ka Reabilitasaun ba EBC 10 de Dezembro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	DOM ALEIXO	Dili	MEJD PKRIE EBC 10 DE DEZEMBRO	KONTRATU COMUNITARIA	$ 128,911.25		8.44%		8.44%
114	Konstrusaun ka Reabilitasaun ba EBC 30 de Agosto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	DOM ALEIXO	Dili	MEJD PKRIE EBC 30 DE AGOSTO	KONTRATU COMUNITARIA	$ 149,978.57		22.81%		22.81%
115	Konstrusaun ka Reabilitasaun ba EBF Naroman	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	DOM ALEIXO	Dili	MEJD PKRIE EBF NAROMAN	KONTRATU COMUNITARIA	$ 105,245.50		0.00%		0.00%
116	Konstrusaun ka Reabilitasaun ba EPE Buras Kadalak	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	DOM ALEIXO	Dili	MEJD PKRIE EPE BURAS KADALAK	KONTRATU COMUNITARIA	$ 80,571.32		13.04%		13.04%
117	Konstrusaun ka Reabilitasaun ba EBF Bebonuk	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	DOM ALEIXO	Dili	MEJD PKRIE EBF BEBONUK	KONTRATU COMUNITARIA	$ 88,127.23		3.05%		3.05%
118	Mudansa Lina Bazeia Rekomendasaun ADN	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Metinaro	Dili	Jofi	0000	$ 2,390.32	Jan. 1, 2016	0.00%		0.00%
119	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Metinaro	Dili	Nimia Unip Lda	RDTL:63/MSS/DNFALM-DAD/X/2015	$ 411,413.54	Oct. 29, 2015	100.00%		100.00%
120	Melhoramento taratamento dezalinasaun iha manleu Metinaro /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO	Metinaro	Dili	Garisiba Unip.Lda	MOP-W-190150	$ 87,856.59	May 11, 2019	87.07%	0.00%	87.07%
121	Construction of Kitchen and Refectory at Componete do Apoio de Serviso (CAS) iha Metinaro	MINISTERIO DA DEFESA	LM-BS	EDIFICIOS PUBLICOS	Metinaro	Dili	Betuhei	la mensiona nomor iha contratu	$ 581,897.61	Oct. 26, 2015	100.00%		100.00%
122	New Construction of WareHouse, Campas, Raodway, Drainage and Pavement at Jardim	MINISTERIO SOLIDARIEDADE SOCIAL E	LM-CD	SOLIDARIEDADE E SOCIAL	Metinaro	Dili	Pro Frawijaya	RDTL:44/MSS/DNFALM-DAD/X/2014	$ 449,600.23	Oct. 16, 2014	86.56%		86.56%
123	Konstrusaun Turismu Komunitariu One Dollar Beach	SEFOPE	LM-TP	PORTOS	Metinaro	Dili	Quindy Eujec Lda.	02/CNFP-B/VII/2019	$ 460,254.00	July 27, 2018	82.03%		82.03%
124	Detailed Engineering Design of New Fisherman Port, Suco Duyung, Metinaro	MINISTERIO AGRIKULTURA E PESCAS	FI	AGRICULTURA	Metinaro	Dili	Consulmar-Projetista e Consultore. Lda de Portugal em Empreendimento Conjunto com a Engipro de TLPty. Ltd		$ 273,270.70		70.00%		70.00%
125	New Construction of Roadways, Drainage and Parking Area no Jardim de Herois de Metinaro	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	ESTRADAS	Metinaro	Dili	Celijo Star	No: 214/MACLN/X/2021	$ 948,930.17	Oct. 20, 2021	24.78%	17.3%	42.13%
126	New Construction of Campas and Grass Planting Jardin dos Herois (JHM) Metinaro	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	TURISMO	Metinaro	Dili	LABILAY, Unipessoal, Lda	216/MACLN/X/2021	$ 397,296.90	Oct. 20, 2021	24.59%		24.59%
127	New Const of F-FDTL home base Fuel Filling Station in Metinaro, Dili Municipality	MINISTERIO DA DEFESA	LM-BS	EDIFICIOS PUBLICOS	Metinaro	Dili	Aitula Construction, Lda	ICB No 05/DNA/MD/2021	$ 809,906.27		0.00%	40.48%	40.48%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
128	Konstrusaun ka Reabilitasaun ba EBF Benunuk Metinaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Metinaro	Dili	MEJD PKRIE EBF BENUNUK METINARO	KONTRATU COMUNITARIA	77,383.99		8.60%		8.60%
129	Konstrusaun ka Reabilitasaun ba ESG 20 de Setembro Metinaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Metinaro	Dili	MEJD PKRIE ESG 20 DE SETEMBRO METINARO	KONTRATU COMUNITARIA	164,146.98		2.93%		2.93%
130	Rehabilitasaun kanu transmisaun husi Benamauk ba WTP Lahane no Becusse	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	Nain Feto	Dili	Lemo Timor Unipessoal Lda	SSS/019/MOP-2020	$ 139,971.80		0.00%		0.00%
131	Consulting Services for detailed Engineering Design of CAC Office Building	CAC	FI	EDIFICIOS PUBLICOS	nain feto	Dili	Imagem, Design and Arquitectura, Lda (IDA) in Association with Vaz, Dotti & Silva, Lda (VDS)	RFP/004/MPW-2013	$ 256,843.00	March 18, 2014	72.71%		72.71%
132	New Construction of Ojetil Office Building Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	EDIFICIOS PUBLICOS	nain feto	Dili	Fitun Diak Unip.Lda	SSS/301/MOPTC-2016	$ 1,753,481.10	Feb. 12, 2016	100.00%		100.00%
133	New Installation MV, LV Line and House Connection from Bidau to Catedral - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	nain feto	Dili	Anicla.Lda	TL/MOPTC-VMOPTC/CGI-PEN : 00000	$ 483,778.67	Sept. 1, 2016	81.60%		81.60%
134	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Nain Feto	Dili	Meteor Unip.Lda	SSS/200/MOPTC-2016	$ 4,032,231.86	Sept. 13, 2016	78.64%		78.64%
135	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Nain Feto	Dili	Suai Indah Unipessoal Lda	SSS/218/MOPTC-2016	$ 999,876.89	Sept. 13, 2016	55.23%		55.23%
136	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Nain Feto	Dili	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	$ 911,145.27	June 4, 2020	86.51%	12.47%	98.99%
137	Installation of Transmission Line, Distribuition Panel & Transformer in Taibesi and Becora	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Nain Feto	Dili	Nizixavane	MPWTC-W-015072	$ 312,775.56	Oct. 28, 2015	97.82%		97.82%
138	Construction of Membrane Tent and Shaded Area of SG-MOPTC	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Nain Feto	Dili	Voar	MPWTC-W-170020	$ 83,897.22	Jan. 9, 2017	91.14%		91.14%
139	Installation of Street Lights Lecidere - Acadiruhun-Acait (Lot 6)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Nain Feto	Dili	Alzes Ukat, Unip.Lda	MPW-W-190266	$ 46,507.85	Oct. 19, 2019	70.12%		70.12%
140	Rehabilitasaun no manutensaun ex edificio diresaun geral organizasaun urbana	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-BS	MANUTENSAUN NO REHABILITASAUN	Nain Feto	Dili	Riri Brothers Unip. Lda.	RDTL,0140/UAD-MAE/XII/2019	$ 26,426.13	Dec. 9, 2019	100.00%		100.00%
141	Rehabilitasaun Edificio Conselho de	CONSELHO DA EMPRENSA	LM-BS	EDIFICIOS PUBLICOS	Nain Feto	Dili	Algis	CI-19-06-C-013	$ 97,498.81	June 4, 2019	95.43%		95.43%
142	Manutensaun Expert Room iha MESCC	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA	LM-BS	MANUTENSAUN NO REHABILITASAUN	Nain Feto	Dili	Katuas Patricio	RFQ19/45-Q	$ 7,583.06	Sept. 16, 2019	97.00%		97.00%
143	Rehabilitation of Volley Ball Beach Facilities in Dili-Lecidere	SEJD	LM-CD	JUVENTUDE NO DESPORTU	Nain Feto	Dili	DVD Electric	NCB/01/SSYS-2019	$ 84,302.72	Oct. 29, 2019	94.93%		94.93%
144	Rehabilitation of GDD Sports Indoors	SEJD	LM-CD	JUVENTUDE NO DESPORTU	Nain Feto	Dili	Victoria Const. Unip. Lda	NCB/02/5595-2019	$ 412,595.61	Oct. 29, 2019	100.00%		100.00%
145	Rehabilitation and Maintenance of Jardim 12 de Novembro at Motael	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	MANUTENSAUN NO REHABILITASAUN	Nain Feto	Dili	Algis	RDTL:47/DNA-MTCI/VII/2019	$ 95,425.00	July 31, 2019	98.48%		98.48%
146	Rehabilitasaun Residencia Vice Presidente Parlamentu Nacional iha Farol	PARLAMENTU NASIONAL	LM-BS	MANUTENSAUN NO REHABILITASAUN	Nain Feto	Dili	Celijo Star	PN/4306/2016	$ 30,037.14	July 21, 2016	100.00%		100.00%
147	Rehabilitasaun Jardim 12 de Novembro iha Igreza Motael nia oin	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-BS	TURISMO	Nain Feto	Dili	Berlosconi	RDTL0144/UADE-MAE/XII/2019	$ 46,905.00	Aug. 15, 2019	90.46%		90.46%
148	Rehabilitation and Maintenance Building PCM	MINISTERIO DA PRESIDENCIA DO	LM-BS	MANUTENSAUN NO REHABILITASAUN	Nain Feto	Dili	Panca Sekawan	PCM-20/01-C/0014	$ 150,000.00	Jan. 15, 2020	100.00%		100.00%
149	Minor Rehabilitasaun of MTC main of Building and Correeios	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	LM-BS	EDIFICIOS PUBLICOS	Nain Feto	Dili	Risumali Unip Lda	RDTL2019-MTC-GS-0041	$ 8,889.74	Jan. 1, 2020	98.90%		98.90%
150	Rehabilitation of Confrence Room at the office of the Primer Minister, building I, Palacio do Governo,Dili Timor Leste	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	Nain Feto	Dili	Gez Unipessoal Lda	RDTL-294/GPM/XI/2019	$ 52,232.55	Nov. 29, 2019	100.00%		100.00%
151	RIVER PROTECTION PALACIO NOBRE	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	FLOOD CONTROL	Nain feto	Dili	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	$ 129,168.62		52.93%	7.3%	60.24%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
152	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	TRIBUNAL RECUSSO	Emergency	EDIFICIOS PUBLICOS	Nain Feto	Dili	Star King Unip. Lda	MPW-SS-210030	$ 122,960.04		100.00%		100.00%
153	Refurbishment of tenis court facilities, Dili	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	JUVENTUDE NO DESPORTU	Nain Feto	Dili	Algis	NCB/01/SSYS/2021	$ 97,389.44	Oct. 4, 2021	62.14%		62.14%
154	aditional for Hospital Dr.Antonio Carvalho I	MINISTERIO SAUDE	LM-BS	SAUDE	Nain Feto	Dili	Hedge Construction, Unip. Lda	RDTL-MS-C19-DNA-DC-21-072	$ 150,710.92	May 14, 2021	26.38%		26.38%
155	New Construction of outdoor sport facilities	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	JUVENTUDE NO DESPORTU	Nain Feto	Dili	UKA II UNIPESSOAL LDA	NCB/02/SSYS/2021	$ 204,254.98		0.00%		0.00%
156	Preparation of detailed engineering design (I	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Nain Feto	Dili	TPF Timor Unipessoal Lda	RT-CD-MOP-21002	$ 87,800.00		0.00%		0.00%
157	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Nain Feto	Dili	Sanford Const. Unip. Lda	MPW-W-210168	$ 284,325.06		22.58%	77.42%	100.00%
158	New Construction of outdoor sport facilities in Taibessi	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	JUVENTUDE NO DESI	Nain Feto	Dili	UKA II UNIPESSOAL LDA	NCB/02/SSYS/2021	$ 204,254.98		0.00%		0.00%
159	Konstrusaun ka Reabilitasaun ba EBF Duque de Caxias	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Nain Feto	Dili	MEJD PKRIE EBF DUGUE DE CAXIAS	KONTRATU COMUNITARIA	$ 80,723.84		0.00%		0.00%
160	Konstrusaun ka Reabilitasaun ba EBC Bidau Akadiru-Hun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Nain Feto	Dili	MEJD PKRIE EBC BIDAU AKADIRU HUN	KONTRATU COMUNITARIA	$ 93,171.12		11.92%		11.92%
161	Konstrusaun ka Reabilitasaun ba EBF Lelaus Dare	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Nain Feto	Dili	MEJD PKRIE EBF LELAUS DARE	KONTRATU COMUNITARIA	$ 77,821.06		0.00%	9.35%	9.35%
162	Rehabilitasaun Eis Hospital Dr.Antonio de Carvalho	MINISTERIO SAUDE	LM-Covid 19	SAUDE	Nain Feto	Dili	Daloveya Unip.Lda	RDTL-MS-C19-DNA-DC-22-019	$ 739,937.34		0.00%		0.00%
163	Construction Of New Office Of Tribunal Distrital De Dili	TRIBUNAL RECUSSO	FI	EDIFICIOS PUBLICOS	vera cruz	Dili	China Shandong International Economic And Technical Cooperation Group. LTD	ICB/008/TR-2019	$ 10,990,769.35	May 12, 2019	25.46%		25.46%
164	Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building	TRIBUNAL RECUSSO	FI	EDIFICIOS PUBLICOS	vera cruz	Dili	Dacrea Desing and Engineering Consultant (Dacrea) (Indonesia) In Association with Archtimor Engineering Consultants (AEC) as Sub-consultant (Timor-Leste)	RFP/012/TR-2019	$ 567,197.00	Dec. 16, 2019	64.95%	0.00%	64.95%
165	Installation of New MV Line in Rotunda Mercado Lama, Culuhun, Ailele Hun, and Lecidere	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	vera cruz	Dili	Ferajota	SSS/072/MOPTC-2015	$ 385,588.18	Dec. 14, 2015	61.92%		61.92%
166	Rehabilitation MV,Line , LV Line and distribution Trasformer from Casa Europa to Pantai Pasir Putih - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	vera cruz	Dili	Inaziju	RDTL/MOP-SEE/CGI-PEN : 0000267	$ 119,600.79	Oct. 2, 2013	100.00%		100.00%
167	Construção Quartel General PNTL em Caicoli	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	vera cruz	Dili	Shangai Construction Group Co.,Ltd	ICB/036/MI-2017	$ 10,177,638.20	Oct. 22, 2019	1.78%		1.78%
168	Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA	vera cruz	Dili	PT. Ceriajasa Cipta Mandiri in Joint Venture with JKC Consultant Engineering Unipessoal Lda	RPF/087/MI-2017	$ 594,360.00	Nov. 22, 2019	10.00%	0.00%	10.00%
169	Consulting Services for Detail Engineering Design of the IGE Office, Workshop and Warehouse Complex Building	MINISTERIO DAS OBRAS PUBLICAS	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	vera cruz	Dili	Scope Australia Pty, Ltd	RFP/039/MPW-2013	$ 295,000.00	March 26, 2014	95.00%		95.00%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
170	Consulting Services for Detailed Architecture and Engineering Design for Press Building Project	SECRETARIADO ESTADO KOMUNIKASAUN	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	vera cruz	Dili	CGM Consultants & Associates Incorporated, Lda.	SSS/051/SECOM-2015	$ 200,000.00	Feb. 25, 2015	40.00%		40.00%
171	Consulting Services for Feasibility Study of the New Buildings for RTTL. P.E and Tatoli P.I.	SECRETARIADO ESTADO KOMUNIKASAUN	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	vera cruz	Dili	Potevio Company Limited	RDTL	$ 212,212.00	Sept. 27, 2020	100.00%		100.00%
172	Additional Drainage Colmera	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	vera cruz	Dili	Hailala Unip.Lda	166139	$ 7,049.68	Aug. 22, 2013	100.00%		100.00%
173	Consulting Services of Detailed Engineering Design of Sport Complex and Building at	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	vera cruz	Dili	ATT consultants Co. Ltd JV SQ Architect and Planner Co. Ltd	RFQ/314/SEJD-2016	$ 285,700.00	May 8, 2017	70.00%		70.00%
174	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	vera cruz	Dili	Bia Mapel	MPW-W190099	$ 44,559.88	Sept. 23, 2019	100.00%		100.00%
175	Rehabilitation of Security Post Building in Caicoli MPW	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Reza	RDTL MPW-014067	$ 28,927.73	Jan. 10, 2014	76.91%		76.91%
176	Prefurasaun Be'e mos iha Area Tuana Laran - Matadouro Suku Vila verde, Postu Administrativo Vera Cruz - Municipiu Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	vera cruz	Dili	Liberta	MPWTC-W-700774	$ 158,815.15	Aug. 16, 2017	100.00%		100.00%
177	Manutensaun ba Edifisio DNGRA-MOP / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	EDIFICIOS PUBLICOS	vera cruz	Dili	Katuas Patricio	RFQ-MOP-190071	$ 8,098.49	May 11, 2019	99.31%		99.31%
178	Rehabilitation of DNA MOP Cobe House in Caicoli Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Surik Saki Rai Unip.Lda	MOP-W-190167	$ 48,635.85	Dec. 1, 2019	97.00%		97.00%
179	Construction of extension office building of the Minister of Public works (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	EDIFICIOS PUBLICOS	vera cruz	Dili	CELFA Unip.Lda	RDTL-NCB-MOP-190088	$ 156,400.69	Dec. 1, 2019	100.00%		100.00%
180	Detailed Engineering design of E-Recruitment Building CFP	CFP	LM-BS	EDIFICIOS PUBLICOS	vera cruz	Dili	De Oliveira design	SSS/045/MT-2017	$ 35,500.00	Oct. 2, 2019	95.00%		95.00%
181	New Construction of Auditorium (Salaun Paroquial) & Class Room & landscape of Catedral. Vila Verde	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	vera cruz	Dili	Bimavi	transferencia publica	$ 825,142.43	March 27, 2015	94.30%		94.30%
182	Construção Pure Hindu Taibesi	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS	vera cruz	Dili	Pantarhei	Transferencia Publica	$ 1,207,958.18	Aug. 25, 2017	74.77%		74.77%
183	New Construction of Administration and Logistic Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Aitula Construction, Lda	059/C/UNTL/XI/2019	$ 678,218.04	Nov. 26, 2019	89.97%	8.76%	98.73%
184	New Construction of Faculidade Econimia e Gesatao Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Aitula Construction, Lda	057/C/UNTL/X/2019	$ 672,666.11	Oct. 29, 2019	95.62%		95.62%
185	New Building Construction of Medicina Ciencia da Saude Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Linier jv Algis	058/C/UNTL/X/2019	$ 678,572.97	Sept. 6, 2019	98.60%		98.60%
186	Konstrusaun Edifisio servisu espesializada iha PGR Colmera	PROCURADORIA GERAL DA REPUBLIKA	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Bobolait	RDTL-D.FEO/APRO/PGR/19.002/2019	$ 551,668.03	Oct. 17, 2019	100.00%		100.00%
187	Rehabilitation of Houses RTTL in Caicoli and Biterlau	RADIO TELEVISAUN TIMOR LESTE	LM-BS	MANUTENSAUN NO REHABILITASAUN	vera cruz	Dili	Gaerenez	10/RDTL,E.P/DAF/VI/2019	$ 37,605.25	June 7, 2019	100.00%		100.00%
188	Konstrusaun Edifisiu Foun ba Diresaun Aprovizionamentu Finansas e Fiskalizasaun	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	PDIM	EDIFICIOS PUBLICOS	vera cruz	Dili	Chipys Unip. Lda	07KDM/AM-DIL/X/2019	$ 143,579.83	Oct. 8, 2019	93.02%		93.02%
189	Maintenance of Building for Trade Invest Timor Leste	TRADE INVEST	LM-BS	MANUTENSAUN NO REHABILITASAUN	vera cruz	Dili	D'CO	RDTL/TITL/C.06/10/2019	$ 37,582.90	Sept. 1, 2019	55.88%		55.88%
190	Rehabilitasaun Hospital Dr.Antonio Carvalho Lahane(Building A) Hodi halo Fatin Izolamentu ba Pasienti Covid-19	MINISTERIO SAUDE	LM-Covid 19	MANUTENSAUN NO REHABILITASAUN	vera cruz	Dili	Hedge Construction, Unip. Lda	NCB/M.S./DNA/DC-20/143	$ 450,153.32	May 25, 2020	86.99%		86.99%
191	Desenho e Espicificacao de Quantidades BoQ para a ampliacao do Balcao de Atendimento na DNRN	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Viros Consultant Unip Lda	RDTL-MJNo.009/MAIO/2019	$ 9,000.00	Jan. 6, 2019	100.00%		100.00%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
192	Rehabilitasaun e Manutensaun Edifisio Armajen DNSA, Dili (Bem Serviso) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	EDIFICIOS PUBLICOS	vera cruz	Dili	B'Two Unip Lda	MOP/W-190186	$ 26,539.42	Dec. 31, 2019	69.53%		69.53%
193	Detailed Engineering Design Hospital Dr. Antonio Carvalho LOT"A" Lahane Oriental	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	vera cruz	Dili	Victoria Cosnt.	FBS-DNA-MOP-19016	$ 375,986.35	March 31, 2020	10.00%		10.00%
194	Improvement of Mina Distribuition Pipe in DMA 31 in Suco Mascarenhas	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	vera cruz	Dili	Amigo Unip. Lda	No : /NCB/MPW/W-200016	$ 51,111.18	Oct. 1, 2019	69.16%		69.16%
195	New Construction of isolation (OPD) Vera cruz relation of covid 19	MINISTERIO SAUDE	LM-Covid 19	EDIFICIOS PUBLICOS	vera cruz	Dili	Romante Pty. Ltd	RDTL-MS-C19-DNA-SS-21-001	$ 265,808.11		87.48%	0.00%	87.48%
196	New construction Warehouse for centro Nacional Chega I.P	Centro Nacional Chega	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	A. L. Unip.Lda	26/CNC/IX/2021	$ 63,878.59	Sept. 3, 2021	98.72%		98.72%
197	Renovation of public Health services at lahane , posto vera cruz Timor Leste	MINISTERIO SAUDE	LM-BS	SAUDE	vera cruz	Dili	Queson SQ Unipessoal Lda	RDTL-MS-DNA-ICB-20-255	$ 282,726.57	Feb. 9, 2021	31.75%		31.75%
198	New Construction Drinage centro Nasional Chega.I.P	Centro Nacional Chega	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Chacailala Unipessoal Lda	27/CNC/IX/2021	$ 70,792.37	Sept. 6, 2021	56.75%	0.00%	56.75%
199	Criacao de estrutura de parede divisorias do ministerio da justica	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	atuk Mota Construction Unipessoal. Lc	MJ-047/junho/2021	$ 61,314.55	July 7, 2021	78.80%		78.80%
200	Extention Office of Legal and Judicial Training Centre	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	HALE ENTERPRICE UNIPESSOAL,I	MJ-066/Novembro/2021	$ 232,916.02		0.00%		0.00%
201	Construction of Faculdade de Agricultura Building (B-01)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Dany stra	RDTL 039/C/UNTL/XII/2021	$ 655,394.42		0.00%		0.00%
202	Construction of Faculdade de Agricultura Building (B-02)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Hedge Construction, Unip. Lda	RDTL 041/C/UNTL/XII/2021	$ 605,337.84		0.00%		0.00%
203	Construction of Faculdade de Agricultura Building (B-03)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Bobolait		$ 630,619.64		0.00%		0.00%
204	Design Edificio MACLN	MINISTRO PARA OS ASSUNT	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Uma de Contrucão Unipessoal Lda	38/MACLN/IX/2021	$ 88,510.00		0.00%	30.00%	30.00%
205	Construction of Faculdade de Agricultura Building (B-01)	UNIVERCIDADE NACIONAL	LM-CD	EDUKASAUN	vera cruz	Dili	Dany Stra Unipessoal Lda	RDTL 039/C/UNTL/XII/2021	$ 655,394.42		0.00%		0.00%
206	New Construction of Faculdade de Agricultura (B-02)	UNIVERCIDADE NACIONAL	LM-CD	EDUKASAUN	vera cruz	Dili	Bobolait Lda	RDTL 041/C/UNTL/XII/2021	$ 630,619.64		0.00%		0.00%
207	New Construction of Faculdade de Agricultura (B-03)	UNIVERCIDADE NACIONAL	LM-CD	EDUKASAUN	vera cruz	Dili	Hedge Construction, Unip. Lda	RDTL040/C/UNTL/XII/2021	$ 605,337.84		0.00%		0.00%
208	Extention Office of Legal and Judicial Training Centre	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	BEHALE ENTERPRICE UNIPESSOAL,LDA	MJ-066/Novembro/2021	$ 232,916.02		0.00%		0.00%
209	Konstrusaun Koby House foun ba Unidade Aprovisionamento Desentralizadu UAD	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-CD	EDIFICIOS PUBLICOS	vera cruz	Dili	Linier Unipessoal Lda	RFQ/088/MAE-2021	$ 78,817.38		0.00%		0.00%
210	Restante Cabo Subteranno Centro Produsaun SAKATO reutiliza ba Hotel Ambeno Programa ZEEMS nian iha Oecusse	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Oe-cusse	Oe-cusse	Lifau Indah	0000	$ 194,924.39	Jan. 1, 2016	0.00%		0.00%
211	Installation New MV Line , Transformer & Extend LV Line and New Distribution Line from Nitib Tuan Oel Tam to nitib Tuan Oecusse District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Oe-cusse	Oe-cusse	Manekat Unip. Lda	RDTL/MOP-SEE/CGI-PEN:0000256	$ 320,740.08	Aug. 15, 2014	98.44%		98.44%
212	New Installation of Under Ground Cable MV Line From Malelat To Pasabe- Oecusse Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Oe-cusse	Oe-cusse	Maubere Spirit	DTL/MOPTC-VOMPTC/CGI-PEN:00004	$ 177,484.78	March 13, 2017	46.49%		46.49%
213	Construção Posto Militar F-FDTL Pante Makasar	MINISTERIO DA DEFESA	FI	SEGURANCA NO DEFESA	Oe-cusse	Oe-cusse	Erver Unip.Lda	NCB/004/MDS-2015	$ 1,660,172.40	Feb. 8, 2015	100.00%		100.00%
214	Detailed Engineering Design (DED) of Dili Water Supply	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	nasional	Dili	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOP-2019	$ 2,718,150.00	Jan. 30, 2020	40.15%		40.15%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
215	Detailed Engineering Design (DED) of Dili Sanitation and Drainage Master Plan-Phase II	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	nasional		ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	SSS/035/MOPTC-2017	$ 1,057,882.00	Sept. 17, 2017	85.00%		85.00%
216	Feasibility Study of Surface Water Resource Development for the Water Supply of Dili Metropolitan Area	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	nasional	Dili	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/002/MOP-2019	$ 459,600.00	Aug. 22, 2019	50.00%		50.00%
217	Pre- Feasibility Study of a Ground Water Resources Development Project for the Water Supply of Dili Metropolitan Area	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	nasional	Dili	TEAM Consulting Engineering and Management PCL, Thailand in JV with ATT Consultants Company limited, Thailand and in association with CQ2 Engineering Consultancy & Diverso Unipessoal Lda, Timor-Leste	RFP/001/MOP-2019	$ 341,500.00	July 10, 2019	65.00%		65.00%
218	Rehabilitasaun Sistema Be,e Mos Iha lahane Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	nasional	Dili	Sicola	SSS/018/MOP-2021	$ 76,750.31	June 12, 2020	73.26%		73.26%
219	Financial Advisory Services Agreement between the Government of Timor - Leste and International Finance Corporation on Development of Presidente Nicolau Lobato Internasional Airport - Airport PPP Project	MINISTERIO FINANCAS	FI	AEROPORTOS	nasional	Dili	International Finance Corporation	604869	$ 1,100,000.00	Feb. 24, 2020	54.55%		54.55%
220	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	nasional	Dili	Sinohidro corporation limited	ICB/07/MPW-2014	$ 48,314,975.87	March 3, 2016	82.44%		82.44%
221	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Nasional	Dili	Lonacca Unipessoal Lda	MPW-W-190177	$ 116,902.51	Nov. 13, 2019	100.00%		100.00%
222	For Preparation of Detailled Engineering and Bid Preparations for New Bridges in 2019 Package I Samalari, Sana Uatolari-Laisorulai, Sumaco (Lacluta Uma Tolu), Malos Matadoro-RTK, Comoro Motaulun	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	nasional	Dili	Vox Da Vinci Consultant Engineering Lda	RDTL	$ 579,908.00	March 25, 2020	70.00%		70.00%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
223	Consulting Services for preparing of design the intersection in the existing Dili Liquixa Road to connect access Road From Tibar Bay Port (Preparasaun Desenho detalhado ba Estrada, Electricidade e Aguas ba Funcionamentu Portu Tibar)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	nasional	Dili	TPF Consultores de Engenharia S.A (Portugal) JV with TPF Timor Unip Lda, (Timor-Leste)	RFP/009/MOP-2019	$ 244,775.00	Nov. 30, 2019	100.00%		100.00%
224	Selection of Design Consultant to Prepare Preliminary Design and Tender Documents for the Upgradition of Liquica 150 KV/20KV Substation to Supply Power to Tibar Bay Port	MINISTERIO DAS OBRAS PUBLICAS	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	nasional	Dili	PT. Malmass Mitra Teknik (Indonesia)	RFP/041/MOP-2019	$ 322,800.00	March 2, 2020	90.00%		90.00%
225	Zebra Cross Marking in The Capital City of Dili (162)	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-BS	ESTRADAS	Nasional	Dili	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	$ 68,526.00	Oct. 8, 2019	75.59%		75.59%
226	Additional Service Statement of Work for Year 2021 - Government Resource Planning Solutions & Supporting IT Infrastructure System Implementation & Support Agreement	MINISTERIO FINANCAS	FI	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS	Nasional	Dili	Freebalance	RDTL-167250	$ 3,106,435.00	July 5, 2010	76.06%		76.06%
227	Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	nasional	Nacional	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	RFP/039/MOP-2019	$ 2,903,356.59	Jan. 16, 2020	53.44%		53.44%
228	Estudos e plano de concepção para Planeamento Urbano a nível nacional	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	FI	DESENVOLVIMENTO URBANO E RURAL	Nasional	Nacional	Intersisment S.A in Joint Venture with Queternaire Portugal Consultoria para o Desenvolvimento. SA	RFP/025/MPW-2013	$ 1,219,755.75	Sept. 12, 2014	70.00%		70.00%
229	Plano Lidar e Mapeamento a todo o territorio, segunda fase	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	FI	DESENVOLVIMENTO URBANO E RURAL	Nasional	Nacional	PT. Karvak Nusa Geomatika, Indonesia	SSS/006/MPIE-2016	$ 22,631,012.85	Aug. 23, 2016	73.25%		73.25%
230	Supply, Installation, Configuration and Comissioning of National Optical Fiber Backbone Network	GABINETE DO PRIMEIRO MINISTRO	FI	EQUIPAMENTO INFROMATICO	Nasional	Nacional	Timor Telecom S.A.	RT/024/GPM-2017	$ 1,877,556.74	Nov. 15, 2017	94.59%		94.59%
231	Supply, Installation, Configuration and Comissioning of Hardware and Software for the Expantion of Data Center Infrastructure | Office of Prime Minister	GABINETE DO PRIMEIRO MINISTRO	FI	EQUIPAMENTO INFROMATICO	Nasional	Nacional	Joint Venture of CMC System Integration Company Limmited and Viettel Timor-Leste Unipessoal, LDA	ICB/025/GPM-2017	$ 1,485,698.00	Feb. 15, 2018	88.70%		88.70%
232	Road Network Upgrading Project (RNUP),Upgrading and Maintenance of Dili (Airport Junction)- Tibar Road- Section 2 : Tasitolu - Tibar	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA-IMPRESTIMO	Nasional	Nacional	CINA WU YI CO.LTD	ICB/032/MPWTC-2015	$ 12,964,487.49	Sept. 14, 2016	92.80%		92.80%
233	Operation And Maintenance Services For National Power Grid Project	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Nasional	Nacional	China Nuclear Industry 22ND Construction Co; LTD	La mensiona iha Kontracto	$ 46,872,339.00	July 15, 2016	66.63%		66.63%
234	Revitalization foot Ball Stadium and tribune Building	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Nasional	Dili	Marino enterprises Lda		$ 1,938,481.77	Dec. 31, 2017	53.05%		53.05%
235	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nasional	Dili	Shangai Construction Group Co.,Ltd		$ 59,287,453.57	Aug. 18, 2016	84.82%		84.82%
236	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nasional	Dili	CBMI Construction Co. Lda Jv Chongqing Roads Engineering		$ 29,315,346.10	Dec. 11, 2016	65.93%		65.93%
237	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nasional	Dili	CBMI Construction Co. Lda Jv Chongqing Roads Engineering		$ 20,748,566.21	Nov. 21, 2016	70.44%		70.44%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
238	Consultant Supervision Road network Upgrading Sector Project, Upgrading and maintenance of Maubara - Karimbala and Atabae - Mota Ain Roads, and Baucau - Lautem	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nasional	Dili	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		$ 7,693,101.00	May 3, 2017	64.01%		64.01%
239	Preparation of Detailed engineering design for Dili Urban Road	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Nasional	Dili	IAT unip.JV PT Purnajasa Bimapratama		$ 276,634.00		0.00%	10 %	1 0.00%
240	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nasional	Dili	China Railway Int. Group co, jv with China oversees		$ 23,853,175.70	March 21, 2019	12.73%		12.73%
241	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nasional	Dili	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)		$ 5,262,302.00	April 3, 2019	27.38%		27.38%
242	Manutensaun ba Edifício no Equipamentu laboratorium dianostika veternaria	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	Nasional	Nacional	Dreams Come True, Lda	RDTL-PO:2019-15736	$ 69,978.38	Sept. 11, 2019	97.14%		97.14%

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNICIPIO DILI

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Abril 2022		
											Progresso atual fulan ida nee	Montante actual fulan ida nee	% actual fulan ida nee
243	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Regional	Regional	Raya Consulting Lda	MPW-CS-2000020	$ 373,666.00	March 25, 2020	70.00%		70.00%
244	Consultant Design (M-L & L-N) & Supervision (D-L & T-G, Tasi Tolu -tibar 4 L)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA-IMPRESTIMO	Regional	Regional	KATAHIRA & ENGINEERS INTERNATIONAL	time base	$ 8,178,886.44	Dec. 14, 2012	81.13%		81.13%
245	The Integrated and Maintenance Service	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL	Regional	Regional	wartsila Indonesia R.P (Interest Late Payment P.T Warstila Indonesia (RP)	SSS-008-MOPTC-2016	$ 53,025,601.00	March 5, 2017	70.88%		70.88%

Inspected by :

Eng. Joao do Rego, Eng Eduardo do Santos
Enginheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Dili A D N IP

Inspected by :

Eng Pedro de Lurdes Alves, Eng Manuel Estrela, Eng Julmira Sampaio, Eng Egidio Goncalves, Rosalia de Fatima
Enginheiro Edificio Public, Agua e Saneamento Municipio Dili A D N IP

Inspected by :

Eng Camilio de Jesus
Enjineiru M& E , A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos
Enginheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Verified by :

Arch. Francisco Xavier de D Jeronimo
Enginheiro Senior ba Edificio Public no Agua e Saneamento A D N IP

Verified by :

Eng Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao qualidade ADN.I.P

MINISTERIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO A

LISTA GERAL PROJECTO MUNICIPIO DILI,NASIONAL,REGIONAL NO RAEOA

NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	SUCO	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHA	NUMERO KONTRATU	MONTANTE KONTI	DATA KONTRATU	PROGRESU FISIKU (%)	PROGRESU PAGAMENTU (%)	PAGAMENTU ($)	BALANSU ($)	OBSERVASAUN
1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN		Atauro	Dili	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	$ 297,409.09	Dec. 20, 2019	19.61%	17.65%	$ 52,499.32	$ 244,909.77	on going
2	New Construction of Laboratory for Covid-19 in Atauro	MINISTERIO SAUDE	Fundo covid-19	EDIFICIOS PUBLICOS		Atauro	Dili	Fitun Galilea Unipessoal Lda	No: /NCB/M.S/DNA/RBK-20-160	$ 69,859.04	Sept. 30, 2020	96.09%	95.91%	67,004.26	$ 2,854.78	FHO
3	New Construction of Isolation for Covid-19 in Atauro	MINISTERIO SAUDE	Fundo covid-19	EDIFICIOS PUBLICOS		Atauro	Dili	Lygelina Alexix Unip. Lda	No: /NCB/M.S/DNA/DC-20-161	$ 303,141.46	Oct. 9, 2020	75.12%	51.97%	$ 157,553.20	$ 145,588.26	on going
4	konstrusaun residensia oficial posto administrativo ataura	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-BS	EDIFICIOS PUBLICOS		Atauro	Dili	Realidade Salmes Unip,Lda		$ 56,359.98		0.00%	0.00%	$ -	$ 56,359.98	on going
5	Konstrusaun ka Reabilitasaun ba EBC Biqueli	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		Atauro	Dili	MEJD PKRIE EBC BIQUELI	0	$ 99,817.07		0.00%				
6	Rehabilitasaun intake no kanu transmisaun iha La Koto & Mutu Dare	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Becora	Cristo Rei	Dili	Amigo Unip. Lda	SSS/021/MOP-2020	$ 51,111.18	June 12, 2020	86.86%	85.28%	43,587.46	$ 7,523.72	on going
7	New Installation Street Light at Cristo Rei - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Cristo Rei	Dili	Silkar International Unip. Lda	RDTL/MOP-SEE/CGI-PEN:0000246	$ 45,715.42	Oct. 2, 2013	100.00%	90.00%	$ 41,143.88	$ 4,571.54	abandon
8	New Installation of MV, LV Line and House Connection from FeederII Becora to Taibesi, Bemori and Balide - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Becora	Cristo Rei	Dili	Ceuilaju.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000444	$ 724,286.69	Sept. 1, 2016	86.66%	77.52%	$ 561,491.70	$ 162,794.99	on going
9	New Installation of MV, LV Line and House Connection from Balide to Delta 3, Fomento, Manleuana, Bualaran, Aldeia Moris Dame, Eskola Fatumeta, Cacaulido, Ailok Laran, Bua Laran and Lisbutak - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Ailok	Cristo Rei	Dili	Derren Construction Unip.Lda.	RDTL/MOPTC-VMOPTC/CGI-PEN : 0000304	$ 1,292,209.31	Sept. 1, 2016	86.00%	77.47%	$ 1,001,051.17	$ 291,158.14	on going
10	New Installation of MV, LV Line and House Connection from Biterlaun Fatu Ahi to Lenuk Hun Cristo Rei - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Ahi	Cristo Rei	Dili	Jmindo	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000442	$ 262,372.99	Sept. 1, 2016	96.27%	86.64%	$ 227,331.39	$ 35,041.60	on going
11	New Installation of MV, LV Line and House Connection from Hera Ailok Laran to Sokaer Laran - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Hera	Cristo Rei	Dili	Vinario Unip.,Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000443	$ 323,645.08	Sept. 10, 2016	96.27%	86.64%	$ 280,403.23	$ 43,241.85	on going
12	New-Construction of ICCU at Hospital Nacional Guido Valadares, Dili Municipality	MINISTERIO SAUDE	FI	SAUDE	ICCU	Cristo Rei	Dili	SIKUNDI, Unipessoal, Lda	SSS/281/MOH-2016	$ 243,636.40	Sept. 14, 2017	32.19%	29.62%	$ 72,169.21	$ 171,467.19	abandon
13	Consulting Services for Detail Engineering Design (DED) for Pediatric and ICCU Building in Guido Valadares National Hospital	MINISTERIO SAUDE	FI	SAUDE	and	Cristo Rei	Dili	Philcoei International, Inc. In JV with Luis and Associates, Co	SSS/035/MOPTC-2017	$ 230,000.00	May 5, 2014	95.00%	95.00%	$ 218,500.00	$ 11,500.00	PHO
14	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Cristo Rei	Dili	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	$ 862,117.01	Aug. 25, 2017	99.62%	89.65%	772,928.36	$ 89,188.65	FHO
15	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	culu hun	Cristo Rei	Dili	Aspalink Unip Lda	SSS/131/MOPTC-2017	$ 1,942,664.52	Sept. 7, 2017	89.36%	80.43%	$ 1,562,395.65	$ 380,268.87	on going
16	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	at	Cristo Rei	Dili	Star King Unip. Lda	SSS/012/MOP-2020	$ 396,875.59	June 4, 2020	100.00%	88.00%	$ 349,250.52	$ 47,625.07	PHO
17	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN		Cristo Rei	Dili	Nimia Unip Lda	RT/154/MOPTC-2016	$ 84,143.33	April 21, 2017	90.00%	47.52%	$ 39,987.73	$ 44,155.60	abandon
18	Rehabilitasaun Tanke Reservatoriu iha Asgor no Bidau Masaur/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Cristo Rei	Dili	Selhar	RFQ-MOP-190047	$ 94,675.28	Oct. 22, 2019	51.65%	46.49%	$ 44,011.90	$ 50,663.38	on going
19	Konstrusaun Moru Hadulas Bomba Bidau /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Cristo Rei	Dili	SARCADEFAT Unip.Lda	MOP-W-190164	$ 93,376.42	Oct. 22, 2019	100.00%	43.84%	$ 40,935.29	$ 52,441.13	on going
20	Konstrusaun Moru Hadulas Bomba fomentu /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Cristo Rei	Dili	H FOUN Unip.Lda	MOP-W-190189	$ 39,586.42	May 11, 2019	100.00%	6.80%	$ 2,689.90	$ 36,896.52	on going
21	Lot 1 Urgent Installation of Street Lights in Mota Ulun-Bedois-Benamauk,Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Cristo Rei	Dili	Sirlacoli Unip. Lda	MPW-W-200032	$ 39,780.30	Dec. 19, 2019	75.91%	68.32%	$ 27,176.29	$ 12,604.01	on going
22	Installation of Street Lights Prizaun Becora-Culuhun California (Lot 2)/162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ELETRIFIKASAUN NASIONAL		Cristo Rei	Dili	Oulale unip.Lda	MPW-W-190261	$ 46,948.00	Oct. 19, 2019	93.48%	84.13%	$ 39,496.39	$ 7,451.61	on going
23	Konstrusaun Igreza Sagrada Corasaun de Jesus Becora	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		Cristo Rei	Dili	Carya Timor Leste Lda	Transferencia Publica	$ 2,068,587.24	Sept. 15, 2015	100.00%	86.48%	$ 1,788,934.93	$ 279,652.31	PHO
24	Rehabilitasaun & Extensaun Laboratorio Nacional Bidau - Dili	HOSPITAL NACIONAL GUIDO VALADARES	LM-BS	MANUTENSAUN NO REHABILITASAUN		Cristo Rei	Dili	Talamori	RDTL-MS-LNS-RFQ-17-064	$ 63,076.61	Dec. 6, 2017	91.23%	82.11%	$ 51,792.75	$ 11,283.86	on going

25	Escola Secundaria Tekniko Vocasional 28 de Novembru iha Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	MANUTENSAUN NO REHABILITASAUN		Cristo Rei	Dili	Dirbajudi	RDTL RCB/01-R/ME-DNA/REHAB	$ 410,299.91	Oct. 27, 2016	65.56%	59.00%	$ 242,093.36	$ 168,206.55	abandon
26	Rehabilitasaun Konstrusaun ESTV 28 Novembro - Dili (Rf)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN		Cristo Rei	Dili	Biqueli Pala Unip. Lda	08KDM/AM-DIL/XI/2019	$ 329,247.37	Nov. 6, 2019	98.60%	98.60%	324,629.33	$ 4,618.04	FHO
27	Rehabilitasaun ESTV Comercio E Economia	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	EDUKASAUN		Cristo Rei	Dili	Fitun Roman Pohnar Unip. Lda	06/KDM/AM-DIL/X/2019	$ 241,963.54	Oct. 8, 2019	93.82%	84.44%	$ 204,308.47	$ 37,655.07	PHO
28	RM Pecas Sofremento pagamento Bee Mos	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO		Cristo Rei	Dili	Flocinob Motis Unip Lda	MOP/W-190185	$ 39,572.89	Dec. 31, 2019	100.00%	23.97%	$ 9,486.72	$ 30,086.17	on going
29	Rehabilitation of Medicine Laboratorium in Lahane	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	SAUDE		Cristo Rei	Dili	Nevan Construction Unip Lda	012/UNTL/EXT/C/2016	$ 201,615.23	Sept. 28, 2015	91.68%	82.51%	$ 166,352.39	$ 35,262.84	PHO
30	Lot 1 Urgent Installation of Street Lights in Cristo Rei,Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Cristo Rei	Dili	Hanaria Electrial Unip.Lda	MOP-W-190136	$ 96,161.99	Aug. 15, 2019	72.97%	65.67%	$ 63,150.09	$ 33,011.90	on going
31	Urgent Installation of Street Lights in Cristo Rei, Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Cristo Rei	Dili	9 Brothers Unip Lda	MOP-W-190134	$ 90,572.75	Aug. 15, 2020	60.75%	54.67%	$ 49,518.47	$ 41,054.28	on going
32	Consultancy to develop A feasibility study and master plan Guido Valadares National Hospital (Bem Serviso)	MINISTERIO SAUDE	LM-BS	EDIFICIOS PUBLICOS		Cristo Rei	Dili	Mafra Consultante Unipessoal Lda	FBS-DNA-MOP-T9018-B	$ 341,781.00	March 25, 2020	70.00%	70.00%	239,246.70	$ 102,534.30	on going
33	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS		Cristo Rei	Dili	Titisa Louro Unip.Lda	MPW-W-210067	$ 173,960.80	June 15, 2021	90.82%	28.70%	$ 49,933.32	$ 124,027.48	on going
34	New Construction of Gabions Tower No.6 section Hera	MINISTERIO DAS OBRAS PUBLICAS	FI	FLOOD CONTROL		Cristo Rei	Dili	Jova Construction	NCB/034/MOP-2020	$ 232,158.43	5-Jul-21	100.00%	89.96%	208,850.52	$ 23,307.91	PHO
35	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY.	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	FLOOD CONTROL		Cristo Rei	Dili	KEFI OEL Unip.Lda		$ 298,820.39		75.09%	65.87%	$ 196,826.43	$ 101,993.96	on going
36	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Habibie	Cristo Rei	Dili	Carya Timor Leste Lda	SSS/009/MOP-2020	$ 477,527.99	June 4, 2020	100.00%	88.00%	$ 420,224.63	$ 57,303.36	PHO
37	For Clean Up of Metiaut - Cristo Rei, Areai Branca - Dolok Oan Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS		Cristo Rei	Dili	Tinolina Unipessoal, Lda	MPW-W-SS-210023	$ 50,020.86	28-May-21	100.00%	100.00%	50,020.87	$ (0.01)	FHO
38	New Construction of Gabion Tower No 6 Section Hera -Manatuto, Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS		Cristo Rei	Dili	Vilagem Construction Unip.Lda	NCB/032/MOP/2020	$ 184,229.60	2-Aug-21	100.00%	43.96%	$ 80,996.20	$ 103,233.40	on going
39	Rehabilitation Construction Of Crocodile Cage Hera	MInisterio Koordenador Asuntu Ekonómikus	LM-BS	EDIFICIOS PUBLICOS		Cristo Rei	Dili	Santana Diak Unipessoal Lda	603DNRHAL/DGA/SEA-MCAE/IX/2021	$ 119,578.85	Sept. 12, 2021	70.64%	37.76%	$ 45,153.74	$ 74,425:11	on going
40	Rehabilitasaun no Konstrusaun Jardim Kristo Rei	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	TURISMO		Cristo Rei	Dili	Mendith UnipLda	01/PDIM/A.M./DILI/X/2017	$ 174,417.64	Oct. 17, 2017	75.00%	61.54%	$ 107,331.66	$ 67,085.98	abandon
41	Konstrusaun sede suko Ailok	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-CD	EDIFICIOS PUBLICOS	Dili	Cristo Rei	Dili	Liberta	05/KAM/AM-DIL/IX/2021	$ 58,919.16		42.62%	17.52%	$ 10,323.23	$ 48,595.93	on going
42	Projetu Konstrusaun Foun no Rehabilitasaun ba EBC Sergio Viera de Melo Becora, Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	Dili	Cristo Rei	Dili	Delatina	NCB:06/MEJD/DNA/2021	$ 149,587.82		0.00%				
43	Projetu Konstrusaun Foun ba ESTV Hera	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	EDUKASAUN	Dili	Cristo Rei	Dili	Timorindo Unip. Lda	NCB:05/MEJD/DNA/2021	$ 199,119.76		0.00%				
44	Konstrusaun ka Reabilitasaun ESTV 28 de Novembro Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Dili	Cristo Rei	Dili	MEJD PKRIE ESTV 28 DE NOVEMBRO BECORA	0000	$ 143,567.64		4.16%				
45	Konstrusaun ka Reabilitasaun ba ESG 12 de Novembro Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Dili	Cristo Rei	Dili	MEJD PKRIE ESG 12 DE NOVEMBRO-BECORA	0000	$ 132,376.67		3.53%				
46	Konstrusaun ka Reabilitasaun ba ESG FINANTIL	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Dili	Cristo Rei	Dili	MEJD PKRIE ESG FINANTIL	0000	$ 71,201.61		3.70%				
47	Konstrusaun ka Reabilitasaun ba EPE Ai-Loktuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Dili	Cristo Rei	Dili	MEJD PKRIE EPE AI-LOKTUTO	0000	$ 79,370.32		20.10%				
48	Emergency Project for Mota Bidau Toko Baru Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	Emergency	MANUTENSAUN NO REHABILITASAUN	Dili	Cristo Rei	Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	311,924.18		100.00%	90.00%	280,731.76	$ 31,192.42	PHO
49	Instalasaun baixada electricidade, instalasaun kanu transmisaun & lutu hadulas estasaun bomba Tuana Laran	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	Bairo pitr	Dom aleixo	Dili	Montez Frere Unip. Lda	MJ-046/Junho 2021	$ 68,988.75	June 12, 2020	85.84%	73.31%	$ 50,579.02	$ 18,409.73	PHO
50	Melhoramento kanu transmisaun no distribuisaun iha Maloa	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	Bairo pitr	Dom aleixo	Dili	Haksolok Java Motor Unip Lda	No: 214/MACLN/X/2021	$ 190,507.61	June 12, 2020	81.85%	72.03%	$ 137,216.58	$ 53,291.03	on going

51	New Installation of MV, LV line and House Connection from Timor Block to Vila Verde, Ponte Comoro and Fomento - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Comoro	Dom aleixo	Dili	Cartilo.Lda	27/CNC/IX/2021	$ 733,130.60	Sept. 1, 2016	46.22%	29.40%	$ 215,548.03	$ 517,582.57	on going
52	Rehabilitasaun Linha Media Tensaun & Baixa Tensaun / Feeder I central eletric comoro Rotunda	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Comoro	Dom aleixo	Dili	Embi elertic.Lda	RDTL-PO:2019-15736	$ 643,682.73	Sept. 1, 2016	27.91%	16.90%	$ 108,803.86	$ 534,878.87	on going
53	New Installation MV, LV Line and House Connection from Bairo Pite to Aldeia ba Dame - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Bairo	Dom aleixo	Dili	Joia Leste Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000409	$ 275,458.38	Sept. 1, 2016	90.00%	80.76%	$ 222,456.28	$ 53,002.10	on going
54	New Installation of MV, LV Line and House Connection from Fatuhada to Behoris, Arbiru Beach, Comoro Market, and Bebonuk - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Dom aleixo	Dili	Ladamutu Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000434	$ 917,122.66	Sept. 1, 2016	50.48%	45.43%	$ 416,628.40	$ 500,494.26	on going
55	New Installation MV, LV Line and House Connection From Rotunda Nicolau Lobato to Terminal Tasi Tolu-Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Nicolau	Dom aleixo	Dili	Sonalevi Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000440	$ 174,335.12	Sept. 1, 2016	94.87%	71.59%	$ 124,814.21	$ 49,520.91	on going
56	Maintenance, Repair & New Electrical Installation at Ministerio Do Plano E Ordenamento	MINISTERIO PLANU E ORDENAMENTU	LM-CD	MANUTENSAUN NO REHABILITASAUN	Fatuhada	Dom aleixo	Dili	Titam Star Supplayer unip.lda	RFQ/040/ANATL,EP-2019	$ 25,089.09	Oct. 26, 2020	92.28%	72.91%	$ 18,291.95	$ 6,797.14	on going
57	Consulting services for DED of the new Ministry of Commerce Industry and Enviroment Training Center	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS		Dom aleixo	Dili	Vítor Hugo Coordenação e Gestão de Projetos, S.A., através de empreendimento conjunto com a Quadromor Timor - Sistemas de Engenharia, S.A	RFP/030/MCIE-2013	$ 216,700.00	May 16, 2014	0.00%	0.00%	$ -	$ 216,700.00	on going
58	Detail Engineering design (DED) of The New Ministry of Commerce, Industry and Environment	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS		Dom aleixo	Dili	Philkoei International Inc. in JV with Arch Haus Asia Consultant, Inc	RFP/029/MCIE-2013	$ 270,000.00	May 28, 2014	40.00%	38.00%	$ 102,600.00	$ 167,400.00	on going
59	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Rehabilitat	Dom aleixo	Dili	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	$ 4,223,035.47	June 8, 2015	83.21%	73.23%	$ 3,092,328.10	$ 1,130,707.37	on going
60	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	river	Dom aleixo	Dili	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	$ 3,752,597.99	Nov. 14, 2014	55.09%	48.48%	$ 1,819,107.90	$ 1,933,490.09	on going
61	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Comoro	Dom aleixo	Dili	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	$ 2,377,535.18	June 23, 2015	63.35%	55.75%	$ 1,325,400.56	$ 1,052,134.62	on going
62	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	river	Dom aleixo	Dili	G and S Unipessoal Lda	SSS/040/MOPTC-2015	$ 4,290,731.32	Nov. 14, 2014	68.35%	60.15%	$ 2,580,786.51	$ 1,709,944.81	on going
63	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Drainage	Dom aleixo	Dili	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	$ 3,501,758.11	June 26, 2015	45.68%	40.20%	$ 1,407,543.92	$ 2,094,214.19	abandon
64	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	and	Dom aleixo	Dili	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	$ 3,854,769.23	June 22, 2015	44.52%	39.18%	$ 1,510,298.22	$ 2,344,471.01	abandon
65	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Road	Dom aleixo	Dili	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	$ 2,471,296.53	Nov. 14, 2014	27.77%	23.90%	$ 590,749.14	$ 1,880,547.39	abandon
66	Road and Drainage Rehabilitation Project Aimutin to Manleuana	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Dom aleixo	Dili	Aspalink Unip Lda	SSS/308/MOPTC-2016	$ 2,238,074.57	July 11, 2016	98.61%	72.88%	$ 1,631,042.87	$ 607,031.70	abandon
67	New Construction of Median Line "Leader to Elemloi JNC"	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Dom aleixo	Dili	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	$ 684,334.48	Sept. 7, 2017	100.00%	95.00%	$ 650,117.75	$ 34,216.73	on going
68	Comoro Power Plant CCTV	MINISTERIO DAS OBRAS PUBLICAS	FI	ICT		Dom aleixo	Dili	SM Bark Technolgy Ltd	SSS/344/MOPTC-2016	$ 1,152,955.98	Dec. 9, 2016	92.00%	80.96%	$ 933,474.50	$ 219,481.48	PHO
69	Maloa River	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Dom aleixo	Dili	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	$ 1,409,964.88	Sept. 12, 2017	50.00%	40.40%	$ 569,564.95	$ 840,399.93	on going
70	Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Comoro	Dom aleixo	Dili	Mejori, Lda	SSS/127/MOPTC-2017	$ 2,571,467.20	Dec. 9, 2017	48.50%	43.65%	$ 1,122,380.78	$ 1,449,086.42	on going
71	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	FLOOD CONTROL	Road	Dom aleixo	Dili	DMF ACESO	MPW-W180036	$ 263,699.22	Jan. 10, 2019	92.53%	92.53%	243,994.87	$ 19,704.35	FHO
72	Konstrusaun Beé mos ba Residencia Sr. Jeneral F-FDTL no Sr. Lu Olo iha Manleuana	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO	Manlaeuar	Dom aleixo	Dili	Caileba	MPWTC-502/5G/MOPTC/V/2017	$ 171,554.48	Aug. 5, 2017	56.89%	51.20%	$ 87,839.97	$ 83,714.51	on going
73	Melhoramento Sistema Beé mos iha Area Delta 1,2,3 no 4	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO		Dom aleixo	Dili	Carisma	MPWTC-NCB-170020	$ 370,082.97	Sept. 12, 2017	100.00%	76.27%	$ 282,248.72	$ 87,834.25	on going
74	Rehabilitasaun no Installasaun Metro Contador Sistema Be'e mos iha Perumnas Bairo Pite (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Dom aleixo	Dili	Sos Alssonix	MPWTC-NCB-170024	$ 178,740.80	Feb. 1, 2018	93.72%	84.35%	$ 150,768.78	$ 27,972.02	PHO
75	Urgent Repair of Roof Leaks at the New Building Ministry of Finance RDTL	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Carya Timor Leste	RDTL-SSS/MOPTC-2017	$ 273,512.05	Sept. 15, 2017	88.17%	79.35%	$ 217,039.61	$ 56,472.44	on going
76	Perfurasaun Sistema Be'e Mos Iha Area Comoro DMA 37 /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Dom aleixo	Dili	Domin Timor Diak Lda	RFQ-MOP-190044	$ 95,321.33	Dec. 31, 2019	100.00%	48.60%	$ 46,326.16	$ 48,995.17	on going

77	Novo construsaun do campo polisportivo do Ministerio das Obras publicas (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	JUVENTUDE NO DESPORTU		Dom aleixo	Dili	ATUNEGOS UNIP.LDA	RFQ MOP/-W-190249	$ 42,859.34	Dec. 15, 2019	79.45%	71.50%	$ 30,644.81	$ 12,214.53	PHO
78	Construction of Terminal in Tasi Tolu	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-CD	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Mar vermelha unip.lda	RDTL-2014-C-101-MTC	$ 464,002.78	Oct. 20, 2014	66.17%	59.55%	$ 276,317.64	$ 187,685.14	abandon
79	Maintenance and Repair at F-FDTL, Head Qaurtel, Fatuhada	MINISTERIO DA DEFESA	LM-BS	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	Victoria Const. Unip. Lda	2015-000065	$ 79,869.00	Sept. 14, 2015	90.57%	81.52%	$ 65,106.35	$ 14,762.65	on going
80	Separasaun ba Aula Tolu iha Ministerio da Defesa	MINISTERIO DA DEFESA	LM-BS	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Algis	la mensiona nomor iha contratu	$ 6,200.17	Aug. 9, 2019	100.00%	90.00%	$ 5,580.15	$ 620.02	PHO
81	Manutensaun Edificio Ministerio da Defesa	MINISTERIO DA DEFESA	LM-BS	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	Algis	RDTL 11 /MNEC /2019	$ 9,082.00	May 6, 2019	96.06%	86.46%	$ 7,851.95	$ 1,230.05	PHO
82	Manutensaun Residencia C.E.M.G. das F-FDTL	MINISTERIO DA DEFESA	LM-BS	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	Panca Sekawan	No la mensiona contratu	$ 207,391.63	Feb. 22, 2019	87.83%	79.04%	$ 163,929.02	$ 43,462.61	on going
83	New Construction of Sao Jose Aimutin Church in Comoro	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Grupo Timindo	Transferencia Publica	$ 3,000,000.00	May 25, 2015	72.33%	0.00%	$ -	$ 3,000,000.00	abandon
84	New Construction of An'Nur Orphanage Building	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Asda A3i Unip. Lda.	Transferencia Publica	$ 269,156.17	Sept. 26, 2016	80.83%	72.75%	$ 195,803.04	$ 73,353.13	on going
85	Konstrusaun Escola de Musica iha fatumeta	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Talisahe	Transferencia Publica	$ 1,684,543.64	Feb. 15, 2017	55.30%	52.53%	$ 884,975.00	$ 799,568.64	on going
86	Konstrusaun Sede Suku Bebonuk	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	PDIM	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Gazelle Unip. Lda	02/KDM/AM-DIL/VIII/2019	$ 54,548.53	Aug. 19, 2019	98.45%	88.61%	$ 48,332.85	$ 6,215.68	on going
87	Konstrusaun Sede Suku Madohi	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	PDIM	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Domcos Hornay Unip. Lda	05/KDM/AM-DIL/VIII/2019	$ 54,547.38	Sept. 18, 2019	97.52%	87.77%	$ 47,874.42	$ 6,672.96	PHO
88	Rehabilitasaun and Maintanance of Vice Minister office in Mandarin	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	Milcha Unip Lda	364/DNA-DGAF-MOP/XII/2019	$ 9,466.24	April 5, 2020	81.76%	73.58%	$ 6,965.27	$ 2,500.97	PHO
89	Manutensaun Edificio iha Gabinete Ministro nian	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	Olsop Paris Unip Lda	RDTL-MAP176/GM/VIII/2019	$ 19,249.03	Aug. 26, 2010	95.84%	95.84%	$ 18,449.03	$ 800.00	PHO
90	Urgent Installation of Street Lights in Tasi Tolu, Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Dom aleixo	Dili	Alefa Unip Lda	MOP-W-190133	$ 87,154.90	Aug. 15, 2019	72.00%	64.80%	$ 56,479.60	$ 30,675.30	on going
91	Konstrusaun Lutu Hadulas WTP Central iha Bairo-Pite Dom Aleixo Municipio Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Dom aleixo	Dili	Iki Bia-Nunu Unip Lda	NCB/MOP/W-200015	$ 197,127.50	Oct. 7, 2019	74.81%	67.33%	$ 132,718.86	$ 64,408.64	on going
92	Rehabilitation Recident & Carport of Vice PM (Bem Serviso)	MINISTERIO PLANU E ORDENAMENTU	LM-BS	EDIFICIOS PUBLICOS		Dom aleixo	Dili	D. Likibo Unip. Lda	05/RDTL/MPO/ADN/DA-Afq/X/2020	$ 49,078.24	Nov. 17, 2020	100.00%	100.00%	$ 49,078.24	$ -	FHO
93	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS		Dom aleixo	Dili	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	$ 314,106.58	April 20, 2021	100.00%	88.00%	$ 276,413.79	$ 37,692.79	on going
94	Revitalization of Community Aitarak Laran	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS		Dom aleixo	Dili	TPF Timor Unipessoal Lda	MPW-S-190272	$ 399,974.64	March 25, 2020	20.00%	20.00%	$ 79,994.92	$ 319,979.72	on going
95	Servisu Manutensaun Edificio Agencia de Desenvolvimento Nasional	MINISTERIO PLANU E ORDENAMENTU	LM-BS	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	Giovanio	002.LM/RDTL/MPO/ADN,I.P/III/2021	$ 60,000.00	March 18, 2021	54.34%	54.34%	32,603.80	$ 27,396.20	on going
96	Instalasaun Agua Potavel iha Edificio Ministerio da Defesa no QG das F-FTL	MINISTERIO DEFESA	LM-CD	MANUTENSAUN NO REHABILITASAUN		Dom aleixo	Dili	CAPTAIN HOOK		$ 38,450.39	24-Apr-21	94.78%	90.04%	$ 34,620.62	$ 3,829.77	on going
97	For River Normalization, Roads Embankment and Road Clean Up of Comoro Mota Ulun - Casnafar, Air Terjun Sarlala Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS		Dom aleixo	Dili	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS-210006	$ 148,256.87	28-May-21	100.00%	100.00%	148,256.88	$ (0.01)	FHO
98	Enhancement of Project - Management Information System (PMIS)	MINISTERIO PLANU E ORDENAMENTU	LM-BS	EQUIPAMENTO INFROMATICO		Dom aleixo	Dili	KINOS Unip,Lda	011/RDTL/MPO/ADN,I.P/V/202	$ 56,935.00	May 24, 2021	85.00%	85.00%	$ 48,394.75	$ 8,540.25	on going
99	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS		Dom aleixo	Dili	Bintang Fajar, Lda	MPW-W-SS 210028	$ 88,970.39	2-Jul-21	100.00%	100.00%	88,970.39	$ -	FHO
100	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	MINISTERIO DAS OBRAS PUBLICAS	Emergency	ESTRADAS		Dom aleixo	Dili	Monte Veado Unip Lda	MPW-W-SS 210008	$ 58,307.54	26-May-21	100.00%	100.00%	58,307.53	$ 0.01	FHO
101	Rehabilitasaun Edificio Dormitoriu INS Comoro-Dili Timor Leste	MINISTERIO SAUDE	LM-CD	SAUDE	Dili	Dom aleixo	Dili	Grandis	RDTL-INS -DAFA-NCB-21-0001	$ 155,299.96	Aug. 4, 2021	82.55%	74.29%	115,375.18	$ 39,924.78	on going
102	New Construction Lanscaping and Gazebo at Vice Prime Minister Official Recident	MINISTERIO PLANU E ORDENAMENTU	LM-BS	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Rubic Unip. Lda	006/RDTL/MPO/ADN,I.P/III202	$ 34,855.64		96.67%	87.01%	$ 30,326.67	$ 4,528.97	PHO
103	Extention of Sames Ware-House Building at Kampo Alor	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS		Dom aleixo	Dili	Unidade Unip Lda	RDTL-SAMES-RFQ-20-063	$ 51,444.91		63.00%	56.70%	$ 29,171.16	$ 22,273.75	on going
104	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS		Dom aleixo	Dili	Lizi Construction, Unipessoal Lda	MOP/CD/NCB/21044	$ 578,040.73		45.78%	0.00%	$ -	$ 578,040.73	on going
105	Consulting services of spatial planing of Timor Leste	MINISTERIO PLANU E ORDENAMENTU	FI	DESENVOLVIMENTO URBANO E RURAL	Dili	Dom aleixo	Dili	Intersisment S.A in Joint Venture with Quetemaire Portugal Consultoria para o Desenvolvimento, SA	SSS/041/MPO-2021	$ 781,121.90		30.00%	28.50%	$ 222,619.74	$ 558,502.16	on going

106	New construction archive werehouse at bebora	MINISTERIO SAUDE	LM-BS	SAUDE	Dili	Dom aleixo	Dili	Hilobadi Unip,Lda	RDTL-MS-C19-DNA-NCB-21-0	$ 109,519.43		47.15%	47.15%	51,642.65	$ 57,876.78	on going
107	Construsaun de Balcao de atendimento publica para a Direcsaun Geral dos servicos de registos e do Notariado do Ministerio da Justica	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	Dili	Dom aleixo	Dili	Fatuk Mota Construction Unipessoal. Lda	MJ-046/Junho 2021	$ 57,463.94		81.42%	73.28%	$ 42,107.87	$ 15,356.07	on going
108	Manutensaun de salao Nobre	MINISTERIO DO INTERIOR	LM-BS	EDIFICIOS PUBLICOS	Dili	Dom aleixo	Dili	DCO Unip.Lda	No: 214/MACLN/X/2021	$ 89,984.12		93.92%	84.52%	$ 76,057.77	$ 13,926.35	on going
109	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	MTC	LM-CD	PORTOS	Dili	Dom aleixo	Dili	Holgapa Unip.Lda	RDTL - 2021 - MTC - CD - 031	$ 386,456.87		44.11%	0.00%		$ 386,456.87	on going
110	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	MINISTERIO DAS OBRAS PUBLICAS	Emergency	PONTES	Bairo pite	Dom aleixo	Dili	Chegue Rau	NCB/040/MOP-2020	$ 24,919.25		100.00%	0.00%		$ 24,919.25	on going
111	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	MINISTERIO DAS OBRAS PUBLICAS	Emergency	PONTES	Bairo pite	Dom aleixo	Dili	Holgapa Unip.Lda	RT/069/MOP-2021	$ 213,895.26		47.16%	0.00%		$ 213,895.26	on going
112	Konstrusaun ka Reabilitasaun ba ESG 10 de Dezembro Comoro - Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		DOM ALEIXO	Dili	MEJD PKRIE ESG 10 DE DEZEMBRO COMORO-DILI		$ 108,265.95		0.00%				
113	Konstrusaun ka Reabilitasaun ba EBC 10 de Dezembro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		DOM ALEIXO	Dili	MEJD PKRIE EBC 10 DE DEZEMBRO		$ 128,911.25		8.44%				
114	Konstrusaun ka Reabilitasaun ba EBC 30 de Agosto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		DOM ALEIXO	Dili	MEJD PKRIE EBC 30 DE AGOSTO		$ 149,978.57		22.81%				
115	Konstrusaun ka Reabilitasaun ba EBF Naroman	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		DOM ALEIXO	Dili	MEJD PKRIE EBF NAROMAN		$ 105,245.50		0.00%				
116	Konstrusaun ka Reabilitasaun ba EPE Buras Kadalak	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		DOM ALEIXO	Dili	MEJD PKRIE EPE BURAS KADALAK		$ 80,571.32		13.04%				
117	Konstrusaun ka Reabilitasaun ba EBF Bebonuk	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN		DOM ALEIXO	Dili	MEJD PKRIE EBF BEBONUK		$ 88,127.23		3.05%				
118	Mudansa Lina Bazeia Rekomendasaun ADN	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Duyung	Metinaro	Dili	Jofi	27/CNC/IX/2021	$ 2,390.32	Jan. 1, 2016	0.00%	0.00%	$ -	$ 2,390.32	la executa
119	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS		Metinaro	Dili	Nimia Unip Lda	RDTL-PO:2019-15736	$ 411,413.54	Oct. 29, 2015	100.00%	79.91%	$ 328,740.58	$ 82,672.96	PHO
120	Melhoramento taratamento dezalinasaun iha manleu Metinaro /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	AGUA E SANEAMENTO		Metinaro	Dili	Garisiba Unip.Lda	MOP-W-190150	$ 87,856.59	May 11, 2019	87.07%	43.07%	$ 37,843.35	$ 50,013.24	on going
121	Construction of Kitchen and Refectory at Componete do Apoio de Serviso (CAS) iha Metinaro	MINISTERIO DA DEFESA	LM-BS	EDIFICIOS PUBLICOS		Metinaro	Dili	Betuhei	la mensiona nomor iha contratu	$ 581,897.61	Oct. 26, 2015	100.00%	90.00%	$ 523,707.86	$ 58,189.75	PHO
122	New Construction of WareHouse, Campas, Raodway, Drainage and Pavement at Jardim dos Herois Metinaro	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	LM-CD	SOLIDARIEDADE E SOCIAL		Metinaro	Dili	Pro Frawijaya	RDTL:44/MSS/DNFALM-DAD/X/2014	$ 449,600.23	Oct. 16, 2014	86.56%	77.90%	$ 350,256.56	$ 99,343.67	on going
123	Konstrusaun Turismu Komunitariu One Dollar Beach	SEFOPE	LM-TP	PORTOS		Metinaro	Dili	Quindy Eujec Lda.	02/CNFP-B/VII/2019	$ 460,254.00	July 27, 2018	82.03%	73.83%	$ 339,787.68	$ 120,466.32	on going
124	Detailed Engineering Design of New Fisherman Port, Suco Duyung, Metinaro	MINISTERIO AGRIKULTURA E PESCAS	FI	AGRICULTURA		Metinaro	Dili	Consulmar-Projetista e Consultore. Lda de Portugal em Empreendimento Conjunto com a Engipro de TLPty. Ltd	RFP/042/MAF-2014	$ 273,270.70	July 27, 2018	70.00%	70.00%	$ 191,289.49	$ 81,981.21	abandon
125	New Construction of Roadways, Drainage and Parking Area no Jardim de Herois de Metinaro	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	ESTRADAS	Dili	Metinaro	Dili	Celijio Star	No: 214/MACLN/X/2021	$ 948,930.17		42.13%	7.04%	$ 66,779.57	$ 882,150.60	on going
126	New Construction of Campas and Grass Planting Jardin dos Herois (JHM) Metinaro	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	TURISMO	Dili	Metinaro	Dili	LABILAY, Unipessoal, Lda	216/MACLN/X/2021	$ 397,296.90		24.59%	10.64%	$ 42,272.58	$ 355,024.32	on going
127	New Const of F-FDTL home base Fuel Filling Station in Metinaro, Dili Municipality	MINISTERIO DA DEFESA	LM-BS	EDIFICIOS PUBLICOS	Dili	Metinaro	Dili	Aitula Construction, Lda	ICB No 05/DNA/MD/2021	$ 809,906.27		0.00%	0.00%		$ 809,906.27	on going
128	Konstrusaun ka Reabilitasaun ba EBF Benunuk Metinaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Dili	Metinaro	Dili	MEJD PKRIE EBF BENUNUK METINARO		77,383.99		8.60%				
129	Konstrusaun ka Reabilitasaun ba ESG 20 de Setembro Metinaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	Dili	Metinaro	Dili	MEJD PKRIE ESG 20 DE SETEMBRO METINARO		164,146.98		2.93%				
130	Rehabilitasaun kanu transmisaun husi Benamauk ba WTP Lahane no Becusse	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO	lahane	Nain Feto	Dili	Lemo Timor Unipessoal Lda	SSS/019/MOP-2020	$ 139,971.80		0.00%	0.00%		$ 139,971.80	on going

131	Consulting Services for detailed Engineering Design of CAC Office Building	CAC	FI	EDIFICIOS PUBLICOS	Bidau	Nain Feto	Dili	Imagem, Design and Arquitectura, Lda (IDA) in Association with Vaz, Dotti & Silva, Lda (VDS)	RFP/004/MPW-2013	$ 256,843.00	March 18, 2014	72.71%	69.08%	$ 177,425.04	$ 79,417.96	on going
132	New Construction of Ojetil Office Building Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	EDIFICIOS PUBLICOS	bidau	Nain Feto	Dili	Fitun Diak Unip.Lda	SSS/301/MOPTC-2016	$ 1,753,481.10	Feb. 12, 2016	100.00%	80.18%	$ 1,405,967.18	$ 347,513.92	on going
133	New Installation MV, LV Line and House Connection from Bidau to Catedral - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Bidau Lec	Nain Feto	Dili	Anicla.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000437	$ 483,778.67	Sept. 1, 2016	81.60%	67.76%	$ 327,828.49	$ 155,950.18	on going
134	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Nain Feto	Dili	Meteor Unip.Lda	SSS/200/MOPTC-2016	$ 4,032,231.86	Sept. 13, 2016	78.64%	69.20%	$ 2,790,269.55	$ 1,241,962.31	on going
135	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Nain Feto	Dili	Suai Indah Unipessoal Lda	SSS/218/MOPTC-2016	$ 999,876.89	Sept. 13, 2016	55.23%	48.60%	$ 485,972.09	$ 513,904.80	abandon
136	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Ponte	Nain Feto	Dili	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	$ 911,145.27	June 4, 2020	98.99%	87.11%	793,683.27	$ 117,462.00	on going
137	Installation of Transmission Line, Distribuition Panel & Transformer in Taibesi and Becora	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Nain Feto	Dili	Nizixavane	MPWTC-W-015072	$ 312,775.56	Oct. 28, 2015	97.82%	88.04%	$ 275,364.75	$ 37,410.81	on going
138	Construction of Membrane Tent and Shaded Area of SG-MOPTC	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS		Nain Feto	Dili	Voar	MPWTC-W-170020	$ 83,897.22	Jan. 9, 2017	91.14%	82.02%	$ 68,816.03	$ 15,081.19	on going
139	Installation of Street Lights Lecidere - Acadiruhun-Acait (Lot 6)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Nain Feto	Dili	Alzes Ukat, Unip.Lda	MPW-W-190266	$ 46,507.85	Oct. 19, 2019	70.12%	63.10%	$ 29,348.21	$ 17,159.64	on going
140	Rehabilitasaun no manutensaun ex edificio diresaun geral organizasaun urbana	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-BS	MANUTENSAUN NO REHABILITASAUN		Nain Feto	Dili	Riri Brothers Unip. Lda.	RDTL,0140/UAD-MAE/XII/2019	$ 26,426.13	Dec. 9, 2019	100.00%	85.73%	$ 22,655.09	$ 3,771.04	on going
141	Rehabilitasaun Edificio Conselho de Empresa	CONSELHO DA EMPRENSA	LM-BS	EDIFICIOS PUBLICOS		Nain Feto	Dili	Algis	CI-19-06-C-013	$ 97,498.81	June 4, 2019	95.43%	85.89%	$ 83,740.72	$ 13,758.09	PHO
142	Manutensaun Expert Room iha MESCC	MINISTERIO ENSINO SUPERIOR CIENCIA E CULTURA	LM-BS	MANUTENSAUN NO REHABILITASAUN		Nain Feto	Dili	Katuas Patricio	RFQ19/45-Q	$ 7,583.06	Sept. 16, 2019	97.00%	87.03%	$ 6,599.24	$ 983.82	PHO
143	Rehabilitation of Volley Ball Beach Facilities in Dili-Lecidere	SEJD	LM-CD	JUVENTUDE NO DESPORTU		Nain Feto	Dili	DVD Electric	NCB/01/SSYS-2019	$ 84,302.72	Oct. 29, 2019	94.93%	90.18%	$ 76,026.71	$ 8,276.01	PHO
144	Rehabilitation of GDD Sports Indoors	SEJD	LM-CD	JUVENTUDE NO DESPORTU		Nain Feto	Dili	Victoria Const. Unip. Lda	NCB/02/5595-2019	$ 446,169.01	Oct. 29, 2019	100.00%	94.27%	$ 420,616.86	$ 25,552.15	on going
145	Rehabilitation and Maintenance of Jardim 12 de Novembro at Motael	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	MANUTENSAUN NO REHABILITASAUN		Nain Feto	Dili	Algis	RDTL:47/DNA-MTCI/VII/2019	$ 95,425.00	July 31, 2019	98.48%	88.63%	$ 84,575.48	$ 10,849.52	PHO
146	Rehabilitasaun Residencia Vice Presidente Parlamentu Nacional iha Farol	PARLAMENTU NASIONAL	LM-BS	MANUTENSAUN NO REHABILITASAUN		Nain Feto	Dili	Celijio Star	PN/4306/2016	$ 30,037.14	July 21, 2016	100.00%	90.00%	$ 27,033.43	$ 3,003.71	PHO
147	Rehabilitasaun Jardim 12 de Novembro iha Igreza Motael nia oin	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-BS	TURISMO		Nain Feto	Dili	Berlosconi	RDTL0144/UADE-MAE/XII/2019	$ 46,905.00	Aug. 15, 2019	90.46%	81.41%	$ 38,186.71	$ 8,718.29	on going
148	Rehabilitation and Maintenance Building PCM	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	LM-BS	MANUTENSAUN NO REHABILITASAUN		Nain Feto	Dili	Panca Sekawan	PCM-20/01-C/0014	$ 150,000.00	Jan. 15, 2020	100.00%	9.14%	$ 13,702.50	$ 136,297.50	on going
149	Minor Rehabilitasaun of MTC main of Building and Correeios	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	LM-BS	EDIFICIOS PUBLICOS		Nain Feto	Dili	Risumali Unip Lda	RDTL2019-MTC-GS-0041	$ 8,889.74	Jan. 1, 2020	98.90%	89.01%	$ 7,912.92	$ 976.82	PHO
150	Rehabilitation of Confrence Room at the office of the Primer Minister, building I, Palacio do Governo,Dili Timor Leste	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		Nain Feto	Dili	Gez Unipessoal Lda	RDTL-294/GPM/XI/2019	$ 52,232.55	Nov. 29, 2019	100.00%	85.62%	$ 44,721.11	$ 7,511.44	PHO
151	RIVER PROTECTION PALACIO NOBRE	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	FLOOD CONTROL		Nain Feto	Dili	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	$ 129,168.62		60.24%	30.21%	$ 39,016.84	$ 90,151.78	on going
152	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	TRIBUNAL RECUSSO	Emergency	EDIFICIOS PUBLICOS		Nain Feto	Dili	Star King Unip. Lda	MPW-SS-210030	$ 122,960.04	10/8/2021	100.00%	90.00%	$ 110,664.03	$ 12,296.01	PHO
153	Refurbishment of tenis court facilities, Dili	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	JUVENTUDE NO DESPORTU	Dili	Nain Feto	Dili	Algis	NCB/01/SSYS/2021	$ 97,389.44		62.14%	27.93%	$ 27,197.75	$ 70,191.69	on going
154	aditional for Hospital Dr.Antonio Carvalho Lahane	MINISTERIO SAUDE	LM-BS	SAUDE	Dili	Nain Feto	Dili	Hedge Construction, Unip. Lda	RDTL-MS-C19-DNA-DC-21-072	$ 150,710.92		26.38%	23.74%	$ 35,778.96	$ 114,931.96	on going
155	New Construction of outdoor sport facilities in Taibessi	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	JUVENTUDE NO DESPORTU	Dili	Nain Feto	Dili	UKA II UNIPESSOAL LDA	NCB/02/SSYS/2021	$ 204,254.98		0.00%	0.00%		$ 204,254.98	on going
156	Preparation of detailed engineering design (DED) for new cable stayed bridge over the becusse river, in Dili, total lenght+25m", Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	lahane	Nain Feto	Dili	TPF Timor Unipessoal Lda	RT-CD-MOP-21002	$ 87,800.00		0.00%	0.00%		$ 87,800.00	on going
157	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	lahane	Nain Feto	Dili	Sanford Const. Unip. Lda	MPW-W-210168	$ 284,325.06		100.00%	0.00%		$ 284,325.06	on going

158	New Construction of outdoor sport facilities in Taibessi	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	JUVENTUDE NO DESI	lahane	Nain Feto	Dili	UKA II UNIPESSOAL LDA	NCB/02/SSYS/2021	$ 204,254.98		0.00%					
159	Konstrusaun ka Reabilitasaun ba EBF Duque de Caxias	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	lahane	Nain Feto	Dili	MEJD PKRIE EBF DUGUE DE CAXIAS	0000	$ 80,723.84		0.00%					
160	Konstrusaun ka Reabilitasaun ba EBC Bidau Akadiru-Hun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	lahane	Nain Feto	Dili	MEJD PKRIE EBC BIDAU AKADIRU HUN	0000	$ 93,171.12		11.92%					
161	Konstrusaun ka Reabilitasaun ba EBF Lelaus Dare	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	EDUKASAUN	lahane	Nain Feto	Dili	MEJD PKRIE EBF LELAUS DARE	0000	$ 77,821.06		0.00%					
162	Rehabilitasaun Eis Hospital Dr.Antonio de Carvalho	MINISTERIO SAUDE	Fundo covid-19	SAUDE		Nain Feto	Dili	DALAVEYA Unip.Lda	RDTL-MS-C19-DNA-DC-22-019	$ 739,937.34	31-03-2022	0.00%					on going
163	Construction Of New Office Of Tribunal Distrital De Dili	TRIBUNAL RECUSSO	FI	EDIFICIOS PUBLICOS	caicoli	vera cruz	Dili	China Shandong International Economic And Technical Cooperation Group. LTD	ICB/008/TR-2019	$ 10,990,769.35	May 12, 2019	25.46%	22.91%	$ 2,518,237.16	$ 8,472,532.19	on going	
164	Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building	TRIBUNAL RECUSSO	FI	EDIFICIOS PUBLICOS	caicoli	vera cruz	Dili	Dacrea Desing and Engineering Consultant (Dacrea) (Indonesia) In Association with Archtimor Engineering Consultants (AEC) as Sub-consultant (Timor-Leste)	RFP/012/TR-2019	$ 567,197.00	Dec. 16, 2019	64.95%	61.70%	$ 349,983.72	$ 217,213.28	on going	
165	Installation of New MV Line in Rotunda Mercado Lama, Culuhun, Ailele Hun, and Lecidere	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	caicoli	vera cruz	Dili	Ferajota	SSS/072/MOPTC-2015	$ 385,588.18	Dec. 14, 2015	61.92%	54.49%	$ 210,088.60	$ 175,499.58	abandon	
166	Rehabilitation MV,Line , LV Line and distribution Trasforner from Casa Europa to Pantai Pasir Putih - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	caicoli	vera cruz	Dili	Inaziju	RDTL/MOP-SEE/CGI-PEN : 0000267	$ 119,600.79	Oct. 2, 2013	100.00%	90.00%	$ 107,640.71	$ 11,960.08	abandon	
167	Construção Quartel General PNTL em Caicoli	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA		vera cruz	Dili	Shangai Construction Group Co.,Ltd	ICB/036/MI-2017	$ 10,177,638.20	Oct. 22, 2019	1.78%	1.16%	$ 117,755.27	$ 10,059,882.93	on going	
168	Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste	MINISTERIO DO INTERIOR	FI	SEGURANCA NO DEFESA		vera cruz	Dili	PT. Ceriajasa Cipta Mandiri in Joint Venture with JKC Consultant Engineering Unipessoal Lda	RPF/087/MI-2017	$ 594,360.00	Nov. 22, 2019	10.00%	9.50%	$ 56,464.20	$ 537,895.80	on going	
169	Consulting Services for Detail Engineering Design of the IGE Office, Workshop and Warehouse Complex Building	MINISTERIO DAS OBRAS PUBLICAS	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS		vera cruz	Dili	Scope Australia Pty, Ltd	RFP/039/MPW-2013	$ 295,000.00	March 26, 2014	95.00%	95.00%	$ 280,250.00	$ 14,750.00	PHO	
170	Consulting Services for Detailed Architecture and Engineering Design for Press Building Project	SECRETARIADO ESTADO KOMUNIKASAUN	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	Architectu	vera cruz	Dili	CGM Consultants & Associates Incorporated, Lda.	SSS/051/SECOM-2015	$ 200,000.00	Feb. 25, 2015	40.00%	38.00%	$ 76,000.00	$ 124,000.00	on going	
171	Consulting Services for Feasibility Study of the New Buildings for RTTL. P.E and Tatoli P.I.	SECRETARIADO ESTADO KOMUNIKASAUN	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS	for	vera cruz	Dili	Potevio Company Limited	RDTL	$ 212,212.00	Sept. 27, 2020	100.00%	0.00%	$ -	$ 212,212.00	on going	
172	Additional Drainage Colnera	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		vera cruz	Dili	Hailala Unip.Lda	166139	$ 7,049.68	Aug. 22, 2013	100.00%	90.00%	$ 6,344.71	$ 704.97	PHO	
173	Consulting Services of Detailed Engineering Design of Sport Complex and Building at Region of Dili	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Sport	vera cruz	Dili	ATT consultants Co. Ltd JV SQ Architect and Planner Co. Ltd	RFQ/314/SEJD-2016	$ 285,700.00	May 8, 2017	70.00%	66.50%	$ 189,990.50	$ 95,709.50	on going	
174	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	MANUTENSAUN NO REHABILITASAUN	lelaus	vera cruz	Dili	Bia Mapel	MPW-W190099	$ 44,559.88	Sept. 23, 2019	100.00%	90.00%	$ 40,103.89	$ 4,455.99	PHO	
175	Rehabilitation of Security Post Building in Caicoli MPW	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS	Caicoli	vera cruz	Dili	Reza	RDTL MPW-014067	$ 28,927.73	Jan. 10, 2014	76.91%	69.22%	$ 20,022.51	$ 8,905.22	on going	
176	Prefurasaun Be'e mos iha Area Tuana Laran - Matadouro Suku Vila verde, Postu Administrativo Vera Cruz - Municipiu Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	AGUA E SANEAMENTO		vera cruz	Dili	Liberta	MPWTC-W-700774	$ 158,815.15	Aug. 16, 2017	100.00%	69.34%	$ 110,115.78	$ 48,699.37	on going	
177	Manutensaun ba Edificio DNGRA-MOP / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	EDIFICIOS PUBLICOS		vera cruz	Dili	Katuas Patricio	RFQ-MOP-190071	$ 8,098.49	May 11, 2019	99.31%	89.38%	$ 7,238.15	$ 860.34	PHO	
178	Rehabilitation of DNA MOP Cobe House in Caicoli Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	EDIFICIOS PUBLICOS		vera cruz	Dili	Surik Saki Rai Unip.Lda	MOP-W-190167	$ 48,635.85	Dec. 1, 2019	97.00%	87.46%	$ 42,535.56	$ 6,100.29	PHO	
179	Construction of extension office building of the Minister of Public works (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	EDIFICIOS PUBLICOS		vera cruz	Dili	CELFA Unip.Lda	RDTL-NCB-MOP-190088	$ 165,991.00	Dec. 1, 2019	100.00%	88.17%	$ 146,361.04	$ 19,629.96	on going	
180	Detailed Engineering design of E-Recruitment Building CFP	CFP	LM-BS	EDIFICIOS PUBLICOS		vera cruz	Dili	De Oliveira design	SSS/045/MT-2017	$ 35,500.00	Oct. 2, 2019	95.00%	95.00%	$ 33,725.00	$ 1,775.00	PHO	
181	New Construction of Auditorium (Salaun Paroquial) & Class Room & landscape of Catedral, Vila Verde	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		vera cruz	Dili	Bimavi	transferencia publica	$ 825,142.43	March 27, 2015	94.30%	84.87%	$ 700,298.38	$ 124,844.05	on going	
182	Construção Pure Hindu Taibesi	GABINETE DO PRIMEIRO MINISTRO	LM-TP	EDIFICIOS PUBLICOS		vera cruz	Dili	Pantarhei	Transferencia Publica	$ 1,207,958.18	Aug. 25, 2017	74.77%	0.00%	$ -	$ 1,207,958.18	on going	

183	New Construction of Administration and Logistic Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS		vera cruz	Dili	Aitula Construction, Lda	059/C/UNTL/XI/2019	$ 678,218.04	Nov. 26, 2019	89.97%	66.05%	$ 447,947.66	$ 230,270.38	on going
184	New Construction of Faculidade Econimia e Gesatao Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS		vera cruz	Dili	Aitula Construction, Lda	057/C/UNTL/X/2019	$ 672,666.11	Oct. 29, 2019	95.62%	78.78%	$ 529,943.95	$ 142,722.16	on going
185	New Building Construction of Medicina Ciencia da Saude Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS		vera cruz	Dili	Linier jv Algis	058/C/UNTL/X/2019	$ 678,572.97	Sept. 6, 2019	98.60%	89.57%	$ 607,777.12	$ 70,795.85	PHO
186	Konstrusaun Edificio servisu espesializada iha PGR Colmera	PROCURADORIA GERAL DA REPUBLIKA	LM-CD	EDIFICIOS PUBLICOS		vera cruz	Dili	Bobolait	RDTL-D.FEO/APRO/PGR/19.002/2019	$ 556,612.74	Oct. 17, 2019	100.00%	89.73%	$ 499,422.83	$ 57,189.91	PHO
187	Rehabilitation of Houses RTTL in Caicoli and Biterlau	RADIO TELEVISAUN TIMOR LESTE	LM-BS	MANUTENSAUN NO REHABILITASAUN		vera cruz	Dili	Gaerenez	10/RDTL,E.P/DAF/VI/2019	$ 37,605.25	June 7, 2019	100.00%	90.00%	$ 33,844.72	$ 3,760.53	PHO
188	Konstrusaun Edifisiu Foun ba Diresaun Aprovizionamentu Finansas e Fiskalizasaun	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	PDIM	EDIFICIOS PUBLICOS		vera cruz	Dili	Chipys Unip. Lda	07KDM/AM-DIL/X/2019	$ 143,579.83	Oct. 8, 2019	93.02%	83.72%	$ 120,198.07	$ 23,381.76	on going
189	Maintenance of Building for Trade Invest Timor Leste	TRADE INVEST	LM-BS	MANUTENSAUN NO REHABILITASAUN		vera cruz	Dili	D'CO	RDTL/TITL/C.06/10/2019	$ 37,582.90	Sept. 1, 2019	55.88%	50.29%	$ 18,900.89	$ 18,682.01	on going
190	Rehabilitasaun Hospital Dr.Antonio Carvalho Lahane(Building A) Hodi halo Fatin Izolamentu ba Pasienti Covid-19	MINISTERIO SAUDE	Fundo covid-19	MANUTENSAUN NO REHABILITASAUN		vera cruz	Dili	Hedge Construction, Unip. Lda	NCB/M.S./DNA/DC-20/143	$ 450,153.32	May 25, 2020	86.99%	83.04%	$ 373,791.56	$ 76,361.76	PHO
191	Desenho e Espicificacao de Quantidades BoQ para a ampliacao do Balcao de Atendimento na DNRN	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS		vera cruz	Dili	Viros Consultant Unip Lda	RDTL-MJNo.009/MAIO/2019	$ 9,000.00	Jan. 6, 2019	100.00%	74.07%	$ 6,666.00	$ 2,334.00	on going
192	Rehabilitasaun e Manutensaun Edifisio Armajen DNSA, Dili (Bem Serviso) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	EDIFICIOS PUBLICOS		vera cruz	Dili	BTwo Unip Lda	MOP/W-190186	$ 26,539.42	Dec. 31, 2019	69.53%	62.58%	$ 16,608.24	$ 9,931.18	on going
193	Detailed Engineering Design Hospital Dr. Antonio Carvalho LOT"A" Lahane Oriental	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS		vera cruz	Dili	Victoria Cosnt.	FBS-DNA-MOP-19016	$ 375,986.35	March 31, 2020	10.00%	9.95%	$ 37,425.67	$ 338,560.68	on going
194	Improvement of Mina Distribuition Pipe in DMA 31 in Suco Mascarenhas	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		vera cruz	Dili	Amigo Unip. Lda	No : /NCB/MPW/W-200016	$ 51,111.18	Oct. 1, 2019	69.16%	45.55%	$ 23,279.56	$ 27,831.62	on going
195	New Construction of isolation (OPD) Vera cruz relation of covid 19	MINISTERIO SAUDE	Fundo covid-19	EDIFICIOS PUBLICOS		vera cruz	Dili	Romante Pty. Ltd	RDTL-MS-C19-DNA-SS-21-001	$ 265,808.11	Jan. 13, 2021	87.48%	67.50%	$ 179,427.97	$ 86,380.14	on going
196	New construction Warehouse for centro Nacional Chega I.P	Centro Nacional Chega	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	A. L. Unip.Lda	26/CNC/IX/2021	$ 63,878.59		98.72%	76.85%	$ 49,088.13	$ 14,790.46	on going
197	Renovation of public Health services at lahane , posto vera cruz Timor Leste	MINISTERIO SAUDE	LM-BS	SAUDE	Dili	vera cruz	Dili	Queson SQ Unipessoal Lda	RDTL-MS-DNA-ICB-20-255	$ 282,726.57		31.75%	15.78%	$ 44,617.10	$ 238,109.47	on going
198	New Construction Drinage centro Nasional Chega.I.P	Centro Nacional Chega	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Chacailala Unipessoal Lda	27/CNC/IX/2021	$ 70,792.37		56.75%	51.07%	$ 36,155.12	$ 34,637.25	on going
199	Criacao de estrutura de parede divisorias do ministerio da justica	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Fatuk Mota Construction Unipessoal. Lda	MJ-047/junho/2021	$ 61,314.55		78.80%	70.92%	$ 43,484.24	$ 17,830.31	on going
200	Extention Office of Legal and Judicial Training Centre	MINISTERIO DA JUSTICA	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	BEHALE ENTERPRICE UNIPESSOAL,LDA	MJ-066/Novembro/2021	$ 232,916.02		0.00%	0.00%		$ 232,916.02	on going
201	Construction of Faculdade de Agricultura Building (B-01)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Dany stra	RDTL 039/C/UNTL/XII/2021	$ 655,394.42		0.00%	0.00%		$ 655,394.42	on going
202	Construction of Faculdade de Agricultura Building (B-02)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Hedge Construction, Unip. Lda	RDTL 041/C/UNTL/XII/2021	$ 605,337.84		0.00%	0.00%		$ 605,337.84	on going
203	Construction of Faculdade de Agricultura Building (B-03)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Bobolait		$ 630,619.64		0.00%	0.00%		$ 630,619.64	on going
204	Design Edificio MACLN	MINISTRO PARA C	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Uma de Contrucão Unipessoal Lda	38/MACLN/IX/2021	$ 88,510.00		30.00%	30.00%	26,553.60	$ 61,956.40	on going
205	Construction of Faculdade de Agricultura Building (B-01)	UNIVERCIDADE N	LM-CD	EDUKASAUN	Dili	vera cruz	Dili	Dany Stra Unipessoal Lda	RDTL 039/C/UNTL/XII/2021	$ 655,394.42		0.00%				
206	New Construction of Faculdade de Agricultura (B-02)	UNIVERCIDADE N	LM-CD	EDUKASAUN	Dili	vera cruz	Dili	Bobolait Lda	RDTL 041/C/UNTL/XII/2021	$ 630,619.64		0.00%				
207	New Construction of Faculdade de Agricultura (B-03)	UNIVERCIDADE N	LM-CD	EDUKASAUN	Dili	vera cruz	Dili	Hedge Construction, Unip. Lda	RDTL040/C/UNTL/XII/2021	$ 605,337.84		0.00%				
208	Extention Office of Legal and Judicial Training Centre	MINISTERIO DA JU	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	BEHALE ENTERPRICE UNIPESSOAL,LDA	MJ-066/Novembro/2021	$ 232,916.02		0.00%				
209	Konstrusaun Koby House foun ba Unidade Aprovisionamento Desentralizadu UAD	MINISTÉRIO DA ADMINISTRAÇÃO ESTATAL	LM-CD	EDIFICIOS PUBLICOS	Dili	vera cruz	Dili	Linier Unipessoal Lda	RFQ/088/MAE-2021	$ 78,817.38		17.39%	15.65%	12,336.48	$ 66,480.90	on going
210	Restante Cabo Subteranno Centro Produsaun SAKATO reutiliza ba Hotel Ambeno Programa ZEEMS nian iha Oecusse	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Oe-cusse	Oe-cusse	Lifau Indah	0000	$ 194,924.39	Jan. 1, 2016	0.00%	0.00%	$ -	$ 194,924.39	on going
211	Installation New MV Line , Transformer & Extend LV Line and New Distribution Line from Nitib Tuan Oel Tam to nitib Tuan Oecusse District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Oe-cusse	Oe-cusse	Manekat Unip. Lda	RDTL/MOP-SEE/CGI-PEN:0000256	$ 320,740.08	Aug. 15, 2014	98.44%	88.59%	$ 284,157.37	$ 36,582.71	on going
212	New Installation of Under Ground Cable MV Line From Malelat To Pasabe- Oecusse Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Oe-cusse	Oe-cusse	Maubere Spirit	RDTL/MOPTC-VOMPTC/CGI-PEN:0000454	$ 177,484.78	March 13, 2017	46.49%	41.84%	$ 74,255.33	$ 103,229.45	on going

213	Construção Posto Militar F-FDTL Pante Makasar	MINISTERIO DA DEFESA	FI	SEGURANCA NO DEFESA		Oe-cusse	Oe-cusse	Ervel Unip.Lda	NCB/004/MDS-2015	$ 1,660,172.40	Feb. 8, 2015	100.00%	90.00%	$ 1,494,155.15	$ 166,017.25	PHO
214	Detailed Engineering Design (DED) of Dili Water Supply	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		Nasional	Dili	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOP-2019	$ 2,718,150.00	Jan. 30, 2020	46.85%	46.85%	1,273,324.46	$ 1,444,825.54	on going
215	Detailed Engineering Design (DED) of Dili Sanitation and Drainage Master Plan-Phase II	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		Nasional	Dili	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	SSS/035/MOPTC-2017	$ 1,057,882.00	Sept. 17, 2017	85.00%	77.32%	$ 817,902.22	$ 239,979.78	PHO
216	Feasibility Study of Surface Water Resource Development for the Water Supply of Dili Metropolitan Area	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		Nasional	Dili	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/002/MOP-2019	$ 459,600.00	Aug. 22, 2019	50.00%	47.50%	218,310.00	$ 241,290.00	on going
217	Pre- Feasibility Study of a Ground Water Resources Development Project for the Water Supply of Dili Metropolitan Area	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		Nasional	Dili	TEAM Consulting Engineering and Management PCL, Thailand in JV with ATT Consultants Company limited, Thailand and in association with CQ2 Engineering Consultancy & Diverso Unipessoal Lda, Timor-Leste	RFP/001/MOP-2019	$ 341,500.00	July 10, 2019	65.00%	61.75%	$ 210,876.25	$ 130,623.75	on going
218	Rehabilitasaun Sistema Be,e Mos Iha Iahane Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		Nasional	Dili	Sicola	SSS/018/MOP-2021	$ 76,750.31	June 12, 2020	73.26%	64.47%	49,482.23	$ 27,268.08	on going
219	Financial Advisory Services Agreement between the Government of Timor - Leste and International Finance Corporation on Development of Presidente Nicolau Lobato Internasional Airport - Airport PPP Project	MINISTERIO FINANCAS	FI	AEROPORTOS	Nacional	Nasional	Dili	International Finance Corporation	604869	$ 1,100,000.00	Feb. 24, 2020	54.55%	54.55%	$ 600,000.00	$ 500,000.00	on going
220	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO		Nasional	Dili	Sinohidro corporation limited	ICB/07/MPW-2014	$ 48,314,975.87	March 3, 2016	82.44%	74.20%	$ 35,849,928.14	$ 12,465,047.73	on going
221	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS		Nasional	Dili	Lonacca Unipessoal Lda	MPW-W-190177	$ 116,902.51	Nov. 13, 2019	100.00%	90.00%	105,212.26	$ 11,690.25	PHO
222	For Preparation of Detailled Engineering and Bid Preparations for New Bridges in 2019 Package 1 Samalari, Sana Uatolari-Laisorulai, Sumaco (Laciuta Uma Tolu), Malos Matadoro-RTK, Comoro Motaulun	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS		Nasional	Dili	Vox Da Vinci Consultant Engineering Lda	RDTL	$ 579,908.00	March 25, 2020	70.00%	70.00%	$ 405,935.60	$ 173,972.40	on going
223	Consulting Services for preparing of design the intersection in the existing Dili Liquixa Road to connect access Road From Tibar Bay Port (Preparasaun Desenho detalhado ba Estrada, Electricidade e Aguas ba Funcionamentu Portu Tibar)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Nasional	Dili	TPF Consultores de Engenharia S.A (Portugal) JV with TPF Timor Unip Lda, (Timor-Leste)	RFP/009/MOP-2019	$ 244,775.00	Nov. 30, 2019	100.00%	95.00%	$ 232,536.27	$ 12,238.73	PHO
224	Selection of Design Consultant to Prepare Preliminary Design and Tender Documents for the Upgradition of Liquica 150 KV/20KV Substation to Supply Power to Tibar Bay Port	MINISTERIO DAS OBRAS PUBLICAS	FI	PREPARASAUN DESENHOS NO SUPERVISAUN - NOVOS PROJECTOS		Nasional	Dili	PT. Malmass Mitra Teknik (Indonesia)	RFP/041/MOP-2019	$ 322,800.00	March 2, 2020	90.00%	85.50%	$ 275,994.00	$ 46,806.00	on going
225	Zebra Cross Marking in The Capital City of Dili (162)	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-BS	ESTRADAS		Nasional	Dili	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	$ 68,526.00	Oct. 8, 2019	75.59%	68.03%	$ 46,620.00	$ 21,906.00	on going
226	Additional Service Statement of Work for Year 2021 - Government Resource Planning Solutions & Supporting IT Infrastructure System Implementation & Support Agreement	MINISTERIO FINANCAS	FI	SISTEMA FINANCEIROS E SUPORTAS INFRAESTRUTURAS		Nasional	Dili	Freebalance	RDTL-167250	$ 3,106,435.00	July 5, 2010	79.40%	79.40%	2,466,564.84	$ 639,870.16	on going
227	Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project	MINISTERIO DAS OBRAS PUBLICAS	FI	AGUA E SANEAMENTO		Nasional	Nacional	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	RFP/039/MOP-2019	$ 2,903,356.59	Jan. 16, 2020	53.44%	50.77%	1,473,965.57	$ 1,429,391.02	on going
228	Estudos e plano de concepção para Planeamento Urbano a nível nacional	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	FI	DESENVOLVIMENTO URBANO E RURAL		Nasional	Nacional	Intersisment S.A in Joint Venture with Quetemaire Portugal Consultoria para o Desenvolvimento. SA	RFP/025/MPW-2013	$ 1,219,755.75	Sept. 12, 2014	70.00%	66.50%	$ 811,137.56	$ 408,618.19	on going
229	Plano Lidar e Mapeamento a todo o territorio, segunda fase	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	FI	DESENVOLVIMENTO URBANO E RURAL		Nasional	Nacional	PT. Karvak Nusa Geomatika, Indonesia	SSS/006/MPIE-2016	$ 22,631,012.85	Aug. 23, 2016	73.25%	73.25%	$ 16,578,048.96	$ 6,052,963.89	on going
230	Supply, Installation, Configuration and Comissioning of National Optical Fiber Backbone Network	GABINETE DO PRIMEIRO MINISTRO	FI	EQUIPAMENTO INFROMATICO		Nasional	Nacional	Timor Telecom S.A.	RT/024/GPM-2017	$ 1,877,556.74	Nov. 15, 2017	94.59%	94.59%	$ 1,776,017.73	$ 101,539.01	PHO
231	Supply, Installation, Configuration and Comissioning of Hardware and Software for the Expantion of Data Center Infrastructure | Office of Prime Minister	GABINETE DO PRIMEIRO MINISTRO	FI	EQUIPAMENTO INFROMATICO		Nasional	Nacional	Joint Venture of CMC System Integration Company Limmited and Viettel Timor-Leste Unipessoal, LDA	ICB/025/GPM-2017	$ 1,485,698.00	Feb. 15, 2018	88.70%	88.70%	$ 1,317,823.63	$ 167,874.37	PHO
232	Road Network Upgrading Project (RNUP),Upgrading and Maintenance of Dili (Airport Junction)- Tibar Road-Section 2 : Tasitolu - Tibar	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA-IMPRESTIMO		Nasional	Nacional	CINA WU YI CO.LTD	ICB/032/MPWTC-2015	$ 12,964,487.49	Sept. 14, 2016	92.80%	83.52%	$ 10,828,352.80	$ 2,136,134.69	on going

233	Operation And Maintenance Services For National Power Grid Project	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Nasional	Nacional	China Nuclear Industry 22ND Construction Co; LTD	La mensiona iha Kontracto	$ 46,872,339.00	July 15, 2016	66.63%	63.33%	$ 29,682,899.05	$ 17,189,439.95	on going
234	Revitalization foot Ball Stadium and tribune Building	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	JUVENTUDE NO DESPORTU	Dili	Nasional	Dili	Marino enterprises Lda		$ 1,938,481.77	Dec. 31, 2017	53.05%	47.75%	$ 925,534.68	$ 1,012,947.09	abandon
235	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nacional	Nasional	Dili	Shangai Construction Group Co.,Ltd		$ 59,287,453.57	Aug. 18, 2016	84.82%	76.34%	$ 45,258,631.13	$ 14,028,822.44	on going
236	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nacional	Nasional	Dili	CBMI Construction Co. Lda Jv Chongqing Roads Engineering		$ 29,315,346.10	Dec. 11, 2016	65.93%	61.59%	18,054,390.28	$ 11,260,955.82	on going
237	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Regional	Nasional	Dili	CBMI Construction Co. Lda Jv Chongqing Roads Engineering		$ 20,748,566.21	Nov. 21, 2016	70.44%	66.39%	$ 13,773,957.09	$ 6,974,609.12	on going
238	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Nacional	Nasional	Dili	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		$ 7,693,101.00	May 3, 2017	75.33%	75.33%	$ 5,795,051.15	$ 1,898,049.85	on going
239	Preparation of Detailed engineering design for Dili Urban Road	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Nacional	Nasional	Dili	KIAT unip.JV PT Purnajasa Binapratama		$ 276,634.00		10.00%	10.00%	27,663.40	$ 248,970.60	on going

240	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Regional	Nasional	Dili	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETILE CONSULTANT, LDA (TIMOR LESTE)		$ 5,262,302.00	April 3, 2019	32.60%	32.60%	1,715,409.90	$ 3,546,892.10	on going
241	Manutensaun ba Edificio no Equipamentu laboratorium dianostika veternaria	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	AGRICULTURA	Dili	Nasional	Nacional	Dreams Come True, Lda	RDTL-PO:2019-15736	$ 69,978.38		97.14%	92.28%	$ 64,579.46	$ 5,398.92	PHO
242	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS		Regional	Regional	Raya Consulting Lda	MPW-CS-2000020	$ 373,666.00	March 25, 2020	70.00%	70.00%	$ 261,565.60	$ 112,100.40	on going
243	Consultant Design (M-L & L-N) & Supervision (D-L & T-G, Tasi Tolu - tibar 4 L)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADA-IMPRESTIMO		Regional	Regional	KATAHIRA & ENGINEERS INTERNATIONAL	time base	$ 8,178,886.44	Dec. 14, 2012	81.13%	81.13%	$ 6,635,478.88	$ 1,543,407.56	on going
244	The Integrated and Maintenance Service	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ELETRIFIKASAUN NASIONAL		Regional	Regional	wartsila Indonesia R.P (Interest Late Payment P.T Warstila Indonesia (RP)	SSS-008-MOPTC-2016	$ 53,025,601.00	March 5, 2017	70.88%	70.88%	$ 37,586,889.12	$ 15,438,711.88	on going

Inspected by :

Eng. Joao do Reno, Eng Eduardo do Santos
Enginheiro ba Projecto Infraestrutura transportes e Irrigasaun
Munisipio Dili A D N IP

Verified by :

Eng. Remigio da C.S.dos Santos
Enginheiro Senior Projecto Infraestrutura transportes e Irrigasaun A D N IP

Inspected by :

Eng Pedro de Lurdes Alves, Eng Manuel Estrela, Eng Julmira Sampaio, Eng Egidio Goncalves, Rosalia de Fatima
Enginheiro Edificio Public, Agua e Saneamento Municipio Dili A D N IP

Verified by :

Arch. Francisco Xavier de D Jeronimo
Enginheiro Senior ba Edificio Public no Agua e Saneamento A D N IP

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de controlu e validacao qualidade ADN.I.P

Inspected by :

Eng Camilo de Jesus
Enjineiru M& E, A D N IP

Verified by :

Eng Deolindo de Fatima Marques
Chefe Sec.Proj. ME & ITC, A D N IP

Anexo C1(CR - 34)
Back-up Data

Naran Projeto : Rehabilitation Construction of Crocodile Cage Hera

No. kontratu : 603 DNRHAL / DGA / SEA -MCAE / IX / 2021

Data Inspesaun : 22 de Abril 2022

Fatin Inspesaun : Dili - Cristo Rei - Hera

Koordinadas :

Start Point : Long : *-8.323906°* Latetude : *125.408652°*

End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Manuel Esterla Soares

2. Rosalia De Fatima

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisik Atingi Ona 77.77%	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisik Atingi Ona 77.77%	

Anexo C1(CR - 34)
Back-up Data

Naran Projeto : Rehabilitation Construction of Crocodile Cage Hera

No. kontratu : 603 DNRHAL / DGA / SEA -MCAE / IX / 2021

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisik Atingi Ona 77.77%	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisik Atingi Ona 77.77%	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Rehabilitation Construction Of Crocodile Cage Hera

Kompanha : Santana Diak unip.Lda

ANEKSU D (CR - 34)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/04/2022	Municipio Dili/Postu Administrativo Cristo Rei - Hera	Manuel Estrela Soares	Teknik ADN/Edificio e Agua Saneamento	1	Husu atu aselera servisu tuir termo kontratu	
					2	mantein spesifikasaun	
					3	mantein desenho	
					4	atu halo mudansa servisu tenke confirma ho owner no hetan aprovasaun antes executa	
					5		
II			Rosalia de Fatima	Teknik ADN/Edificio e Agua Saneamento	1	Husu atu aselera servisu tuir termo kontratu	
					2	mantein spesifikasaun	
					3	mantein desenho	
					4	atu halo mudansa servisu tenke confirma ho owner no hetan aprovasaun antes executa	
					5		
III					1		
					2		
					3		
					4		
					5		

Contract No.	**: 603 DNRHAL / DGA / SEA -MCAE / IX / 2021**
Contract Name	**: Rehabilitation Construction of Crocodile Cage Hera**
Location	**: Hera , Municipality Dili**
Name of Contractor	**: Santana Diak Unipessoal, Lda**
Date	**:UP TO April 2022**

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2(CR - 34)

SUMMARY BILL OF QUANTITIES

NO	DESKRISAUN	TOTAL FOLIN (US$)	Previous		This-Period		To-Date	
			Amount ($USD)	Weight (%)	Amount ($USD)	Weight (%)	Amount ($USD)	Weight (%)
A	GENERAL REQUIREMENTS	$ 3,875.60	$ 2,030.00	1.70%	$ -	0.00%	$ 2,030.00	1.70%
B	EARTHWORKS	$ 11,129.63	$ 8,251.09	6.90%	$ -	0.00%	$ 8,251.09	6.90%
C	CONCRETE WORK	$ 56,810.67	$ 46,578.52	38.95%	$ -	0.00%	$ 46,578.52	38.95%
D	MASORY WORK	$ 17,641.55	$ 10,094.49	8.44%	$ -	0.00%	$ 10,094.49	8.44%
E	PAINTING	$ 4,165.50	$ -	0.00%	$ 4,165.50	3.48%	$ 4,165.50	3.48%
F	Fance	$ 6,461.13	$ 6,461.13	5.40%	$ -	0.00%	$ 6,461.13	5.40%
G	PLUMBING AND SANITARY	$ 681.34	$ 681.34	0.57%	$ -	0.00%	$ 681.34	0.57%
H	ELECTRICAL WORK	$ 3,424.74	$ -	0.00%	$ 3,424.74	2.86%	$ 3,424.74	2.86%
I	**TOTAL**	**$ 104,190.16**	**$ 74,096.56**	61.96%	**$ 7,590.24**	6.35%	**$ 81,686.80**	68.31%
II	**Contractor Fee (10% x I)**	**$ 10,419.02**	**$ 7,409.66**	6.20%	**$ 759.02**	0.63%	**$ 8,168.68**	6.83%
III	**Ovrehead**	**$ 2,625.00**	**$ 1,312.50**	1.10%	**$ -**	0.00%	**$ 1,312.50**	1.10%
IV	**Taxa (2% x (I + II + III))**	**$ 2,344.68**	**$ 1,656.37**	1.39%	**$ 166.99**	0.14%	**$ 1,823.36**	1.52%
V	**Contigencia**	**$ -**	**$ -**		**$ -**		**$ -**	0.00%
VI	**GRAND TOTAL (I + II + III + IV)**	**$ 119,578.86**	**$ 84,475.09**	70.64%	**$ 8,516.25**	7.12%	**$ 92,991.34**	77.77%

DILI,22 April 2022
Inspection By :

Manuel Estrela Soares
Engineer of ADN, I.P.

Verified by :

Arch. Fransisco Xavier de Deus Jeronimo
Senior Eng Ba Projeito Edificio Publico e Agua Saneamento-ADN, I.P.

Dili,...../...../ 2022
Certified by :

Eng.Emerenciana da Costa Maia
Coord da Unidade de Controlo e Valide de QualidadeADN, I.P

Anexo C1 (VR-21)
Back-up Data

Naran Projeto : New Construction Of Administration And Logistic Building

No. kontratu : /NCB/006/UNTL/VII/2019
Data Inspesaun : 26 De Abril 2022

Fatin Inspesaun : Dili – Vera Cruz - Caicoli

Koordinadas :

Start Point : Long : ***-8.556149°*** Latetude : ***125°579293***

End Point : Long : ....., Latetude : .....

Naran Inspector : 1.Manuel Estrela Soares de Oliveira

2. Rosalia De Fatima

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisiko Ate Agora : 98.73%	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisiko Ate Agora : 98.73%	

Anexo C1 (VR-21)
Back-up Data

Naran Projeto : New Construction Of Administration And Logistic Building

No. kontratu : /NCB/006/UNTL/VII/2019

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisiko Ate Agora : 98.73%	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Progress Fisiko Ate Agora : 98.73%	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Construction of Administration and Logistic Building

Kompanha : Aitula Unip,Lda

ANEKSU D (VR 21)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/05/2022	Municipio Dili/Postu Administrativo Vera-Cruz	Manuel Estrela Soares	Teknik ADN/Edificio e Agua Saneamento	1	Husu atu aselera servisu tuir termo kontratu	
					2	mantein spesifikasaun	
					3	mantein desenho	
					4	atu halo mudansa servisu tenke confirma ho owner no hetan aprovasaun antes executa	
					5		
II			Rosalia de Fatima	Teknik ADN/Edificio e Agua Saneamento	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

NAME OF PROJECT : New Construction of Administration & Logistic Building

LOCATION : Caicoli,Dili Timor Leste

PROJECT OWNER : Universidade Nacional Timor Lorosae (UNTL)

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEKSU C2 (VR 21)

SUMMARY

NO	DESCRIPTION	Original Contract		Previous		This-Period		To-Date	
		TOTAL	Weight (%)	Amount ($USD)	Weight (%)	Amount ($USD)	Weight (%)	Amount ($USD)	Weight (%)
I	PRELIMINARIES	$ 7,775.00	1.15%	$ 6,858.00	1.01%	$ 917.00	0.14%	$ 7,775.00	1.146%
II	SITE WORK	$ 3,000.41	0.44%	$ 3,000.41	0.44%	$ -	0.00%	$ 3,000.41	0.442%
III.	GROUND WORK	$ 12,025.36	1.77%	$ 12,025.36	1.77%	$ -	0.00%	$ 12,025.36	1.773%
IV	MASONRY WORK	$ 49,343.03	7.28%	$ 49,343.03	7.28%	$ -	0.00%	$ 49,343.03	7.275%
V	REINFORCED CONCRETE	$ 307,503.05	45.34%	$ 307,503.05	45.34%	$ -	0.00%	$ 307,503.05	45.340%
VI.	FLOORING WORK	$ 59,917.02	8.83%	$ 59,917.02	8.83%	$ -	0.00%	$ 59,917.02	8.834%
VII.	PAINTING WORK	$ 21,355.52	3.15%	$ 21,355.52	3.15%	$ -	0.00%	$ 21,355.52	3.149%
VIII.	ROOFING AND STEEL TRUSSES WORKING	$ 12,285.00	1.81%	$ 12,285.00	1.81%	$ -	0.00%	$ 12,285.00	1.811%
IX	CELING WORK	$ 27,780.78	4.10%	$ 27,780.78	4.10%	$ -	0.00%	$ 27,780.78	4.096%
X	DOOR & WINDOW	$ 28,748.57	4.24%	$ 28,748.57	4.24%	$ -	0.00%	$ 28,748.57	4.239%
XI	PLUMBING	$ 19,990.77	2.95%	$ 11,187.20	1.65%	$ 8,803.57	1.30%	$ 19,990.77	2.948%
XII	ELECTRICAL INSTALLATION	$ 43,206.14	6.37%	$ -	0.00%	$ 43,206.14	6.37%	$ 43,206.14	6.371%
A	**Total Construction**	**$ 592,930.64**	**87.42%**	**$ 540,003.93**	**79.62%**	**$ 52,926.70**	**7.80%**	**$ 592,930.64**	**87.425%**
B	**Contractor Fee (10%)**	**$ 59,293.06**	**8.74%**	**$ 54,000.39**	**7.96%**	**$ 5,292.67**	**0.78%**	**$ 59,293.06**	**8.742%**
C	**Overhead**	**$ 11,900.00**	**1.75%**	**$ 4,250.00**	**0.63%**	**$ -**	**0.00%**	**$ 4,250.00**	**0.627%**
D	**Tax 2%**	**$ 13,282.47**	**1.96%**	**$ 11,965.09**	**1.76%**	**$ 1,164.39**	**0.17%**	**$ 13,129.47**	**1.936%**
E	**GRAND TOTAL**	**$ 678,218.04**	**100.00%**	**$ 610,219.41**	**89.97%**	**$ 59,383.76**	**8.76%**	**$ 669,603.18**	**98.73%**

DILI,26 Abril 2022
Inspection By ;

Manuel Estrela Soares
Engineer of ADN, I.P.

Verified by :

Eng. Fransisco Xavier de Deus Jeronimo
Senior Eng Ba Projeito Edificio Publico e Agua Saneamento-ADN, I.P.

Dili,...../...../ 2022
Certified by :

Eng.Emerenciana da Costa Maia
Coord da Unidade de Controlo e Valide de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

NAME OF PROJECT : New Construction of Isolation for Covid 19 in
AtauroLOCATION : Dili-Atauro
PROJECT OWNER : Ministry of Health

ANEKSU C2 (AT 03)

SUMMARY

NO	DESCRIPTION	Original Contract		Previous		This-Period		To-Date	
		TOTAL	Weight (%)	Amount ($USD)	Weight (%)	Amount ($USD)	Weight (%)	Amount ($USD)	Weight (%)
I	PREPARATION WORK	$ 8,795.97	2.90%	$ 8,795.98	2.90%	$ -	0.00%	$ 8,795.98	2.90%
II	FOUDATION WORKS	$ 2,114.62	0.70%	$ 2,114.66	0.70%	$ -	0.00%	$ 2,114.66	0.70%
III	CONCRETE WOEKS	$ 48,048.68	15.85%	$ 48,048.37	15.85%	$ -	0.00%	$ 48,048.37	15.85%
VI	WALL INSTALLATION AND PLESTERING	$ 34,681.37	11.44%	$ 34,681.37	11.44%	$ -	0.00%	$ 34,681.37	11.44%
V	CARPENTER WORKS	$ 14,188.72	4.68%	$ 14,188.72	4.68%	$ -	0.00%	$ 14,188.72	4.68%
VI	ROOFING WORKS	$ 35,034.52	11.56%	$ 35,034.52	11.56%	$ -	0.00%	$ 35,034.52	11.56%
VII	CEILING WORKS	$ 11,387.87	3.76%	$ 11,387.87	3.76%	$ -	0.00%	$ 11,387.87	3.76%
VIII	FLOOR TILE WORKS	$ 20,721.57	6.84%	$ 20,721.57	6.84%	$ -	0.00%	$ 20,721.57	6.84%
IX	ELECTRICAL WORKS	$ 24,436.19	8.06%	$ -	0.00%	$ 24,436.19	8.06%	$ 24,436.19	8.06%
X	SANITASI WORKS	$ 16,515.76	5.45%	$ 15,622.19	5.15%	$ -	0.00%	$ 15,622.19	5.15%
XI	PAINTING WORKS	$ 9,238.74	3.05%	$ 9,238.74	3.05%	$ -	0.00%	$ 9,238.74	3.05%
XII	FURNITURE	$ 14,475.00	4.77%	$ -	0.00%	$ -	0.00%	$ -	0.00%
XIII	PROVISIONAL SUM FOR EXTERNAL WORK	$ 3,750.00		$ -	0.00%	$ -	0.00%	$ -	0.00%
XIV	FINAL CLEARING	$ 500.00	0.16%	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**$ 243,889.01**	80.45%	**$ 199,833.99**	65.92%	**$ 24,436.19**	8.06%	$ 224,270.18	73.98%
B	**PROFIT (10% X A)**	**$ 24,388.90**	8.05%	**$ 19,983.40**	6.59%	**$ 2,443.62**	0.81%	$ 22,427.02	7.40%
C	**OVERHEAD**	**$ 4,900.00**	1.62%	**$ 3,450.00**	1.14%	**$ -**	0.00%	$ 3,450.00	1.14%
D	**TAX (2% X (A+B+C))**	**$ 5,463.56**	1.80%	**$ 4,465.35**	1.47%	**$ 537.60**	0.18%	$ 5,002.94	1.65%
E	**CONTIGENCY 7 % OF CONSTRUCTION COST**	**$ 24,500.00**	8.08%	**$ -**	0.00%	**$ -**	0.00%	$ -	0.00%
F	**GRAND TOTAL (A+B+C+D+E)**	**$ 303,141.47**	100.00%	**$ 227,732.73**	75.12%	**$ 27,417.40**	9.04%	$ 255,150.14	84.17%

DILI,08 Abril 2022
Inspection By ;

Manuel Estrela Soares
Engineer of ADN, I.P.

Verified by :

Eng. Francisco Xavier de Deus Jeronimo
Senior Eng Ba Projeito Edifício Publico e Agua Saneamento-ADN, I.P.

Dili,...../...../ 2021
Certified by :

Eng.Emerenciana da Costa Maia
Coord da Unidade de Controlo e Valide de QualidadeADN, I.P

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Construction of Isolation for Covid 19 in Atauro

Kompanha : Lygelina Alexix Unip,Lda

ANEKSU D (AT 03)


No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/5/2022	Municipio Dili/Postu Administrativo Ataoru	Manuel Estrela Soares	Teknik ADN/Edificio e Agua Saneamento	1	Persija aslera servisu hodi termina tuir contrato	
					2	Persija aumenta badain hodi aslera servisu	
					3		
					4		
					5		
II			Silvino D Rita Rebelo Soares	Teknik ADN/M & E	1	Persija aslera servisu hodi termina tuir contrato	
					2	Persija aumenta badain hodi aslera servisu	
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

ANEXO C1 (CR 23)

Back-Up Data Quantity Sketch

NAME OF PROJECT : **RM Pecas Sofremento Pagamento Be,e Mos (Loket Pagamento/Billing System)**
LOCATION : **Komoro-Dili Timor Leste**
PROJECT OWNER : **Ministerio das Obras Publicas**
Data Inspesaun : **15-04-2022**
Naran inspector : **Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point) : **-8.555432°**
Longitude (Starting Point) : **125.539323°**

Foto Actividades Iha Tereno Actual

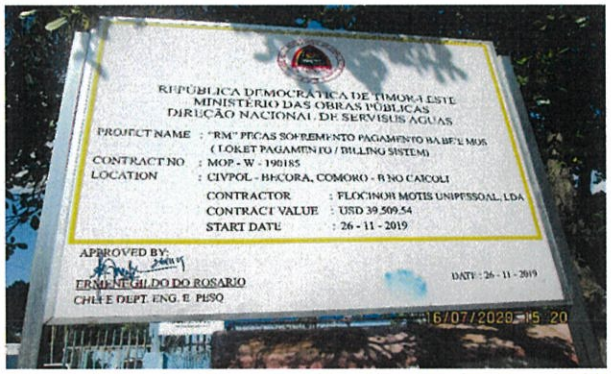





Skecth & Foto Desenho

Progresu fisik iha tereno atinji ona 100%..,Maibe tamba sidauk iha justifikasaun husi parte dono de projeito sobre (Provisional (phisical/material contingencies) sum (uza orsamentu nee tuir instrusaun husi DAA DNSA no approvasaun husi Corporate Service) hodi sosa material nebe la identifika iha kontratu nee).

ANEXO C1 (CR 15)

Back-Up Data Quantity Sketch

NAME OF PROJECT : **Konstrusaun Moru Hadulas Bomba Fumento**
LOCATION : **Komoro-Dili Timor Leste**
PROJECT OWNER : **Ministerio das Obras Publicas**
Data Inspesaun : **15-04-2022**
Naran inspector : **Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point) : **-8.560283°**
Longitude (Starting Point) : **125.538323°**

Foto Actividades Iha Tereno Actual







Skecth & Foto Desenho

Progresu fisik iha tereno atinji ona 100%..,Maibe tamba sidauk iha justifikasaun husi parte dono de projeito sobre (Provisional (phisical/material contingencies) sum (uza orsamentu nee tuir instrusaun husi DAA DNSA no approvasaun husi Corporate Service) hodi sosa material nebe la identifika iha kontratu nee).

ANEXO C1 (CR-01)

Back-Up Data Quantity Sketch

NAME OF PROJECT : **Rehabilitation Intake Transmission of Water Pipeline and Sanitationat Lakoto**
LOCATION : **Lakoto-Mutudare-Dili Timor Leste**
PROJECT OWNER : **Ministerio das Obras Publicas**
Data Inspesaun : **29-05-2022**
Naran inspector : **Manuel Estrela Soares de Oliveira**
Latitude (Starting Point) : **-8.589233°**
Longitude (Starting Point) : **125.594592°**

Foto Actividades Iha Tereno Actual







Skecth & Foto Desenho

Observasaun ou komentario seluk : (1) Hein Pagamento Retensaun 10% ba Companhia

ANEXO C1 (MTN 03)

Back-Up Data Quantity Sketch

NAME OF PROJECT : **Melhoramento Tratamento Dezalinasaun iha Manleu-Metinaro**
LOCATION : **Metinaro,Dili-Timor Leste**
PROJECT OWNER : **Ministerio das Obras Publicas (BTL,E.P.)**
Data Inspesaun : **03-05-2022**
Naran inspector : **Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point) : **-8.490705°**
Longitude (Starting Point) : **125.823707°**

Foto Actividades Iha Tereno Actual





Skecth & Foto Desenho

Progresu fisik iha tereno atinji ona 100%..,Maibe tamba sidauk iha justifikasaun husi parte dono de projeito sobre (Provisional (phisical/material contingencies) sum (uza orsamentu nee tuir instrusaun husi DAA DNSA no approvasaun husi Corporate Service) hodi sosa material nebe la identifika iha kontratu nee).

ANEXO C1 (DA 53)

Back-Up Data Quantity Sketch

NAME OF PROJECT	**: Rehabilitasaun Edifisiu Dormitoriu Instituto Nasional de Saude (INS)**
LOCATION	**: Comoro-Dili Timor Leste**
PROJECT OWNER	**: Ministerio Saude**
Data Inspesaun	**: 22-05-2022**
Naran inspector	**: Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point)	**: -8.3336789°**
Longitude (Starting Point)	**: 125.314691°**

Foto Actividades Iha Tereno Actual







Observasaun ou komentario seluk

Baseia ba inspeksaun tekniku ADN Progresu fisiku ba projectu refere iha terrenu atinji ona 100 %,Maibe sidauk halo CCO ba ba item servisu nebe iha mudansa iha tereno ho nune husi parte teknik ADN sidauk konsidera pagamento ba 100% ba companhia hein husi parte dono de projeito atu halo back_Up data item sira nebe iha mudansa.

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Rehabilitasaun Edifício Dormitoriu Instituto Nasional da saude

Kompanha : Grandis Unip,Lda

ANEKSU D (DA-53)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/05/2022	Municipio Dili/Postu Administrativo Vera-Cruz	Manuel Estrela Soares	Teknik ADN/Edificio e Agua Saneamento	1	Husu atu aselera servisu tuir termo kontratu	
					2	mantein spesifikasaun	
					3	mantein desenho	
					4	atu halo mudansa servisu tenke confirma ho owner no hetan aprovasaun antes executa	
					5		
II			Rosalia de Fatima	Teknik ADN/Edificio e Agua Saneamento	1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		

ANEXO C1 (DA 28)

Back-Up Data Quantity Sketch

NAME OF PROJECT : **Perfurasaun Sistema Be,e Mos iha Area Comoro**
LOCATION : **Comoro,Dili-Timor Leste**
PROJECT OWNER : **Ministerio das Obras Publicas (BTL.E.P.)**
Data Inspesaun : **22-05-2022**
Naran inspector : **Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point) : **-8.555633°**
Longitude (Starting Point) : **125.532882°**

Foto Actividades Iha Tereno Actual







Skecth & Foto Desenho

Progresu fisik iha tereno atinji ona 100%..,Maibe tamba sidauk iha justifikasaun husi parte dono de projeito sobre (Provisional (phisical/material contingencies) sum (uza orsamentu nee tuir instrusaun husi DAA DNSA no approvasaun husi Corporate Service) hodi sosa material nebe la identifika iha kontratu nee).

ANEXO C1 (DA 02)

Back-Up Data Quantity Sketch

NAME OF PROJECT	**: Melhoramente Sistema Be,e Mos iha maloa Dili Municipality**
LOCATION	**: Dare/Lemo-Nara Dili Timor-Leste**
PROJECT OWNER	**: Ministerio das Obras Publicas**
Data Inspesaun	**: 20-05-2022**
Naran inspector	**: Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point)	**: -8.574853°**
Longitude (Starting Point)	**: 125.565312°**

Foto Actividades Iha Tereno Actual







Skecth & Foto Desenho

Relasiona ho Prosesu Implementasaun Projeto Melhoramente Sistema Be,e Mos iha maloa Dili Municipality. Projeto refere finalija ona husi companhia,maibe iha Prosesu Pagamento ba companhia refere sidauk bele halo tamba persija atu halo verefikasaun Preco Unitario ba item Provisional Sum (*Provisional (phisical/material contingencies) sum (uza orsamentu ne'e tuir instrusaun husi DAA DNSA no approvasaun husi Corporate Service) hodi sosa material nebe la identifika iha kontratu nee*). Ne,be sidauk hetan verifikasun Preo Unitario husi Parte *Unidade de Avaliacao de Projectos.*,molok atu prosesu pagamentu ba companhia

ANEXO C1 (VR 33)

Back-Up Data Quantity Sketch

NAME OF PROJECT	**: New Construction of Isolation (OPD) Vera_Cruz**
LOCATION	**: Caicoli-Dili Timor Leste**
PROJECT OWNER	**: M.S**
Data Inspesaun	**: 27-02-2022**
Naran inspector	**: Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point)	**: -8.562792°**
Longitude (Starting Point)	**: 125.574126°**

Foto Actividades Iha Tereno Actual





Skecth & Foto Desenho

Progresu fisik iha tereno atinji ona 100%..,Maibe tamba sidauk iha justifikasaun husi parte dono de projeito sobre (Provisional (phisical/material contingencies)

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : New Construction of isolation (OPD) Vera cruz relation of covid 19

Kompanha : Romante Pty. Ltd

ANEKSU D (VR-33)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	21/02/2022	Municipio Dili/Postu AdministrativoVera_Cruz	Manuel Estrela Soares	Teknik ADN/Edificio e Agua Saneamento	1	Mudansa dezenho iha site persisa hetan aprovasaun husi owner	
					2	Anexo AS built drawing wainhira submete pagamento 100%	
					3	Sei hein justifikasaun ba osan contigency	
					4		
					5		
II				Teknik ADN/M & E	1	Mudansa dezenho iha site persisa hetan aprovasaun husi owner	
					2	Anexo AS built drawing wainhira submete pagamento 100%	
					3	Sei hein justifikasaun ba osan contigency	
					4		
					5		
III				Teknik ADN/Edificio e Agua Saneamento	1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		

ANEXO C1 (VR 36)

Back-Up Data Quantity Sketch

NAME OF PROJECT : **New Construction Drainage Centro Nacional Chega I.P.**
LOCATION : **Balide,Dili-Timor Leste**
PROJECT OWNER : **Centro Nacional Chega I.P**
Data Inspesaun : **19-05-2022**
Naran inspector : **Manuel Estrela Soares de Oliveira,Rosalia de Fatima**
Latitude (Starting Point) : **-8.5654374°**
Longitude (Starting Point) : **125.577724°**

Foto Actividades Iha Tereno Actual







Skecth & Foto Desenho

Observasaun ou komentario seluk : Sidauk iha Quantidade nebe aumenta iha tereno hodi kompleta balansu osan nebe sei iha

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPEKSAUN

Naran Eng.	Manuel Estrela Soares,Rosalia de Fatima
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria		Dono do Projeto		Remark's
Atauro	2	New Construction of Laboratory for Covid-19 in Atauro	Fitun Galilea Unipessoal Lda	No: /NCB/M.S/DNA/RBK-20-160	LM		MS	Plan	F.H.O
								Actual	
Atauro	3	New Construction of Isolation for Covid-19 in Atauro	Lygelina Alexix Unip. Lda	No: /NCB/M.S/DNA/DC-20-161	LM	✓	MS	Plan	Fisik Iha Tereno 100%
								Actual	
Cristo Rei	1	Rehabilitasaun intake no kanu transmisaun iha La Koto & Mutu Dare	Amigo Unip. Lda	SSS/021/MOP-2020	LM	✓	MOP	Plan	P.H.O
								Actual	
Cristo Rei	14	Konstrusaun Moru Hadulas Bomba Bidau /162	SARCADEFAT Unip.Lda	MOP-W-190164	LM		MOP	Plan	Fisik iha Tereno 100%,Hein Pagamento
								Actual	
Cristo Rei	15	Konstrusaun Moru Hadulas Bomba fomentu /162	H FOUN Unip.Lda	MOP-W-190189	LM	✓	MOP	Plan	
								Actual	
Cristo Rei	19	Rehabilitasaun & Extensaun Laboratorio Nacional Bidau - Dili	Talamori	RDTL-MS-LNS-RFQ-17-064	LM		HNGV	Plan	F.H.O
								Actual	
Cristo Rei	20	Escola Secundaria Tekniko Vocasional 28 de Novembru iha Becora	Dirbajudi	RDTL RCB/01-R/ME-DNA/REHAB	LM		ME	Plan	Abandona
								Actual	
Cristo Rei	23	RM Pecas Sofremento pagamento Bee Mos	Flocinob Motis Unip Lda	MOP/W-190185	LM	✓	MOP	Plan	Fisik Iha Tereno 100%,Hein Pagamento
								Actual	
Cristo Rei	34	Rehabilitation Construction Of Crocodile Cage Hera	Santana Diak Unipessoal Lda	603 DNEHAL/DGA/SEA-MCAE/IX/2021	FI	✓	LM - BS	Plan	
								Actual	
Cristo Rei	18	Konstrusaun Igreza Sagrada Corasaun de Jesus Becora	Carya Timor Leste Lda	transferencia publica	LM		GABINETE DO PRIMEIRO MINISTRO	Plan	Tengki konfirma ho dono de projeito sobre pagamento ba companhia
								Actual	
Cristo Rei	24	Rehabilitation of Medicine Laboratorium in Lahane	Nevan Construction Unip Lda	012/UNTL/EXT/C/2016	LM		UNTL	Plan	F.H.O
								Actual	
Dom aleixo	1	Instalasaun baixada electricidade, instalasaun kanu transmisaun & lutu hadulas estasaun bomba Tuana Laran	Montez Frere Unip. Lda	MJ-046/Junho 2021	FI		MOP	Plan	P.H.O
								Actual	
Dom aleixo	2	Melhoramento kanu transmisaun no distribuisaun iha Maloa	Haksolok Java Motor Unip Lda	No: 214/MACLN/X/2021	FI	✓	MOP	Plan	Fisik Iha Tereno 100%,Hein Pagamento 100%
								Actual	
Dom aleixo	25	Melhoramento Sistema Beé mos iha Area Delta 1,2,3 no 4	Carisma	MPWTC-NCB-170020	LM		MOP	Plan	Fisik Iha Tereno 100%,Hein Pagamento 100%
								Actual	
Dom aleixo	26	Rehabilitasaun no Installasaun Metro Contador Sistema Be'e mos iha Perumnas Bairo Pite (162)	Sos Alssonix	MPWTC-NCB-170024	LM		MOP	Plan	P.H.O
								Actual	
Dom aleixo	27	Urgent Repair of Roof Leaks at the New Building Ministry of	Carya Timor Leste	RDTL-SSS/MOPTC-2017	LM		MOP	Plan	P.H.O

ABRIL

fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPEKSAUN

Naran Eng.	Manuel Estrela Soares,Rosalia de Fatima
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		ABRIL																																				Remark's
								fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa										
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30										
Dom aleixo	27	Finance RDTL	Carya Timor-Leste	RDTL-333/MOP-TC-2017	LM	MOP	Actual																																							
Dom aleixo	28	Perfurasaun Sistema Be'e Mos Iha Area Comoro DMA 37 /162	Domin Timor Diak Lda	RFQ-MOP-190044	LM	MOP	Plan																																							Fisik iha Tereno 100%,Hein Pagamento 100%
							Actual																																						
Dom aleixo	29	Novo construsaun do campo polisportivo do Ministerio das Obras publicas (162)	ATUNEGOS UNIP.LDA	RFQ MOP/-W-190249	LM	MOP	Plan																																							P.H.O
							Actual																																						
Dom aleixo	30	Construction of Terminal in Tasi Tolu	Mar vermelha unip.lda	RDTL-2014-C-101-MTC	LM	MTK	Plan																																							Husi parte dono de projeito hapara tiona kontratu ba companhia refere
							Actual																																						
Dom aleixo	32	Separasaun ba Aula Tolu iha Ministerio da Defesa	Algis	la mensiona nomor iha contratu	LM	MD	Plan																																							P.H.O
							Actual																																						
Dom aleixo	33	Manutensaun Edificio Ministerio da Defesa	Algis	RDTL 11 /MNEC /2019	LM	MD	Plan																																							P.H.O
							Actual																																						
Dom aleixo	34	Manutensaun Residencia C.E.M.G. das F-FDTL	Panca Sekawan	No la mensiona contratu	LM	MD	Plan																																							P.H.O
							Actual																																						
Dom aleixo	36	New Construction of An'Nur Orphanage Building	Asda A3i Unip. Lda.	Transferencia Publica	LM	GM	Plan																																							Tengki konfirma ho dono de projeito sobre pagamento ba companhia
							Actual																																						
Dom aleixo	37	Konstrusaun Escola de Musica iha fatumeta	Talisahe	Transferencia Publica	LM	GM	Plan																																							
							Actual																																						
Dom aleixo	40	Rehabilitasaun and Maintanance of Vice Minister office in Mandarin	Milcha Unip Lda	364/DNA-DGAF-MOP/XII/2019	LM	MOP	Plan																																							P.H.O
							Actual																																						
Dom aleixo	41	Manutensaun Edificio iha Gabinete Ministro nian	Otsop Paris Unip Lda	RDTL-MAP176/GM/VIII/2019	LM	MAP	Plan																																							P.H.O
							Actual																																						
Dom aleixo	43	Konstrusaun Lutu Hadulas WTP Central iha Bairo-Pite Dom Aleixo Municipio Dili /162	Iki Bia-Nunu Unip Lda	NCB/MOP/W-200015	LM	MOP	Plan																																							
							Actual																																						
Dom aleixo	48	Instalasaun Agua Potavel iha Edificio Ministerio da Defesa no QG das F-FTL	CAPTAIN HOOK		LM	MD	Plan																																						
							Actual																																						
Dom aleixo	53	Rehabilitasaun Edificio Dormitoriu INS Comoro-Dili Timor Leste	Grandis	RDTL/INS/Dafa - NCB - 21 -001	LM	MS	Plan																																							
							Actual																																						
Dom aleixo	58	New construction archive werehouse at bebora	Hilobadi Unip,Lda	RDTL/MS - C19 - DNA-NCB-21 -011	LM	MS	Plan																																							
							Actual																																						
Dom aleixo	59	Construsaun de Balcao de atendimento publica para a Direcsaun Geral dos servicos de registos e do Notariado do Ministerio da Justica	Fatuk Mota Construction Unipessoal. Lda	MJ-046/Junho 2021	LM	MJ	Plan																																							
							Actual																																						

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPEKSAUN

Naran Eng.	Manuel Estrela Soares,Rosalia de Fatima
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Remark's
Dom aleixo	60	Manutensaun de salao Nobre	DCO Unip.Lda	No: 214/MACLN/X/2021	LM	MI	Plan	
							Actual	
Dom aleixo	24	Konstrusaun Beé mos ba Residencia Sr. Jeneral F-FDTL no Sr. Lu Olo iha Manleuana	Caileba	MPWTC-502/56/MOPTC/V/2017	LM	MOP	Plan	Tengki konfirma ho Dono Projeito
							Actual	
Dom aleixo	31	Maintenance and Repair at F-FDTL, Head Qaurtel, Fatuhada	Victoria Const. Unip. Lda	2015-000065	LM	MD	Plan	Tengki konfirma ho Dono Projeito
							Actual	
Metinaro	3	Melhoramento taratamento dezalinasaun iha manleu Metinaro /162	Garisiba Unip.Lda	MOP-W-190150	LM	MOP	Plan	Fisik Iha Tereno 100%,Hein Pagamento
							Actual	
Metinaro	4	Construction of Kitchen and Refectory at Componete do Apoio de Serviso (CAS) iha Metinaro	Betuhei	la mensiona nomor iha contratu	LM	MD	Plan	P.H.O
							Actual	
Metinaro	5	New Construction of WareHouse, Campas, Raodway, Drainage and Pavement at Jardim dos Herois Metinaro	Pro Frawijaya	RDTL:44/MSS/DNFALM-DAD/X/2014	LM	MSS	Plan	F.H/O
							Actual	
Metinaro	9	New Construction of Campas and Grass Planting Jardin dos Herois (JHM) Metinaro	LABILAY, Unipessoal, Lda	-	LM	MPACLN	Plan	
							Actual	
Metinaro	10	New Construction Of F-FDTL Fuel Station at Metinaro,Dili	Aitula,Lda	ICB No.05/DNA/MoD/2021	LM	M.D	Plan	Iha tereno Fisik 100%
							Actual	
Nain Feto	1	Rehabilitasaun kanu transmisaun husi Benamauk ba WTP Lahane no Becusse	Lemo Timor Unipessoal Lda	SSS/019/MOP-2020	FI	MOP	Plan	
							Actual	
Nain Feto	3	New Construction of Ojetil Office Building Dili District	Fitun Diak Unip.Lda	SSS/301/MOPTC-2016	FI	MOP	Plan	
							Actual	
Nain Feto	8	Installation of Transmission Line, Distribuition Panel & Transformer in Taibesi and Becora	Nizixavane	MPWTC-W-015072	LM	MOP	Plan	F.H.O
							Actual	
Nain Feto	9	Construction of Membrane Tent and Shaded Area of SG-MOPTC	Voar	MPWTC-W-170020	LM	MOP	Plan	
							Actual	
Nain Feto	11	Rehabilitasaun no manutensaun ex edificio diresaun geral organizasaun urbana	Riri Brothers Unip. Lda.	RDTL,0140/UAD-MAE/XII/2019	LM	MTK	Plan	P.H.O
							Actual	
Nain Feto	12	Rehabilitasaun Edificio Conselho de Empresa	Algis	CI-19-06-C-013	LM	MTCI	Plan	F.H.O
							Actual	
Nain Feto	13	Manutensaun Expert Room iha MESCC	Katuas Patricio	RFQ19/45-Q	LM	MOP	Plan	P.H.O
							Actual	
Nain Feto	14	Rehabilitation of Volley Ball Beach Facilities in Dili-Lecidere	DVD Electric	NCB/01/SSYS-2019	LM	SEJD	Plan	P.H.O
							Actual	
Nain Feto	15	Rehabilitation of GDD Sports Indoors	Victoria Const. Unip. Lda	NCB/02/5595-2019	LM	SEJD	Plan	P.H.O
							Actual	

ABRIL

fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

PLANU INSPEKSAUN

Naran Eng.	Manuel Estrela Soares,Rosalia de Fatima
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Remark's
Nain Feto	16	Rehabilitation and Maintenance of Jardim 12 de Novembro at Motael	Algis	RDTL:47/DNA-MTCI/VII/2019	LM	MTCI	Plan	
							Actual	F.H.O
Nain Feto	17	Rehabilitasaun Residencia Vice Presidente Parlamentu Nacional iha Farol	Celijio Star	PN/4306/2016	LM	PN	Plan	
							Actual	F.H.O
Nain Feto	18	Rehabilitasaun Jardim 12 de Novembro iha Igreza Motael nia oin	Berlosconi	RDTL0144/UADE-MAE/XII/2019	LM	Estatal	Plan	
							Actual	F.H.O
Nain Feto	19	Rehabilitation and Maintenance Building PCM	Panca Sekawan	PCM-20/01-C/0014	LM	MPC	Plan	
							Actual	
Nain Feto	20	Minor Rehabilitasaun of MTC main of Building and Correeios	Risumali Unip Lda	RDTL2019-MTC-GS-0041	LM	MPC	Plan	
							Actual	F.H.O
Nain Feto	21	Rehabilitation of Confrence Room at the office of the Primer Minister, building I, Palacio do Governo,Dili Timor Leste	Gez Unipessoal Lda	RDTL-294/GPM/XI/2019	LM	GPM	Plan	
							Actual	P.H.O
Nain Feto	24	Refurbishment of tenis court facilities, Dili	Algis	NCB/01/SSYS/2021	LM	SEJD	Plan	
							Actual	
Nain Feto	25	aditional for Hospital Dr.Antonio Carvalho Lahane	Hedge Construction, Unip. Lda	RDTL-MS-C19-DNA-DC-21-072	LM	MS	Plan	
							Actual	P.H.O
vera cruz	1	Construction Of New Office Of Tribunal Distrital De Dili	China Shandong International Economic And Technical Cooperation Group. LTD	ICB/008/TR-2019	FI	TR	Plan	
							Actual	
vera cruz	5	Construção Quartel General PNTL em Caicoli	Shangai Construction Group Co.,Ltd	ICB/036/MI-2017	FI	MI	Plan	
							Actual	
vera cruz	15	Manutensaun ba Edificio DNGRA-MOP / 162	Katuas Patricio	RFQ-MOP-190071	LM	MOP	Plan	
							Actual	F.H.O
vera cruz	16	Rehabilitation of DNA MOP Cobe House in Caicoli Dili	Surik Saki Rai Unip.Lda	MOP-W-190167	LM	MOP	Plan	
							Actual	F.H.O
vera cruz	17	Construction of extension office building of the Minister of Public works (162)	CELFA Unip.Lda	RDTL-NCB-MOP-190088	LM	MOP	Plan	
							Actual	P.H.O
vera cruz	19	New Construction of Auditorium (Salaun Paroquial) & Class Room & landscape of Catedral. Vila Verde	Bimavi	transferencia publica	LM	GPM	Plan	
							Actual	F.H.O
vera cruz	20	Construção Pure Hindu Taibesi	Pantarhei	Transferencia Publica	LM	GPM	Plan	
							Actual	
vera cruz	21	New Construction of Administration and Logistic Building	Aitula Construction, Lda	059/C/UNTL/XI/2019	LM	UNTL	Plan	
							Actual	
vera cruz	22	New Construction of Faculidade Econimia e Gesatao Building	Aitula Construction, Lda	057/C/UNTL/X/2019	LM	UNTL	Plan	
							Actual	Iha tereno Fisik 100%

ABRIL

fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

PLANU INSPEKSAUN

Naran Eng.	Manuel Estrela Soares,Rosalia de Fatima
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato		Kategoria	Dono do Projeto		Remark's
vera cruz	23	New Building Construction of Medicina Ciencia da Saude Building	Linier jv Algis	058/C/UNTL/X/2019		LM	UNTL	Plan	P.H.O
								Actual	
vera cruz	24	Konstrusaun Edificio servisu espesializada iha PGR Colmera	Bobolait	RDTL-D.FEO/APRO/PGR/19.002/2019		LM	PGR	Plan	P.H.O
								Actual	
vera cruz	25	Rehabilitation of Houses RTTL in Caicoli and Biterlau	Gaerenez	10/RDTL,E.P/DAF/VI/2019		LM	RTTL	Plan	F.H.O
								Actual	
vera cruz	27	Maintenance of Building for Trade Invest Timor Leste	D'CO	RDTL/TITL/C.06/10/2019		LM	TI	Plan	P.H.O
								Actual	
vera cruz	28	Rehabilitasaun Hospital Dr.Antonio Carvalho Lahane(Building A) Hodi halo Fatin Izolamentu ba Pasienti Covid-19	Hedge Construction, Unip. Lda	NCB/M.S./DNA/DC-20/143		LM	MS	Plan	P.H.O
								Actual	
vera cruz	29	Desenho e Espicificacao de Quantidades BoQ para a ampliacao do Balcao de Atendimento na DNRN	Viros Consultant Unip Lda	RDTL-MJNo.009/MAIO/2019		LM	MJ	Plan	Croos Cek...
								Actual	
vera cruz	30	Rehabilitasaun e Manutensaun Edifisio Armajen DNSA, Dili (Bem Serviso) (162)	BTwo Unip Lda	MOP/W-190186		LM	MOP	Plan	
								Actual	
vera cruz	32	Improvement of Mina Distribuition Pipe in DMA 31 in Suco Mascarenhas	Amigo Unip. Lda	No : /NCB/MPW/W-200016		FI	MOP	Plan	Croos cek...
								Actual	
vera cruz	33	New Construction of isolation (OPD) Vera cruz relation of covid 19	Romante Pty. Ltd	RDTL-MS-C19-DNA-SS-21-001	✓	LM	MS	Plan	Hein jusstifikasaun husi dono de projeito atu uja osan kontijensia
								Actual	
vera cruz	34	New construction Warehouse for centro Nacional Chega I.P	A. L. Unip.Lda	26/CNC/IX/2021	✓	LM	CNC	Plan	
								Actual	
vera cruz	35	Renovation of public Health services at lahane , posto vera cruz Timor Leste	Queson SQ Unipessoal Lda	RDTL-MS-DNA-ICB-21-084		LM	MS	Plan	
								Actual	
vera cruz	36	New Construction Drinage centro Nasional Chega.I.P	Chacailala Unipessoal Lda	27/CNC/IX/2021	✓	LM	CNC	Plan	
								Actual	
vera cruz	37	Criacao de estrutura de parede divisorias do ministerio da justica	Fatuk Mota Construction Unipessoal. Lda	MJ-047/JUNHO/2021		LM	MJ	Plan	
								Actual	
vera cruz	39	Construction of Faculdade de Agricultura Building (B-01)	Dany star	RDTL/039/C/UNTL/XII/2021		LM	UNTL	Plan	
								Actual	
vera cruz	40	Construction of Faculdade de Agricultura Building (B-02)	Hedge Construction, Unip. Lda	RDTL/041/C/UNTL/XII/2021		LM	UNTL	Plan	
								Actual	
vera cruz	41	Construction of Faculdade de Agricultura Building (B-03)	Bobolait	RDTL/040/C/UNTL/XII/2021		LM	UNTL	Plan	
								Actual	
vera cruz	46	Extention Office of Legal and Judicial Training	Behale Entrprice,Unp.Lda	MJ/ICB/04/VIII/2021		LM	M.J	Plan	
								Actual	
Nasional	5	Rehabilitasaun Sistema Be,e Mos Iha lahane Dili Municipality	Sicola	SSS/018/MOP-2021		FI	MOP	Plan	Hein jusstifikasaun

ABRIL

fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPEKSAUN

Naran Eng.	Manuel Estrela Soares,Rosalia de Fatima
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		ABRIL																																Remark's
								fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa		
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30		
							Actual																																husi dono de projeto atu uja osan kontijensia
Nasional	29	Manutensaun ba Edificio no Equipamentu laboratorium dianostika veternaria	Dreams Come True, Lda	RDTL-PO:2019-15736	LM	MAP	Plan																																
							Actual																																
Nasional	21	Revitalization foot Ball Stadium and tribune Building	Marino enterprises Lda	-	LM	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	Plan																																Hapara Kontrato
							Actual																																

Note

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Manuel Estrela Soares de Oliveira)
Eng Municipio-Dili

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coord da Unidade de Controlo e Valide de Qualidade ADN.I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director ADN.I.P.

ANEXO C1 (CR 36)

Back-up Data

Naran Projeto : Konstrusaun Sede Suku Ailok
No. kontratu : 03/KDM/AM-DIL/VIII/2019

Data Inspesaun : Ailok

Fatin Inspesaun : 26/04/2022

Koordinadas :

Start Point : Long :-8.5895 Latetude : 125.6082


End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Pedro de Lourdes Alves

2. .....

3. .....


4. .....

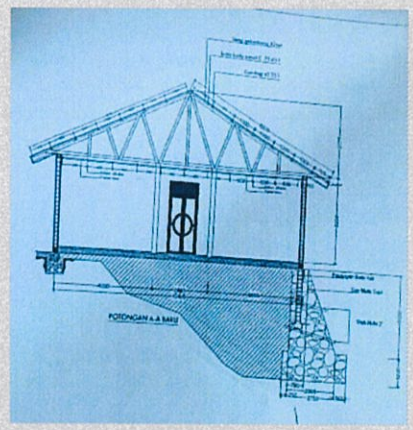Sketch Item Serviso	Observasaun iha tereno no Foto Aktual
Servisu rangka plafon 	

ANEXO C1 (CR 36)

Back-up Data

Naran Projeto : Konstrusaun Sede Suku Ailok
No. kontratu : 03/KDM/AM-DIL/VIII/2019

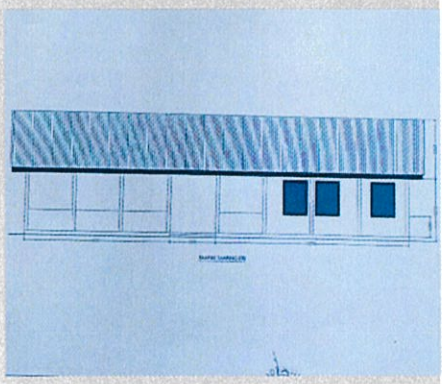Sketch Item Serviso	Observasaun iha tereno no Foto Aktual
Servisu monta kakuluk Vol = 322.40 m2 	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (CR 36)

PROJECT OWNER : AUTORIDADE MUNICIPAL DE DILI
PROJECT TITLE : KONSTRUSAUN SEDE SUCO AILOK
LOCATION : MUNICIPIO DE DILI

No	Item Description	Original Contrac	Aditional	Original Contrac + Adisional	Previews		This Period		Up to Date	
		Total Price (USD)	Total Price (USD)		Amounth	Weigth	Amounth	Weigth	Amounth	Weigth
I	PEKERJAAN PERSIAPAN	$ 906.78		$ 906.78	$ 694.28	1.18%	$ -	0.00%	$ 694.28	1.18%
II	PEKERJAAN TANAH DAN PONDASI	$ -	$ 10,907.06	$ 10,907.06	$ 9,208.00	15.63%	$ 1,699.06	2.88%	$ 10,907.06	18.51%
III	PEKERJAAN DINDING DAN BETON	$ 3,662.67	$ 145.00	$ 3,807.67	$ 3,514.95	5.97%	$ -	0.00%	$ 3,514.95	5.97%
IV	PEKERJAAN LANTAI DAN KERAMIK	$ 7,917.75	$ 2,129.48	$ 10,047.23	$ 1,830.77	3.11%	$ 321.72	0.55%	$ 2,152.49	3.65%
V	PEKERJAAN ATAP	$ 11,035.99		$ 11,035.99	$ 5,816.46	9.87%	$ 3,952.51	6.71%	$ 9,768.97	16.58%
VI	PEKERJAAN PINTU DAN JENDELA	$ 4,872.40		$ 4,872.40	$ 818.10	1.39%	$ -	0.00%	$ 818.10	1.39%
VII	PEKERJAAN PLAFON	$ 4,926.40		$ 4,926.40	$ -	0.00%	$ -	0.00%	$ -	0.00%
VIII	PEKERJAAN INSTALASI LISTRIK	$ 964.62		$ 964.62	$ -	0.00%	$ -	0.00%	$ -	0.00%
IX	PEKERJAAN SANITASI	$ 1,884.16		$ 1,884.16	$ 500.00	0.85%	$ -	0.00%	$ 500.00	0.85%
X	PEKERJAAN PENGECATAN	$ 2,060.31		$ 2,060.31	$ -	0.00%	$ -	0.00%	$ -	0.00%
XI	PEKERJAAN AKHIR	$ 100.00		$ 100.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**Total Contruction (I + II + III + IV + V + VI + VII + VIII + IX + X + XI)**	**$ 38,331.08**	**$ 13,181.54**	**$ 51,512.62**	**$ 22,382.56**	**37.99%**	**$ 5,973.29**	10.14%	**$ 28,355.85**	**48.13%**
B	**Profit 10%**	**$ 3,833.11**	**$ 1,318.15**	**$ 5,151.26**	**$ 2,238.26**	**3.80%**	**$ 597.33**	1.01%	**$ 2,835.59**	**4.81%**
C	**Overhad**	**$ 1,100.00**	**$ -**	**$ 1,100.00**	**$ -**	**0.00%**	**$ 450.00**	0.76%	**$ 450.00**	**0.76%**
D	**Tax 2%**	**$ 865.28**	**$ 289.99**	**$ 1,155.28**	**$ 492.42**	**0.84%**	**$ 140.41**	0.24%	**$ 632.83**	**1.07%**
E	**Total Contract**	**$ 44,129.47**	**$ 14,789.69**	**$ 58,919.16**	**$ 25,113.23**	**42.62%**	**$ 7,161.04**	**12.15%**	**$ 32,274.27**	**54.78%**

Prepara Husi :

Arq. Pedro de Lourdes Alves

Teknik ADN, I.P. Municipio Dili

Verifika Husi :

Arq. Francisco X. de Deus Jeronimo

Eng. Senior ba Edificio Publico no Agua e Saneamento A D N, I.P.

Certifika Husi :

Eng. Emerenciana da Costa Maia Freitas

Coor. Unidade de Controlo e Validacao de Qualidade A D N,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO D (CR 36)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Konstrusaun Sede Suku Ailok

Kompanha : Liberta Unip, Lda.

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	26/04/2022	Cristo Rei	Pedro de L. A	Teknik	1	Material sira nebeé uza ba konstrusaun, kompania tengke halo lista no hetan aprovasaun husi projeito nain.	
					2		
					3		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		

MINISTÉRIO DO PLAN
E ORDENAMENT
VIII GOVERNO CONSTITUCIONAL

ANEXO C2 (NF 32)

PROJECT NAME : NOVA CONSTRUCAO ESCOLA BASICA F
LOCATION : DARE,VERA CRUZ,DILI

SUMMAR

NO	ITEM SERVISU
1	Preliminaries Works
2	Class Room Building Ca
3	Provisional Sum for Site Works

Prepared by :

Arq. Pedro de Lourdes Alves
Enjenheiru ADN,I.P. Municipio Dili

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NF 32)

Back-up Data

Naran Projeto : Konstrusaun ka Reabilitasaun ba EBF Lelaus Dare
No. kontratu :

Data Inspesaun : 29/04/2022

Fatin Inspesaun : Dare

Koordinadas :

Start Point : Long : -8.5996 Latetude : 125.5452


End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Pedro de Lourdes Alves

2. .....

3. .....

4. .....

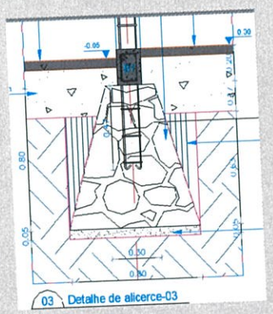Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Galian Pondasi vol = 56 m3 	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público


INSTRUSAUN / REKOMENDASAUN

Naran projeto : Konstrusaun ka Reabilitasaun ba EBF Lelaus Dare

Kompanha : Grupo Komunitario

ANEXO D (NF 32)

No	Data inspesaun	Municipiu / Posto	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	29/04/2022	Nain Feto	Teknik	1	Tengke prepara enginheiro iha terreno hodi foorientasaun serviso	
				2	Waihira atu cor sloof tengke halo karta ba laboratorio obras publik.	
				3	besi tulangan ba sloof no ring balk tengke hatama iha kolom laran.	
				4	wainhira atu cor tengke prepara molen.	
II						
III						
IV						
V						

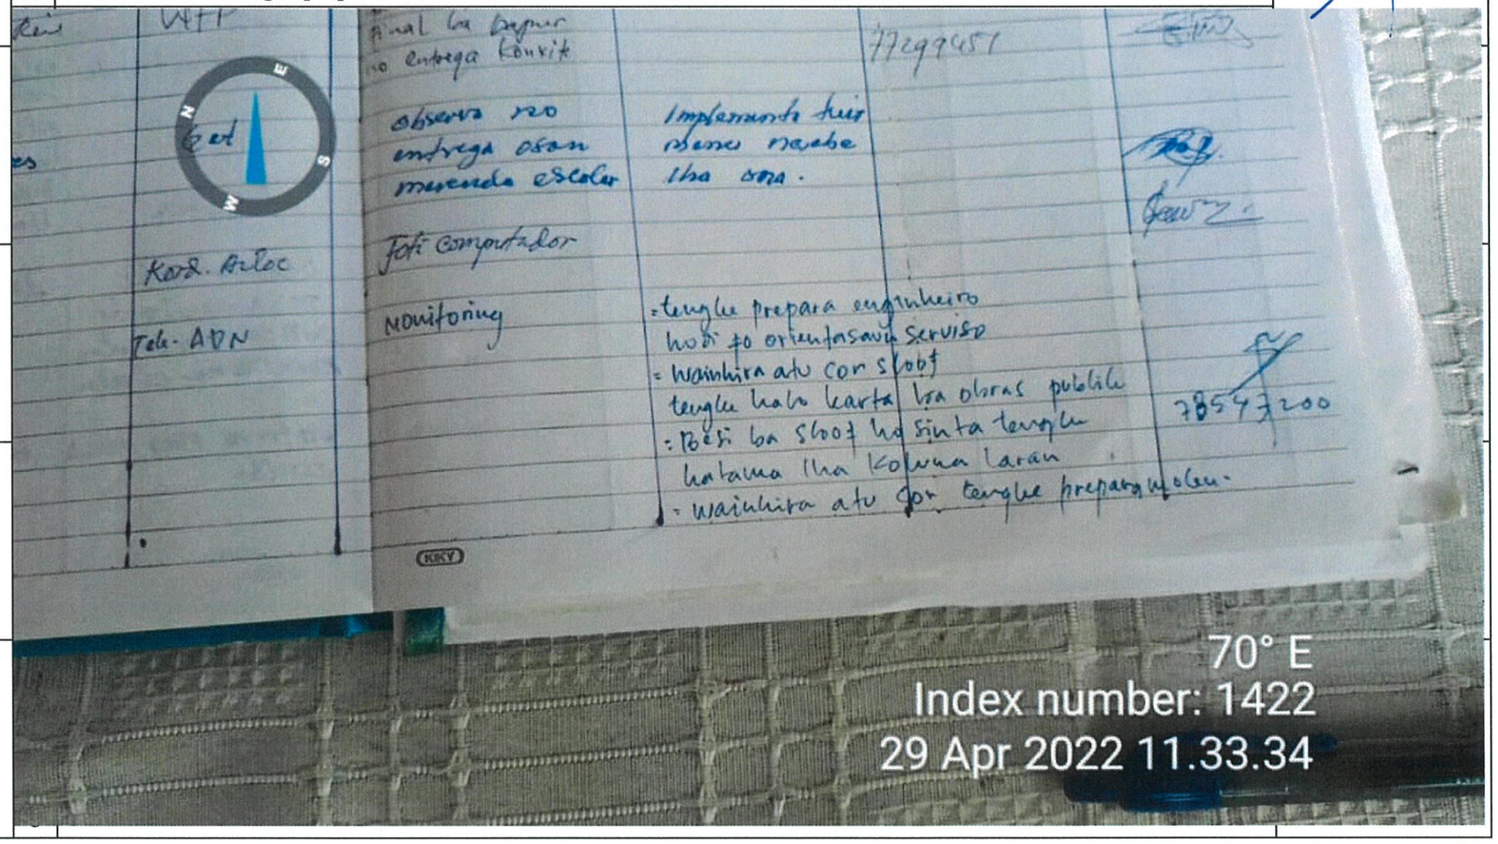

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng. PEDRO DE LURDES ALVES

MUNICIPIO MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
ATAURO	1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	Plan																														
							Actual																														
	2	New Construction of Laboratory for Covid-19 in Ataruo	MINISTERIO SAUDE	LM-Covid 19	Fitun Galilea Unipessoal Lda	No: /NCB/M.S/DNA/RBK-20-160	Plan																														
							Actual																														
	3	New Construction of Isolation for Covid-19 in Ataruo	MINISTERIO SAUDE	LM-Covid 19	Lygelina Alexix Unip. Lda	No: /NCB/M.S/DNA/DC-20-161	Plan																														
							Actual																														
	4	konstrusaun residensia oficial posto administrativo atauro	ESTATAL	LM-BS	Realidade Salmes Unip,Lda		Plan																														
							Actual																														
	5	Konstrusaun ka Reabilitasaun ba EBC Biqueli	MINISTERIO DA EDUKASAUN	LM-TP	MEJD PKRIE EBC BIQUELI	0	Plan																														On Goin
							Actual																														
CRISTO REI (CR)	1	Rehabilitasaun intake no kanu transmisaun iha La Koto & Mutu Dare	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Amigo Unip. Lda	SSS/021/MOP-2020	Plan																														
							Actual																														
	2	New Installation Street Light at Cristo Rei - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	Silkar International Unip. Lda	RDTL/MOP-SEE/CGI-PEN:0000246	Plan																														
							Actual																														
	3	New Installation of MV, LV Line and House Connection from Feederll Becora to Taibesi, Bemori and Balide - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Ceuilaju.Lda	RDTL/MOPTC-VOMPTC/CGI-PEN:0000444	Plan																														
							Actual																														
	4	New Installation of MV, LV Line and House Connection from Balide to Delta 3, Fomento, Manleuana, Bualaran, Aldeia Moris Dame, Eskola Fatumeta, Cacaulido, Ailok Laran, Bua Laran and Lisbutak - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Derren Construction Unip.Lda.	RDTL/MOPTC-VMOPTC/CGI-PEN : 0000304	Plan																														
							Actual																														
	5	New Installation of MV, LV Line and House Connection from Biterlaun Fatu Ahi to Lenuk Hun Cristo Rei - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Jmindo	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000442	Plan																														
							Actual																														
	6	New Installation of MV, LV Line and House Connection from Hera Ailok Laran to Sokaer Laran - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Vinario Unip.,Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000443	Plan																														
							Actual																														
	7	New Construction of ICCU at Hospital Nacional Guido Valadares, Dili Municipality	MINISTERIO SAUDE	FI	SIKUNDI, Unipessoal, Lda	SSS/281/MOH-2016	Plan																														
							Actual																														
	8	Consulting Services for Detail Engineering Design (DED) for Pediatric and ICCU Building in Guido Valadares National Hospital	MINISTERIO SAUDE	FI	Philcoei International, Inc. In JV with Luis and Associates, Co	SSS/035/MOPTC-2017	Plan																														
							Actual																														
	9	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)	MINISTERIO DAS OBRAS PUBLICAS	FI	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	Plan																														
							Actual																														
	10	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	Aspalink Unip Lda	SSS/131/MOPTC-2017	Plan																														
							Actual																														
	11	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	Star King Unip. Lda	SSS/012/MOP-2020	Plan																														
							Actual																														
	12	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	MINISTERIO DAS OBRAS PUBLICAS	FI	Nimia Unip Lda	RT/154/MOPTC-2016	Plan																														
							Actual																														
	13	Rehabilitasaun Tanke Reservatoriu iha Asgor no Bidau Masaur/ 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Selhar	RFQ-MOP-190047	Plan																														
							Actual																														
	14	Konstrusaun Moru Hadulas Bomba Bidau /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	SARCADEFAT Unip.Lda	MOP-W-190164	Plan																														
							Actual																														
	15	Konstrusaun Moru Hadulas Bomba fomentu /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	H FOUN Unip.Lda	MOP-W-190189	Plan																														
							Actual																														
	16	Lot 1 Urgent Installation of Street Lights in Mota Ulun-Bedois-Benamauk,Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Sirlacoli Unip. Lda	MPW-W-200032	Plan																														
							Actual																														
	17	Installation of Street Lights Prizaun Becora-Culuhun California (Lot 2)/162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Oulale unip.Lda	MPW-W-190261	Plan																														
							Actual																														
	18	Konstrusaun Igreza Sagrada Corasaun de Jesus Becora	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Carya Timor Leste Lda	Transferencia Publica	Plan																														
							Actual																														
	19	Rehabilitasaun & Extensaun Laboratorio Nacional Bidau - Dili	HOSPITAL NACIONAL GUIDO VALADARES	LM-BS	Talamori	RDTL-MS-LNS-RFQ-17-064	Plan																														
							Actual																														
	20	Escola Secundaria Tekniko Vocasional 28 de Novembru iha Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-BS	Dirbajudi	RDTL RCB/01-R/ME-DNA/REHAB	Plan																														
							Actual																														
	21	Rehabilitasaun Konstrusaun ESTV 28 Novembro - Dili (Rf)	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	Biqueli Pala Unip. Lda	08KDM/AM-DIL/XI/2019	Plan																														
							Actual																														Falta FHO
	22	Rehabilitasaun ESTV Comercio E Economia	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	PDIM	Fitun Roman Polmar Unip. Lda	06/KDM/AM-DIL/X/2019	Plan																														
							Actual																														Falta FHO
	23	RM Pecas Sofremento pagamento Bee Mos	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Flocinob Motis Unip Lda	MOP/W-190185	Plan																														
							Actual																														
	24	Rehabilitation of Medicine Laboratorium in Lahane	UNIVERCIDADE NACIONAL TIMOR LORO SAE	LM-CD	Nevan Construction Unip Lda	012/UNTL/EXT/C/2016	Plan																														
							Actual																														
	25	Lot 1 Urgent Installation of Street Lights in Cristo Rei,Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Hanaria Electrial Unip.Lda	MOP-W-190136	Plan																														
							Actual																														
	26	Urgent Installation of Street Lights in Cristo Rei, Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	9 Brothers Unip Lda	MOP-W-190134	Plan																														
							Actual																														
	27	Consultancy to develop A feasibility study and master plan Guido Valadares National Hospital (Bem Serviso)	MINISTERIO SAUDE	LM-BS	Mafra Consultante Unipessoal Lda	FBS-DNA-MOP-19018-B	Plan																														
							Actual																														
	28	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Titisa Louro Unip.Lda	MPW-W-210067	Plan																														
							Actual																														
	29	New Construction of Gabions Tower No.6 section Hera	MINISTERIO DAS OBRAS PUBLICAS	FI	Jova Construction	NCB/034/MOP-2020	Plan																														
							Actual																														
	30	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	KEFI OEL Unip.Lda		Plan																														
							Actual																														
	31	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau	MINISTERIO DAS OBRAS	FI			Plan																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng.	**PEDRO DE LURDES ALVES**
MUNICIPIO	**MUNICIPIO DILI NO POSTOS**

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
	31	Santa-Ana (Pacote I) Municipality Dili	PUBLICAS	FI	Catya Timor Leste Lda	SSS/009/MOP-2020	Actual																														
	32	For Clean Up of Metiaut - Cristo Rei, Areai Branca - Dolok Oan Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	Tinolina Unipessoal, Lda	MPW-W-SS-210023	Plan																														
							Actual																														
	33	New Construction of Gabion Tower No 6 Section Hera - Manatuto, Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	Emergency	Vilagem Construction Unip.Lda	NCB/032/MOP/2020	Plan																														
							Actual																														
	34	Rehabilitation Construction Of Crocodile Cage Hera	MInisterio Koordenador Asuntu Ekonómikus	LM-BS	Santana Diak Unipessoal Lda	603DNRHAL/DGA/SEA-MCAE/IX/2021	Plan																														
							Actual																														
	35	Rehabilitasaun no Konstrusaun Jardim Kristo Rei	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	PDIM	Mendith UnipLda	01/PDIM/A.M./DILI/X/2017	Plan																														
							Actual																														
	36	Konstrusaun sede suko Ailok	Ministério da Administração Estatal	LM-CD	Liberta	05/KAM/AM-DIL/IX/2021	Plan																														
							Actual																														On Goin
	37	Projetu Konstrusaun Foun no Rehabilitasaun ba EBC Sergio Viera de Melo Becora, Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	Delatina	NCB:06/MEJD/DNA/2021	Plan																														
							Actual																														On Goin
	38	Projetu Konstrusaun Foun ba ESTV Hera	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-CD	Timorindo Unip. Lda	NCB:05/MEJD/DNA/2021	Plan																														
							Actual																														On Goin
	39	Konstrusaun ka Reabilitasaun ESTV 28 de Novembro Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE ESTV 28 DE NOVEMBRO BECORA	0000	Plan																														
							Actual																														On Goin
	40	Konstrusaun ka Reabilitasaun ba ESG 12 de Novembro Becora	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE ESG 12 DE NOVEMBRO-BECORA	0000	Plan																														
							Actual																														On Goin
	41	Konstrusaun ka Reabilitasaun ba ESG FINANTIL	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE ESG FINANTIL	0000	Plan																														
							Actual																														On Goin
	42	Konstrusaun ka Reabilitasaun ba EPE Ai-Loktuto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EPE AI-LOKTUTO	0000	Plan																														
							Actual																														On Goin
	1	Instalasaun baixada electricidade, instalasaun kanu transmisaun & lutu hadulas estasaun bomba Tuana Laran	MINISTERIO DAS OBRAS PUBLICAS	FI	Montez Frere Unip. Lda	MJ-046/Junho 2021	Plan																														
							Actual																														
	2	Melhoramento kanu transmisaun no distribuisaun iha Maloa	MINISTERIO DAS OBRAS PUBLICAS	FI	Haksolok Java Motor Unip Lda	No: 214/MACLN/X/2021	Plan																														
							Actual																														
	3	New Installation of MV, LV line and House Connection from Timor Block to Vila Verde, Ponte Comoro and Fomento - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	Cartilo.Lda	27/CNC/IX/2021	Plan																														
							Actual																														
	4	Rehabilitasaun Linha Media Tensaun & Baixa Tensaun / Feeder 1 central elctric comoro Rotunda	MINISTERIO DAS OBRAS PUBLICAS	FI	Embi elctic.Lda	RDTL-PO:2019-15736	Plan																														
							Actual																														
	5	New Installation MV, LV Line and House Connection from Bairo Pite to Aldeia ba Dame - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Joia Leste Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000409	Plan																														
							Actual																														
	6	New Installation of MV, LV Line and House Connection from Fatuhada to Behoris, Arbiru Beach, Comoro Market, and Bebonuk - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Ladamutu Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000434	Plan																														
							Actual																														
	7	New Installation MV, LV Line and House Connection From Rotunda Nicolau Lobato to Terminal Tasi Tolu-Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Sonalevi Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000440	Plan																														
							Actual																														
	8	Maintenance, Repair & New Electrical Installation at Ministerio Do Plano E Ordenamento	MINISTERIO PLANU E ORDENAMENTU	LM-CD	Titam Star Supplayer unip.lda	RFQ/040/ANATL/EP-2019	Plan																														
							Actual																														On Goin
	9	Consulting services for DED of the new Ministry of Commerce Industry and Enviroment Training Center	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	Vitor Hugo Coordenação e Gestão de Projetos, S.A., através de emprendimento conjunto com a Quadromor Timor - Sistemas de Engenharia, S.A	RFP/030/MCIE-2013	Plan																														
							Actual																														
	10	Detail Engineering design (DED) of The New Ministry of Commerce, Industry and Environment	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	FI	Philkoei International Inc. in JV with Arch Haus Asia Consultant, Inc	RFP/029/MCIE-2013	Plan																														
							Actual																														
	11	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	Plan																														
							Actual																														
	12	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	MINISTERIO DAS OBRAS PUBLICAS	FI	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	Plan																														
							Actual																														
	13	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	MINISTERIO DAS OBRAS PUBLICAS	FI	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	Plan																														
							Actual																														
	14	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	MINISTERIO DAS OBRAS PUBLICAS	FI	G and S Unipessoal Lda	SSS/040/MOPTC-2015	Plan																														
							Actual																														
	15	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	MINISTERIO DAS OBRAS PUBLICAS	FI	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	Plan																														
							Actual																														
	16	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	MINISTERIO DAS OBRAS PUBLICAS	FI	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	Plan																														
							Actual																														
	17	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	MINISTERIO DAS OBRAS PUBLICAS	FI	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	Plan																														
							Actual																														
	18	Road and Drainage Rehabilitation Project Aimutin to Manleuana	MINISTERIO DAS OBRAS PUBLICAS	FI	Aspalink Unip Lda	SSS/308/MOPTC-2016	Plan																														
							Actual																														
	19	New Construction of Median Line "Leader to Elemloi JNC"	MINISTERIO DAS OBRAS PUBLICAS	FI	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	Plan																														
							Actual																														
	20	Comoro Power Plant CCTV	MINISTERIO DAS OBRAS PUBLICAS	FI	SM Bark Technolgy Ltd	SSS/344/MOPTC-2016	Plan																														
							Actual																														
	21	Maloa River	MINISTERIO DAS OBRAS PUBLICAS	FI	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	Plan																														
							Actual																														
	22	Road Rehabilitation Project, Road Section: Aldeia 30 de	MINISTERIO DAS OBRAS	FI	Meiroi Lda	SSS/127/MOPTC-2017	Plan																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng. PEDRO DE LURDES ALVES

MUNICIPIO MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
DOMALEXO (DA(	22	Augusto, Comoro Municipality of Dili	PUBLICAS		Mapri, Unip	[illegible]	Actual																														
	23	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	DMF ACESO	MPW-W180036	Plan																														
							Actual																														
	24	Konstrusaun Beé mos ba Residencia Sr. Jeneral F-FDTL no Sr. Lu Olo iha Manleuana	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Caileba	MPWTC-502/5G/MOPTC/V/2017	Plan																														
							Actual																														
	25	Melhoramento Sistema Beé mos iha Area Delta 1,2,3 no 4	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Carisma	MPWTC-NCB-170020	Plan																														
							Actual																														
	26	Rehabilitasaun no Installasaun Metro Contador Sistema Be'e mos iha Perumnas Bairo Pite (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Sos Alssonix	MPWTC-NCB-170024	Plan																														
							Actual																														
	27	Urgent Repair of Roof Leaks at the New Building Ministry of Finance RDTL	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Carya Timor Leste	RDTL-SSS/MOPTC-2017	Plan																														
							Actual																														
	28	Perfurasaun Sistema Be'e Mos Iha Area Comoro DMA 37 /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Domin Timor Diak Lda	RFQ-MOP-190044	Plan																														
							Actual																														
	29	Novo construsaun do campo polisportivo do Ministerio das Obras publicas (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ATUNEGOS UNIP.LDA	RFQ MOP/W-190249	Plan																														
							Actual																														
	30	Construction of Terminal in Tasi Tolu	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-CD	Mar vermelha unip.lda	RDTL-2014-C-101-MTC	Plan																														
							Actual																														
	31	Maintenance and Repair at F-FDTL, Head Qaurtel, Fatuhada	MINISTERIO DA DEFESA	LM-BS	Victoria Const. Unip. Lda	2015-000065	Plan																														
							Actual																														
	32	Separasaun ba Aula Tolu iha Ministerio da Defesa	MINISTERIO DA DEFESA	LM-BS	Algis	la mensiona nomor iha contratu	Plan																														
							Actual																														
	33	Manutensaun Edifício Ministerio da Defesa	MINISTERIO DA DEFESA	LM-BS	Algis	RDTL 11 /MNEC /2019	Plan																														
							Actual																														
	34	Manutensaun Residencia C.E.M.G. das F-FDTL	MINISTERIO DA DEFESA	LM-BS	Panca Sekawan	No la mensiona contratu	Plan																														
							Actual																														
	35	New Construction of Sao Jose Aimutin Church in Comoro	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Grupo Timindo	Transferencia Publica	Plan																														
							Actual																														
	36	New Construction of An'Nur Orphanage Building	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Asda A3i Unip. Lda.	Transferencia Publica	Plan																														
							Actual																														
	37	Konstrusaun Escola de Musica iha fatumeta	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Talisahe	Transferencia Publica	Plan																														
							Actual																														
	38	Konstrusaun Sede Suku Bebonuk	ESTATAL	PDIM	Gazelle Unip. Lda	02/KDM/AM-DIL/VIII/2019	Plan																														Falta FHO
							Actual																														
	39	Konstrusaun Sede Suku Madohi	ESTATAL	PDIM	Domcos Hornay Unip. Lda	05/KDM/AM-DIL/VIII/2019	Plan																														Falta FHO
							Actual																														
	40	Rehabilitasaun and Maintanance of Vice Minister office in Mandarin	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Milcha Unip Lda	364/DNA-DGAF-MOP/XII/2019	Plan																														
							Actual																														
	41	Manutensaun Edifício iha Gabinete Ministro nian	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	Otsop Paris Unip Lda	RDTL-MAP176/GM/VIII/2019	Plan																														
							Actual																														
	42	Urgent Installation of Street Lights in Tasi Tolu, Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alefa Unip Lda	MOP-W-190133	Plan																														
							Actual																														
	43	Konstrusaun Lutu Hadulas WTP Central iha Bairo-Pite Dom Aleixo Municipio Dili /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Iki Bia-Nunu Unip Lda	NCB/MOP/W-200015	Plan																														
							Actual																														
	44	Rehabilitation Recident & Carport of Vice PM (Bem Serviso)	MINISTERIO PLANU E ORDENAMENTU	LM-BS	D. Likibo Unip. Lda	05/RDTL/MPO/ADN/DA-Afq/X/2020	Plan																														FHO ona
							Actual																														
	45	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	Plan																														
							Actual																														
	46	Revitalization of Community Aitarak Laran	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	TPF Timor Unipessoal Lda	MPW-S-190272	Plan																														
							Actual																														
	47	Servisu Manutensaun Edifício Agencia de Desenvolvimento Nasional	MINISTERIO PLANU E ORDENAMENTU	LM-BS	Giovanio	002.LM/RDTL/MPO/ADN.I.P/III/2021	Plan																														
							Actual																														
	48	Instalasaun Agua Potavel iha Edifício Ministerio da Defesa no QG das F-FTL	MINISTERIO DEFESA	LM-CD	CAPTAIN HOOK		Plan																														
							Actual																														
	49	For River Normalization, Roads Embankment and Road Clean Up of Comoro Mota Ulun - Casnafar, Air Terjun Sarlala Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS-210006	Plan																														
							Actual																														
	50	Enhancement of Project - Management Information System (PMIS)	MINISTERIO PLANU E ORDENAMENTU	LM-BS	KINOS Unip,Lda	011/RDTL/MPO/ADN.I.P/V/202	Plan																														
							Actual																														
	51	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	MINISTERIO DAS OBRAS PUBLICAS	Emergency	Bintang Fajar, Lda	MPW-W-SS 210028	Plan																														
							Actual																														
	52	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	MINISTERIO DAS OBRAS PUBLICAS	Emergency	Monte Veado Unip Lda	MPW-W-SS 210008	Plan																														
							Actual																														
	53	Rehabilitasaun Edifício Dormitoriu INS Comoro-Dili Timor Leste	MINISTERIO SAUDE	LM-CD	Grandis	RDTL-INS -DAFA-NCB-21-0001	Plan																														
							Actual																														
	54	New Construction Lanscaping and Gazebo at Vice Prime Minister Official Recident	MINISTERIO PLANU E ORDENAMENTU	LM-BS	Rubic Unip. Lda	006/RDTL/MPO/ADN.I.P/III2021	Plan																														Falta FHO
							Actual																														
	55	Extention of Sames Ware-House Building at Kampo Alor	MINISTERIO SAUDE	LM-CD	Unidade Unip Lda	RDTL-SAMES-RFQ-20-063	Plan																														
							Actual																														
	56	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Lizi Construction, Unipessoal Lda	MOP/CD/NCB/21044	Plan																														
							Actual																														
	57	Consulting services of spatial planing of Timor Leste	MINISTERIO PLANU E ORDENAMENTU	FI	Intersisment S.A in Joint Venture with Queternaire Portugal Consultoria para o Desenvolvimento. SA	SSS/041/MPO-2021	Plan																														
							Actual																														
	58	New construction archive werehouse at bebora	MINISTERIO SAUDE	LM-BS	Hilobadi Unip,Lda	RDTL-MS-C19-DNA-NCB-21-011	Plan																														
							Actual																														
	59	Construsaun de Balcao de atendimento publica para a Direcsaun Geral dos servicos de registos e do Notariado do Ministerio da Justica	MINISTERIO DA JUSTICA	LM-CD	Fatuk Mota Construction Unipessoal. Lda	MJ-046/Junho 2021	Plan																														
							Actual																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng.	PEDRO DE LURDES ALVES
MUNICIPIO	MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
	60	Manutensaun de salao Nobre	MINISTERIO DO INTERIOR	LM-BS	DCO Unip.Lda	No: 214/MACLN/X/2021	Plan																														
							Actual																															
	61	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	MTC	LM-CD	Holgapa Unip.Lda	RDTL - 2021 - MTC - CD - 031	Plan																														
							Actual																															
	62	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	MINISTERIO DAS OBRAS PUBLICAS	Emergency	Chegue Rau	NCB/040/MOP-2020	Plan																														
							Actual																															
	63	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	MINISTERIO DAS OBRAS PUBLICAS	Emergency	Holgapa Unip.Lda	RT/069/MOP-2021	Plan																														
							Actual																															
	64	Konstrusaun ka Reabilitasaun ba ESG 10 de Dezembro Comoro - Dili	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE ESG 10 DE DEZEMBRO COMORO-DILI		Plan																															On Goin
							Actual																															
	65	Konstrusaun ka Reabilitasaun ba EBC 10 de Dezembro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBC 10 DE DEZEMBRO		Plan																															On Goin
							Actual																															
	66	Konstrusaun ka Reabilitasaun ba EBC 30 de Agosto	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBC 30 DE AGOSTO		Plan																															On Goin
							Actual																															
	67	Konstrusaun ka Reabilitasaun ba EBF Naroman	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBF NAROMAN		Plan																															On Goin
							Actual																															
	68	Konstrusaun ka Reabilitasaun ba EPE Buras Kadalak	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EPE BURAS KADALAK		Plan																															On Goin
							Actual																															
	69	Konstrusaun ka Reabilitasaun ba EBF Bebonuk	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBF BEBONUK		Plan																															On Goin
							Actual																															
M E T I N A R O (M T N)	1	Mudansa Lina Bazeia Rekomendasaun ADN	MINISTERIO DAS OBRAS PUBLICAS	FI	Jofi	27/CNC/IX/2021	Plan																														
							Actual																															
	2	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Nimia Unip Lda	RDTL-PO:2019-15736	Plan																														
							Actual																															
	3	Melhoramento taratamento dezalinasaun iha manleu Metinaro /162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Garisiba Unip.Lda	MOP-W-190150	Plan																														
							Actual																															
	4	Construction of Kitchen and Refectory at Componete do Apoio de Serviso (CAS) iha Metinaro	MINISTERIO DA DEFESA	LM-BS	Betuhei	la mensiona nomor iha contratu	Plan																														
							Actual																															
	5	New Construction of WareHouse, Campas, Raodway, Drainage and Pavement at Jardim dos Herois Metinaro	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	LM-CD	Pro Frawijaya	RDTL:44/MSS/DNFALM-DAD/X/2014	Plan																														
							Actual																															
	6	Konstrusaun Turismu Komunitariu One Dollar Beach	SEFOPE	LM-TP	Quindy Eujec Lda.	02/CNFP-B/VII/2019	Plan																														
							Actual																															
	7	Detailed Engineering Design of New Fisherman Port, Suco Duyung, Metinaro	MINISTERIO AGRIKULTURA E PESCAS	FI	Consulmar-Projetista e Consultore. Lda de Portugal em Empreendimento Conjunto com a Engipro de TLPty. Ltd	RFP/042/MAF-2014	Plan																														
							Actual																															
	8	New Construction of Roadways, Drainage and Parking Area no Jardim de Herois de Metinaro	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	Celijio Star	No: 214/MACLN/X/2021	Plan																														
							Actual																															
	9	New Construction of Campas and Grass Planting Jardin dos Herois (JHM) Metinaro	MINISTRO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	LM-CD	LABILAY, Unipessoal, Lda	216/MACLN/X/2021	Plan																														
							Actual																															
	10	New Const of F-FDTL home base Fuel Filling Station in Metinaro, Dili Municipality	MINISTERIO DA DEFESA	LM-BS	Aitula Construction, Lda	ICB No 05/DNA/MD/2021	Plan																														
							Actual																															
	11	Konstrusaun ka Reabilitasaun ba EBF Benunuk Metinaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBF BENUNUK METINARO		Plan																															On Goin
							Actual																															
	12	Konstrusaun ka Reabilitasaun ba ESG 20 de Setembro Metinaro	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE ESG 20 DE SETEMBRO METINARO		Plan																															On Goin
							Actual																															
	1	Rehabilitasaun kanu transmisaun husi Benamauk ba WTP Lahane no Becusse	MINISTERIO DAS OBRAS PUBLICAS	FI	Lemo Timor Unipessoal Lda	SSS/019/MOP-2020	Plan																														
							Actual																															
	2	Consulting Services for detailed Engineering Design of CAC Office Building	CAC	FI	Imagem, Design and Arquitectura, Lda (IDA) in Association with Vaz, Dotti & Silva, Lda (VDS)	RFP/004/MPW-2013	Plan																														
							Actual																															
	3	New Construction of Ojetil Office Building Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	Fitun Diak Unip.Lda	SSS/301/MOPTC-2016	Plan																														
							Actual																															
	4	New Installation MV, LV Line and House Connection from Bidau to Catedral - Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Anicla.Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000437	Plan																														
							Actual																															
	5	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	MINISTERIO DAS OBRAS PUBLICAS	FI	Meteor Unip.Lda	SSS/200/MOPTC-2016	Plan																														
							Actual																															
	6	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	MINISTERIO DAS OBRAS PUBLICAS	FI	Suai Indah Unipessoal Lda	SSS/218/MOPTC-2016	Plan																														
							Actual																															
	7	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	MINISTERIO DAS OBRAS PUBLICAS	FI	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	Plan																														
							Actual																															
	8	Installation of Transmission Line, Distribuition Panel & Transformer in Taibesi and Becora	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Nizixavane	MPWTC-W-015072	Plan																														
							Actual																															
	9	Construction of Membrane Tent and Shaded Area of SG-MOPTC	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Voar	MPWTC-W-170020	Plan																														
							Actual																															
	10	Installation of Street Lights Lecidere -Acadiruhun-Acait (Lot 6)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Alzes Ukat, Unip.Lda	MPW-W-190266	Plan																														
							Actual																															
	11	Rehabilitasaun no manutensaun ex edificio diresaun geral organizasaun urbana	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-BS	Riri Brothers Unip. Lda.	RDTL,0140/UAD-MAE/XII/2019	Plan																														
							Actual																															
	12	Rehabilitasaun Edificio Conselho de Empresa	CONSELHO DA EMPRENSA	LM-BS	Algis	CI-19-06-C-013	Plan																														
							Actual																															
	13	Manutensaun Expert Room iha MESCC	MINISTERIO ENSINO SUPERIOR CIENCIA E	LM-BS	Katuas Patricio	RFQ19/45-Q	Plan																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng.	PEDRO DE LURDES ALVES
MUNICIPIO	MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
NAIN FETO (NF)			CULTURA				Actual																														
	14	Rehabilitation of Volley Ball Beach Facilities in Dili-Lecidere	SEJD	LM-CD	DVD Electric	NCB/01/SSYS-2019	Plan																														
							Actual																														
	15	Rehabilitation of GDD Sports Indoors	SEJD	LM-CD	Victoria Const. Unip. Lda	NCB/02/5595-2019	Plan																														
							Actual																														
	16	Rehabilitation and Maintenance of Jardim 12 de Novembro at Motael	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	LM-BS	Algis	RDTL:47/DNA-MTCI/VII/2019	Plan																														
							Actual																														
	17	Rehabilitasaun Residencia Vice Presidente Parlamentu Nacional iha Farol	PARLAMENTU NASIONAL	LM-BS	Celijio Star	PN/4306/2016	Plan																														
							Actual																														
	18	Rehabilitasaun Jardim 12 de Novembro iha Igreza Motael nia oin	ESTATAL	LM-BS	Berlosconi	RDTL0144/UADE-MAE/XII/2019	Plan																														
							Actual																														
	19	Rehabilitation and Maintenance Building PCM	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	LM-BS	Panca Sekawan	PCM-20/01-C/0014	Plan																														
							Actual																														
	20	Minor Rehabilitasaun of MTC main of Building and Correeios	MINISTERIO DA PRESIDENCIA DO CONSELHO DE MINISTROS	LM-BS	Risumali Unip Lda	RDTL2019-MTC-OS-0041	Plan																														
							Actual																														
	21	Rehabilitation of Confrence Room at the office of the Primer Minister, building I, Palacio do Governo,Dili Timor Leste	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Gez Unipessoal Lda	RDTL-294/GPM/XI/2019	Plan																														
							Actual																														
	22	RIVER PROTECTION PALACIO NOBRE	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	Plan																														
							Actual																														
	23	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	TRIBUNAL RECUSSO	Emergency	Star King Unip. Lda	MPW-SS-210030	Plan																														
							Actual																														
	24	Refurbishment of tenis court facilities, Dili	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	Algis	NCB/01/SSYS/2021	Plan																														
							Actual																														
	25	aditional for Hospital Dr.Antonio Carvalho Lahane	MINISTERIO SAUDE	LM-BS	Hedge Construction, Unip. Lda	RDTL-MS-C19-DNA-DC-21-072	Plan																														
							Actual																														
	26	New Construction of outdoor sport facilities in Taibessi	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	UKA II UNIPESSOAL LDA	NCB/02/SSYS/2021	Plan																														
							Actual																														
	27	Preparation of detailed engineering design (DED) for new cable stayed bridge over the becusse river, in Dili, total lenght+25m², Municipio Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	TPF Timor Unipessoal Lda	RT-CD-MOP-21002	Plan																														
							Actual																														
	28	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Sanford Const. Unip. Lda	MPW-W-210168	Plan																														
							Actual																														
	29	New Construction of outdoor sport facilities in Taibessi	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	LM-CD	UKA II UNIPESSOAL LDA	NCB/02/SSYS/2021	Plan																														
							Actual																														
	30	Konstrusaun ka Reabilitasaun ba EBF Duque de Caxias	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBF DUGUE DE CAXIAS	0	Plan																														On Goin
							Actual																														
	31	Konstrusaun ka Reabilitasaun ba EBC Bidau Akadiru-Hun	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBC BIDAU AKADIRU HUN	0000	Plan																														On Goin
							Actual																														
	32	Konstrusaun ka Reabilitasaun ba EBF Lelaus Dare	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	LM-TP	MEJD PKRIE EBF LELAUS DARE	0000	Plan																														On Goin
							Actual																														
	1	Construction Of New Office Of Tribunal Distrital De Dili	TRIBUNAL RECUSSO	FI	China Shandong International Economic And Technical Cooperation Group. LTD	ICB/008/TR-2019	Plan																														
							Actual																														
	2	Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building	TRIBUNAL RECUSSO	FI	Dacrea Desing and Engineering Consultant (Dacrea) (Indonesia) In Association with Archtimor Engineering Consultants (AEC) as Sub-consultant (Timor-Leste)	RFP/012/TR-2019	Plan																														
							Actual																														
	3	Installation of New MV Line in Rotunda Mercado Lama, Culuhun, Ailele Hun, and Lecidere	MINISTERIO DAS OBRAS PUBLICAS	FI	Ferajota	SSS/072/MOPTC-2015	Plan																														
							Actual																														
	4	Rehabilitation MV,Line , LV Line and distribution Trasformer from Casa Europa to Pantai Pasir Putih - Dili District	MINISTERIO DAS OBRAS PUBLICAS	FI	Inaziju	RDTL/MOP-SEE/CGI-PEN : 0000267	Plan																														
							Actual																														
	5	Construção Quartel General PNTL em Caicoli	MINISTERIO DO INTERIOR	FI	Shangai Construction Group Co.,Ltd	ICB/036/MI-2017	Plan																														
							Actual																														
	6	Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste	MINISTERIO DO INTERIOR	FI	PT. Ceriajasa Cipta Mandiri in Joint Venture with JKC Consultant Engineering Unipessoal Lda	RPF/087/MI-2017	Plan																														
							Actual																														
	7	Consulting Services for Detail Engineering Design of the IGE Office, Workshop and Warehouse Complex Building	MINISTERIO DAS OBRAS PUBLICAS	FI	Scope Australia Pty, Ltd	RFP/039/MPW-2013	Plan																														
							Actual																														
	8	Consulting Services for Detailed Architecture and Engineering Design for Press Building Project	SECRETARIADO ESTADO KOMUNIKASAUN	FI	CGM Consultants & Associates Incorporated, Lda.	SSS/051/SECOM-2015	Plan																														
							Actual																														
	9	Consulting Services for Feasibility Study of the New Buildings for RTTL. P.E and Tatoli P.I.	SECRETARIADO ESTADO KOMUNIKASAUN	FI	Potevio Company Limited	RDTL	Plan																														
							Actual																														
	10	Additional Drainage Colmera	MINISTERIO DAS OBRAS PUBLICAS	FI	Hailala Unip.Lda	166139	Plan																														
							Actual																														
	11	Consulting Services of Detailed Engineering Design of Sport Complex and Building at Region of Dili	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	ATT consultants Co. Ltd JV SQ Architect and Planner Co. Ltd	RFQ/314/SEJD-2016	Plan																														
							Actual																														
	12	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Bia Mapel	MPW-W190099	Plan																														
							Actual																														
	13	Rehabilitation of Security Post Building in Caicoli MPW	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Reza	RDTL MPW-014067	Plan																														
							Actual																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng. PEDRO DE LURDES ALVES

MUNICIPIO MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
V E R A C R U Z (V R)	14	Prefurasaun Be'e mos iha Area Tuana Laran - Matadouro Suku Vila verde, Postu Administrativo Vera Cruz - Municipiu Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Liberta	MPWTC-W-700774	Plan																														
							Actual																														
	15	Manutensaun ba Edifício DNGRA-MOP / 162	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Katuas Patricio	RFQ-MOP-190071	Plan																														
							Actual																														
	16	Rehabilitation of DNA MOP Cobe House in Caicoli Dili	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Surik Saki Rai Unip.Lda	MOP-W-190167	Plan																														
							Actual																														
	17	Construction of extension office building of the Minister of Public works (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	CELFA Unip.Lda	RDTL-NCB-MOP-190088	Plan																														
							Actual																														
	18	Detailed Engineering design of E-Recruitment Building CFP	CFP	LM-BS	De Oliveira design	SSS/045/MT-2017	Plan																														
							Actual																														
	19	New Construction of Auditorium (Salaun Paroquial) & Class Room & landscape of Catedral. Vila Verde	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Bimavi	transferencia publica	Plan																														
							Actual																														
	20	Construção Pure Hindu Taibesi	GABINETE DO PRIMEIRO MINISTRO	LM-TP	Pantarhei	Transferencia Publica	Plan																														
							Actual																														
	21	New Construction of Administration and Logistic Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	Aitula Construction, Lda	059/C/UNTL/XI/2019	Plan																														
							Actual																														
	22	New Construction of Faculidade Econimia e Gesatao Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	Aitula Construction, Lda	057/C/UNTL/X/2019	Plan																														
							Actual																														
	23	New Building Construction of Medicina Ciencia da Saude Building	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	Linier jv Algis	058/C/UNTL/X/2019	Plan																														
							Actual																														
	24	Konstrusaun Edifício servisu espesializada iha PGR Colmera	PROCURADORIA GERAL DA REPUBLIKA	LM-CD	Bobolait	RDTL-D.FEO/APRO/PGR/19.002/2019	Plan																														
							Actual																														
	25	Rehabilitation of Houses RTTL in Caicoli and Biterlau	RADIO TELEVISAUN TIMOR LESTE	LM-BS	Gaerenez	10/RDTL,E.P/DAF/VI/2019	Plan																														
							Actual																														
	26	Konstrusaun Edifisiu Foun ba Diresaun Aprovizionamentu Finansas e Fiskalizasaun	ESTATAL	PDIM	Chipys Unip. Lda	07KDM/AM-DIL/X/2019	Plan																														On Goin
							Actual																														
	27	Maintenance of Building for Trade Invest Timor Leste	TRADE INVEST	LM-BS	D'CO	RDTL/TITL/C.06/10/2019	Plan																														
							Actual																														
	28	Rehabilitasaun Hospital Dr.Antonio Carvalho Lahane(Building A) Hodi halo Fatin Izolamentu ba Pasienti Covid-19	MINISTERIO SAUDE	LM-Covid 19	Hedge Construction, Unip. Lda	NCB/M.S./DNA/DC-20/143	Plan																														
							Actual																														
	29	Desenho e Espicificacao de Quantidades BoQ para a amplincao do Balcao de Atendimento na DNRN	MINISTERIO DA JUSTICA	LM-CD	Viros Consultant Unip Lda	RDTL-MJNo.009/MAIO/2019	Plan																														
							Actual																														
	30	Rehabilitasaun e Manutensaun Edifisio Armajen DNSA, Dili (Bem Serviso) (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	BTwo Unip Lda	MOP/W-190186	Plan																														
							Actual																														
	31	Detailed Engineering Design Hospital Dr. Antonio Carvalho LOT"A" Lahane Oriental	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Victoria Cosnt.	FBS-DNA-MOP-19016	Plan																														
							Actual																														
	32	Improvement of Mina Distribuition Pipe in DMA 31 in Suco Mascarenhas	MINISTERIO DAS OBRAS PUBLICAS	FI	Amigo Unip. Lda	No : /NCB/MPW/W-200016	Plan																														
							Actual																														
	33	New Construction of isolation (OPD) Vera cruz relation of covid 19	MINISTERIO SAUDE	LM-Covid 19	Romante Pty. Ltd	RDTL-MS-C19-DNA-SS-21-001	Plan																														
							Actual																														
	34	New construction Warehouse for centro Nacional Chega I.P	Centro Nacional Chega	LM-CD	A. L. Unip.Lda	26/CNC/IX/2021	Plan																														
							Actual																														
	35	Renovation of public Health services at lahane , posto vera cruz Timor Leste	MINISTERIO SAUDE	LM-BS	Queson SQ Unipessoal Lda	RDTL-MS-DNA-ICB-20-255	Plan																														
							Actual																														
	36	New Construction Drinage centro Nasional Chega.I.P	Centro Nacional Chega	LM-CD	Chacailala Unipessoal Lda	27/CNC/IX/2021	Plan																														
							Actual																														
	37	Criacao de estrutura de parede divisorias do ministerio da justica	MINISTERIO DA JUSTICA	LM-CD	Fatuk Mota Construction Unipessoal. Lda	MJ-047/junho/2021	Plan																														
							Actual																														
	38	Extention Office of Legal and Judicial Training Centre	MINISTERIO DA JUSTICA	LM-CD	BEHALE ENTERPRICE UNIPESSOAL,LDA	MJ-066/Novembro/2021	Plan																														
							Actual																														
	39	Construction of Faculdade de Agricultura Building (B-01)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	Dany stra	RDTL 039/C/UNTL/XII/2021	Plan																														
							Actual																														
	40	Construction of Faculdade de Agricultura Building (B-02)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	Hedge Construction, Unip. Lda	RDTL 041/C/UNTL/XII/2021	Plan																														
							Actual																														
	41	Construction of Faculdade de Agricultura Building (B-03)	UNIVERCIDADE NACIONAL TIMOR LORO SA'E	LM-CD	Bobolait		Plan																														
							Actual																														
	42	Design Edifício MACLN	TOS DOS COMBATENTES D	LM-CD	Uma de Contrucão Unipessoal Lda	38/MACLN/IX/2021	Plan																														
							Actual																														
	43	Construction of Faculdade de Agricultura Building (B-01)	CIDADE NACIONAL TIMOR L	LM-CD	Dany Stra Unipessoal Lda	RDTL 039/C/UNTL/XII/2021	Plan																														
							Actual																														
	44	New Construction of Faculdade de Agricultura (B-02)	CIDADE NACIONAL TIMOR L	LM-CD	Bobolait Lda	RDTL 041/C/UNTL/XII/2021	Plan																														
							Actual																														
	45	New Construction of Faculdade de Agricultura (B-03)	CIDADE NACIONAL TIMOR L	LM-CD	Hedge Construction, Unip. Lda	RDTL040/C/UNTL/XII/2021	Plan																														
							Actual																														
	46	Extention Office of Legal and Judicial Training Centre	MINISTERIO DA JUSTICA	LM-CD	BEHALE ENTERPRICE UNIPESSOAL,LDA	MJ-066/Novembro/2021	Plan																														
							Actual																														
	47	Konstrusaun Koby House foun ba Unidade Aprovisionamento Desentralizadu UAD	Ministério da Administração Estat	LM-CD	Linier Unipessoal Lda	RFQ/088/MAE-2021	Plan																														
							Actual																														
O E	1	Restante Cabo Subteranno Centro Produsaun SAKATO reutiliza ba Hotel Ambeno Programa ZEEMS nian iha Oecusse	MINISTERIO DAS OBRAS PUBLICAS	FI	Lifau Indah	0000	Plan																														
							Actual																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng. PEDRO DE LURDES ALVES

MUNICIPIO MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
E C U S S E	2	Installation New MV Line , Transformer & Extend L.V Line and New Distribution Line from Nitib Tuan Oel Tam to nitib Tuan Oecusse District	MINISTERIO DAS OBRAS PUBLICAS	FI	Manekat Unip. Lda	RDTL/MOP-SEE/CGI-PEN:0000256	Plan																														
							Actual																														
	3	New Installation of Under Ground Cable MV Line From Malelat To Pasabe- Oecusse Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Maubere Spirit	RDTL/MOPTC-VOMPTC/CGI-PEN:0000454	Plan																														
							Actual																														
	4	Construção Posto Militar F-FDTL Pante Makasar	MINISTERIO DA DEFESA	FI	Ervel Unip.Lda	NCB/004/MDS-2015	Plan																														
							Actual																														
N A S I O N A L	1	Detailed Engineering Design (DED) of Dili Water Supply	MINISTERIO DAS OBRAS PUBLICAS	FI	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOP-2019	Plan																														
							Actual																														
	2	Detailed Engineering Design (DED) of Dili Sanitation and Drainage Master Plan-Phase II	MINISTERIO DAS OBRAS PUBLICAS	FI	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	SSS/035/MOPTC-2017	Plan																														
							Actual																														
	3	Feasibility Study of Surface Water Resource Development for the Water Supply of Dili Metropolitan Area	MINISTERIO DAS OBRAS PUBLICAS	FI	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/002/MOP-2019	Plan																														
							Actual																														
	4	Pre- Feasibility Study of a Ground Water Resources Development Project for the Water Supply of Dili Metropolitan Area	MINISTERIO DAS OBRAS PUBLICAS	FI	TEAM Consulting Engineering and Management PCL, Thailand in JV with ATT Consultants Company limited, Thailand and in association with CQ2 Engineering Consultancy & Diverso Unipessoal Lda, Timor-Leste	RFP/001/MOP-2019	Plan																														
							Actual																														
	5	Rehabilitasaun Sistema Be,e Mos Iha Iahane Dili Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	Sicola	SSS/018/MOP-2021	Plan																														
							Actual																														
	6	Financial Advisory Services Agreement between the Government of Timor - Leste and International Finance Corporation on Development of Presidente Nicolau Lobato Internasional Airport - Airport PPP Project	MINISTERIO FINANCAS	FI	International Finance Corporation	604869	Plan																														
							Actual																														
	7	National Road No.1 Upgrading Project Dili - Manatuto (Package A01-01)	MINISTERIO DAS OBRAS PUBLICAS	FI	Sinohidro corporation limited	ICB/07/MPW-2014	Plan																														
							Actual																														
	8	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Lonacca Unipessoal Lda	MPW-W-190177	Plan																														
							Actual																														
	9	For Preparation of Detailled Engineering and Bid Preparations for New Bridges in 2019 Package I Samalari, Sana Uatolari-Laisorulai, Sumaco (Lacluta Uma Tolu), Malos Matadoro-RTK, Comoro Motaulun	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	Vox Da Vinci Consultant Engineering Lda	RDTL	Plan																														
							Actual																														
	10	Consulting Services for preparing of design the intersection in the existing Dili Liquica Road to connect access Road From Tibar Bay Port (Preparasaun Desenho detalhado ba Estrada, Electricidade e Aguas ba Funcionamentu Portu Tibar)	MINISTERIO DAS OBRAS PUBLICAS	FI	TPF Consultores de Engenharia S.A (Portugal) JV with TPF Timor Unip Lda, (Timor-Leste)	RFP/009/MOP-2019	Plan																														
							Actual																														
	11	Selection of Design Consultant to Prepare Preliminary Design and Tender Documents for the Upgradition of Liquica 150 KV/20KV Substation to Supply Power to Tibar Bay Port	MINISTERIO DAS OBRAS PUBLICAS	FI	PT. Malmass Mitra Teknik (Indonesia)	RFP/041/MOP-2019	Plan																														
							Actual																														
	12	Zebra Cross Marking in The Capital City of Dili (162)	MINISTERIO TRANPORTES E KOMUNIKASAUN	LM-BS	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	Plan																														
							Actual																														
	13	Additional Service Statement of Work for Year 2021 - Government Resource Planning Solutions & Supporting IT Infrastructure System Implementation & Support Agreement	MINISTERIO FINANCAS	FI	Freebalance	RDTL-167250	Plan																														
							Actual																														
	14	Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project	MINISTERIO DAS OBRAS PUBLICAS	FI	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	RFP/039/MOP-2019	Plan																														
							Actual																														
	15	Estudos e plano de concepção para Planeamento Urbano a nivel nacional	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	FI	Intersismert S.A in Joint Venture with Quaternaire Portugal Consultoria para o Desenvolvimento, SA	RFP/025/MPW-2013	Plan																														
							Actual																														
	16	Plano Lidar e Mapeamento a todo o territorio, segunda fase	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	FI	PT. Karvak Nusa Geomatika, Indonesia	SSS/006/MPIE-2016	Plan																														
							Actual																														
	17	Supply, Installation, Configuration and Comissioning of National Optical Fiber Backbone Network	GABINETE DO PRIMEIRO MINISTRO	FI	Timor Telecom S.A.	RT/024/GPM-2017	Plan																														
							Actual																														
	18	Supply, Installation, Configuration and Comissioning of Hardware and Software for the Expantion of Data Center Infrastructure | Office of Prime Minister	GABINETE DO PRIMEIRO MINISTRO	FI	Joint Venture of CMC System Integration Company Limmited and Viettel Timor-Leste Unipessoal, LDA	ICB/025/GPM-2017	Plan																														
							Actual																														
	19	Road Network Upgrading Project (RNUP),Upgrading and Maintenance of Dili (Airport Junction)- Tibar Road- Section 2 : Tasitolu - Tibar	MINISTERIO DAS OBRAS PUBLICAS	FI	CINA WU YI CO.LTD	ICB/032/MPWTC-2015	Plan																														
							Actual																														
	20	Operation And Maintenance Services For National Power Grid Project	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	China Nuclear Industry 22ND Construction Co; LTD	La mensiona iha Kontracto	Plan																														
							Actual																														
	21	Revitalization foot Ball Stadium and tribune Building	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	FI	Marino enterprises Lda		Plan																														
							Actual																														
	22	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	MINISTERIO DAS OBRAS PUBLICAS	FI	Shangai Construction Group Co .,Ltd		Plan																														
							Actual																														
	23	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Excentions)	MINISTERIO DAS OBRAS PUBLICAS	FI	CBMI Construction Co. Lda Jv Chongqing Roads Engineering		Plan																														
							Actual																														
	24	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	MINISTERIO DAS OBRAS PUBLICAS	FI	CBMI Construction Co. Lda Jv Chongqing Roads Engineering		Plan																														
							Actual																														
	25	Consultant Supervision Road network Upgrading Sector Project, Upgrading and maintenance of Maubara -	MINISTERIO DAS OBRAS	FI	Dongsung Engineering Co,Ltd JV with		Plan																														

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

ABRIL

NARAN Eng. PEDRO DE LURDES ALVES

MUNICIPIO MUNICIPIO DILI NO POSTOS

NU.	E DISTI	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	NARAN COMPANHA	NUMERO KONTRATU		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fr 29	Sa 30	Observasaun
		Karimbala and Alabae - Mota Ain Roads, and Baucau - Lautem	PUBLICAS		Kunhwa Engineering and Consulting Co.Ltd.		Actual																														
	26	Preparation of Detailed engineering design for Dili Urban Road	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	KIAT unip JV PT Purnajasa Bimapratama		Plan																															
							Actual																															
	27	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	MINISTERIO DAS OBRAS PUBLICAS	FI	China Railway Int. Group co, jv with China overseas		Plan																															
							Actual																															
	28	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	MINISTERIO DAS OBRAS PUBLICAS	FI	INTERCONTINENTAL CONSULTANTS AND TECHNOCRATS PVT.LTD IN ASSOCIATION WITH INFRA CONSULTANTS IN THE PHILS. (ICP) INC. (PHILIPPINES) AND DEZEMVOLVE TIMOR LESTE (DETIL) E CONSULTANT		Plan																																	
							Actual																															
	29	Manutensaun ba Edificio no Equipamentu laboratorium dianostika veternaria	MINISTERIO AGRIKULTURA E PESCAS	LM-BS	Dreams Come True, Lda	RDTL-PO:2019-15736	Plan																														
							Actual																															
REGIONAL	1	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	Raya Consulting Lda	MPW-CS-2000020	Plan																															
							Actual																															
	2	Consultant Design (M-L & L-N) & Supervision (D-L & T-G, Tasi Tolu -tibar 4 L)	MINISTERIO DAS OBRAS PUBLICAS	FI	KATAHIRA & ENGINEERS INTERNATIONAL	time base	Plan																															
							Actual																															
	3	The Integrated and Maintenance Service	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	wartsila Indonesia R.P (Interest Late Payment P.T Warstila Indonesia (RP)	SSS-008-MOPTC-2016	Plan																															
							Actual																															

Note :

Planu Periode Inspesaun iha Tereino

Implementasun Periode Inspesaun iha Tereino

Relatorio Avaliasaun Mensal iha Dili

Inspesaun Pagamento

Prepara husi

Arq. Pedro de Lurdes Alves
Eng. ADN I.P. Municipio Dili

Certifika Husi

Eng. Emerenciana da Costa Maia Freitas
Coord. da Unidade de Controlo e Validacao de Qualidade ADN, I.P.

Aprova Husi:

Eng. Januario Maia Guterres
Adjunto Diretur Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN ANEXO - D#DAMACLN

Naran projeto : Detailed Engineering Design (DED) for the New Construction of Ministerio para os Assuntos dos Combatentes da Libertacao Nacional (MACLN) Offices

Kompanha : Uma De Construcao

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	4/Fev/2022	Dili/Dom Aleixo	1. Egidio Goncalves	Tekniku EPAS	1	Tuir aprezentasaun husi konsultor ba servisu inception report	
					2	Husu ba konsultor atu hadia no kompleta input hirak nebe parte MOP no A D N hato'o liga ba assuntu arkitekhtura (modelu tata ruangan no seluk tan), *kompleta molok hakat ba faze tuir mai (Iterim report Development Design) bazeia ba TOR kontrato	
			2. Julmira S. Sampaio		3		
					4		
					5		
II	11/Fev/2022	Dili/Dom Aleixo	1. Egidio Goncalves	Tekniku EPAS	1	Tuir aprezentasaun husi konsultor ba servisu Interim report (Preliminary Design)	
					2	Husu ba konsultor atu hadia no kompleta input hirak nebe parte MOP no A D N hato'o liga ba, design struktural, Electrikal no Spesifikasaun tekniku, *kompleta molok hakat ba faze tuir mai (Draft final report) bazeia ba TOR kontrato	
			2. Julmira S. Sampaio		3		
					4		
					5		
III	21-Mar-22	Dili/Dom Aleixo	1. Egidio Goncalves	Tekniku EPAS		Rekomendasaun pagamento ba servisu Iception report, Iterim report (Preliminary design) ho total 30%, bazeia ba TOR	
					1	Husu ba konsultor atu hadia no kompleta input hirak nebe parte MOP no A D N hato'o liga ba, design struktural, Electrikal no Spesifikasaun tekniku.	
			2. Julmira S. Sampaio		2	Husu atu iha partisipasaun husi key experts wainhira halo aprezentasaun tuir mai	
					3		
					4		
IV	7-Apr-22	Dili/Dom Aleixo	1. Egidio Goncalves	Tekniku EPAS		**Halo diskusaun ho Diretor konsultor Uma De Construcao**	
					1	parte EPAS-A D N, husu ba konsultor atu kompleta lai input no sujestaun hirak nebe husi MOP no A D N, hato'o molok submete pagamento Interim report (development design)	
			2. Julmira S. Sampaio		2	ba pagamento agora parte EPAS-A D N, sei rekomenda deit ba servisu Inception no Interim report (preliminary design) ho total porcento 30%	
					4		
					5		
V	22-Apr-22	Dili/Dom Aleixo	1. Egidio Goncalves	Tekniku EPAS	1	proseso rekomendasaun pagamento ba servisu Iception report, Iterim report (Preliminary design) ho total 30%	
					2		
			2. Julmira S. Sampaio		3		
					4		
					5		

ANEXO-C1#DAMACLN

Back-up Data

Naran Projeto : Detailed Engineering Design (DED) for the New Construction of Ministerio para os Assuntos dos Combatentes da Libertacao Nacional (MACLN) Offices

No. kontratu : 38/MACLN/IX/2021

Data Inspesaun : 7 & 21 Abril 2022

Fatin Inspesaun :

Koordinadas :

Start Point : Long : 125.56252621 Latetude : -8.55699929

End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Egidio Gonçalves

2. Julmira Soares Sampaio

Sketch & Foto Desenho



Observasaun iha tereno no Foto Aktual

Parte EPAS-ADN no Diretor konsultor Uma De Construção Diskuti ba assuntu pagamento nebe parte konsultor submete. Pagamento ba Inception no Iterim report.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2#DA MACLN..

SUMMARY BACK UP PROGGRESS

Project Name	**Design de Edificio do MACLN**
Contract No.	**04/MACLN/III/2022**
Consultant	**Uma De Construcao Unip. Lda.**
Amount Contract	**$ 88,510.00**

Number of Invoice Request	DESCRIPTION	PREVIOUS BILL	%	THIS BILL	%	UP TO DATE	%
1	Progress Claim No. 1 (Inception report 10% no Interim Report (Preliminary Design) 20%	$ -	0.00%	$ 26,553.00	30.00%	$ 26,553.00	30.00%

Cheked by :

Julimira S. Sampaio
Eng. Municipio Dili ADN, I.P.

Egidio Goncalves
Eng. Municipio Dili ADN, I.P.

Verified by :

Arch. Francisco X. de Deus Jeronimo
Senior Eng. Ba Projetu Edificio Publico e Agua Saneamento ADN, I.P.

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN KADA PROJETO
ANEXO - D #VR2

Naran projeto: Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN	Asinatura
VI	23-Mar-22	Dili/Vera Cruz	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Aktividade Survey husi ekipa A D N, Obras Publicas, Dono do Projeto hodi halo kross cek ba dadus penurunan husi edificio nebe parte kompanhia relata ba konsultor	
					2	Husu ba konsultor atu nafatin halo kross cek data penurunan kada semana ba edificio refere	
VII	4-Apr-22	Dili/Vera Cruz	Egidio Goncalves, Julmira Soares Sampaio	Tekniku		Weekly meeting: diskuti proposta ba mudansa servisu hirak nebe parte kompanhia hato'o mai konsultor hanesan: ***Wall Partions, Ceilling, Roof top water proofing and pumps***	
					1	Husu ba parte konsultor atu hare didiak ba assuntu tekniku no espisifikasaun husi material hirak nebe proposta, hodi bele garanteia qualidade	
					2	Sei koordena ho parte verifikasaun (UAP) A D N, ba ssuntu refere	
VIII	22-Apr-22	Dili/Vera Cruz	Egidio Goncalves, Julmira Soares Sampaio	Tekniku		Weekly meeting: Diskuti_***proposta kompanhia nebe aseita ho rezultadu verifikasaun A D N, I.,_Proposta ba extensaun tempo konstrusaun no proposta Prosedimento ba aprovasaun VO-1***	
					1	Husu ba dono projeito atu assileira proseso aprovasaun VO-1 tuir kontrato	
					2	Husu ba konsultor atu hare didiak ba timeline servisu kompanhia molok hato'o karta extensaun ba dono do projeito	

ANEXO C1 #VR2

Back-up Data

Naran Projeto : Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building

No. kontratu : RFP/012/TR-2019

Data Inspesaun : 4 & 22 Abril 2022

Fatin Inspesaun : Caicoli, Vera Cruz - Dili

Koordinadas :

Start Point : Long : 125.57580146 Latetude : -8.56040158

End Point : Long : Latetude :

Naran Inspector : 1. Egidio Gonçalves

2. Julmira Soares Sampaio

Foto/Desenho	Observasaun iha tereno no Foto Aktual
	Weekly meeting I: diskuti proposta ba mudansa servisu hirak nebe parte kompanhia hato'o mai konsultor hanesan: ***Wall Partions, Ceilling, Roof top water proofing and pumps***
	Weekly meeting II: ***Diskuti_proposta kompanhia nebe aseita ho rezultadu verifikasaun A D N, I.,_Proposta ba extensaun tempo konstrusaun no proposta Prosedimento ba aprovasaun VO-1***

INVOICE - 12 (1 June 2021 - 30 June 2021)

FIN- 2

SUMMARY OF COSTS

Consulting Services For Construction Supervision for Tribunal Distrital Dili Office Building

ANEXO C2# VR2

SUMMARY

CONTRACT			CONSULTANT												ADN RECOMMENDED					
ITEM	COST		PREVIOUS INVOICE			INVOICE - 12 (1 June 2021 - 30 June 2021)			Up to Date			CONTRACT REMAINING			Previous Invoice		INVOICE - 12 (1 June 2021 - 30 June 2021)		To Date	
			Amount (USD)		%	Amount (USD)		%	Amount (USD)		%	COST		%	Amount $	%	Amount $	%	Amount $	%
Competitive Components																				
Remuneration, Expert (Key and Non Key) DACRE	USD	304,480.00	USD	227,562.48	74.74%	USD	14,850.50	4.88%	USD	242,412.98	79.62%	USD	62,067.02	20.38%	$ 194,296.03	34.26%	$ 14,738.85	2.60%	$ 209,034.87	36.85%
Remuneration, Expert (Key and Non Key) AEC	USD	58,100.00	USD	38,554.20	66.36%	USD	4,560.00	7.85%	USD	43,114.20	74.21%	USD	14,985.80	25.79%	$ 26,829.00	4.73%	$ 3,472.31	0.61%	$ 30,301.31	5.34%
Remuneration, Support Staff (AEC)	USD	80,920.00	USD	53,257.60	65.82%	USD	4,760.00	5.88%	USD	58,017.60	71.70%	USD	22,902.40	28.30%	$ 43,854.22	7.73%	$ 4,528.46	0.80%	$ 48,382.68	8.53%
Other Expenses (DACREA)	USD	31,740.00	USD	18,378.26	57.90%	USD	2,246.33	7.08%	USD	20,624.59	64.98%	USD	11,115.41	35.02%	1306731.10%	2.30%	$ 2,246.33	0.40%	$ 15,313.64	2.70%
Other Expenses (AEC)	USD	91,957.00	USD	60,794.76	66.11%	USD	5,321.00	5.79%	USD	66,115.76	71.90%	USD	25,841.24	28.10%	$ 60,050.41	10.59%	$ 5,321.00	0.94%	$ 65,371.41	11.53%
Sub-Total	**USD**	**567,197.00**	**USD**	**398,547.29**	**70.27%**	**USD**	**31,737.83**	**5.60%**	**USD**	**430,285.13**	**75.86%**	**USD**	**136,911.87**	**24.14%**	**$ 338,096.97**	**59.61%**	**$ 30,306.95**	**5.34%**	**$ 368,403.91**	**64.95%**
Non-Competitive Components																				
Provisional Sums	USD	-	USD	-	-	USD	-	-	USD	-	-	USD	-	-						
Contingency	USD	-	USD	-	-	USD	-	-	USD	-	-	USD	-	-						
Sub-Total	**USD**	-	**USD**	-	-	**USD**	-	-	**USD**	-	-	**USD**	-	-						
Total Cost of INVOICE - 12	**USD**	**567,197.00**	**USD**	**398,547.29**	**70.27%**	**USD**	**31,737.83**	**5.60%**	**USD**	**430,285.13**	**75.86%**	**USD**	**136,911.87**	**24.14%**	**$ 338,096.97**	**59.61%**	**$ 30,306.95**	**5.34%**	**$ 368,403.91**	**64.95%**

Prepared by,

1. Egidio Goncalves

2. Julmira S. Sampaio
Tek. Municipio Dili, ADN, I.P

Verified by,

Francisco Xavier de Deus Jeronimo
Enginheiro Senior ba Projeito Edificio Publiku Be'e Saneamento, ADN, I.P

Certified by,

Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN ANEXO D #NASIONAL 1

Naran projeto : Detailed Engineering Design (DED) of Dili Water Supply

Kompanha : Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	8/Fevereiro/2022	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan: **Hydraulic modeling**	
					2		
					3		
					4		
					5		
II	18/Fevereiro/2022	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan **Topographic survey**	
					2		
					3		
					4		
					5		
III	7/Abril/2023	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan No. 5 Survey and Mapping = 8.34%	
					2	Rekomendasaun pagamento ba servisu hanesan No. No. 6 Design Development = 8.34%	
					3	Tot. porcento pagamento ate a data = **56.84%**	
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2# NASIONAL 1

SUMMARY BACK UP PROGGRESS

Project Name		*Consulting Services for Detailed Engineering Design of dili Urban Water*
Contract No.		**RFP/038/MOP-2019**
Consultant		*Donsung Engineering Co. LTD (korea) in joint venture with Kunhwa Engineering & Consulting Co. LTD (Korea)*
Amount Contrcat (Cost of Services + Prov Sum)		*$ 2,718,150.00*
	Cost of Services	$ 2,268,150.00
	Provisional Sum	$ 450,000.00

Number of Invoice Request	DESCRIPTION	PREVIOUS BILL	%	THIS BILL	%	UP TO DATE	%
1	Progress Claim No. 1 (Inception report)	$ -	0.00%	$ 226,815.00	8.34%	$ 226,815.00	8.34%
2	progress Claim No. 2 Interim Report - Preliminary Design	$ 226,815.00	8.34%	$ 226,815.00	8.34%	$ 453,630.00	16.69%
3.1	progress Claim No. 3 Survey and Mapping Report - Geotechnical Investigation 3.1 (provisional sum)	$ 453,630.00	16.69%	$ 95,600.00	3.52%	$ 549,230.00	20.21%
3.4	progress Claim No. 3 Survey and Mapping Report - Borehole Assessment 3.4 (provisional sum)	$ 549,230.00	20.21%	$ 30,766.46	1.13%	$ 579,996.46	21.34%
3.5	progress Claim No. 3 Survey and Mapping Report - Existing Pipe Identification 3.5 (provisional sum)	$ 579,996.46	21.34%	$ 87,300.00	3.21%	$ 667,296.46	24.55%
3.6	progress Claim No. 3 Survey and Mapping Report -Water Quality Test 3.6 (provisional sum)	$ 667,296.46	24.55%	$ 3,410.42	0.13%	$ 670,706.88	24.68%
3.7	progress Claim No. 3 Survey and Mapping Report -Surface Water Quantity Survey 3.7 (provisional sum)	$ 670,706.88	24.68%	$ 33,200.00	1.22%	$ 703,906.88	25.90%
3.8	progress Claim No. 3 Survey and Mapping Report -Satelite Mapping 3.8 (provisional sum)	$ 703,906.88	25.90%	$ 4,000.00	0.15%	$ 707,906.88	26.04%
3.2	progress Claim No. 3 Survey and Mapping Report -GPS Survey g 3.2 (provisional sum)	$ 707,906.88	26.04%	$ 59,290.00	2.18%	$ 767,196.88	28.22%
4	progress Claim No. 4 Hydraulic Modelling report	$ 767,196.88	28.22%	$ 226,815.00	8.34%	$ 994,011.88	36.57%
3.3	progress Claim No. 3 Topografic Survey	$ 994,011.88	36.57%	$ 97,344.79	3.58%	$ 1,091,356.67	40.15%
5	progress Claim No. 5 Survey and Mapping	$ 1,091,356.67	40.15%	$ 226,815.00	8.34%	$ 1,318,171.67	48.50%
6	progress Claim No. 6 Design Development	$ 1,318,171.67	48.50%	$ 226,815.00	8.34%	$ 1,544,986.67	56.84%

Checked by :

Julmira S. Sampaio
Eng. Municipio Dili ADN, I.P.

Egidio Goncalves

Verified by :

Arch. Francisco X. de Deus Jeronimo
Senior Eng. Ba Projeitu Edificio Publico e Agua Saneamento
ADN, I.P.

Certified by :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN ANEXO D#NASIONAL 20

Naran projeto : Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project

Kompanha : ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	28/Fev/2022	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan: **Water Resources Development Report & Lospalos Water Treatment Report**	
					2		
					3		
					4		
					5		
II	4/7/2022	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan: **R1. Classical Topography Survey in Baucau and Same (invoice 30)= 1.17%**	
					2	R2. Topography Survey (Drone) in Baucau (**invoice 31**) = **1.55%**	
					3	Total porcento pagamento ate a data = **56.16%**	
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO
C2#NASIONAL 20

SUMMARY BACK UP PROGRESS

Project Name	**Counsulting Services For Detailed Engineering Design Timor Leste Four Municipal Capital Water Supply and Sanitation Project**	
Contract No.	**RFP/039/MOP-2019**	
Contractor	**ADP Timor Leste, Unip. Lda. In Joint Venture with Engidro Engineering Solutions LDA (Portugal)**	
Amount Contract (Cost of Services + Prov. Sum)	**$**	**2,903,356.59**
Cost of Services	$	1,442,395.00
Provisional Sum	$	1,460,961.59

Number of Invoice request	DESCRIPTION	Previous Bill	%	This Bill	%	Up to Date	%
1	Progress Claim No 1. (Feasibility Study)	$ -	0.00%	$ 144,239.50	4.97%	$ 144,239.50	4.97%
2	Progress Claim No 2. (Preliminary Design Report)	$ 144,239.50	4.97%	$ 216,359.25	7.45%	$ 360,598.75	12.42%
8	Progress Claim No 3.b (Topographical Survey in Lospalos)	$ 360,598.75	12.42%	$ 17,339.91	0.60%	$ 377,938.66	13.02%
12	Progress Claim No 3.d. (Ground Water Investigation in Lospalos)	$ 377,938.66	13.02%	$ 170,900.00	5.89%	$ 548,838.66	18.90%
5	Progress Claim No 3.a. (Water Resources Investigation- Viqueque Municipal Capital)	$ 548,838.66	18.90%	$ 62,400.00	2.15%	$ 611,238.66	21.05%
9	Progress Claim No 3.c. (Ground Water Investigation in Same)	$ 611,238.66	21.05%	$ 209,100.00	7.20%	$ 820,338.66	28.25%
13	Water Surface Monitoring in Same, Lospolas & Viqueque	$ 820,338.66	28.25%	$ 54,898.71	1.89%	$ 875,237.37	30.15%
15	Topography Survey (Drone) in Baucau, Same, Lospalos & Viqueque	$ 875,237.37	30.15%	$ 107,500.00	3.70%	$ 982,737.37	33.85%
16	Topography Survey in Same & Viqueque	$ 982,737.37	33.85%	$ 24,083.46	0.83%	$ 1,006,820.83	34.68%
18	Water Quality Monitoring (Same, Lospalos, Baucau & Viqueque)	$ 1,006,820.83	34.68%	$ 47,566.85	1.64%	$ 1,054,387.68	36.32%
20	Water Resource Investigation (Baucau)	$ 1,054,387.68	36.32%	$ 21,750.00	0.75%	$ 1,076,137.68	37.07%
21	Surface Water Monitoring (Viqueque & Baucau)	$ 1,076,137.68	37.07%	$ 20,575.21	0.71%	$ 1,096,712.89	37.77%
24	Geotechnical Ground Investigation (Lospalos, Baucau & Viqueque)	$ 1,096,712.89	37.77%	$ 127,083.33	4.38%	$ 1,223,796.22	42.15%
19	Drone Survey (Lospalos and Viqueque)	$ 1,223,796.22	42.15%	$ 21,250.00	0.73%	$ 1,245,046.22	42.88%
25	Classic Topographical Survey (Viqueque)	$ 1,245,046.22	42.88%	$ 18,017.47	0.62%	$ 1,263,063.69	43.50%
22	Water Resources Development Report & Lospalos Water Treatment Report	$ 1,263,063.69	43.50%	$ 288,479.00	9.94%	$ 1,551,542.69	53.44%
30	R1. Classical Topography Survey in Baucau and Same	$ 1,551,542.69	53.44%	$ 34,073.30	1.17%	$ 1,585,615.99	54.61%
31	R2. Topography Survey (Drone) in Baucau	$ 1,585,615.99	54.61%	$ 44,968.75	1.55%	$ 1,630,584.74	56.16%

Prepara husi:

Julmira Soares Sampaio — Eguino Goncalves
Eng. Municipio Dili- ADN, I.P

Verifika husi:

Francisco Xavier de Deus Jeronimo
Enginheiro Senior ba Projeito Edificio Publiku Be'e Saneamento- ADN, I.P

Sertifika husi:

Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validasaun de Qualidade- ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN KADA PROJETO ANEXO D#VR7

Naran projeto: Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	14/Fev/2022	Dili/Vera Cruz	Egidio Goncalves & Julmira Soares Sampaio	Tekniku	1	Husu ba Ministerio do Interior (dono do projeto) atu bele lalais hetan karta aprovasaun ba proposta servisu adicional husi Ministro atu nunu'e bele kontinua hahu servisu iha terrenu	
					2	Husu ba dono do projeto atu toma medida halo atuasaun ba komunidade hirak nebe okupa area nebe partensi ba konstrusaun edificio QG PNTL Caicoli-Dili	
					3	Projeto refere seidauk kontinua fali servisu iha terrenu	
					4		
					5		
II	9-Mar-22	Dili/Vera Cruz	Egidio Goncalves & Julmira Soares Sampaio	Tekniku		**INKONTRU;** Tekniku Ministerio do Interior relata imformasaun konaba proposta adicional nebe parte konsultor supervizaun submete ba Ministerio;	
					1	Rekomenda ba dono projeto atu hare didiak proposta refere hodi verifika tuir kontrato	
					2	Rekomenda ba dono projeto atu iha koordenasaun nebe diak ho parte Aprovisionameto Intrerior nian no C N A atu hare didiak kontiudu husi kondisaun kontrato ba konsultor hodi fo Parecer/Ideas ruma liga ba proposta konsultor nian.	
II	13-Apr-22	Dili/Vera Cruz	Egidio Goncalves & Julmira Soares Sampaio	Tekniku		**INKONTRU;** diskuti ho parte kontraktor nebe rezeita hodi la assina rezultadu verifikasaun husi A D N ba servisu adicional pondasi nebe konsidera montante kiik liu husi proposta nebe parte kompanhia hato'o no kompanhia husu atu aumenta item servisu foun balun nebe iha ligasaun ho pondasi ida nebe antes ne'e seidauk halo verifikasaun	
					1	parte governo (MOP, A D N, MPC no MoI) husu ba kompanhia atu prepara justifikasaun tekniku liga item servisu foun hirak nebe seidauk inklui iha verifikasaun liu ba	
					2	justifikasaun tekniku hirak nebe prepara tenki hetan verifikasaun husi konsultor supervizaun molok submete mai owner hodi halo aprovasun	
					3	justifikasaun tekniku hirak ne'e tenki submete iha tempo badak	

ANEXO C1 #VR7

Back-up Data

Naran Projeto : Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste

No. kontratu : RFP/012/TR-2019

Data Inspesaun : 1, 8 & 13 Abril 2022

Fatin Inspesaun : Caicoli, Vera Cruz - Dili

Koordinadas :

Start Point : Long : 125.57809677 Latetude : -8.55831917

End Point : Long : Latetude :

Naran Inspector : 1. Egidio Gonçalves

2. Julmira Soares Sampaio

Foto/Desenho	Observasaun iha tereno no Foto Aktual
	Reuniaun hodi ***diskuti ho parte kontraktor nebe rezeita hodi la assina rezultadu verifikasaun husi A D N ba servisu adicional pondasi nebe konsidera montante kiik liu husi proposta nebe parte kompanhia hato'o no kompanhia husu atu aumenta item servisu foun balun nebe iha ligasaun ho pondasi ida nebe antes ne'e seidauk halo verifikasaun***
	

ANEXO C1 #VR7

Back-up Data

Naran Projeto : Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste

No. kontratu : RFP/012/TR-2019



Reuniaun hodi ***diskuti ho parte kontraktor nebe rezeita hodi la assina rezultadu verifikasaun husi A D N ba servisu adicional pondasi nebe konsidera montante kiik liu husi proposta nebe parte kompanhia hato'o no kompanhia husu atu aumenta item servisu foun balun nebe iha ligasaun ho pondasi ida nebe antes ne'e seidauk halo verifikasaun***



Esplika ba parte tekniku dono projeto (MoI) no tekniku kompanhia (Sanghai) konaba differencia montante husi rezultadu verifikasaun A D N no proposta kompanhia atravez husi konsultor supervizaun. Parte kompanhia komprende no intende ho rezultadu husi A D N.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN KADA PROJETO ANEXO D#VR..

Naran projeto: Supervision Consulting Services for New Construction of Memorial Monument of The Santa Cruz

No.	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No.	INSTRUSAUN / REKOMENDASAUN	Asinatura
IV	4-Mar-22	Dili/Vera Cruz	Egidio Goncalves & Julmira Soares Sampaio	Tekniku		**Weekly Meeting**: Diskuti item servisu PORTICO (Main Gate Enterance) servisu Strutura nebe iha DED initial parte konsultor FIHIR (DED konsultor) la aneksu dok. analisa strutura. Parte konsultor supervizaun no kompanhia konsidera DED refere la iha razaun fundamental ba assuntu tekniku, Ho ida ne'e mak:	
					1	Parte kompanhia no konsultor supervizaun aprezenta shop-drawing hodi halo Re-Kalkulasaun ba strutura PORTICO	
					2	Aprezenta mos servisu sira seluk nebe iha diferensia entre BOQ, Dezenhu ho kondisaun aktual hanesan, Moru haleu no walk path iha area rate	
					3	Rekomenda wainhira halo aprezentasaun ba mudancas servisu tenki hato'o imformasaun kompleto entre Desain original no Actual	
V	22-Mar-22	Dili/Vera Cruz	Egidio Goncalves & Julmira Soares Sampaio	Tekniku		**Weekly Meeting:** Kontinua Diskuti item servisu PORTICO (Main Gate Enterance) servisu Strutura nebe iha DED initial parte konsultor FIHIR (DED konsultor) la aneksu dok. analisa strutura. Parte konsultor supervizaun no kompanhia konsidera DED refere la iha razaun fundamental ba assuntu tekniku, Ho ida ne'e mak:	
					1	Parte konsultor FIHIR nebe prepara DED hodi husu atu mantein strutura nebe iha ona la bele iha mudancas	
V	1-Apr-22	Dili/Vera Cruz	Egidio Goncalves & Julmira Soares Sampaio	Tekniku		**Weekly Meeting:** Kontinua Diskuti item servisu PORTICO (Main Gate Enterance) servisu Strutura nebe iha DED initial parte konsultor FIHIR (DED konsultor) la aneksu dok. analisa strutura. Parte konsultor supervizaun no kompanhia konsidera DED refere la iha razaun fundamental ba assuntu tekniku, Ho ida ne'e mak:	
					1	Husu ba parte dono do projeto atu hato'o karta justifikasaun ba konsultor supervizaun no ekipa PMU hodi deklara katak antes ne'e la iha aneksu dokumentos ba servisu analisa strutura ba PORTICO, hodi nune'e servisu bele avansa ho analisa strutura foun nebe prepara husi parte kompanhia (Bobolait) no hetan aprovasun husi konsultor supervizaun (Aria)	
					2	Husu ba parte dono do projeto atu fo konhesemento ba familia matebian hirak nebe RATE hetan afeita husi area ***walk side***	
					3	Husu ba konsultor atu submete dezenhu no BOQ ba servisu parede/moru nebe antes ne'e la temi iha kontrato original	

ANEXO-C1#DAMACLN

Back-up Data

Naran Projeto : Supervision Consulting Services for New Construction of Memorial Monument of The Santa Cruz

No. kontratu : 38/MACLN/IX/2021

Data Inspesaun : 1 Abril 2022

Fatin Inspesaun :

Koordinadas :

Start Point : Long : 125.58544066 Latetude : -8.56342821


End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Egidio Gonçalves

2. Julmira Soares Sampaio

Sketch & Foto Desenho



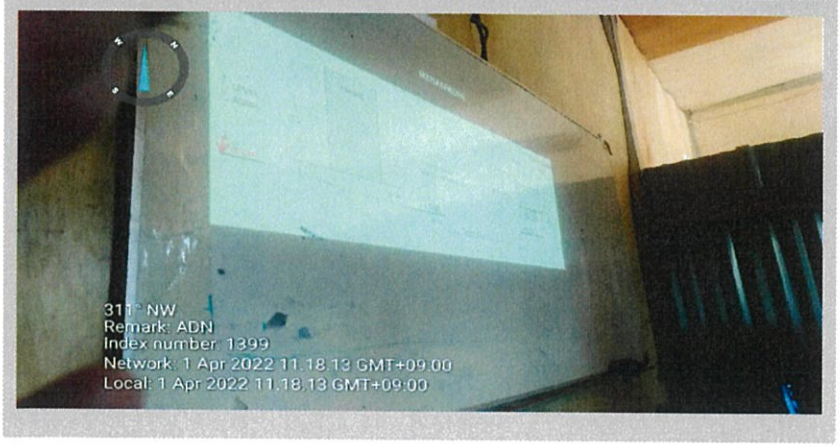

Observasaun iha tereno no Foto Aktual

Diskuti item servisu PORTICO (Main Gate Enterance) servisu Strutura nebe iha DED initial parte konsultor FIHIR (DED konsultor) la aneksu dok. analisa strutura. Parte konsultor supervizaun no kompanhia konsidera DED refere la iha razaun fundamental ba assuntu tekniku.

ANEXO-C1#DAMACLN

Back-up Data

Naran Projeto : Supervision Consulting Services for New Construction of Memorial Monument of The Santa Cruz

No. kontratu : 38/MACLN/IX/2021





Parte kompanhia kontinua ezekuta servisu iha terrenu hodi halo excavasaun ba area portico, kapela no parede.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN ANEXO D#NASIONAL 20

Naran projeto : Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project

Kompanha : ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	28/Fev/2022	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan: **Water Resources Development Report & Lospalos Water Treatment Report**	
					2		
					3		
					4		
					5		
II	4/7/2022	Dili/Nasional	Egidio Goncalves, Julmira Soares Sampaio	Tekniku	1	Rekomendasaun pagamento ba servisu hanesan: **R1. Classical Topography Survey in Baucau and Same (invoice 30)**	
					2	R2. Topography Survey (Drone) in Baucau (**invoice 31**)	
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		

MINISTÉRIO DO PLANO E ORDENAMENTO
VI.I GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Egidio Goncalves

Municipio MUNICIPIO DILI NO POSTOS

2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		ABRIL fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	fr 29	Sa 30	Obs
CRISTO REI (CR)	9	Consulting Services for Detail Engineering Design (DED) for Pediatric and ICCU Building in Guido Valadares National Hospital	Philcoei International, Inc. In JV with Luis and Associates, Co	SSS/035/MOPTC-2017	FI	MDS	Plan																														
							Actual																														
	35	Consultancy to develop A feasibility study and master plan Guido Valadares National Hospital (Bem Serviso)	Mafra Consultante Unipessoal Lda	FBS-DNA-MOP-19018-B	LM/BS	MDS	Plan																														
							Actual																														
DOM ALEIXO (DA)	9	Consulting services for DED of the new Ministry of Commerce Industry and Enviroment Training Center	Vitor Hugo Coordenacao e Gestao de projetos, SA atraves de emprendimento conjunto com a Quadramor Timor Sistemas de Engenharia, S.A	RFP/030/MCIE-2013	FI	MTCI	Plan																														
							Actual																														
	10	Detail Engineering design (DED) of The New Ministry of Commerce, Industry and Environment	Philkoei International Inc. in JV with Arch Haus Asia Consultant, Inc	RFP/029/MCIE-2013	FI	MTCI	Plan																														
							Actual																														Sevisu Konsultant Design, sei adjusta tuir planu husi Projeto Nain
	58	Consulting Services of Spatial Planing of Timor Leste	Intersismet in Joint Venture With Quetenaire Portugal Consultoria para o Desenvolvimento SA		FI	MPO	Plan																														
							Actual																														
	46	Revitalization of Community Aitarak Laran	TPF Timor Unip. Lda.	MPW-S-190272	LM	MOP	Plan																														
							Actual																														
		Detail Engineering Design MACLN Building	Uma de Construcão Unip. Lda.		LM	MACLN	Plan																														
							Actual																														
NAIN FETO (NF)	2	Consulting Services for detailed Engineering Design of CAC Office Building	Imagem, Design and Arquitectura, Lda (IDA) in Association with Vaz, Dotti & Silva, Lda (VDS)	RFP/004/MPW-2013	FI	CAC	Plan																														
							Actual																														
VERA CRUZ	2	Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building	Dacrea Desing and Engineering Consultant (Dacrea) (Indonesia) In Association with Archtimor Engineering Consultants (AEC) as Sub-consultant (Timor-Leste)	RFP/012/TR-2019	FI	TR	Plan																														
							Actual																														
	7	Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste	PT. Ceriajasa Cipta Mandiri in Joint Venture with JKC Consultant Engineering Unipessoal Lda	RPF/087/MI-2017	FI	MI	Plan																														
							Actual																														
	8	Consulting Services for Detail Engineering Design of the IGE Office, Workshop and Warehouse Complex Building	Scope Australia Pty, Ltd	RFP/039/MPW-2013	FI	MOP	Plan																														
							Actual																														
	9	Consulting Services for Detailed Architecture and Engineering Design for Press Building Project	CGM Consultants & Associates Incorporated, Lda.	SSS/051/SECOM-2015	FI	SECOM	Plan																														
							Actual																														
	10	Consulting Services for Feasibility Study of the New Buildings for RTTL. P.E and Tatoli P.I.	Potevio Company Limited	RDTL	FI	SECOM	Plan																														
							Actual																														Sevisu Konsultant Design, sei adjusta tuir planu husi Projeto Nain
	15	Consulting Services of Detailed Engineering Design of Sport Complex and Building at Region of Dili	ATT consultants Co. Ltd JV SQ Architect and Planner Co. Ltd	RFQ/314/SEJD-2016	FI	SEJD	Plan																														
							Actual																														
	24	Detailed Engineering design of E-Recruitment Building CFP	De Oliveira design	SSS/045/MT-2017	LM	CFP	Plan																														
							Actual																														
		Supervision Consulting Services for New Construction of Memorial Monument of The Santa Cruz	Aria Unip. Lda. JV With Jamori Lda.	RFP/042/MACLN-2021	LM	MACLN	Plan																														
							Actual																														
NASIONAL	1	Detailed Engineering Design (DED) of Dili Water Supply	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOP-2019	FI	MOP	Plan																														
							Actual																														
	3	Feasibility Study of Surface Water Resource Development for the Water Supply of Dili Metropolitan Area	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/002/MOP-2019	FI	MOP	Plan																														
							Actual																														
	4	Pre- Feasibility Study of a Ground Water Resources Development Project for the Water Supply of Dili Metropolitan Area	TEAM Consulting Engineering and Management PCL, Thailand in JV with ATT Consultants Company limited, Thailand and in association with CQ2 Engineering Consultancy & Diverso Unipessoal Lda, Timor-Leste	RFP/001/MOP-2019	FI	MOP	Plan																														
							Actual																														Sevisu Konsultant Design, sei adjusta tuir planu husi Projeto Nain
	20	Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	RFP/039/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	21	Estudos e plano de concepção para Planeamento Urbano a nivel nacional	Intersisment S.A in Joint Venture with Quetenaire Portugal Consultoria para o Desenvolvimento. SA	RFP/025/MPW-2013	FI	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	Plan																														
							Actual																														
TOTAL PROJETO ON-GOING																																				

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha terenu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Egidio Goncalves)
Eng Municipio

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Oualidade

Aprova Husi :

(Eng. Januario M. Guterres)
Adiunto Director Executivo ADN, I.P.

MINISTERIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Julmira S. Sampaio

Municipio MUNICIPIO DILI NO POSTOS

2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		ABRIL fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	fr 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	fr 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	fr 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	fr 29	Sa 30	Obs
CRISTO REI (CR)	9	Consulting Services for Detail Engineering Design (DED) for Pediatric and ICCU Building in Guido Valadares National Hospital	Philcoei International, Inc. In JV with Luis and Associates, Co.	SSS/035/MOPTC-2017	FI	MDS	Plan																														
							Actual																														
	35	Consultancy to develop A feasibility study and master plan Guido Valadares National Hospital (Bem Serviso)	Mafra Consultante Unipessoal Lda	FBS-DNA-MOP-19018-B	LM/BS	MDS	Plan																														
							Actual																														
DOM ALEIXO (DA)	9	Consulting services for DED of the new Ministry of Commerce Industry and Enviroment Training Center	Vitor Hugo Coordenacao e Gestao de projetos, SA atraves de emprendimento conjunto com a Quadramor Timor Sistemas de Engenharia, S.A	RFP/030/MCIE-2013	FI	MTCI	Plan																														
							Actual																														
	10	Detail Engineering design (DED) of The New Ministry of Commerce, Industry and Environment	Philkoei International Inc. in JV with Arch Haus Asia Consultant, Inc	RFP/029/MCIE-2013	FI	MTCI	Plan																														
							Actual																														Sevisu Konsultant Design, sei adjusta tuir planu husi Projeto Nain
	58	Consulting Services of Spatial Planing of Timor Leste	Intersismet in Joint Venture With Queternaire Portugal Consultoria para o Desenvolvimento SA		FI	MPO	Plan																														
							Actual																														
	46	Revitalization of Community Aitarak Laran	TPF Timor Unip. Lda.	MPW-S-190272	LM	MOP	Plan																														
							Actual																														
		Detail Engineering Design MACLN Building	Uma de Construcão Unip. Lda.		LM	MACLN	Plan																														
							Actual																														
NAIN FETO (NF)	2	Consulting Services for detailed Engineering Design of CAC Office Building	Imagem, Design and Arquitectura, Lda (IDA) in Association with Vaz, Dotti & Silva, Lda (VDS)	RFP/004/MPW-2013	FI	CAC	Plan																														
							Actual																														
VERA CRUZ	2	Consulting Services for Construction Supervision of Tribunal Distrital Dili Office Building	Dacrea Desing and Engineering Consultant (Dacrea) (Indonesia) In Association with Archtimor Engineering Consultants (AEC) as Sub-consultant (Timor-Leste)	RFP/012/TR-2019	FI	TR	Plan																														
							Actual																														
	7	Consultant Services Construction Supervision and Quality Control of New Construction of Quartel Geral PNTL Office Building in Caicoli Dili Timor Leste	PT. Cerisjasa Cipta Mandiri in Joint Venture with JKC Consultant Engineering Unipessoal Lda	RPF/087/MI-2017	FI	MI	Plan																														
							Actual																														
	8	Consulting Services for Detail Engineering Design of the IGE Office, Workshop and Warehouse Complex Building	Scope Australia Pty, Ltd	RFP/039/MPW-2013	FI	MOP	Plan																														
							Actual																														
	9	Consulting Services for Detailed Architecture and Engineering Design for Press Building Project	CGM Consultants & Associates Incorporated, Lda.	SSS/051/SECOM-2015	FI	SECOM	Plan																														
							Actual																														
	10	Consulting Services for Feasibility Study of the New Buildings for RTTL P.E and Tatoli P.I.	Potevio Company Limited	RDTL	FI	SECOM	Plan																														
							Actual																														Sevisu Konsultant Design, sei adjusta tuir planu husi Projeto Nain
	15	Consulting Services of Detailed Engineering Design of Sport Complex and Building at Region of Dili	ATT consultants Co. Ltd JV SQ Architect and Planner Co. Ltd	RFQ/314/SEJD-2016	FI	SEJD	Plan																														
							Actual																														
	24	Detailed Engineering design of E-Recruitment Building CFP	De Oliveira design	SSS/045/MT-2017	LM	CFP	Plan																														
							Actual																														
		Supervision Consulting Services for New Construction of Memorial Monument of The Santa Cruz	Aria Unip. Lda. JV With Jamori Lda.	RFP/042/MACLN-2021	LM	MACLN	Plan																														
							Actual																														
NASIONAL	1	Detailed Engineering Design (DED) of Dili Water Supply	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/038/MOP-2019	FI	MOP	Plan																														
							Actual																														
	3	Feasibility Study of Surface Water Resource Development for the Water Supply of Dili Metropolitan Area	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.	RFP/002/MOP-2019	FI	MOP	Plan																														
							Actual																														
	4	Pre- Feasibility Study of a Ground Water Resources Development Project for the Water Supply of Dili Metropolitan Area	TEAM Consulting Engineering and Management PCL, Thailand in JV with ATT Consultants Company limited, Thailand and in association with CQ2 Engineering Consultancy & Diverso Unipessoal Lda, Timor-Leste	RFP/001/MOP-2019	FI	MOP	Plan																														
							Actual																														Sevisu Konsultant Design, sei adjusta tuir planu husi Projeto Nain
	20	Consulting sevices for detailed Engineering Design of Timor Leste Four Municipal Capitals Water Supply & Sanitation Project	ADP Unipessoal LDA (Timor-Leste) in JV with Engidro Engineering Solutions, Lda (Portugal)	RFP/039/MOP-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																														
							Actual																														
	21	Estudos e plano de concepção para Planeamento Urbano a nivel nacional	Intersisment S.A in Joint Venture with Quetenaire Portugal Consultoria para o Desenvolvimento. SA	RFP/025/MPW-2013	FI	MINISTERIO PLANU E ORDENAMENTU, MINISTERIO FINANCAS	Plan																														
							Actual																														
TOTAL PROJETO ON-GOING																																				

Note:

Planu Periode inspesaun iha tereinu — **Implementa Periode inspesaun iha terenu** — **Relatoriu avaliasuan mensal iha Dili** — **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Julmira S. Sampaio)
Eng Municipio

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade

Aprova Husi :

(Eng. Januario M. Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (NF- 07)

PROJECT NAME : EMERGENCY PROJECT PONTE MY FRIEND - PONTE HALI LARAN, KULUHUN 2020 (PACOTE NO. 3) - MUNICIPALITY OF DILILOCATION :
MUNICIPALITY OF DILI, Timor Leste

GRAND SUMMARY

ORIGINAL CONTRACT			PREVIOUS MONTH		THIS MONTH		UP TO DATE	
NO.	**DESCRIPTIONS WORKS**	**AMOUNT (USD)**	**AMOUNT (USD)**	**PERCENT %**	**THIS BILLING**	**PERCENT %**	**UP TO DATE**	**PERCENT %**
100	GENERAL	$ 7,900.00	5,925.00	0.65%	$ 1,975.00	0.22%	$ 7,900.00	0.87%
200	EARTHWORK	$ 53,039.50	28,407.47	3.12%	$ 16,403.45	1.80%	$ 44,810.92	4.92%
400	SURFACE COURSE	$ -	-	0.00%	$ -	0.00%	$ -	0.00%
500	BRIDGE CONSTRUCTION	$ -	-	0.00%	$ -	0.00%	$ -	0.00%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURE	$ 723,215.51	665,319.51	73.02%	$ 57,896.00	6.35%	$ 723,215.51	79.37%
700	MISCELLANEOUS STRUCTURES	$ -	-	0.00%	$ -	0.00%	$ -	0.00%
A	**TOTAL CONSTRUCTION COST**	**$ 784,155.01**	**$ 699,651.98**	**76.79%**	**$ 76,274.45**	**8.37%**	**$ 775,926.43**	**85.16%**
B	**CONTRACTOR FEE (10% X A)**	**$ 78,415.50**	**$ 69,965.20**	**7.68%**	**$ 7,627.45**	**0.84%**	**$ 77,592.64**	**8.52%**
C	**OVERHEAD**	**$ 4,250.00**	**$ 3,187.50**	**0.35%**	**$ 1,062.50**	**0.12%**	**$ 4,250.00**	**0.47%**
D	**PROVISIONAL SUM FOR DAYWORKS (NORMALIZATION)**	**$ 26,459.17**	**$ -**		**$ 26,459.17**	**2.90%**	**$ 26,459.17**	**2.90%**
F	**CONSTRUCTION TAX 2%**	**$ 17,865.59**	**$ 15,456.09**	**1.70%**	**$ 2,228.47**	**0.24%**	**$ 17,684.56**	**1.94%**
F	**GRAND TOTAL (D + E)**	**$ 911,145.27**	**$ 788,260.77**	**86.51%**	**$ 113,652.03**	**12.47%**	**$ 901,912.81**	**98.99%**

Inspection by :

Eng. Eduardo dos Santos
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Inspection by :

Eng. Joao Quintao do Rego
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Verified By :

Eng. Remigio da C.S. dos Santos
Enginheiro Senior ba projecto Infrastrutura, transporte e Irigasaun ADN I.P

Certified By :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação de Qualidade ADN I.P


ANEXO C1 (NF - 07)

Naran Projeto	: EMERGENCY PROJECT PONTE MY FRIEND - PONTE HALI LARAN, KULUHUN 2020 (PACOTE NO. 3) - MUNICIPALITY OF DILI
No. kontratu	: SSS/010/MOP-2020

Data Inspesaun	: 14-04-2022				
Fatin Inspesaun	: PONTE MY FRIEND - PONTE HALI LARAN, KULUHUN				
Koordinadas	:				
	Start Point	**Long**	**-8.567685**	**Latetude**	**125.5832817**
	End Point	**Long**	**-8.557799**	**Latetude**	**125.5916503**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

CONCRETE CYCLOPE

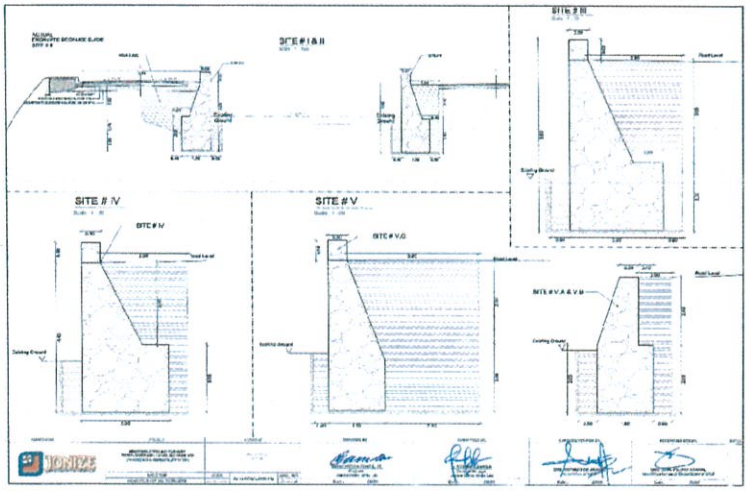





STA 0+000 - 0+547

STATION		AREA (Sq.m)	DISTANCE	VOLUME (Cu.m)	REMARK
0+000	0+060	4.6	96	440.66	
TOTAL VOLUME				440.66 Cu.m	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (MTN-08)

PROJECT NAME : NEW CONSTRUCTION OF ROADWAYS,DRAINAGE AND PARKING AREA NO JARDIM DE HEROIS DE MATINARO
KONTRACTOR : CELIJO STAR UNIPESSOAL, LDA
LOCATION : JARDIM DE HEROIS DE MATINARO

GRAND SUMMARY

ORIGINAL CONTRACT			PREVIOUS MONTH		THIS MONTH		UP TO DATE	
NO.	**DESCRIPTIONS WORKS**	**AMOUNT (USD)**	**AMOUNT (USD)**	**PERCENT %**	**THIS BILLING**	**PERCENT %**	**UP TO DATE**	**PERCENT %**
100	Section 100. General Requirements	$ 6,800.00	2,100.00	0.22%	$ -	0.00%	$ 2,100.00	0.22%
200	Section 200. Earth Works	$ 117,939.92	74,534.11	7.85%	$ -	0.00%	$ 74,534.11	7.85%
300	Section 300. Subbase and Base Course	$ 299,010.88	-	0.00%	$ 133,647.40	14.08%	$ 133,647.40	14.08%
500	Section.500 Bridge Construction	$ 49,214.44	-	0.00%	$ -	0.00%	$ -	0.00%
600	Section.600 Drainage and Slope Protection Works	$ 156,412.51	130,540.06	13.76%	$ 13,040.92	1.37%	$ 143,580.98	15.13%
700	MISCELLANEOUS STRUCTURE	$ 189,461.07	-	0.00%	$ -	0.00%	$ -	0.00%
A	**TOTAL CONSTRUCTION COST**	**$ 818,838.81**	**$ 207,174.17**	**21.83%**	**$ 146,688.32**	**15.46%**	**$ 353,862.49**	**37.29%**
B	**CONTRACTOR FEE AND OVERHEAD (10% X A)**	**$ 84,574.88**	**$ 20,960.42**	**2.21%**	**$ 14,668.83**	**1.55%**	**$ 35,629.25**	**3.75%**
C	**OVERHEAD**	**$ 26,910.00**	**$ 2,430.00**	**0.26%**	**$ -**	**0.00%**	**$ 2,430.00**	**0.26%**
D	**TOTAL (A + B + C)**	**$ 930,323.70**	**$ 230,564.59**	**24.30%**	**$ 161,357.15**	**17.00%**	**$ 391,921.74**	**41.30%**
E	**CONSTRUCTION TAX (2% X D)**	**$ 18,606.47**	**$ 4,611.29**	**0.49%**	**$ 3,227.14**	**0.34%**	**$ 7,838.43**	**0.83%**
F	**GRAND TOTAL (D + E)**	**$ 948,930.17**	**$ 235,175.88**	**24.78%**	**$ 164,584.29**	**17.34%**	**$ 399,760.17**	**42.13%**

Inspection by :

Eng. Eduardo dos Santos
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Inspection by :

Eng. Joao Quintao do Rego
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Verified By :

Eng. Remigio da C.S. dos Santos
Enginheiro Senior ba projecto Infrastrutura, transporte e Irigasaun ADN I.P

Certified By :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação de Qualidade ADN I.P


ANEXO C1 (MTN - 08)

Naran Projeto	: NEW CONSTRUCTION OF ROADWAYS,DRAINAGE AND PARKING AREA NO JARDIM DE HEROIS DE METINARO
No. kontratu	: 214/MACLN/X/2021


Data Inspesaun	: 22-04-2022				
Fatin Inspesaun	:JARDIM DE HEROIS DE MATINARO				
Koordinadas	:				
	Start Point	**Long**	**-8.505154**	**Latetude**	**125.81428**
	End Point	**Long**	**-8.505216**	**Latetude**	**125.813803**


Sketch & Foto Desenho

SUB BASE COURSE

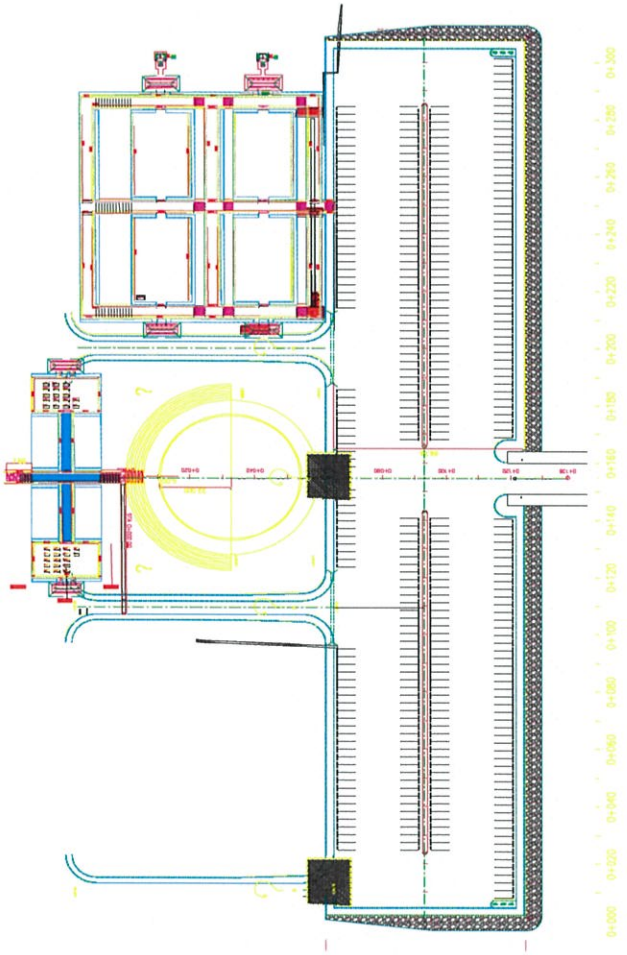

Observasaun iha tereno no Foto Aktual

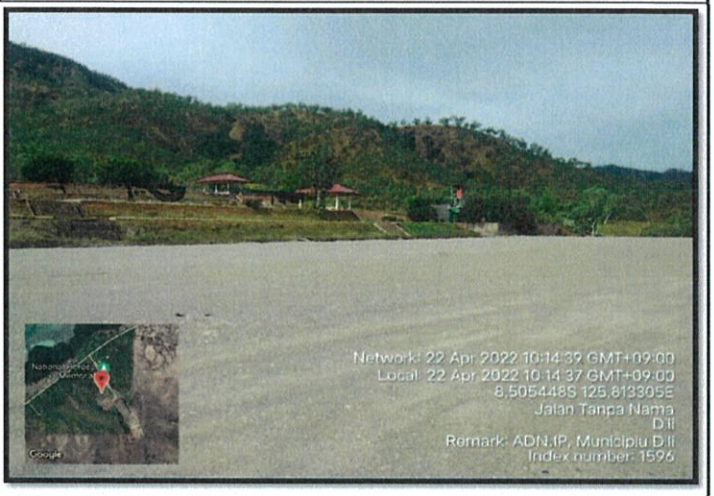

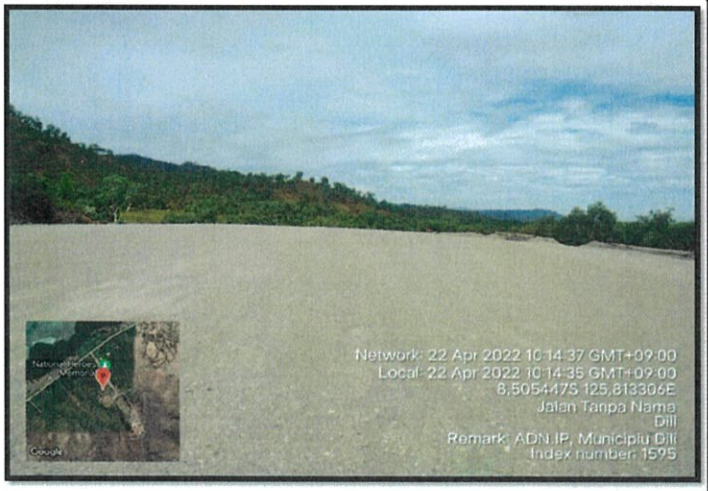

STATION		AREA B (Sq.m)	DISTANCE	VOLUME (Cu.m)	REMARK
0+000	0+300	12.11	300	3,632.71	
TOTAL VOLUME				3,632.71 Cu.m	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público


ANEXO C1 (MTN - 08)

Naran Projeto	: NEW CONSTRUCTION OF ROADWAYS,DRAINAGE AND PARKING AREA NO JARDIM DE HEROIS DE METINARO
No. kontratu	: 214/MACLN/X/2021

Data Inspesaun	: 15-03-2022				
Fatin Inspesaun	:JARDIM DE HEROIS DE MATINARO				
Koordinadas	:				
	Start Point	**Long**	**-8.505154**	**Latetude**	**125.81428**
	End Point	**Long**	**-8.505216**	**Latetude**	**125.813803**

Sketch & Foto Desenho

STONE MASONRY

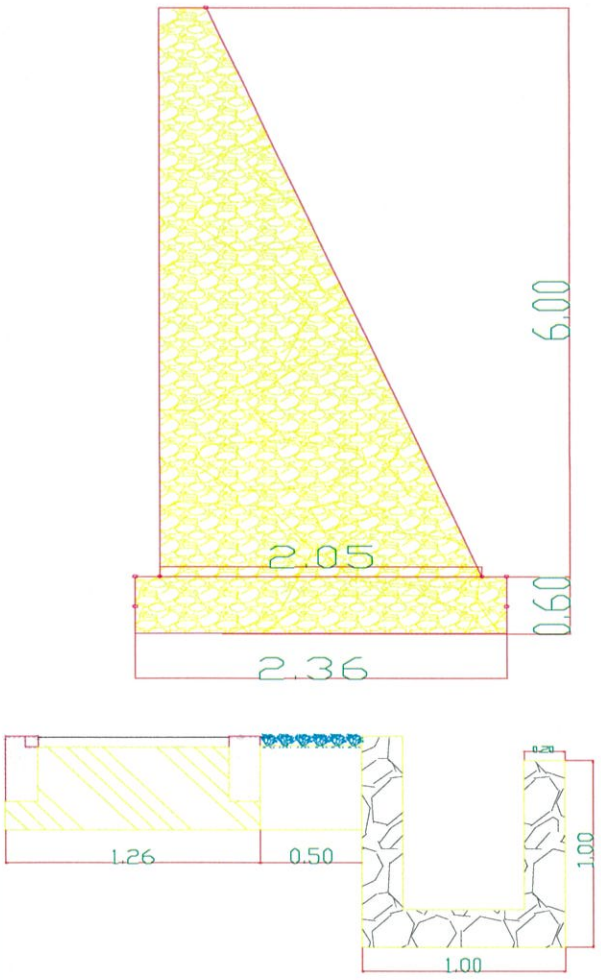

Observasaun iha tereno no Foto Aktual





STATION		AREA B (Sq.m)	DISTANCE	VOLUME (Cu.m)	REMARK
0+000	0+300	5.875	30	176.25	WALL
0+000	0+300	0.54	15	8.10	DRAINAGE
TOTAL VOLUME				184.35 Cu.m	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C2 (DA - 56)

Name of project : Dili Roads and Drainage Rehabilitation
Location of Project : Jct. Australia Embassy - Marconi Road (Assesment to Hotel Hilton) sta. 0+000 - 0+504

GRAND SUMMARY

NO.	DESCRIPTION	ORIGINAL CONTRACT	PREVIOUS MONTH		THIS MONTH		UP TO DATE	
		AMOUNT US $	AMOUNT US $	WEIGHT %	AMOUNT US $	WEIGHT %	AMOUNT US $	WEIGHT %
i	GENERAL REQUIREMENTS	$ 1,000.00	$ 250.00	0.04%	$ -	0.00%	$ 250.00	0.04%
ii	EARTHWORKS	$ 10,844.05	$ 7,238.18	1.25%	$ -	0.00%	$ 7,238.18	1.25%
iii	SUB BASE AND BASE COURSE	$ 43,786.00	$ 10,702.43	1.85%	$ 11,675.79	2.02%	$ 22,378.21	3.87%
iv	SURFACE COURSE	$ 60,466.11	$ -	0.00%	$ -	0.00%	$ -	0.00%
v	BRIDGE CONSTRUCTION	$ 359,697.10	$ 108,780.83	18.82%	$ 72,645.97	12.57%	$ 181,426.81	31.39%
vi	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 21,450.28	$ 21,181.96	3.66%	$ -	0.00%	$ 21,181.96	3.66%
vii	MISCELLANEOUS STRUCTURES	$ 11,853.36	$ -	0.00%	$ -	0.00%	$ -	0.00%
A	**CONSTRUCTION COST**	**$ 509,096.91**	**$ 148,153.40**	**25.63%**	**$ 84,321.76**	**14.59%**	**$ 232,475.16**	**40.22%**
B	**PROFIT (10%)*A**	**$ 50,909.69**	**$ 14,815.34**	**2.56%**	**$ 8,432.18**	**1.46%**	**$ 23,247.52**	**4.02%**
C	**OVERHEAD**	**$ 6,700.00**	**$ 2,000.00**	**0.35%**	**$ 1,700.00**	**0.29%**	**$ 3,700.00**	**0.64%**
D	**TAX 2%*(A+B+C)**	**$ 11,334.13**	**$ 3,299.37**	**0.57%**	**$ 1,889.08**	**0.33%**	**$ 5,188.45**	**0.90%**
E	**TOTAL (A+B+C+D)**	**$ 578,040.73**	**$ 168,268.11**	**29.11%**	**$ 96,343.01**	**16.67%**	**$ 264,611.12**	**45.78%**

Inspection by :

Eng. Eduardo dos Santos
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Inspection by :

Eng. Joao Quintao do Rego
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Verified By :

Eng. Remigio da C.S. dos Santos
Enginheiro Senior ba projecto Infrastrutura, transporte e Irigasaun ADN I.P

Certified By :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação de Qualidade ADN I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público


ANEXO C1 (DA - 56)

Naran Projeto	:REHABILITATION OF JCT. AUSTRALIA EMBASSY-MARCONI ROAD (ACCESS TO HOTEL HILTON)				
No. kontratu	RFQ/068/MOP-2021				
Data Inspesaun	: 12 de Abril 2022				
Fatin Inspesaun	: JCT. AUSTRALIA EMBASSY-MARCONI ROAD				
Koordinadas	:				
	Start Point	**Long**	**-8.55188**	**Latetude**	**125.557028**
	End Point	**Long**	**-8.551623**	**Latetude**	**125.558977**

Sketch & Foto Desenho


Observasaun iha tereno no Foto Aktual

STRUCTURAL CONCRETE

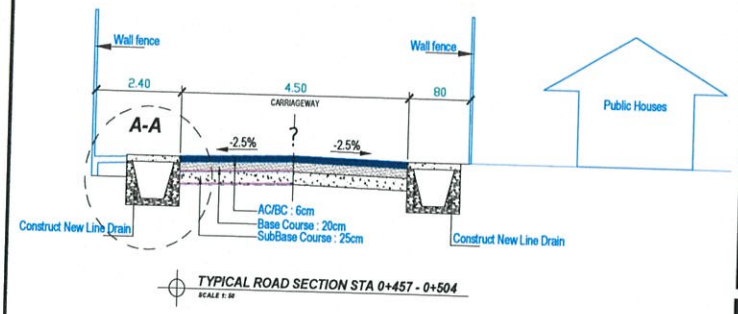

TYPICAL ROAD SECTION STA 0+457 - 0+504



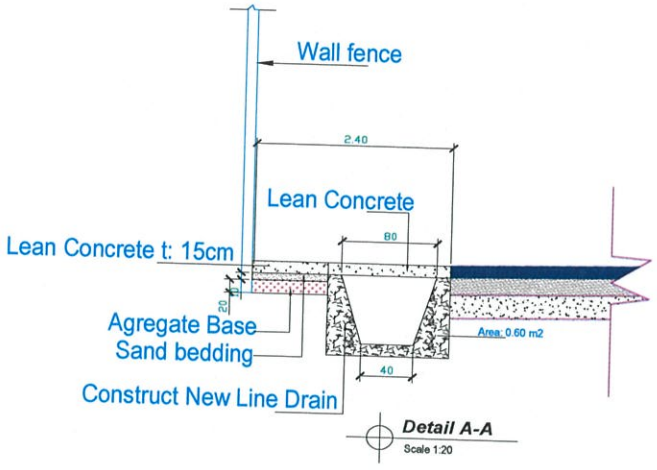

Detail A-A
Scale 1:20



RC DRAINAGE

STATION (RS)		LENGTH	AREA
0+258	0+515	64	0.64

TOTAL VOLUME **40.96 Cu.m**

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público


ANEXO C1 (DA - 56)

Naran Projeto	:REHABILITATION OF JCT. AUSTRALIA EMBASSY-MARCONI ROAD (ACCESS TO HOTEL HILTON)
No. kontratu	RFQ/068/MOP-2021

Data Inspesaun	: 12 de Abril 2022				
Fatin Inspesaun	: JCT. AUSTRALIA EMBASSY-MARCONI ROAD				
Koordinadas	:				
	Start Point	**Long**	**-8.55188**	**Latetude**	**125.557028**
	End Point	**Long**	**-8.551623**	**Latetude**	**125.558977**


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

REINFORCING STEEL

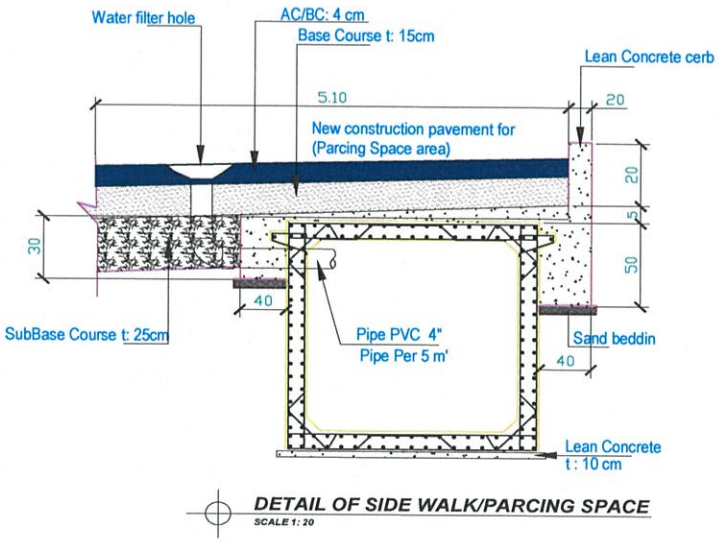

DETAIL OF SIDE WALK/PARCING SPACE

SCALE 1: 20

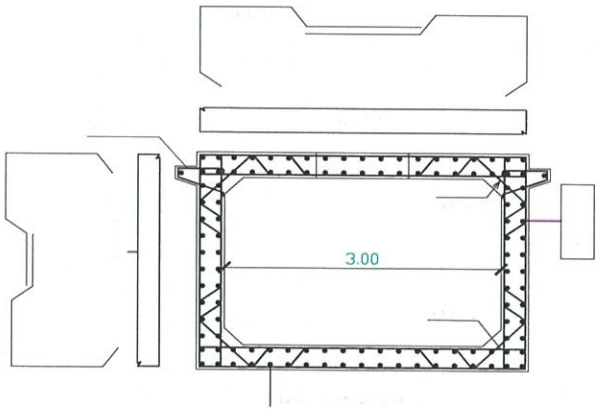





STATION		VOLUME (Kg)	REMARK
0+225	0+504	313.88	
TOTAL VOLUME	**Cu.m**	**313.88**	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de
Desenvolvimento
Nacional, Instituto Público

ANEXO C2 (NF- 22)

NAME OF PROJECT : **RIVER PROTECTION AT PALACIO NOBRE LAHANE Sta. 0 + 000 to 0 + 176 Dili Municipality.**
LOCATION OF PROJECT : **MUNICIPALITY OF DILI**
WORK ITEM : **SUMMARY BILL OF QUANTITIES**

SUMMARY

ORIGINAL CONTRACT			PREVIOUS MONTH		THIS MONTH		UP TO DATE	
SECTION NO.	DESCRIPTION	TOTAL COST US$	AMOUNT (USD)	PERCENT %	AMOUNT (USD)	PERCENT %	AMOUNT (USD)	PERCENT %
100	GENERAL REQUIREMENTS	5,000.00	3,000.00	2.32%	$ -	0.00%	$ 3,000.00	2.32%
200	EARTHWORKS	8,329.00	2,628.00	2.03%	$ -	0.00%	$ 2,628.00	2.03%
500	BRIDGE CONSTRUCTION	12,100.00	2,200.00	1.70%	$ 2,406.25		$ 4,606.25	3.57%
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	84,240.00	49,020.00	37.95%	$ 6,000.00	4.65%	$ 55,020.00	42.60%
A	**Construction Cost**	**109,669.00**	**$ 56,848.00**	**44.01%**	**$ 8,406.25**	**6.51%**	**$ 65,254.25**	**50.52%**
B	**Contractor Fee (10% x A)**	**10,966.90**	**$ 5,684.80**	**4.40%**	**$ 840.63**	**0.65%**	**$ 6,525.43**	**5.05%**
C	**Overhead**	**6,000.00**	**$ 4,500.00**	**3.48%**	**$ -**	**0.00%**	**$ 4,500.00**	**3.48%**
D	**Tax (2% x (A+B+C))**	**2,532.72**	**$ 1,340.66**	**1.04%**	**$ 184.94**	**0.14%**	**$ 1,525.59**	**1.18%**
E	**Grand Total (A + B + C + D+E)**	**129,168.62**	**68,373.46**	**52.93%**	**$ 9,431.81**	**7.30%**	**$ 77,805.27**	**60.24%**

Inspection by :

Eng. Eduardo dos Santos
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Inspection by :

Eng. Joao Quintao do Rego
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Verified By :

Eng. Remigio da C.S. dos Santos
Enginheiro Senior ba projecto Infrastrutura, transporte e Irigasaun ADN I.P

Certified By :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação de Qualidade ADN I.P

ANEXO C1 (NF - 22)


Naran Projeto	**RIVER PROTECTION AT PALACIO NOBRE LAHANE Sta. 0 + 000 to 0 + 176 Dili Municipality.**
No. kontratu	**NCB/040/MOP-2020**

Data Inspesaun	: 26 - 04 - 2022
Fatin Inspesaun	**: LAHANE**


Koordinadas	:				
	Start Point	**Long**	**-8.574282**	**Latetude**	**-125.583522**
	End Point	**Long**	**-8.574558**	**Latetude**	**-125.584077**

Sketch & Foto Desenho


GABIONS SITE B

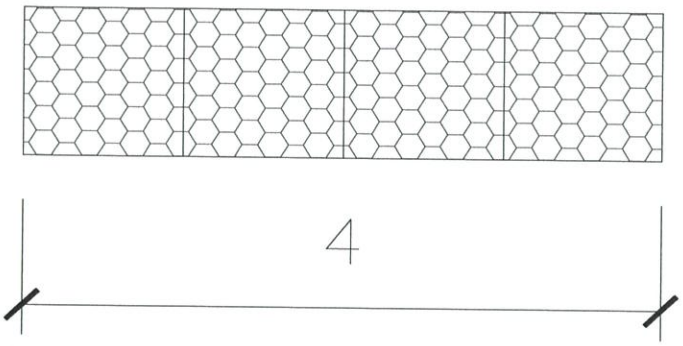


STA 0+000 - 0+050

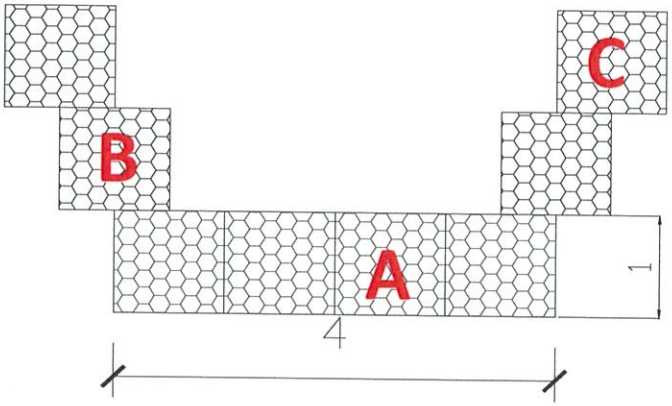

Observasaun iha tereno no Foto Aktual

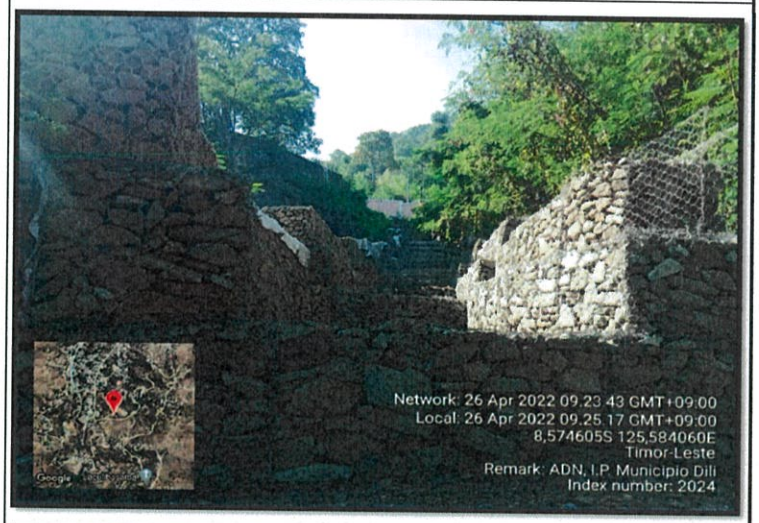

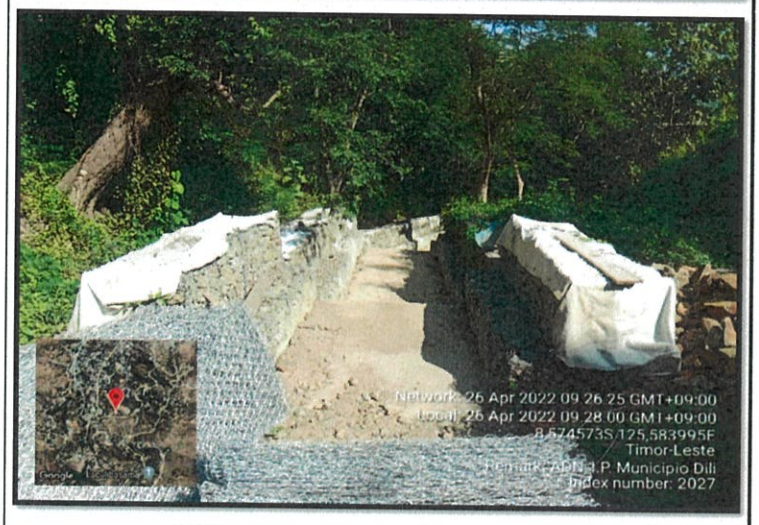

INSTALASAUN ITEM GABIONS


SITE I GABIONS (B & C)			
LENGTH (L) :		**1**	**m'**
HIGHT (H):		**2**	**m'**
TOTAL AREA		**2**	**m'**
Total Length		**25.000**	**m²**
VOLUME TOTAL		**100.00**	**m3**

ANEXO C1 (NF - 22)

Naran Projeto	RIVER PROTECTION AT PALACIO NOBRE LAHANE Sta. 0 + 000 to 0 + 176 Dili Municipality.				
No. kontratu	NCB/040/MOP-2020				
Data Inspesaun	: 26 - 04 - 2022				
Fatin Inspesaun	: LAHANE				
Koordinadas	:				
	Start Point	**Long**	**-8.574282**	**Latetude**	**-125.583522**
	End Point	**Long**	**-8.574558**	**Latetude**	**-125.584077**

Sketch & Foto Desenho

LEAN CONCRETE

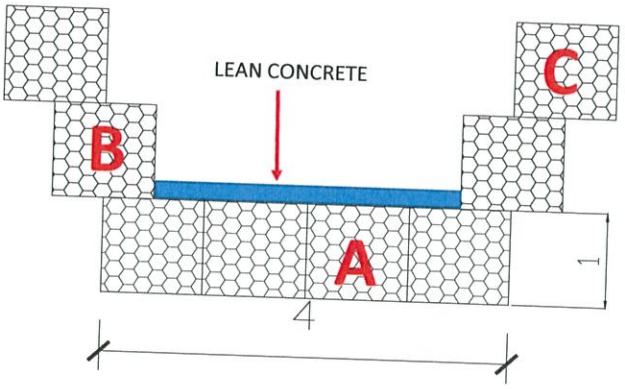

Observasaun iha tereno no Foto Aktual





INSTALASAUN ITEM LEAN CONCRETE

SITE I LEAN CONCRETE			
WEIGTH (L) :		2.5	m'
HIGHT (H):		0.25	m'
TOTAL AREA		0.625	m'
Total Length		15.000	m²
VOLUME TOTAL		9.38	m3

SITE II LEAN CONCRETE			
WEIGTH (L) :		2.5	m'
HIGHT (H):		0.25	m'
TOTAL AREA		0.625	m'
Total Length		20.000	m²
SUB VOLUME TOTAL		12.50	m3

VOLUME TOTAL 21.88 **m3**

ANEXO C2 (NF- 28)

PROJECT NAME : REHALITASAUN ESTRADA URBANA PONTE HALI LARAN - PONTE MY FREND - PONTE CULUHUN (STA 0 + 000 - 1 + 450)
LOCATION : MUNICIPALITY OF DILI, Timor Leste

GRAND SUMMARY

NO.	DESCRIPTIONS WORKS	ORIGINAL CONTRACT AMOUNT (USD)	PREVIOUS MONTH AMOUNT (USD)	PREVIOUS MONTH PERCENT %	THIS MONTH THIS BILLING	THIS MONTH PERCENT %	UP TO DATE UP TO DATE	UP TO DATE PERCENT %
100	GENERAL REQUIREMENTS	$ 2,636.89	1,318.44	0.46%	$ 1,318.44	0.46%	$ 2,636.89	0.93%
200	EARTHWORKS	$ 9,786.43	9,786.43	3.44%	$ -	0.00%	$ 9,786.43	3.44%
300	SUB BASE AND BASE COURSE	$ 39,818.55	39,818.55	14.00%	$ -	0.00%	$ 39,818.55	14.00%
400	SURFACE COURSE	$ 193,098.12	-	0.00%	$ 193,098.12	67.91%	$ 193,098.12	67.91%
500	BRIDGE CONSTRUCTION	$ 470.83	470.83	0.17%	$ -	0.00%	$ 470.83	0.17%
700	MISCELLANEOUS STRUCTURES	$ 4,052.88	4,052.88	1.43%	$ -	0.00%	$ 4,052.88	1.43%
A	TOTAL CONSTRUCTION COST	$ 249,863.70	55,447.13	19.50%	$ 194,416.56	68.38%	$ 249,863.70	87.88%
B	CONTRACTOR FEE AND OVERHEAD (10% X A)	$ 24,986.37	$ 5,544.71	1.95%	$ 19,441.66	6.84%	$ 24,986.37	8.79%
C	OVERHEAD	$ 3,900.00	$ 1,950.00	0.69%	$ 1,950.00	0.69%	$ 3,900.00	1.37%
D	TOTAL (A + B + C)	$ 278,750.07	$ 62,941.85	22.14%	$ 215,808.22	75.90%	$ 278,750.07	98.04%
E	CONSTRUCTION TAX (2% X D)	$ 5,575.00	$ 1,258.84	0.44%	$ 4,316.16	1.52%	$ 5,575.00	1.96%
F	GRAND TOTAL (D + E)	$ 284,325.07	$ 64,200.68	22.58%	$ 220,124.38	77.42%	$ 284,325.07	100.00%

Inspection by :

Eng. Eduardo dos Santos
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Inspection by :

Eng. Joao Quintao do Rego
Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun Municipio Dili, ADN I.P.

Verified By :

Eng. Remigio da C.S. dos Santos
Enginheiro Senior ba projecto Infrastrutura, transporte e Irigasaun ADN I.P

Certified By :

Eng. Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação de Qualidade ADN I.P


ANEXO C1 (NF - 28)

Naran Projeto	: REHALITASAUN ESTRADA URBANA PONTE HALI LARAN - PONTE MY FREND - PONTE CULUHUN (STA 0 + 000 - 1 + 450)
No. kontratu	: MPW-W-210168
Data Inspesaun	: 06-04-2022
Fatin Inspesaun	: Hali Laran

Koordinadas					
	Start Point	**Long**	**-8.565235**	**Latetude**	**125.585812**
	End Point	**Long**	**-8.567558**	**Latetude**	**125.583427**


Sketch & Foto Desenho


ASPHALT CONCRETE BINDER COURSE

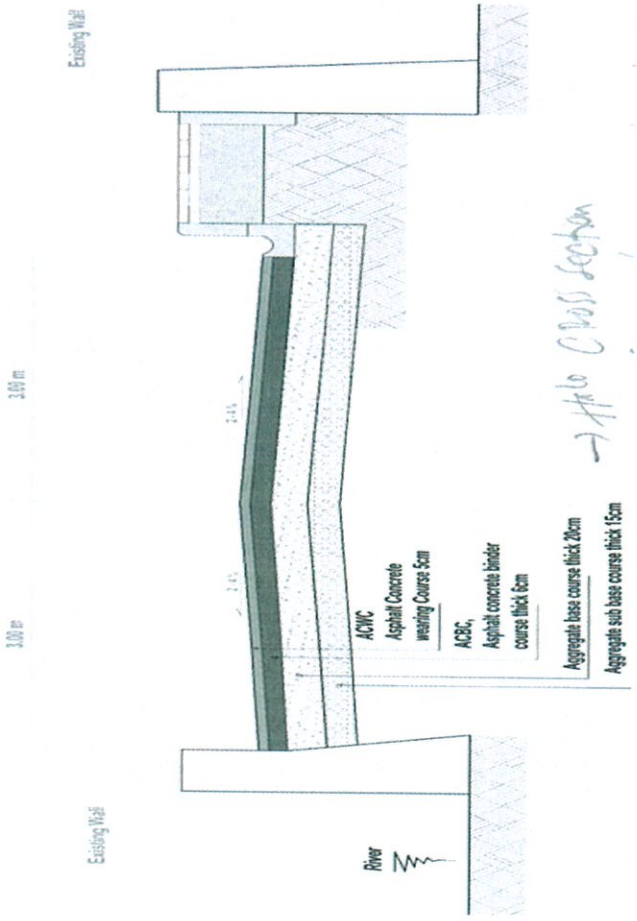

STA 0+000 - 0+547

Observasaun iha tereno no Foto Aktual

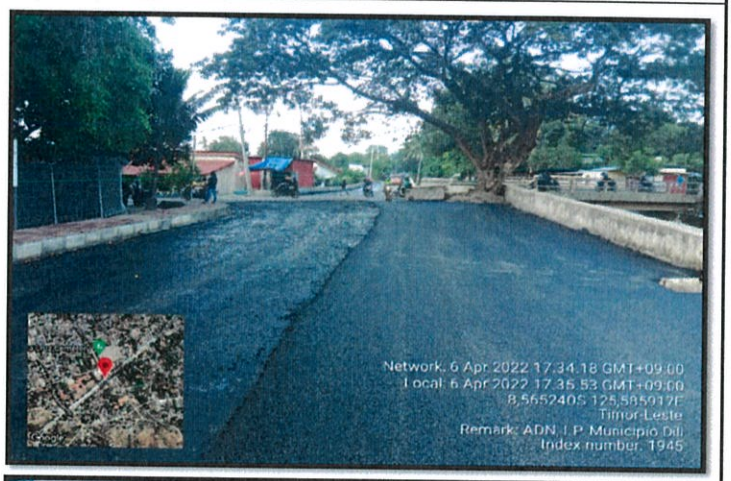

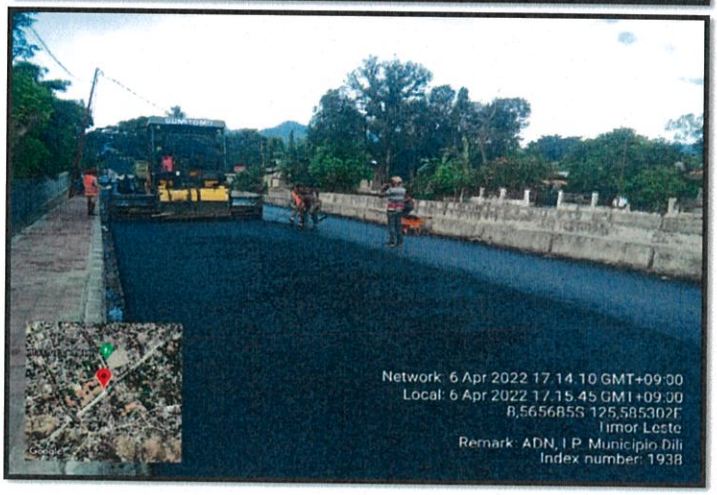

STATION		AREA (Sq.m)	DISTANCE	VOLUME (Cu.m)	REMARK
0+000	0+060	6	547	3,282.00	
TOTAL VOLUME				3,282.00 Cu.m	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público


ANEXO C1 (NF - 28)

Naran Projeto	: REHALITASAUN ESTRADA URBANA PONTE HALI LARAN - PONTE MY FREND - PONTE CULUHUN (STA 0 + 000 - 1 + 450)				
No. kontratu	: MPW-W-210168				
Data Inspesaun	: 26-04-2022				
Fatin Inspesaun	: Hali Laran				
Koordinadas	:				
	Start Point	**Long**	**-8.565235**	**Latetude**	**125.585812**
	End Point	**Long**	**-8.567558**	**Latetude**	**125.583427**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

ASPHALT CONCRETE WEARING COURSE

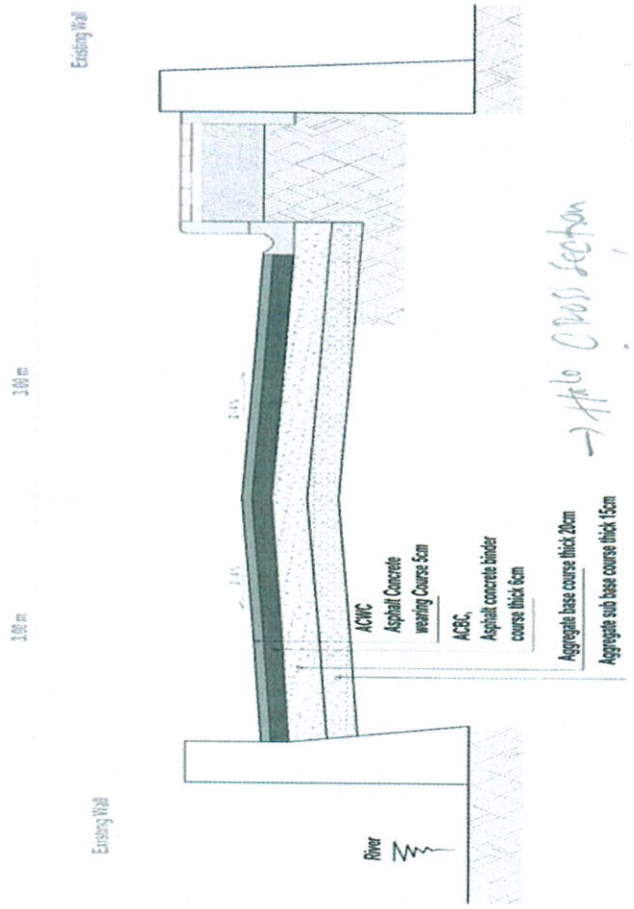

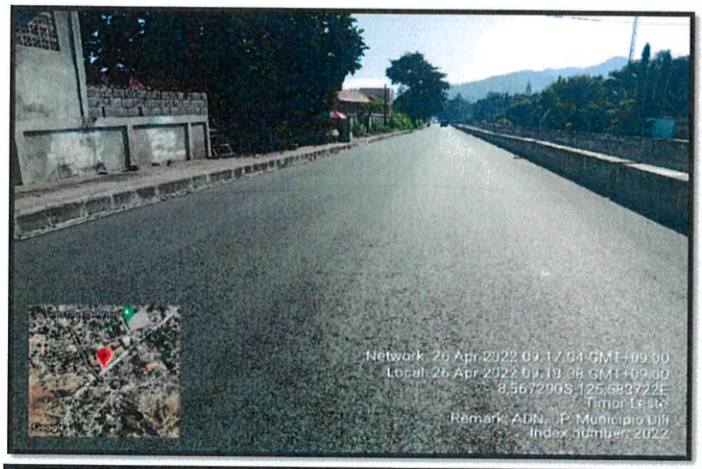



STA 0+000 - 0+547

STATION		AREA (Sq.m)	DISTANCE	VOLUME (Cu.m)	REMARK
0+000	0+493	6	647	3,882.00	
TOTAL VOLUME				3,882.00 Cu.m	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (AT - 1)

Naran Projeto	: R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality
No. kontratu	: RT/029/MOP-2019
Data Inspesaun	: 26 - 07 - 2021
Fatin Inspesaun	: Pala - Iliana - Tasi Atauro

Koordinadas :

	Start Point	Long	8.1720616	Latetude	125.630511
	End Point	Long	8.17273	Latetude	125.632220

Naran Inspector : 1. Eng. Eduardo Dos Santos	Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili
2. Eng. Joao Quintao do Rego	Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Pic No.1 Estar Point



√ On-Going, Projecto refere sei halo escavasan no Lan

Concrete, Stone masonry

√

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 10)

Naran Projeto	: Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili				
No. kontratu	: SSS/131/MOPTC-2017				
Data Inspesaun	: 27 / 04/2022				
Fatin Inspesaun	: Jct. Culuhun - Jct Halilaran				
Koordinadas	:				
	Start Point	Long		Latetude	
	End Point	Long		Latetude	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Pic No.1
Estar Point



√ Iao hela nia fisiko atinji ona 89,36 %

√ Parado hela Aprovasaun Variation Order husi Owner

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 31)

Naran Projeto	: **Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili**				
No. kontratu	: **SSS/009/MOP-2020**				
Data Inspesaun	: **24/09/2021**				
Fatin Inspesaun	: **Kuluhun Ate Ponte Habibie/Bidau Santa-Ana**				
Koordinadas	:				
	Start Point	**Long**	8555694	**Latetude**	125.589200
	End Point	**Long**		**Latetude**	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point

√ PHO, Tempo retensaun seidauk to'o

√ Projecto Refere fisikamente 100% ona sei falta pagamento retensaun 12 %



Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 29)

Naran Projeto	: **New Construction of Gabions Tower No.6 section Hera**				
No. kontratu	: **NCB/034/MOP-2020**				
Data Inspesaun	: **22 - 04 - 2022**				
Fatin Inspesaun	: **Hera**				
Koordinadas	:				
	Start Point	**Long**	8.544233	**Latetude**	125.680170
	End Point	**Long**	8.54416	**Latetude**	125.680992
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**


Pic No.1
Estar Point



√ Fisiko atinji ona 100 %

√ PHO

Pic No.2 End Point

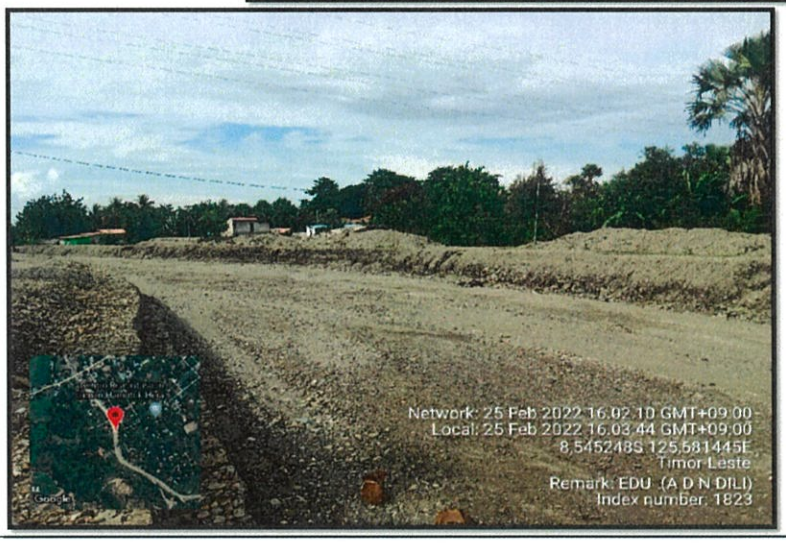

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 9)

Naran Projeto	: **Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)**				
No. kontratu	: **SSS/082/MOPTC-2017**				
Data Inspesaun	: **24 de Setembro de 2021**				
Fatin Inspesaun	:				
Koordinadas	:				
	Start Point	**Long**	8.564323	**Latetude**	125.622238
	End Point	**Long**	8.564323	**Latetude**	125.622238
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
Pic No.1 Estar Point √ Projecto Refere parado hela √	
Pic No.2 End Point	

MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 30)

Naran Projeto	: **New Construction of Gabions Tower No. 19 Section Hera - Dili**				
No. kontratu	: **NCB/033/MOP-2020**				
Data Inspesaun	:				
Fatin Inspesaun	: **Hera-Acanuno**				
Koordinadas	:				
	Start Point	**Long**	8.56178	**Latetude**	125.646012
	End Point	**Long**	8.561205	**Latetude**	125.646115
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1
Estar Point

√ Parado hela, sei hein Aprovasaun Variation Order husi Owner



Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 12)

Naran Projeto	: **Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)**				
No. kontratu	: **RT/154/MOPTC-2016**				
Data Inspesaun	:				
Fatin Inspesaun	: **Hera,Benamauk**				
Koordinadas	:				
	Start Point	**Long**	8.569213	**Latetude**	125.619793
	End Point	**Long**	8.550993	**Latetude**	125.662253
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point

√ Projecto Refere parado hela



Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (CR - 28)

Naran Projeto	: HERA - SUCO LIURAI STAR 0 + 000 - 4 + 000 DILI AND AILEU MUNICIPALITY				
No. kontratu	MPW-W-210067				
Data Inspesaun	: 22 - 03 - 2022				
Fatin Inspesaun	HERA - SUCO				
Koordinadas	:				
	Start Point	**Long**	8.537618	**Latetude**	125.698548
	End Point	**Long**	8.557139	**Latetude**	125.709654
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

√ On-Going

√ line Draing

Pic No.1
Estar Point



Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 18)

Naran Projeto	: Road and Drainage Rehabilitation Project, Road Section: Aimutin to Manleuana Sta. 0+000 - Sta. 1+215 (1.22Km)				
No. kontratu	: SSS/308/MOPTC-2016				
Data Inspesaun	: 25 - 02 - 2022				
Fatin Inspesaun	: Aimutin to Manleuana				
Koordinadas	:				
	Start Point	**Long**	8.561107	**Latetude**	125.545472
	End Point	**Long**	8.570077	**Latetude**	125.542730
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point



√ PARADO

√ Projecto Refere fisikamente 100% ona maibe iha Adisional Cost nebee mak seidauk hetan aprovasaun husi CAFI.

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO



VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 19)

Naran Projeto	: **New Design of Median Line Garden from Leader - Elemloi & Hudi Laran-Timor Block**				
No. kontratu	**SSS/129/MOPTC-2017**				
Data Inspesaun	: **22 - 09 - 2021**				
Fatin Inspesaun	: **Leader - Elemloi & Hudi Laran-Timor Block**				
Koordinadas	:				
	Start Point	**Long**	8.555912	**Latetude**	125.540965
	End Point	**Long**	8.560875	**Latetude**	125.537417
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

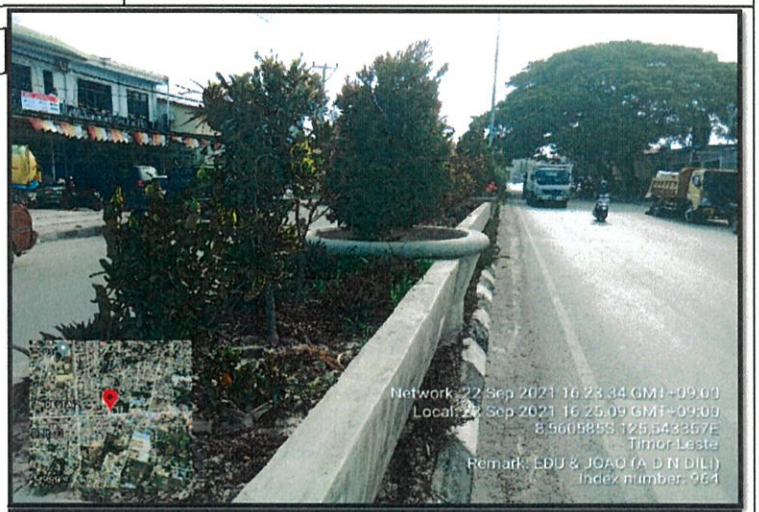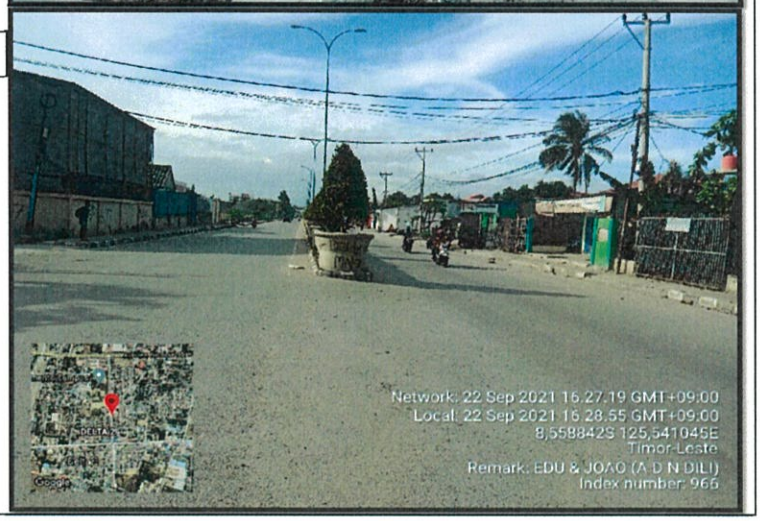Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
√ PHO, Tempo retensaun seidauk to'o √ Projecto Refere fisikamente 100%	Pic No.1 Estar Point  Pic No.2 End Point 

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 23)

Naran Projeto	: **Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)**				
No. kontratu	: **MPW-W180036**				
Data Inspesaun	: **24 - 09- 2021**				
Fatin Inspesaun	: **Manleu (Maok River)**				
Koordinadas	:				
	Start Point	**Long**	8.561107	**Latetude**	125.545472
	End Point	**Long**	8.570077	**Latetude**	125.542730
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point

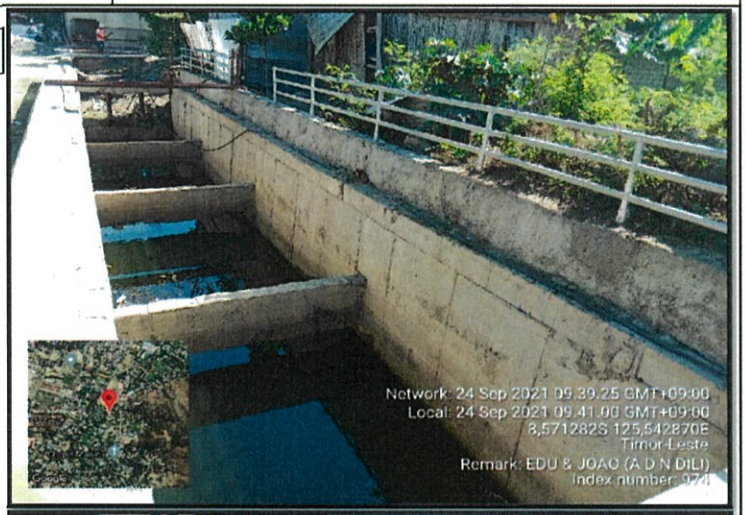

√ On-Going

√ Projecto Refere agora dadaun nia fisiko atinje ona 100%.
(tuir informasaun Contractor submete ona As-Build Drawing, Back-Up Quantity no pagamento 100% ba Owner).

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 14)

Naran Projeto	: **Dili Roads and Drainage Rehabilitation Comoro River Down Stream-Comoro Bridge Area Road**				
No. kontratu	: **SSS/041/MOPTC-2015**				
Data Inspesaun	:				
Fatin Inspesaun	: **Down Stream-Comoro Bridge**				
Koordinadas	:				
	Start Point	**Long**		**Latetude**	
	End Point	**Long**		**Latetude**	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e ligasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point



√ PARADO

√ Projecto Refere parado hela, hein proseso aprovasaun Variation order no pagamento final husi Owner

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO


VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 15)

Naran Projeto	: Dili Road Drainage and Rehabilitation Cruzamento Aitarak laran-Mesjid Anur-KBRI				
No. kontratu	SSS/033/MOPTC-2015				
Data Inspesaun	: 22 - 03 - 2022				
Fatin Inspesaun	: Aitarak laran-Mesjid Anur				
Koordinadas	:				
	Start Point	**Long**	8.549833	**Latetude**	125.561630
	End Point	**Long**	8.549772	**Latetude**	125.560750
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

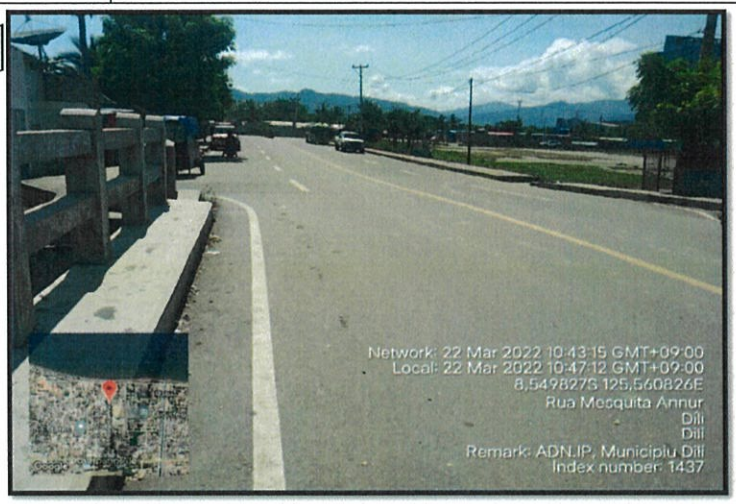Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
√ PARADO √ Projecto Refere parado hela, hein proseso aprovasaun Variation order husi Owner	Pic No.1 Estar Point  Pic No.2 End Point 

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 17)

Naran Projeto	: **Roads and Drainage Rehabilitation Auto Timor - Bebonuk**				
No. kontratu	: **SSS/043/MOPTC-2015**				
Data Inspesaun	: **22 - 03 - 2022**				
Fatin Inspesaun	: **Auto Timor - Bebonuk**				
Koordinadas	:				
	Start Point	**Long**	8.549718	**Latetude**	125.540488
	End Point	**Long**	8.541442	**Latetude**	125.542520
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
Pic No.1 Estar Point √ PARADO √ Projecto Refere parado hela, hein proseso aprovasaun Variation order husi Owner	
Pic No.2 End Point	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 16)

Naran Projeto	: **Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun**				
No. kontratu	: **SSS/032/MOPTC-2015**				
Data Inspesaun	: **22 - 03 - 2022**				
Fatin Inspesaun	: **Presidente - Financas**				
Koordinadas	:				
	Start Point	**Long**	8.551722	**Latetude**	125.562930
	End Point	**Long**	8.549140	**Latetude**	125.561977
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**


Pic No.1 Estar Point



√ PARADO

√ Projecto Refere parado hela, hein proseso aprovasaun Variation order husi Owner

Pic No.2 End Point

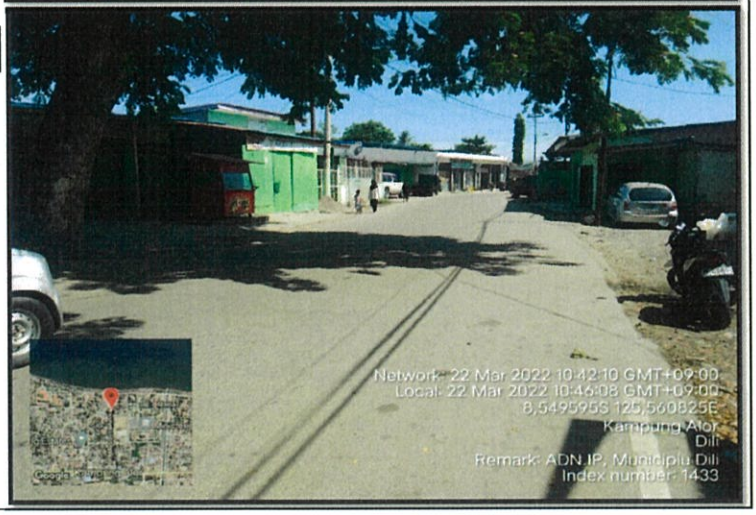

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 21)

Naran Projeto	: **Maloa River**				
No. kontratu	: **SSS/132/MOPTC-2017**				
Data Inspesaun	:				
Fatin Inspesaun	: **Maloa-River**				
Koordinadas	:				
	Start Point	**Long**	8.555579	**Latetude**	125.564332
	End Point	**Long**	9.555579	**Latetude**	126.564332
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**


√ PARADO

√ Aprovasaun Variation Order husi Owner

Pic No.1 Estar Point



Pic No.2 End Point

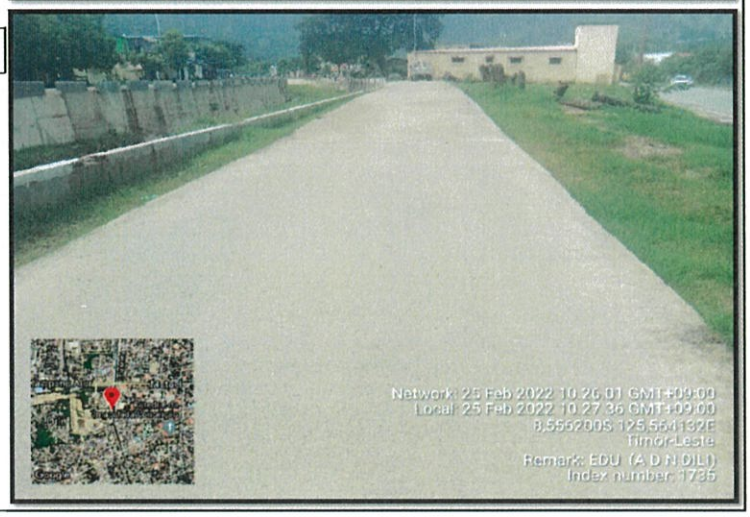

MINISTÉRIO DO PLANO E ORDENAMENTO


VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 44)

Naran Projeto	: **Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili**				
No. kontratu	: **MOP-W-SS-210001**				
Data Inspesaun	: **22-03-2022**				
Fatin Inspesaun	: **Farol**				
Koordinadas	:				
	Start Point	**Long**	8.5481	**Latetude**	12556325
	End Point	**Long**	8.54823	**Latetude**	125.563220
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigaaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

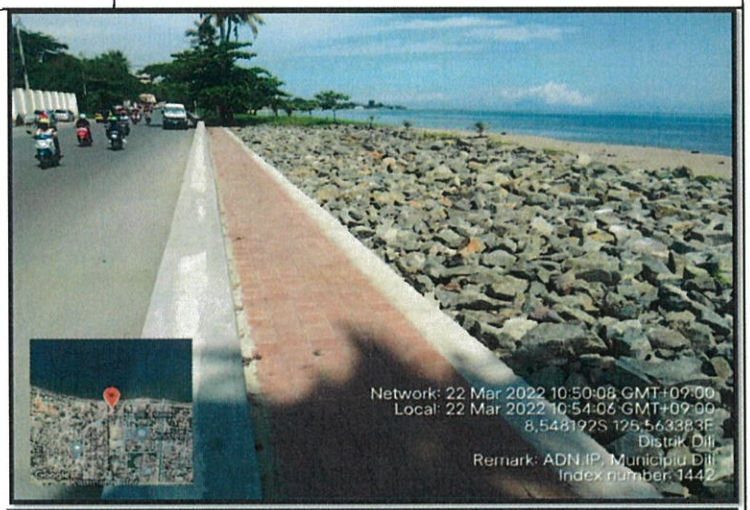Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
√ PHO, Tempo retensaun seidauk remata √ Projecto refere atinji ona 100%	Pic No.1 Estar Point  Pic No.2 End Point 

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 22)

Naran Projeto	: **Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili**				
No. kontratu	: **SSS/127/MOPTC-2017**				
Data Inspesaun	:22 - 03 - 2022				
Fatin Inspesaun	: **Kampung Baru**				
Koordinadas	:				
	Start Point	**Long**	8.561107	**Latetude**	125.545472
	End Point	**Long**	8.570077	**Latetude**	125.542730
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
√ PARADO √ Aprovasaun Variation Order husi Owner	Pic No.1 Estar Point  Pic No.2 End Point 

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 13)

Naran Projeto	: **Dili Roads and Drainage Rehabilitation Comoro River Down Stream-Comoro Bridge Area Road**				
No. kontratu	: **SSS/041/MOPTC-2015**				
Data Inspesaun	:**22 - 03 - 2022**				
Fatin Inspesaun	: **Down Stream-Comoro Bridge**				
Koordinadas	:				
	Start Point	**Long**	8.561107	**Latetude**	125.545472
	End Point	**Long**	8.570077	**Latetude**	125.542730
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**


Pic No.1 Estar Point

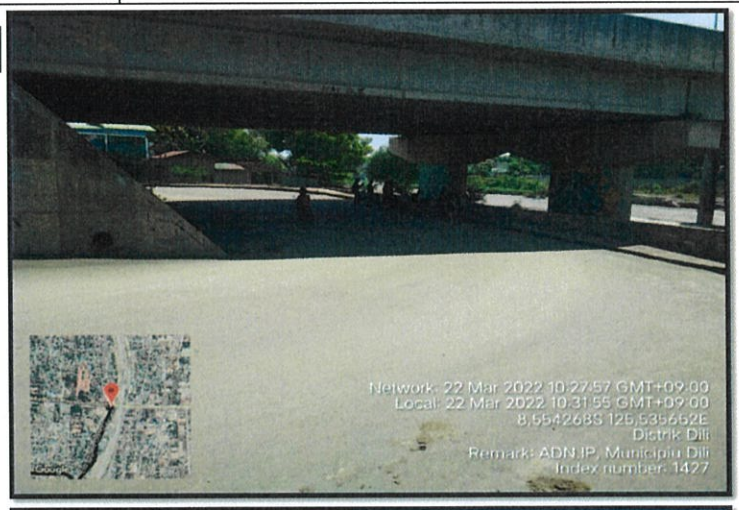

√ PARADO

√ Projecto Refere parado hela, hein proseso aprovasaun Variation order husi Owner

Pic No.2 End Point

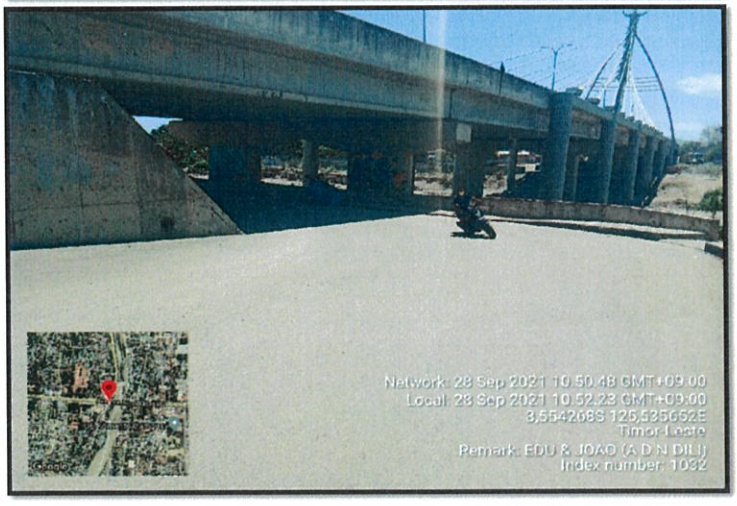

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 11)

Naran Projeto	: **Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili**				
No. kontratu	: **SSS/039/MOPTC-2015**				
Data Inspesaun	:				
Fatin Inspesaun	: **Aimutin to Manleuana**				
Koordinadas	:				
	Start Point	**Long**		**Latetude**	
	End Point	**Long**		**Latetude**	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point



√ Parado

√ Projecto Refere agora dadaun nia fisiko atinje ona 100%.
(tuir informasaun Contractor submete ona As-Build Drawing no pagamento 100% ba Owner).

√

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (DA - 12)


Naran Projeto	: Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro				
No. kontratu	: SSS/042/MOPTC-2015				
Data Inspesaun	: 22 - 03 - 2022				
Fatin Inspesaun	: Komoro				
Koordinadas	:				
	Start Point	**Long**	8.561107	**Latetude**	125.545472
	End Point	**Long**	8.570077	**Latetude**	125.542730
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

√ PARADO

√ Projecto Refere sei hein aprovasaun variation order husi Owner

Pic No.1 Estar Point

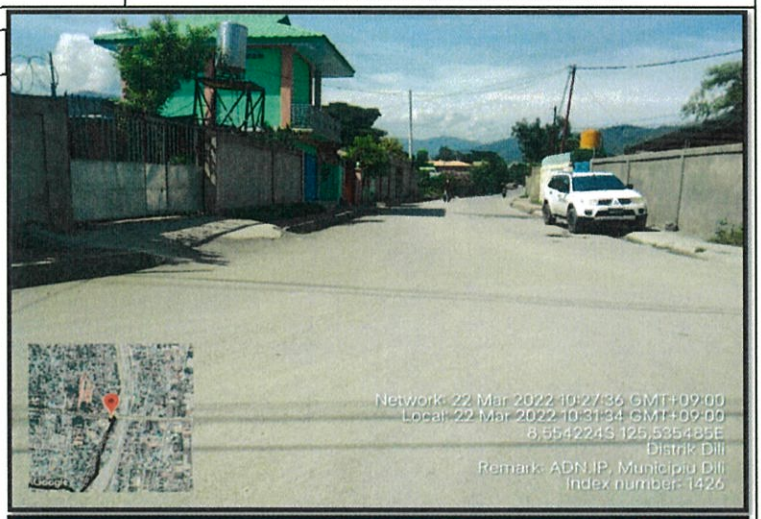

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (MTN - 2)

Naran Projeto	: Constructionof Roadway and Patway at Jardim dos Heroes Metinaro				
No. kontratu	: RDTL:63/MSS/DNFALM-DAD/X/2015				
Data Inspesaun	: 28/02/2022				
Fatin Inspesaun	: Metinaro				
Koordinadas	:				
	Start Point	**Long**	8.50318	**Latetude**	125.812920
	End Point	**Long**	8.504177	**Latetude**	125.813427
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point



√ PARADO

√ Projecto Refere Fisikamente 100% ona (PHO) Falta Retensaun (Restu fila ba kofre Estado).

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NAS - 16)

Naran Projeto	: **Zebra Cross Marking in The Capital City of Dili (162)**				
No. kontratu	:**RDTL 2019-MTC-CD-0040**				
Data Inspesaun	:				
Fatin Inspesaun	: **Catedgral-Vila Verde**				
Koordinadas	:				
	Start Point	**Long**	8.556960	**Latetude**	125.568900
	End Point	**Long**	8.558023	**Latetude**	125.568978
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
√ On-Going √ sei falta Variation order, owner sei verifica √	Pic No.1 Estar Point  Pic No.2 End Point 

MINISTÉRIO DO PLANO E ORDENAMENTO



VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NAS - 9)

Naran Projeto	: For Routine Maintenance - Dili Urban Roads Dili Municipality (162)				
No. kontratu	:MPW-W-190177				
Data Inspesaun	:				
Fatin Inspesaun	: Farol-Metiaut				
Koordinadas	:				
	Start Point	**Long**	8.548605	**Latetude**	125.567070
	End Point	**Long**	8.54360	**Latetude**	125.607700
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

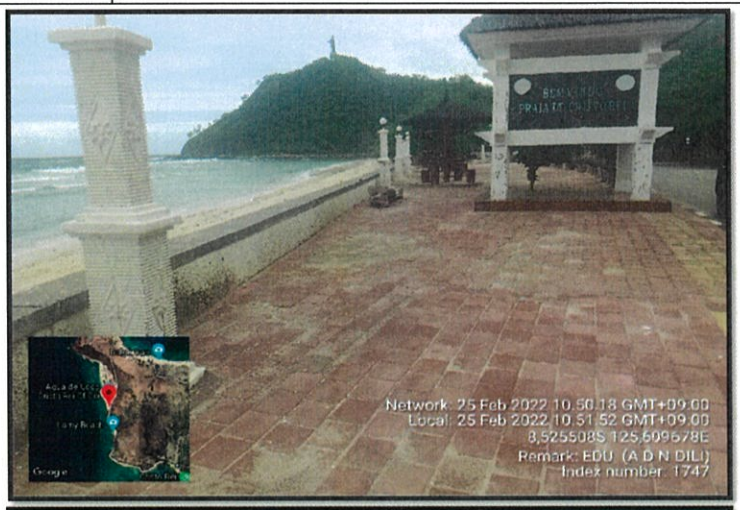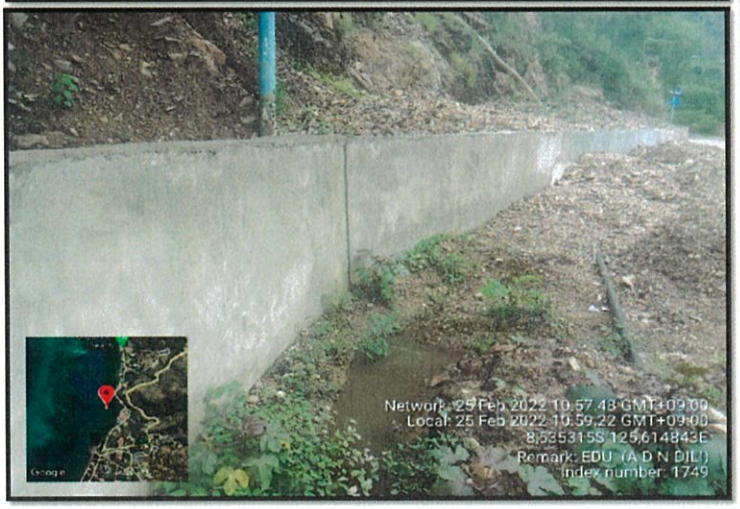Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**
√ On-Going √ Projecto Refere fisikamente 100% sei falta Variation order AS- Build no Back Up Quantity, Aprovasaun husi owner √	Pic No.1 Estar Point  Pic No.2 End Point 

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NF - 12)

Naran Projeto	: Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162
No. kontratu	:MPW-W190099
Data Inspesaun	:
Fatin Inspesaun	: Dare - Lelaus

Koordinadas	:				
	Start Point	Long		Latetude	
	End Point	Long		Latetude	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

√ PHO, Tempo retensaun seidauk remata

√ Projecto Refere fisikamente 100% sei falta pagamento retensaun 12 %

√

Pic No.1 Estar Point



Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NF - 5)

Naran Projeto	: **Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360**				
No. kontratu	: **SSS/200/MOPTC-2016**				
Data Inspesaun	: **16 -03-2022**				
Fatin Inspesaun	: **Dare-Manumeta rai hun**				
Koordinadas	:				
	Start Point	**Long**		**Latetude**	
	End Point	**Long**		**Latetude**	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point



√ PARADO

√ Projecto Refere Fisikamente 100%

√ Sei hein Aprovasaun As-Build ho Back Up Quantity

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NF - 22)

Naran Projeto	: **RIVER PROTECTION AT PALACIO NOBRE LAHANE Sta. 0 + 000 to 0 + 176 Dili Municipality.**				
No. kontratu	:				
Data Inspesaun	: **26 - 04 - 2022**				
Fatin Inspesaun	: **PALACIO NOBRE LAHANE**				
Koordinadas	:				
	Start Point	**Long**	8.56178	**Latetude**	125.646012
	End Point	**Long**	8.561205	**Latetude**	125.646115
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1
Estar Point



√ On-Going, Projecto refere sei halo escavasaun no instala bronjong

√

Pic No.2 End Point



MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

ANEXO C1 (NF - 6)

Naran Projeto	: **Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)**				
No. kontratu	**SSS/218/MOPTC-2016**				
Data Inspesaun	:				
Fatin Inspesaun	: **Mercado lama**				
Koordinadas	:				
	Start Point	**Long**		**Latetude**	
	End Point	**Long**		**Latetude**	
Naran Inspector : 1. Eng. Eduardo Dos Santos				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasun,ADN I.P. Munisipiu Dili	
2. Eng. Joao Quintao do Rego				Enginheiro ba Projeitu Infrastrutura, transporte e Irigasaun,ADN I.P. Munisipiu Dili	

Sketch & Foto Desenho	**Observasaun iha tereno no Foto Aktual**

Pic No.1 Estar Point

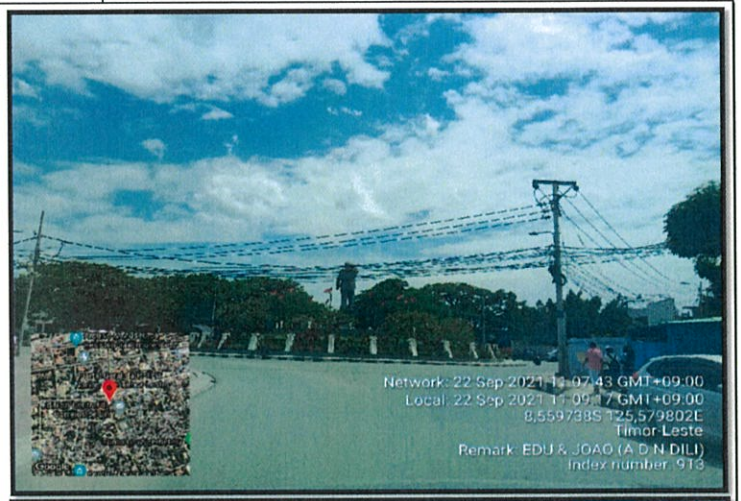


√ PARADO

√ Projecto Refere parado hela, hein proseso aprovasaun Variation order husi Owner

√ Foto laiha tanba sei halo pagamento

Pic No.2 End Point

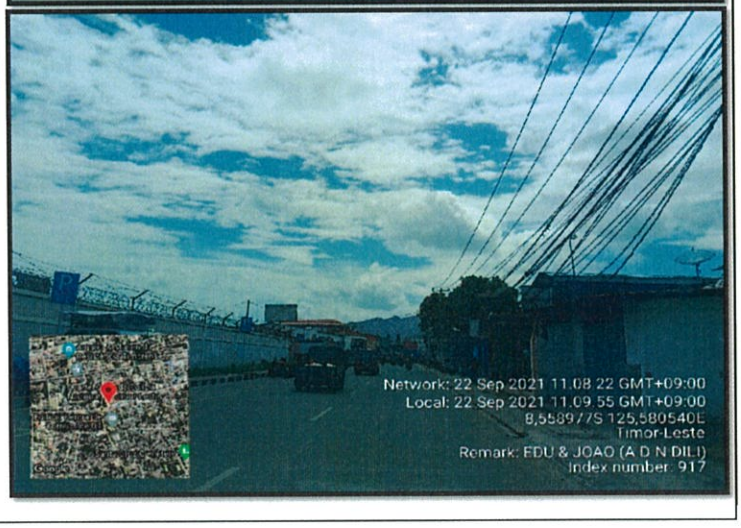

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Eduardo dos Santos	PLANU INSPESAUN
Municipio	MUNICIPIO DILI NO POSTOS	2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL	OBSERVASAUN
								Tu 1 · We 2 · Sa 5 · Su 6 · Sa 5 · Su 6 · Mo 7 · Tu 8 · Sa 5 · Su 6 · fr 11 · Sa 12 · Su 13 · Mo 14 · Tu 15 · Sa 16 · Su 17 · fr 18 · Sa 19 · Su 20 · Mo 21 · Tu 22 · We 23 · Th 24 · fr 25 · Sa 26 · Su 27 · Mo 28 · Tu 29 · We 30 · Th 31	
ATAURO (AT)	1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	FI	MOP	Plan		PARADO
							Actual		
CRISTO REI (CR)	9	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	FI	MOP	Plan		PHO
							Actual		
	10	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	Aspalink Unip Lda	SSS/131/MOPTC-2017	FI	MOP	Plan		PARADO
							Actual		
	11	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio Dili	Star King Unip. Lda	SSS/012/MOP-2020	FI	MOP	Plan		PHO
							Actual		
	12	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	Nimia Unip Lda	RT/154/MOPTC-2016	FI	MOP	Plan		PARADO
							Actual		
	28	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	Titisa Louro Unip.Lda	MPW-W-210067	LM	MOP	Plan		LAO HELA
							Actual		
	29	New Construction of Gabions Tower No.6 section Hera	Jova Construction	NCB/034/MOP-2020	LM	MOP	Plan		PHO
							Actual		
	30	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY.	KEFI OEL Unip.Lda	NCB/033/MOP-2020	LM	MOP	Plan		PARADO
							Actual		
	31	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili	Carya Timor Leste Lda	SSS/009/MOP-2020	FI	MOP	Plan		PHO
							Actual		
	32	For Clean Up of Metiaut - Cristo Rei, Areai Branca - Dolok Oan Emergency Project	Tinolina Unipessoal, Lda	MPW-W-SS 210023	FI	MOP	Plan		PHO
							Actual		
	33	New Construction of Gabion Tower No 6 Section Hera -Manatuto, Dili Municipality	Vilagem Construction Unip.Lda	NCB/032/MOP-2020	FI		Plan		PHO
							Actual		
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan		LAO HELA
							Actual		
DOM ALEIXO (DA)	11	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	12	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	13	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	14	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	G and S Unipessoal Lda	SSS/040/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	15	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	16	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	17	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	FI	MOP	Plan		PARADO
							Actual		
	18	Road and Drainage Rehabilitation Project Aimutin to Manleuana	Aspalink Unip Lda	SSS/308/MOPTC-2016	FI	MOP	Plan		PARADO
							Actual		
	19	New Construction of Median Line "Leader to Elemloi JNC"	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	FI	MOP	Plan		PHO
							Actual		
	21	Maloa River	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	FI	MOP	Plan		PARADO
							Actual		
	22	Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili	Mejori, Lda	SSS/127/MOPTC-2017	FI	MOP	Plan		LAO HELA
							Actual		
	23	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	DMF ACESO	MPW-W180036	LM	MOP	Plan		PHO
							Actual		
	44	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	LM	MPO	Plan		PHO
							Actual		
	48	For River Normalization, Roads Embankment and Road Clean Up of Comoro Mota Ulun - Casnafar, Air Terjun Sarlala Emergency Project	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS 210006	LM	MPO	Plan		PHO
							Actual		
	50	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	Bintang Fajar, Lda	No : MPW-W-SS 210022	LM	MPO	Plan		PHO
							Actual		
	51	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	Monte Veado Unip Lda	MPW-W-SS 210008	LM	MPO	Plan		FHO
							Actual		
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan		PHO
							Actual		

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Eduardo dos Santos	PLANU INSPESAUN
Municipio	MUNICIPIO DILI NO POSTOS	2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL																														OBSERVASAUN
								Tu	We	Sa	Su	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	
								1	2	5	6	5	6	7	8	5	6	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
	56	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	Lizi Construction, Unipessoal Lda		LM	MPO	Plan																															PARADO
							Actual																															
	61	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	Holgapa Unip.Lda	RDTL-2021-MTP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
	62	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	Chegue Rau	RFQ/068/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
	63	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	Holgapa Unip.Lda	RT/069/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
METINARO (MTN)	2	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	Nimia Unip Lda	RDTL:63/MSS/DNFALM-DAD/X/2015	LM	MOP	Plan																															PHO
							Actual																															
	8	New Construction of roadways drainage and parking areia no jardim de harois de Metinaro	Celijo Star Unipesoal Lda	214/MACLN/X/2021	LM	MACLN	Plan																															LAO HELA
							Actual																															
NAIN FETO	5	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	Meteor Unip.Lda	SSS/200/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																															
	6	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	**Suai Indah Unipessoal Lda**	SSS/218/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																															
	7	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	FI	MOP	Plan																															PARADO
							Actual																															
	22	RIVER PROTECTION PALACIO NOBRE	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	LM	GPM	Plan																															LAO HELA
							Actual																															
	23	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	Star King Unip. Lda	MPW-W-SS 210030	FI	MOP	Plan																															PHO
							Actual																															
	28	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	Sanford Const. Unip. Lda	MPW-W-210168	FI	MOP	Plan																															LAO HELA
							Actual																															
	10	Additional Drainage Colmera	**Hailala**	RDTL-MPWTC-W-166139	LM	MOP	Plan																															FHO
							Actual																															
	12	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	Bia Mapel	MPW-W190099	LM	MOP	Plan																															PHO
							Actual																															
NASIONAL	9	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	Lonacca Unipessoal Lda	MPW-W-190177	LM	MOP	Plan																															PHO
							Actual																															
	16	Zebra Cross Marking in The Capital City of Dili (162)	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	LM	MOP	Plan																															PARADO
							Actual																															
TOTAL PROJETO ON-GOING																																						

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

PARADO	18
LAO HELA	14
PHO	5
FHO	3

Prepara Husi :

(Eng. Eduardo dos Santos)
Enginheiro ba Projecto Infrastrutura,Transportes e Irigasaun
Municipio Dili, ADN I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Joao Quintao do Rego
Municipio	MUNICIPIO DILI NO POSTOS

PLANU INSPESAUN

2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL																										OBSERVASAUN
								Tu	We	Sa	Su	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	
								1	2	5	6	5	6	7	8	5	6	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
ATAURO (AT)	1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	FI	MOP	Plan											■							■						■							PARADO
							Actual																															
CRISTO REI (CR)	9	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	FI	MOP	Plan																													■	PHO
							Actual																															
	10	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	Aspalink Unip Lda	SSS/131/MOPTC-2017	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	11	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio Dili	Star King Unip. Lda	SSS/012/MOP-2020	FI	MOP	Plan																													■	PHO
							Actual																															
	12	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	Nimia Unip Lda	RT/154/MOPTC-2016	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	28	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	Titisa Louro Unip.Lda	MPW-W-210067	LM	MOP	Plan	■						■								■						■						■				LAO HELA
							Actual																															
	29	New Construction of Gabions Tower No.6 section Hera	Jova Construction	NCB/034/MOP-2020	LM	MOP	Plan																													■	PHO
							Actual																															
	30	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY.	KEFI OEL Unip.Lda	NCB/033/MOP-2020	LM	MOP	Plan		■						■								■						■										PARADO
							Actual																															
	31	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili	Carya Timor Leste Lda	SSS/009/MOP-2020	FI	MOP	Plan																													■	PHO
							Actual																															
	32	For Clean Up of Metiaut - Cristo Rei, Areai Branca - Dolok Oan Emergency Project	Tinolina Unipessoal, Lda	MPW-W-SS 210023	FI	MOP	Plan																													■	PHO
							Actual																															
	33	New Construction of Gabion Tower No 6 Section Hera -Manatuto, Dili Municipality	Vilagem Construction Unip.Lda	NCB/032/MOP-2020	FI		Plan								■																					■	PHO
							Actual																															
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan																												■			
							Actual																															
DOM ALEIXO (DA)	11	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	12	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	13	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	14	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	G and S Unipessoal Lda	SSS/040/MOPTC-2015	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	15	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	16	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	FI	MOP	Plan	■						■								■						■										PARADO
							Actual																															
	17	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	FI	MOP	Plan		■						■								■						■										PARADO
							Actual																															
	18	Road and Drainage Rehabilitation Project Aimutin to Manleuana	Aspalink Unip Lda	SSS/308/MOPTC-2016	FI	MOP	Plan		■						■								■						■										PARADO
							Actual																															
	19	New Construction of Median Line "Leader to Elemloi JNC"	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	FI	MOP	Plan																													■		PHO
							Actual																															
	21	Maloa River	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	FI	MOP	Plan		■						■								■						■										PARADO
							Actual																															
	22	Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili	Mejori, Lda	SSS/127/MOPTC-2017	FI	MOP	Plan		■						■								■						■						■				LAO HELA
							Actual																															
	23	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	DMF ACESO	MPW-W180036	LM	MOP	Plan																													■		PHO
							Actual																															
	44	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	LM	MPO	Plan																													■		PHO
							Actual																															
	48	For River Normalization, Roads Embankment and Road Clean Up of Comoro Mota Ulun - Casnafar, Air Terjun Sarlala Emergency Project	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS 210006	LM	MPO	Plan																													■		PHO
							Actual																															
	50	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	Bintang Fajar, Lda	No : MPW-W-SS 210022	LM	MPO	Plan																													■		PHO
							Actual																															
	51	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	Monte Veado Unip Lda	MPW-W-SS 210008	LM	MPO	Plan																															FHO
							Actual																															
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan																													■		PHO
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Joao Quintao do Rego
Municipio	MUNICIPIO DILI NO POSTOS

PLANU INSPESAUN

2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL																										OBSERVASAUN
								Tu	We	Sa	Su	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	
								1	2	5	6	5	6	7	8	5	6	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
	56	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	Lizi Construction, Unipessoal Lda		LM	MPO	Plan																														PARADO
							Actual																														
	61	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	Holgapa Unip.Lda	RDTL-2021-MTP-2021	LM	MPO	Plan																														LAO HELA
							Actual																														
	62	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	Chegue Rau	RFQ/068/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																														
	63	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	Holgapa Unip.Lda	RT/069/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																														
METINARO (MTN)	2	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	Nimia Unip Lda	RDTL:63/MSS/DNFALM-DAD/X/2015	LM	MOP	Plan																															PHO
							Actual																														
	8	New Construction of roadways drainage and parking areia no jardim de harois de Metinaro	Celijo Star Unipesoal Lda	214/MACLN/X/2021	LM	MACLN	Plan																															LAO HELA
							Actual																														
NAIN FETO	5	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	Meteor Unip.Lda	SSS/200/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																														
	6	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	**Suai Indah Unipessoal Lda**	SSS/218/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																														
	7	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	FI	MOP	Plan																															PARADO
							Actual																														
	22	RIVER PROTECTION PALACIO NOBRE	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	LM	GPM	Plan																															LAO HELA
							Actual																														
	23	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	Star King Unip. Lda	MPW-W-SS 210030	FI	MOP	Plan																															PHO
							Actual																														
	28	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	Sanford Const. Unip. Lda	MPW-W-210168	FI	MOP	Plan																															LAO HELA
							Actual																														
	10	Additional Drainage Colmera	**Hailala**	RDTL-MPWTC-W-166139	LM	MOP	Plan																															FHO
							Actual																														
	12	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	Bia Mapel	MPW-W190099	LM	MOP	Plan																															PHO
							Actual																														
NASIONAL	9	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	Lonacca Unipessoal Lda	MPW-W-190177	LM	MOP	Plan																															PHO
							Actual																														
	16	Zebra Cross Marking in The Capital City of Dili (162)	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	LM	MOP	Plan																															PARADO
							Actual																														
		TOTAL PROJETO ON-GOING																																			

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

PARADO	18
LAO HELA	14
PHO	5
FHO	3

Prepara Husi :

(Eng. João Quintão do Rego)
Enginheiro ba Projecto Infrastrutura,Transportes e Irigasaun
Municipio Dili, ADN I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e validasaun de Qualidade ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Eduardo dos Santos
Municipio	MUNICIPIO DILI NO POSTOS

PLANU INSPESAUN

2022

ABRIL

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	Tu 1	We 2	Sa 5	Su 6	Sa 5	Su 6	Mo 7	Tu 8	Sa 5	Su 6	fr 11	Sa 12	Su 13	Mo 14	Tu 15	Sa 16	Su 17	fr 18	Sa 19	Su 20	Mo 21	Tu 22	We 23	Th 24	fr 25	Sa 26	Su 27	Mo 28	Tu 29	We 30	Th 31	OBSERVASAUN
ATAURO (AT)	1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	FI	MOP	Plan																																PARADO
							Actual																																
CRISTO REI (CR)	9	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	FI	MOP	Plan																															PHO
							Actual																																
	10	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	Aspalink Unip Lda	SSS/131/MOPTC-2017	FI	MOP	Plan																															PARADO
							Actual																																
	11	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio Dili	Star King Unip. Lda	SSS/012/MOP-2020	FI	MOP	Plan																															PHO
							Actual																																
	12	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	Nimia Unip Lda	RT/154/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																																
	28	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	Titisa Louro Unip.Lda	MPW-W-210067	LM	MOP	Plan																															LAO HELA
							Actual																																
	29	New Construction of Gabions Tower No.6 section Hera	Jova Construction	NCB/034/MOP-2020	LM	MOP	Plan																															PHO
							Actual																																
	30	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY.	KEFI OEL Unip.Lda	NCB/033/MOP-2020	LM	MOP	Plan																															PARADO
							Actual																																
	31	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili	Carya Timor Leste Lda	SSS/009/MOP-2020	FI	MOP	Plan																															PHO
							Actual																																
	32	For Clean Up of Metiaut - Cristo Rei, Areai Branca - Dolok Oan Emergency Project	Tinolina Unipessoal, Lda	MPW-W-SS 210023	FI	MOP	Plan																															PHO
							Actual																																
	33	New Construction of Gabion Tower No 6 Section Hera -Manatuto, Dili Municipality	Vilagem Construction Unip.Lda	NCB/032/MOP-2020	FI		Plan																															PHO
							Actual																																
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																																
DOM ALEIXO (DA)	11	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	12	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	13	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	14	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	G and S Unipessoal Lda	SSS/040/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	15	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	16	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	17	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																																
	18	Road and Drainage Rehabilitation Project Aimutin to Manleuana	Aspalink Unip Lda	SSS/308/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																																
	19	New Construction of Median Line "Leader to Elemloi JNC"	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	FI	MOP	Plan																															PHO
							Actual																																
	21	Maloa River	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	FI	MOP	Plan																															PARADO
							Actual																																
	22	Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili	Mejori, Lda	SSS/127/MOPTC-2017	FI	MOP	Plan																															LAO HELA
							Actual																																
	23	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	DMF ACESO	MPW-W180036	LM	MOP	Plan																															FHO
							Actual																																
	44	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	LM	MPO	Plan																															PHO
							Actual																																
	48	For River Normalization, Roads Embankment and Road Clean Up of Comoro Mota Ulun - Casnafar, Air Terjun Sarlala Emergency Project	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS 210006	LM	MPO	Plan																															FHO
							Actual																																
	50	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	Bintang Fajar, Lda	No : MPW-W-SS 210022	LM	MPO	Plan																															FHO
							Actual																																
	51	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	Monte Veado Unip Lda	MPW-W-SS 210008	LM	MPO	Plan																															FHO
							Actual																																
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan																															PHO
							Actual																																

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Eduardo dos Santos	PLANU INSPESAUN
Municipio	MUNICIPIO DILI NO POSTOS	2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL																														OBSERVASAUN
								Tu	We	Sa	Su	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	
								1	2	5	6	5	6	7	8	5	6	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
	56	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	Lizi Construction, Unipessoal Lda		LM	MPO	Plan																															PARADO
							Actual																															
	61	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	Holgapa Unip.Lda	RDTL-2021-MTP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
	62	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	Chegue Rau	RFQ/068/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
	63	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	Holgapa Unip.Lda	RT/069/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
METINARO (MTN)	2	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	Nimia Unip Lda	RDTL:63/MSS/DNFALM-DAD/X/2015	LM	MOP	Plan																															PHO
							Actual																															
	8	New Construction of roadways drainage and parking areia no jardim de harois de Metinaro	Celijo Star Unipesoal Lda	214/MACLN/X/2021	LM	MACLN	Plan																															LAO HELA
							Actual																															
NAIN FETO	5	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	Meteor Unip.Lda	SSS/200/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																															
	6	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	**Suai Indah Unipessoal Lda**	SSS/218/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																															
	7	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	FI	MOP	Plan																															PHO
							Actual																															
	22	RIVER PROTECTION PALACIO NOBRE	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	LM	GPM	Plan																															LAO HELA
							Actual																															
	23	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	Star King Unip. Lda	MPW-W-SS 210030	FI	MOP	Plan																															PHO
							Actual																															
	28	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	Sanford Const. Unip. Lda	MPW-W-210168	FI	MOP	Plan																															LAO HELA
							Actual																															
	10	Additional Drainage Colmera	**Hailala**	RDTL-MPWTC-W-166139	LM	MOP	Plan																															FHO
							Actual																															
	12	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	Bia Mapel	MPW-W190099	LM	MOP	Plan																															PHO
							Actual																															
NASIONAL	9	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	Lonacca Unipessoal Lda	MPW-W-190177	LM	MOP	Plan																															PHO
							Actual																															
	16	Zebra Cross Marking in The Capital City of Dili (162)	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	LM	MOP	Plan																															PARADO
							Actual																															
TOTAL PROJETO ON-GOING																																						

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

PARADO	17
LAO HELA	9
PHO	14
FHO	5

Prepara Husi :

(Eng. Eduardo dos Santos)
Enginheiro ba Projecto Infrastrutura,Transportes e Irigasaun
Municipio Dili, ADN I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Joao Quintao do Rego
Municipio	MUNICIPIO DILI NO POSTOS

PLANU INSPESAUN

2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL																													OBSERVASAUN
								Tu	We	Sa	Su	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	Sa	Su	fr	Sa	Su	Mo	Tu	We	Th	fr	Sa	Su	Mo	Tu	We	Th	
								1	2	5	6	5	6	7	8	5	6	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
ATAURO (AT)	1	R4D Rural Road Rehabilitation Pala - Iliana - Tasi Chainage 0+000 - 7+000 Atauro Dili Municipality	Chime Naya Buras Unip. Lda	RT/029/MOP-2019	FI	MOP	Plan																															PARADO
							Actual																															
CRISTO REI (CR)	9	Emergency Project in 2016 Flood Control Project Bedois River, Dili District (1,030 km)	JRM JV DRQ, Unip. Lda	SSS/082/MOPTC-2017	FI	MOP	Plan																															PHO
							Actual																															
	10	Dili Roads and Drainage Rehabilitation Road Section : Jct. Culuhun - Jct Halilaran and Audian - Bemori - St. Cruz Municipality Dili	Aspalink Unip Lda	SSS/131/MOPTC-2017	FI	MOP	Plan																															PARADO
							Actual																															
	11	Emergency Work For River Protection at 5 de Maio, Becora (Pacote No. 5) Municipio Dili	Star King Unip. Lda	SSS/012/MOP-2020	FI	MOP	Plan																															PHO
							Actual																															
	12	Road Maintenance Section Area Branca - Hera,Benamauk - Hera (A01)	Nimia Unip Lda	RT/154/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																															
	28	Spot Improvement Hera - Liurai Star 0+000 - 4+000 Dili and Aileu Municipality	Titisa Louro Unip.Lda	MPW-W-210067	LM	MOP	Plan																															LAO HELA
							Actual																															
	29	New Construction of Gabions Tower No.6 section Hera	Jova Construction	NCB/034/MOP-2020	LM	MOP	Plan																															PHO
							Actual																															
	30	NEW CONSTRUCTION OF RETAINING WALL PROTECTION & INSTALLATION GABIONS TOWER NO.19 SECTION HERA - DILI, DILI MUNICIPALITY.	KEFI OEL Unip.Lda	NCB/033/MOP-2020	LM	MOP	Plan																															PARADO
							Actual																															
	31	Emergency Work for Kuluhun Ate Ponte Habibie/Bidau Santa-Ana (Pacote I) Municipality Dili	Carya Timor Leste Lda	SSS/009/MOP-2020	FI	MOP	Plan																															PHO
							Actual																															
	32	For Clean Up of Metiaut - Cristo Rei, Areai Branca - Dolok Oan Emergency Project	Tinolina Unipessoal, Lda	MPW-W-SS 210023	FI	MOP	Plan																															PHO
							Actual																															
	33	New Construction of Gabion Tower No 6 Section Hera -Manatuto, Dili Municipality	Vilagem Construction Unip.Lda	NCB/032/MOP-2020	FI		Plan																															PHO
							Actual																															
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan																															LAO HELA
							Actual																															
DOM ALEIXO (DA)	11	Dili Roads and Drainage Rehabilitation Road Section Hudilaran - Bairo Pite Municipality Dili	Pereira Limitada Unipessoal Lda	SSS/039/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	12	Dili Roads and Drainage Rehabilitation Timor Block east Comoro river and intersection of futura bridge 3 west Comoro	Sangus I Unipessoal Lda	SSS/042/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	13	Dili Roads and Drainage Rehabilitation Comoro River Down Stream - Comoro Bridge Area Road	Nautetu I, II Unipessoal Lda	SSS/041/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	14	Dili Roads and Drainage Rehabilitation Ocean view (Arbiru Hotel) Comoro river down stream Comoro Bridge (North of Bridges)	G and S Unipessoal Lda	SSS/040/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	15	Dili Roads and Drainage Rehabilitation Cruzamento Aitarak Laran Mesid An'ur KBRI	Helmi Construction Unipessoal Lda	SSS/033/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	16	Dili Roads and Drainage Rehabilitation Palacio Presidente - Financas - Tasi Ibun	Hidayat Unipessoal Lda	SSS/032/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	17	Roads and Drainage Rehabilitation Auto Timor - Bebonuk	Hidayat Unipessoal Lda	SSS/043/MOPTC-2015	FI	MOP	Plan																															PARADO
							Actual																															
	18	Road and Drainage Rehabilitation Project Aimutin to Manleuana	Aspalink Unip Lda	SSS/308/MOPTC-2016	FI	MOP	Plan																															PARADO
							Actual																															
	19	New Construction of Median Line "Leader to Elemloi JNC"	Delta Flores Unipessoal, Lda	SSS/129/MOPTC-2017	FI	MOP	Plan																															PHO
							Actual																															
	21	Maloa River	Montana Diak, Unipessoal, Lda	SSS/132/MOPTC-2017	FI	MOP	Plan																															PARADO
							Actual																															
	22	Road Rehabilitation Project, Road Section: Aldeia 30 de Augusto, Comoro Municipality of Dili	Mejori, Lda	SSS/127/MOPTC-2017	FI	MOP	Plan																															LAO HELA
							Actual																															
	23	Rebidding of Packega New Sand Pocket Construction Road Maintenance Section Manleu (Maok River) Municipality Dili (162)	DMF ACESO	MPW-W180036	LM	MOP	Plan																															FHO
							Actual																															
	44	Emergency Projecto Estrada Kampu Alor Tasi Ibun Municipio Dili	Montana Diak, Unipessoal, Lda	MOP-W-SS-210001	LM	MPO	Plan																															PHO
							Actual																															
	48	For River Normalization, Roads Embankment and Road Clean Up of Comoro Mota Ulun - Casnafar, Air Terjun Sarlala Emergency Project	(NTN) Natureza Timor Naroman, Lda	MPW-W-SS 210006	LM	MPO	Plan																															FHO
							Actual																															
	50	For River Normalization And Roads Clean Up Casnafar, Manleu-Aldeia Mane and Aldeia Laulora Emergency Project	Bintang Fajar, Lda	No : MPW-W-SS 210022	LM	MPO	Plan																															FHO
							Actual																															
	51	Cleaning Up of River Adjacent to Palacio Presidente Aitarak Laran, Farol & Fomento Ponte Comoro 2 Emergency Projec	Monte Veado Unip Lda	MPW-W-SS 210008	LM	MPO	Plan																															FHO
							Actual																															
	52	Emergency Project for Mota Bidau Toko Baru Municipio Dili	Santana Diak Unipessoal Lda	RT/066/MOP-2021	LM	MPO	Plan																															PHO
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Joao Quintao do Rego
Municipio	MUNICIPIO DILI NO POSTOS

PLANU INSPESAUN

2022

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	ACTION	ABRIL	OBSERVASAUN
								Tu 1 · We 2 · Sa 5 · Su 6 · Sa 5 · Su 6 · Mo 7 · Tu 8 · Sa 5 · Su 6 · fr 11 · Sa 12 · Su 13 · Mo 14 · Tu 15 · Sa 16 · Su 17 · fr 18 · Sa 19 · Su 20 · Mo 21 · Tu 22 · We 23 · Th 24 · fr 25 · Sa 26 · Su 27 · Mo 28 · Tu 29 · We 30 · Th 31	
	56	Rehabilitation of JCT. Australia Embassy - Marconi Roas (Access to Hotel Hilton) Municipio Dili	Lizi Construction, Unipessoal Lda		LM	MPO	Plan		PARADO
							Actual		
	61	New Construction of Runway Shoulder & Replacement of Runway Concrete to Runway Asphalt Aeroporto Internacional Nicoulau Lobato	Holgapa Unip.Lda	RDTL-2021-MTP-2021	LM	MPO	Plan		LAO HELA
							Actual		
	62	Emergency project of new construction Boc Culvert (Single Cell) Ailok Laran	Chegue Rau	RFQ/068/MOP-2021	LM	MPO	Plan		LAO HELA
							Actual		
	63	Emergency Project concrete retaining wall protection of Maloa River sta 0+000-0+100	Holgapa Unip.Lda	RT/069/MOP-2021	LM	MPO	Plan		LAO HELA
							Actual		
METINARO (MTN)	2	Construction of Roadway and Pathway at Jardim dos Heroes Metinaro	Nimia Unip Lda	RDTL:63/MSS/DNFALM-DAD/X/2015	LM	MOP	Plan		PHO
							Actual		
	8	New Construction of roadways drainage and parking areia no jardim de harois de Metinaro	Celijo Star Unipesoal Lda	214/MACLN/X/2021	LM	MACLN	Plan		LAO HELA
							Actual		
NAIN FETO	5	Construction of Jct. Dare-Manumetan Raihun road Sta. 0+000-6+360	Meteor Unip.Lda	SSS/200/MOPTC-2016	FI	MOP	Plan		PARADO
							Actual		
	6	Dili Roads and Drainage Reh. Rotunda Mercado Lama-Ponte Comoro (Variation Order)	**Suai Indah Unipessoal Lda**	SSS/218/MOPTC-2016	FI	MOP	Plan		PARADO
							Actual		
	7	Emergency Project Ponte Ponte My Friend - Ponte Hali Laran, Kuluhun 2020 (Pakote No. 3) Municipality Dili	Jonize Construction, Unip. Lda	SSS/010/MOP-2020	FI	MOP	Plan		PHO
							Actual		
	22	RIVER PROTECTION PALACIO NOBRE	ROYAL TIMORENSE Unip.Lda	NCB/040/MOP-2020	LM	GPM	Plan		LAO HELA
							Actual		
	23	For River Normalization of Lahane River (Be'e Dois), Mortuario Lahane Emergency Project	Star King Unip. Lda	MPW-W-SS 210030	FI	MOP	Plan		PHO
							Actual		
	28	Projecto Rehabilitasaun estrada urbana , Ponte Hali laran/Ponte My friend/Ponte Kuluhun (Sta 0+000-1+450)	Sanford Const. Unip. Lda	MPW-W-210168	FI	MOP	Plan		LAO HELA
							Actual		
	10	Additional Drainage Colmera	**Hailala**	RDTL-MPWTC-W-166139	LM	MOP	Plan		FHO
							Actual		
	12	Rural Road Maintenance in Dili Dare - Lelaus Road Sta. 0+000 - 5+000 Municipality Dili / 162	Bia Mapel	MPW-W190099	LM	MOP	Plan		PHO
							Actual		
NASIONAL	9	For Routine Maintenance - Dili Urban Roads Dili Municipality (162)	Lonacca Unipessoal Lda	MPW-W-190177	LM	MOP	Plan		PHO
							Actual		
	16	Zebra Cross Marking in The Capital City of Dili (162)	Fariviolet Unipessoal Lda	RDTL 2019-MTC-CD-0040	LM	MOP	Plan		PARADO
							Actual		
TOTAL PROJETO ON-GOING									

Note:

Planu Periode inspesaun iha tereinu — **Implementa Periode inspesaun iha tereinu** — **Relatoriu avaliasuan mensal iha Dili** — **Inspesaun Pagamentu Anual iha tereinu**

PARADO	17
LAO HELA	9
PHO	14
FHO	5

Prepara Husi :

(Eng. João Quintão do Rego)
Enginheiro ba Projecto Infrastrutura,Transportes e Irigasaun
Municipio Dili, ADN I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P

Project Name : **Preparation For Deitalied Engineering Design DED for Dili Urban Road (re Tender)**

Location : **Cristo Rei - Dolok Oan Junction, 5 km**

Consultant : **Kiat, Unipessal Lda Joint Venture PT Purnajasa Bimapratama**

Invoice Number : Interim Billing no.01

#ANEXU (C2)

No	DESCRIPTION		Contract Amount	CONSULTAN/OWNER INVOICE			ADN RECOMMENDATION			Progress (%)
			Original	Previous Invoice	This Invoice	Total-to-Date	Previous Billing	This Billing	Total-to-Date	
				Amount	Amount	Amount	Amount	Amount	Amount	
1	**1st payment (10%): Inception Report by Activity**	**AREA OF ACTIVITY (4 Area base on Revised Payment Schedule**								
a	Area	Cristo Rei With Distance 5 Km and Estimated Proposed Budget of USD	$ 99,874.00	$ -	$ 9,987.40	$ 9,987.40	$ -	$ 9,987.40	$ 9,987.40	3.6%
b	Area	Delta I,II,IV & Manleu With Estimated Budget USD	$ 69,600.00		$ 6,960.00	$ 6,960.00		$ 6,960.00	$ 6,960.00	2.5%
c	Area	Estrada Ponte becusse- ponte maufelo(Liman Los no Karuk), Marabia(Dalan ba Capela), Estrada Cruzamento Taibessi(Dalan california 7 mercadu Taibesi). Estrada Becusse- Aituri Laran (sorin los no Karuk) With proposed budget USD	$ 65,040.00		$ 6,504.00	$ 6,504.00		$ 6,504.00	$ 6,504.00	2.4%
d	Area	Perumnas Pintu I & Perumnas Pintu II With Estimated Budget	$ 42,120.00		$ 4,212.00	$ 4,212.00		$ 4,212.00	$ 4,212.00	1.5%
		TOTAL CONTRACT PRICE	**276,634.00**	**$ -**	**$ 27,663.40**	**$ 27,663.40**	**$ -**	**$ 27,663.40**	**$ 27,663.40**	**10%**

Checked by

1.Eng. Tito Edgar F.N de Jesus
Engineiro Projecto Imprestimo e konsultan,ADN,I.P

2.Eng. Teresa Gomes
Engineira Projecto Imprestimo e konsultan,ADN,I.P

Verified by

Eng. Remigio do Santos
Enginheiro Senior ba Projecto Infrastrutura,Transportes e Irigasaun,ADN , I.P.

Certified by

Eng.Emerenciana da Costa Maia Freitas
Coordenadora Unidade de Controlo e Validação de Qualidade,ADN, I.P.)

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

2022

April

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fri 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fri 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fri 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fri 29	Sa 30	OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Iha Dili**
							Actual																															
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Konsultan iha Dili**
							Actual																															
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Pagamento Konsultan iha Dili**
							Actual																															
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Pagamento Konsultan iha Dili**
							Actual																															
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Pagamento Konsultan iha Dili**
							Actual																															
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															**PHO**
							Actual																															
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Pagamento Konsultan iha Dili**
							Actual																															
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															**PHO**
							Actual																															
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															**Halo Relatorio Pagamento Konsultan iha Dili**
							Actual																															
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

Vidal Guterres
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	**Tito Edgar F.N de Jesus**
Municipio	**MUNICIPIO DILI NO POSTOS**

2022

April

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Fr 1	Sa 2	Su 3	Mo 4	Tu 5	We 6	Th 7	Fri 8	Sa 9	Su 10	Mo 11	Tu 12	We 13	Th 14	Fri 15	Sa 16	Su 17	Mo 18	Tu 19	We 20	Th 21	Fri 22	Sa 23	Su 24	Mo 25	Tu 26	We 27	Th 28	Fri 29	Sa 30	OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Iha Dili
							Actual																															
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Konsultan iha Dili
							Actual																															
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento Konsultan iha Dili
							Actual																															
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento Konsultan iha Dili
							Actual																															
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento Konsultan iha Dili
							Actual																															
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento Konsultan iha Dili
							Actual																															
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO Lda		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento Konsultan iha Dili
							Actual																															
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															
							Actual																															

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual		
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
								PHO
TOTAL PROJETO ON-GOING								

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

Tito Edgar F. N de Jesus
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.


Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Eng.	Teresa Gomes						
Municipio	MUNICIPIO DILI NO POSTOS						
Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co .,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual

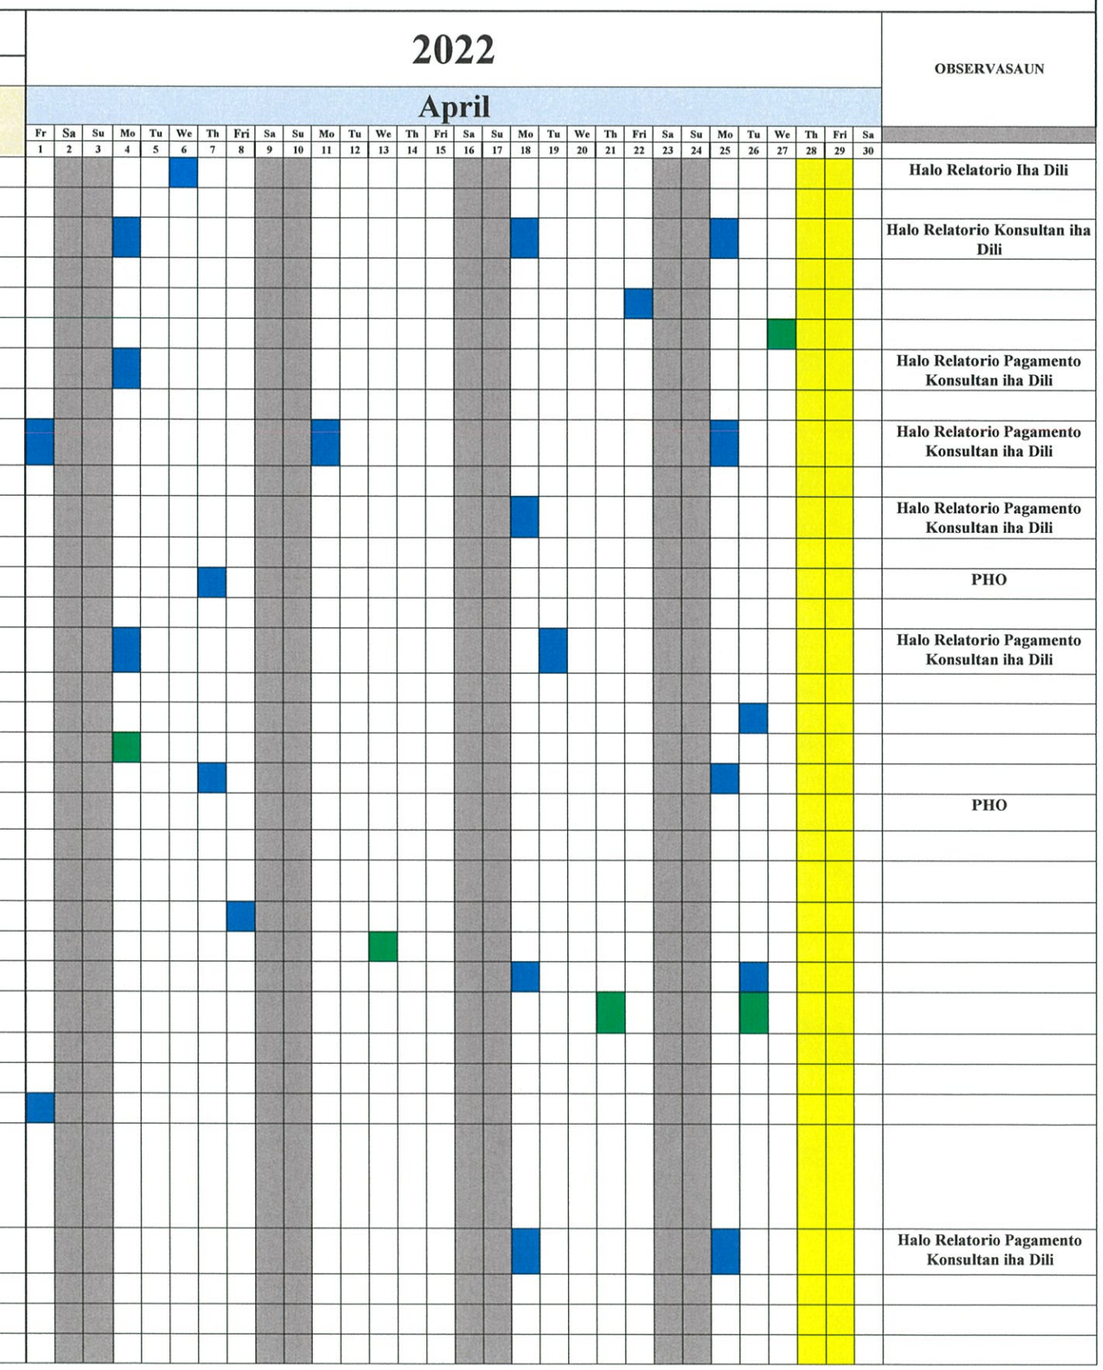

OBSERVASAUN
Halo Relatorio Iha Dili
Halo Relatorio Konsultan iha Dili
Halo Relatorio Pagamento Konsultan iha Dili
Halo Relatorio Pagamento Konsultan iha Dili
Halo Relatorio Pagamento Konsultan iha Dili
PHO
Halo Relatorio Pagamento Konsultan iha Dili
PHO
Halo Relatorio Pagamento Konsultan iha Dili

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual		
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
								PHO
TOTAL PROJETO ON-GOING								

Note:

Planu Periode inspesaun iha tereinu **Implementa Periode inspesaun iha tereinu** **Relatoriu avaliasuan mensal iha Dili** **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

Teresa Gomes
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

Municipio / Posto

IMPRESTIMO

2022

OBSERVASAUN

April

No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	
1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan / Actual
3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan / Actual
4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section (Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan / Actual
7	Road Climate Resilience project (RCRP) upgrading project and maintenance of Dili-Ainaro Road, Lot 3(Solerema - Hatu Udo Section (Km 34+620 - Km 56+000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan / Actual
8	Road Climate Resilience project (RCRP) upgrading and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan / Actual
9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan / Actual
10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan / Actual
11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan / Actual
12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta 100+360 - 144+995 Manatuto	China Nuclear industry 22ND Construction CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan / Actual
13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+520) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Engr. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan / Actual
14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan / Actual
15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phils, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan / Actual
`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan / Actual

PHO

PHO

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau Irigation Schema	PT.Susnda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	Konsultan la serviso ona iha tereno,maibe pagamento scidauk hotu
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

Eng. Vidal Guterres
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng.	Teresa Gomes
Municipio	MUNICIPIO DILI NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto	
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Juncaos (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6) and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd (Joint venture)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A02-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	7	Road Climate Resilience project (RCRP) upgranding project and maintenance of Dili- Ainaro Road Lot 3(Solerema - Dandudatu Section (Km 39+620 - Km 68+000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili - Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+033) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili - Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 132+000)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no : 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co.Ltd JV with Kenhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN) TIM	Plan / Actual
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.Ltd JV with Kenhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Soleirma Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunlwn Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Soleirma Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	Intercontinental Consultanst and Technocrats Pvt Ltd. (India) in Association With Infra Consultants in the Phils. (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan / Actual
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan / Actual

2022

April

Fr	Sa	Su	Mo	Tu	We	Th	Sa	Su	Mo	Tu	We	Th	Sa	Su	Mo	Tu	We	Th	Sa	We	Th	Fr	Sa	Su	Mo	We	Th	Fr	Sa
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

OBSERVASAUN

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) mofas matadoro - RTK, Comoro mota ulun	Vov Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Supervision of daradau irigation Schema	PT.Sunda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	
	TOTAL PROJETO ON-GOING						

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

PHO

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

Eng. Teresa Gomes
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng.	Tito Edgar F.N. de Jesus
Municipio	MUNICIPIO DILI NO POSTOS

2022

April

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Corp		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd (Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,ltd (Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintenance of Dili- Ainaro Road Lot 3(Seloreno - Bandudsto Section (Km 34+620 - Km 64+000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudsto-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no. 3020 - TIM and 3021 - TLS)	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co.Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22nD Construction.CO.Ltda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Soibada Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Soibenta Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consultng Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste	Intercontinental Consultanst and Technocrats Pvt Ltd. (India) in Association With Infra Consultants in the Phils. (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS - 2000025	LM	MOP	Plan Actual		
21	For Preparation of detailed engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Hasin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Nicoles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Exusting dili liquisa road to consc akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Supervisi for Konstruction Supervision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu
								PHO
TOTAL PROJETO ON-GOING								

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

Eng. Tito Edgar F.N. de Jesus
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.
