REPÚBLICA DEMOCRÁTICA DE TIMOR LESTE
MINISTÉRIO DO PLANO E ORDENAMENTO

Agência de Desenvolvimento Nacional, Instituto Público

A.D.N. I.P.
Agência de Desenvolvimento Nacional, Instituto Público

RELATÓRIU MENSÁL IMPLEMENTASAUN PROJETUS MUNISÍPIU VIQUEQUE

JUNHO 2022



SUMÁRIO

RELATÓRIO
IMPLEMENTASAUN PROJETU INFRAESTRUTURA IHA MUNICIPIO VIQUEQUE
JUNHO 2022

Prepara Husi :

(Eng. Roberto M. Martins)
Eng. ba Projetu Infraestrutura, Transportes e Irigasaun, Municipio Viqueque ADN, I.P

(Eng. Salvador Martins)
Eng. ba Projetu Infraestrutura, Transportes e Irigasaun, Municipio Viqueque ADN, I.P

(Eng. Bebiano C. de Jesus Lopes)
Eng. ba Projetu Edifício Publiku no Beé Saneamentu, Municipio Viqueque ADN, I.P

(Eng. Adonis Julio Fernandes)
Eng. ba Projetu Mekanikal Elektrikal, Municipio Viqueque ADN, I.P

Verifika Husi :

(Arc. Fransisco X D D Jeronimo)
Eng. Senior ba Edificio Publiku no Beé Saneamentu, ADN, I.P

(Eng. Remigio da C.S dos Santos)
Eng. Senior ba Projetu Infraestrutura Transportes e Irigasaun, ADN, I.P

(Deolindo de F Marques)
Chefe Sek. Projetu M.E & ITC, ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade, ADN, I.P

Aprova Husi :

(Mariano Renato Monteiro da Cruz, ST. M.Eng)
Director Ezecutivo , ADN, I.P

INDICE

SUMÁRIO **2**

INDICE **3**

I. INTRODUSAUN **4**

1.1 Enkuadramentu Legal 4
1.2 Perfil Municipio Viqueque 4
1.3 Lista Projecto 7

II. PROGRESU FISIKU **16**

2.1 Progresso Fisiku Kada Fulan 16

III. OBSTÁCLO IHA TERENU **17**

3.1 Obstáclo Servisu Iha Terenu 17

IV. REKOMENDASAUN IHA TERENU **18**

4.1 Rekomendasaun Servisu Iha Terenu 18

INDICE TABELA

Tabela 1 : Postos Administrativos, Sucos no Aldeia 5
Tabela 1.1 : Forca Trabalho ADN, I.P Municipio Viqueque 6
Tabela 1.2 : Lista Asset ADN, I.P Municipio Viqueque 6
Tabela 1.3.1 : Tabela Municipio Viqueque Por Fundus Finansiamento 7
Tabela 1.3.2 : Tabela Municipio Viqueque Por Sectores 9
Tabela 1.3.3 : Tabela Municipio Viqueque Por Ministerio 12
Tabela 1.4 : Dadus populasaun Munisipiu Viqueque 16


I. INTRODUSAUN

1.1 Enkuadramentu Legal

Agência ba Desenvolvimento Nacional ou ADN hari'i baseia ba Decretu Lei No. 11/2011 (Aprovadu hosi Konsellu Ministrus iha 19/2/2011, promulgadu husi Prezidente RDTL iha 16/3/2011, publika iha 23/03/2011). Iha 2020 Dekrtu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ho Misaun ADN nian maka atu asegura katak orsamento estadu nian ne'ebe aloka hodi hala'o projetos (konstrusaun sivil) iha teritorio tomak, hala'o duni ho kualidade ne'ebe diak no tuir espesifikasaun, dezeñu, kustu no análize kustu-benefísiu ne'ebe razoável no viavél. Depois de Dekretu lei ne'e hetan revogasaun husi dekretu lei Nu.60/2020 de 25 de Novembro de 2020 ne'ebe hatur ADN hanesan insituto Púbico (IP), ADN nia knar principal iha 3 mak hanesan:

1. Halo avaliasaun ba mérito no viabilidade husi projeitu Kapital Desenvolvimentu nian.
2. Halo fiskalizasaun no sertifikasaun kualidade ba projetu sira iha programa Kapital Desenvolvimentu nian ho koordensaun ho ministerios relevantes sira.
3. Avalia pedido Pagamento liu husi halo analiza ba dokumento no halo *site visit* ba terreno karik nesesaria.

1.2 Perfil Municipio Viqueque

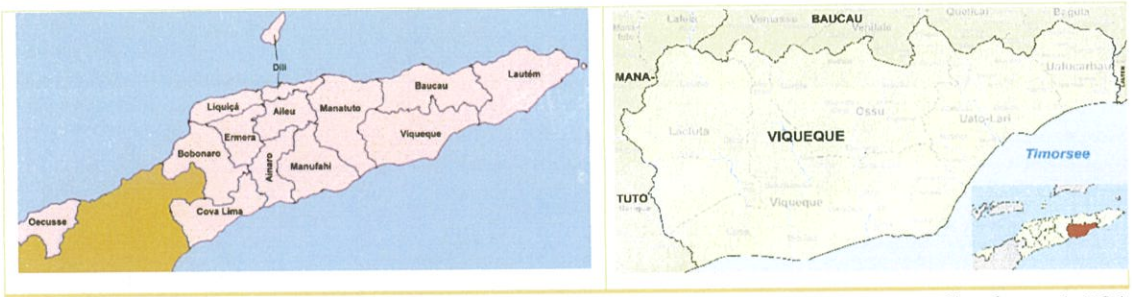

Mapa 2 hatudu pozisaun jeográfika Administrasaun Munisipal Viqueque iha luan 1,781 km² ho populasaun 70,036 tuir Sensus 2010. Administrasaun Munisipal Viqueque iha Postos Administrativos lima (5), Sukus 35 no Aldeias 228,mak hanesan hatudu iha Tabela 1.

Tabela 1 : Postos Administrativos, Sucos no Aldeia

Lacluta		Ossu		Viqueque	
Sukus	**Aldeias**	**Sukus**	**Aldeias**	**Sukus**	**Aldeias**
Ahic	5	Builale	5	Bahalarauain	6
Dilor	5	Liaruca	5	bibileo	8
Laline	5	Loi-Huno	5	Caraubalu	7
Uma tolu	5	Naha Reka	5	Fatudere	3
-	-	Ossu Rua	12	luca	4
-	-	Ossu Decima	8	Maluru	3
-	-	Uabubo	6	Uai Mori	6
-	-	Uaguia	6	Uma Quic	8
-	-	Uaibobo	7	Uma Uain Craic	9
-	-	-	-	Uma Uain Leten	8
Total	**20**	-	**59**	-	**62**

Uato-Carbau		Watulari	
Sukus	**Aldeias**	**Sukus**	**Aldeias**
Afaloicai	4	Babulo	8
Bahatata	4	Macadique	21
Irabin de Baixo	7	Matohoi	12
Irabin de Cima	5	Uaitame	5
Loi Ulo	5	Vesoru	7
Uani Uma	5	Afaloicai	4
-	-	-	
-	-	-	
-	-	-	
-	-	-	
-	**30**	-	**57**

Data husi livro 3B, OJE 2021, Pajina 86

Tabela 1.1 : Forca Trabalho ADN, I.P Municipio Viqueque

Forca de Trabalho ADN,I.P Municipio Viqueque								
No	Deskrisaun	Total Membros Kada Tinan						
		2021	2022	2023	2024	2025	Total	OBS
1	Engineiro	**3**					**3**	
2	Administrasaun no Financas	**0**					**0**	
3	Motorista	**1**					**1**	
4	Seguransa	**0**					**0**	
Total		**4**					**4**	

Tabela 1.2 : Lista Asset ADN, I.P Municipio Viqueque

ASET ADN,IP MUNICIPIO VIQUEQUE								
No	**Deskrisaun**	**Total Aset Kada Tinan**					**Total**	**OBS**
		2021	**2022**	**2023**	**2024**	**2025**		
1	Edificio	1					**1**	
2	Kareta	1					**1**	
3	Desktop HP / Monitor	1					**1**	
4	Laptop HP	1					**1**	
5	Printer Cannon (Color)	1					**1**	Aát
6	UPS	1					**1**	
7	Armario File	2					**2**	
8	Armario Tau hena	3					**3**	
9	Meja escritorio	1					**1**	
10	Meja han	1					**1**	
11	Meja TV (kiik)	1					**1**	
12	Kadeira escritorio	6					**6**	
13	Kadeira han	4					**4**	
14	Sofa	1 Set					**1 Set**	
15	Springbed	3 Set					**3 Set**	
16	Jeleira	1					**1**	
17	Water Dispenser	1					**1**	Aát
18	TV + Parabola	1 Set					**1 Set**	Parabola Aát
19	AC	4					**4**	
20	Kompor	1						La iha
21	Kompor Gas	1					**1**	Aát
22	Rack sepatu	3						La iha
23	Rack Piring	1						La iha
24	Water Pump Sanyo	1						La iha

1.3 Lista Projecto

Projetu hotu neébe akumula iha lista neé bazeia ba dadus projetu neébe sei laó hela no mos projetu neébe abandona ona iha tinan barak nia laran, projetu hirak neé fahe tuir lista tabela 1.3.1 Projetu por Fundus Finansiamento, tabela 1.3.2 Projetu por Sectores no tabela 1.3.3 Projetu por Ministerio, no lista detallu kada projetu bele hare iha #Anexu A.

Tabela 1.3.1 : Tabela Municipio Viqueque Por Fundus Finansiamento

NO	POSTO ADMNISTRATIVO	TOTAL FI+LM-BS+LM-CD+PDIM		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	Lacluta	2	$ 9,781,560.84	74.86%
2	Regional	1	$ 23,853,175.70	24.01%
3	Ossu	13	$ 11,557,374.74	60.02%
4	Uatocarbau	8	$ 10,497,394.45	54.78%
5	Uatolari	17	$ 13,407,650.28	28.92%
6	Viqueque	17	$ 20,446,334.56	44.05%
	Grand Total	**58**	**$ 89,543,490.57**	43.13%

NO POSTO ADMNISTRATIVO		FI		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	Lacluta	2	$ 9,781,560.84	74.86%
2	Regional	1	$ 23,853,175.70	24.01%
3	Ossu	4	$ 9,461,469.53	68.30%
4	Uatocarbau	5	$ 10,124,353.34	54.83%
5	Uatolari	5	$ 11,155,838.98	29.24%
6	Viqueque	8	$ 18,890,123.05	46.64%
	Grand Total	**25**	**$ 83,266,521.44**	44.60%

NO	POSTO ADMNISTRATIVO	LM-BS		
		TOTAL PROJETO	MONTANTE KONTRATO ($)	PERSENTAGEM EXEKUSAUN (%)
1	Lacluta			
2	Regional			
3	Ossu			
4	Uatocarbau			
5	Uatolari	1	$ 145,269.48	0 %
6	Viqueque	2	$ 155,719.93	50.07%
	Grand Total	**3**	**$ 300,989.41**	**25.90%**

NO	POSTO ADMNISTRATIVO	LM + CD		
		TOTAL PROJETO	MONTANTE KONTRATO ($)	PERSENTAGEM EXEKUSAUN (%)
1	Lacluta			
2	Regional			
3	Ossu	5	$ 1,666,711.28	28.51%
4	Uatocarbau			
5	Uatolari	3	$ 1,197,488.93	41.06%
6	Viqueque	1	$ 169,404.00	70.00%
	Grand Total	**9**	**$ 3,033,604.21**	35.78%

NO	POSTO ADMNISTRATIVO	PDIM		
		TOTAL PROJETO	MONTANTE KONTRATO ($)	PERSENTAGEM EXEKUSAUN (%)
1	Lacluta			
2	Regional			
3	Ossu			
4	Uatocarbau	1	$ 197,429.13	90.00%
5	Uatolari	1	$ 158,411.79	78.30%
6	Viqueque			
	Grand Total	**2**	**$ 355,840.92**	84.79%

Dadus detallu kada projetu: #Anexu A

NO	POSTO ADMNISTRATIVO	TP		
		TOTAL PROJETO	MONTANTE KONTRATO ($)	PERSENTAGEM EXEKUSAUN (%)
1	Lacluta			
2	Regional			
3	Ossu	4	$ 429,193.93	0.00%
4	Uatocarbau	2	$ 175,611.98	12.48%
5	Uatolari	7	$ 750,641.10	0.00%
6	Viqueque	5	$ 425,721.17	0.00%
	Grand Total	**18**	**$ 1,781,168.18**	1.23%

Tabela 1.3.2 : **Tabela Municipio Viqueque Por Sectores**

NO	SECTOR PROJETO	TOTAL PROJECTO		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA	3	$ 5,472,502.45	73.86%
2	EDIFICIOS PUBLICOS	25	$ 3,695,589.43	13.27%
3	ELETRIFIKASAUN NASIONAL	4	$ 2,296,509.09	65.49%
4	ESTRADAS	22	$ 52,858,602.47	49.49%
5	IMPRESTIMO	1	$ 23,853,175.70	24.01%
6	MANUTENSAUN NO REHABILITASAUN	2	$ 609,021.05	25.35%
7	PONTES	1	$ 758,090.38	72.01%
	Grand Total	58	$ 89,543,490.57	43.13%

NO	SECTOR PROJETO	LACLUTA		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA			
2	EDIFICIOS PUBLICOS			
3	ELETRIFIKASAUN NASIONAL			
4	ESTRADAS	2	$ 9,781,560.84	74.86%
5	IMPRESTIMO			
6	MANUTENSAUN NO REHABILITASAUN			
7	PONTES			
	Grand Total	2	$ 9,781,560.84	74.86%

NO	SECTOR PROJETO	OSSU		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA			
2	EDIFICIOS PUBLICOS	5	$ 756,426.59	21.66%
3	ELETRIFIKASAUN NASIONAL			
4	ESTRADAS	6	$ 10,191,927.10	64.94%
5	IMPRESTIMO			
6	MANUTENSAUN NO REHABILITASAUN	2	$ 609,021.05	25.35%
7	PONTES			
	Grand Total	13	$ 11,557,374.74	60.02%

NO	SECTOR PROJETO	REGIONAL		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA			
2	EDIFICIOS PUBLICOS			
3	ELETRIFIKASAUN NASIONAL			
4	ESTRADAS			
5	IMPRESTIMO	1	$ 23,853,175.70	24.01%
6	MANUTENSAUN NO REHABILITASAUN			
7	PONTES			

	Grand Total	1	$ 23,853,175.70	24.01%

NO	SECTOR PROJETO	UATUCARBAU		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA	2	$ 5,025,018.02	77.32%
2	EDIFICIOS PUBLICOS	3	$ 373,041.11	53.51%
3	ELETRIFIKASAUN NASIONAL	2	$ 1,147,191.84	81.19%
4	ESTRADAS	1	$ 3,952,143.48	18.58%
5	IMPRESTIMO			
6	MANUTENSAUN NO REHABILITASAUN			
7	PONTES			
	Grand Total	8	$ 10,497,394.45	54.78%

NO	SECTOR PROJETO	UATULARI		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA	1	$ 447,484.43	34.91%
2	EDIFICIOS PUBLICOS	10	$ 1,329,326.87	9.55%
3	ELETRIFIKASAUN NASIONAL	2	$ 1,149,317.25	49.82%
4	ESTRADAS	4	$ 10,481,521.73	28.83%
5	IMPRESTIMO			
6	MANUTENSAUN NO REHABILITASAUN			
7	PONTES			
	Grand Total	17	$ 13,407,650.28	28.92%

NO	SECTOR PROJETO	VIQUEQUE		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	AGRICULTURA			

2	EDIFICIOS PUBLICOS	7	$ 1,236,794.86	0.00%
3	ELETRIFIKASAUN NASIONAL			
4	ESTRADAS	9	$ 18,451,449.32	45.86%
5	IMPRESTIMO			
6	MANUTENSAUN NO REHABILITASAUN			
7	PONTES	1	$ 758,090.38	72.01%
	Grand Total	17	$ 20,446,334.56	44.05%

Dadus detallu kada projetu: #Anexu A

Tabela 1.3.3 : **Tabela Municipio Viqueque Por Ministerio**

NO	DONO DO PROJETO	TOTAL PROJECTO		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL	2	$ 355,840.92	84.79%
2	IGREJA PROTESTANTE TIMOR	1	$ 145,269.48	0.00%
3	MENISTERIO DA EDUCASAUN	18	$ 1,781,168.18	1.23%
4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	1	$ 805,366.41	0.00%
5	MINISTERIO AGRIKULTURA E PESCAS	3	$ 5,472,502.45	73.86%
6	MINISTERIO DAS OBRAS PUBLICAS	30	$ 80,375,398.69	42.41%
7	MINISTERIO DO PLANO e ORDENAMENTO	1	$ 5,707.28	0.00%
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL	1	$ 275,004.50	1.06%
9	MINISTERIO SAUDE	1	$ 327,232.66	50.07%
	Grand Total	58	$ 89,543,490.57	43.13%

NO	DONO DO PROJETO	LACLUTA		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL			
2	IGREJA PROTESTANTE TIMOR			
3	MENISTERIO DA EDUCASAUN			

4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN			
5	MINISTERIO AGRIKULTURA E PESCAS			
6	MINISTERIO DAS OBRAS PUBLICAS	2	$ 9,781,560.84	74.86%
7	MINISTERIO DO PLANO e ORDENAMENTO			
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL			
9	MINISTERIO SAUDE			
	Grand Total	2	$ 9,781,560.84	74.86%

NO	DONO DO PROJETO	OSSU		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL			
2	IGREJA PROTESTANTE TIMOR			
3	MENISTERIO DA EDUCASAUN	4	$ 429,193.93	0.00%
4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN			
5	MINISTERIO AGRIKULTURA E PESCAS			
6	MINISTERIO DAS OBRAS PUBLICAS	8	$ 10,800,948.15	62.71%
7	MINISTERIO DO PLANO e ORDENAMENTO			
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL			
9	MINISTERIO SAUDE	1	$ 327,232.66	
	Grand Total	13	$ 11,557,374.74	60.02%

NO	DONO DO PROJETO	REGIONAL		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL			
2	IGREJA PROTESTANTE TIMOR			
3	MENISTERIO DA EDUCASAUN			
4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN			

5	MINISTERIO AGRIKULTURA E PESCAS			
6	MINISTERIO DAS OBRAS PUBLICAS	1	$ 23,853,175.70	24.01%
7	MINISTERIO DO PLANO e ORDENAMENTO			
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL			
9	MINISTERIO SAUDE			
	Grand Total	1	$ 23,853,175.70	24.01%

NO	DONO DO PROJETO	UATUCARBAU		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL	1	$ 197,429.13	90.00%
2	IGREJA PROTESTANTE TIMOR			
3	MENISTERIO DA EDUCASAUN	2	$ 175,611.98	12.48%
4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN			
5	MINISTERIO AGRIKULTURA E PESCAS	2	$ 5,025,018.02	77.32%
6	MINISTERIO DAS OBRAS PUBLICAS	3	$ 5,099,335.32	32.67%
7	MINISTERIO DO PLANO e ORDENAMENTO			
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL			
9	MINISTERIO SAUDE			
	Grand Total	8	$ 10,497,394.45	54.78%

NO	DONO DO PROJETO	UATULARI		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL	1	$ 158,411.79	78.30%
2	IGREJA PROTESTANTE TIMOR	1	$ 145,269.48	0.00%

3	MENISTERIO DA EDUCASAUN	7	$ 750,641.10	0.00%
4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN			
5	MINISTERIO AGRIKULTURA E PESCAS	1	$ 447,484.43	34.91%
6	MINISTERIO DAS OBRAS PUBLICAS	6	$ 11,630,838.98	30.91%
7	MINISTERIO DO PLANO e ORDENAMENTO			
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL	1	$ 275,004.50	1.06%
9	MINISTERIO SAUDE			
	Grand Total	17	$ 13,407,650.28	28.92%

NO	DONO DO PROJETO	VIQUEQUE		
		TOTAL PROJETO	MONTANTE KONTRATU ($)	PERSENTAGEM EXEKUSAUN (%)
1	ESTATAL			
2	IGREJA PROTESTANTE TIMOR			
3	MENISTERIO DA EDUCASAUN	5	$ 425,721.17	0.00%
4	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	1	$ 805,366.41	0.00%
5	MINISTERIO AGRIKULTURA E PESCAS			
6	MINISTERIO DAS OBRAS PUBLICAS	10	$ 19,209,539.70	46.89%
7	MINISTERIO DO PLANO e ORDENAMENTO	1	$ 5,707.28	0.00%
8	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL			
9	MINISTERIO SAUDE			
	Grand Total	17	$ 20,446,334.56	44.05%

Dadus detallu kada projetu: #Anexu A

Tabela 1.4 : **Dadus populasaun Munisipiu Viqueque**

Administrative Post, Suco and Sex	2021				
	Total	Idade produktivu (idade 15-64)		Ida la produktivu (idade 0-14+65 ba leten)	
		Male	Female	Male	Female
Lacluta	7,098	2,152	1,917	1,528	1,501
Ossu	17,972	4621	4946	4241	4164
Uato-Lari	19,580	4,927	5,199	4,879	4,575
Uatucarbau	7,669	1,842	2,060	1,896	1,871
Viqueque	26,822	7,370	7,549	6,184	5,720

Fontes : Projeksaun Populasaun bazea ba Census Populasaun no Uma Kain 2015
Direcção Geral de Estatistika, MOF

II. PROGRESU FISIKU

2.1 Progresso Fisiku Kada Fulan

Progresu Fisiku kada fulan refere hetan husi progresu servisu ne'ebe kompana sira atinje iha fulan ne'e nia laran, husi lista ne'ebe iha #Anexu B hatudu progresu actual fulan ida ne'e ho nia persentagen servisu, montante actual bazeia ba orsamentu neébe hetan husi progresu fulan ida neé, ikus liu persentagen actual fulan ida neé hatudu progressu fisiku komulativu husi porsentu anterior no fulan ida neé nian, lista kompletu ba detallu bele hareé iha #Anexu B, detallu ba Back-up Fotografia #Anexu C1, detallu ba Back-up BoQ #Anexu C2 no Instrusaun Servisu bele hareé #Anexu D.

3.1 Obstáclo Servisu Iha Terenu

- ❖ Durante Equipa ADN, I.P. Viqueque halo monitorizasaun no Inspeksaun hasoru obstaklo sira iha Terreno mak hanesan tuir mai ne'e :
- ➢ Ekipa ADN, I.P. Viqueque, halo monitorizasasun no inspeksaun indentifika kompanhia balun la kumpri rekomendasaun ne'ebe equipa hato'o, hanesan :
  a) Atu taka dokumentos *Time Schedule* no Dezenho service iha Site office maibe sira nafatin la taka ate a data.
  b) Kompanhia servisu parado no Equipa ADN, I.P. viqueque orienta atu kontinua fali maibe ate a data seidauk kontinua.
  c) Iha kompanhia balu nebe'e laiha *site office* iha terreno.
- ➢ Ba projetu abandona sira ne'ebe abandona durante ne'e (husi tinan 2014 ate a data) no lokaliza iha fatin ne'ebe do'ok tuir orientasaun tenki halo planu ba observa dala rua maibe iha tempu udan defisil atu asesu ba, no maioria gastus tempu barak liu ba projetu ne'ebe abandona
- ➢ Iha projeto sira site supervisor husi ministerio relevente la iha terreno, no kontrator sira dalaruma servisu la tuir espesifikasaun iha kontrato, maibe parte tekniko ADN, I.P. tempo la to'o atu diariamente kontrola iha terreno, hodi nune'e servisu sira ne'ebe iha rai laran ona susar atu indentifika.
- ➢ Ekipa ADN, I.P. Viqueque, la konsege lao tuir plano inspesaun nebe'e planeia ona tamba factor distancia (projecto ida ba projetco seluk), ho nune'e ekipa ADN, I.P. Viqueque halo monitorizasaun ba projeto hirak ne'e mais ou menus loron ida hare projetu ida ou rua deit.

- ❖ Durante Equipa ADN, I.P. Viqueque halo servisu iha Eskritorio ADN, I.P. Municipio hasoru obstaklo sira mak hanesan :
- ➢ Printer la diak, no lebele uza, krik atu print asuntu inportante ruma presiza ba print fali iha fatin seluk, ida nee mos bele fo impakto ba dokumentos konfidensial sira.
- ➢ Internet iha Municipio lao ladun diak hodi nune susar tebes atu asesu manda dokumentos ruma *via email* liu liu *Dropbox.*

ami nia dados sira labele asesu iha nacional tamba *Memory Drop Box Full.*

- Ami nia Edificio / Residencia refere presiza manutensaun tamba iha parte electrical no odatamatan balu la seguro, no ami araska asesu be'e mos.
- Fasilidade la sufisiente apoiu servisu diariamente hanesan laptop, tamba ami tekniku munisipiu Viqueque iha deit laptop ida e nee mos la sufisiente atu halo *back up data* no update ba *folder system.*

❖ **Obstaclo Parte Eletricidade :**

Obtaklu nebe durante Prosesu monitorizasaun Eng. Mekanikal, Elecktrikal & ITC hasoru iha base mak hanesan tuir mai nee:

1. Laptop Laiha atu halo relatorio wainhira iha municipio.
2. Transporte (Kareta/ Motor) la suficiente atu koresponde ba plano nebe Aprovado.
3. Combustivel/Mina (Municipio Baucau, Viqueque, Lautem Pertamina Eto Laiha).
4. Kontractor laiha site ou kontaktu/telepon la tama no contractor la ba iha site/terenu
5. Menus Enginheiro ME.
6. Natureza hanesan Udan boot, Estrada kotu dalan la asesu ba kareta.

IV. REKOMENDASAUN IHA TERENU

4.1 Rekomendasaun Servisu Iha Terenu

1. Rekomenda ba superior ADN, I.P. atu kordena ho ministerio relevantes sira hodi nune'e bele fo penalidade ba komphia sira nebe servisu parado no abandona hela sira nia servico sem informasaun.
2. Rekomenda ba parte Lina Ministerial sira atu foti desizaun ba projeto sira ne'ebe parado no abandona iha terreno.
3. Ministerio relevante sira atu implementa projeto sira tenke iha mos *Site Supervisor*, hodi nune bele kontrola servisu Diariamente iha terreno.
4. Ami Rekomenda ba superior sira atu prepara printer nebe bele print *kertas* A3 no A4 hodi nune'e bele fasilita ami nia servisu iha Municipio.
5. Rekomenda ba Seksaun ITC hare konaba velosidade internet nebe'e mak iha munisipiu ho velosidade nebe'e ki'ik susar atu envia dokumentus ba *dropbox.*

distribui ba Munisipiu sira ho kapasidade nebe'e bo'ot hodi nune'e bele akumula dados hotu iha laran.

7. Husu ba parte Logistica atu tun Direita hodi hare ami nia residensia refere iha municipio, hodi nune'e bele halo manutensaun, tamba ami hato'o ona proposta ba parte Logistika.
8. Rekomenda mos ba seksaun ITC atu aumenta fasilidade Laptop ba iha Munisipiu tamba tekniku nain tolu assesu *dropbox* iha laptop ida deit, hodi nune'e susar atu fahe servisu.

❖ **Recomendação Parte Electricidade :**

1. Rekomenda ba Parte Logistik atu prepara Laptop kada enginheiro (Ba Enginheiro nebe seidauk Hetan)
2. Rekomenda ba Logistik atu Aumenta transporte kareta ba Enginheiro Electricidade
3. Rekomenda ba parte Logistik atu hare problema kombustivel/mina iha parte leste mak hanesan Municipio Baucau, Municipio Lautem no Municipio Viqueque problema iha neba pertamina Eto Laiha nemak dificulta Ami nia plano monitorizasaun karik mina hotu ami tenki fila mai atesta iha municipio Manatuto
4. Rekomenda ba Superior sira atu koordena ho Dono do Projeito (EDTL, EP) oinsa atu kria linha koordenasaun nebe diak
5. Rekomenda ba HR atu Aumenta eng. Electricidade (Recruta tan enginheiro ME)
6. Rekomenda ba Parte Logistik atu prepara ou facilita simcard office nian ba enginheiro.

Note: Assinatura husi Eng Municipio Viqueque

Força de Trabalho ADN, I.P Municipio Viqueque						
No	Deskrisaun	Identidade				
		Naran Kompletu	Nu. ID Card	Pozisaun	Fotografia	Asinatura
1	Engenheiro	Bebiano C. de Jesus Lopes	156	Engenheiro EPAS		
2	Engenheiro	Roberto M. Martins	175	Engenheiro ITI		
3	Engenheiro	Salvador Martins	133	Engenheiro ITI		
4	Engenheiro	Adonis Julio Fernandes	152	Engenheiro METIC		
5	Engenheiro	Joao Paulo Amaral	077	Enginheiro VEBD		

6	**Motorista**	**Bendito M. Bento**	**027**	**Motorista**		

Viseu
Junho 2022

ANEXU C1 (Ossu-11)

Back-up Data

Naran Projeto : **Nova Construcão da Escola Pre Escolar Uaibua**
No. kontratu :

Data Inspesaun : 14-06-2022

Fatin Inspesaun : Ossu Decima,Ossu

Koordinadas :

Start Point : Long : -8.449576" 126.228748

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : Serbisu sinta leten remata hein ba serbisu pasangan kuda2.	

ANEXU C1 (Ossu-11)

Back-up Data

Naran Projeto : **Nova Construcão da Escola Pre Escolar Uaibua**
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu :



 # ANEXU A

Municipio Viqueque (Lista Geral)

					Localizasaun Projeto													
NU.	NARAN PROJ.	DONO PROJETU	KATEGORIA PROJETU	SECTOR	Suco	Posto Administrativo	MUNI.	NARAN COMPANHIA	NUMERU KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. ($)	BAL. ($)	STATUS PROJECT	OBS	
1	Package II Dilor	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dilor	Lacluta	Viqueque	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	$ 4,886,127.61	Aug. 25, 2017	81.48%	64.25%	$ 3,139,406.69	$ 1,746,720.92	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 1.64%
2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Dilor	Lacluta	Viqueque	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	$ 4,895,433.23	May 17, 2016	97.10%	85.45%	$ 4,183,098.19	$ 712,335.04	ABANDONA	Parado	
3	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Ossu	Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	$ 4,849,333.48	Aug. 25, 2017	61.65%	59.28%	$ 2,874,731.17	$ 1,974,602.31	ON-GOING	ON-GOING	
4	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750- Municipal of Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Loi-Huno/Ossoroa	Ossu	Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	$ 183,928.35	Sept. 22, 2016	99.81%	73.61%	$ 135,393.13	$ 48,535.22	ON-GOING	ON-GOING	
5	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Ossu de Cima/Loi-Huno	Ossu	Viqueque	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	$ 425,092.70	Aug. 25, 2020	8.72%	4.47%	$ 18,999.26	$ 406,093.44	ABANDONA	ON-GOING	
6	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loi-Huno	Ossu	Viqueque	Kay Seng Unip. Lda	MPW-W-190084	$ 298,505.70	Aug. 16, 2019	53.01%	38.48%	$ 114,868.58	$ 183,637.12	ON-GOING	ON-GOING	
7	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Nahareca	Ossu	Viqueque	Costa Key Unip Lda	MPW-W-210053	$ 74,854.80	June 10, 2021	23.92%	21.13%	$ 15,817.10	$ 59,037.70	ON-GOING	ON-GOING	
8	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Loi-Huno	Ossu	Viqueque	Manoko Unip. Lda	MPW-W-210050	$ 474,365.56	June 10, 2021	27.92%	20.56%	$ 97,521.76	$ 376,843.80	ON-GOING	ON-GOING	
9	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Ossu	Viqueque	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	$ 4,003,115.00	June 25, 2013	95.28%	85.75%	$ 3,432,678.18	$ 570,436.82	ABANDONA	Parado	
10	R4D Rural Roads Periodic Maintenance Ossu-Nahareka Chainage 4+350-6+350	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS		Ossu	Viqueque	Fin-Los Unip.Lda JV Costa Key Unip. Lda	MPW-W-NCB-R-190037	$ 491,752.56	Aug 16,2019	21.57%	16.91%	$ 83,143.62	$ 408,608.94	Parado	Parado	
11	New Construction of Health Post and Doctor's House Building in Builele,Ossu, Viqueque, Timor Leste	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS		Ossu	Viqueque	Borala Lda	RDTL-MS-DNA-ICB21-075	$ 327,232.66	Aug-25,2021	54.85%	50.07%	$ 163,850.75	$ 163,381.91	ON-GOING	ON-GOING	
12	EBF Uaibobo	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Ossu	Viqueque	Grupo Komunitario		$ 116,970.18		0.00%	0.00%	$ -	$ 116,970.18	ON-GOING	ON-GOING	
13	Pre Escolar Uaibua	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Ossu	Viqueque	Grupo Komunitario		$ 86,739.52		30.00%	0.00%	$ -	$ 86,739.52	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 7.86%
14	ESG Oloaasa	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Ossu	Viqueque	Grupo Komunitario		$ 112,885.23		28.84%	0.00%	$ -	$ 112,885.23	ON-GOING	ON-GOING	
15	Nova Construcao da Escola Basica Filial Liaruca	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Ossu	Viqueque	Grupo Komunitario		$ 112,599.00		0.00%	0.00%	$ -	$ 112,599.00	ON-GOING	ON-GOING	
16	Construction of Dardau Irrigation Scheme Municipality Viqueque	MINISTERIO AGRIKULTURA E PESCAS	FI	AGRICULTURA		Uatocarbau	Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	$ 4,009,902.86	Jan. 18, 2019	84.92%	76.02%	$ 3,048,458.88	$ 961,443.98	ON-GOING	ON-GOING	
17	Consulting Services For Construction Supervision of Dardau Irrigation	MINISTERIO AGRIKULTURA E PESCAS	FI	AGRICULTURA		Uatocarbau	Viqueque	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	$ 1,015,115.16	Dec. 6, 2019	82.46%	82.46%	$ 837,100.99	$ 178,014.17	ON-GOING	ON-GOING	
18	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Uatocarbau	Viqueque	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	$ 591,750.15	Sept. 1, 2016	95.79%	85.91%	$ 508,351.69	$ 83,398.46	ON-GOING	ON-GOING	
19	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Uatocarbau	Viqueque	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	$ 555,441.69	July 6, 2016	98.65%	76.17%	$ 423,062.89	$ 132,378.80	ON-GOING	Progres Fisiko 100%	
20	Konstrusaun Edificio Posto Administrativo Uato-Carbau	ESTATAL	PDIM	EDIFICIOS PUBLICOS		Uatocarbau	Viqueque	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	$ 197,429.13	Aug. 5, 2019	98.56%	90.00%	$ 177,686.22	$ 19,742.91	ON-GOING	PHO	
21	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Loi-Huno	Uatocarbau	Viqueque	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	$ 3,952,143.48	Sept. 15, 2017	24.35%	18.58%	$ 734,308.26	$ 3,217,835.22	ON-GOING	ON-GOING	
22	Konstrusaun ka Rehabilitasaun ba EBC 2,3 Uatocarbau Nunu Uata	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatocarbau	Viqueque	Grupo Komunitario		$ 85,016.63		25.98%	25.78%	$ 21,917.29	$ 63,099.34	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 3.36%
23	ESG Uatocarbau	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatocarbau	Viqueque	Grupo Komunitario		$ 90,595.35		16.35%	0.00%	$ -	$ 90,595.35	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 4.62%
24	New installation of mv,lv line and house connection in Area Lawai Viqueque District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Uma Uain Leten	Uatolari	Viqueque	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	$ 97,892.93	March 25, 2015	63.38%	46.30%	$ 45,324.43	$ 52,568.50	ON-GOING	Parado	
25	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL		Uatolari	Viqueque	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	$ 1,051,424.32	Sept. 1, 2016	72.06%	50.15%	$ 527,283.76	$ 524,140.56	ON-GOING	ON-GOING	
26	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Uatolari	Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	$ 4,045,100.44	Aug. 28, 2017	63.29%	25.65%	$ 1,037,517.23	$ 3,007,583.21	ON-GOING	ON-GOING	
27	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Uatolari	Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	$ 4,322,335.54	Aug. 25, 2017	58.62%	22.80%	$ 985,435.28	$ 3,336,900.26	ON-GOING	ABANDONA	
28	New Construction of Gapura,Stairs and Wall Protection in Garden of Heroes	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL	LM-CD	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Natureza Furak Unip/ Lda	ICB/005/DNAL/MACLN/VIII/2021	$ 275,004.50	Jan. 01, 2021	46.36%	1.06%	$ 2,911.53	$ 272,092.97	ON-GOING	ON-GOING	
29	Konstrusaun Edificio Posto Administrativo Uatolari	ESTATAL	PDIM	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	$ 158,411.79	Aug. 5, 2019	100.00%	78.30%	$ 124,036.43	$ 34,375.36	ON-GOING	ON-GOING	
30	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS		Uatolari	Viqueque	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	$ 475,000.00	March 25, 2020	70.00%	70.00%	$ 332,500.00	$ 142,500.00	ABANDONA	ABANDONA	
31	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Uatolari	Viqueque	Karakuta Unip Lda	MPW-2013/JUNE	$ 1,639,085.75	June 25, 2014	41.68%	40.68%	$ 666,780.08	$ 972,305.67	ON-GOING	ON-GOING	
32	New Construction of Chapel Betesda Naedala Afolicai-Uatolari	IGREJA PROTESTANTE TIMOR	LM-BS	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Be'e Horis Unip. Lda		$ 145,269.48		34.50%	0.00%	$ -	$ 145,269.48	ON-GOING	ON-GOING	
33	Konstrusaun Kanais Irigasaun iha Bebui	MINISTERIO AGRIKULTURA E PESCAS	LM-CD	AGRICULTURA		Uatolari	Viqueque	L.K. Caicasa Metin Unip.Lda	RDTL-MAFFO2021.15965	$ 447,484.43	Oct. 08, 2021	98.52%	34.91%	$ 156,226.47	$ 291,257.96	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 11.13%
34	EBF Nahae	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 114,134.85		15.04%	0.00%	$ -	$ 114,134.85	ON-GOING	ON-GOING	
35	EBF Uaibira	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 103,117.97		0.00%	0.00%	$ -	$ 103,117.97	ON-GOING	ON-GOING	
36	EBC Uatolari	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 70,191.21		13.84%	0.00%	$ -	$ 70,191.21	ON-GOING	ON-GOING	
37	EBF Edemumu	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 98,958.49		0.00%	0.00%	$ -	$ 98,958.49	ON-GOING	ON-GOING	
38	EBF Ualake	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 106,475.42		7.60%	0.00%	$ -	$ 106,475.42	ON-GOING	ON-GOING	
39	ESTV Kaluheda	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 159,590.65		6.83%	0.00%	$ -	$ 159,590.65			
40	EBF Debuisi	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Uatolari	Viqueque	Grupo Komunitario		$ 98,172.51		13.89%	0.00%	$ -	$ 98,172.51	ON-GOING	ON-GOING	
41	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Caraubalo	Viqueque	Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	$ 75,260.55	Dec. 1, 2015	100.00%	88.00%	$ 66,229.28	$ 9,031.27	ON-GOING	Progres Fisiko 100%	
42	Rehabilitation of Urban Road Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS		Viqueque	Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	$ 4,246,801.65	Aug. 25, 2017	99.14%	88.03%	$ 3,738,450.12	$ 508,351.73	ON-GOING	Parado	
43	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Bahalara-Uain	Viqueque	Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	$ 3,666,919.24	Sept. 15, 2017	68.29%	61.46%	$ 2,253,608.32	$ 1,413,310.92	ON-GOING	Progres Fisiko 100%	
44	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES		Viqueque	Viqueque	Arquiris	SSS/105/MOPTC-2017	$ 758,090.38	Sept. 7, 2017	100.00%	72.01%	$ 545,900.59	$ 212,189.79	ON-GOING	Parado	
45	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	MINISTERIO DAS OBRAS PUBLICAS	LM-BS	ESTRADAS	Luca	Viqueque	Viqueque	Dira Nova Unip. Lda	MPW - W - 190114	$ 150,012.65	March 9, 2019	75.00%	51.97%	$ 77,967.95	$ 72,044.70	ON-GOING	ABANDONA	
46	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package: 12 Luca - Lacluta	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Luca	Viqueque	Viqueque	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	$ 169,404.00	March 25, 2020	70.00%	70.00%	$ 118,582.80	$ 50,821.20	ABANDONA	ON-GOING	
47	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uai-Mori	Viqueque	Viqueque	Uma Liurai unip, lda	SSS/138/MOPTC-2016	$ 3,664,122.77	Aug. 1, 2016	27.42%	24.12%	$ 883,922.53	$ 2,780,200.24	ABANDONA	Parado	

NU.	NARAN PROJ.	DONO PROJETU	KATEGORIA PROJETU	SECTOR	Suco	Posto Administrativo	MUNI.	NARAN COMPANHIA	NUMERU KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	PROG. FISIKU (%)	PROG. PAGA. (%)	PAGA. ($)	BAL. ($)	STATUS PROJECT	OBS	
48	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uai-mori	Viqueque	Viqueque	Bihalutur Unip, lda	SSS/141/MOPTC-2016	$ 2,073,894.13	Aug. 1, 2016	10.33%	9.09%	$ 188,464.84	$ 1,885,429.29	ON-GOING	ON-GOING	
49	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section : Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uai-mori	Viqueque	Viqueque	Loke Matan unip, lda	SSS/307/MOPTC-2016	$ 2,455,115.74	May 12, 2016	30.76%	22.03%	$ 540,920.78	$ 1,914,194.96	ON-GOING	ON-GOING	
50	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uai-mori	Viqueque	Viqueque	Caburela unip,lda	SSS/306/MOPTC-2016	$ 1,949,918.39	Nov. 22, 2016	48.92%	30.42%	$ 593,217.81	$ 1,356,700.58	ON-GOING	ON-GOING	
51	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO		Multi Posto Administrativo	Regional	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	$ 23,853,175.70	March 21, 2019	24.20%	24.01%	$ 5,727,619.26	$ 18,125,556.44	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 12.58%
52	Servisu Manutensaun Edifício Agencia de Desenvolvimento Nacional, I.P. Municipio Viqueque	MINISTERIO DO PLANO e ORDENAMENTO	LM-BS	EDIFICIOS PUBLICOS		Viqueque	Viqueque	Luminar Unip. Lda	22/RDTL/MPO/AND.I.P/XI/2021	$ 5,707.28		100.00%	0.00%	$ -	$ 5,707.28	ON-GOING	Progres Fisiko 100%	
53	ESG Calixa	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Viqueque	Viqueque	Grupo Komunitario		$ 113,359.66		17.86%	0.00%	$ -	$ 113,359.66	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 7.00%
54	EBF Ular Rihik	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Viqueque	Viqueque	Grupo Komunitario		$ 70,633.26		16.27%	0.00%	$ -	$ 70,633.26	ON-GOING	ON-GOING	
55	Pre Escolar Maria Lobato Raithu	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Viqueque	Viqueque	Grupo Komunitario		$ 99,496.02		25.62%	0.00%	$ -	$ 99,496.02	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 5.74%
56	EBC Caibirsoan	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Viqueque	Viqueque	Grupo Komunitario		$ 52,836.14		53.87%	0.00%	$ -	$ 52,836.14	ON-GOING	ON-GOING	
57	Pre Escolar Sebastiao Gomes Uai Mori Tula	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS		Viqueque	Viqueque	Grupo Komunitario		$ 89,396.09		13.64%	0.00%	$ -	$ 89,396.09	ON-GOING	ON-GOING	
58	New Construction Office, Were House And Landscaping Of Viqueque Distric	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	LM	EDIFICIOS PUBLICOS		Viqueque	Viqueque	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	$ 805,366.41		4.41%	0.00%	$ -	$ 805,366.41	ON-GOING	ON-GOING	Progresso iha Fulan Junho Aumenta 4.41%
										$ 89,543,490.57			**43.13%**	**$ 38,623,294.12**	**$ 50,920,196.45**			

Inspecsaun Husi,

(Eng. Roberto M. Martins)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

(Eng. Salvador Martins)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

(Eng. Beliano C. de Jesus Lopes)
Eng. ba Projeto Edifício Publico no Beé Saneamento ADN, I.P

(Eng. Adonis Julio Fernandes)
Eng. ba Projeto Mecanical Electrical, ADN, I.P

Verifika Husi,

(Eng. Renigio da C.S dos Santos)
Eng. Senior ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

(Arch. Francisco Xavier de Deus Jeronimo)
Eng. Senior ba Projeto Edifício Publiku No Beé Saneamento ADN, I.P

(Eng. Deolindo de Fatima Marques)
Chefe Seksaun Mecanical Electrical, Informasaun Tecnologia no Komunikasaun ADN, I.P

Cedrtifika Husi

(Eng. Emerenciana da Costa Maia Freitas)
Cooedenadora da Unidade de Controla e Validasaun de Qualidade, ADN, I.P.

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU VIQUEQUE

					Localizasaun Projeto						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERU KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	Progress This Month	Progress Komulative
1	Package II Dilor	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lacluta	Viqueque	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	$ 4,886,127.61	Aug. 25, 2017	79.84%	1.64%	81.48%
2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Lacluta	Viqueque	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	$ 4,895,433.23	May 17, 2016	97.10%		97.10%
3	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Ossu	Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	$ 4,849,333.48	Aug. 25, 2017	61.63%		61.63%
4	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750- Municipal of Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Ossu	Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	$ 183,928.35	Sept. 22, 2016	99.81%		99.81%
5	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	MANUTENSAUN NO REHABILITASAUN	Ossu	Viqueque	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	$ 425,092.70	Aug. 25, 2020	8.72%		8.72%
6	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Ossu	Viqueque	Kay Seng Unip. Lda	MPW-W-190084	$ 298,505.70	Aug. 16, 2019	53.01%		53.01%
7	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Ossu	Viqueque	Costa Key Unip Lda	MPW-W-210053	$ 74,854.80	June 10, 2021	23.92%		23.92%
8	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Ossu	Viqueque	Manoko Unip. Lda	MPW-W-210050	$ 474,365.56	June 10, 2021	27.92%		27.92%
9	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Ossu	Viqueque	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	$ 4,003,115.00	June 25, 2013	95.28%		95.28%
10	R4D Rural Roads Periodic Maintenance Ossu-Nahareka Chainage 4+350-6+350	MINISTERIO DAS OBRAS PUBLICAS	LM-CD	ESTRADAS	Ossu	Viqueque	Fin-Los Unip.Lda JV Costa Key Unip. Lda	MPW-W-NCB-R-190037	$ 491,752.56	Aug 16,2019	21.57%		21.57%
11	New Construction of Health post and Doctor's House Building in Builale, Ossu, Viqueque Timor Leste	MINISTERIO SAUDE	LM-CD	EDIFICIOS PUBLICOS	Ossu	Viqueque	Borala Unip. Lda	RDTL-MS-DNA-ICB21-075	$ 327,232.66	Aug-25,2021	54.85%		54.85%
12	EBF Uaibobo	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Ossu	Viqueque	Grupo Komunitario		$ 116,970.18		0.00%		0.00%
13	Pre Escolar Uaibua	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Ossu	Viqueque	Grupo Komunitario		$ 86,739.52		22.14%	7.86%	30.00%
14	ESG Oloaasa	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Ossu	Viqueque	Grupo Komunitario		$ 87,453.73		28.84%		28.84%
15	Nova Construcao da Escola Basica Filial Liaruca	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Ossu	Viqueque	Grupo Komunitario		$ 112,599.00		0.00%		0.00%
16	Construction of Dardau Irrigation Scheme Municipality Viqueque	MINISTERIO AGRIKULTURA E PESCAS	FI	AGRICULTURA	Uatocarbau	Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	$ 3,912,226.56	Jan. 18, 2019	84.92%		84.92%
17	Consulting Services For Construction Supervision of Dardau Irrigation	MINISTERIO AGRIKULTURA E PESCAS	FI	AGRICULTURA	Uatocarbau	Viqueque	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	$ 1,015,115.16	Dec. 6, 2019	82.46%		82.46%
18	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Uatocarbau	Viqueque	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN , 00000441	$ 591,750.15	Sept. 1, 2016	95.79%		95.79%
19	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Uatocarbau	Viqueque	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN , 00000346	$ 555,441.69	July 6, 2016	98.65%		98.65%
20	Konstrusaun Edificio Posto Administrativo Uato-Carbau	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Uatocarbau	Viqueque	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	$ 197,429.13	Aug. 5, 2019	98.56%		98.56%
21	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uatucarbau	Viqueque	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	$ 3,952,143.48	Sept. 15, 2017	24.35%		24.35%
22	EBC 2.3 Uatocarbau	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatocarbau	Viqueque	Grupo Komunitario		$ 85,016.63		22.62%	3.36%	25.98%
23	ESG Uatocarbau	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatocarbau	Viqueque	Grupo Komunitario		$ 90,595.35		11.73%	4.62%	16.35%
24	New installation of mv,lv line and house connection in Area Lawai Viqueque District	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Uatolari	Viqueque	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN.0000459	$ 97,892.93	March 25, 2015	63.38%		63.38%
25	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ELETRIFIKASAUN NASIONAL	Uatolari	Viqueque	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN , 00000433	$ 1,051,424.32	Sept. 1, 2016	72.06%		72.06%
26	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uatolari	Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	$ 4,045,100.44	Aug. 28, 2017	63.29%		63.29%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU VIQUEQUE

					Localizasaun Projeto						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERU KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	Progress This Month	Progress Komulative
27	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uatolari	Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	$ 4,322,335.54	Aug. 25, 2017	58.62%		58.62%
28	New construction of Gapura Stairs and wall protection no jardim de herois de Viqueque	MINISTERIO PARA OS ASSUNTOS DOS COMBANTENTES DA LIBERTACAO NACIOANL	LM-CD	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Natureza Furak Unip/ Lda	ICB/005/DNAL/MACLN/VIII/2021	$ 275,004.50	Aug. 31, 2016	46.36%		46.36%
29	Konstrusaun Edificio Posto Administrativo Uatolari	ESTATAL	PDIM	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	$ 158,411.79	Aug. 5, 2019	100.00%		100.00%
30	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Uatolari	Viqueque	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	$ 475,000.00	March 25, 2020	70.00%		70.00%
31	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Uatolari	Viqueque	Karakuta Unip Lda	MPW-2013/JUNE	$ 1,639,085.75	June 25, 2014	41.68%		41.68%
32	New Construction of Capela	IGREJA PROTESTANTE TIMOR	LM	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Be'e Horis Unip. Lda		$ 145,269.48		34.50%		34.50%
33	Konstrusaun Kanais Irrigasaun iha Bebui Municipio Viqueque	MINISTERIO DA AGRIKULTURA	LM-CD	IRIGASAUN	Uatolari	Viqueque	L.K. Caicasa Metin Unip.Lda	RDTL-MAPPO2021.15965	$ 447,484.43	Oct. 08, 2021	87.39%	11.13%	98.52%
34	EBF Nahae	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 114,134.85		15.04%		15.04%
35	EBF Uaibira	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 103,117.97		0.00%		0.00%
36	EBC Uatolari	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 70,191.21		13.84%		13.84%
37	EBF Edemumu	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 98,958.49		0.00%		0.00%
38	EBF Ualake	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 106,475.42		7.60%		7.60%
39	ESTV Kaluheda	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 159,590.65		6.83%		6.83%
40	EBF Debuisi	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Uatolari	Viqueque	Grupo Komunitario		$ 98,172.51		13.89%		13.89%
41	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	$ 75,260.55	Dec. 1, 2015	100.00%		100.00%
42	Rehabilitation of Urban Road Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	$ 4,246,801.85	Aug. 25, 2017	99.14%		99.14%
43	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	$ 3,666,919.24	Sept. 15, 2017	68.29%		68.29%
44	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	MINISTERIO DAS OBRAS PUBLICAS	FI	PONTES	Vlqueque	Viqueque	Arquiris Unip. Lda	SSS/105/MOPTC-2017	$ 758,090.38	Sept. 7, 2017	100.00%		100.00%
45	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Viqueque	Viqueque	Dira Nova Unip. Lda	MPW - W - 190114	$ 150,012.65	March 9, 2019	75.00%		75.00%

ANEXO B

PROGRESSU FISIKU KADA FULAN MUNISIPIU VIQUEQUE

					Localizasaun Projeto						Jun-22		
NU.	NARAN PROJETU	DONO PROJETU	KATEGORIA PROJETU	SECTOR	POSTO ADMINISTRATIVO	MUNISIPIU	NARAN COMPANHIA	NUMERU KONTRATU	MONTANTE KONTRATU ($)	DATA KONTRATU	Previous Progress	Progress This Month	Progress Komulative
46	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package, 12 Luca - Laclúta	MINISTERIO DAS OBRAS PUBLICAS	LM	ESTRADAS	Viqueque	Viqueque	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	$ 169,404.00	March 25, 2020	70.00%		70.00%
47	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Uma Liurai unip, lda	SSS/138/MOPTC-2016	$ 3,664,122.77	Aug. 1, 2016	27.42%		27.42%
48	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Bihalutur Unip, lda	SSS/141/MOPTC-2016	$ 2,073,894.13	Aug. 1, 2016	10.33%		10.33%
49	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section , Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Loke Matan unip, lda	SSS/307/MOPTC-2016	$ 2,455,115.74	May 12, 2016	30.76%		30.76%
50	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	MINISTERIO DAS OBRAS PUBLICAS	FI	ESTRADAS	Viqueque	Viqueque	Caburela unip,lda	SSS/306/MOPTC-2016	$ 1,949,918.39	Nov. 22, 2016	48.92%		48.92%
51	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2, Venilale - Viqueque , Sta. 27 + 120 to Sta. 62 + 010	MINISTERIO DAS OBRAS PUBLICAS	FI	IMPRESTIMO	Multi Posto Administrativo	Regional	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	$ 23,853,175.70	March 21, 2019	21.62%	2.58%	24.20%
52	Servisu Manutensaun Edificio Agencia de Desenvolvimento Nacional, I.P. Municipio Viqueque	MINISTERIO DO PLANO e ORDENAMENTO	LM	EDIFICIOS PUBLICOS	Viqueque	Viqueque	Luminar Unip. Lda	22/RDTL/MPO/AND.I.P/XI/2021	$ 5,707.28		100.00%		100.00%
53	ESG Calixa	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Viqueque	Viqueque	Grupo Komunitario		$ 113,359.66		10.86%	7.00%	17.86%
54	EBF Ular Rihik	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Viqueque	Viqueque	Grupo Komunitario		$ 70,633.26		16.27%		16.27%
55	Pre Escolar Maria Lobato Raithu	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Viqueque	Viqueque	Grupo Komunitario		$ 99,496.02		19.88%	5.74%	25.62%
56	EBC Caibiraoan	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Viqueque	Viqueque	Grupo Komunitario		$ 52,836.14		53.87%		53.87%
57	Pre Escolar Sebastiao Gomes Uai Mori Tula	MENISTERIO DA EDUCASAUN	TP	EDIFICIOS PUBLICOS	Viqueque	Viqueque	Grupo Komunitario		$ 89,396.09		13.64%		13.64%
58	New Construction Office, Were House And Landscaping Of Viqueque Distric	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	LM	EDIFICIOS PUBLICOS	Viqueque	Viqueque	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	$ 805,366.41		0.00%	4.41%	4.41%

Inspesaun Husi :

(Eng. Roberto M. Martins)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

(Eng. Salvador Martins)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

(Eng. Bebiano C. de Jesus Lopes)
Eng. ba Projeto Edificio Publico no Beé Saneamento ADN, I.P

(Eng. Adonis Julio Fernandes)
Eng. ba Projeto Mecanical Electrical, ADN, I.P

Verifika Husi :

(Eng. Remigio da C.S dos Santos)
Eng. Senior ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

(Arch. Francisco Xavier de Deus Jeronimo)
Eng. Senior ba Projeto Edificio Publiku No Beé Saneamento ADN, I.P

(Eng. Deolindo de Fatima Marques)
Chefe Seksaun Mecanical Electrical, Informasaun Tecnologia no Komunikasaun ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Fre
Cooedenadora da Unidade de Controla e Validasaun d

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projetu : Nova Construção da Escola Pre Escolar Uaibua no code emis 1694
Lokalidade : Lugabuti, Ossu de Cima, Ossu, Viqueque
Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY

	MAIN SUMMARY	Page No	Amount		Previous		This Billing		Up to Date	
					Amount $	Percent %	Amount $	Percent %	Amount $	Percent %
I	PRELIMINARIES WORKS	PP/3	US$	3.579,26	1.789,63	2,06%	$ -	0,00%	1.789,63	2,06%
II	CLASSROOM BUILDING	C/39 (i)	US$	62.959,35	17.412,18	20,07%	$ 2.805,56	3,23%	20.217,74	23,31%
III	PROFESSIONAL SUM for SITEWORKS	SW/24 (i)	US$	10.860,91	-	0,00%	$ 2.437,72	2,81%	2.437,72	2,81%
	CONSTRUCTION COST		**US$**	**77.399,52**	19.201,81	22,14%	**$ 5.243,28**	**6,04%**	**24.445,09**	**28,18%**
	CONTIGENCY		US$	3.000,00	-	0,00%	$ -	0,00%	-	0,00%
	OVERHEAD		US$	6.340,00	-	0,00%	$ 1.572,50	1,81%	1.572,50	1,81%
	GRAND TOTAL		**US$**	**86.739,52**	**19.201,81**	**22,14%**	**$ 6.815,78**	**7,86%**	**26.017,59**	**30,00%**

Prepared By

Eng. Bebiano Crecêncio De Jesus Lopes
Eng. Municipio Viqueque

Cheked By

Arch. Francisco Xavier de Deus Jeronimo
Engineiro Senior ba Projeitu Edifício Publiku No Bee Saneamento

Aproved By

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade

ANEXU C1 (Ossu-12)

Back-up Data

Naran Projeto : **Nova Construção da Escola secundaria geral olocassa**
No. kontratu :

Data Inspesaun : 14-06-2022

Fatin Inspesaun : Ossu Decima,Ossu


Koordinadas :

Start Point : Long : -8.525418" 126.2155866

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

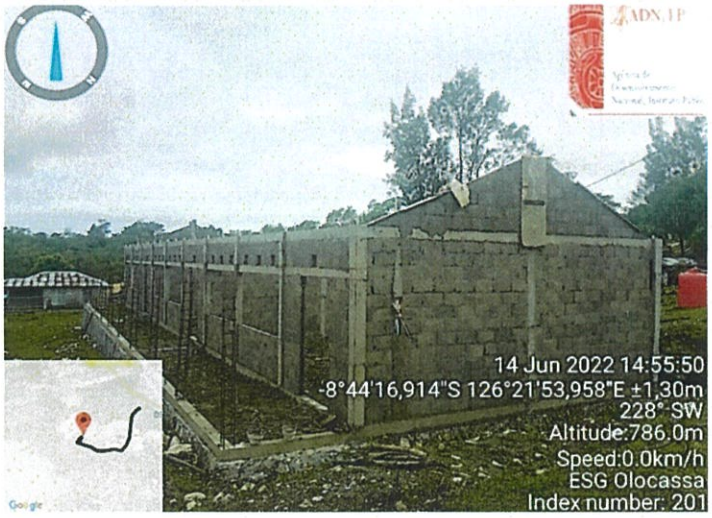
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu :	
Serbisu sinta leten remata hein ba serbisu pasangan kuda2	

ANEXU C1 (Ossu-12)

Back-up Data

Naran Projeto : **Nova Construção da Escola secundaria geral olocassa**
No. kontratu :

Serbisu pasangan batako ba toilet remata

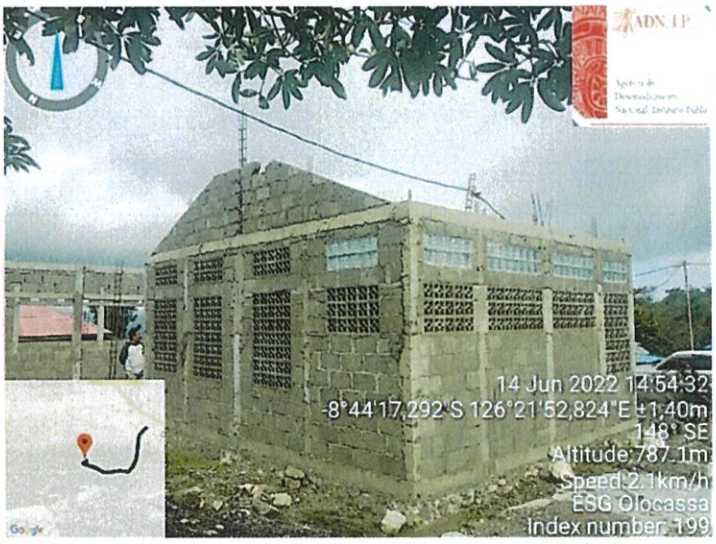

ANEXU D (Ossu-12)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Nova Construção da Escola secundaria geral olocassa

Kompanha : PKRIE,PROJECTO KOMUNITARIO

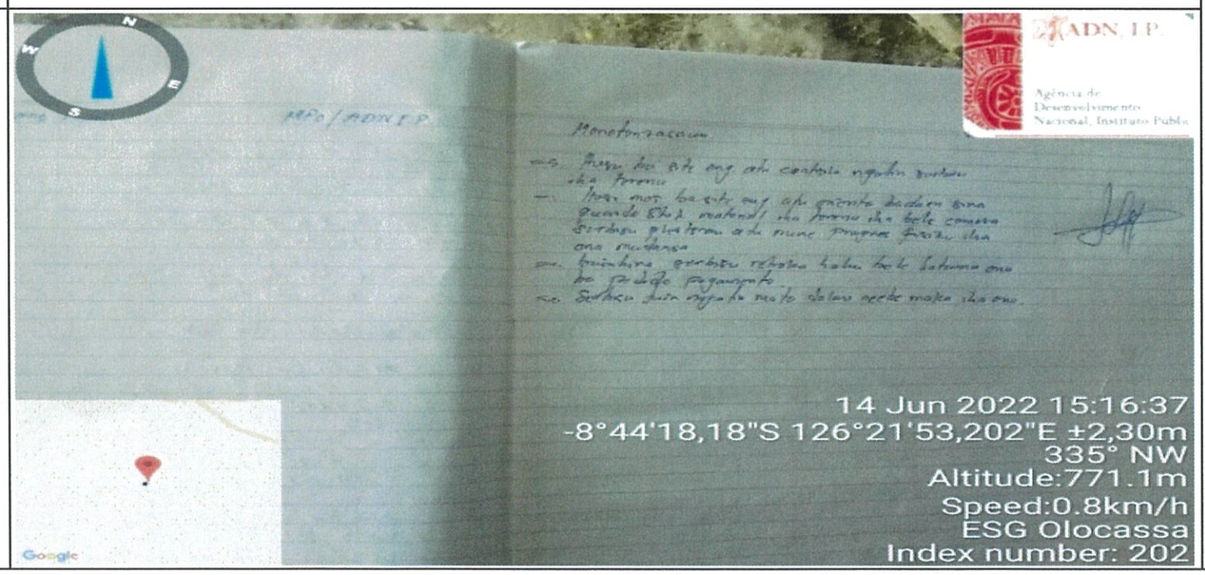No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	14/06/2022	Ossu	Bebiano C. de Jesus Lopes	Tekniko	1	Husu ba site eng. Atu controla nafatin serbisu iha terenu	
					2	Husu mos ba site eng. Atu orienta badaen sira quando stok material iha terenu sei iha bele comesa serbisu ba plesteran atu nune progress fisiku iha terenu bele aumenta	
					3	bainhira serbisu plesteran hahu bele submete ona pedido pagamento	
					4		
							

ANEXU C1 (UatC- 5)

Back-up Data

Naran Projeto : **Konstrusaun Edificio Posto Administrativo Uato-Carbau**
No. kontratu : **675/004/PDIM/KDM-VQQ/VIII/2019**

Data Inspesaun : 15-06-2022

Fatin Inspesaun : Suco Irabin Decima,Uatocarbau,Viqueque

Koordinadas :

Start Point : Long : -8.45097156 , Latetude : 126.415350248


End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Eng. Bebiano Crecencio de Jesus Lopes

2. .....

3. .....

4. .....

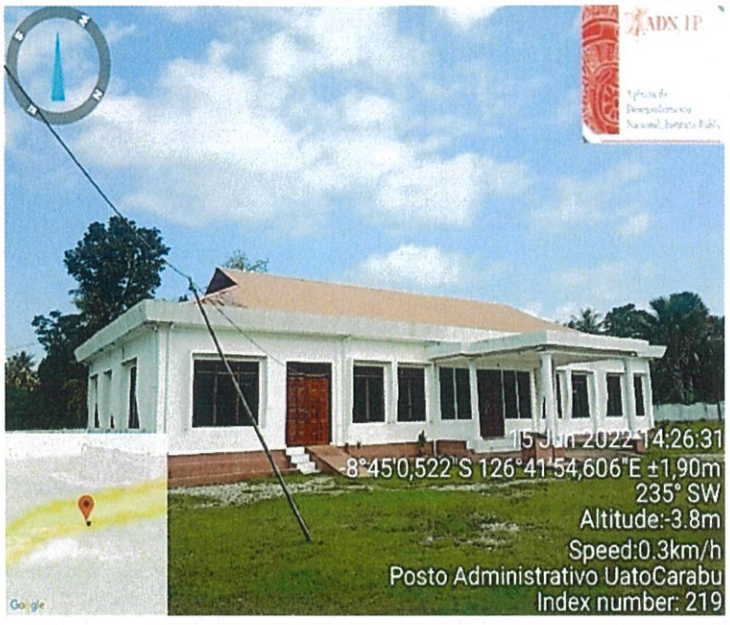Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ..... ➢ Projeto refere nia fisiku atinji ona 100% no pagamento atinji ona 100% falta FHO	

ANEXU C1 (Uatocarbau-8)

Back-up Data

Naran Projeto : **Nova Construção da Escola Ensino Secundario Geral Uatucarbau**
No. kontratu :

Data Inspesaun : 15-06-2022

Fatin Inspesaun : Irabin de Bixo, Posto Administrativo Uato Carbau

Koordinadas :

Start Point : Long : -8.4458932" 126.421584

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : Serbisu pasangan batako	

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projetu : Nova Construção da Escola ESG Uatucarbau
Lokalidade : Irabin de Bixo, Posto Administrativo Uato Carbau, Municipio Viqueque
Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY

	MAIN SUMMARY	Page No	Amount		Previous		This Billing		Up to Date	
					Amount	%	Amount	%	Amount	%
I	PRELIMINARIES WORKS	PP/3	US$	4,279.26	$ 1,729.26	1.91%	$ -	0.00%	$ 1,729.26	1.91%
II	CLASSROOM BUILDING Ca	C/39 (i)	US$	73,342.16	$ 8,357.50	9.23%	$ 4,183.31	4.62%	$ 12,540.81	13.84%
III	PROFESSIONAL SUM for SITEWORKS	SW/24 (i)	US$	3,633.93	$ -	0.00%	$ -	0.00%	$ -	0.00%
	CONSTRUCTION COST		**US$**	**81,255.35**	**$ 10,086.76**	**11.13%**	**$ 4,183.31**	**4.62%**	**$ 14,270.07**	**15.75%**
	CONTIGENCY		US$	3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
	OVERHEAD		US$	6,340.00	$ 540.00	0.60%	$ -	0.00%	$ 540.00	0.60%
	GRAND TOTAL		**US$**	**90,595.35**	**$ 10,626.76**	**11.73%**	**$ 4,183.31**	**4.62%**	**$ 14,810.07**	**16.35%**

Prepared By

Eng. Bebiano Crecencio De Jesus Lopes
Eng. Municipio Viqueque ADN, I.P.

Cheked By

Arch. Francisco Xavier de Deus Jeronimo
Engineiro Senior ba Projeitu Edifício Publiku No Bee Saneamento ADN, I.P.

Aproved By

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

ANEXU D (Uatocarbau-8)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Nova Construção da Escola Ensino Secundario Geral Uatucarbau

Kompanha : PKRIE,PROJECTO KOMUNITARIO

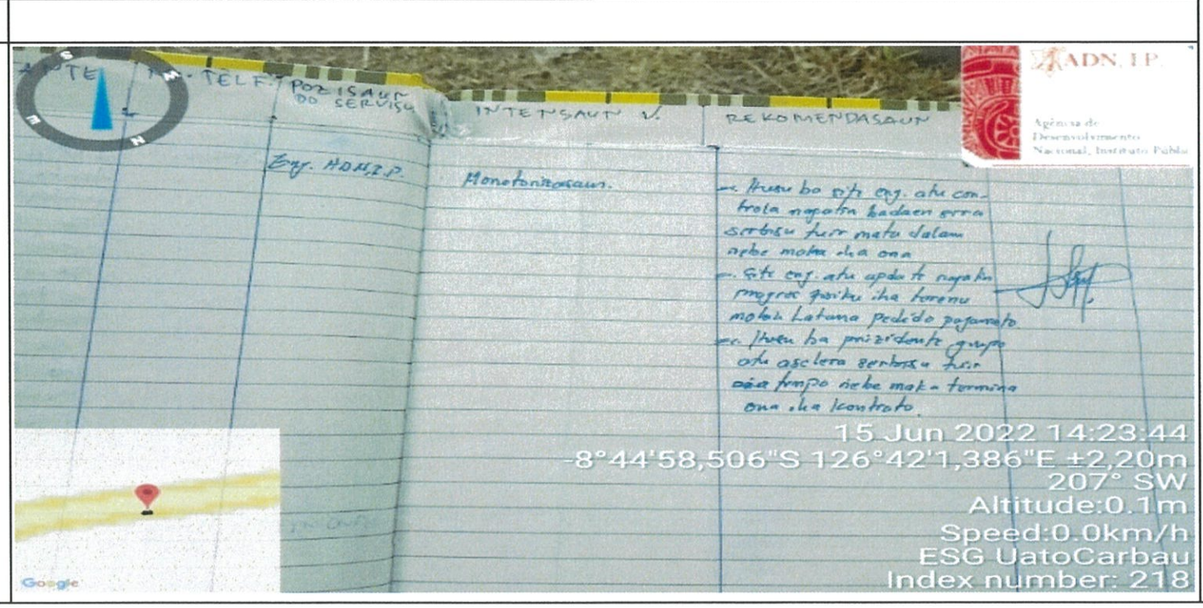No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	15/06/2022	Uatocarbau	Bebiano C. de Jesus Lopes	Tekniko	1	Husu ba site eng.atu controla nafatin badaen sira iha terenu	
					2	site eng.update nafatin progress fisiku iha terenu molok submete pedido pagamento	
					3	Husu ba prezidente grupo atu aselera serbisu iha terenu tuir tempo neebe maka termina ona iha kontrato	
					4		
							

ANEXU C1 (Uatocarbau-7)

Back-up Data

Naran Projeto : **Nova Construção da Escola basica central uatocarbao**
No. kontratu :

Data Inspesaun : 15-06-2022

Fatin Inspesaun : Irabin Literia,Uatocarbau


Koordinadas :

Start Point : Long : -8.452418" 126.4144874

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

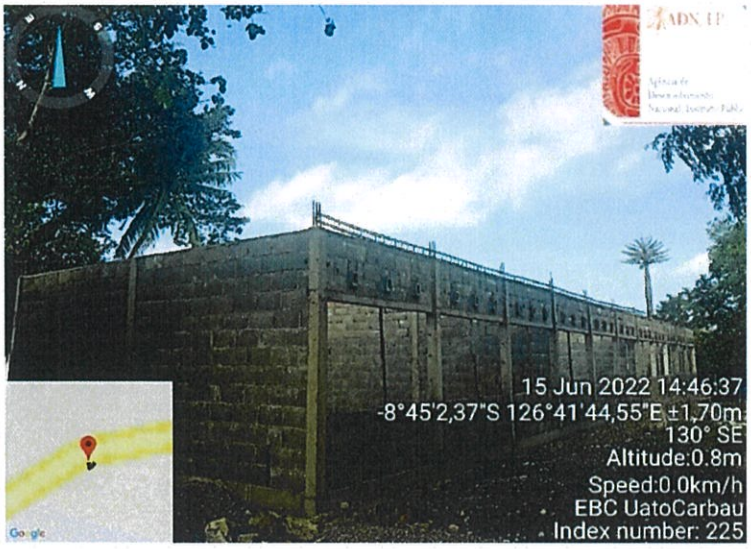Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : Serbisu hada batako keliling bangunan remata	

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projetu : Nova Construção da Escola basica central uatocarbao no code emis 5319
Lokalidade : Matadalan,, Irabin de Bixo,UatoCarbau, viqueque.
Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY

	MAIN SUMMARY	Page No	Amount	Previous		This Billing		Up to Date	
				Amount $	Percent %	Amount $	Percent %	Amount $	Percent %
I	PRELIMINARIES WORKS	PP/3	US$ 3,879.26	$ 1,289.26	1.52%	$ -	0.00%	$ 1,289.26	1.52%
II	CLASSROOM BUILDING Ca	C/39 (i)	US$ 66,202.64	$ 17,404.16	20.47%	$ -	0.00%	$ 17,404.16	20.47%
IV	PROVISIONAL SUM for SITEWORKS	SW/24 (i)	US$ 5,594.73	$ -	0.00%	$ 2,857.02	3.36%	$ 2,857.02	3.36%
	CONSTRUCTION COST		**US$ 75,676.63**	**$ 18,693.42**	**21.99%**	**$ 2,857.02**	**3.36%**	**$ 21,550.44**	**25.35%**
	CONTIGENCY		US$ 3,000.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
	OVERHEAD		US$ 6,340.00	$ 540.00	0.64%	$ -	0.00%	$ 540.00	0.64%
	GRAND TOTAL		**US$ 85,016.63**	**$ 19,233.42**	**22.62%**	**$ 2,857.02**	**3.36%**	**$ 22,090.44**	**25.98%**

Prepared By

Eng. Bebiano Crecencio De Jesus Lopes
Eng. Municipio Viqueque ADN,I.P.

Cheked By

Arch. Francisco Xavier de Deus Jeronimo
Engineiro Senior ba Projeitu Edificio Publiku No Bee Saneamento ADN,I.P.

Aproved By

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN,I.P.

ANEXU D (Uatocarbau-7)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Nova Construção da Escola basica central uatocarbau

Kompanha : PKRIE,PROJECTO KOMUNITARIO

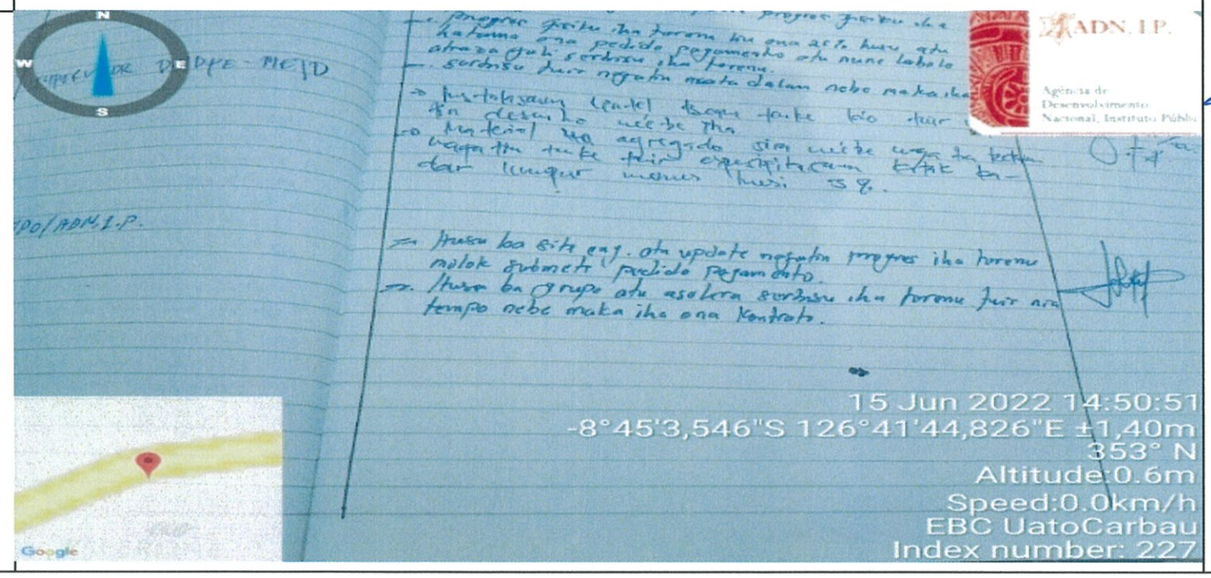No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	15/6/2022	Uatocarbau	Bebiano C. de Jesus Lopes	Tekniko	1	Husu ba site eng. atu update nafatin progress fisiku iha terenu,molok submete pedido pagamento	
					2	Husu ba grupo atu aselera serbisu tuir nia tempo iha kontrato	
					3		
					4		
							

ANEXU C1 (UatL- 6)

Back-up Data

Naran Projeto : **Konstrusaun Edificio Posto Administrativo Uatolari**
No. kontratu : **665/004/PDIM/KDM-VQQ/VIII/2019**

Data Inspesaun : 15-06-2022

Fatin Inspesaun : **Suco Matahoi,Uatolari,Viqueque**

Koordinadas :

Start Point : Long : -8.491503 , Latetude : 126.3155386

End Point : Long : ....., Latetude : .....

Naran Inspector : 1. Eng. Bebiano Crecencio de Jesus Lopes

2. .....

3. .....

4. .....

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu .....

- Projeto refere nia fisiku atinji ona 100% maibe pagamento atinji deit 97.23 % tanba iha mudansa item iha terenu. Falta deit FHO



ANEXU C1 (Viqueque-12)

Back-up Data

Naran Projeto : **Nova Construcao Escola Secundario Geral Calixa**
No. kontratu :

Data Inspesaun : 30-06-2022

Fatin Inspesaun : Caraubalu,viqueque vila


Koordinadas :

Start Point : Long : -8.5243842" 126.2234492

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

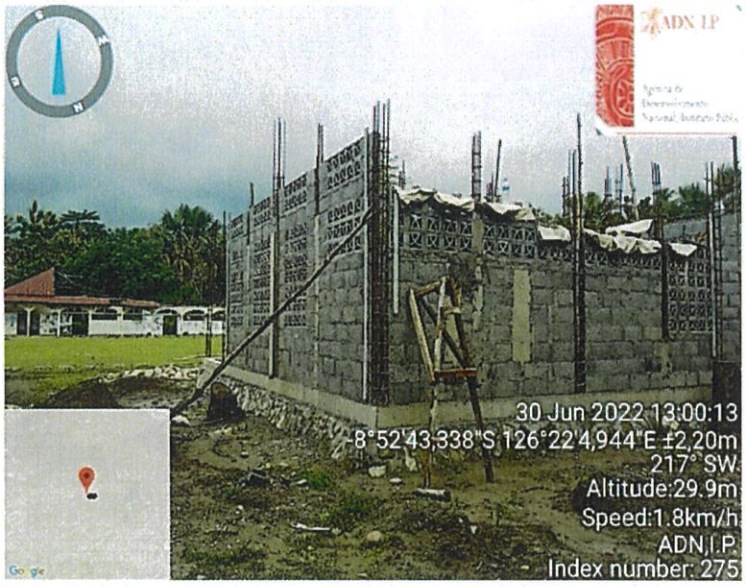Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu :	
Serbisu pemasgan batako seidauk remata	


ANEXU C1 (Viqueque-12)

Back-up Data

Naran Projeto : **Nova Construcao Escola Secundario Geral Calixa**
No. kontratu :

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu :

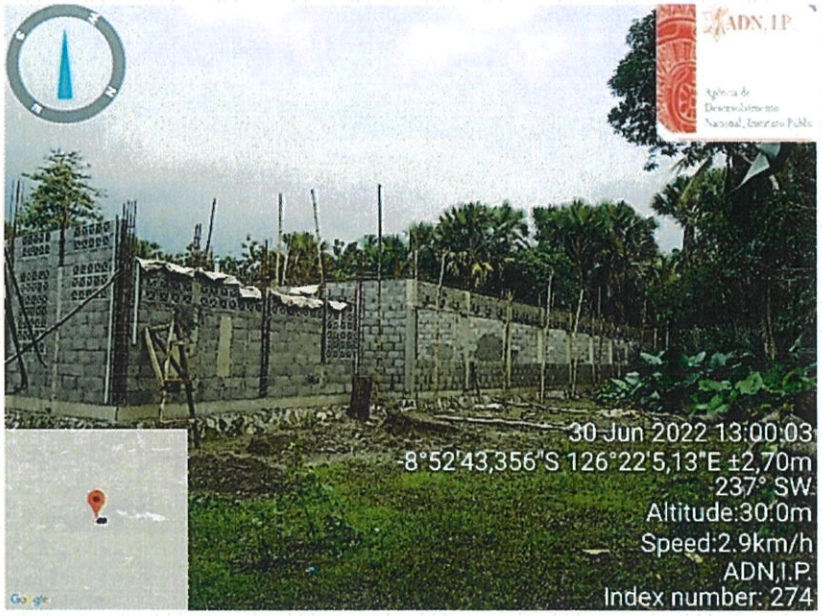

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projetu : Nova Construção da Escola secundaria geral calixa no code emis 5121
Lokalidade : Macdean uma quic Viqueque villa
Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY

							PREVIOUS		THIS MONTH		UP TO DATE	
	MAIN SUMMARY	Page No		Amount			AMOUNT $	%	AMOUNT $	%	AMOUNT $	%
I	PRELIMINARIES WORKS	PP/3		US$	3,075.00		$ 1,300.00	1.15%	$ -	0.00%	$ 1,300.00	1.15%
II	CLASSROOM BUILDING C	C/39	(i)	US$	58,664.20		$ 8,311.41	7.33%	$ 4,118.93	3.63%	$ 12,430.34	10.97%
III	TOILET BUILDING			US$	32,529.17		$ 2,699.90	2.38%	$ 3,820.34	3.37%	$ 6,520.23	5.75%
IV	PROFESSIONAL SUM for SITEWORKS	SW/24	(i)	US$	9,751.28		$ -	0.00%	$ -	0.00%	$ -	0.00%
	CONSTRUCTION COST			**US$**	**104,019.66**		$ 12,311.30	10.86%	$ 7,939.27	7.00%	$ 20,250.57	17.86%
	CONTIGENCY			US$	3,000.00		$ -	0.00%	$ -	0.00%	$ -	0.00%
	OVERHEAD			US$	6,340.00		$ -	0.00%	$ -	0.00%	$ -	0.00%
	GRAND TOTAL			**US$**	**113,359.66**		**$ 12,311.30**	**10.86%**	**$ 7,939.27**	**7.00%**	**$ 20,250.57**	**17.86%**

Prepared By

Eng. Bebiano Crecencio De Jesus Lopes
Eng. Municipio Viqueque ADN,I.P.

Cheked By

Arch. Francisco Xavier de Deus Jeronimo
Engineiro Senior ba Projeitu Edificio Publiku No Bee Saneamento ADN, I.P.

Aproved By

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validacão de Oualidade ADN.I.P.

ANEXU C1 (Viqueque-14)

Back-up Data

Naran Projeto : **Nova Construção da Escola Pre-Escolar Maria Lobato**
No. kontratu :

Data Inspesaun : 29-06-2022

Fatin Inspesaun : Bosa bein uma wain craic,viqueque villa

Koordinadas :

Start Point : Long : -8.553792" 126.242214

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : Serbisu Hada Batako remata,continuasaun ba serbisu sinta leten.	

ANEXU C1 (Viqueque-14)

Back-up Data

Naran Projeto : **Nova Construção da Escola Pre-Escolar Maria Lobato**
No. kontratu :



MINISTÉRIO DO PLANO
E ORDENAMENATO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projetu : Nova Construção da Escola maria lobato no code emis 1638
Lokalidade : Bosa bein uma wain craic viqueque villa
Projetu nain : Ministério da Educação, Juventude e Desporto, MEJD - TL

SUMMARY

	MAIN SUMMARY	Page No	Amount	Previous		This Billing		Up To Date	
				Amount $	%	Amount $	%	Amount $	%
I	PRELIMINARIES WORKS	PP/3	US$ 3.279,26	$ 1.309,63	1,41%	$ 219,63	0,13%	$ 1.529,26	1,54%
II	CLASSROOM BUILDING C2	C/39 (i)	US$ 56.119,79	$ 16.624,45	17,89%	$ 4.076,76	2,92%	$ 20.701,21	20,81%
III	PROVISIONAL SUM for SITEWORKS	SW/24 (i)	US$ 24.199,84	$ -	0,00%	$ 920,71	0,93%	$ 920,71	0,93%
	CONSTRUCTION COST		**US$ 83.598,89**	**$ 17.934,08**	**19,30%**	**$ 5.217,09**	**3,97%**	**$ 23.151,18**	**23,27%**
	CONTIGENCY		US$ 3.000,00	$ -	0,00%	$ -	0,00%	$ -	0,00%
	OVERHEAD		US$ 6.340,00	$ 540,00	0,58%	$ 1.797,50	1,77%	$ 2.337,50	2,35%
	GRAND TOTAL		**US$ 92.938,89**	**$ 18.474,08**	**19,88%**	**$ 7.014,59**	**5,74%**	**$ 25.488,68**	**25,62%**

Prepared By

Eng. Bebiano Crecencio De Jesus Lopes
Eng. Municipio Viqueque ADN,I.P.

Cheked By

Arch. Francisco Xavier de Deus Jeronimo
Engineiro Senior ba Projeitu Edificio Publiku No Bee Saneamento ADN,I.P.

Aproved By

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN,I.P.

ANEXU D (Viqueuqe-14)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Nova Construção da Escola Pre-Escolar Maria Lobato

Kompanha : PKRIE,PROJECTO KOMUNITARIO

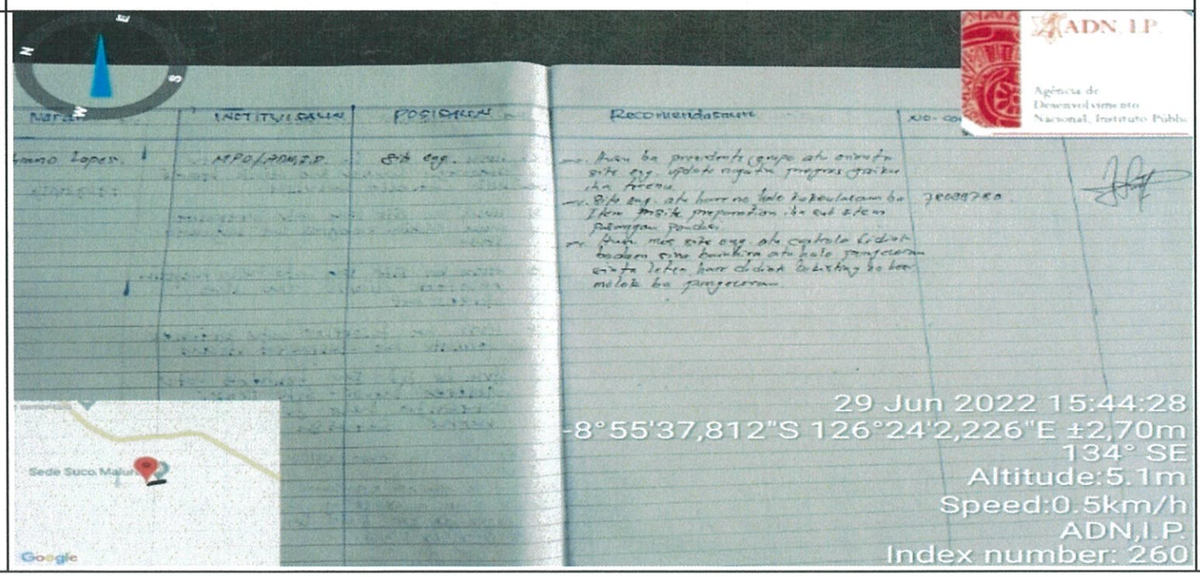No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	29/06/2022	Viqueuque Vila	Bebiano C. de Jesus Lopes	Tekniko	1	Husu ba site eng. Atu update nafatin progress fisiku iha terenu	
					2	husu mos ba site eng.atu halo estimasaun ba item site preparation iha sub item pasangan pondasi	
					3	site eng.atu controla didiak badaen sira bainhra atu monta bekisting no besi ba ringbalk molok halo pengecoran	
					4		
							

ANEXU C1 (Uatolari-10)

Back-up Data

Naran Projeto : **New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari**
No. kontratu :

Data Inspesaun : 15-06-2022

Fatin Inspesaun : Afaloicai

Koordinadas :

Start Point : Long : -8.5119278, 126.2148024

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : Serbisu sinta leten ramata	

ANEXU C1 (Uatolari-10)

Back-up Data

Naran Projeto : **New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari**
No. kontratu :



ANEXU D (Uatolari-11)


MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

NEW CONSTRUCTION OF CHAPEL BETESDA NAEDALA AFFALOICAI-UATOLARI

Kompanha : Be'e Horis unip,lda

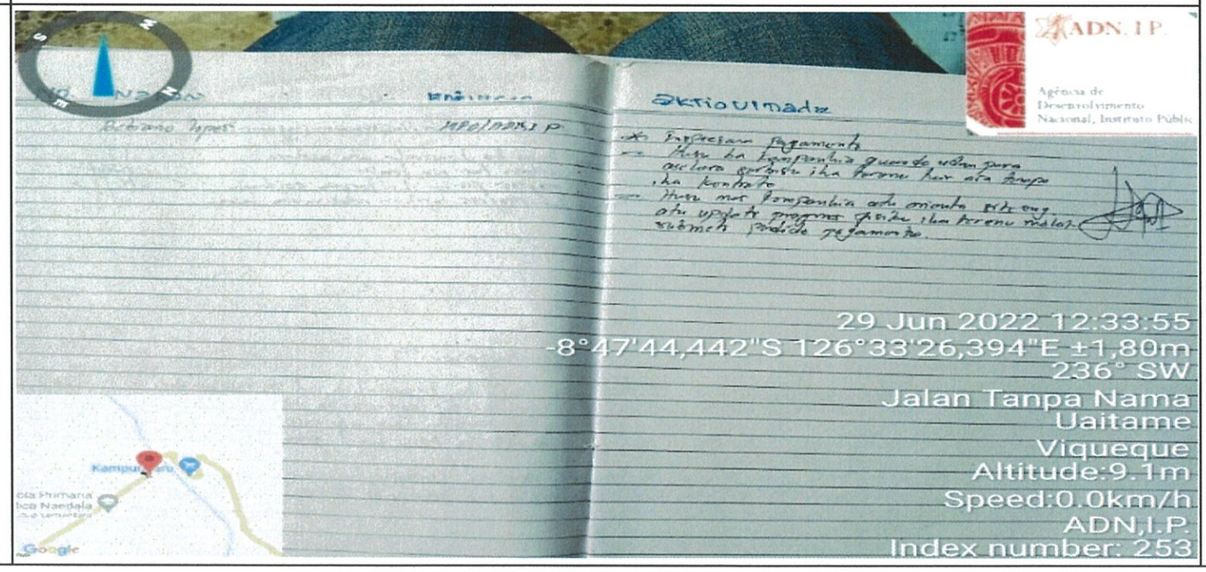No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	29/06/2022	Uatolari, Afaloicai	Bebiano C. de Jesus Lopes	Tekniko	1	Husu ba kompanhia bainhira udan para aselera serbisu iha terenu tuir nia tempo iha kontrato	
					2	Husu mos ba director kompanhia atu orienta site eng.update progress fisiku iha terenu molok submete pedido pagamento	
					3		
							

ANEXU C1 (Viqueque_17)

Back-up Data

Naran Projeto : **New Construction Office, Were House And Landscaping Of Viqueque Distric**
No. kontratu :

Data Inspesaun : 15-06-2022

Fatin Inspesaun : Rai Tahu,Viqueque Vila

Koordinadas :

Start Point : Long : -8.5441892, 126.2339576

End Point : Long :

Naran Inspector : 1. Bebiano Crecencio de Jesus Lopes

2.

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Serbisu pengecoran pasangan pondasi Office Building	

ANEXU C1 (Viqueque_17)

Back-up Data

Naran Projeto : **New Construction Office, Were House And Landscaping Of Viqueque Distric**
No. kontratu :

Sketch Item servisu : Observasaun iha tereno no Foto Aktual



MINISTÉRIO DO PLANO
E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

Naran Projectu : **New Construction Office , Warehouse and Landscaping**
CSSM - Viqueque
Nain ba Projectu : **Ministry Solidarity Social**
Fatin Projectu : **Suco Ratau, Viqueque Vila, Viqueque Municipality - Timor**

NO	DESCRIPTIONS OF WORKS	ORIGINAL CONTRAC	PREVIOUS MONTH		THIS MONTH		UP TO DATE	
A.	OFFICE BUILDING	AMOUNTH $	AMOUNTH $	%	AMOUNTH $	%	AMOUNTH $	%
1	PREPARATION WORKS	$ 14,760.92	$ 903.93	0.11%	$ -	0.00%	$ 903.93	0.11%
2	EARTH WORKS	$ 22,432.19	$ 903.93	0.11%	$ -		$ 903.93	0.11%
3	MASONRY WORKS	$ 82,579.83	$ -	0.00%	$ 8,599.96	1.07%	$ 8,599.96	1.07%
4	CONCRETE WORKS	$ 52,025.12	$ -	0.00%	$ -	0.00%	$ -	0.00%
5	ROOFING WORKS	$ 46,919.22	$ -	0.00%	$ -	0.00%	$ -	0.00%
6	CEILING WORKS	$ 21,320.84	$ -	0.00%	$ -	0.00%	$ -	0.00%
7	CARPENTERY WORKS	$ 19,700.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
8	ELECTRICAL WORKS	$ 11,318.39	$ -	0.00%	$ -	0.00%	$ -	0.00%
9	SANITATION WORKS	$ 9,903.36	$ -	0.00%	$ -	0.00%	$ -	0.00%
10	PAINTING WORKS	$ 7,588.47	$ -	0.00%	$ -	0.00%	$ -	0.00%
	TOTAL	**$ 288,548.35**	**$ 1,807.86**	**0.22%**	**$ 8,599.96**	**1.07%**	**$ 10,407.81**	**1.29%**
B.	WAREHOUSE							
1	EARTH WORKS	$ 4,425.76	$ 756.06	0.09%	$ -	0.00%	$ 756.06	0.09%
2	MASONRY WORKS	$ 14,378.42	$ -	0.00%	$ 2,461.86	0.31%	$ 2,461.86	0.31%
3	CONCRETE WORKS	$ 34,502.01	$ 4,775.32	0.59%	$ -	0.00%	$ 4,775.32	0.59%
4	ROOFING WORKS	$ 28,120.33	$ -	0.00%	$ -	0.00%	$ -	0.00%
5	CARPENTERY WORKS	$ 6,269.62	$ -	0.00%	$ -	0.00%	$ -	0.00%
6	ELECTRICAL WORKS	$ 2,497.99	$ -	0.00%	$ -	0.00%	$ -	0.00%
7	PAINTING WORKS	$ 2,745.37	$ -	0.00%	$ -	0.00%	$ -	0.00%
	TOTAL	**$ 92,939.50**	**$ 5,531.38**	**0.69%**	**$ 2,461.86**	**0.31%**	**$ 7,993.24**	**0.99%**
C.	LANDSCAPING WORKS							
1	PARK AND OFFICE PLATFORM WORKS	$ 192,445.89	$ -	0.00%	$ -	0.00%	$ -	0.00%
2	PARK ELECTRICAL WORKS	$ 4,922.36	$ -	0.00%	$ -	0.00%	$ -	0.00%
3	FENCE WOKS	$ 89,396.67	$ 2,852.02	0.35%	$ 10,498.68	1.30%	$ 13,350.70	1.66%
4	SECURITY POST	$ 32,014.67	$ -	0.00%	$ -	0.00%	$ -	0.00%
	TOTAL	**$ 318,779.58**	**$ 2,852.02**	**0.35%**	**$ 10,498.68**	**1.30%**	**$ 13,350.70**	**1.66%**
I	**TOTAL (A+B+C)**	$ 700,267.43	$ 10,191.25	1.27%	$ 21,560.50	2.68%	$ 31,751.75	3.94%
II	**CONTRACTOR FEE & OVERHEAD 10% x I**	$ 70,026.74	$ 1,019.13	0.13%	$ 2,156.05	0.27%	$ 3,175.17	0.39%
III	**OVERHEAD**	$ 5,550.00	$ -	0.00%	$ -	0.00%	$ -	0.00%
IV	**TAX 2% x (I+II+III)**	$ 15,516.88	$ 224.21	0.03%	$ 474.33	0.06%	$ 698.54	0.09%
V	**CONTINGENCY 2% x I**	$ 14,005.35	$ -	0.00%	$ -	0.00%	$ -	0.00%
VI	**GRAND TOTAL (I+II+III+IV+V)**	**$ 805,366.41**	**$ 11,434.59**	**1.42%**	**$ 24,190.88**	**3.00%**	**$ 35,625.46**	**4.42%**

Prepared By

Eng. Bebiano Crecencio De Jesus Lopes
Eng. Municipio Viqueque, ADN, I.P.

Cheked By

Arch. Francisco Xavier de Deus Jeronimo
Engineiro Senior ba Projeitu Edificio Publiku No Bee Saneamento, ADN,I.P.

Aproved By

Eng. Emerenciana da Costa Maia Freitas
Coordenadora da Unidade de Controlo e Validação de Qualidade, ADN,I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
Lacluta	1	Package II Dilor	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
OSSU	1	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	2	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750-Municipal of Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	3	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	4	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	Kay Seng Unip. Lda	MPW-W-190084	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	5	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	Costa Key Unip Lda	MPW-W-210053	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	6	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	Manoko Unip. Lda	MPW-W-210050	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	7	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	
	8	New Construction of Health Post and Doctor's House building in Builale	Borala Unipessoal Lda	RDTL-MS-DNA-ICB-21-075	LM	MINISTERIO DA SAUDE	Plan																															Lao Hela
							Actual																															
	9	R4D Riral Roads Periodic Maintenance ossu - Nahareka Chainage 4+350 - 6+350	Fin-Los Unip. Lda JV Costa Key Unip. Lda	MPW - W - 190085	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	10	EBF Uaibobo	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela,Condisaun dalan asesu ladiak
							Actual																															
	11	Pre Escolar Uaibua	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	12	ESG Oloaasa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	13	EBF Liaruca	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela,Condisaun dalan asesu ladiak
							Actual																															
AU	1	Construction of Dardau Irrigation Scheme Municipality Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															
							Actual																																	
	2	Consulting Services For Construction Supervision of Dardau Irrigation	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															
							Actual																																	
	3	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30	OBS
UATOCARB.	4	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	5	Konstrusaun Edificio Posto Administrativo Uato-Carbau	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan		PHO
							Actual		
	6	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	7	EBC 2.3 Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	8	ESG Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
UATOLARI	1	New installation of mv,lv line and house connection in Area Lawai Viqueque District	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	2	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	3	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	4	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	5	New Construction Of Gapura,Stairs and Wall Protection in Garden Of Heroes	Natureza Furak,Unip Lda	ICB/005/DNAL/MACLN/VIII/2021	LM	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	Plan		Lao Hela
							Actual		
	6	Konstrusaun Edificio Posto Administrativo Uatolari	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan		PHO
							Actual		
	7	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	8	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	Karakuta Unip Lda	MPW-2013/JUNE	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	10	New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari	Be'e Horis unip,lda		LM	IGREJA PROTESTANTE TIMOR	Plan		Lao Hela
							Actual		
	11	Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque	L.M. Caicasa Metin Unip,Lda	RDTL-MAP-PO2021:15965	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan		
							Actual		
	12	EBF Nahae	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	13	EBF Uaibira	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	14	EBC Uatolari	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	15	EBF Edemumu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	16	EBF Ualake	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan								■								■							■									Lao Hela
							Actual																																
	17	ESTV Kaluheda	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan								■								■							■									Lao Hela
							Actual																																
	18	EBF Debuisi	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan								■								■							■									Lao Hela
							Actual																																
VIQUEQUE	1	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	2	Rehabilitation of Urban Road Municipality Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	3	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	4	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	Arquiris	SSS/105/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	5	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	Dira Nova Unip. Lda	MPW - W - 190114	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	6	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package: 12 Luca - Lacluta	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	7	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	Uma Liurai unip, lda	SSS/138/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	8	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	Bihalutur Unip, lda	SSS/141/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	9	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section : Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	Loke Matan unip, lda	SSS/307/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	10	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	Caburela unip,lda	SSS/306/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	11	Servisu Manutensaun Edifício Agencia de Desemvolvimentu Nasional, I.P, Municipio Viqueque	Luminar, Unip,Lda	22/RDTL/MPO/AND,I.P/XI/2021	LM	MOP/ADN,I.P	Plan																																PHO/FHO
							Actual																																
	12	ESG Calixa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	13	EBF Ular Rihik	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	14	Pre Escolar Maria Lobato Raithu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	15	EBC Caibiraoan	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	16	Pre Escolar Sebastiao Gomes Uai Mori Tula	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	17	New Construction Office, Were House And Landscaping Of Viqueque Distric	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	LM	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	Plan																																Lao Hela
							Actual																																
MULTI POSTO ADMINISTRATIVO	1	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
TOTAL PROJETO ON-GOING																																					

Note:

Plano Periode inspesaun iha terenu | **Implementa Planu Periode Inspesaun** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Prosesu Pagamentu**

Prepara Husi :

(Eng. Bebiano C. de Jesus Lopes)
Eng. Munisipiu Viqueque ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres .)
Adjunto Director Executivo ADN,I.P.

ANEXU C1 (Oss-4)

Back-up Data

Naran Projeto : **Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)**

No. kontratu : **MPW-W-190084**

Data Inspesaun **:21/06/2022**

Fatin Inspesaun : Ossu Luihonu

Koordinadas :

Start Point : Long : (S -8.464097932), Latetude : (E 126.231849766)

End Point : Long : (S -8.464108523), Latetude : (E 126.232043187)

Naran Inspector **: 1. Eng.Roberto M. Martins**

2. Eng. Salvador Martins

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …	
Projetu Refere Paradu hela Laiha Actividade Servisu iha Terren,, Direksiket kompania nian taka hela, Imformasaun husi kompania Sei hein pagamentu hafoin kompania kontinua fila fali servisu.	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)

Kompanha : Kay Seng Unip. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	21/6/2022	Ossu Luihono. Viqueque	Roberto M. Martins & Salvador Martins	Eng. ITI.ADN,IP. Municipio Viqueque	1	Monitoring Servisu tuir palnu Inspesaun Projetu iha Terreno	
					2	Bainhira Eng Municipio Halo Monitring la Hasoru Eng. kompania iha terreno	
					3		
					4		
					5		

Back-up Data

Naran Projeto : **Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 Package VII) in Uatolari Municipality Viqueque**

No. kontratu :

Data Inspesaun : 22/06/2022

Fatin Inspesaun : Uatulari



Koordinadas :

Start Point : Long : - 8.82026 S Latetude : 126.53278 E

End Point : Long : - 8.82897 S Latetude : 126.52511 E

Naran Inspector : 1. Eng. Salvador Martins

2. Eng. Roberto M. Martins

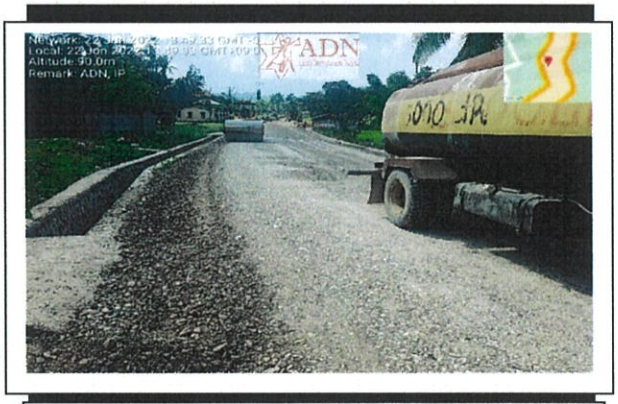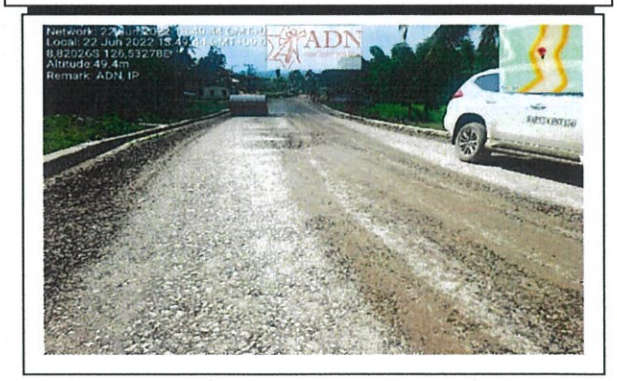Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …	Servico Base Course Watulari
Companhia plano no Prepara Hela Hela material Basee Course ba 5km iha area Watulari nian.	 

Back-up Data

Naran Projeto : **Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque**
No. kontratu : **RDTL-MAP-PO2021:15965**

Data Inspesaun : 22/06/2022

Fatin Inspesaun : Uatulari


Koordinadas :

Start Point : Long : - 8.80299 S Latetude : 126.56135 E

End Point : Long : - 8.80583 S Latetude : 126.56372 E

Naran Inspector : 1. Eng. Salvador Martins
2. Eng. Roberto M. Martins

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu … Strukture excavation for Krip Rip - Rap Volume = 234 Cu.m	Structure Excavation For Krip







Back-up Data


Naran Projeto : **Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque**
No. kontratu : **RDTL-MAP-PO2021:15965**

ketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …Embankment with compation Sta Sta 0 + 00 to 0 + 294.28 Distance = 294.28 m Area = 5.25 Sq.m Volume = 1545Cu.m	Sketch Item servisu …Embankment with compation

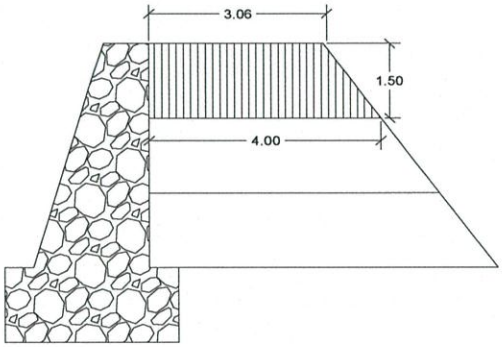

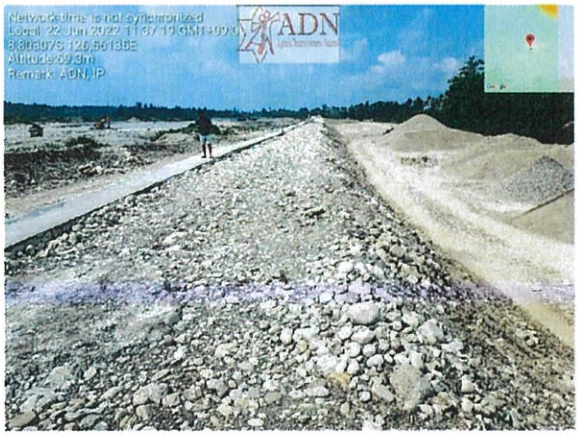

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Stone masonry For Krip Rip Rap L = 3.5, Area = 8 Sq.m = 28 Cu.m = 28 x 12 titik Volume = 336.71 Cu.m	Stone masonry For Krip Rip Rap

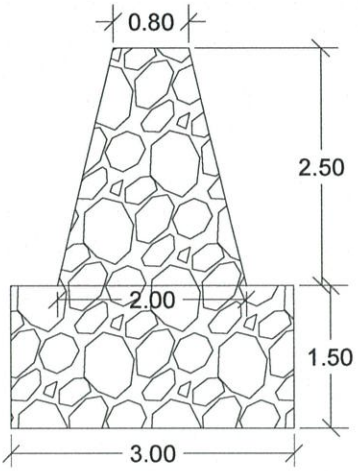




Back-up Data


Naran Projeto : **Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque**
No. kontratu : **RDTL-MAP-PO2021:15965**


Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu … Embankment with compation Sta Sta 0 + 00 to 0 + 401 Volume = 1381.5 Cu.m	Embankment with compation Sta Sta 0 + 00 to 0 + 401

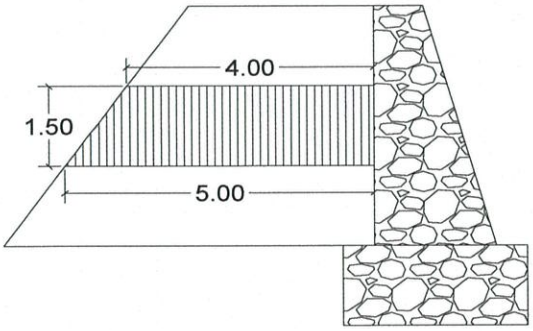



Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …Plestering for Stone Masonri Retaining Wall And Krip Rip - Rap Volume = 1651.8 Sq.m	Plestering 1 : 3

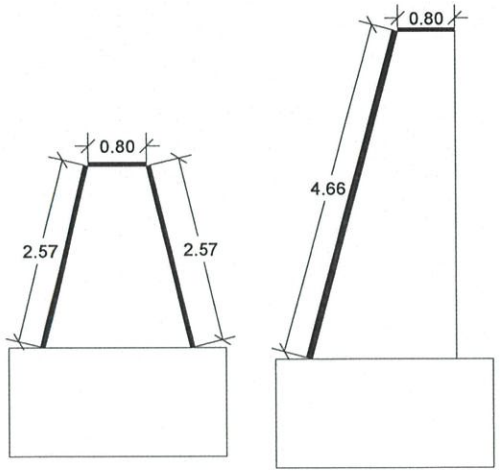

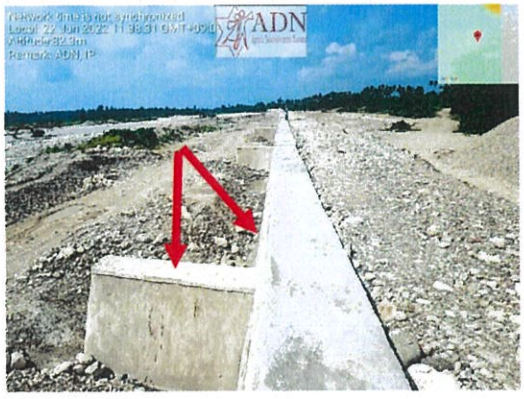

VIII GOVERNO CONSTITUCIONAL
MINISTÉRIO DO PLANEAMENTO E
INVESTIMENTO ESTRATÉGICO

ADN
Agência de Desenvolvimento Nacional

ANEXU C-2 (UatL-11)

Project Owner : **Ministry of Agriculture and Fisheries**
Location : **Bebui, Uatulari Sub District, Viqueque Municipality**
Name of Project : **Rehabilitation of Bebui Wall Protection**

BACK UP DATA

BILL OF QUANTITY				PROGRESS MONITORING PROJEC 2022						
No	ITEM OF WORKS	TOTAL COST (USD)	WEIGHT %	PROGRESS PREVIOUS QUANTITY	PROGRESS PREVIOUS COST ($)	Junho 2022 QUANTITY	Junho 2022 COST ($)	PROGRESS TO DATE QUANTITY	PROGRESS TO DATE COST ($)	REMARKS
I.	Preparation Works	$ 16,650.12	3.72%	$ 11,110.06	2.48%	$ 1,420.06	0.32%	$ 12,530.12	2.80%	
II.	Eart Work	$ 9,345.00	2.09%	$ 6,930.00	1.55%	$ 819.00	0.18%	$ 7,749.00	1.73%	
III.	Stone Masonry, Plastering & weephole works	$ 293,297.36	65.54%	$ 264,499.05	59.11%	$ 28,798.31	6.44%	$ 293,297.36	65.54%	
IV.	Embankment with compation work	$ 26,460.00	5.91%	$ 21,052.50	4.70%	$ 5,407.50	1.21%	$ 26,460.00	5.91%	
V.	River Normalization Work	$ 52,875.00	11.82%	$ 44,943.75	10.04%	$ 7,931.25	1.77%	$ 52,875.00	11.82%	
VI.	Finishing work	$ 200.00	0.04%	$ -	0.00%	$ -	0.00%	$ -	0.00%	
A	TAL CONSTRUCTION COST (I+II+III +IV+V+	$ 398,827.48	89.13%	$ 348,535.36	77.89%	$ 44,376.12	9.92%	$ 392,911.48	87.80%	
B	ITEM OF WORKS (A X 10%)	$ 39,882.75	8.91%	$ 34,853.54	7.79%	$ 4,437.61	0.99%	$ 39,291.15	8.78%	
C	TAX (A+B)*2%	$ 8,774.20	1.96%	$ 7,667.78	1.71%	$ 976.27	0.22%	$ 8,644.05	1.93%	
D	GRAND TOTAL COST (A+B+C)	$ 447,484.43	100.00%	$ 391,056.67	87.39%	$ 49,790.01	11.13%	$ 440,846.68	98.52%	

Prepara Husi :

1. (Eng. Salvador Martins)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

2. (Eng. Roberto M. Martins)
Eng. ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

Verifika Husi :

(Eng. Remigio da C.S. dos Santos)
Eng. Senior ba Projeto Infrastructura, Transportes e Irigasaun ADN, I.P

Sertifika Husi :

(Eng. Emerenciana da C. Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.


Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto :Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque

Kompanha : L.M. Caicasa Metin Unip,Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	22/6/2022	Uatulari	Roberto M. Martins & Salvador Martins	Eng.ITI,ADN,IP. Municipio Viqueque	1	Halo monitoring Servisu,Update Progres Fisik Servisu,Plestering,Stone Masonry for Krip Embankmen	
					2	Sujere ba kompania Atu Finaliza lalais Embankment iha Retaining Wall nia oin	
					3	Sujere ba kompania atu halo kontinuasaun normaliza River, Rai henek nebe'e normaliza geser mai iha retening wal nian oin	
					4	Sujere ba kompania atu finalija lalais servisu neb'e sedauk finaliza atu nune bele seubmete ona pagamentu.	

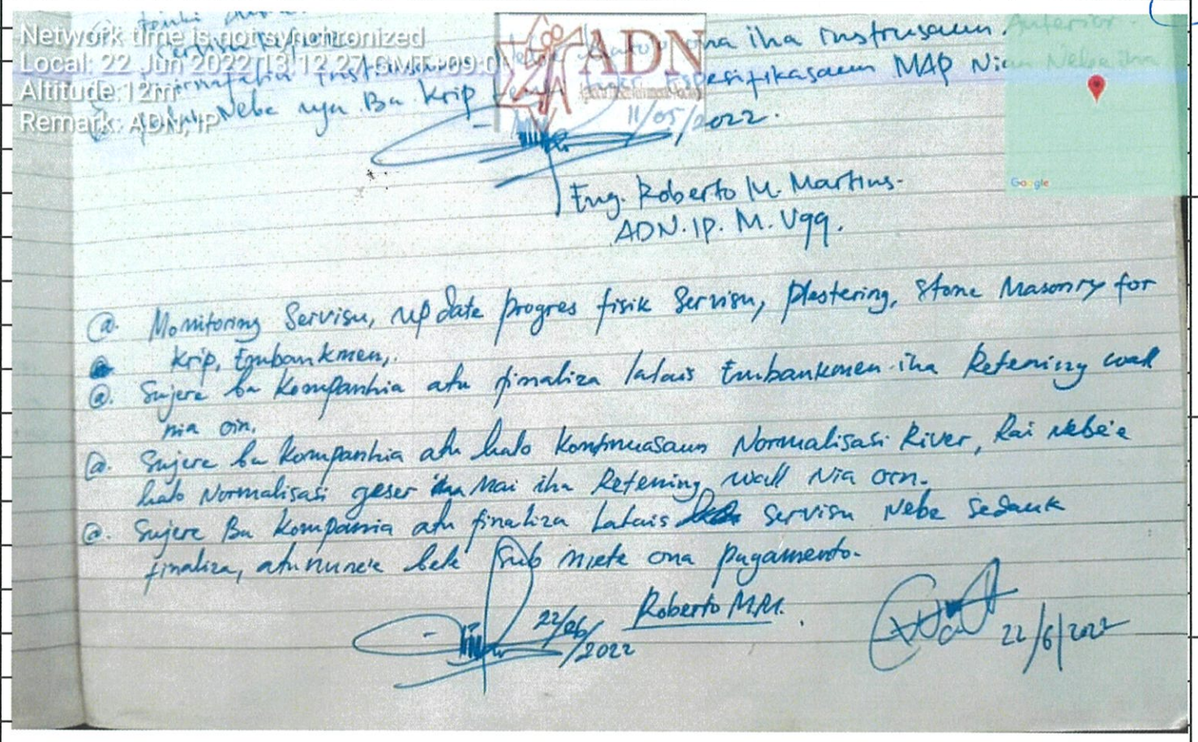

ANEXU C1 (Oss-2)

Back-up Data

Naran Projeto : **Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750- Municipal of Viqueque**

No. kontratu : **RT/072/MOPTC-2016**

Data Inspesaun : 21/ 06 / 2022

Fatin Inspesaun : Ossu, Luihono Osorua


Koordinadas :

Start Point : Long : (S. -8.452196), Latetude : (E.126.244785)

End Point : Long : (S. -8.452219), Latetude : (E. 126.244734)

Naran Inspector : **Eng. Roberto M. Martins**

Eng. Salvador Martins

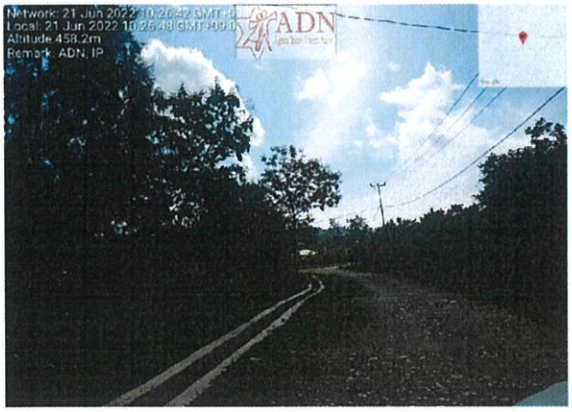Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
La iha Actividade Servisu iha terreno, bainhira Eng Municipio halo monitorijasaun la hasoru Eng kompania.	

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750- Municipal of Viqueque

Kompanha : Boru- Buty Unip.Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	21Junho 2022	Ossu	Roberto M.M & Salvador Martins	Eng. ITI,ADN,I.P. Municipio Viqueque	1	Eng. kompanhia laiha terreno	
					2	Direksiket Companhia Mamuk	
					3		
					4		
					5		
II					1		
					2		
					3		
					4		
					5		
III					1		
					2		
					3		
					4		
					5		
IV					1		
					2		
					3		
					4		
					5		
V					1		
					2		
					3		
					4		
					5		

ANEXU C1 (Oss-1)

Back-up Data

Naran Projeto : **Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque**

No. kontratu : **SSS/064/MOPTC-2017**

Data Inspesaun : 31/06/2022

Fatin Inspesaun : Ossu

Koordinadas :

Start Point : Long : (-8°38'38.21" S) Latetude : (126'22'33.38" E)

End Point : Long : (-8°50'55.35" S) Latetude : (126'21'59.71" E)

Naran Inspector : Eng. Roberto M. Martins

Eng. Salvador Martins

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu : Retaining Wall	Retaining Wall
Iha Data 31 Laiha Actividade Servico Iha tereno tamaba Udan, no laiaha travalhador iha service fatin.	
	

ANEXU D (Oss-1)

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque

Kompanha : Uhacae, Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	31/06/2022	Viqueque / Osso	Roberto M.Martins & Salvador Martins	Eng.ITI,ADN,IP. Municipio Viqueque	1	Monitoring Servisu ba Reatening Wall No Stone Massonry, maibe Comp.laiha fatin tamba Udan.	
					3	Compania Liha Lokasi Tamba Udan iha kosta sul makas no la fo tempo atu bele Comp. halo servico, tamba ne'e laiha progreco iha semana ida ne'e.	

ANEXU C1 (Lac-1)

Back-up Data

Naran Projeto : **Package II Dilor**
No. kontratu : **SSS/089/MOPTC-2017**

Data Inspesaun : 30 / 06 / 2022

Fatin Inspesaun : Dilor Lacluta, Viqueque

Koordinadas :

Start Point : Long : (S -8.5623784) Latetude : (E 126.621888)

End Point : Long : (S -8.5622812) Latetude : (E 126.62145)


Sketch & Foto Desenho

Sketch Item servisu : Koncrete 31.5 Mpa

Area = 5.125 Sq.m

Distance = 24 m

Volume = 123 Cu.m

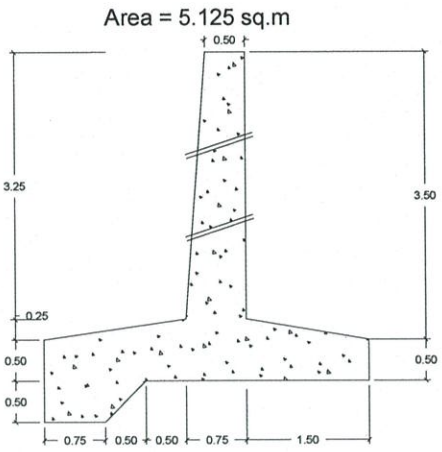

Observasaun iha tereno no Foto Aktual

Kompania Sedauk kontinua servisu Reiforced Concret 31.5 Mpa



Sketch & Foto Desenho

Observasaun iha tereno no Foto Aktual

ANEXU C1 (Lac-1)

Back-up Data


Naran Projeto : **Package II Dilor**
No. kontratu : **SSS/089/MOPTC-2017**


Sketch Item servisu : Estructure Excavation

Area = 9.625 Sq.m

Distance = 24 m

Volume = 231 Cu.m

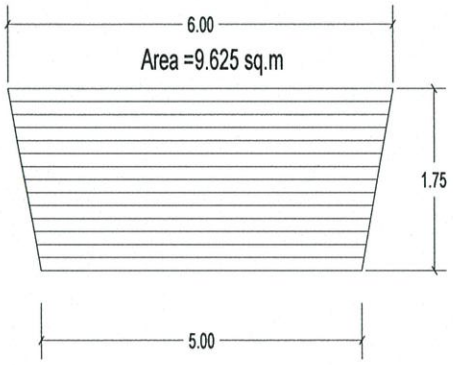

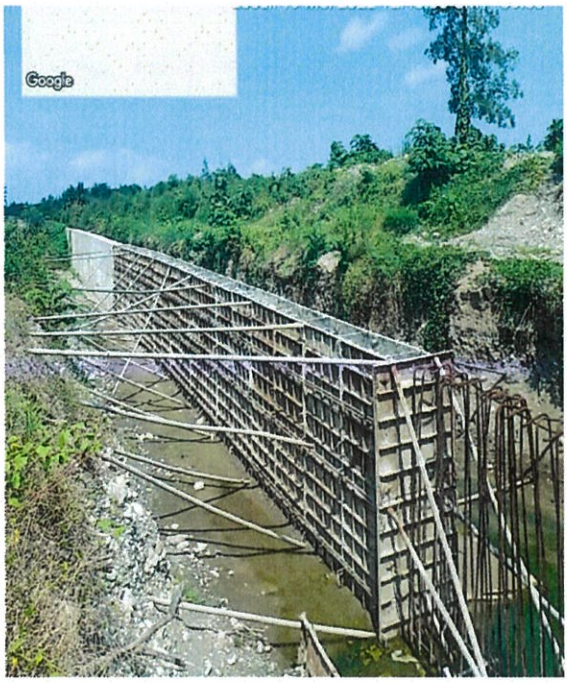

MINISTERIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Package II Dilor

Kompanha : Sheramor Construction Unipessoal, Lda

No	Data Inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	30/6/2022	Viqueque / Lacluta	Roberto M. Martins	Eng.ITI,AND,I.P. Municipio Viqueque	1	Eng. AND, I.P. Municipio Viqueque Labele fo instrusaun tamba la hasoru Eng. Husi kompanhia iha terreno.	
II	30/6/2022	Viqueque / Lacluta	Salvador Martins	Eng.ITI,AND,I.P. Municipio Viqueque	2	Eng. AND, I.P. Laiha Dalan alternativo hodi ultrapasa ba Direksiket kompania nian tamba Ponte Dilor kotu no mota bot	

ANEXU C1 (Oss-6)

Back-up Data

Naran Projeto : **R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800**

No. kontratu : **MPW-W-210050**

Data Inspesaun : **21 / 06 / 2022**

Fatin Inspesaun : Ossu


Koordinadas :

Start Point : Long : S. (-8. 7452) Latetude : E. (126.3851)

End Point : Long : S. (-8. 7505) Latetude : E. (126.4091)

Naran Inspector : **1. Eng. Roberto M. Martins**

: **2. Eng. Salvador Martins**

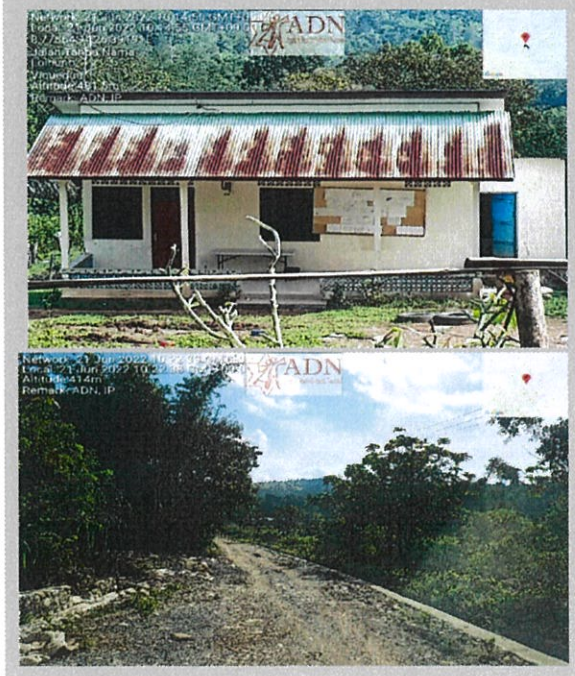Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Projetu Refere Paradu hela Laiha Actividade Servisu iha Terreno, Direksiket kompania nian taka hela, Imformasaun husi kompania Sei hein pagamentu hafoin kompania kontinua fila fali servisu.	Item : 

#ANNEXU D (Oss-6)

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

INSTRUSAUN / REKOMENDASAUN

Naran projeto : R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800

Kompanha : Manoko Unip. Lda

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	21/6/2022	Ossu	Roberto M.M & Salvador Martins	Eng.ITI,AND,I.P, Municipio Viqueque	1	Monitoring Sevisu bajeia ba planu ispesaun Projetu	
					2	laiha Actividade servisu	
					3	Eng ADN municipio labele fo instrusaun de servisu tamba bainhira halo inspesaun la hasoru Eng kompania no Direksiket kompania nian mos taka hela	

ANEXU C1 MP-16

Back-up Data

Naran Projeto : **Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120**
No. kontratu : **ICB/046/MOPTC-2017**

Data Inspesaun : **10/ 06/ 2022**

Fatin Inspesaun : Baucau -venilale

Koordinadas :

Start Point : Long : (-8.48'34,833" S), Latetude : (-8'64'38,31 S)


End Point : Long : (126'45'78,15" E), Latetude : (126'37'60,73 E)

Naran Inspector : **1 Eng. Salvador Martins**

2. Eng. Tito Edgar F.N. de Jesus

3. Eng. Augusta da Costa Ferreira

Sketch & Foto Desenho Stone Masonry

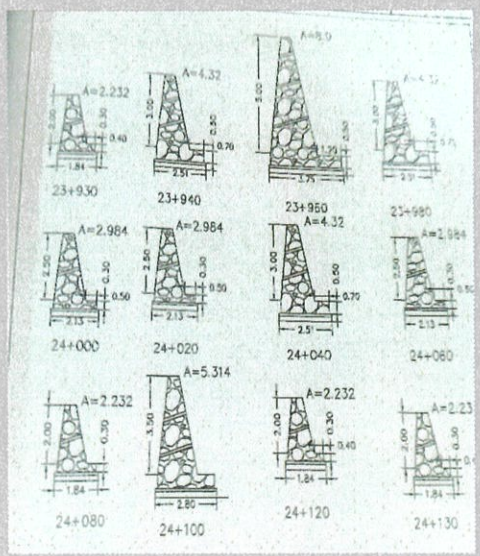


Observasaun iha tereno no Foto Aktual



ANEXU C1 MP-16

Back-up Data

Naran Projeto : **Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120**
No. kontratu : **ICB/046/MOPTC-2017**

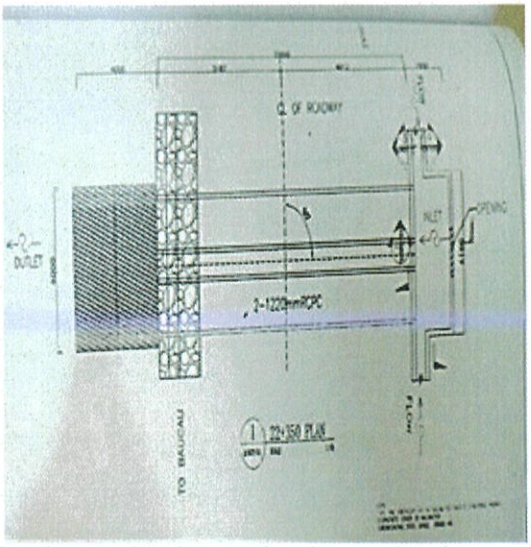Foto Desemho Item Servisu Catch Basin	Observasaun iha Teresnu no foto Actual
	


ANEXU C1 MP-16


Back-up Data

Naran Projeto : **Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120**
No. kontratu : **ICB/046/MOPTC-2017**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual

Sketch Item servisu Pipe Culvert

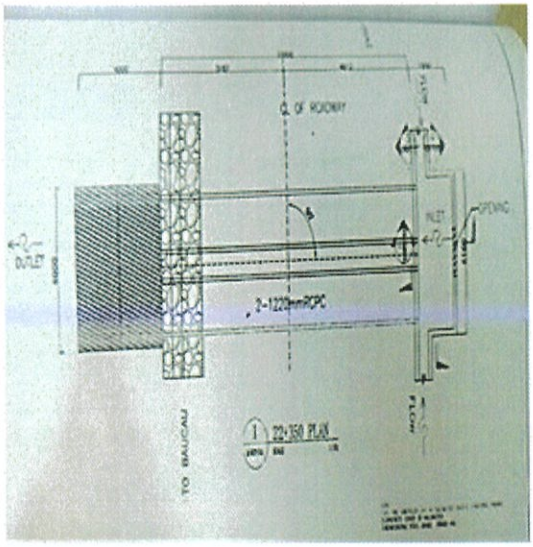

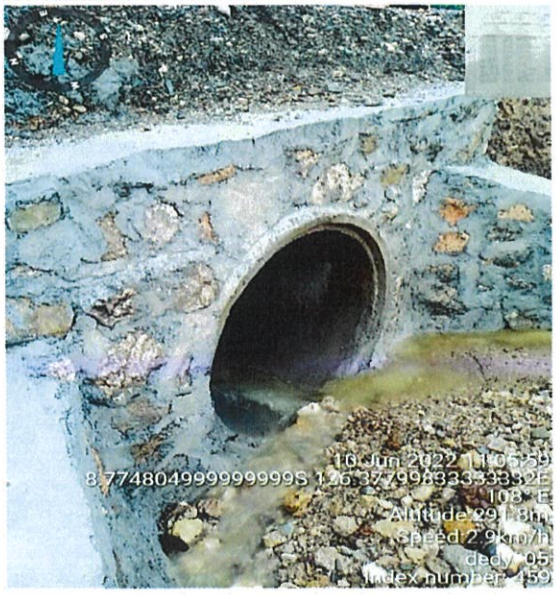

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

#ANEXU C2 (MP- 2)

Project Name : Road Network Upgrading Sector Project (RNUSP) ADB Loan Nos.3643-TIM and 3644- TIM (COL) Upgrading and Maintenance of Baucau-Viqueque Highway Project Lot 2: Venilale- Viqueque Sta.27+120 to Sta. 62+010 (with exceptions) ICB/046/MOPTC/2017

Contractor : China Railway International Group Co.,Ltd in Joint Venture With China Overseas Engineering(Group)Co.,Ltd.

IPC no. : IPC. No. 9 (December 26, 2021 - March 25, 2021)

SECTION NO.	DESCRIPTION	TOTAL CONTRACT COST	TOTAL VALUE OF WORK PREVIOUSLY	PERCENT PREVIOUS	TOTAL VALUE OF WORK THIS BILLING	PERCENT THIS MONTH	TOTAL VALUE OF WORK TO DATE	% TO DATE	BALANCE OF COST TO DATE
		(US Dollar)	(US Dollar)	%	(US Dollar)	%	(US Dollar)	%	(US Dollar)
100	GENERAL REQUIREMENTS	$ 1,341,469.63	$ 937,145.90	3.93%	$ 135,868.38	0.57%	$ 1,073,014.28	4.50%	$ 268,455.35
200	EARHWORKS	$ 1,696,790.33	$ 565,865.12	2.37%	$ 62,368.67	0.26%	$ 628,233.80	2.63%	$ 1,068,556.53
300	SUBBASE AND BASE COURSES	$ 2,271,730.88	$ 145,424.07	0.61%	$ -	0.00%	$ 145,424.07	0.61%	$ 2,126,306.81
400	SURFACE COURSE	$ 2,746,887.61	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 2,746,887.61
500	BRIDGE CONSTRUCTION	$ 3,740,360.05	$ 1,367,240.93	5.73%	$ 127,677.04	0.54%	$ 1,494,917.97	6.27%	$ 2,245,442.08
600	DRAINAGE AND SLOPE PROTECTION STRUCTURES	$ 5,814,913.55	$ 1,617,417.88	6.78%	$ 273,686.09	1.15%	$ 1,891,103.96	7.93%	$ 3,923,809.59
700	MISCELLANEOUS STRUCTURES	$ 753,963.46	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 753,963.46
800	BIO ENGINEERING	$ 273,338.60	$ 17,726.40	0.07%	$ 14,772.00	0.06%	$ 32,498.40	0.14%	$ 240,840.20
DW	DAYWORKS	$ 218,962.39	$ 38,842.66	0.16%	$ -	0.00%	$ 38,842.66	0.16%	$ 180,119.73
	PROVISIONAL SUM AND CONTINGENCY	$ 4,804,000.00	$ 423,584.05	1.78%	$ -	0.00%	$ 423,584.05	1.78%	$ 4,380,415.95
	TOTAL =	**$ 23,662,416.50**	**$ 5,113,247.08**	**21.44%**	**$ 614,372.18**	**2.58%**	**$ 5,727,619.20**	**24.01%**	**$ 17,934,797.31**
	PERFORMANCE BASED MAINTENANCE WORKS	$ 190,759.20	$ -	0.00%	$ -	0.00%	$ -	0.00%	$ 190,759.20
	CONTRACT AMOUNT	**$ 23,853,175.70**	**$ 5,113,247.08**	21.44%	**$ 614,372.18**	2.58%	$ -	24.01%	**$ 23,853,175.70**
	GRAND TOTAL	**$ 23,853,175.70**	**$ 5,113,247.08**	**21.44%**	**$ 614,372.18**	**2.58%**	**$ 5,727,619.20**	**24.01%**	**$ 18,125,556.51**

Inspection By :

For

(Eng. Roberto Martins)
Eng. ba Projeito Infraestructura, Transporte e Irrigasaun Municipio Baucau, ADN, I.P.

(Eng. Salvador Martins)
Eng. PMU ba Projeito (Imprestimu), ADN, I.P.

(Eng. Tito Edgar F.N. de Jesus)
Eng. PMU ba Projeito (Imprestimu), ADN, I.P.

(Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projeito (Imprestimu), ADN, I.P.

FOR

(Eng. Vidal Guterres)
Eng. PMU ba Projeito (Imprestimu), ADN, I.P.

Verifika Husi :

(Eng. Remigio da C. S. dos Santos)
Eng. Senior ba projeito Infraestrutura, Transporte e Irrigasaun, ADN, I.P.

Sertifika husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validação de Qualidade ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público


ANEXU D (MP-16)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale- Viqueque : 27 + 120 to Sta. 62+010 (with exceptions) ICB/046/MOPTC/2017

Kompanhia : China Railway Int. Group co, jv with China oversees

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	10/6/2022	Viqueque	Salvador Martins	Eng. Ba Projetu ITI Munisipiu Viqueque, ADN, I.P.	1	Inspesaun ba Pagmento IPC No.9.	
II			Tito Edgar F.N.de Jesus	Eng. PMU ba Projetu (Imprestimo), ADN, I.P.	2	Husu ba Kontraktor atu servisu baseia ba schedule ne'ebe planeia ona.	
III			Augusta da Costa Ferreira		3	Presiza tau atensaun ba area ne'ebe mak risku sliding no husu mos ba kontractor atu toma atensaun ba refere nomos koodena ho PMU.	

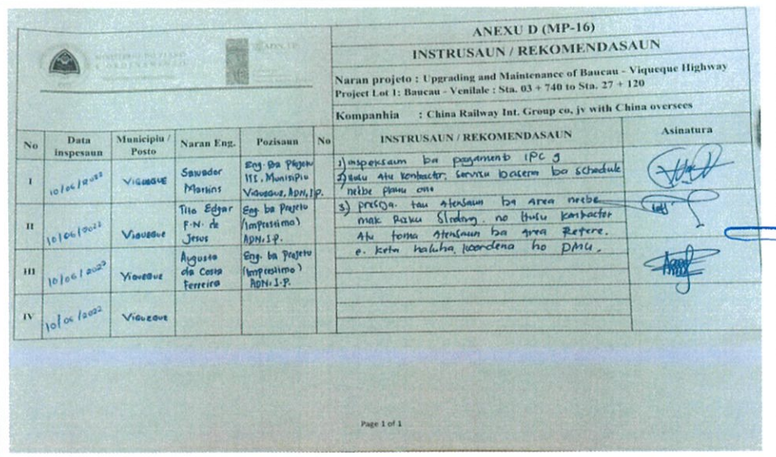

ANEXU D (MP-16)

INSTRUSAUN / REKOMENDASAUN

Naran projeto : Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 1: Baucau - Venilale : Sta. 03 + 740 to Sta. 27 + 120

Kompanhia : China Railway Int. Group co, jv with China oversees

No	Data inspesaun	Municipiu / Posto	Naran Eng.	Pozisaun	No	INSTRUSAUN / REKOMENDASAUN	Asinatura
I	10/06/2022	Viqueque	Salvador Martins	Eng. Ba Projetu ITI, Munisipiu Viqueque, ADN, IP.	1	1) inspesaun ba pagamentu IPC 9	
II	10/06/2022	Viqueque	Tito Edgar F.N. de Jesus	Eng. ba Projetu (Imprestimo) ADN, I.P.	2	2) husu atu kontractor servisu baseia ba schedule ne'ebe planeia ona	
III	10/06/2022	Viqueque	Augusta da Costa Ferreira	Eng. ba Projetu (Imprestimo) ADN. I.P.	3	3) presiza tau atensaun ba area ne'ebe mak perku Sliding no husu kontactor atu toma atensaun ba area Refere. e. kota halaiha koordena ho PMU.	
IV	10/06/2022	Viqueque					

Page 1 of 1

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Tito Edgar F.N. de Jesus

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		We 1	Th 2	Fr 3	Sa 4	Su 5	Mo 6	Tu 7	We 8	Th 9	Fr 10	Sa 11	Su 12	Mo 13	Tu 14	We 15	Th 16	Fr 17	Sa 18	Su 19	Mo 20	Tu 21	We 22	Th 23	Fr 24	Sa 25	Su 26	Mo 27	Tu 28	We 29	Th 30	OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															PHO
							Actual																															
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Pagamento
							Actual																															
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Iep) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun Pagamento
							Actual																															
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															Halo Relatorio Pagamento
							Actual																															
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan																															Inspecsaun ba Pagamento
							Actual																															

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual		
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		
TOTAL PROJETO ON-GOING								

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu

PHO

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Tito Edgar F.N. de Jesus)
Eng. PMU ba Projetu (Impréstimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO

VIII GOVERNO CONSTITUCIONAL

ADN, I.P.

Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Tito Edgar F.N. de Jesus

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phils, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

Eng. Tito Edgar F.N. de Jesus
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Teresa Gomes

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Pagamento
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun ba Pagamento

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual		
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municipio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
								PHO
TOTAL PROJETO ON-GOING								

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Teresa Gomes)
Eng. PMU ba Projetu (Impréstimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Teresa Gomes

Municipio MUNICIPIO DILI NO POSTOS

2022

OBSERVASAUN

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		Junho
								We 1 · Th 2 · Fr 3 · Sa 4 · Su 5 · Mo 6 · Tu 7 · We 8 · Th 9 · Fr 10 · Sa 11 · Su 12 · Mo 13 · Tu 14 · We 15 · Th 16 · Fr 17 · Sa 18 · Su 19 · Mo 20 · Tu 21 · We 22 · Th 23 · Fr 24 · Sa 25 · Su 26 · Mo 27 · Tu 28 · We 29 · Th 30
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co.Ltd Jv P.T. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan	
							Actual	

PHO

PHO

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual		
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual		
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual		
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual		
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual		
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual		
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual		
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual		
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual		
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual		
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual		
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual		
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual		
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual		
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual		
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual		
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual		Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu
								PHO
TOTAL PROJETO ON-GOING								

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

Eng. Teresa Gomes
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto, Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng.	**Augusta da Costa Ferreira**
Municipio	**MUNICIPIO DILI NO POSTOS**

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Pagamento
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun ba Pagamento

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu
							PHO
TOTAL PROJETO ON-GOING							

SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.

Note:

Planu Periode inspesaun iha tereinu

Implementa Periode inspesaun iha tereinu

Relatoriu avaliasuan mensal iha Dili

Inspesaun Pagamentu Anual iha tereinu

Prepara Husi :

(Eng. Augusta da Costa Ferreira)
Eng. PMU ba Projetu (Impréstimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng.	**Augusta da Costa Ferreira**
Municipio	**MUNICIPIO DILI NO POSTOS**

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezenvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Augusta da Costa Ferreira)
Eng Imprestimo e consultant ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto. Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv P.T. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	

| | | |

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

Naran Eng. Vidal Guterres

Municipio MUNICIPIO DILI NO POSTOS

2022

Junho

Municipio / Posto	No.	Naran Projeto	Naran Companha	No Contrato	Kategoria	Dono do Projeto		OBSERVASAUN
IMPRESTIMO	1	National road no. 1 Upgrading project Manatuto - Baucau (package A01-02)Package A01-02/sta 56+400-114+102(56.82km)	Shanghai Construction Group Co,Ltd Jv PT. Brantas Abipraya(Persero)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	2	National road no. 1 Upgrading project Dili - Manatuto (package A01-01) (km 12+966.66-km 61+706.66)	Sinohydro Corporation Limited		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	3	Road Network Upgrading Sector Project (RNUP) for Manatuto - Laclubar Junction (Sta. 65+235 - 100+355)	R.D Interior Junior Construction / Hebei Road and Bridge Group		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	4	RNUSP/ Road Link No. A01 - 03 : Upgrading and Maintenance of Baucau - Lautem Section : Sta. 123 + 105 to Sta. 182 + 040 (with Exceptions)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	5	RNUSP / Road Link No. A01 - 03 : Upgrading and Maintenance of Maubara - Karimbala Road (Km. 49.7 to Km. 54.1 and Km.58.1 to Km. 62.6)and Atabae - Mota Ain Road (Km 85.3 to Km.114.2)	CBMI Const.Co.,Ltd. / Chongqing Road Engineering (Group)Co.,Ltd.(Joiunt venture)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	6	Road Network Upgranding Project (RNUP) Upgrading and Maintanace of Dili (Air Port Junction - Tibar)Road - Section 2 (Tasitolu - Tibar Road Link A03-01/ Sta 8 + 740 - Sta 13 + 290)	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	7	Road Climate Resilience project (RCRP) upgranding project and maintanace of Dili- Ainaro Road Lot 3(Solerema - Bandudatu Section (Km 34 +620 - Km 64 + 000)(29km)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	8	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 4 Bandudato-Aituto section (km 64+00 -km 89+000) (ICB/034/MPW-2013)	Chongqing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	9	Road Climate Resilience project (RCRP) upgranding and maintenance of Dili-Ainaro Road, Lot 5 Aituto-Ainaro section (km 89+00 -km 112+000)	Chongquing International Construction Corporation		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	10	Road Network Upgrading Sector Project Consulting Services : Preparation of Designs for 169 Km of National Roads (Baucau to Lospalos, Lautem to Com and Baucau to Viqueque) (ADB LOAN no . 3020 - TIM and 3021 - TIM)	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	PHO
	11	Road Network Upgrading Project (Additional Financing) - Construction Supervision for the Upgrading and Maintenance of Baucau to Lautem, Maubara to Karimbala and Atabae to Mota Ain Roads	Dongsung Engineering Co,Ltd JV with Kunhwa Engineering and Consulting Co.Ltd.		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Pagamento
	12	Upgrading and Maintenance of Laclubar Jct Natarbora Roads Sta. 100+360 - 144+995 Manatuto	China Nuclear Industry 22ND Construction CO.Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	13	Selection of Consulting Service for : Construction Supervision for the Upgrading and Maintenance of the Dili - Ainaro Road, Lot 2 : Laulara - Solerema Section (12+000 - 34+620) and Post Upgrading Economic Evaluation of the Entire Dili - Ainaro Road (Lots 1 - 5)	Kunhwa Eng. & Consulting Co.,Ltd in Joint Venture with Dongsung Eng. Co.,Ltd., and in Association with Desing Science, INC., and Kai Watu Kmanek Consultants, Unip Lda		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	14	Upgrading and Maintenance of Dili - Ainaro Road Lot 2 : Laulara - Solerema Section (km 12+000 - 34+620 km) Municipality Aileu	China Wu Yi Co.,Ltd		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	15	Consulting Services for Project Implementation and Construction Supervision for the Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120), Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	Intercontinental Consultanst and Technocrats Pvt.Ltd. (India) in Association With Infra Consultants in the Phlis, (Icp) Inc. (Philippines) (As Sub - Consultant) and Dezemvolve Timor Leste (Detile) Consultant, Lda (Timor Leste (As sub - Consultant)		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun Pagamento
	16	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 1 : Baucau - Venilale Section (Sta. 3+740 - Sta. 27+120)	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Halo Relatorio Pagamento
	`17	Upgrading and Maintenance of the Baucau - Venilale - Viqueque Highway Project, Lot 2 : Venilale - Viqueque Section (Sta. 27+120 - Sta. 62+010), Timor Leste.	China Railway JV COVEC		IMPRESTIMO	ADB (LOAN)	Plan Actual	Inspecsaun ba Pagamento

18	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 7 : Seloi - Aileu to Gleno - Ermera (162)	Raya Konsultan LDA	MPW- Cs 2000020	LM	MOP	Plan Actual	
19	Preparation of Detail Engineering & Bidding Dokument Preparation for New Bridges in 2019 suco Liurai maubara 1 Bera Railako, Sanfuk, tutu luru same fahi nehan	Lelo eng. Unip Lda Jv, Pt.Multi Karidi - Guna Jasa & PT. Cipta Design Indonesia	MPW-Cs -2000032	LM	MOP	Plan Actual	
20	Preparation of Detailed Engineering Design for Rehabilitation of Municipio Roads Package 2 : Uatulari - laisorulai	Bragtojul Unip Lda	MPW-CS -2000025	LM	MOP	Plan Actual	
21	For Preparation of detailled engineering for Rehabilitation of Municipios Roads Package 12 : Luca to Lacluta	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000022	LM	MOP	Plan Actual	
22	Preparation of Detailed Engineering For Rehabilitation of Municipio Roads Package : 1 JCT A - 16 (bobonaro) to lolotoe Town	Hilobadi Jv Pt. Siarplan Utama	MPW - CS- 2000030	LM	MOP	Plan Actual	
23	preparation of DED for Rehabilitation of Municpio Roads Package 10 : Soibada to Soibada town	Hilobadi Jv Pt. Siarplan Utama	MPW- CS 2000024	LM	MOP	Plan Actual	
24	Preparation of detailled Design for Rahabilitation municipio Roads Package 4 : turiscai to Alas	Wan Husin & Associates SDN. BHD Jv Consultant & eng. Interconental Unip Lda	MPW- CS 2000028	LM		Plan Actual	**SERVISU BA KONSULTAN DESIGN SEI AJUSTA TUIR PLANO HUSI PROJECTO NAIN .OU BAZEIA BA DOKUMENTOS KONSULTAN NIAN NEBE SUPMETE MAI HUSI PROJECTO NAIN.**
25	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000029	LM	MOP	Plan Actual	
26	Preparation Deitaled Design for Rahbilitation of Municipios	Detile Consultant	MPW- CS 2000027	LM	MOP	Plan Actual	
27	Preparation Deitaled Design for Rahbilitation of Municipios	Niceles Unip Lda	MPW- CS 2000026	LM	MOP	Plan Actual	
28	Preparation of Detailed Engineering & bid Preparation for new Bridge in 2019 package 1 : Samalari, sana uatulari- lai sorulai, sumaco (lacluta uma tolu) molas matadoro - RTK, Comoro mota ulun	Vox Da Vinci Consultant Engineering Lda	MPW- CS 2000031	LM	MOP	Plan Actual	
29	Preparation Deitaled Design for Rahbilitation of Municipios	Team Consultant Jv. ATT & ATT & Triangle	MPW- CS 2000021	LM	MOP	Plan Actual	
30	Preparation Deitaled Design for Rahbilitation of Municipios	Aureum Solis Consultant, Unip Lda Jv PT Bikarma	MPW- CS 2000033	LM	MOP	Plan Actual	
31	Preparation Deitaled Design for Rahbilitation of Municipios	PT. Bikarma JV Aureum Solis Consultant, Unip Lda	MPW- CS 2000023	LM	MOP	Plan Actual	
32	Intersection in the Existing dili liquisa road to conec akses road from tibar Bay Port	TPF Timor Unipessoal Lda	REP/009/MOP/2019	FI	MOP	Plan Actual	
33	Preparation Deitaled Design for Enginnering Desing Dili Urban Roads	Kiat Konsultan				Plan Actual	
34	Konsultan Suprevisi for Konstruction Suprevision of daradau irigation Schema	PT.Suanda karya Jv KWK	REP/042/MAP/2017	FI	MOP	Plan Actual	**Konsultan la serviso ona iha tereno,maibe pagamento seidauk hotu**
							PHO
TOTAL PROJETO ON-GOING							

Note:

Planu Periode inspesaun iha tereinu | **Implementa Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Eng. Vidal Guterres)
Eng. PMU ba Projetu (Imprestimo) ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenadora da Unidade de Controlo e Validasaun de Qualidade ADN,I.P.

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo ADN, I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
Laeluta	1	Package II Dilor	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Falta Retensaun 12 %
							Actual																																
OSSU	1	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	2	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750-Municipal of Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	3	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	4	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	Kay Seng Unip. Lda	MPW-W-190084	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	5	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	Costa Key Unip Lda	MPW-W-210053	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	6	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	Manoko Unip. Lda	MPW-W-210050	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	7	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																																
	8	New Construction of Health Post and Doctor's House building in Builale	Borala Unipessoal Lda	RDTL-MS-DNA-ICB-21-075	LM	MINISTERIO DA SAUDE	Plan																															
							Actual																																
	9	R4D Riral Roads Periodic Maintenance ossu - Nahareka Chainage 4+350 - 6+350	Fin-Los Unip. Lda JV Costa Key Unip. Lda	MPW - W - 190085	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																																
	10	EBF Uaibobo	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																																
	11	Pre Escolar Uaibua	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																																
	12	ESG Oloaasa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																																
	13	EBF Liaruca	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																																
UATOCARBAU	1	Construction of Dardau Irrigation Scheme Municipality Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															Lao Hela
							Actual																																
	2	Consulting Services For Construction Supervision of Dardau Irrigation	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																																
	3	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																
	4	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																																
	5	Konstrusaun Edificio Posto Administrativo Uato-Carbau	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																															
							Actual																																

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
UATOLARI	6	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	7	EBC 2.3 Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	8	ESG Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	1	New installation of mv,lv line and house connection in Area Lawai Viqueque District	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																	
	2	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																	
	3	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Lao Hela
							Actual																																
	4	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Lao Hela
							Actual																																
	5	New Construction Of Gapura,Stairs and Wall Protection in Garden Of Heroes	Natureza Furak,Unip Lda	ICB/005/DNAL/MACLN/VIII/2021	LM	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO	Plan																																
							Actual																																	
	6	Konstrusaun Edificio Posto Administrativo Uatolari	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																																
							Actual																																	
	7	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																																
	8	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	Karakuta Unip Lda	MPW-2013/JUNE	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																																
	10	New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari	Be'e Horis unip,lda		LM	IGREJA PROTESTANTE TIMOR	Plan																																
							Actual																																	
	11	Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque	L.M. Caicasa Metin Unip,Lda	RDTL-MAP-PO2021:15965	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																																Lao Hela
							Actual																																
	12	EBF Nahae	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	13	EBF Uaibira	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	14	EBC Uatolari	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	15	EBF Edemumu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	16	EBF Ualake	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	17	ESTV Kaluheda	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	
	18	EBF Debuisi	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
VIQUEQUE	1	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Falta retensaun
							Actual																																	
	2	Rehabilitation of Urban Road Municipality Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%
							Actual																																	
	3	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%
							Actual																																	
	4	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	Arquiris	SSS/105/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%
							Actual																																	
	5	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	Dira Nova Unip. Lda	MPW - W - 190114	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100% maibe kondisaun iha tereno sei a'at hela
							Actual																																	
	6	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package: 12 Luca - Lacluta	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																																	
	7	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	Uma Liurai unip, lda	SSS/138/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	8	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	Bihalutur Unip, lda	SSS/141/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																																	
	9	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section : Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	Loke Matan unip, lda	SSS/307/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	10	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	Caburela unip,lda	SSS/306/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	11	Servisu Manutensaun Edifício Agencia de Desemvolvimentu Nasional, I.P, Municipio Viqueque	Luminar, Unip,Lda	22/RDTL/MPO/AND,I.P/XI/2021	LM	MOP/ADN,I.P	Plan																																Lao Hela
							Actual																																
	12	ESG Calixa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																
	13	EBF Ular Rihik	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																
	14	Pre Escolar Maria Lobato Raithu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																
	15	EBC Caibiraoan	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																
	16	Pre Escolar Sebastiao Gomes Uai Mori Tula	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																
							Actual																																
	17	New Construction Office, Were House And Landscaping Of Viqueque Distric	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	LM	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	Plan																																
							Actual																																
MULTI POSTO ADMINIST RATIVO	1	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																Lao Hela
							Actual																																
TOTAL PROJETO ON-GOING																																						

Note:

Plano Periode inspesaun iha terenu | **Implementa Planu Periode Inspesaun** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Prosesu Pagamentu**

Prepara Husi :

(Eng.Roberto M. Martins)
Eng. Munisipiu Viqueque ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres .)
Adjunto Director Executivo ADN,I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
Lacluta	1	Package II Dilor	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Falta Retensaun 12 %
							Actual																																	
OSSU	1	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	2	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750-Municipal of Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	3	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	4	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	Kay Seng Unip. Lda	MPW-W-190084	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	5	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	Costa Key Unip Lda	MPW-W-210053	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	6	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	Manoko Unip. Lda	MPW-W-210050	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	7	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																																	
	8	New Construction of Health Post and Doctor's House building in Builale	Borala Unipessoal Lda	RDTL-MS-DNA-ICB-21-075	LM	MINISTERIO DA SAUDE	Plan																																	
							Actual																																	
	9	R4D Riral Roads Periodic Maintenance ossu - Nahareka Chainage 4+350 - 6+350	Fin-Los Unip. Lda JV Costa Key Unip. Lda	MPW - W - 190085	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	10	EBF Uaibobo	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	11	Pre Escolar Uaibua	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	12	ESG Oloaasa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	13	EBF Liaruca	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	1	Construction of Dardau Irrigation Scheme Municipality Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	Lao Hela
							Actual																																	
	2	Consulting Services For Construction Supervision of Dardau Irrigation	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																																	Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																																	

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
UATOCARBAU	3	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	4	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	5	Konstrusaun Edifício Posto Administrativo Uato-Carbau	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																															
							Actual																															
	6	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																															
	7	EBC 2.3 Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	8	ESG Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
UATOLARI	1	New installation of mv,lv line and house connection in Area Lawai Viqueque District	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	3	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																															
	4	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																															
	5	New Construction Of Gapura,Stairs and Wall Protection in Garden Of Heroes	Natureza Furak,Unip Lda	ICB/005/DNAL/MACLN/VIII/2021	LM	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	Plan																															
							Actual																															
	6	Konstrusaun Edifício Posto Administrativo Uatolari	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																															
							Actual																															
	7	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																															
	8	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	Karakuta Unip Lda	MPW-2013/JUNE	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																															
	10	New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari	Be'e Horis unip,lda		LM	IGREJA PROTESTANTE TIMOR	Plan																															
							Actual																															
	11	Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque	L.M. Caicasa Metin Unip,Lda	RDTL-MAP-PO2021:15965	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																															Lao Hela
							Actual																															
	12	EBF Nahae	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	13	EBF Uaibira	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	14	EBC Uatolari	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	15	EBF Edemumu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	16	EBF Ualake	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	17	ESTV Kaluheda	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	18	EBF Debuisi	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	1	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Falta retensaun**
							Actual																															
	2	Rehabilitation of Urban Road Municipality Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%**
							Actual																															
	3	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%**
							Actual																															
	4	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	Arquiris	SSS/105/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%**
							Actual																															
	5	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	Dira Nova Unip. Lda	MPW - W - 190114	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100% maibe kondisaun iha tereno sei a'at hela**
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Roberto M. Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
VIQUEQUE	6	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package: 12 Luca - Lacluta	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																																	
	7	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	Uma Liurai unip, lda	SSS/138/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	8	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	Bihalutur Unip, lda	SSS/141/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																																	
	9	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section : Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	Loke Matan unip, lda	SSS/307/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	10	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	Caburela unip,lda	SSS/306/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	11	Servisu Manutensaun Edificio Agencia de Desemvolvimentu Nasional, I.P, Municipio Viqueque	Luminar, Unip,Lda	22/RDTL/MPO/AND,I.P/XI/2021	LM	MOP/ADN,I.P	Plan																																	Lao Hela
							Actual																																	
	12	ESG Calixa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	13	EBF Ular Rihik	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	14	Pre Escolar Maria Lobato Raithu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	15	EBC Caibiraoan	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	16	Pre Escolar Sebastiao Gomes Uai Mori Tula	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	17	New Construction Office, Were House And Landscaping Of Viqueque Distric	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	LM	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	Plan																																	
							Actual																																	
MULTI POSTO ADMINISTRATIVO	1	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	
							Actual																																	Lao Hela
TOTAL PROJETO ON-GOING																																						

Note:

Plano Periode inspesaun iha terenu | **Implementa Planu Periode Inspesaun** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Prosesu Pagamentu**

Prepara Husi :

(Eng.Roberto M. Martins)
Eng. Munisipiu Viqueque ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres .)
Adjunto Director Executivo ADN,I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng.	**Salvador Martins**
Municipio	**MUNICIPIO VIQUEQUE NO POSTOS**

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
Lacluta	1	Package II Dilor	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Falta Retensaun 12 %**
							Actual																															
OSSU	1	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	2	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750-Municipal of Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	3	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	4	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	Kay Seng Unip. Lda	MPW-W-190084	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	5	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	Costa Key Unip Lda	MPW-W-210053	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	6	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	Manoko Unip. Lda	MPW-W-210050	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	7	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania**
							Actual																															
	8	New Construction of Health Post and Doctor's House building in Builale	Borala Unipessoal Lda	RDTL-MS-DNA-ICB-21-075	LM	MINISTERIO DA SAUDE	Plan																															
							Actual																															
	9	R4D Riral Roads Periodic Maintenance ossu - Nahareka Chainage 4+350 - 6+350	Fin-Los Unip. Lda JV Costa Key Unip. Lda	MPW - W - 190085	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Lao Hela**
							Actual																															
	10	EBF Uaibobo	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	11	Pre Escolar Uaibua	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	12	ESG Oloaasa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	13	EBF Liaruca	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	1	Construction of Dardau Irrigation Scheme Municipality Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															**Lao Hela**
							Actual																															
	2	Consulting Services For Construction Supervision of Dardau Irrigation	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															**Lao Hela Toma konta Eng.Konsultan ADN,IP**
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Salvador Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
UATOCARBAU	3	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	4	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	5	Konstrusaun Edificio Posto Administrativo Uato-Carbau	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																															
							Actual																															
	6	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																															
	7	EBC 2.3 Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	8	ESG Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
UATOLARI	1	New installation of mv,lv line and house connection in Area Lawai Viqueque District	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	3	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																															
	4	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela
							Actual																															
	5	New Construction Of Gapura,Stairs and Wall Protection in Garden Of Heroes	Natureza Furak,Unip Lda	ICB/005/DNAL/MACLN/VIII/2021	LM	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	Plan																															
							Actual																															
	6	Konstrusaun Edificio Posto Administrativo Uatolari	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																															
							Actual																															
	7	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																															
	8	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	Karakuta Unip Lda	MPW-2013/JUNE	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																															
	10	New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari	Be'e Horis unip,lda		LM	IGREJA PROTESTANTE TIMOR	Plan																															
							Actual																															
	11	Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque	L.M. Caicasa Metin Unip,Lda	RDTL-MAP-PO2021:15965	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																															Lao Hela
							Actual																															
	12	EBF Nahae	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	13	EBF Uaibira	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Salvador Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	14	EBC Uatolari	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	15	EBF Edemumu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	16	EBF Ualake	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	17	ESTV Kaluheda	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	18	EBF Debuisi	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															
							Actual																															
	1	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Falta retensaun**
							Actual																															
	2	Rehabilitation of Urban Road Municipality Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%**
							Actual																															
	3	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%**
							Actual																															
	4	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	Arquiris	SSS/105/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100%**
							Actual																															
	5	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	Dira Nova Unip. Lda	MPW - W - 190114	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															**Fisikamente Finaliza ona falta Dadus Administrasaun hodi prosesa pagamentu 100% maibe kondisaun iha tereno sei a'at hela**
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Salvador Martins

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
VIQUEQUE	6	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package: 12 Luca - Lacluta	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela Toma konta Eng.Konsultan ADN,IP
							Actual																																	
	7	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	Uma Liurai unip, lda	SSS/138/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	8	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	Bihalutur Unip, lda	SSS/141/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Paradu Total (Sei iha Problema ho Fisiku Konstrusaun) laiha imformasaun Husi kompania
							Actual																																	
	9	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section : Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	Loke Matan unip, lda	SSS/307/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	10	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	Caburela unip,lda	SSS/306/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
	11	Servisu Manutensaun Edificio Agencia de Desemvolvimentu Nasional, I.P, Municipio Viqueque	Luminar, Unip,Lda	22/RDTL/MPO/AND,I.P/XI/2021	LM	MOP/ADN,I.P	Plan																																	Lao Hela
							Actual																																	
	12	ESG Calixa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	13	EBF Ular Rihik	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	14	Pre Escolar Maria Lobato Raithu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	15	EBC Caibiraoan	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	16	Pre Escolar Sebastiao Gomes Uai Mori Tula	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																	
							Actual																																	
	17	New Construction Office, Were House And Landscaping Of Viqueque Distric	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	LM	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	Plan																																	
							Actual																																	
MULTI POSTO ADMINISTRATIVO	1	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																	Lao Hela
							Actual																																	
TOTAL PROJETO ON-GOING																																						

Note:

Plano Periode inspesaun iha terenu | **Implementa Planu Periode Inspesaun** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Prosesu Pagamentu**

Prepara Husi :

(Eng.Salvador Martins)
Eng. Munisipiu Viqueque ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres .)
Adjunto Director Executivo ADN,I.P.

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
Lacluta	1	Package II Dilor	Sheramor Construction Unipessoal, Lda	SSS/089/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	Nova Construção de Moro Protecção da Ribeira de Dilor (Pakote1-Sta. 0+000 To 0+800)	Atramor Sucesso Unip. Lda	SSS/093/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
OSSU	1	Road Rehabilitation of Assalaitula - Ossu Sta. 5+155 - 14+000 Municipality Viqueque	Uhacae, Lda	SSS/064/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	Manutensaun Estrada Luihono-Osorua Sta. 0+000-6+750-Municipal of Viqueque	Boru- Buty Unip.Lda	RT/072/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	3	R4D Rural Road Rehabilitation Ossu de Cima - Liawaioli Chainage 0+000 - 2+000 Viqueque Municipality	Kay Seng Unip. Lda	NCB/056/MOPTC-2019	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	4	Rural Roads Periodic Maintenance Luihono - Osorua Chainage 0+000 - 6+800 Routine Maintenance Ossu - Nahareka Chainage 0+000 - 3+400 Municipality Viqueque (162)	Kay Seng Unip. Lda	MPW-W-190084	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	5	R4D Rural Road Spot Improvement Ossu-Nahareca Chainage 0+000-3+400	Costa Key Unip Lda	MPW-W-210053	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	6	R4D Rural Road Spot Improvement Loihunu-Uagia Chainage 0+000 - 6+800	Manoko Unip. Lda	MPW-W-210050	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	7	Emergency Road Rehabilitation Package II from Ossu - Viqueque District	Modena Tecnic Unipessoal Lda	MOPW-F1-W-166514	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	8	New Construction of Health Post and Doctor's House building in Builale	Borala Unipessoal Lda	RDTL-MS-DNA-ICB-21-075	LM	MINISTERIO DA SAUDE	Plan																															Lao Hela
							Actual																															
	9	R4D Riral Roads Periodic Maintenance ossu - Nahareka Chainage 4+350 - 6+350	Fin-Los Unip. Lda JV Costa Key Unip. Lda	MPW - W - 190085	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	10	EBF Uaibobo	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	11	Pre Escolar Uaibua	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	12	ESG Oloaasa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	13	EBF Liaruca	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
AU	1	Construction of Dardau Irrigation Scheme Municipality Viqueque	Pembinaan Pulau Sebang SDN. BHD	ICB/041/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															
							Actual																															
	2	Consulting Services For Construction Supervision of Dardau Irrigation	PT. Suwanda Karya Mandiri	RFP/042/MAP-2017	FI	MINISTERIO AGRIKULTURA E PESCAS	Plan																															
							Actual																															
	3	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30	OBS
UATOCARB.	4	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	5	Konstrusaun Edificio Posto Administrativo Uato-Carbau	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan		Lao Hela
							Actual		
	6	Rehabilitasaun Nacional Roads (53+000-58+300) Package XI (Caidilale - Tardai/Post Polisi)	Sabirara, Unip. Lda	SSS/155/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	7	EBC 2.3 Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	8	ESG Uatocarbau	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
UATOLARI	1	New installation of mv,lv line and house connection in Area Lawai Viqueque District	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	2	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	3	Rehabilitation of Viqueque - Uatocarbau Road Sta. 26+500 - 31+800 (Package) Area in Viqueque Municipality Viqueque	Helamula Unipessoal, Lda	SSS/096/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	4	Rehabilitation of Viqueque - Uatocarbau Road Sta. 31+800 - 37+100 (Package VII) in Uatolari Municipality Viqueque	Greu Unipessoal, Lda	SSS/093/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	5	New Construction Of Gapura,Stairs and Wall Protection in Garden Of Heroes	Natureza Furak,Unip Lda	ICB/005/DNAL/MACLN/VIII/2021	LM	MINISTERIO PARA OS ASSUNTOS DOS COMBATENTES DA LIBERTAÇÃO NACIONAL	Plan		Lao Hela
							Actual		
	6	Konstrusaun Edificio Posto Administrativo Uatolari	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan		Lao Hela
							Actual		
	7	Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package 2 Uatolari - Laisorulai (162)	Bragtojul Unip. Lda JV PT Decont Mitra Consolindo	MPW-CS-2000025	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	8	Rehabilitation of Miabuti Edmumo, Sapatula Road /reabilitacao de estradas distritais de Uatolari Viqueque District	Karakuta Unip Lda	MPW-2013/JUNE	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan		
							Actual		
	10	New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari	Be'e Horis unip,lda		LM	IGREJA PROTESTANTE TIMOR	Plan		Lao Hela
							Actual		
	11	Konstrusaun Kanais Irrigasaun Iha Bebui - Viqueque	L.M. Caicasa Metin Unip,Lda	RDTL-MAP-PO2021:15965	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan		
							Actual		
	12	EBF Nahae	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	13	EBF Uaibira	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	14	EBC Uatolari	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		
	15	EBF Edemumu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan		Lao Hela
							Actual		

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng.	**Bebiano C. de Jesus Lopes**
Municipio	**MUNICIPIO VIQUEQUE NO POSTOS**

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
VIQUEQUE	16	EBF Ualake	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	17	ESTV Kaluheda	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	18	EBF Debuisi	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																															Lao Hela
							Actual																															
	1	Emergency work package caused by climate change on June 2013 (Gabion protection works in Lamak Laran) Municipio Viqueque	Consorcio Unidos Genero, Lda	SSS/100/MOPTC-2015	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	2	Rehabilitation of Urban Road Municipality Viqueque	Urukai II, Unip. Lda	SSS/072/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	3	Rehabilitation of Roads From Junction Bemvindo Bahalara - Uain We Bubur - Natar Tali Belanda Road Sta. 0+000 - 5+500 Municipality Viqueque	Arpy Unipessoal, Lda	SSS/163/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	4	Rehabilitation of Suspension Bridge, Municipality of Viqueque.	Arquiris	SSS/105/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	5	Routitine Road Maintenance Lot 1 - Viqueuqe - Dilor A07, Lot 2 - Jct Luca - Lacluta C5 Municipality Viqueque (162)	Dira Nova Unip. Lda	MPW - W - 190114	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	6	For Preparation of Detailed Engineering Design for Road Rehabilitation of "Municipal Road" Package: 12 Luca - Lacluta	Hilobadi Unip. Lda JV PT. Siarplan Utama Konsultan	MPW-CS-2000022	LM	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	7	Rehabilatation of Venilale - Hatulia, Uamori Road Package 2 (STA. 10+300 - STA. 15+475) in Baucau Municipality	Uma Liurai unip, lda	SSS/138/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	8	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 15+476-20+625	Bihalutur Unip, lda	SSS/141/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	9	Rehabilitation of Vanilale - Hatulari - Uaimori Road (30.880km) Roads Section : Venilale - Hatulia Roads Package 5 Sta. 20+625 - 25+755 Municipality Baucau	Loke Matan unip, lda	SSS/307/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															
	10	Rehabilitasaun Estrada Venilale - Hatulia - Uaimori fase 25+775-30+880	Caburela unip,lda	SSS/306/MOPTC-2016	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																															
							Actual																															

MINISTÉRIO DO PLANO E ORDENAMENTO
VIII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Bebiano C. de Jesus Lopes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
	11	Servisu Manutensaun Edificio Agencia de Desemvolvimentu Nasional, I.P, Municipio Viqueque	Luminar, Unip,Lda	22/RDTL/MPO/AND,I.P/XI/2021	LM	MOP/ADN,I.P	Plan																																Lao Hela
							Actual																																
	12	ESG Calixa	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	13	EBF Ular Rihik	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	14	Pre Escolar Maria Lobato Raithu	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	15	EBC Caibiraoan	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	16	Pre Escolar Sebastiao Gomes Uai Mori Tula	Grupo Komunitario		TT	MENISTERIO DA EDUCASAUN	Plan																																Lao Hela
							Actual																																
	17	New Construction Office, Were House And Landscaping Of Viqueque Distric	L.M. Caicasa Metin Unip,Lda	01/MSSI/DGAF/DNA/I/2022	LM	MENISTERIO SOLIDARIDADE SOSIAL E INCLUZAUN	Plan																																
							Actual																																
MULTI POSTO ADMINISTRATIVO	1	Upgrading and Maintenance of Baucau - Viqueque Highway Project Lot 2: Venilale - Viqueque : Sta. 27 + 120 to Sta. 62 + 010	China Railway Int. Group co, jv with China oversees	ICB/046/MOPTC-2017	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
TOTAL PROJETO ON-GOING																																						

Note:

Plano Periode inspesaun iha terenu | **Implementa Planu Periode Inspesaun** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Prosesu Pagamentu**

Prepara Husi :

(Eng.Bebiano C. de Jesus Lopes)
Eng. Munisipiu Viqueque ADN,I.P.

Sertifika Husi :

(Eng. Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade ADN, I.P.

Aprova Husi :

(Eng. Januario Maia Guterres .)
Adjunto Director Executivo ADN,I.P.

#ANEXU C1 (UatL – 1)

Back-up Data

Naran Projeto : **New installation of mv,lv line and house connection in Area Lawai Viqueque District**

No. kontratu : **RDTL/MOPTC-VOMPTC/CGI-PEN:0000459**

Data Inspesaun : 30 – 06 - 2022

Fatin Inspesaun : Lawai - Uatolari

Koordinadas :

Start Point : Long : 8.93164339S, Latetude : 126.49095769S

End Point : Long : 8.91427577S, Latetude : 126.50009669E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Arde ba ending baixadas seidauk monta/ installa& treckschoor mamar	

#ANEXU C1 (UatL – 1)

Back-up Data

Naran Projeto : **New installation of mv,lv line and house connection in Area Lawai Viqueque District**

No. kontratu : **RDTL/MOPTC-VOMPTC/CGI-PEN:0000459**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Fiu outgoing nia koneksaun ladik/ lametin, warning sign no climber protection	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Cabo baixadas monu ou tabele	

#ANEXU C1 (UatL – 1)

Back-up Data

Naran Projeto : **New installation of mv,lv line and house connection in Area Lawai Viqueque District**

No. kontratu : **RDTL/MOPTC-VOMPTC/CGI-PEN:0000459**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Suspention seidauk installa	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Suspension linha baixadas nian ladauk instala	

ANEXU C1 (UatC – 4)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346**

Data Inspesaun : 30 - 06 - 2022

Fatin Inspesaun : Hae Oli, Uani Uma & Ringgit

Koordinadas :

Start Point : Long : 8.75815027S, Latetude : 126.67350657E

End Point : Long : 8.74863203S, Latetude : 126.70498036E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu	
Start point project	


ANEXU C1 (UatC – 4)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Treckschoor Mamar	

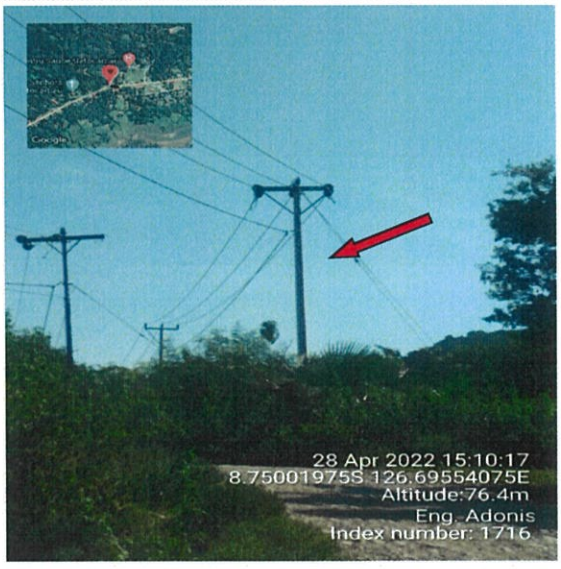Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 12 m halis / kleuk	

ANEXU C1 (UatC – 4)

Back-up Data

Naran Projeto : **New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..….. Pondasi rahun	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Trafo warning sign no climber protection seidauk installa	

#ANEXU C1 (UatC – 3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441**

Data Inspesaun : 30 – 06 - 2022

Fatin Inspesaun : Maumua - Dirinuu

Koordinadas :

Start Point : Long : 8. 72327782S, Latetude : 126.73435711E

End Point : Long : 8.74276514S, Latetude : 126.75989149E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste pinta mos ona	

#ANEXU C1 (UatC – 3)


□▯ 긜㵎刃 Ì⅄ Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441**

Cabo Baixadas monu ou tabele

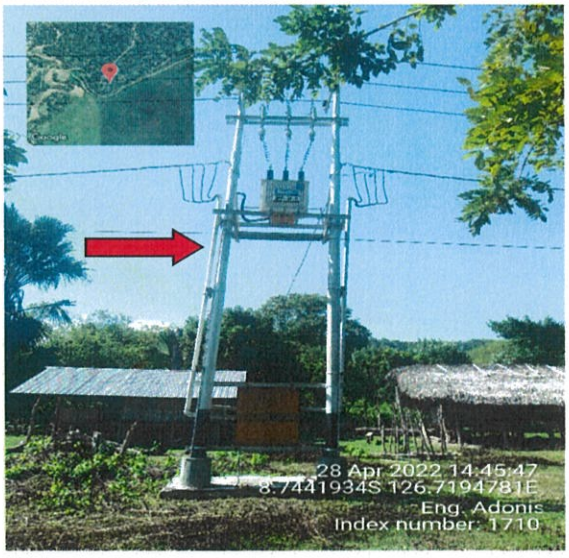

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..	
Hadia Assecores Panel & Climber Protection seidauk monta/Installa	

#ANEXU C1 (UatC – 3)

Back-up Data

Naran Projeto : **New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste kleuk/ halis	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Poste 9 m pinta mos ona	

#ANEXU C1 (UatL – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433**

Data Inspesaun : 30 – 06 - 2022

Fatin Inspesaun : Diribuu, Liasidi & Nunumalau

Koordinadas :

Start Point : Long : 8.75178994S, Latetude : 126.58012437E

End Point : Long : 8.70641417S Latetude : 126.57638368E

Naran Inspector : Adonis Julio Fernandes

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Treckschoor Mamar	


#ANEXU C1 (UatL – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433**

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …….. Poste 12 m halis/kleuk), Treckschoor mamar& fiu baixadas tabele	

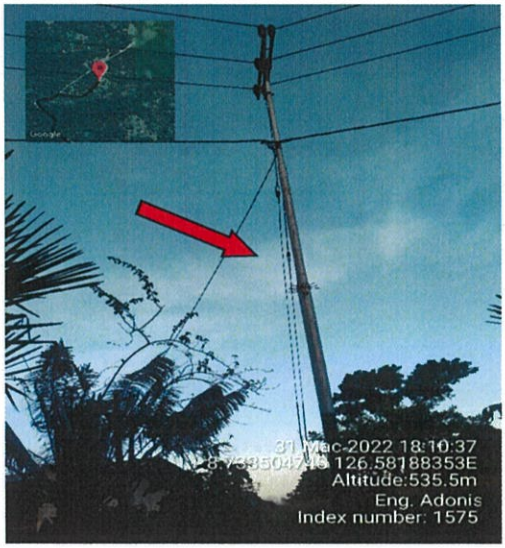
Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu …… Treckschoor Mamar & Poste Halis/ kleuk	

#ANEXU C1 (UatL – 2)

Back-up Data

Naran Projeto : **New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality**

No. kontratu : **RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433**

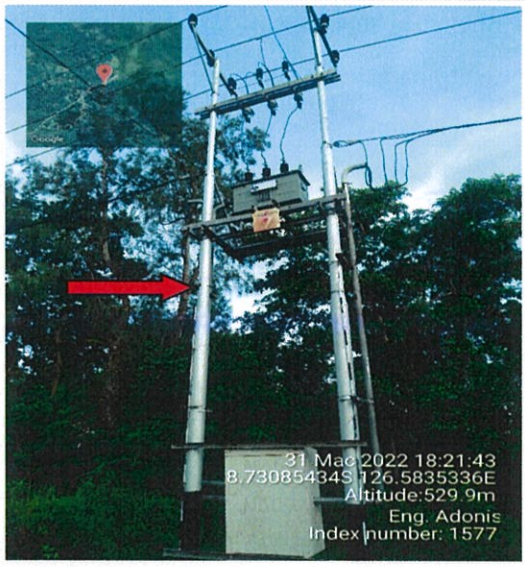Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..…..	
Pondasi trafo nakfera & climber protection seidauk installa	

Sketch & Foto Desenho	Observasaun iha tereno no Foto Aktual
Sketch Item servisu ……..	
Cabo baixadas kois (suspention kotu)	

MINISTERIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional - Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Adonis Julio Fernandes

Municipio MUNICIPIO VIQUEQUE NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
OSSU	1	Konstrusaun ka Rehabilitasaun ba EBF Liaruca	MEJD PKRIE EBF LIARUCA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	2	Konstrusaun ka Rehabilitasaun ba EBF 1,2 Uibobo	MEJD PKRIE EBF 1,2 UIBOBO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	3	Konstrusaun ka Rehabilitasaun ba EPE Uaibua/Ossu	MEJD PKRIE EBC UAI-BUA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	4	Konstrusaun ka Rehabilitasaun ba ESG Olokassa Ossu	MEJD PKRIE ESG OLAKASSA OSSU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	5	New Construction of Health Post and Doctor's House building in Builale	Borala Unipessoal Lda	RDTL-MS-DNA-ICB-21-075	LM	MINISTERIO DA SAUDE	Plan																																
							Actual																																Servisu electricidade seidauk
UATOCARBAU	1	Konstrusaun ka Rehabilitasaun ba ESG Uatucarbau	MEJD PKRIE ESG UATOCARBAU LESURUBI	00	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	2	Konstrusaun ka Rehabilitasaun ba ESG Uatucarbau	MEJD PKRIE ESG UATOCARBAU LESURUBI	00	LM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	3	New Installation, MV, LV Line and House Connection from Mota Irabere to Mauma'a, Floresta Dirimu, Uatocarabau - Viqueque Municipality	Divita Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000441	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	4	New Installation Mv, Lv Line & House Connection From Lefara to Hae Oli, Uani Uma and Ringgit Baru - Viqueque Municipality	Jonel Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000346	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	5	Konstrusaun Edificio Posto Administrativo Uato-Carbau	Luminar Unip. Lda	675/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																																
							Actual																																
UATOLARI	1	Konstrusaun ka Rehabilitasaun ba EBF 1,2 Debuisi	MEJD PKRIE EBF 1,2 DEBIUSI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	2	Konstrusaun ka Rehabilitasaun ba ESTV Kalo-Heda Uatolari	MEJD PKRIE ESTV KALO-HEDA UATOLARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	3	Konstrusaun ka Rehabilitasaun ba EBF Ualaque	MEJD PKRIE EBF UALUQUE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	4	Konstrusaun ka Rehabilitasaun ba ESF Uaibira	MEJD PKRIE EBF UAIBIRA 781	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	5	Konstrusaun ka Rehabilitasaun ba EBF Nahae	MEJD PKRIE EBF NAHAE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	6	Konstrusaun ka Rehabilitasaun ba EBC 07 Uatolari	MEJD PKRIE EBC 07 UATOLARI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	7	Konstrusaun ka Rehabilitasaun ba EBF Edemumo	MEJD PKRIE EBF EDEMUMO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk
	8	New installation of mv,lv line and house connection in Area Lawai Viqueque District	Laway	RDTL/MOPTC-VOMPTC/CGI-PEN:0000459	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	9	New Construction Of Chapel Betesda Naedala Affaloicai-Uatolari	Be'e Horis unip,lda		LM	IGREJA PROTESTANTE TIMOR	Plan																																
							Actual																																Servisu electricidade seidauk
	10	New Installation MV, LV Line and House Connection from Diribu to Liasidi, Nunumalau, Iralere and Ulusu, Uatolari - Viqueque Municipality	Habere Unip.lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000433	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																
	11	New Construction of Entry Gate and Wall Protection Works for Garden of Herois in Lugasa Uatolari	Silverquen	24/MSS/DNFALM-DAD/VIII/2016	LM	MINISTERIO SOLIDARIEDADE SOCIAL E INKLUSAUN	Plan																																
							Actual																																
	12	Konstrusaun Edificio Posto Administrativo Uatolari	Lemadae Unipessoal Lda	665/004/PDIM/KDM-VQQ/VIII/2019	PDIM	ESTATAL	Plan																																
							Actual																																
	1	Konstrusaun ka Rehabilitasaun ba EBF Ular Rihik Kraras	MEJD PKRIE EBF ULAR RIHIK KRARAS	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																Servisu electricidade seidauk

Municipio / Posto	No.	Naran Projeto	Naran Companhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho																													OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
VIQUEQUE	2	Konstrusaun ka Rehabilitasaun ba EBC Cabira-Oan	MEJD PKRIE EBC CABIRA-OAN	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																																Servisu electricidade seidauk
	3	Konstrusaun ka Rehabilitasaun ba ESG Calixa Viqueque	MEJD PKRIE ESG CALIXA VIQUEQUE	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																																Servisu electricidade seidauk
	4	Konstrusaun ka Rehabilitasaun ba EPE Maria Lobato	MEJD PKRIE EPE MARIA LOBATO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																																Servisu electricidade seidauk
	5	Konstrusaun ka Rehabilitasaun ba EPE Sebastiao Gomes	MEJD PKRIE EPE SEBASTIAO GOMES	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																														
							Actual																																Servisu electricidade seidauk
	6	Servisu Manutensaun Edifício Agencia de Desemvolvimentu Nasional, I.P, Municipio Viqueque	Luminar, Unip,Lda	22/RDTL/MPO/AND,I.P/XI/2021	22/RDTL/MPO/AND,I.P/XI/2021	MOP/ADN,I.P	Plan																														
							Actual																																
		TOTAL PROJETO ON-GOING																																			

Note:

Plano Periode inspesaun iha terenu

Implementa Planu Periode Inspesaun

Relatoriu avaliasuan mensal iha Dili

Inspesaun Prosesu Pagamentu

Prepara Husi :

(Adonis Julio Fernandes)
Eng. ba Projeitu ME, ADN,I.P

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN,I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo, ADN,I.P

MINISTÉRIO DO PLANO E ORDENAMENTO
VII GOVERNO CONSTITUCIONAL

ADN, I.P.
Agência de Desenvolvimento Nacional, Instituto Público

PLANU INSPESAUN

2022

Naran Eng. Adonis Julio Fernandes

Municipio MUNICIPIO MANATUTO NO POSTOS

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho 1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	OBS
MANATUTO VILA (MV)	1	Konstrusaun ka Rehabilitasaun ba EBF Batara	MEJD PKRIE EBF BATARA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	2	Konstrusaun ka Rehabilitasaun ba EBF Aisiu-Um	MEJD PKRIE EBF AISIU-UM	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	3	Konstrusaun ka Rehabilitasaun ba EBC Remanarun	MEJD PKRIE EBC REMANARUN	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	4	Konstrusaun ka Rehabilitasaun ba EBC Weaihudik	MEJD PKRIE EBC WEAIHUDIK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	5	Konstrusaun ka Rehabilitasaun ba EBF Rentau	MEJD PKRIE EBF RENTAU	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	6	Konstrusaun ka Rehabilitasaun ba ESG Kay Rala	MEJD PKRIE ESG KAY RALA	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	7	Konstrusaun ka Rehabilitasaun ba EBF Obrato	MEJD PKRIE EBF OBRATO	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	8	Construção de novo Estadio de Futebol em Manatuto	Obrai Unipesoal, Lda	ICB/0128/SEJD-2014	FI	SECRETARIADO ESTADO JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	9	Konstrusaun ESTV Beadi-Manatuto	Ralan Unip. Lda	03/PDIM-II/MNTT/IX/2019	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	10	Continuacao Requalificacao do Jardim Onde se Localiza Monumento Municipal Manatuto	Carya Timor Leste Unip. Lda	08/PDIM-I/MNTT/XII/2019	PDIM	ESTATAL	Plan																																
							Actual																																
	11	Continuacao e Finalizacao dos Acessores Monumentos Municipio Manatuto	Carya Timor Leste Lda	01/PDIM-I/MNTT/XII/2019	PDIM	ESTATAL	Plan																																
							Actual																																
	12	Costrusaun Fatin Izolamento Iha Municipio Manatuto	Talamori Unip.Lda	RDTL-MS-DNA-DC-20-254	LM	SAUDE	Plan																																
							Actual																																
	13	New Construction of Laboratory for Covid 19 at Manatuto, Ministery of Helath, Timor Leste	Kartini Unipessoal Lda	RDTL-MS-DNA-RBK-20-186	LM	MINISTERIO SAUDE	Plan																																
							Actual																																
LALEIA (LAL)	1	Konstrusaun ka Rehabilitasaun ba EP Cairui	MEJD PKRIE EP CAIRUI	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																																
							Actual																																
	2	Rehabilitasaun Kampu Foteboll iha Postu Administrativu Laleia	DCO Unip.Lda	011LM/AND/MPIE/VII/DILI/2019/EDIFICIO DEPARTMENT	LM	MINISTERIO PLANU E ORDENAMENTU	Plan																																
							Actual																																
	3	Konstrusaun Edificio Posto Administrativo Laleia	Hare Unip.Lda	02/PDIM-I/MNTT/IX/2019	PDIM	ESTATAL	Plan																																
							Actual																																
AC)	1	New Installation Mv, Lv Line & House Connection From Laclubar Vila to Funar And Fatuk Manu - Manatuto Municipality	Tasibala III Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000412	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																																
							Actual																																

Municipio / Posto	No.	Naran Projeto	Naran Kompanhia	No Contrato	Kategoria	Dono do Projeto	Action	Junho																											OBS
								1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	
LACLUBAR (L	2	Konstrusaun Posto Saude Iha iha Suku Funar - Laklubar	Ladiama Unip. Lda	04/PDIM I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																													
							Actual																														
	3	Konstrusaun Rezidensia Pesoal Iha iha Suku Funar - Laklubar	Tonijo Unip. Lda	05/PDIM-I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																													
							Actual																														
	1	Kontinuasaun Konst. Postu Saude Iha Suku Fatumakerek	Hatuwari Unip. Lda	02/PDD-II/MNTT/VII/2015	PDIM	MINISTERIO SAUDE	Plan																													
							Actual																														
	2	Konstrusaun ESTV Soibada Manatuto (CA + CB)	Manufahi Kiik Unip. Lda	01/PDIM-I/MNTT/IX/2019	PDIM	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																														
BARIQUE (BA)	1	New Construction Centre of Rice Milling, Fence, Office & Housing in Natarbora	Tasibala II Const	RDTL/PO:2016-11272	LM	MINISTERIO AGRIKULTURA E PESCAS	Plan																													
							Actual																														
	2	Konstrusaun Postu Saude Aimeta Laran-Barique	Malack II Unip. Lda	03/PDIM-I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																													
							Actual																														
	3	Construction of Residense for Health Staff in Suku Aimeta Laran-Barique	Macucuren Unip. Lda	03/PDIM-I/MNTT/IX/2019	PDIM	MINISTERIO SAUDE	Plan																													
							Actual																														
LACLO (LA)	1	New Installation MV, LV Line and House Connection from Laclo to Mantane - Manatuto Municipality	Anopa Electrical Unip. Lda	RDTL/MOPTC-VMOPTC/CGI-PEN : 00000421	FI	MINISTERIO DAS OBRAS PUBLICAS	Plan																													
							Actual																														
	2	Konstrusaun Edificio Posto Administrativo Laclo	Ailili Const. Unip. Lda	02/PDIM-I/MNTT/IX/2019	PDIM	ESTATAL	Plan																													
							Actual																														
	3	Rehabilitation of Behau Mini Tradisional Food	Esa-Un	RDTL:74/GMTAC/X//2015	LM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																													
							Actual																														
	4	Konstrusaun Mercado Komunitaria Kikan Ilimano	Surprise Unip. Lda	07/PDIM-II/MNTT/VIII/2016	PDIM	MINISTERIO TURISMO KOMERCIO E INDUSTRIA	Plan																													
							Actual																														
	5	Konstrusaun ka Rehabilitasaun ba PE Rembor	MEJD PKRIE PE REMBOR	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																														
	6	Konstrusaun ka Rehabilitasaun ba EBF Bahadik	MEJD PKRIE EBF BAHADIK	00	LM-TP	MINISTERIO EDUKASAUN JUVENTUDE E DESPORTU	Plan																													
							Actual																														
TOTAL PROJETO ON-GOING																																			

Note:

Plano Periode inspesaun iha tereinu | **Implementasaun Plano Periode inspesaun iha tereinu** | **Relatoriu avaliasuan mensal iha Dili** | **Inspesaun Pagamentu Anual iha tereinu**

Prepara Husi :

(Adonis Julio Fernandes)
Eng. Electricidade, ADN, I.P

Sertifika Husi :

(Emerenciana da Costa Maia Freitas)
Coordenador da Unidade de Controlo e Validasaun de Qualidade, ADN, I.P

Aprova Husi :

(Eng. Januario Maia Guterres)
Adjunto Director Executivo,ADN, I.P
